

386th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
December 2017



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for December 2017 contains information on the status of the 1302 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 31 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 31 projects, 17 are **Mega** Projects costing ₹1000 crore and above.

(ii). Total original cost of implementation of the 1302 projects was Rs. 16,20,089.45 crore and their anticipated completion cost is likely to be Rs. 18,38,119.90 crore, which reflects overall cost overruns of Rs. 2,18,030.45 crore (13.46% of original cost). The expenditure incurred on these projects till December 2017 is Rs. 6,58,680.80 crore, which is 35.83% of the anticipated cost of the projects.

(iii). Out of a total of 1302 projects, 4 projects have reported completion and 17 new projects have been initiated on the monitor of this ministry during the current month. Of these, 15 projects are ahead of schedule, 310 are on schedule, 287 are delayed, 359 projects are showing cost overrun and 104 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 250 if delay is calculated with reference to latest revised schedules of completion. For 690 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 287 delayed projects, 53 projects have overall delay in the range of 1 to 12 months, 58 projects have delay in the range of 13 to 24 months, 103 projects have delay in the range of 25 to 60 months and 73 projects have delay of 61 months and above.

(v). Further, out of the 287 delayed projects, 104 projects have cost overruns. Out of these, the cost for 49 projects has been revised and for 55 projects the cost has not yet been revised. Of the 49 projects where cost has been revised, the anticipated cost of 9 projects has again exceeded the revised cost. Out of 287 delayed projects, 141 projects have not provided any milestones and in 98 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 269 projects which though on schedule but are having cost overruns. Of these, the cost for 76 projects has since been revised. Of the 76 projects where cost has been revised, the anticipated cost of 33 projects has exceeded even the revised costs. Out of these 269 projects, 162 projects have not provided any milestones and for 6 projects the completion date of milestone(s) has already lapsed.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1302 projects 394 are mega projects. Total original cost of implementation of these 394 projects was Rs. 12,50,917.13 crore and their anticipated completion cost is likely to be Rs. 14,41,771.27 crore, which reflects overall cost overruns of Rs. 1,90,854.14 crore (15.26% of original cost). The expenditure incurred on these projects till December 2017 is Rs. 5,53,436.28 crore, which is 38.39% of the anticipated cost of the projects. Out of the 394 mega projects, 153 projects have cost overruns with respect to original cost and the number of such projects decreases to 118 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 126 delayed mega projects, 53 projects have cost overruns. Out of these, the cost for 25 projects has been revised and for 28 projects the cost has not yet been revised. Of the 25 projects where cost has been revised, the anticipated cost of 5 projects has again exceeded the revised cost. Out of 126 delayed projects, 65 projects have not provided any milestones and in 50 cases the dates of completion of the milestones have already lapsed.

(iii) In addition to above there are 100 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 28 projects has since been revised and for 72 projects cost has not been revised. Of the 28 projects where cost has been revised, the anticipated cost of 13 projects has exceeded even the revised costs. Out of these 100 projects, 58 projects have not provided any milestones and for 1 project the completion date of milestone(s) has already lapsed.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.
7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.
8. The status as on 31.12.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).
9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs 150 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	509	3
2	RAILWAYS	351	0
3	POWER	125	16
4	PETROLEUM	112	6
5	COAL	92	1
6	URBAN DEVELOPMENT	34	0
7	STEEL	31	3
8	HEALTH AND FAMILY WELFARE	14	1
9	SHIPPING AND PORTS	10	0
10	TELECOMMUNICATIONS	9	0
11	ATOMIC ENERGY	4	0
12	MINES	4	0
13	CIVIL AVIATION	2	0
14	FERTILISERS	2	1
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1302	31

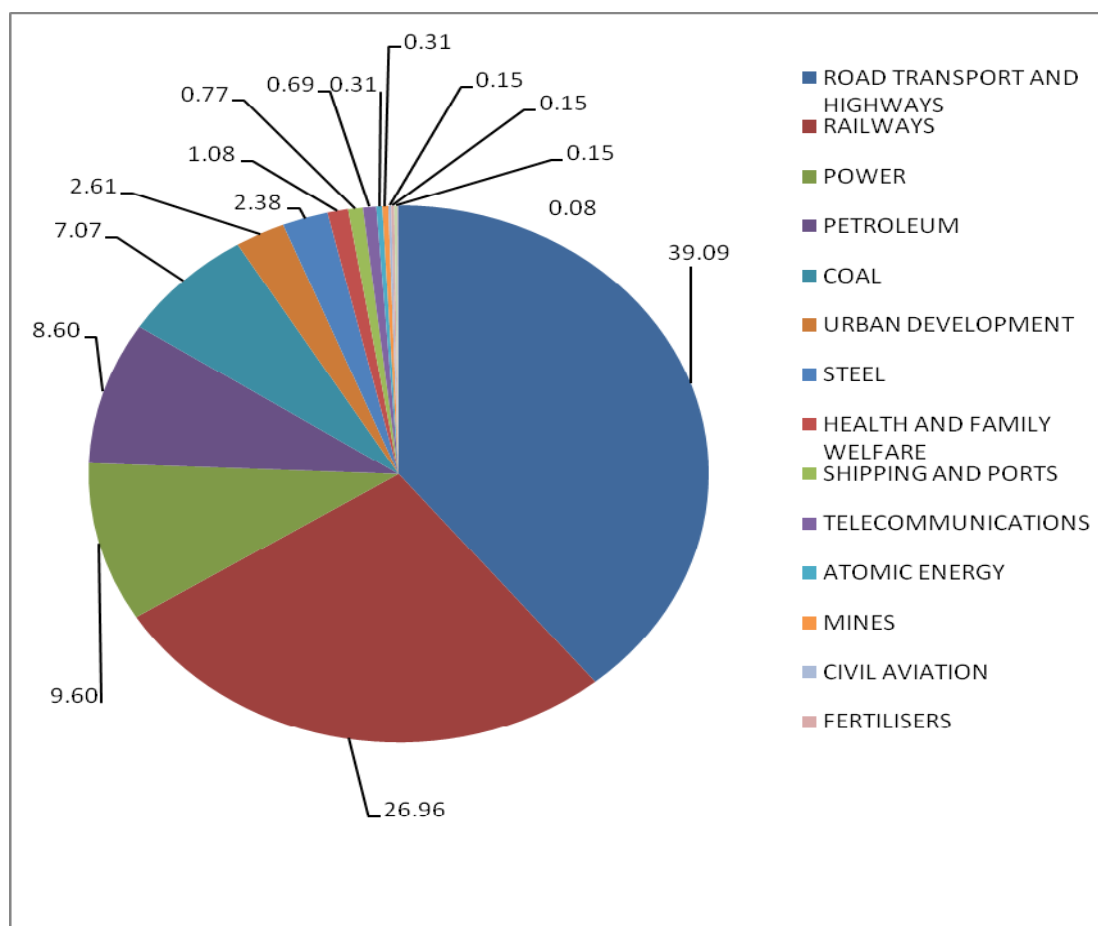


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT (BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94
	June,2017			
	<u>STEEL</u>			
10	SMS-1 CONVERTERS REVAMPING (RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]	404.16	07/2015	394.74
	<u>POWER</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000166]	378.71	10/2016	257.90
12	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000167]	400.47	04/2017	265.20
13	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]	187.04	06/2018	54.60
	July,2017			
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]	752.64	07/2013	633.62
15	WARDHA-HYDERABAD 765 KV LINK (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]	3,662.02	05/2018	2,302.40
	August,2017			
16	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]	1,575.30	05/2016	1,328.51
	September,2017			
	<u>ATOMIC ENERGY</u>			
17	KUDANKULAM APP (NPCIL) (NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100040]	13,171.00	12/2008	22,340.00
	<u>CIVIL AVIATION</u>			
18	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000069]	335.61	05/2012	305.59
	<u>PETROLEUM</u>			
19	DE-BOTTLENECKING OF SMPL (INDIAN OIL CORPORATION LIMITED) - [N16000089]	1,584.00	03/2017	1,355.45
20	INTEGRATED REFINERY EXPANSION PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000143]	16,504.00	03/2017	15,090.99
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000146]	666.00	11/2015	606.13
22	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000149]	586.00	08/2015	440.20
23	MARKETING TOP AT KORBA (INDIAN OIL CORPORATION LIMITED) - [N16000186]	141.86	09/2016	174.37

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
24	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000205]	1,714.00	06/2017	1,067.89
	<u>POWER</u>			
25	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000112]	2,127.51	07/2014	2,582.69
26	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000125]	9,569.76	06/2015	7,311.17
27	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000191]	3,984.03	01/2013	3,290.44
	October,2017			
	<u>COAL</u>			
28	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU (NEYVELI LIGNITE CORPORATION) - [N06000110]	364.75	10/2014	333.05
	<u>STEEL</u>			
29	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS (RASTRIYA ISPAT NIGAM LIMITED) - [N12000089]	877.73	07/2015	747.81
30	TURBO BLOWER - 5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000092]	280.00	09/2016	157.09
	<u>PETROLEUM</u>			
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000180]	163.88	07/2016	82.45
32	50 MW 10 PERSENT WIND ENERGY POWER PROJECT Central Sector Projects(OIL INDIA LIMITED) - [N16000208]	500.00	03/2017	368.24
33	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) (INDIAN OIL CORPORATION LIMITED) - [N16000217]	150.00	07/2014	251.90
	<u>RAILWAYS</u>			
34	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR (SOUTH WESTERN RAILWAY) - [220100183]	295.00	-	1,509.88
35	GURIYA-MARWAR AND KARJODA-PALANPUR (NORTH WESTERN RAILWAY) - [N22000154]	239.73	-	195.42

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
36	HOSADURGA - CHICKJAJUR (28.89 KM) (SOUTH WESTERN RAILWAY) - [N22000324]	203.40	-	282.69
	<u>URBAN DEVELOPMENT</u>			
37	BANGALORE METRO RAIL PROJECT (METROPOLITAN RAPID TRANSPORT PROJECTS) - [N28000008]	6,395.00	06/2011	14,200.11
38	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000074]	315.00	06/2015	302.82
39	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000077]	405.01	12/2014	349.54
	November,2017			
	<u>MINES</u>			
40	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra Private(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000008]	355.13	11/2016	355.13
41	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN PPP (ANNUITY)(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000009]	344.50	11/2016	344.50
	<u>POWER</u>			
42	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000186]	550.06	03/2018	470.07
43	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000207]	244.19	07/2018	123.33
	December,2017			
	<u>COAL</u>			
44	PURNADIH OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000085]	210.98	03/2013	206.80
	<u>STEEL</u>			
45	3RD CONVERTER AND 4TH CASTER (RASTRIYA ISPAT NIGAM LIMITED) - [N12000088]	974.76	07/2016	676.93
	<u>HEALTH AND FAMILY WELFARE</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
46	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000004]	444.70	12/2015	326.30
47	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000005]	196.70	01/2016	170.00

TABLE-3

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2017			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]	940.00	07/2012	1,415.36
2	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]	359.00	09/2013	2.74
3	BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]	500.29	08/2013	869.91
4	4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]	580.43	08/2013	226.67
5	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]	828.00	09/2014	870.15
6	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH- 200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366]	996.37	12/2017	0.00
7	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]	725.95	06/2019	0.00
	September,2017			
	<u>POWER</u>			
8	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [180100261]	358.42	12/2008	0.00
9	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000099]	1,585.12	11/2013	1,452.46
10	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000114]	552.44	02/2014	501.60
11	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000170]	188.75	02/2017	0.00
12	PATAN WIND FARM SITE, GUJARAT 50 MW (THDC INDIA LIMITED) - [N18000204]	315.00	10/2016	311.96

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	KANDORNA AND BHANWAD WIND FARM (THDC INDIA LIMITED) - [N18000234]	415.49	03/2017	415.50
	October,2017			
14	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000259]	955.00	12/2015	74.00
15	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000260]	2,525.00	11/2017	564.00


Summary of projects in the Flash Report for the month of December, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1289
Number of Projects completed/dropped/frozen in Current Month	4
	0
Number of Projects Added in Current Month	17
Number of Projects in Current Month	1302

Brief Analysis

Project Status with respect to Original Schedule: Out of 1302 projects, 15 projects are ahead of schedule, 310 projects are on schedule 287 projects are delayed. 542 projects do not have fixed dates of commissioning. 148 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

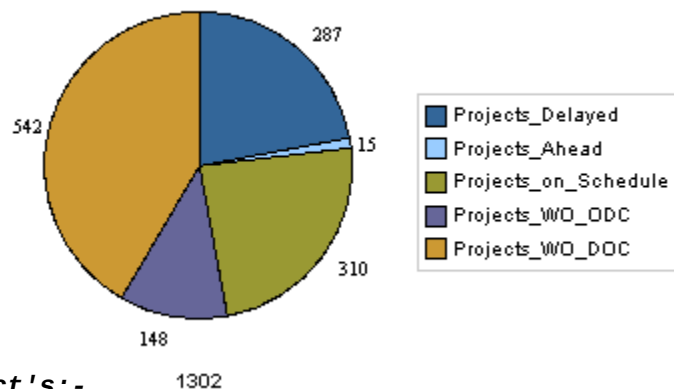

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1302 projects when sanctioned, was of the order of Rs. 1620089.45 crore but this was subsequently revised to Rs. 1838119.9 crore implying a cost overrun of 13.5%. The expenditure incurred on these projects till December, 2017 is Rs. 658680.8 crore, which is 35.8% of the anticipated cost of the projects.

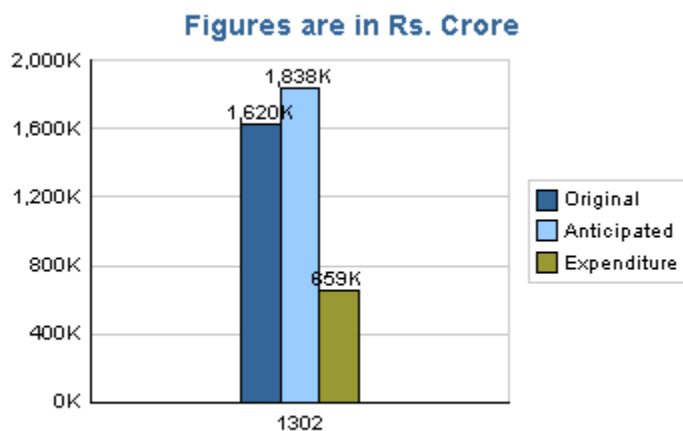


TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 crore and above

No of Projects in Previous Month	1289
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	17
No of Projects in Current Month	1302

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	287 (22.04%)	15 (1.15%)	310 (23.81%)	148 (11.37%)	542 (41.63%)	1302
Latest Approved (Date)	250 (19.20%)	13 (1.00%)	352 (27.04%)	144 (11.06%)	543 (41.71%)	1302

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1129	14,02,143.82	15,24,892.45	4,77,331.17	31.30	1,22,748.63	8.80
Project with Revision in Cost	173	2,91,641.51	3,13,227.45	1,81,349.63	57.90	21,585.94	7.40
Total	1,302	16,93,785.33	18,38,119.90	6,58,680.80	35.83	1,44,334.57	8.52
Original Cost of All Projects							
Original Cost	1,302	16,20,089.45	18,38,119.90	6,58,680.80	35.83	2,18,030.45	13.46
Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	287	6,27,769.77	7,65,358.56	4,39,112.58	57.40	1,37,588.79	21.90
Latest Approved (RCE)	250	5,89,076.32	6,72,745.83	3,73,698.46	55.50	83,669.51	14.20
Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	31	1,14,295.26	1,28,829.32	97,544.54	75.70	14,534.06	12.70
Total	31	1,14,295.26	1,28,829.32	97,544.54	75.72	14,534.06	12.72

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	89,695.08	89,199.09	-0.55	9	19,751.90	21,090.72	6.78
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	3.35
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	31	55,217.00	55,430.68	0.39	5	1,639.71	2,211.39	34.86
7	PETROLEUM	112	2,01,408.83	2,02,790.33	0.69	19	28,273.91	35,027.99	23.89
8	POWER	125	3,38,658.41	3,97,484.24	17.37	43	1,04,449.62	1,63,275.45	56.32
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	351	3,53,800.77	4,83,480.73	36.65	218	1,33,921.02	3,24,078.27	141.99
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,047.00	3,45,419.20	1.88	43	25,598.69	32,656.93	27.57
13	SHIPPING AND PORTS	10	4,910.75	5,535.92	12.73	5	1,205.50	2,172.77	80.24
14	TELECOMMUNICATIONS	9	16,952.95	28,189.47	66.28	2	13,546.70	24,886.00	83.71
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,035.91	3.63	6	17,021.00	22,244.19	30.69
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	2	453.64	469.04	3.39
Total		1302	16,20,089.45	18,38,119.90	13.46	359	3,52,545.30	6,39,929.73	81.52

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	60	97,515.51	1,01,522.54	4.11	9	6,577.56	11,610.74	76.52
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	6	9,755.78	26,709.21	173.78
3	ASSAM	48	33,455.72	49,200.77	47.06	17	16,060.10	31,967.74	99.05
4	BIHAR	79	68,372.22	85,193.29	24.60	21	33,916.51	51,033.53	50.47
5	GOA	9	4,043.51	4,058.91	0.38	2	453.64	469.04	3.39
6	GUJARAT	43	38,941.93	41,578.30	6.77	10	5,641.30	9,568.61	69.62
7	HARYANA	21	14,081.22	15,967.45	13.40	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	2	4,966.47	12,898.75	159.72
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	355.99
10	KARNATAKA	44	72,280.39	81,988.83	13.43	19	10,319.82	21,192.04	105.35
11	KERALA	21	21,774.25	27,871.82	28.00	7	3,017.36	9,114.93	202.08
12	MADHYA PRADESH	59	62,349.33	65,892.80	5.68	8	6,120.00	10,654.83	74.10
13	MAHARASHTRA	123	1,77,734.51	1,90,392.94	7.12	32	40,786.97	58,273.16	42.87
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	6,942.57	246.92	2	988.06	5,929.43	500.11
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	72	74,459.24	82,559.02	10.88	21	9,275.99	17,392.06	87.50
19	PUNJAB	28	15,555.77	15,561.50	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	62	45,695.77	47,536.64	4.03	13	5,311.37	7,187.76	35.33
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	65	1,10,018.77	1,25,859.19	14.40	21	27,563.13	44,494.76	61.43
23	TRIPURA	11	4,400.64	9,067.42	106.05	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	88	1,11,448.36	1,15,138.64	3.31	19	29,399.72	33,544.58	14.10
25	WEST BENGAL	55	56,532.37	71,188.94	25.93	23	24,955.79	40,210.46	61.13
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
27	DELHI	14	49,878.66	50,145.97	0.54	2	1,375.86	1,789.17	30.04
28	CHHATISGARH	38	82,769.79	84,960.97	2.65	5	3,354.55	5,545.73	65.32
29	JHARKHAND	47	46,513.55	50,225.71	7.98	10	9,447.31	13,163.25	39.33
30	UTTARAKHAND	14	17,481.68	32,916.29	88.29	6	9,407.32	24,842.44	164.08
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	36	24,952.57	27,674.71	10.91	11	3,122.03	6,035.26	93.31
33	MULTI STATE	183	3,02,573.52	3,00,732.55	-0.61	71	68,914.84	1,23,365.38	79.01
Total		1302	16,20,089.45	18,38,119.90	13.46	359	3,52,545.30	6,39,929.73	81.52

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	89,695.08	89,199.09	-0.55	37	20,254.10	20,473.06	6 - 132
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	2 - 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	31	55,217.00	55,430.68	0.39	17	46,561.67	46,373.46	2 - 72
7	PETROLEUM	112	2,01,408.83	2,02,790.33	0.69	30	54,427.11	56,556.23	1 - 93
8	POWER	125	3,38,658.41	3,97,484.24	17.37	65	2,24,055.02	2,61,600.25	2 - 118
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	6	1,689.51	1,711.99	6 - 16
11	RAILWAYS	351	3,53,800.77	4,83,480.73	36.65	34	42,047.55	1,14,569.54	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,047.00	3,45,419.20	1.88	63	55,031.75	58,574.37	5 - 117
13	SHIPPING AND PORTS	10	4,910.75	5,535.92	12.73	3	1,116.39	1,527.36	20 - 141
14	TELECOMMUNICATIONS	9	16,952.95	28,189.47	66.28	2	13,752.26	25,082.26	9 - 47
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,035.91	3.63	22	99,001.16	1,04,189.97	4 - 72
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	-
Total		1302	16,20,089.45	18,38,119.90	13.46	287	6,27,769.77	7,65,358.56	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above
(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	60	97,515.51	1,01,522.54	4.11	9	9,541.96	11,222.60	2 - 144
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	3	3,209.82	7,672.72	36 - 99
3	ASSAM	48	33,455.72	49,200.77	47.06	13	10,388.54	18,800.70	15 - 122
4	BIHAR	79	68,372.22	85,193.29	24.60	9	30,657.27	40,640.20	11 - 113
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	43	38,941.93	41,578.30	6.77	8	16,533.35	18,214.87	3 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	3	2,216.53	3,396.53	6 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	3	6,107.21	10,586.37	15 - 111
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	6	19,130.27	47,361.54	12 - 193
10	KARNATAKA	44	72,280.39	81,988.83	13.43	4	43,935.34	43,935.34	6 - 19
11	KERALA	21	21,774.25	27,871.82	28.00	6	11,313.37	11,420.56	9 - 65
12	MADHYA PRADESH	59	62,349.33	65,892.80	5.68	8	14,436.98	14,999.21	4 - 96
13	MAHARASHTRA	123	1,77,734.51	1,90,392.94	7.12	22	53,558.94	57,839.63	2 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 50
16	MIZORAM	5	2,001.20	6,942.57	246.92	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	72	74,459.24	82,559.02	10.88	16	26,403.22	27,631.35	5 - 108
19	PUNJAB	28	15,555.77	15,561.50	0.04	4	1,512.09	1,512.09	6 - 23
20	RAJASTHAN	62	45,695.77	47,536.64	4.03	8	16,919.83	17,605.45	6 - 74
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	65	1,10,018.77	1,25,859.19	14.40	20	76,743.60	84,418.66	1 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	3	1,231.33	3,893.38	7 - 72
24	UTTAR PRADESH	88	1,11,448.36	1,15,138.64	3.31	8	22,510.81	22,609.99	4 - 61
25	WEST BENGAL	55	56,532.37	71,188.94	25.93	16	27,379.30	29,553.71	6 - 57
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	1	6,086.08	5,479.75	5 - 5
27	DELHI	14	49,878.66	50,145.97	0.54	7	42,999.38	43,372.17	5 - 27
28	CHHATISGARH	38	82,769.79	84,960.97	2.65	11	49,049.07	50,068.29	19 - 93
29	JHARKHAND	47	46,513.55	50,225.71	7.98	20	24,771.45	25,123.59	5 - 166
30	UTTARAKHAND	14	17,481.68	32,916.29	88.29	5	7,719.83	11,020.99	50 - 89
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	36	24,952.57	27,674.71	10.91	13	5,449.94	5,987.93	12 - 132
33	MULTI STATE	183	3,02,573.52	3,00,732.55	-0.61	49	91,646.15	1,26,739.80	2 - 261
Total		1302	16,20,089.45	18,38,119.90	13.46	287	6,27,769.77	7,65,358.56	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.
Cost Overrun = Anticipated Cost minus Original Cost

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	89,474.77	89,199.09	-0.31	35	13,146.07	13,807.08	0 - 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	-
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	31	55,597.97	55,430.68	-0.30	16	31,061.06	30,848.46	2 - 72
7	PETROLEUM	112	2,02,786.93	2,02,790.33	0.00	8	6,049.76	6,271.00	1 - 74
8	POWER	125	3,74,600.80	3,97,484.24	6.11	57	2,30,394.52	2,40,687.70	2 - 113
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	5	1,325.52	1,348.00	6 - 16
11	RAILWAYS	351	3,81,692.98	4,83,480.73	26.67	37	62,549.85	1,17,652.86	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,621.02	3,45,419.20	1.71	63	55,047.52	58,574.37	5 - 117
13	SHIPPING AND PORTS	10	4,582.25	5,535.92	20.81	3	774.39	1,527.36	20 - 141
14	TELECOMMUNICATIONS	9	16,959.47	28,189.47	66.22	2	13,752.26	25,082.26	9 - 47
15	URBAN DEVELOPMENT	34	1,44,866.57	1,44,035.91	-0.57	18	1,03,637.76	1,02,950.11	5 - 72
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	-
Total		1302	16,93,785.33	18,38,119.90	8.52	250	5,89,076.32	6,72,745.83	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	89,474.77	89,199.09	-0.31	7	19,411.53	20,221.55	4.17
4	FERTILISERS	2	692.29	703.44	1.61	1	482.85	494.00	2.31
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	31	55,597.97	55,430.68	-0.30	3	1,586.97	1,777.68	12.02
7	PETROLEUM	112	2,02,786.93	2,02,790.33	0.00	12	16,752.52	20,510.59	22.43
8	POWER	125	3,74,600.80	3,97,484.24	6.11	16	51,034.45	74,402.46	45.79
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	351	3,81,692.98	4,83,480.73	26.67	198	1,40,163.98	2,99,322.95	113.55
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,621.02	3,45,419.20	1.71	33	23,181.71	29,854.53	28.78
13	SHIPPING AND PORTS	10	4,582.25	5,535.92	20.81	5	1,219.00	2,172.77	78.24
14	TELECOMMUNICATIONS	9	16,959.47	28,189.47	66.22	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	34	1,44,866.57	1,44,035.91	-0.57	2	662.97	669.61	1.00
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	2	454.00	469.04	3.31
Total		1302	16,93,785.33	18,38,119.90	8.52	285	2,76,471.95	4,85,672.72	75.67

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	89,474.77	89,199.09	-0.31	5	1,777.44	2,541.33	6- 132
4	FERTILISERS	2	692.29	703.44	1.61	0	0.00	0.00	0- 0
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	31	55,597.97	55,430.68	-0.30	1	343.00	488.40	29- 29
7	PETROLEUM	112	2,02,786.93	2,02,790.33	0.00	3	1,188.26	1,409.50	15- 20
8	POWER	125	3,74,600.80	3,97,484.24	6.11	11	30,737.28	41,240.96	11- 111
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	10- 10
11	RAILWAYS	351	3,81,692.98	4,83,480.73	26.67	26	43,737.45	97,834.24	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,621.02	3,45,419.20	1.71	7	3,665.56	7,192.92	63- 112
13	SHIPPING AND PORTS	10	4,582.25	5,535.92	20.81	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	9	16,959.47	28,189.47	66.22	1	13,334.00	24,664.00	47- 47
15	URBAN DEVELOPMENT	34	1,44,866.57	1,44,035.91	-0.57	1	166.97	170.62	72- 72
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	0- 0
Total		1302	16,93,785.33	18,38,119.90	8.52	61	1,03,344.86	1,87,371.44	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	89,695.08	89,199.09	-0.55	6	1,929.87	3,000.82	6- 132
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	2- 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	31	55,217.00	55,430.68	0.39	2	545.61	715.40	12- 29
7	PETROLEUM	112	2,01,408.83	2,02,790.33	0.69	10	17,529.25	22,025.87	9- 70
8	POWER	125	3,38,658.41	3,97,484.24	17.37	36	85,911.47	1,23,456.70	3- 118
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	10- 10
11	RAILWAYS	351	3,53,800.77	4,83,480.73	36.65	27	27,085.68	99,616.22	33- 261
12	ROAD TRANSPORT AND HIGHWAYS	509	3,39,047.00	3,45,419.20	1.88	8	3,804.49	7,347.92	36- 112
13	SHIPPING AND PORTS	10	4,910.75	5,535.92	12.73	2	516.39	1,269.46	96- 141
14	TELECOMMUNICATIONS	9	16,952.95	28,189.47	66.28	1	13,334.00	24,664.00	47- 47
15	URBAN DEVELOPMENT	34	1,38,993.10	1,44,035.91	3.63	6	17,021.00	22,244.19	5- 70
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	0- 0
Total		1302	16,20,089.45	18,38,119.90	13.46	104	1,74,051.91	3,15,604.03	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

Table-13

State-Wise Position of Central Sector Projects costing Rs.150_Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	60	97,515.51	1,01,522.54	4.11	3	1,241.74	3,280.38	29 - 144
2	ARUNACHAL PRADESH	31	16,602.41	33,555.84	102.11	3	3,209.82	7,672.72	36 - 99
3	ASSAM	48	33,455.72	49,200.77	47.06	9	7,355.39	15,853.81	15 - 122
4	BIHAR	79	68,372.22	85,193.29	24.60	5	27,943.43	37,926.36	11 - 113
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	43	38,941.93	41,578.30	6.77	2	1,827.34	3,559.49	63 - 84
7	HARYANA	21	14,081.22	15,967.45	13.40	1	1,108.00	2,288.00	76 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	1	3,919.59	8,398.75	111 - 111
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	12 - 193
10	KARNATAKA	44	72,280.39	81,988.83	13.43	0	0.00	0.00	-
11	KERALA	21	21,774.25	27,871.82	28.00	1	607.06	714.25	17 - 17
12	MADHYA PRADESH	59	62,349.33	65,892.80	5.68	2	946.60	1,516.57	72 - 96
13	MAHARASHTRA	123	1,77,734.51	1,90,392.94	7.12	10	16,189.38	21,964.35	2 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	5	2,001.20	6,942.57	246.92	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	72	74,459.24	82,559.02	10.88	2	316.64	1,545.07	58 - 105
19	PUNJAB	28	15,555.77	15,561.50	0.04	0	0.00	0.00	-
20	RAJASTHAN	62	45,695.77	47,536.64	4.03	3	1,832.95	2,518.57	36 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	65	1,10,018.77	1,25,859.19	14.40	6	22,648.70	31,414.97	6 - 141
23	TRIPURA	11	4,400.64	9,067.42	106.05	2	1,015.95	3,678.00	12 - 72
24	UTTAR PRADESH	88	1,11,448.36	1,15,138.64	3.31	1	195.42	294.60	61 - 61
25	WEST BENGAL	55	56,532.37	71,188.94	25.93	4	11,601.45	13,775.87	9 - 57
26	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
27	DELHI	14	49,878.66	50,145.97	0.54	1	1,219.21	1,592.00	5 - 5
28	CHHATISGARH	38	82,769.79	84,960.97	2.65	3	2,223.98	3,243.20	40 - 93
29	JHARKHAND	47	46,513.55	50,225.71	7.98	2	1,161.75	1,513.89	99 - 166
30	UTTARAKHAND	14	17,481.68	32,916.29	88.29	3	4,749.74	8,051.41	58 - 84
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	36	24,952.57	27,674.71	10.91	4	1,463.44	2,104.31	33 - 132
33	MULTI STATE	183	3,02,573.52	3,00,732.55	-0.61	28	49,492.89	84,751.72	3 - 261
Total		1302	16,20,089.45	18,38,119.90	13.46	104	1,74,051.91	3,15,604.03	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-14

EXECUTIVE SUMMARY COSTING Rs. 1000 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	134	0
2	ROAD TRANSPORT AND HIGHWAYS	110	2
3	POWER	65	10
4	PETROLEUM	45	4
5	COAL	12	0
6	URBAN DEVELOPMENT	10	0
7	STEEL	9	1
8	ATOMIC ENERGY	4	0
9	TELECOMMUNICATIONS	2	0
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	394	17

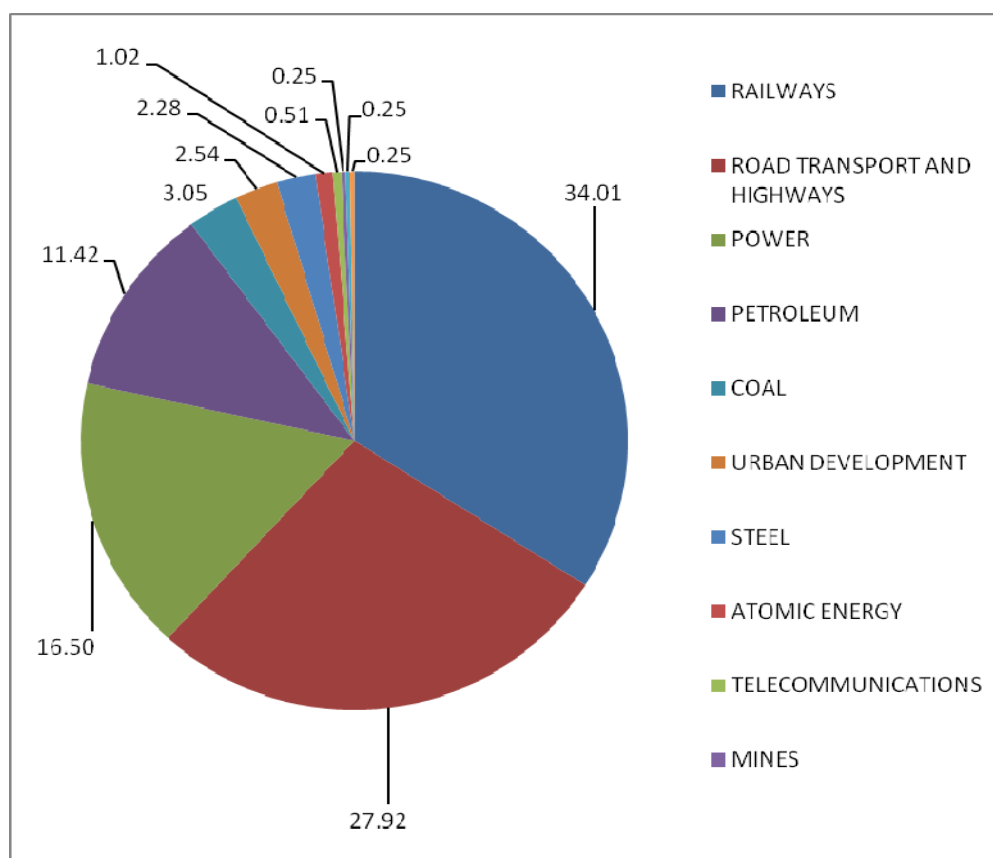


TABLE-15

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	387
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	6
No of Projects in Current Month	394

Project status Rs.100 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	126 (31.98%)	4 (1.02%)	87 (22.08%)	55 (13.96%)	122 (30.96%)	394
Latest Approved (Date)	106 (26.90%)	3 (.76%)	110 (27.92%)	52 (13.20%)	123 (31.22%)	394

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	321	10,66,475.80	11,68,216.14	3,89,683.15	33.40	1,01,740.34	9.50
Project with Revision in Cost	73	2,55,008.05	2,73,555.13	1,63,753.13	59.90	18,547.08	7.30
Total	394	13,21,483.85	14,41,771.27	5,53,436.28	38.39	1,20,287.42	9.10
Original Cost of All Projects							
Original Cost	394	12,50,917.13	14,41,771.27	5,53,436.28	38.39	1,90,854.14	15.26

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	126	5,64,485.37	6,96,117.11	4,04,063.05	58.00	1,31,631.74	23.30
Latest Approved (RCE)	106	5,31,656.27	6,10,617.17	3,42,925.68	56.20	78,960.90	14.90

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	17	1,07,753.14	1,21,749.14	93,044.78	76.40	13,996.00	13.00
Total	17	1,07,753.14	1,21,749.14	93,044.78	76.42	13,996.00	12.99

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs.1000_Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	45	1,73,778.98	1,75,531.15	1.01	11	25,469.28	31,113.81	22.16
6	POWER	65	3,14,747.99	3,71,925.17	18.17	27	97,751.62	1,54,928.80	58.49
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	134	2,72,733.80	3,78,603.18	38.82	93	95,772.36	2,59,526.11	170.98
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	2	15,819.21	20,650.00	30.54
Total		394	12,50,917.13	14,41,771.27	15.26	153	2,88,775.56	5,42,010.43	87.69

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	4	5,360.88	8,685.95	62.02
2	ARUNACHAL PRADESH	4	10,609.32	27,330.31	157.61	3	9,356.22	26,077.21	178.72
3	ASSAM	9	21,033.85	34,844.26	65.66	5	12,723.01	26,620.00	109.23
4	BIHAR	14	39,632.94	54,365.80	37.17	7	28,983.86	43,716.72	50.83
5	GUJARAT	10	23,570.79	26,172.48	11.04	3	3,221.99	5,823.68	80.75
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	4,966.47	12,898.75	159.72
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	355.99
9	KARNATAKA	20	60,672.06	69,275.41	14.18	11	7,389.10	16,751.45	126.70
10	KERALA	7	16,657.19	22,154.71	33.00	2	1,450.00	6,947.52	379.14
11	MADHYA PRADESH	16	39,844.82	44,152.48	10.81	7	5,860.60	10,168.26	73.50
12	MAHARASHTRA	45	1,46,268.44	1,57,238.87	7.50	20	36,453.02	51,807.77	42.12
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	2	988.06	5,929.43	500.11	2	988.06	5,929.43	500.11
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	24	56,093.98	63,001.08	12.31	7	5,666.20	12,573.30	121.90
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	37.84
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	10	24,589.22	39,230.47	59.54
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	34	87,539.87	90,087.41	2.91	8	25,275.08	28,277.20	11.88
24	WEST BENGAL	22	43,988.95	56,149.65	27.64	10	21,717.19	34,106.32	57.05
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	0.00
26	DELHI	4	45,462.73	45,689.52	0.50	1	1,219.21	1,592.00	30.58
27	CHHATISGARH	11	71,673.86	73,327.88	2.31	3	2,877.22	4,531.24	57.49
28	JHARKHAND	10	33,188.25	35,781.77	7.81	3	7,451.01	10,044.53	34.81
29	UTTARAKHAND	6	14,392.36	29,462.99	104.71	3	8,930.78	24,001.41	168.75
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	70	2,57,222.41	2,48,772.40	-3.29	28	54,795.85	1,01,334.33	84.93
Total		394	12,50,917.13	14,41,771.27	15.26	153	2,88,775.56	5,42,010.43	87.69

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above
(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	3	8,192.43	8,192.43	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	7	42,646.34	42,288.34	4 - 59
5	PETROLEUM	45	1,73,778.98	1,75,531.15	1.01	14	47,963.68	49,545.57	5 - 74
6	POWER	65	3,14,747.99	3,71,925.17	18.17	41	2,13,581.62	2,49,478.37	2 - 118
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	134	2,72,733.80	3,78,603.18	38.82	25	38,644.98	1,09,369.22	12 - 261
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	24	36,613.18	39,521.95	9 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47 - 47
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	6	94,671.14	99,501.93	5 - 29
Total		394	12,50,917.13	14,41,771.27	15.26	126	5,64,485.37	6,96,117.11	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	4	7,685.71	8,409.71	10 - 144
2	ARUNACHAL PRADESH	4	10,609.32	27,330.31	157.61	2	3,070.89	7,517.72	55 - 99
3	ASSAM	9	21,033.85	34,844.26	65.66	3	8,340.50	15,978.89	66 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	11 - 113
5	GUJARAT	10	23,570.79	26,172.48	11.04	3	14,357.72	16,086.49	45 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	5,836.38	10,315.54	15 - 111
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	6	19,130.27	47,361.54	12 - 193
9	KARNATAKA	20	60,672.06	69,275.41	14.18	3	43,226.34	43,226.34	13 - 19
10	KERALA	7	16,657.19	22,154.71	33.00	2	9,770.08	9,770.08	9 - 29
11	MADHYA PRADESH	16	39,844.82	44,152.48	10.81	3	13,338.65	13,681.45	16 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,238.87	7.50	14	49,672.70	53,293.11	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	24	56,093.98	63,001.08	12.31	7	23,811.71	24,830.55	7 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	3	14,823.44	15,137.40	48 - 74
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	8	70,204.64	78,441.19	9 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	34	87,539.87	90,087.41	2.91	3	20,622.72	20,622.72	4 - 26
24	WEST BENGAL	22	43,988.95	56,149.65	27.64	9	24,132.55	26,284.48	9 - 57
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	1	6,086.08	5,479.75	5 - 5
26	DELHI	4	45,462.73	45,689.52	0.50	3	41,198.73	41,571.52	5 - 25
27	CHHATISGARH	11	71,673.86	73,327.88	2.31	5	47,614.65	48,096.71	19 - 59
28	JHARKHAND	10	33,188.25	35,781.77	7.81	6	20,164.09	20,389.93	5 - 99
29	UTTARAKHAND	6	14,392.36	29,462.99	104.71	3	7,127.06	10,276.99	58 - 89
30	TELANGANA	6	14,904.53	16,572.01	11.19	1	1,266.60	1,266.60	18 - 18
31	MULTI STATE	70	2,57,222.41	2,48,772.40	-3.29	26	80,535.57	1,14,171.78	2 - 261
Total		394	12,50,917.13	14,41,771.27	15.26	126	5,64,485.37	6,96,117.11	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.
Cost Overrun = Anticipated Cost minus Original Cost

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	2	2,285.32	2,285.32	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	6	27,121.34	26,763.34	4 - 59
5	PETROLEUM	45	1,75,438.27	1,75,531.15	0.05	1	2,915.00	2,915.00	74 - 74
6	POWER	65	3,49,483.91	3,71,925.17	6.42	34	2,19,684.13	2,29,535.79	2 - 113
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
8	RAILWAYS	134	2,98,896.13	3,78,603.18	26.67	27	58,487.07	1,11,874.54	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	24	36,613.18	39,521.95	9 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47 - 47
12	URBAN DEVELOPMENT	10	1,38,291.23	1,37,453.93	-0.61	6	1,00,193.23	99,501.93	5 - 29
Total		394	13,21,483.85	14,41,771.27	9.10	106	5,31,656.27	6,10,617.17	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.
 Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

<u>Extent of cost overrun in projects with respect to latest schedule</u>						RS.1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	45	1,75,438.27	1,75,531.15	0.05	7	15,047.26	18,523.84	23.10
6	POWER	65	3,49,483.91	3,71,925.17	6.42	10	48,638.02	71,563.85	47.14
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	134	2,98,896.13	3,78,603.18	26.67	81	1,04,054.89	2,39,202.29	129.88
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	15	17,413.21	22,849.27	31.22
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	10	1,38,291.23	1,37,453.93	-0.61	0	0.00	0.00	0.00
Total		394	13,21,483.85	14,41,771.27	9.10	118	2,24,190.35	4,05,081.69	80.69

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	45	1,75,438.27	1,75,531.15	0.05	0	0.00	0.00	0- 0
6	POWER	65	3,49,483.91	3,71,925.17	6.42	7	29,432.98	39,495.14	11- 111
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	134	2,98,896.13	3,78,603.18	26.67	19	41,175.38	93,548.09	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	2	2,617.10	5,525.87	63- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47- 47
12	URBAN DEVELOPMENT	10	1,38,291.23	1,37,453.93	-0.61	0	0.00	0.00	0- 0
Total		394	13,21,483.85	14,41,771.27	9.10	31	93,954.46	1,73,160.40	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-23

<u>Extent of time & cost overrun in projects with respect to original schedule</u>						Rs.1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	45	1,73,778.98	1,75,531.15	1.01	5	15,828.24	19,562.62	9- 58
6	POWER	65	3,14,747.99	3,71,925.17	18.17	21	80,003.60	1,15,900.35	11- 118
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
8	RAILWAYS	134	2,72,733.80	3,78,603.18	38.82	20	24,605.82	95,330.07	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	110	1,60,068.25	1,65,504.31	3.40	2	2,617.10	5,525.87	63- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	47- 47
12	URBAN DEVELOPMENT	10	1,32,769.14	1,37,453.93	3.53	2	15,819.21	20,650.00	5- 24
	Total	394	12,50,917.13	14,41,771.27	15.26	53	1,57,417.97	2,91,560.21	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.

Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

State-Wise Position of Central Sector Projects costing Rs. 100 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	1	743.00	1,825.00	144 - 144
2	ARUNACHAL PRADESH	4	10,609.32	27,330.31	157.61	2	3,070.89	7,517.72	55 - 99
3	ASSAM	9	21,033.85	34,844.26	65.66	2	5,875.35	13,600.00	79 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	11 - 113
5	GUJARAT	10	23,570.79	26,172.48	11.04	1	1,509.10	3,237.87	63 - 63
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	1	3,919.59	8,398.75	111 - 111
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	12 - 193
9	KARNATAKA	20	60,672.06	69,275.41	14.18	0	0.00	0.00	-
10	KERALA	7	16,657.19	22,154.71	33.00	0	0.00	0.00	-
11	MADHYA PRADESH	16	39,844.82	44,152.48	10.81	1	687.20	1,030.00	96 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,238.87	7.50	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,929.43	500.11	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	24	56,093.98	63,001.08	12.31	1	183.23	1,202.07	58 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	57 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	4	21,811.42	30,047.97	24 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	34	87,539.87	90,087.41	2.91	0	0.00	0.00	-
24	WEST BENGAL	22	43,988.95	56,149.65	27.64	3	11,432.55	13,584.49	9 - 57
25	D & N HAVELI	1	6,086.08	5,479.75	-9.96	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,689.52	0.50	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	11	71,673.86	73,327.88	2.31	1	1,746.65	2,228.71	40 - 40
28	JHARKHAND	10	33,188.25	35,781.77	7.81	1	900.05	1,125.89	99 - 99
29	UTTARAKHAND	6	14,392.36	29,462.99	104.71	2	4,635.48	7,785.41	58 - 84
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	70	2,57,222.41	2,48,772.40	-3.29	14	44,032.44	77,668.65	23 - 261
Total		394	12,50,917.13	14,41,771.27	15.26	53	1,57,417.97	2,91,560.21	

Time Overrun = Anticipated Date of Commissioning minus Original Date of Commissioning.
Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

<u>List of projects completed/dropped/Frozen during current month</u> Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	PUFNADIH OCP (3.0 MTY)	07/2008	210.98	03/2013	210.98	12/2017	206.80
	<u>HEALTH AND FAMILY WELFARE</u>						
2	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	444.70	12/2015	444.70	12/2017	326.30
3	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	01/2016	209.00	12/2017	170.00
	<u>STEEL</u>						
4	3RD CONVERTER AND 4TH CASTER	07/2011	974.76	07/2016	974.76	12/2017	676.93

TABLE-26

List of projects added Rs 150 Crore and above						
(December 2017)						
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	4,006.83	5/2021	4,006.83	5/2021
	<u>POWER</u>					
2	NAITWAR MORI HEP	10/2017	648.33	12/2021	648.33	12/2021
	<u>RAILWAYS</u>					
3	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	119.73	3/2022	184.97	3/2022
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
4	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	950.27	/	950.27	-
5	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	379.90	/	379.90	-
6	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	1,308.73	/	1,308.73	-
7	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	1,232.21	/	1,232.21	-
8	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	404.94	/	404.94	-
9	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	2,598.00	/	2,598.00	-
10	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	686.65	/	686.65	-
11	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	417.51	/	417.51	-
12	CONSTRUCTION OF STAND ALONE RING ROAD/	12/2017	1,471.75	/	1,471.75	-

List of projects added Rs 150 Crore and above

(December 2017)

			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE					
13	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	328.67	/	328.67	-
14	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	1,323.15	/	1,323.15	-
15	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	357.00	/	357.00	-
16	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	207.00	/	207.00	-
17	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	305.00	/	305.00	-

TABLE-27

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		3962	
Achieved up to month		2125	

TABLE-28

<u>List of projects reporting additional delayed Rs. 150 Crore and above</u>							
(December 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI SOLAR POWER PROJECT 130 MW NLC	687.28	767.00	06/2017	10/2017	12/2017	2
	<u>FERTILISERS</u>						
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. RCF	482.85	494.00	12/2017	12/2017	02/2018	2
	<u>STEEL</u>						
3	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	12/2017	02/2018	2
4	CENTRAL DISPATCH YARD RINL	320.66	320.66	08/2018	08/2018	10/2018	2
5	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) RINL	465.85	465.85	07/2018	07/2018	09/2018	2
	<u>PETROLEUM</u>						
6	PARADIP LPG IMPORT FACILITY IOCL	690.00	690.00	07/2018	07/2020	08/2020	1
7	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY CPCL Central Sector Projects	367.11	367.11	04/2017	12/2017	01/2018	1
8	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,256.72	05/2013	12/2017	03/2018	3
9	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS ONGC	4,124.35	5,637.00	04/2016	12/2017	03/2018	3
10	DHAMRA-ANGUL PIPELINE PROJECT GAIL	1,933.00	2,253.00	12/2020	12/2019	12/2020	12
11	DOBHI-DURGAPUR PIPELINE PROJECT GAIL	2,433.00	2,250.00	12/2020	12/2019	12/2020	12
	<u>POWER</u>						
12	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	8,150.00	09/2011	03/2018	04/2018	1
13	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,932.88	12/2012	02/2018	03/2018	1

List of projects reporting additional delayed Rs. 150 Crore and above

(December 2017)


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	882.13	11/2014	02/2018	03/2018	1
15	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) NTPC	11,846.00	11,846.00	06/2017	12/2018	01/2019	1
16	EASTERN REGION STRENGTHENING SCHEME-III PGCIL	1,272.80	1,731.10	11/2012	12/2017	02/2018	2
17	KUDGI STPP STAGE 1 NTPC	15,166.19	15,166.19	01/2017	12/2017	02/2018	2
18	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B PGCIL	155.57	206.42	03/2016	01/2018	03/2018	2
19	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM PGCIL	162.11	162.11	05/2018	01/2018	03/2018	2
20	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) SJVN	330.00	330.00	11/2017	12/2017	02/2018	2
21	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,891.41	04/2016	03/2018	06/2018	3
22	TANDA TPP STAGE-II (2X660 MW) NTPC	9,188.98	9,188.98	03/2019	06/2019	09/2019	3
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP PGCIL	268.80	340.88	03/2018	03/2018	06/2018	3
24	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I NTPC	11,638.55	11,638.55	09/2017	09/2018	01/2019	4
25	DARLIPALLI STPP STAGE-I (2X800 MW) NTPC	12,532.44	12,532.44	08/2018	11/2018	03/2019	4
26	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT SJVN	436.68	602.44	12/2016	12/2017	12/2018	12
27	BARH STPP(3X660MW) NTPC	8,692.97	15,095.67	01/2011	03/2019	06/2020	15
	<u>HEALTH AND FAMILY WELFARE</u>						
28	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR HSCC	505.58	505.58	03/2018	03/2018	09/2018	6
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
29	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER NHAI	946.00	946.00	N.A.	03/2018	06/2018	3

List of projects reporting additional delayed Rs. 150 Crore and above


(December 2017)

		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
30	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 NHAI PPP (BOT)	1,250.00	1,250.00	12/2013	12/2017	12/2018	12
31	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB NHAI	1,664.20	1,664.20	N.A.	04/2019	04/2020	12

Graphical Presentation of All Projects w.r.t. Original Schedule

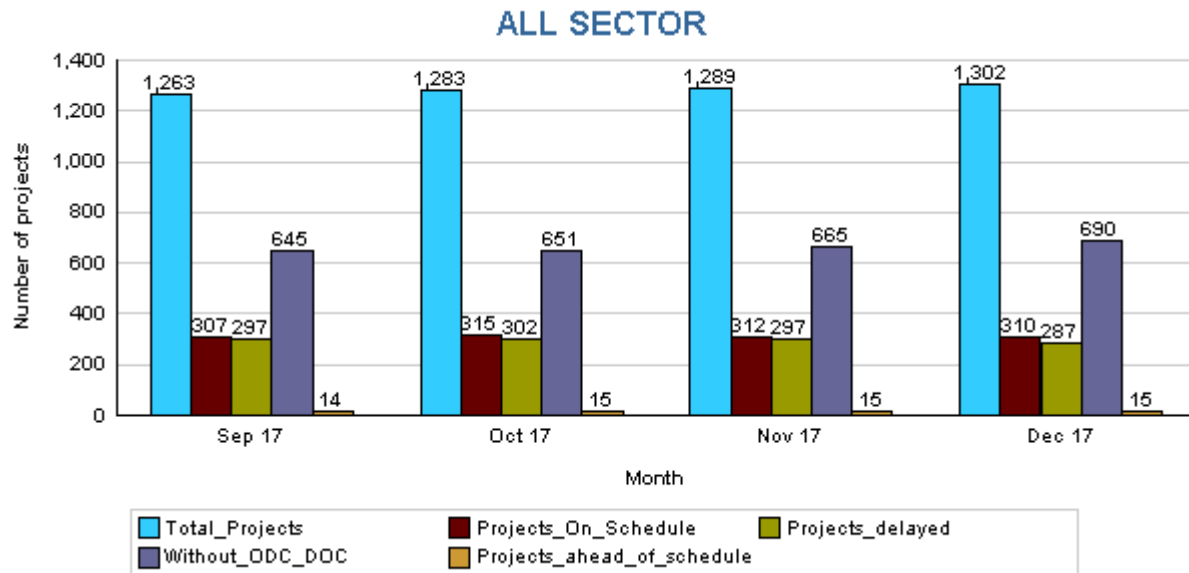

Break-up of 287 Delayed projects in December 2017

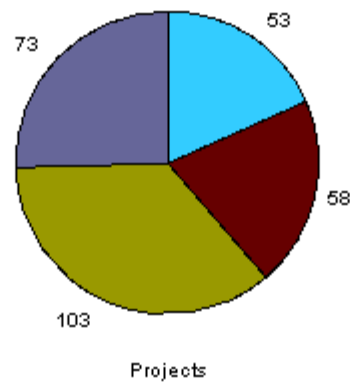

Delay in Months



Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

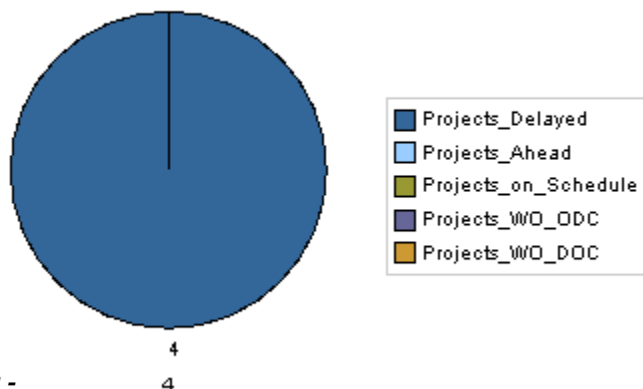


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 69728 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till December, 2017 is Rs. 27419.63 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

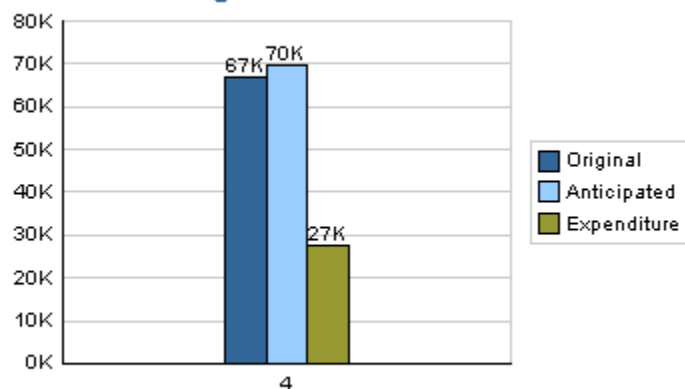

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

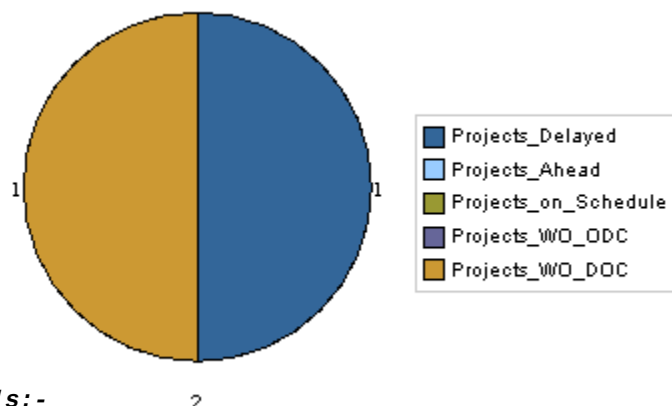


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till December, 2017 is Rs. 549.39 crore, which is 55.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

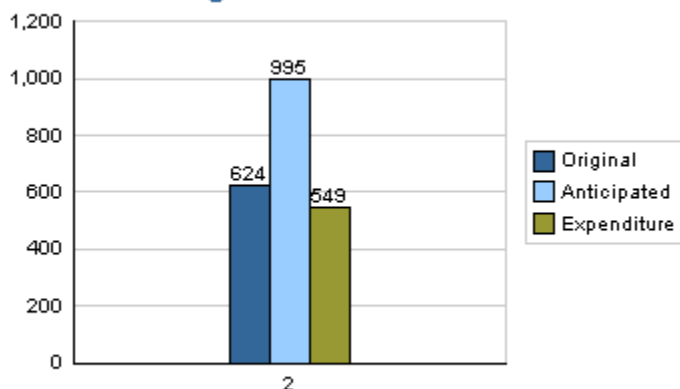

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	92
Number of Projects On Schedule	51
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 1 project is ahead of schedule, 51 projects are on schedule 37 projects are delayed. 3 projects do not have fixed dates of commissioning.

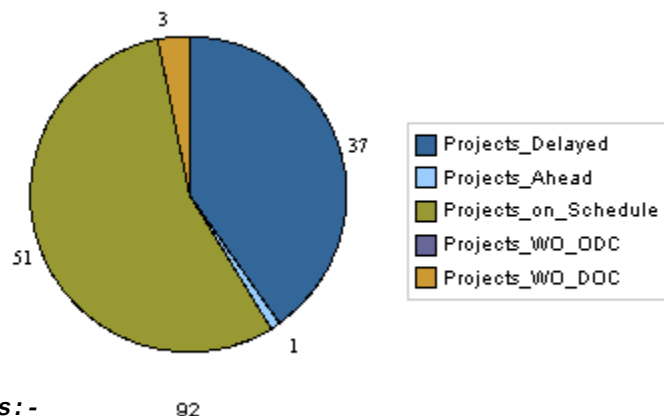


Total No Of Project's:-

92

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 89695.08 crore but this was subsequently anticipated to Rs. 89199.09 cr The expenditure incurred on these projects till December, 2017 is Rs. 22387.17 crore, which is 25.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

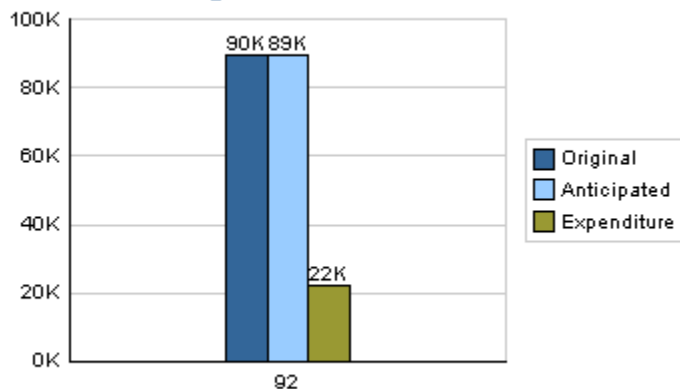

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

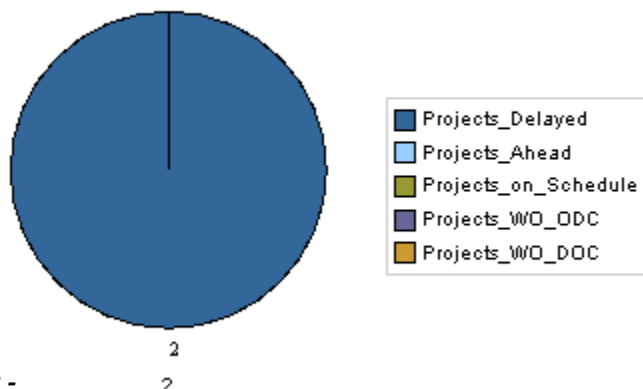


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till December, 2017 is Rs. 516.36 crore, which is 73.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

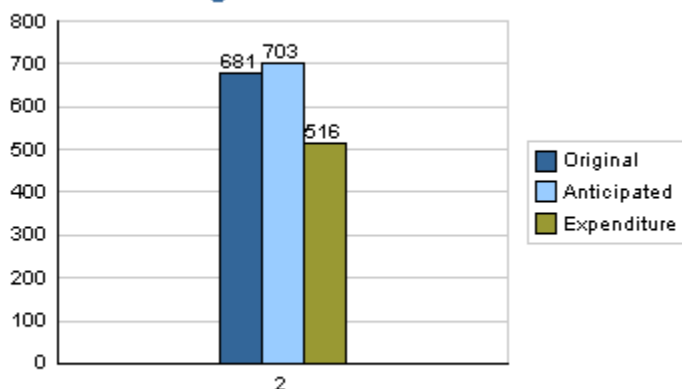

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till December, 2017 is Rs. 344.73 crore, which is 5% of the anticipated cost of the projects.

Figures are in Rs. Crore

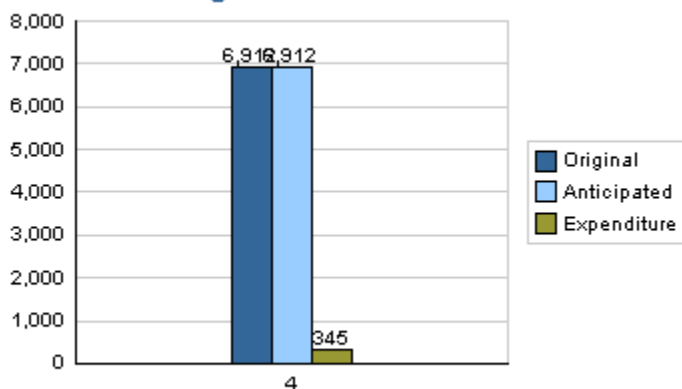

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	31
Number of Projects On Schedule	5
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 31 projects, 5 projects are on schedule 17 projects are delayed. 8 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

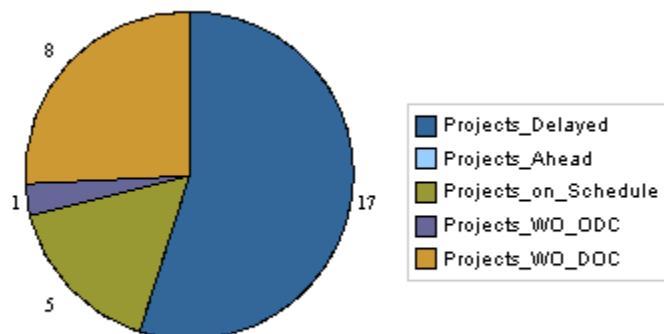


Total No Of Project's:-

31

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 55217 crore but this was subsequently anticipated to Rs. 55430.68 crore implying a cost overrun of .4%. The expenditure incurred on these projects till December, 2017 is Rs. 39041.51 crore, which is 70.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

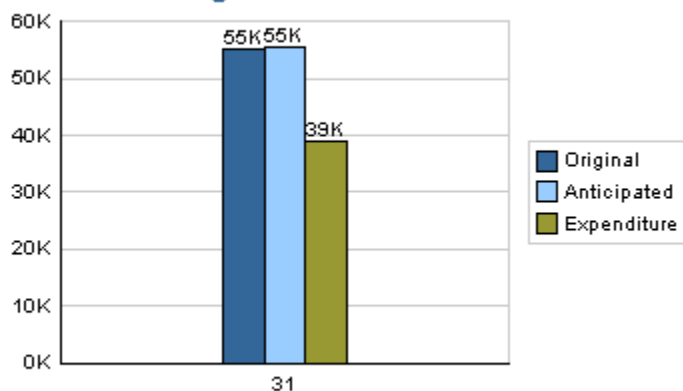

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	112
Number of Projects On Schedule	66
Number of Projects Delayed	30
Number of Projects Ahead	8
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 112 projects, 8 projects are ahead of schedule, 66 projects are on schedule 30 projects are delayed. 8 projects do not have fixed dates of commissioning.

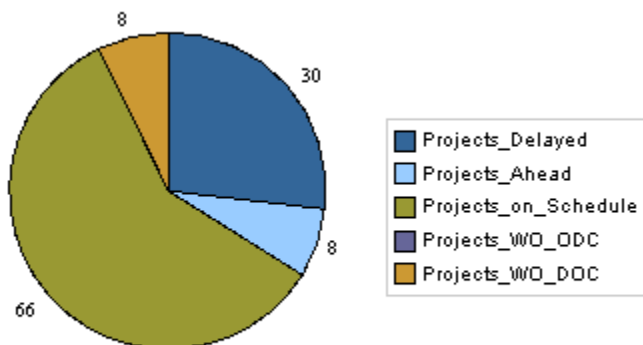


Total No Of Project's:-

112

Investment Scenario

Total original cost of implementation of 112 projects when sanctioned, was of the order of Rs. 201408.83 crore but this was subsequently anticipated to Rs. 202790.33 crore implying a cost overrun of .7%. The expenditure incurred on these projects till December, 2017 is Rs. 57163.11 crore, which is 28.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

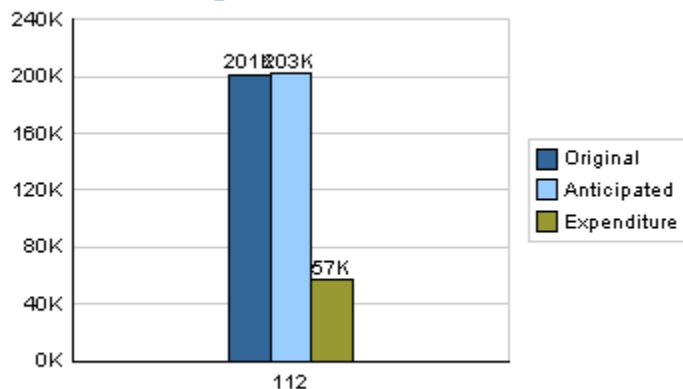

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	125
Number of Projects On Schedule	48
Number of Projects Delayed	65
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 125 projects, 2 projects are ahead of schedule, 48 projects are on schedule 65 projects are delayed. 10 projects do not have fixed dates of commissioning.

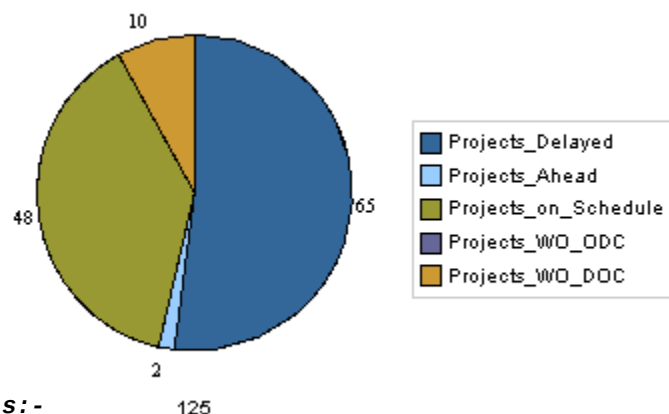


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 125 projects when sanctioned, was of the order of Rs. 338658.41 crore but this was subsequently anticipated to Rs. 397484.24 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till December, 2017 is Rs. 230686.08 crore, which is 58% of the anticipated cost of the projects.

Figures are in Rs. Crore

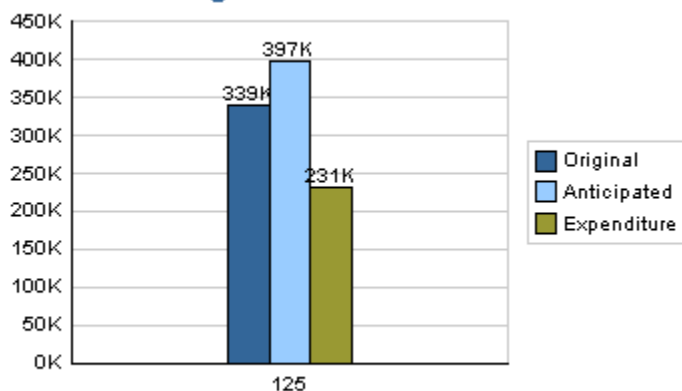

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

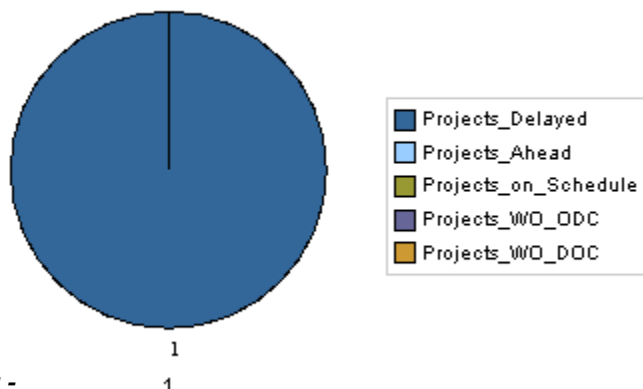


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till December, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

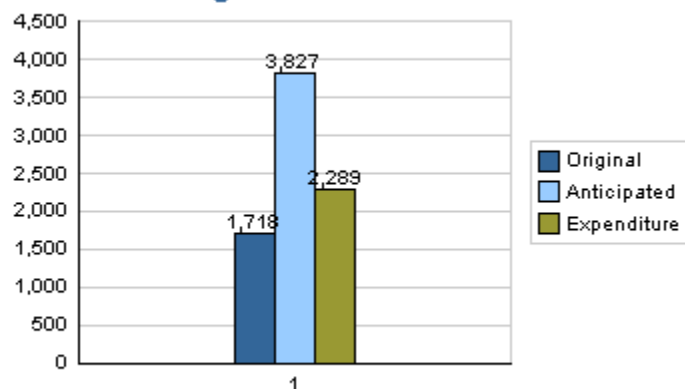

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	14
Number of Projects On Schedule	5
Number of Projects Delayed	6

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 5 projects are on schedule 6 projects are delayed. 3 projects do not have fixed dates of commissioning.

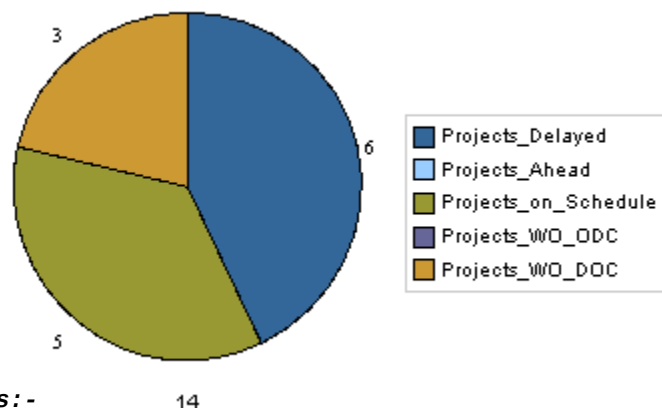


Total No Of Project's:-

14

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 3897.21 crore but this was subsequently anticipated to Rs. 3919.69 crore implying a cost overrun of .6%. The expenditure incurred on these projects till December, 2017 is Rs. 1507.4 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

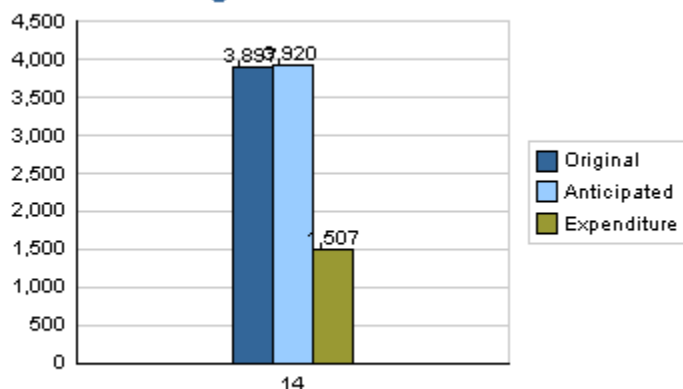

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	351
Number of Projects On Schedule	39
Number of Projects Delayed	34
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	80
Number of Projects Without Date Of Commissioning	197

Brief Analysis


Project Status with respect to Original Schedule: Out of 351 projects, 1 project is ahead of schedule, 39 projects are on schedule 34 projects are delayed. 197 projects do not have fixed dates of commissioning. 80 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

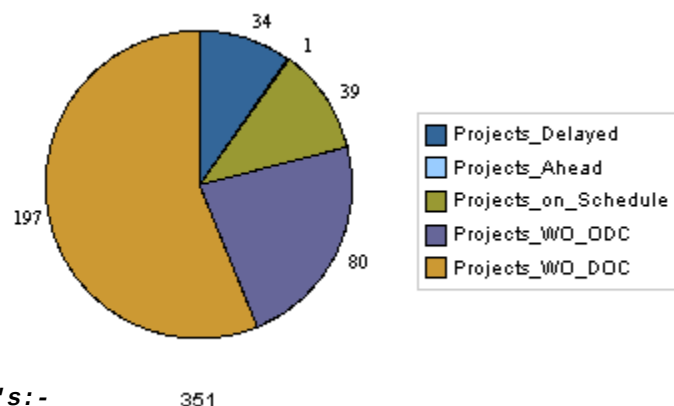

Investment Scenario

Total original cost of implementation of 351 projects when sanctioned, was of the order of Rs. 353800.77 crore but this was subsequently anticipated to Rs. 483480.73 crore implying a cost overrun of 36.7%. The expenditure incurred on these projects till December, 2017 is Rs. 142505.66 crore, which is 29.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

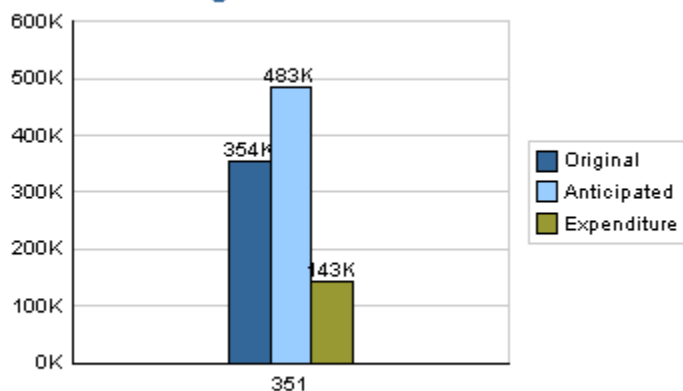

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	509
Number of Projects On Schedule	77
Number of Projects Delayed	63
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	66
Number of Projects Without Date Of Commissioning	301

Brief Analysis

Project Status with respect to Original Schedule: Out of 509 projects, 2 projects are ahead of schedule, 77 projects are on schedule 63 projects are delayed. 301 projects do not have fixed dates of commissioning. 66 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

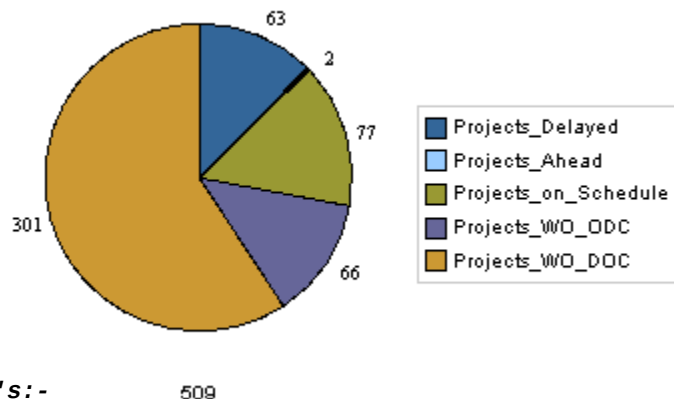


Total No Of Project's:-

509

Investment Scenario

Total original cost of implementation of 509 projects when sanctioned, was of the order of Rs. 339047 crore but this was subsequently anticipated to Rs. 345419.2 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till December, 2017 is Rs. 62454.56 crore, which is 18.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

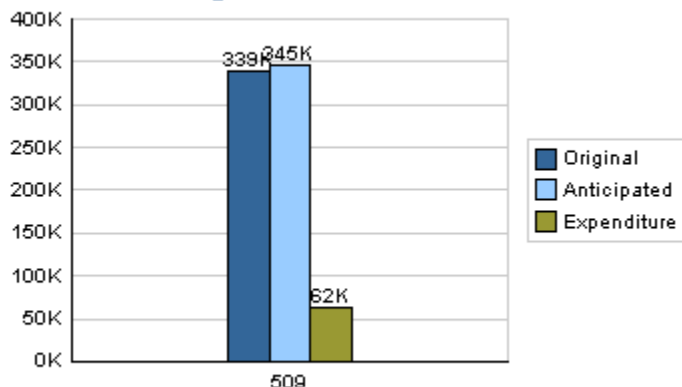

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	10
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 2 projects are on schedule 3 projects are delayed. 5 projects do not have fixed dates of commissioning.

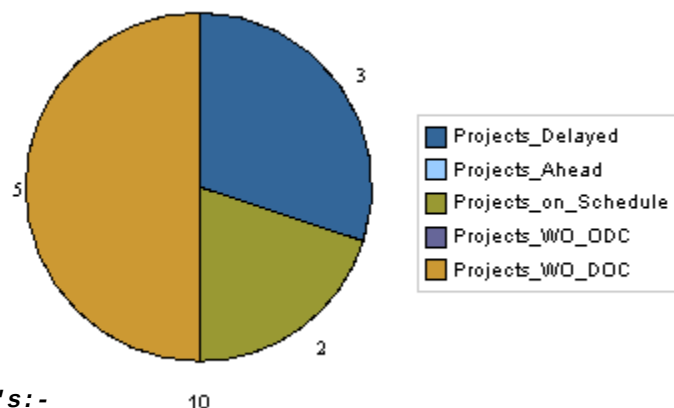


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 4910.75 crore but this was subsequently anticipated to Rs. 5535.92 crore implying a cost overrun of 12.7%. The expenditure incurred on these projects till December, 2017 is Rs. 2068.38 crore, which is 37.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

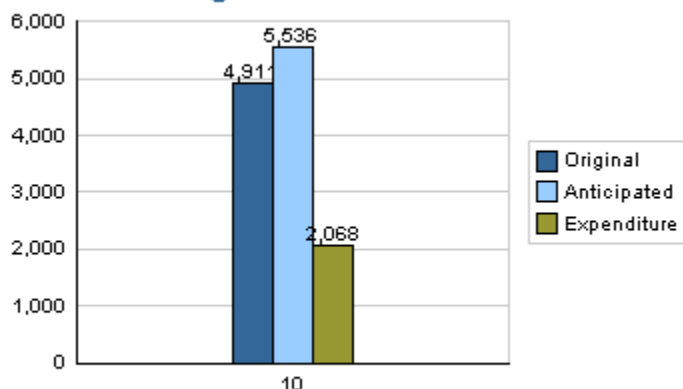

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	9
Number of Projects On Schedule	5
Number of Projects Delayed	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is ahead of schedule, 5 projects are on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

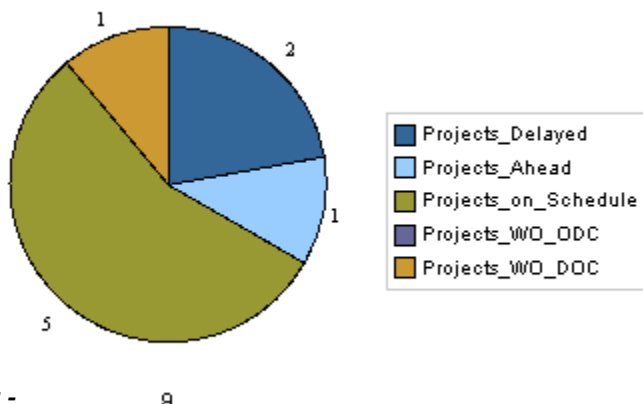


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 16952.95 crore but this was subsequently anticipated to Rs. 28189.47 crore implying a cost overrun of 66.3%. The expenditure incurred on these projects till December, 2017 is Rs. 7086.2 crore, which is 25.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

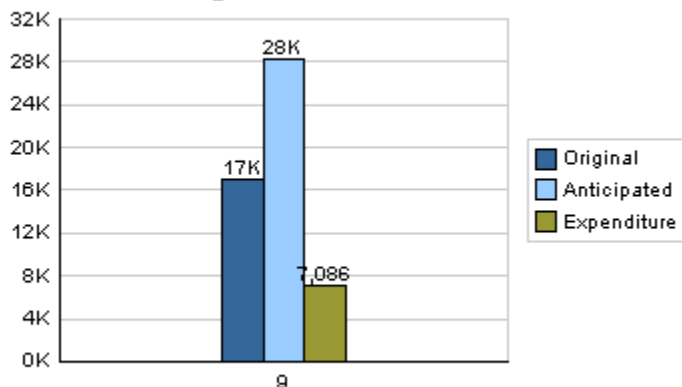

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	34
Number of Projects On Schedule	6
Number of Projects Delayed	22

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 6 projects are on schedule 22 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

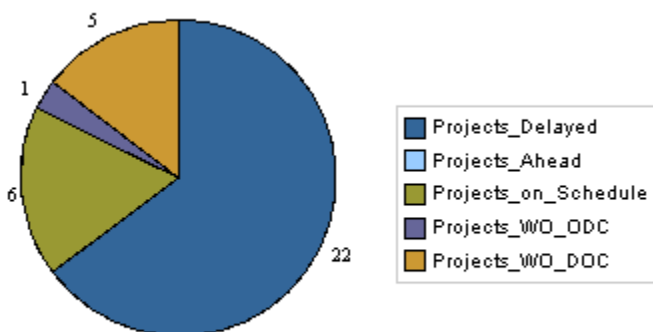


Total No Of Project's:-

34

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 138993.1 crore but this was subsequently anticipated to Rs. 144035.91 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till December, 2017 is Rs. 62590.76 crore, which is 43.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

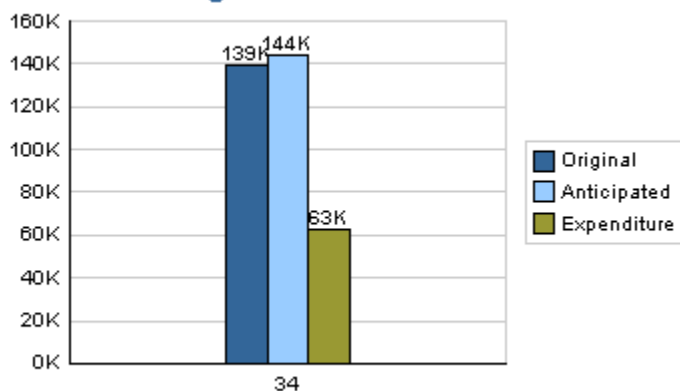

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till December, 2017 is Rs. 70.86 crore, which is 15.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

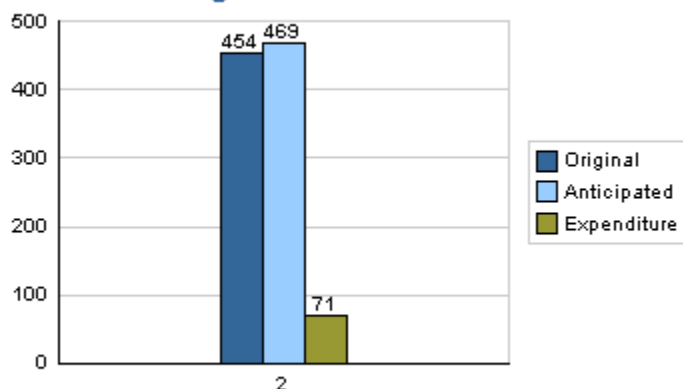


TABLE-29

<u>Sector wise analysis of projects</u> Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	69,728.00	27,419.63
CIVIL AVIATION	2	624.07	6,24.07	994.86	549.39
COAL	92	89,695.08	894,74.77	89,199.09	22,387.17
FERTILISERS	2	680.64	6,92.29	703.44	516.36
MINES	4	6,912.00	69,12.00	6,912.00	344.73
STEEL	31	55,217.00	555,97.97	55,430.68	39,041.51
PETROLEUM	112	2,01,408.83	2,027,86.93	2,02,790.33	57,163.11
POWER	125	3,38,658.41	3,746,00.80	3,97,484.24	2,30,686.08
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	14	3,897.21	38,97.21	3,919.69	1,507.40
RAILWAYS	351	3,53,800.77	3,816,92.98	4,83,480.73	1,42,505.66
ROAD TRANSPORT AND HIGHWAYS	509	3,39,047.00	3,396,21.02	3,45,419.20	62,454.56
SHIPPING AND PORTS	10	4,910.75	45,82.25	5,535.92	2,068.38
TELECOMMUNICATIONS	9	16,952.95	169,59.47	28,189.47	7,086.20
URBAN DEVELOPMENT	34	1,38,993.10	1,448,66.57	1,44,035.91	62,590.76
DEFENCE PRODUCTION	2	453.64	4,54.00	469.04	70.86
Grand total	1302	16,20,089.45	16,93,785.33	18,38,119.90	6,58,680.80

TABLE-30

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	11,088.00	12/2015 11/2016	11/2019	47(O) 36(R)	46/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	8,666.00	12/2016 03/2017	12/2020	48(O) 45(R)	35/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,100.00	5,532.63	09/2010 09/2016	06/2018	93(O) 21(R)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36(O) -	0/0
	Total		67,120.00 -	69,728.00	27,419.63				164/225
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT , PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	522.95	01/2011 09/2017	10/2017	-	0/0
	Total		624.07 -	994.86	549.39				0/0
	<u>COAL</u>								
7	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,563.46	03/2023 -	03/2023	0(O) -	13/17
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,444.26	03/2023 -	03/2023	0(O) -	4/19
9	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023	0(O) -	1/11
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	135.12	03/2015 03/2020	03/2020	60(O) 0(R)	2/8
11	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	199.85	03/2014 -	03/2018	48(O) -	0/3
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24(O) -	6/8
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	153.43	03/2016 -	03/2018	24(O) -	4/7
15	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022	0(O) -	1/8
16	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	49.19	03/2020 -	03/2020	0(O) -	3/7
17	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	48.78	03/2018 -	03/2018	0(O) -	1/6

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	38.29	03/2020 -	03/2020	0(O) -	0/5
19	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	.57	03/2023 -	03/2023	0(O) -	1/9
20	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/3
21	VIJAY WEST OPENCAS PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/0
22	MAGADH OC 20 MTY (CCL) - [N06000015]JCLL,JHARKHAND ,	08/2008	706.40 -	706.40	120.77	07/2012 03/2017	03/2021	104(O) 48(R)	2/4
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	05/2017	-	6/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]JCLL,JHARKHAND ,	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108(O) -	2/4
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCLL,JHARKHAND ,	12/2007	179.87 -	179.87	98.06	03/2012 -	03/2019	84(O) -	2/4
26	TAPIN OCP (2.5 MTY) - [N06000086]JCLL,JHARKHAND ,	08/2008	264.68 -	264.68	153.85	03/2012 -	03/2019	84(O) -	2/4
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCLL,JHARKHAND ,	12/2009	510.85 -	510.85	347.32	03/2016 -	03/2018	24(O) -	2/4
28	KARMA OCP (1.0MTY) - [N06000088]JCLL,JHARKHAND ,	06/2009	162.46 -	162.46	84.15	03/2014 -	03/2019	60(O) -	2/4
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	207.23	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]JCLL,JHARKHAND ,	02/2012	858.11 -	858.11	175.94	03/2020 -	03/2020	0(O) -	4/5
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	156.92	05/2014 -	04/2018	47(O) -	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	153.87	04/2014 -	04/2018	48(O) -	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	38.57	03/2022 -	03/2022	0(O) -	1/21
37	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 -	486.57	397.54	03/2012 -	03/2018	72(O) -	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	69.04	03/2023 -	03/2021	-24(O) -	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	115.62	03/2021 -	03/2021	0(O) -	1/8
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021	0(O) -	1/7
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	1/6

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	111.56	03/2021 -	03/2021	0(O) -	2/3
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	12.79	03/2022 -	03/2022	0(O) -	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	31.42	03/2021 -	03/2021	0(O) -	0/0
47	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	176.03	03/2020 -	03/2020	0(O) -	6/11
48	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	368.02	03/2020 -	03/2020	0(O) -	2/8
49	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	138.85	03/2021 -	03/2021	0(O) -	9/12
50	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	204.93	03/2018 -	03/2018	0(O) -	7/7
51	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	72.23	03/2023 02/2017	03/2023	0(O) 73(R)	7/11
52	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	88.13	03/2019 -	03/2019	0(O) -	10/13
53	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	70.86	03/2020 -	03/2020	0(O) -	5/10
54	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	72.65	03/2021 -	03/2021	0(O) -	2/6
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	231.76	03/2025 -	03/2025	0(O) -	3/13
56	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
57	KAMPTTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	.42	03/2021 -	03/2021	0(O) -	2/6
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020	0(O) -	2/6
59	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	39.89	03/2019 -	03/2019	0(O) -	2/9
60	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	126.57	03/2019 -	03/2019	0(O) -	1/8
61	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	199.31	03/2020 -	03/2020	0(O) -	0/0
62	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	.04	03/2022 -	03/2022	0(O) -	0/3
63	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	-	03/2022 -	03/2022	0(O) -	0/12
64	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	47.85	03/2021 -	03/2021	0(O) -	1/6
65	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	331.06	03/2010 -	03/2018	96(O) -	9/10
66	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	282.30	03/2017 -	05/2018	14(O) -	11/12
67	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	405.44	03/2013 -	11/2018	68(O) -	8/9

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	195.09	03/2010 -	03/2019	108(O) -	3/4
69	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	259.50	03/2012 -	03/2019	84(O) -	4/5
70	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	221.47	03/2013 -	03/2019	72(O) -	5/8
71	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	25.13	03/2019 -	03/2019	0(O) -	2/9
72	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026	0(O) -	3/15
73	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	30.12	03/2019 -	03/2019	0(O) -	3/6
74	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	2/5
75	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	370.58	03/2021 -	03/2021	0(O) -	3/9
76	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	5.69	09/2019 -	09/2019	0(O) -	0/0
77	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	167.34	12/2019 -	12/2019	0(O) -	0/0
78	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	5,039.57	12/2015 04/2018	04/2018	28(O) 0(R)	16/35
79	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	320.01	06/2015 09/2019	09/2019	51(O) 0(R)	4/7
80	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 -	767.00	733.23	06/2017 -	12/2017	6(O) -	0/0
81	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	163.85	03/2012 -	03/2019	84(O) -	32/42
82	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
83	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132(O) -	0/2
84	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	144.33	03/2015 -	03/2018	36(O) -	29/31
85	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72(O) -	5/6
86	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	.34	03/2015 -	03/2020	60(O) -	0/5
87	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60(O) -	4/29
88	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	437.51	267.42	03/2015 -	03/2021	72(O) -	5/13
89	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	121.94	06/2015 -	03/2018	33(O) -	27/36
90	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	417.33	67.63	07/2016 -	03/2020	44(O) -	19/28
91	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	147.18	03/2016 -	03/2018	24(O) -	33/39
92	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	47.29	03/2019 -	03/2019	0(O) -	6/18

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
93	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9
94	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
95	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	430.99	03/2018 -	03/2018	0(O) -	6/10
96	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	1,184.47	11/2021 -	11/2021	0(O) -	0/0
97	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	284.27	03/2022 -	03/2022	0(O) -	6/12
98	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	321.06	03/2018 -	03/2020	24(O) -	8/15
	Total		89,695.08 -	89,199.09	22,387.17				402/900
	<u>FERTILISERS</u>								
99	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	103.35	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
100	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 -	494.00	413.01	12/2017 02/2018	02/2018	2(O) 0(R)	0/1
	Total		680.64 -	703.44	516.36				1/14
	<u>MINES</u>								
101	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	44.60	04/2021 04/2021	04/2021	0(O) 0(R)	2/2
102	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	286.25	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
103	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 355.00	355.00	13.88	11/2020 11/2020	11/2020	0(O) 0(R)	1/1
104	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	-	04/2021 04/2021	04/2021	0(O) 0(R)	0/0
	Total		6,912.00 -	6,912.00	344.73				4/5
	<u>STEEL</u>								
105	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	234.69	10/2016 -	03/2019	29(O) -	0/2
106	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
107	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	715.85	12/2017 -	10/2018	10(O) -	0/2

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	23.78	08/2018 -	10/2018	2(O) -	0/2
109	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	53.91	07/2018 -	09/2018	2(O) -	0/3
110	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
111	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	18,303.09	03/2013 -	02/2018	59(O) -	35/38
112	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	114.58	04/2015 -	-	-	4/5
113	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	13,054.00	05/2015 10/2018	10/2018	41(O) 0(R)	55/86
114	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020	0(O) -	4/12
115	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	12/2017	- -	0/0
116	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND ,	10/2013	245.67 -	245.67	196.21	05/2016 -	12/2017	19(O) -	3/3
117	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND ,	03/2015	255.19 -	255.19	168.02	03/2018 -	03/2018	0(O) -	1/2
118	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	200.59	10/2017 -	07/2018	9(O) -	0/2
119	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	528.08	12/2017 -	05/2018	5(O) -	1/2
120	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	75.63	09/2017 -	-	-	0/0
121	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
122	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
123	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
124	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
125	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019	0(O) -	0/1
126	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
127	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
128	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
129	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA ,	04/2015	3,127.30 -	3,127.30	1,837.55	04/2018 -	02/2019	10(O) -	1/3
130	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN ,	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
131	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
132	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12(O) -	0/0
133	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
134	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	63.94	09/2018 -	01/2019	4(O) -	0/3
135	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES (ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		55,217.00 -	55,430.68	39,041.51				104/166
	<u>PETROLEUM</u>								
136	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/1
137	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL, ANDHRA PRADESH ,	09/2016	407.00 -	407.00	39.60	09/2019 09/2019	09/2019	0(O) 0(R)	18/27
138	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020	0(O) 0(R)	0/0
139	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH ,	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0
140	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH ,	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0
141	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH ,	04/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
142	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL, ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	53.50	02/2019 -	12/2018	-2(O) -	2/10
143	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM ,	03/2009	2,465.15 -	2,378.89	2,065.39	03/2013 09/2018	09/2018	66(O) 0(R)	5/15
144	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP) - [N16000127]ONGC, ASSAM ,	06/2010	202.94 341.70	330.35	5.63	01/2014 11/2019	11/2019	70(O) 0(R)	0/2
145	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM ,	03/2009	228.64 -	256.41	147.19	12/2016 -	03/2018	15(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
146	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018	0(O) -	46/61
147	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	91.45	08/2019 -	08/2019	0(O) -	2/13
148	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	316.80	11/2019 -	11/2019	0(O) -	5/17
149	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020	0(O) 0(R)	0/0
150	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	960.00	03/2015 -	11/2017	-	0/5
151	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	272.86	11/2018 -	11/2018	0(O) -	3/8
152	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	215.86	12/2020 -	02/2020	-10(O) -	1/2
153	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	11.35	06/2020 -	06/2020	0(O) -	2/2
154	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,479.75	5,479.75	2,236.63	05/2019 10/2019	10/2019	5(O) 0(R)	0/0
155	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT ,	09/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018	23(O) 0(R)	5/12
156	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	367.84	11/2019 12/2018	12/2018	-11(O) 0(R)	0/0
157	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	157.51	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
158	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	124.98	03/2018 -	03/2018	0(O) -	16/22
159	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	15.92	04/2018 -	04/2018	0(O) -	15/20
160	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT ,	02/2016	931.00 -	931.00	435.08	07/2017 -	02/2018	7(O) -	6/7
161	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	207.09	03/2026 03/2026	03/2026	0(O) 0(R)	0/0
162	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	16.93	07/2020 -	07/2020	0(O) -	0/0
163	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018	0(O) -	0/0
164	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	81.33	05/2019 -	12/2018	-5(O) -	1/13
165	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	32.65	09/2019 -	09/2019	0(O) -	2/2
166	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 06/2017	06/2017	-	8/12
167	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	5.87	03/2023 03/2022	03/2022	-12(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL, KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	11/2017	-	0/0
169	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	542.00	02/2020 -	02/2020	0(O) -	0/0
170	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN, KARNATAKA ,	05/2015	224.00 207.00	207.25	55.76	04/2019 -	04/2019	0(O) -	5/8
171	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN, KARNATAKA ,	10/2015	135.00 170.70	170.70	88.68	03/2019 -	03/2019	0(O) -	4/11
172	BSVI UPGRADATION - [N16000257]MANGALORE REFIN, KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	57.29	12/2019 -	12/2019	0(O) -	7/9
173	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA ,	10/2015	607.06 -	714.25	276.85	10/2017 -	03/2019	17(O) -	36/52
174	PALAKKAD LPG PLANT - [N16000225]BPCL, KERALA ,	02/2015	184.00 -	184.00	89.85	12/2017 -	12/2017	0(O) -	0/10
175	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA ,	11/2014	4,588.29 5,245.96	4,588.29	1,025.00	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
176	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA ,	02/2016	3,313.00 -	3,313.00	89.27	02/2020 -	02/2020	0(O) -	0/0
177	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA ,	05/2015	337.06 -	337.06	24.35	08/2018 -	08/2018	0(O) -	0/0
178	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	164.86	01/2017 03/2018	03/2018	14(O) 0(R)	0/0
179	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,183.39	05/2013 03/2018	03/2018	58(O) 0(R)	1/5
180	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA ,	12/2011	2,059.63 -	2,665.65	1,671.57	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
181	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA ,	03/2012	2,592.17 -	2,592.17	2,084.15	05/2014 05/2018	05/2018	48(O) 0(R)	0/21
182	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12(O) 0(R)	7/16
183	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,306.72	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
184	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA ,	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12(O) 0(R)	0/0
185	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	593.82	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
186	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	3,480.50	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
187	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	1,163.47	04/2018 04/2018	04/2018	0(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.


(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	185.08	08/2021 -	08/2021	0(O) -	2/2
189	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	32.34	02/2020 -	02/2020	0(O) -	0/0
190	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	97.51	12/2019 -	12/2019	0(O) -	0/0
191	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	12.13	01/2019 -	01/2019	0(O) -	0/0
192	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0(O) -	0/0
193	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0
194	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
195	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
196	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	155.33	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
197	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
198	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	-	11/2019 -	11/2019	0(O) -	0/0
199	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 -	968.61	-	11/2019 -	11/2019	0(O) -	0/0
200	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,006.83	123.41	05/2021 -	05/2021	0(O) -	0/0
201	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,397.00	3,397.00	1,548.90	12/2018 -	12/2018	0(O) -	28/39
202	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	542.65	09/2011 06/2019	06/2019	93(O) 0(R)	0/0
203	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 06/2017	06/2017	-	8/8
204	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE ,	04/2012	600.17 -	600.17	703.97	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
205	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,052.91	06/2018 -	06/2018	0(O) -	1/1
206	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	422.29	10/2014 03/2018	03/2018	41(O) 0(R)	29/40

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
207	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	134.50	03/2017 -	11/2018	20(O) -	0/0
208	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 4,259.59	5,637.00	4,050.69	04/2016 03/2018	03/2018	23(O) 0(R)	0/3
209	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	127.28	12/2020 -	12/2020	0(O) -	0/0
210	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	64.86	12/2020 -	08/2020	-4(O) -	1/2
211	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	262.60	10/2019 -	10/2019	0(O) -	2/3
212	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	133.91	07/2018 08/2020	08/2020	25(O) 0(R)	11/36
213	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	312.83	06/2020 -	06/2020	0(O) -	8/24
214	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	16.95	02/2019 -	02/2019	0(O) -	6/13
215	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	1.06	10/2020 -	10/2020	0(O) -	0/0
216	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	7.09	12/2019 -	12/2019	0(O) -	0/0
217	LAYING OF VIJAIIPUR-AURAIYA PIPELINE SECTION OF VIJAIIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,881.40	12.07	12/2019 -	12/2019	0(O) -	9/24
218	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,250.00	18.19	12/2020 -	12/2020	0(O) -	10/24
219	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,212.00	6.30	12/2020 -	12/2020	0(O) -	9/24
220	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	2,915.00	1,469.29	12/2012 -	02/2019	74(O) -	7/42
221	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	-	03/2021 -	03/2021	0(O) -	0/0
222	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	1,546.59	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
223	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	173.17	03/2017 10/2017	10/2017	-	6/6
224	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	2,253.00	14.19	12/2020 -	12/2020	0(O) -	13/24
225	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	70.83	01/2019 -	01/2019	0(O) -	2/6
226	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019	0(O) -	0/0

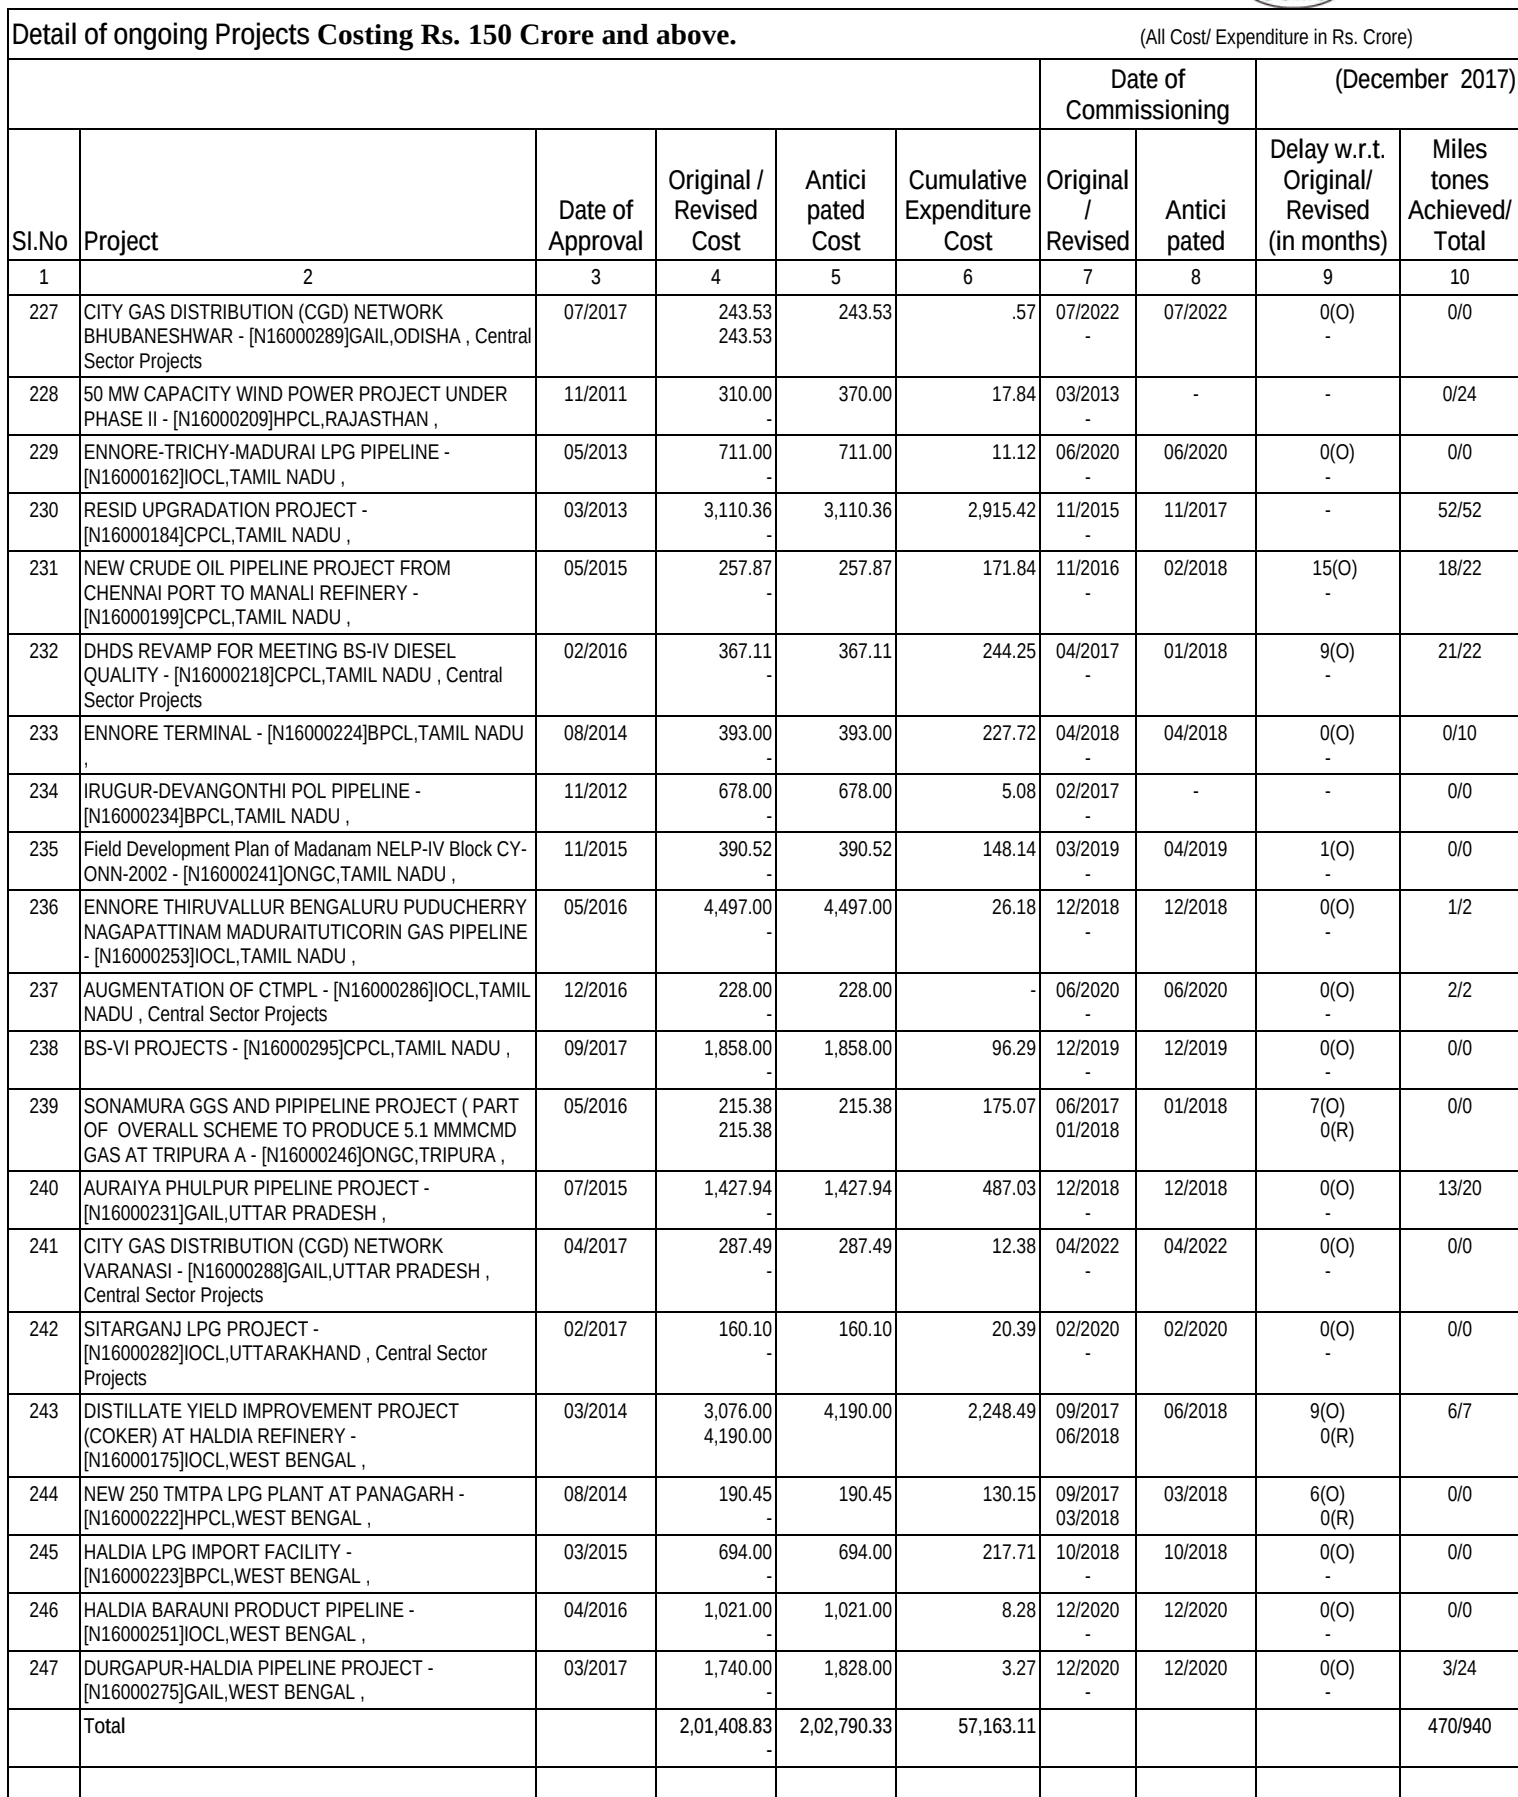

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
248	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	98.02	07/2018 -	01/2018	-6(O) -	0/0
249	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	18,559.49	9,610.95	09/2010 -	-	-	0/0
250	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,099.06	12/2009 03/2018	03/2018	99(O) 0(R)	18/30
251	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH ,	12/2008	573.99 1,337.76	1,337.76	1,544.55	08/2013 03/2018	03/2018	55(O) 0(R)	32/38
252	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	6,860.00	09/2011 06/2017	04/2018	79(O) 10(R)	31/37
253	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	13,932.00	01/2011 05/2018	06/2020	113(O) 25(R)	26/47
254	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57(O) 17(R)	2/18
255	NPGCL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11(O) -	27/31
256	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	478.69	12/2016 -	12/2018	24(O) -	10/16
257	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.30	342.29	06/2019 -	06/2019	0(O) -	0/0
258	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH ,	12/2011	1,746.65 2,228.71	2,228.71	1,971.62	08/2014 12/2017	12/2017	40(O) 0(R)	11/11
259	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	11,846.00	8,892.00	06/2017 12/2017	01/2019	19(O) 13(R)	33/40
260	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	41.97	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
261	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	32.97	10/2018 -	10/2018	0(O) -	0/0
262	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	51.97	12/2018 -	12/2018	0(O) -	0/0
263	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	186.30	11/2017 -	02/2018	3(O) -	1/4
264	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	4.99	09/2018 -	09/2018	0(O) -	0/0
265	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,597.22	09/2009 -	12/2018	111(O) -	2/3
266	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,882.01	5,186.86	01/2016 -	02/2018	25(O) -	6/6
267	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	881.41	04/2020 12/2017	06/2023	38(O) 66(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
268	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,213.54	09/2017 -	09/2018	12(O) -	0/0
269	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	14,366.58	5,674.00	02/2019 02/2020	09/2020	19(O) 7(R)	18/21
270	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND ,	08/2006	2,313.00 4,138.41	4,366.64	3,484.00	12/2011 03/2016	02/2017	-	14/14
271	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,361.82	10/2017 12/2016	12/2016	-	0/0
272	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	15,166.19	14,795.00	01/2017 07/2017	02/2018	13(O) 7(R)	47/48
273	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	-	02/2019 -	02/2019	0(O) -	0/0
274	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	11,638.55	8,413.00	09/2017 03/2018	01/2019	16(O) 10(R)	32/41
275	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019	0(O) -	22/24
276	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	165.34	03/2017 10/2017	01/2018	10(O) 3(R)	0/0
277	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	81.99	06/2018 -	06/2018	0(O) -	0/0
278	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	38.90	09/2020 -	09/2020	0(O) -	9/16
279	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	570.00	06/2018 -	06/2018	0(O) -	0/0
280	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	653.52	09/2010 12/2017	06/2018	93(O) 6(R)	5/8
281	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 03/2017	03/2017	-	41/41
282	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,206.00	11/2016 12/2017	12/2018	25(O) 12(R)	34/38
283	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects	04/2015	2,225.00 2,225.00	2,225.00	1,033.00	01/2018 -	01/2018	0(O) -	0/0
284	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM ,	07/1998	368.72 1,329.43	1,329.43	1,337.43	07/2006 11/2017	11/2017	-	13/13
285	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,489.03	10/2012 02/2018	06/2018	68(O) 4(R)	8/11
286	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,575.15	08/2013 12/2017	02/2018	54(O) 2(R)	22/26
287	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,589.80	12/2012 02/2018	03/2018	63(O) 1(R)	16/23

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
288	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE ,	02/2010	232.34 -	341.00	246.39	06/2012 -	01/2018	67(O) -	1/4
289	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,425.08	11/2012 12/2017	02/2018	63(O) 2(R)	10/13
290	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	485.99	06/2014 03/2018	09/2018	51(O) 6(R)	10/12
291	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 346.79	426.29	364.29	08/2014 12/2017	03/2018	43(O) 3(R)	8/10
292	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	136.45	09/2014 09/2017	03/2018	42(O) 6(R)	0/0
293	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE ,	11/2011	723.63 882.13	882.13	727.62	11/2014 06/2017	03/2018	40(O) 9(R)	7/10
294	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 703.10	703.10	585.89	06/2015 12/2017	05/2018	35(O) 5(R)	7/10
295	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	2,514.88	2,048.50	12/2015 12/2017	06/2018	30(O) 6(R)	15/18
296	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,174.49	04/2016 09/2017	06/2018	26(O) 9(R)	8/12
297	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	121.98	04/2016 12/2017	03/2018	23(O) 3(R)	0/0
298	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	393.44	06/2016 02/2018	06/2018	24(O) 4(R)	9/11
299	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE ,	02/2014	908.08 969.97	969.97	732.28	06/2016 02/2018	12/2017	18(O) -2(R)	18/18
300	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE ,	05/2014	829.98 -	829.98	419.93	08/2016 10/2017	12/2017	16(O) 2(R)	4/4
301	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	374.70	11/2016 11/2017	03/2018	16(O) 4(R)	8/12
302	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	140.76	03/2016 07/2017	03/2018	24(O) 8(R)	4/6
303	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	1,707.65	03/2018 -	06/2018	3(O) -	9/12
304	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 -	376.09	231.75	02/2017 06/2017	03/2018	13(O) 9(R)	7/12
305	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	134.45	02/2016 08/2017	03/2018	25(O) 7(R)	15/17
306	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36	3,557.86	04/2018 -	04/2018	0(O) -	3/12
307	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	169.37	03/2018 -	06/2018	3(O) -	0/3
308	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	06/2018	8(O) 8(R)	0/5
309	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	168.86	07/2017 -	12/2018	17(O) -	3/5

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	58.24	03/2018 -	03/2018	0(O) -	0/0
311	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	477.43	09/2017 -	09/2018	12(O) -	0/0
312	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,296.77	04/2018 -	07/2018	3(O) -	5/9
313	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30	733.18	04/2017 03/2018	03/2018	11(O) 0(R)	6/8
314	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	834.84	07/2018 -	07/2018	0(O) -	0/0
315	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	758.15	07/2018 -	07/2018	0(O) -	0/0
316	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	243.37	01/2018 -	03/2019	14(O) -	0/0
317	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	60.40	11/2018 -	11/2018	0(O) -	0/0
318	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	600.02	05/2019 -	05/2019	0(O) -	0/0
319	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	812.04	11/2019 -	11/2019	0(O) -	0/0
320	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	411.76	12/2018 -	12/2018	0(O) -	0/0
321	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	50.40	11/2018 -	11/2018	0(O) -	0/0
322	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	37.81	07/2018 -	07/2018	0(O) -	0/0
323	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	171.22	03/2019 -	03/2019	0(O) -	0/0
324	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	.77	02/2019 -	02/2019	0(O) -	0/0
325	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	10.95	02/2019 -	02/2019	0(O) -	0/0
326	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	18.56	03/2019 -	03/2019	0(O) -	0/0
327	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	-	06/2019 -	06/2019	0(O) -	0/0
328	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE ,	10/2016	167.75 -	167.75	7.82	04/2019 -	04/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	7.71	11/2019 -	11/2019	0(O) -	0/0
330	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	51.76	01/2019 -	01/2019	0(O) -	0/0
331	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	11.77	04/2019 -	04/2019	0(O) -	0/0
332	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(O) -	0/0
333	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	15.59	02/2019 -	02/2019	0(O) -	0/0
334	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	1.43	03/2019 -	03/2019	0(O) -	0/0
335	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	7.29	06/2019 -	06/2019	0(O) -	0/0
336	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	19.67	12/2019 -	12/2019	0(O) -	0/0
337	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	7.45	09/2019 -	09/2019	0(O) -	0/0
338	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	322.43	04/2020 -	04/2020	0(O) -	0/0
339	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	6.00	06/2019 -	06/2019	0(O) -	0/0
340	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	4,754.42	466.74	12/2018 -	12/2019	12(O) -	0/0
341	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	5,111.33	386.29	12/2018 -	12/2019	12(O) -	0/0
342	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 1,161.00	1,364.00	1,091.00	12/2015 -	03/2018	27(O) -	0/0
343	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,565.00	11/2017 -	01/2018	2(O) -	0/0
344	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	1,043.00	04/2019 -	04/2019	0(O) -	0/0
345	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	109.00	07/2020 -	07/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
346	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	-	02/2020 -	02/2020	0(O) -	0/0
347	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	12,532.44	6,615.00	08/2018 -	03/2019	7(O) -	26/32
348	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	137.00	04/2019 -	04/2019	0(O) -	0/0
349	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	176.23	11/2017 -	06/2018	7(O) -	0/0
350	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN ,	02/2015	302.49 302.00	302.49	270.77	02/2016 -	-	-	1/1
351	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	163.78	01/2019 -	01/2019	0(O) -	0/0
352	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	1,969.63	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
353	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,357.64	09/2014 06/2017	03/2018	42(O) 9(R)	11/13
354	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU ,	01/2016	162.11 -	162.11	119.40	05/2018 -	03/2018	-2(O) -	0/0
355	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU ,	06/2017	287.48 -	287.48	28.79	03/2018 -	03/2018	0(O) -	0/0
356	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	8.00	07/2019 -	07/2019	0(O) -	0/0
357	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	1,106.00	07/2020 -	07/2020	0(O) -	13/18
358	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 1,078.31	1,078.31	963.23	07/2013 -	-	-	26/26
359	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA ,	05/2016	409.19 -	409.19	66.46	05/2018 -	05/2018	0(O) -	0/0
360	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
361	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	3,400.00	03/2019 -	09/2019	6(O) -	19/28
362	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	148.06	02/2014 02/2018	03/2019	61(O) 13(R)	4/5
363	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26(O) -	29/34
364	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	3,939.11	2,443.93	02/2016 09/2019	12/2020	58(O) 15(R)	16/26
365	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,359.00	03/2013 06/2019	03/2020	84(O) 9(R)	3/15
366	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	2,491.58	1,312.24	06/2013 -	11/2020	89(O) -	8/11

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
367	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 1,801.07	1,527.00	148.00	08/2017 -	-	-	0/15
368	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	-	12/2021 -	12/2021	0(O) -	0/0
369	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL ,	04/2010	4,404.57 5,135.01	5,135.01	3,488.99	01/2015 03/2018	03/2018	38(O) 0(R)	14/16
370	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 1,592.34	1,381.84	294.00	09/2019 -	03/2021	18(O) -	5/8
371	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL ,	04/2007	4,122.00 8,781.30	9,142.58	8,300.00	02/2011 -	03/2016	-	26/26
372	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	147.51	04/2018 -	04/2018	0(O) -	0/0
	Total		3,38,658.41 -	3,97,484.24	2,30,686.08				890/1161
	<u>HEAVY INDUSTRY</u>								
373	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
374	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	24.38	03/2019 -	03/2019	0(O) -	0/0
375	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
376	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
377	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13(O) -	0/2
378	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16(O) -	0/5
379	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6(O) -	0/2
380	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	312.99	149.00	08/2018 -	08/2018	0(O) -	0/1
381	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	29.68	03/2019 -	03/2019	0(O) -	0/0
382	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	21.00	05/2018 08/2019	08/2019	15(O) 0(R)	0/0
383	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6(O) -	0/1
384	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	158.65	11/2013 09/2017	09/2017	-	0/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
385	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL ,	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10(O) -	0/3
386	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL ,	08/2016	244.00 -	244.00	77.50	09/2018 -	09/2018	0(O) -	0/0
387	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	21.79	03/2019 -	03/2019	0(O) -	0/0
	Total		3,897.21 -	3,919.69	1,507.40				0/22
	<u>RAILWAYS</u>								
388	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH ,	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106(O) -	0/0
389	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH ,	12/2001	330.00 -	2,125.18	14.17	- -	03/2021	- -	0/0
390	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH ,	04/2003	136.62 -	380.00	379.63	12/2007 03/2010	03/2017	-	0/0
391	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	1,478.11	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
392	GUDUR-DURGARAJAPATNAM - [N220000265]SCR, ANDHRA PRADESH ,	04/2011	283.54 -	759.41	.51	- -	-	-	0/0
393	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.48	- -	-	-	0/1
394	NADIKUDE-SRI KALAHASTI - [N220000286]SCR, ANDHRA PRADESH ,	04/2011	1,313.48 -	1,313.48	8.06	- -	-	-	0/1
395	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N220000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	566.74	- -	03/2020	- -	0/0
396	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	-	- -	-	-	0/0
397	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	4,000.00 -	3,631.00	-	- -	-	-	0/0
398	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	-	- -	-	-	0/0
399	KOTTAVALSA - KORAPUT DOUBLING - [N220000377]ECOR, ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	37.12	03/2021 -	03/2022	12(O) -	0/0
400	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N220000424]CCOI, ANDHRA PRADESH ,	01/2013	387.70 -	387.70	361.35	03/2018 -	03/2018	0(O) -	0/0
401	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N220000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	234.50	.39	03/2019 -	03/2019	0(O) -	0/0
402	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM ,	09/1997	1,500.00 -	5,450.00	4,892.39	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
403	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086]NFR, ASSAM ,	09/2006	200.00 -	780.00	436.01	- -	03/2020	- -	0/0
404	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM ,	04/1998	227.90 -	509.00	417.62	12/2012 -	05/2016	-	0/0
405	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N220000127]NFR, ASSAM ,	04/1996	1,676.31 -	7,300.00	7,137.21	03/2009 -	11/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
406	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	535.00	509.15	- -	03/2019	- -	0/0
407	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	115.62	- -	03/2019	- -	0/0
408	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM ,	04/2003	971.22 -	966.27	834.11	- -	12/2009	- -	0/0
409	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM ,	04/2003	4,300.00 -	4,520.00	4,440.32	- -	08/2015	- -	0/0
410	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM ,	04/2007	180.09 -	180.00	157.12	- -	05/2011	- -	0/0
411	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.00	68.44	- -	03/2022	- -	0/0
412	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	871.00	25.71	- -	03/2021	- -	0/0
413	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
414	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	919.92	12/2010 -	-	-	0/0
415	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
416	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
417	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
418	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
419	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	412.05	364.40	- -	03/2018	- -	0/0
420	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
421	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,135.00	921.36	- -	03/2020	- -	0/0
422	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	- -	03/2020	- -	0/0
423	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	490.80 -	490.80	.39	- -	-	-	0/0
424	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
425	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0
426	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
427	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
428	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
429	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
430	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
431	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
432	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
433	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
434	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
435	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
436	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
437	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
438	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
439	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	-	- -	-	-	0/0
440	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(O) -	0/1
441	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
442	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
443	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	1,141.70	509.95	12/2012 -	-	-	0/0
444	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	555.00	500.67	03/2010 -	12/2017	93(O) -	0/3
445	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	466.17	- -	03/2020	-	0/1
446	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	671.78	03/2020 -	03/2020	0(O) -	0/0
447	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	145.79	03/2018 -	03/2018	0(O) -	0/0
448	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
449	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
450	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84(O) -	0/0
451	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45(O) -	0/0
452	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84(O) -	0/0
453	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
454	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	361.26	- -	03/2020	- -	0/0
455	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	36.97	- -	12/2020	- -	0/0
456	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	845.68	.78	- -	-	-	0/0
457	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	399.63	-	- -	03/2019	- -	0/0
458	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,548.66	442.97	- -	12/2020	- -	0/0
459	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	- -	0/0
460	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 -	355.00	323.64	- -	-	-	0/0
461	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	- -	0/0
462	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	245.96	03/2019 -	03/2019	0(O) -	0/0
463	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
464	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	- -	-	-	0/0
465	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	- -	-	-	0/0
466	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA ,	05/2015	400.00 -	400.00	-	- -	-	-	0/0
467	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	208.87	03/2019 -	03/2019	0(O) -	0/0
468	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	4,500.00	110.45	- -	03/2019	- -	0/0
469	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193(O) -	0/0
470	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 111(R)	0/0
471	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 -	491.33	548.77	06/2004 -	-	-	0/0
472	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
473	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	388.00	343.71	02/2006 -	12/2019	166(O) -	0/1
474	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	207.11	03/2012 -	-	-	0/0
475	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	583.00	402.65	12/2015 -	-	-	0/0
476	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	98.37	- -	12/2017	- -	0/0
477	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	105.32	12/2016 -	-	-	0/0
478	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
479	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	133.91	- -	-	-	0/0
480	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA ,	02/1998	242.42 369.70	1,542.41	927.68	- 05/2009	-	-	0/1
481	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	6.12	- -	-	-	0/0
482	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA ,	04/2007	482.00 -	874.57	992.03	03/2013 -	-	-	0/0
483	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 -	1,801.01	2.56	- -	-	-	0/0
484	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 -	1,350.91	799.73	- -	-	-	0/1
485	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	274.85	- -	-	-	0/1
486	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	- -	-	-	0/0
487	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 -	832.47	.94	- -	-	-	0/0
488	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.35	- -	-	-	0/0
489	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	847.70	- -	03/2019	-	0/1
490	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	-	-	0/0
491	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	6.28	- -	-	-	0/0
492	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	- -	-	-	0/0
493	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	3.57	01/1999 -	-	-	0/0
494	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	481.99	- 03/2020	-	-	0/5
495	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	324.71	- 11/2015	03/2020	- 52(R)	0/2
496	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 -	2,815.62	240.68	- -	01/2018	-	0/0
497	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	7.74	- -	-	-	0/0
498	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	378.76	- -	-	-	0/0
499	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.28	- -	12/2017	-	0/0
500	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	4,131.90	-	- -	-	-	0/0
501	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	- -	-	-	0/0
502	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 727.13	2,713.09	-	- -	03/2021	-	0/0
503	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
504	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH ,	09/2007	687.20 -	1,030.00	1,020.64	03/2010 -	03/2018	96(O) -	0/0
505	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 -	1,030.29	628.11	03/2012 -	-	-	0/0
506	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
507	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.85	718.67	12/2020 -	12/2020	0(O) -	0/0
508	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022	0(O) -	0/1
509	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	582.13	-	03/2020 -	03/2020	0(O) -	0/1
510	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	103.59	03/2019 -	03/2019	0(O) -	0/0
511	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.97	703.51	06/1999 -	-	-	0/0
512	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	678.01	03/2004 -	03/2020	192(O) -	0/0
513	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	1,386.59	-	03/2021	-	0/0
514	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60(O) -	0/0
515	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
516	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 2,491.43	3,168.29	734.00	-	03/2023	-	0/0
517	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	213.92	-	03/2021	-	0/0
518	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	146.86	-	03/2019	-	0/0
519	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	123.73	-	03/2022	-	0/0
520	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	.74	-	03/2024	-	0/0
521	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	1.99	-	03/2024	-	0/0
522	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	-	-	03/2024	-	0/0
523	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	57.85	-	03/2022	-	0/0
524	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 2,449.91	2,449.91	18.91	-	03/2023	-	0/0
525	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	17.13	-	03/2024	-	0/0
526	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	-	-	03/2023	-	0/0
527	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 1,035.16	1,035.16	2.04	-	03/2023	-	0/0
528	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 637.95	637.95	2.37	-	03/2022	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
529	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,750.00	1,237.34	03/2020 -	03/2020	0(O) -	0/0
530	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.16	12/2025 -	12/2025	0(O) -	0/0
531	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
532	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	221.08	03/2019 -	03/2019	0(O) -	0/0
533	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 -	9,658.00	6,985.58	03/2011 -	03/2020	108(O) -	0/0
534	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	255.59	-	03/2021	-	0/0
535	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 -	4,600.00	1,825.65	04/2014 -	03/2020	71(O) -	0/0
536	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
537	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	-	-	-	0/0
538	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
539	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
540	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 236.41	525.00	544.20	-	03/2019	-	0/0
541	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
542	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	-	-	-	-	1/1
543	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
544	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	-	-	-	0/6
545	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,040.00	2,748.23	12/2008 -	03/2019	123(O) -	0/0
546	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 -	350.00	321.09	02/2011 -	-	-	0/0
547	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	973.33	613.71	12/2012 12/2012	-	-	0/0
548	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	279.46	-	05/2019	-	0/0
549	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE ,	12/2006	170.00 -	465.00	440.72	03/2011 -	10/2011	-	0/0
550	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	268.78	98.78	-	08/2017	-	0/0
551	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	109.01	-	10/2018	-	0/0
552	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	270.58	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
553	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	331.91	- -	03/2022	- -	0/0
554	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,562.27	180.13	- -	-	-	0/1
555	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
556	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46(O) -	0/0
557	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 -	1,009.00	7.88	- -	-	-	0/0
558	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
559	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
560	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
561	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39 -	1,810.00	1,673.99	- -	03/2018	- -	0/1
562	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
563	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	52.57	- -	03/2020	- -	0/0
564	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
565	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	122.81	- -	03/2020	- -	0/0
566	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,081.96	- -	03/2018	- -	0/0
567	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 -	1,800.00	77.17	- -	-	-	0/0
568	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	319.58	141.88	- -	-	-	0/0
569	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
570	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.60	6.42	- -	-	-	0/0
571	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 1,130.13	1,130.13	.30	- -	-	-	0/0
572	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
573	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	51.31	- -	-	-	0/0
574	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	87.22	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
575	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
576	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
577	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	160.97	56.25	- -	-	-	0/0
578	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.00	92.93	- -	-	-	0/0
579	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 -	198.88	15.83	- -	-	-	0/0
580	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	47.63	- -	11/2018	- -	0/0
581	BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
582	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
583	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
584	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 -	186.64	150.28	- -	-	-	0/0
585	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	18.54	- -	-	-	0/0
586	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.11	03/2017 -	-	-	0/0
587	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0
588	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.01	- -	-	-	0/0
589	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	186.89	62.73	- -	-	-	0/0
590	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 -	681.68	135.79	- -	-	-	0/0
591	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 -	720.59	456.58	03/2017 -	-	-	0/0
592	SANTOSHPUUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
593	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
594	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE ,	04/2007	98.74 203.00	371.85	362.54	- -	-	-	0/0
595	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE ,	04/2006	96.16 260.16	277.00	274.54	- -	-	-	0/0
596	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 -	2,200.00	85.33	- -	-	-	0/0
597	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	1.11	- -	-	-	0/1
598	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
599	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
600	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	-	- -	-	-	0/0
601	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	1,714.49	632.77	- -	-	-	0/2
602	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	792.01	1.13	- -	-	-	0/1
603	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,050.00	200.35	- -	-	-	0/1
604	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
605	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
606	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	- -	-	-	0/0
607	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
608	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	8.43	- -	-	-	0/0
609	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE ,	04/2007	313.24 -	554.70	342.00	01/1999 -	-	-	0/0
610	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
611	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	2.88	- -	03/2020	-	0/0
612	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	96.14	- -	-	-	0/0
613	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	325.13	- -	03/2020	-	0/0
614	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	504.12	- -	-	-	0/0
615	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 -	678.54	-	- -	12/2018	-	0/38
616	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
617	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	.14	- -	03/2021	- -	0/0
618	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	- -	-	-	0/0
619	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE ,	04/1992	315.64 -	315.00	312.54	- -	11/2014	-	0/0
620	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE ,	04/2006	614.54 -	613.00	556.97	- -	03/2014	-	0/0
621	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	406.14	03/2015 -	03/2020	60(O) -	0/0
622	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	- -	0/0
623	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,004.90	944.84	- -	06/2021	- -	0/0
624	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.99	1,025.83	- 09/2009	03/2019	- 114(R)	0/0
625	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA ,	04/1999	166.16 -	380.00	369.99	02/2009 02/2009	06/2017	-	0/1
626	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.07	583.08	02/2015 -	12/2019	58(O) -	0/0
627	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	343.00	362.24	03/2009 03/2009	12/2017	105(O) 105(R)	1/1
628	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	478.29	- -	12/2022	- -	0/0
629	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
630	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,111.99	1,579.27	605.54	- -	03/2021	- -	0/0
631	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 -	843.04	47.24	- -	03/2021	- -	0/0
632	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA ,	03/2006	201.00 -	230.00	241.95	- -	-	-	0/0
633	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	155.28	- -	03/2020	- -	0/0
634	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA ,	03/2011	165.16 -	234.71	224.64	03/2015 07/2015	07/2015	-	0/0
635	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	66.36	03/2021 -	03/2021	0(O) -	0/0
636	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	22.36	03/2021 -	03/2022	12(O) -	0/0
637	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	50.37	03/2021 -	03/2021	0(O) -	0/0
638	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	110.88	03/2021 -	03/2020	-12(O) -	0/0
639	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020	0(O) -	0/0
640	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	183.99	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
641	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	44.95	- -	12/2024	- -	0/0
642	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	739.22	03/2020 -	03/2020	0(O) -	0/0
643	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	835.03	03/2019 -	03/2019	0(O) -	0/0
644	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
645	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
646	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
647	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	827.84	375.56	- -	08/2018	- -	0/0
648	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,143.70	514.27	03/2015 -	12/2019	57(O) -	0/0
649	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	895.00	676.07	03/2014 -	06/2019	63(O) -	0/0
650	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN ,	04/2008	516.23 -	735.00	694.13	03/2014 -	-	-	0/0
651	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	43.98	- -	03/2019	- -	0/0
652	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	109.39	- -	10/2018	- -	0/0
653	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
654	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	- -	-	-	0/0
655	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 -	420.48	35.80	- -	05/2018	- -	0/0
656	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN ,	04/2010	739.65 -	872.22	796.25	- -	-	-	0/1
657	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	105.69	- -	03/2019	- -	0/0
658	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 335.53	346.35	199.68	- -	10/2018	- -	0/0
659	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 281.03	349.00	144.37	- -	03/2019	- -	0/0
660	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	873.71	-	- -	-	-	0/0
661	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	383.20	03/2018 -	03/2018	0(O) -	0/0
662	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN ,	04/2012	471.82 -	471.82	20.03	03/2019 -	03/2019	0(O) -	0/0
663	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
664	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.81	- -	-	-	0/0
665	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	732.89	386.97	06/2013 -	03/2017	-	1/4
666	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	404.19 -	2,072.50	1,028.20	- -	-	-	0/0
667	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,053.63	- -	-	-	0/0
668	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	456.00 582.83	2,300.00	221.17	- 07/2008	-	-	0/0
669	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	446.87 527.37	1,105.00	3.34	- 01/2011	-	-	0/0
670	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
671	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	464.68	- -	-	-	0/0
672	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
673	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	36.18	- -	-	-	0/0
674	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU ,	04/2011	190.10 -	350.00	297.24	- -	03/2019	- -	0/0
675	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 -	1,010.00	919.06	- -	-	-	0/0
676	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 -	480.00	3.48	07/2008 -	-	-	0/0
677	MANOHARABAD-KOTHPALLI NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 -	1,160.47	1.74	- -	03/2022	-	0/1
678	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	491.31	03/2016 -	12/2018	33(O) -	0/0
679	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	1,112.00	.36	- -	-	-	0/1
680	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	.36	- -	-	-	0/1
681	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
682	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	35.23	12/2024 -	12/2024	0(O) -	0/0
683	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	-	03/2022 -	03/2022	0(O) -	0/0
684	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,451.00	2,407.41	03/2014 -	03/2020	72(O) -	0/0
685	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 -	1,857.00	1,495.92	03/2007 -	04/2016	-	0/0
686	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 -	580.00	-	- -	07/2019	- -	2/3

Detail of ongoing Projects Costing Rs. 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
687	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH ,	03/1997	677.97 1,062.36	1,679.13	1,781.64	- -	-	-	0/0
688	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
689	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
690	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
691	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
692	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	-	- -	-	-	0/0
693	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	474.30	421.94	- -	03/2018	-	0/0
694	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	199.75	220.72	- -	03/2018	-	0/0
695	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	-	- -	-	-	0/0
696	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
697	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
698	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
699	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	- -	-	-	0/0
700	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH ,	04/1997	836.26 -	1,072.52	1,026.65	- -	-	-	0/0
701	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,295.42	-	03/2022 -	03/2022	0(O) -	0/0
702	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(O) -	0/6
703	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	750.56	23.63	12/2024 -	12/2024	0(O) -	0/0
704	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	798.85	03/2019 -	03/2019	0(O) -	0/0
705	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.92	-	12/2025 -	12/2025	0(O) -	0/0
706	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.30	767.18	12/2020 -	12/2020	0(O) -	0/0
707	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	73.95	03/2020 -	03/2020	0(O) -	0/0
708	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12(O) -	0/0
709	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
710	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
711	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	16,216.00	549.59	12/2026 -	12/2026	0(O) -	0/0
712	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	36.80 274.41	614.00	261.71	- -	03/2020	- -	0/0
713	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.48	03/2007 03/2007	-	-	0/0
714	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
715	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
716	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7
717	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
718	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
719	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,070.00	40.16	03/2014 -	-	-	0/0
720	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,541.16	03/2016 -	12/2020	57(O) -	0/0
721	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	722.31	03/2016 -	12/2018	33(O) -	0/0
722	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL ,	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
723	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL ,	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
724	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL ,	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
725	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL ,	04/1999	207.52 -	334.87	293.47	12/2012 -	-	-	0/0
726	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
727	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	434.00	-	- -	-	-	0/0
728	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64 -	760.00	-	- -	-	-	0/0
729	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL ,	04/2010	171.02 -	250.00	242.02	06/2013 -	12/2016	-	0/0
730	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	33.53	- -	03/2020	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
731	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL ,	04/2011	209.77 -	630.00	590.90	- -	03/2018	- -	0/0
732	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55 -	450.00	331.37	- -	03/2019	- -	0/0
733	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
734	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	.64	- -	-	-	0/0
735	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
736	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	556.31 -	612.00	-	- -	03/2020	- -	0/0
737	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021	0(O) -	0/0
738	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	-	03/2003 -	-	-	0/0
	Total		3,53,800.77 -	4,83,480.73	1,42,505.66				13/109
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
739	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,373.60	05/2013 -	12/2017	55(O) -	0/0
740	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50(O) -	0/0
741	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,170.77	05/2014 -	06/2017	-	0/0
742	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
743	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
744	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0
745	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 200.69	207.40	44.08	07/2014 -	-	-	0/1
746	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
747	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1
748	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
749	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
750	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0
751	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
752	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
753	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
754	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
755	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	-	2/4
756	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	-	0/4
757	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	-	0/0
758	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
759	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
760	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
761	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
762	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	268.10	- -	11/2018	- -	0/0
763	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	02/2017	-	0/0
764	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	-	03/2020 -	03/2020	0(O) -	0/0
765	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020	0(O) -	0/0
766	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	-	06/2017 -	-	-	0/0
767	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	-	- -	-	-	0/0
768	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	-	- -	-	-	0/0
769	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	-	- -	-	-	0/0
770	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
771	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
772	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
773	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(O) -	1/4
774	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
775	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
776	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
777	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
778	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
779	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0
780	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
781	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
782	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4
783	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	-	- -	-	-	0/0
784	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
785	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	-	- -	-	-	0/0
786	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
787	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0
788	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
789	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
790	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
791	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
792	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
793	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0
794	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
795	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
796	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
797	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	-	02/2009 -	12/2017	106(O) -	0/0
798	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	-	04/2009 -	12/2017	104(O) -	0/0
799	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	-	11/2008 -	11/2017	-	0/0
800	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112(O) -	0/0
801	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	-	04/2009 -	12/2017	104(O) -	0/0
802	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	-	03/2008 -	11/2017	-	0/0
803	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	-	06/2008 -	10/2017	-	0/0
804	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116(O) -	0/0
805	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117(O) -	0/0
806	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	-	07/2009 -	12/2017	101(O) -	0/0
807	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95(O) -	0/0
808	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
809	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
810	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
811	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
812	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
813	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4
814	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	-	0/0
815	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
816	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
817	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
818	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
819	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
820	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
821	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
822	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
823	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
824	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64(O) -	0/0
825	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	-	0/0
826	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
827	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	-	0/0
828	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
829	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56(O) -	0/0
830	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49(O) -	0/0
831	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
832	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0
833	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
834	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	-	- -	-	-	0/0
835	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
836	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	-	- -	-	-	0/0
837	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
838	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	-	- -	-	-	0/0
839	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	-	- -	-	-	0/0
840	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
841	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	-	- -	-	-	0/0
842	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
843	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
844	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	- -	-	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	- -	-	-	0/0
846	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	-	-	0/0
847	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	-	08/2014 -	08/2014	-	0/0
848	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	-	08/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
849	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	-	07/2016 -	-	-	0/0
850	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	-	07/2016 -	-	-	0/0
851	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	-	05/2016 -	-	-	0/0
852	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	-	06/2016 -	06/2016	-	0/0
853	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	-	05/2016 -	-	-	0/0
854	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	-	-	0/0
855	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
856	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
857	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	-	05/2017 -	-	-	0/0
858	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
859	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(O) -	0/0
860	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(O) -	0/0
861	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	-	08/2017 -	-	-	0/0
862	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	-	- -	-	-	0/0
863	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
864	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
865	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
866	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
867	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
868	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
869	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
870	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
871	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28(O) -	0/0
872	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	- -	05/2018	- -	0/0
873	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	- -	04/2018	- -	0/0
874	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	- -	04/2018	- -	0/0
875	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	-	- -	03/2018	- -	0/0
876	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	- -	0/1
877	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
878	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
879	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
880	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
881	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
882	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
883	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63(O) -	2/3
884	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
885	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	07/2017	-	0/3
886	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	-	08/2016 -	-	-	0/0
887	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	-	- -	-	-	0/0
888	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	-	- -	-	-	0/0
889	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	-	- -	-	-	0/0
890	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	-	- -	-	-	0/0
891	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	-	- -	-	-	0/0
892	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	-	- -	-	-	0/0
893	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	-	- -	-	-	0/0
894	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	-	- -	-	-	0/0
895	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT ,	01/2017	1,251.11 -	1,251.11	-	- -	-	-	0/0
896	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT ,	06/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020	0(O) -	0/0
897	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	-	10/2017 -	-	-	0/0
898	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	-	05/2010 -	08/2017	-	0/0
899	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76(O) -	0/0
900	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	-	11/2013 -	08/2017	-	0/0
901	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA ,	08/2015	723.54 -	723.54	-	02/2018 -	02/2018	0(O) -	0/0
902	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA ,	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
903	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
904	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
905	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	04/2019	-	0/0
906	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	-	-	01/2018	-	0/0
907	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	-	-	05/2018	-	0/0
908	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	-	-	05/2018	-	0/0
909	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	-	-	05/2019	-	0/0
910	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	-	-	05/2019	-	0/0
911	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	-	03/2020 -	03/2020	0(O) -	0/0
912	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15(O) -	0/0
913	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
914	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	-	02/2019	-	0/0
915	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	-	-	-	0/0
916	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	-	-	-	-	0/0
917	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	-	-	-	-	0/0
918	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020	0(O) -	0/0
919	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44(O) -	0/0
920	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	-	-	0/0
921	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	-	0/0
922	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42(O) -	0/0
923	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
924	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
925	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	-	- -	-	-	0/0
926	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	856.59	06/2015 -	12/2017	30(O) -	0/0
927	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND ,	09/2015	341.61 -	341.61	319.04	09/2017 -	09/2017	-	0/0
928	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	302.45	- -	03/2019	-	0/0
929	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	- -	-	-	0/0
930	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	19.87	- -	08/2018	-	0/0
931	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
932	4 LANING OF KUTCERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0
933	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	- -	06/2018	-	3/3
934	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	-	0/0
935	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	-	0/0
936	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	252.39	09/2017 -	03/2018	6(O) -	0/0
937	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
938	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,424.00	08/2016 -	03/2018	19(O) -	0/0
939	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	576.00	- -	08/2018	-	0/0
940	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	-	- -	03/2019	-	0/0
941	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	-	- -	03/2019	-	0/0
942	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
943	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	49.55	- -	04/2020	- -	0/0
944	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	90.43	- -	03/2019	- -	0/0
945	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	-	- -	08/2019	- -	0/0
946	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA ,	03/2017	985.41 -	1,200.00	-	03/2020 -	03/2020	0(O) -	0/0
947	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	-	03/2020 -	03/2020	0(O) -	0/0
948	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	-	03/2020 -	03/2020	0(O) -	0/0
949	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64(O) -	0/0
950	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	-	0/0
951	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017	-	0/0
952	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	-	- -	11/2017	- -	0/0
953	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
954	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	-	09/2017 -	-	-	0/0
955	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	-	0/0
956	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	07/2017	-	0/0
957	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	-	0/0
958	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	-	0/0
959	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
960	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	-	-	0/0
961	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
962	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	-	0/0
963	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	-	0/0
964	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
965	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	-	0/0
966	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
967	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0
968	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
969	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	-	- -	-	-	0/0
970	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	-	- -	-	-	0/0
971	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	-	0/0
972	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
973	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
974	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
975	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	-	0/0
976	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
977	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
978	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	-	- -	-	-	0/0
979	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	-	0/0
980	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	-	0/0
981	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	- -	01/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
982	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	-	10/2017 -	-	-	0/0
983	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	-	09/2017 -	-	-	0/0
984	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	-	09/2017 -	-	-	0/0
985	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	-	- -	-	-	0/0
986	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
987	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,063.52	03/2013 -	12/2017	57(O) -	0/0
988	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	395.20	06/2014 -	03/2018	45(O) -	0/0
989	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49(O) -	2/2
990	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
991	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	- -	10/2017	-	0/4
992	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12
993	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	- -	06/2017	-	0/4
994	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4
995	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
996	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	65.16	- 03/2013	-	-	0/0
997	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	205.97	- 11/2014	11/2014	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
998	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
999	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	- -	0/0
1000	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	105.63	- -	05/2018	- -	0/0
1001	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	57.86	- -	05/2018	- -	0/0
1002	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	- -	0/0
1003	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	-	- -	05/2018	- -	0/0
1004	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	11.42	- -	03/2019	- -	0/0
1005	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	101.53	- -	05/2018	- -	0/0
1006	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,479.14	07/2017 -	01/2018	6(O) -	0/0
1007	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	503.52	11/2016 -	11/2017	-	0/0
1008	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1009	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,805.32	01/2018 -	01/2018	0(O) -	0/0
1010	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,094.55	06/2012 -	03/2018	69(O) -	0/0
1011	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
1012	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1013	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
1014	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
1015	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1016	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1017	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	-	-	-	-	0/0
1018	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	-	-	-	-	0/0
1019	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	-	-	-	-	0/0
1020	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	-	-	03/2019	-	0/0
1021	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	-	-	03/2019	-	0/0
1022	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	-	-	-	-	0/0
1023	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	29.50	-	05/2019	-	0/0
1024	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	-	02/2020	02/2020	0(O)	0/0
1025	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	-	03/2020	03/2020	0(O)	0/0
1026	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	-	03/2020	03/2020	0(O)	0/0
1027	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	-	03/2020	03/2020	0(O)	0/0
1028	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	-	03/2020	03/2020	0(O)	0/0
1029	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	-	03/2017	-	-	0/0
1030	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	6.54	03/2020	05/2019	-10(O)	0/0
1031	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	-	03/2020	03/2020	0(O)	0/0
1032	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	-	-	-	-	0/0
1033	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014	03/2018	50(O)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1034	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1035	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	-	- -	05/2018	- -	0/0
1036	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1037	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
1038	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1039	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
1040	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	-	2/2
1041	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40(O) -	0/0
1042	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49(O) -	0/0
1043	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,142.86	03/2013 -	11/2017	-	0/0
1044	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	-	04/2015 -	12/2017	32(O) -	0/0
1045	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	- -	-	-	0/0
1046	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
1047	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	-	- -	-	-	0/0
1048	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
1049	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1050	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1052	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1053	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42(O) -	0/0
1054	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	12/2017	42(O) -	0/0
1055	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	29.27	10/2017 -	10/2017	-	0/0
1056	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1057	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 265.35	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0
1058	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1059	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	-	-	-	-	0/0
1060	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	-	-	-	0/0
1061	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	-	0/0
1062	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1063	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	-	-	-	0/0
1064	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	-	-	-	-	0/0
1065	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	-	-	-	-	0/0
1066	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	-	0/0
1067	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1068	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	-	0/0
1069	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	-	0/0
1070	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1071	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	-	01/2017 -	-	-	0/0
1072	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	-	06/2016 -	03/2017	-	0/0
1073	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1074	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0
1075	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020	0(O) -	0/0
1076	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	-	07/2017 -	-	-	0/0
1077	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	-	- -	-	-	0/0
1078	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	-	- -	-	-	0/0
1079	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1080	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1081	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1082	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1083	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	-	01/2016 -	12/2017	23(O) -	0/0
1084	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1085	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1086	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1087	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1088	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1089	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1090	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1091	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1092	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1093	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	-	- -	11/2017	-	0/0
1094	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	-	- -	12/2017	-	0/0
1095	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	0(O) -	0/0
1096	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16(O) -	0/0
1097	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1098	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1099	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	-	0/0
1100	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	- -	-	-	0/0
1101	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1102	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
1103	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	-	0/0
1104	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	-	03/2016 -	-	-	0/0
1105	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1106	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1107	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1108	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
1109	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1110	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
1111	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	0(O) -	0/0
1112	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	-	0/0
1113	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	-	02/2018 -	02/2018	0(O) -	0/0
1114	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	-	0/0
1115	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	-	05/2017 -	-	-	0/0
1116	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	-	04/2017 -	-	-	0/0
1117	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(O) -	0/0
1118	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1119	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	206.78	05/2016 -	05/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1120	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN ,	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1121	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	-	-	0/0
1122	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
1123	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1124	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1125	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	-	10/2011 -	12/2017	74(O) -	0/0
1126	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	-	- -	02/2018	- -	0/0
1127	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0
1128	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
1129	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1130	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	-	- -	-	-	0/0
1131	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	-	- -	10/2018	- -	0/0
1132	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN ,	08/2016	320.30 -	320.30	-	- -	01/2019	- -	0/0
1133	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	-	- -	-	-	0/0
1134	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	-	- -	-	-	0/0
1135	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	-	- -	-	-	0/0
1136	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN ,	04/2017	894.00 -	894.00	-	04/2020 -	04/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1137	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	-	10/2017 -	-	-	0/0
1138	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	-	-	-	-	0/0
1139	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
1140	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
1141	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1142	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	-	10/2017 -	10/2017	-	0/0
1143	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	913.37	03/2013 -	-	-	0/0
1144	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60(O) -	0/0
1145	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	319.76	06/2013 -	-	-	0/0
1146	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55(O) -	0/0
1147	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52(O) -	0/0
1148	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1149	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
1150	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1151	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1152	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	730.88	11/2017 -	08/2018	9(O) -	0/0
1153	TWO LANING WITH PS. OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12(O) -	0/0
1154	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1155	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1156	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1157	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	129.75	- -	08/2018	- -	0/0
1158	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	-	- -	07/2018	- -	0/0
1159	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	-	03/2020 -	03/2020	0(O) -	0/0
1160	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	97.35	07/2016 -	07/2018	24(O) -	0/0
1161	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	-	08/2017 -	-	-	0/0
1162	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU , Central Sector Projects	08/2017	652.55 -	652.55	-	08/2017 -	-	-	0/0
1163	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	-	09/2017 -	-	-	0/0
1164	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	-	09/2017 -	-	-	0/0
1165	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	-	- -	-	-	0/0
1166	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	1,374.50	09/2016 -	03/2018	18(O) -	0/0
1167	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1168	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1169	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1170	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1171	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1172	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1173	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1174	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1175	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1176	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	- -	0/0
1177	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1178	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4
1179	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,667.96	06/2013 -	09/2017	-	0/0
1180	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	08/2017	-	0/0
1181	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	629.45	09/2013 -	10/2017	-	0/0
1182	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47(O) -	0/0
1183	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	-	0/0
1184	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
1185	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1186	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1187	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13(O) -	0/0
1188	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	395.72	01/2016 -	11/2017	-	0/0
1189	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	-	0/0
1190	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	-	01/2016 -	-	-	0/0
1191	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	537.71	01/2016 -	11/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1192	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1193	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0
1194	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1195	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
1196	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1197	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0
1198	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1199	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	612.73	03/2018 -	03/2018	0(O) -	0/0
1200	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	443.77	03/2018 -	03/2018	0(O) -	0/0
1201	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	675.07	03/2018 -	03/2018	0(O) -	0/0
1202	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	710.31	03/2018 -	03/2018	0(O) -	0/0
1203	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	355.00	- -	01/2019	-	0/0
1204	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	286.02	06/2016 -	06/2018	24(O) -	0/0
1205	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	116.26	06/2018 -	06/2018	0(O) -	0/0
1206	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	188.28	06/2018 -	06/2018	0(O) -	0/0
1207	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	147.29	07/2018 -	06/2018	-1(O) -	0/0
1208	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	200.36	06/2018 -	06/2018	0(O) -	0/0
1209	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1210	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1211	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
1212	MEERUT-BULANDSHAHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	.45	-	-	-	0/0
1213	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	-	05/2019	-	0/0
1214	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	-	06/2019	-	0/0
1215	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	71.78	-	04/2019	-	0/0
1216	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	9.62	-	-	-	0/0
1217	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	-	-	-	-	0/0
1218	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	14.24	-	04/2019	-	0/0
1219	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	-	04/2019	-	0/0
1220	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	-	-	-	-	0/0
1221	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	-	-	-	-	0/0
1222	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	-	-	-	-	0/0
1223	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	-	04/2019	-	0/0
1224	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	24.37	-	-	-	0/0
1225	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	81.97	-	-	-	0/0
1226	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	-	03/2020	03/2020	0(0)	0/0
1227	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	-	03/2020	03/2020	0(0)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1228	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020	0(O) -	0/0
1229	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020	0(O) -	0/0
1230	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	-	- -	-	-	0/0
1231	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	-	- -	-	-	0/0
1232	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	-	- -	-	-	0/0
1233	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	-	10/2013 -	12/2017	50(O) -	0/0
1234	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	- -	-	-	0/0
1235	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	-	- -	-	-	0/0
1236	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	-	- -	07/2018	- -	0/0
1237	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,416.68	08/2013 -	12/2017	52(O) -	0/0
1238	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55(O) -	0/0
1239	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,724.78	09/2014 -	12/2017	39(O) -	0/0
1240	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44(O) -	0/0
1241	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1243	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15	-	- -	01/2018	- -	0/0
1244	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	157.03	06/2018 -	06/2018	0(O) -	0/0
1245	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,313.68	- -	12/2017	- -	0/0
1246	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37	35.17	- -	11/2018	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1247	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHA, WEST BENGAL ,	09/2016	767.03 -	767.03	87.78	- -	08/2018	- -	0/0
	Total		3,39,047.00 -	3,45,419.20	62,454.56				23/182
	SHIPPING AND PORTS								
1248	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA ,	03/2007	245.67 -	409.83	350.68	04/2009 -	-	-	0/0
1249	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96(O) -	0/0
1250	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER - [N25000069]SHIPP., MAHARASHTRA , Central Sector Projects	03/2017	193.00 -	193.00	193.00	04/2017 -	-	-	0/0
1251	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1252	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141(O) -	0/0
1253	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL, TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	98.60	06/2017 -	-	-	0/1
1254	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017	0(O) -	0/1
1255	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL, TAMIL NADU ,	12/2014	274.85 -	274.85	43.83	04/2017 -	-	-	0/1
1256	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU ,	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1257	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU ,	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20(O) -	0/0
	Total		4,910.75 -	5,535.92	2,068.38				0/3
	TELECOMMUNICATIONS								
1258	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI ,	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9(O) -	0/0
1259	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL, GUJARAT , Central Sector Projects	09/2017	171.54 -	171.54	-	05/2018 -	04/2018	-1(O) -	0/0
1260	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	159.30 159.30	159.30	-	04/2018 -	04/2018	0(O) -	0/0
1261	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	167.68 164.90	164.90	-	04/2018 -	04/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1262	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	212.70 222.00	222.00	-	05/2018 -	05/2018	0(O) -	0/0
1263	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 -	215.30	-	05/2018 -	05/2018	0(O) -	0/0
1264	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47(O) -	0/0
1265	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
1266	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH ,	11/2017	163.00 -	163.00	-	08/2018 -	08/2018	0(O) -	0/0
	Total		16,952.95 -	28,189.47	7,086.20				0/70
	<u>URBAN DEVELOPMENT</u>								
1267	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	111.09	03/2017 -	-	-	1/5
1268	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	- -	-	-	0/0
1269	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	.20	06/2017 06/2020	06/2020	36(O) 0(R)	0/0
1270	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24(O) -	0/0
1271	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 2,283.30	1,592.00	157.53	10/2019 -	03/2020	5(O) -	0/0
1272	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	528.94	12/2015 -	03/2018	27(O) -	0/0
1273	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019	0(O) -	1/7
1274	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	4.06	- -	04/2019	- -	0/2
1275	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	126.71	11/2014 -	10/2018	47(O) -	0/8
1276	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	38.76	03/2016 -	12/2018	33(O) -	1/6
1277	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1278	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	-	02/2020 -	02/2020	0(O) -	0/0
1279	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65(O) 11(R)	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1280	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1281	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	74.54	11/2015 -	12/2017	25(O) -	0/0
1282	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH ,	12/2012	188.87 -	188.87	184.89	12/2015 03/2018	03/2018	27(O) 0(R)	0/0
1283	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	12/2016	164.00 -	164.00	69.25	01/2018 05/2018	05/2018	4(O) 0(R)	5/11
1284	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	269.50	03/2016 12/2017	03/2018	24(O) 3(R)	0/13
1285	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72(O) -	11/20
1286	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21(O) -	0/0
1287	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	-	-	0/0
1288	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44(O) -	0/10
1289	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	309.07	05/2017 02/2018	02/2018	9(O) 0(R)	7/12
1290	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	57.58	04/2019 -	04/2019	0(O) -	1/8
1291	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	414.62	03/2015 12/2017	03/2018	36(O) 3(R)	0/0
1292	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	332.72	260.88	09/2016 -	11/2017	-	0/0
1293	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24(O) -	11/24
1294	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	15.28	- -	-	-	0/6
1295	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1296	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	.61	03/2020 -	03/2020	0(O) -	0/5
1297	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1298	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(December 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1299	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	122.43	08/2016 -	06/2018	22(O) -	8/13
1300	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	39.73	04/2018 -	05/2019	13(O) -	1/6
	Total		1,38,993.10 -	1,44,035.91	62,590.76				47/157
	<u>DEFENCE PRODUCTION</u>								
1301	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	172.99	31.56	05/2018 -	05/2018	0(O) -	4/5
1302	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	296.05	39.30	08/2020 -	08/2020	0(O) -	3/3
	Total		453.64 -	469.04	70.86				7/8
	Grand Total		16,20,089.45	18,38,119.90	6,58,680.80				2125/3962


Summary of projects in the Flash Report for the month of December, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1289
Number of Projects completed/dropped/frozen in Current Month	4
	0
Number of Projects Added in Current Month	17
Number of Projects in Current Month	1302

Brief Analysis

Project Status with respect to Original Schedule: Out of 1302 projects, 15 projects are ahead of schedule, 310 projects are on schedule 287 projects are delayed. 542 projects do not have fixed dates of commissioning. 148 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

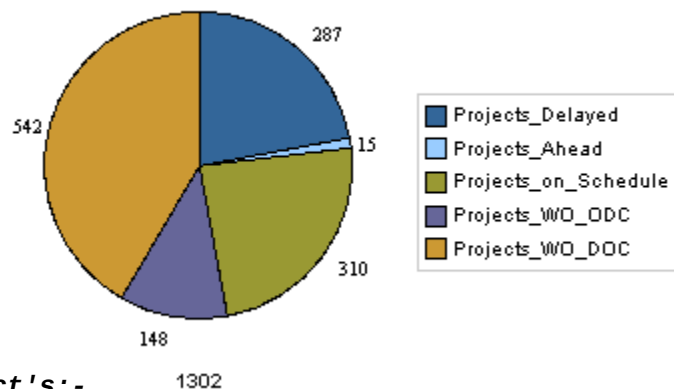


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1302 projects when sanctioned, was of the order of Rs. 1620089.45 crore but this was subsequently revised to Rs. 1838119.9 crore implying a cost overrun of 13.5%. The expenditure incurred on these projects till December, 2017 is Rs. 658680.8 crore, which is 35.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

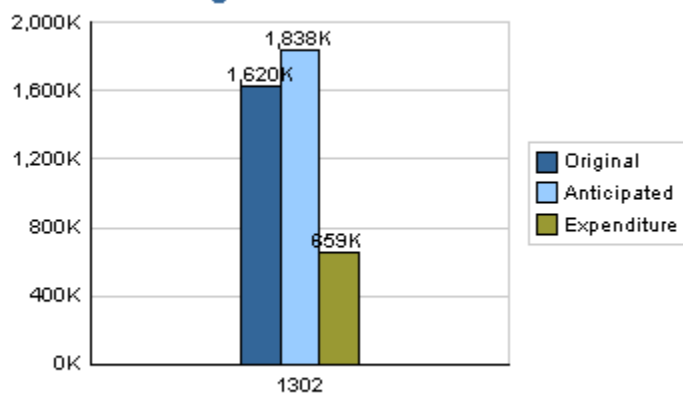

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

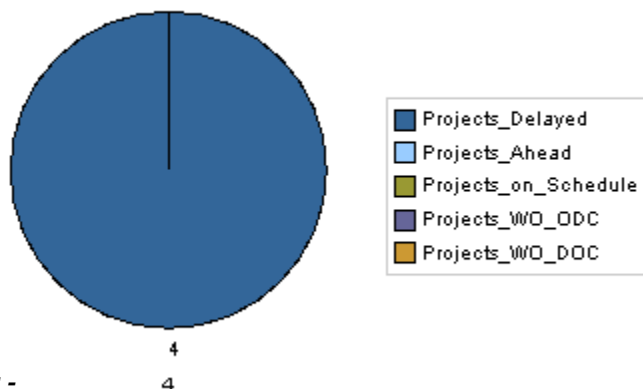


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 69728 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till December, 2017 is Rs. 27419.63 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

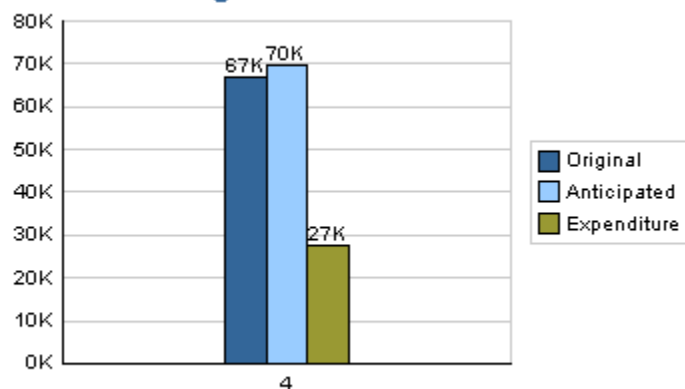

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

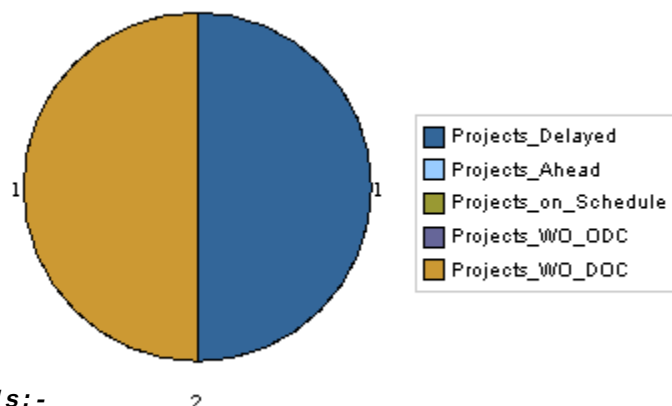


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till December, 2017 is Rs. 549.39 crore, which is 55.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

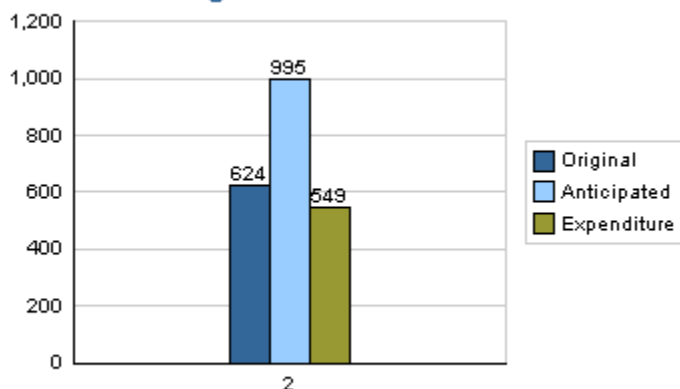

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	92
Number of Projects On Schedule	51
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 1 project is ahead of schedule, 51 projects are on schedule 37 projects are delayed. 3 projects do not have fixed dates of commissioning.

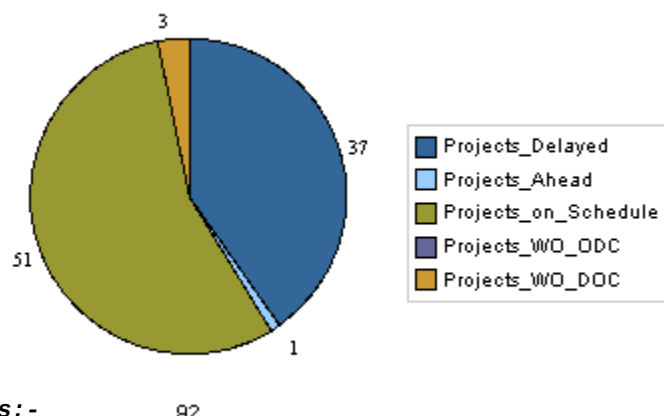


Total No Of Project's:-

92

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 89695.08 crore but this was subsequently anticipated to Rs. 89199.09 cr The expenditure incurred on these projects till December, 2017 is Rs. 22387.17 crore, which is 25.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

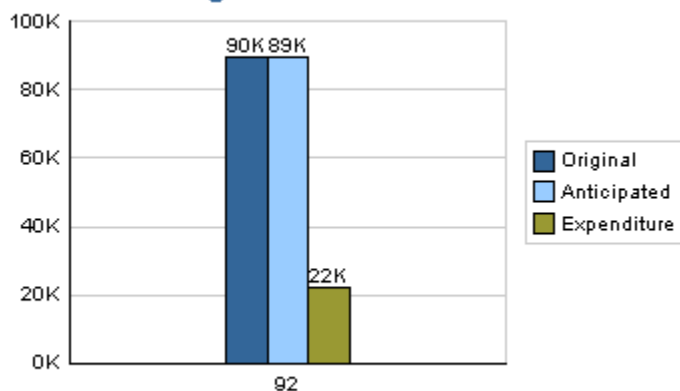

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

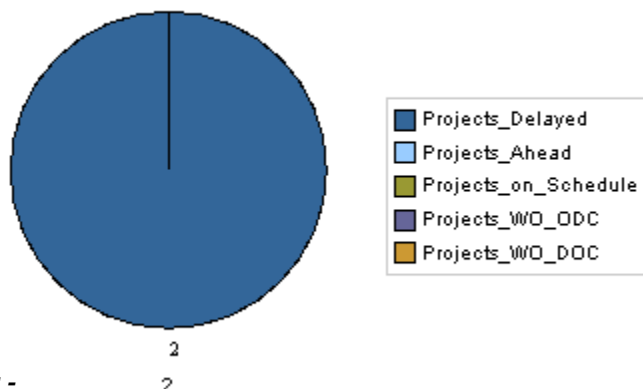


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till December, 2017 is Rs. 516.36 crore, which is 73.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

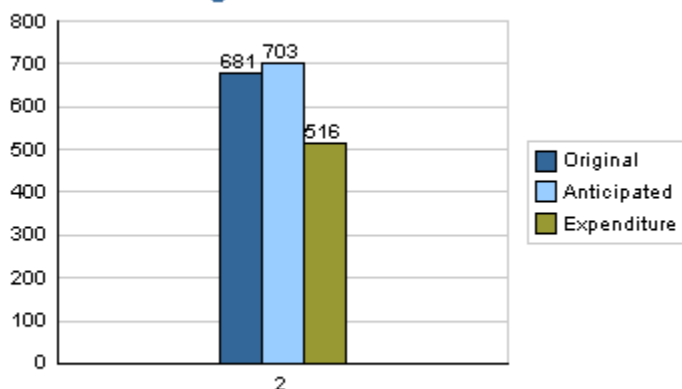

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till December, 2017 is Rs. 344.73 crore, which is 5% of the anticipated cost of the projects.

Figures are in Rs. Crore

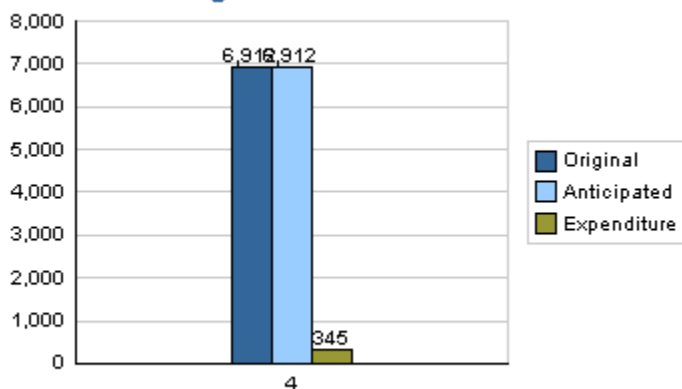

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	31
Number of Projects On Schedule	5
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 31 projects, 5 projects are on schedule 17 projects are delayed. 8 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

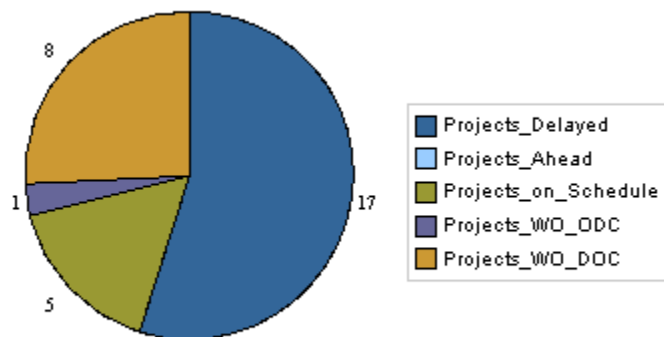


Total No Of Project's:-

31

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 55217 crore but this was subsequently anticipated to Rs. 55430.68 crore implying a cost overrun of .4%. The expenditure incurred on these projects till December, 2017 is Rs. 39041.51 crore, which is 70.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

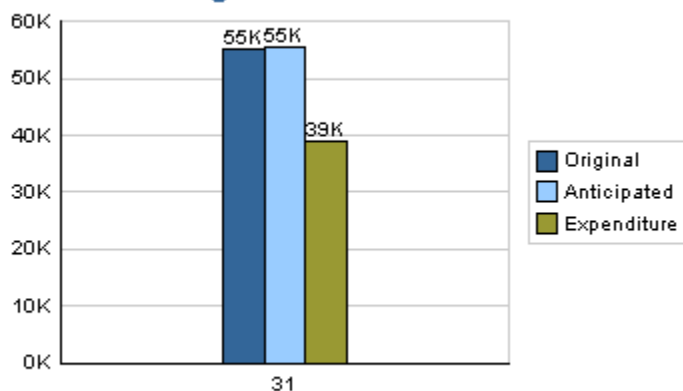

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	112
Number of Projects On Schedule	66
Number of Projects Delayed	30
Number of Projects Ahead	8
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 112 projects, 8 projects are ahead of schedule, 66 projects are on schedule 30 projects are delayed. 8 projects do not have fixed dates of commissioning.

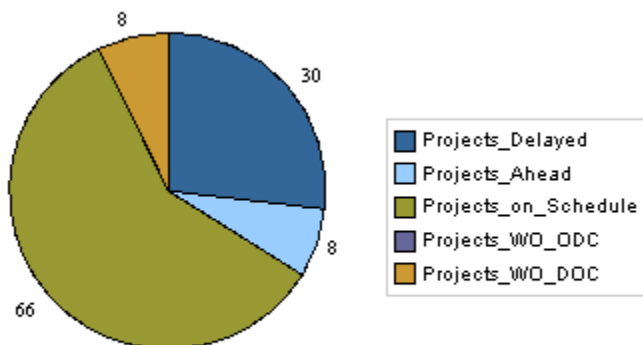


Total No Of Project's:-

112

Investment Scenario

Total original cost of implementation of 112 projects when sanctioned, was of the order of Rs. 201408.83 crore but this was subsequently anticipated to Rs. 202790.33 crore implying a cost overrun of .7%. The expenditure incurred on these projects till December, 2017 is Rs. 57163.11 crore, which is 28.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

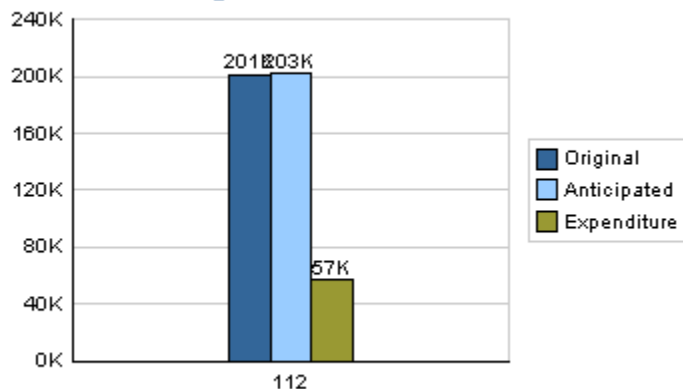

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	125
Number of Projects On Schedule	48
Number of Projects Delayed	65
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	10

Brief Analysis

Project Status with respect to Original Schedule: Out of 125 projects, 2 projects are ahead of schedule, 48 projects are on schedule 65 projects are delayed. 10 projects do not have fixed dates of commissioning.

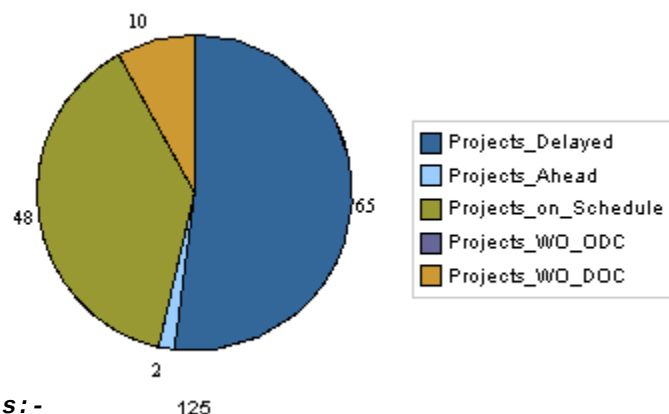


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 125 projects when sanctioned, was of the order of Rs. 338658.41 crore but this was subsequently anticipated to Rs. 397484.24 crore implying a cost overrun of 17.4%. The expenditure incurred on these projects till December, 2017 is Rs. 230686.08 crore, which is 58% of the anticipated cost of the projects.

Figures are in Rs. Crore

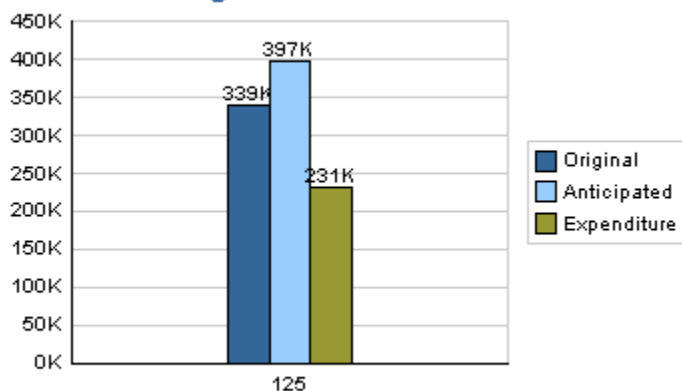

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till December, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

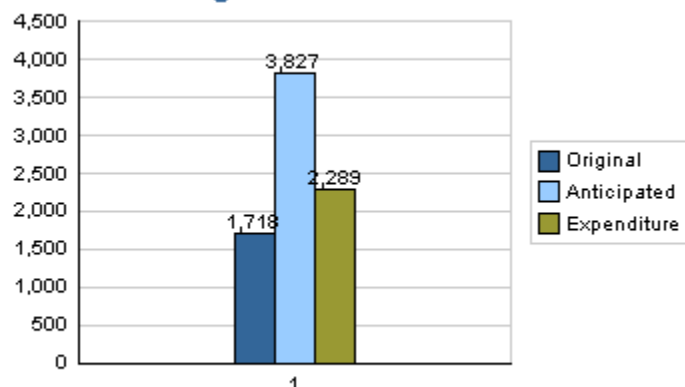

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	14
Number of Projects On Schedule	5
Number of Projects Delayed	6

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 5 projects are on schedule 6 projects are delayed. 3 projects do not have fixed dates of commissioning.

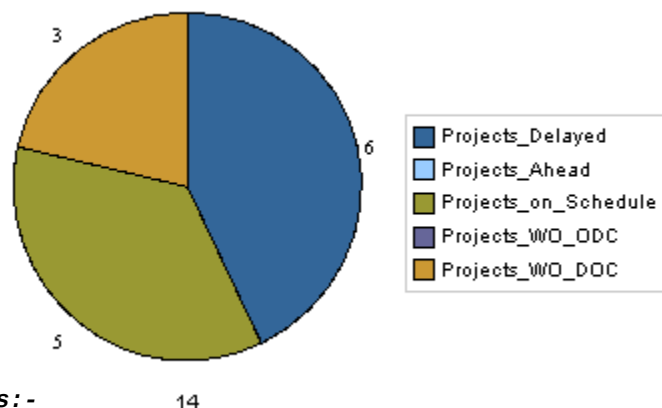


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 3897.21 crore but this was subsequently anticipated to Rs. 3919.69 crore implying a cost overrun of .6%. The expenditure incurred on these projects till December, 2017 is Rs. 1507.4 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

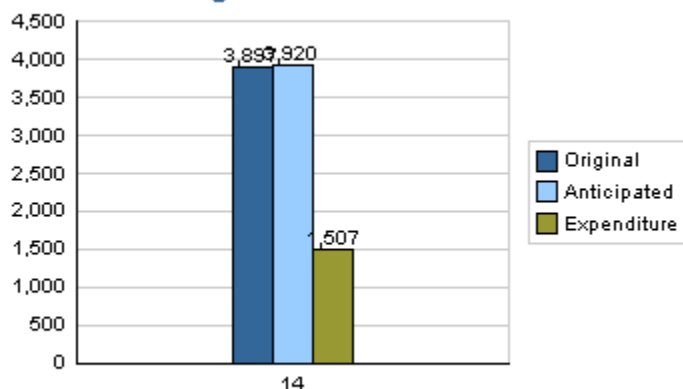

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	351
Number of Projects On Schedule	39
Number of Projects Delayed	34
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	80
Number of Projects Without Date Of Commissioning	197

Brief Analysis

Project Status with respect to Original Schedule: Out of 351 projects, 1 project is ahead of schedule, 39 projects are on schedule 34 projects are delayed. 197 projects do not have fixed dates of commissioning. 80 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

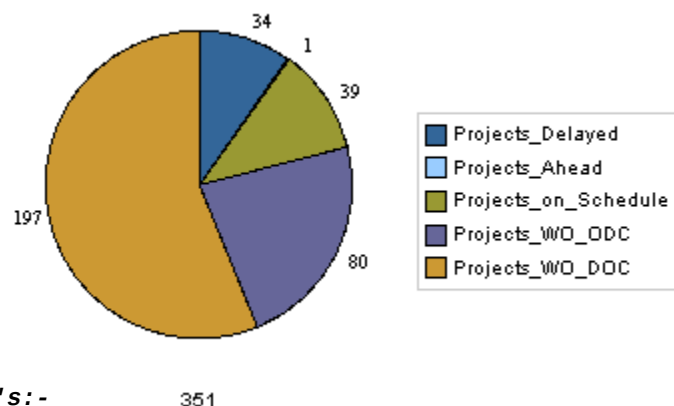


Total No Of Project's:-

351

Investment Scenario

Total original cost of implementation of 351 projects when sanctioned, was of the order of Rs. 353800.77 crore but this was subsequently anticipated to Rs. 483480.73 crore implying a cost overrun of 36.7%. The expenditure incurred on these projects till December, 2017 is Rs. 142505.66 crore, which is 29.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

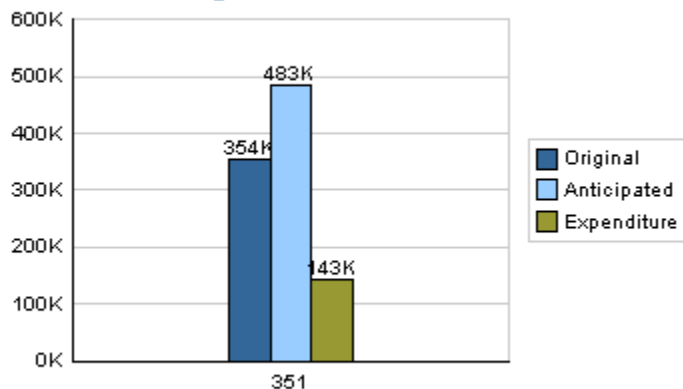

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	509
Number of Projects On Schedule	77
Number of Projects Delayed	63
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	66
Number of Projects Without Date Of Commissioning	301

Brief Analysis

Project Status with respect to Original Schedule: Out of 509 projects, 2 projects are ahead of schedule, 77 projects are on schedule 63 projects are delayed. 301 projects do not have fixed dates of commissioning. 66 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

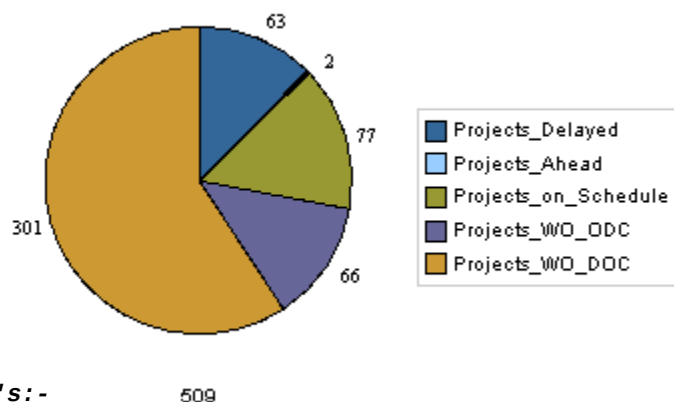


Total No Of Project's:-

509

Investment Scenario

Total original cost of implementation of 509 projects when sanctioned, was of the order of Rs. 339047 crore but this was subsequently anticipated to Rs. 345419.2 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till December, 2017 is Rs. 62454.56 crore, which is 18.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

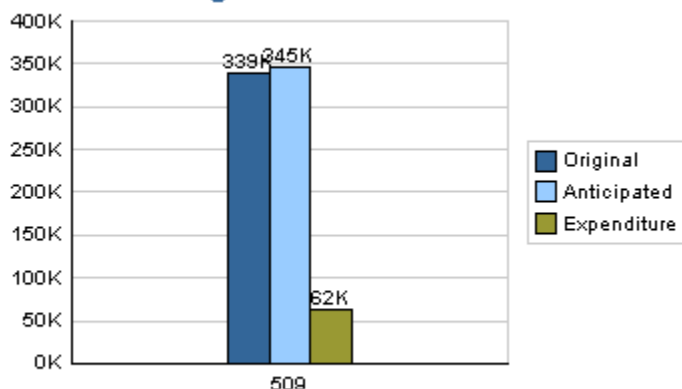

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	10
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 2 projects are on schedule 3 projects are delayed. 5 projects do not have fixed dates of commissioning.

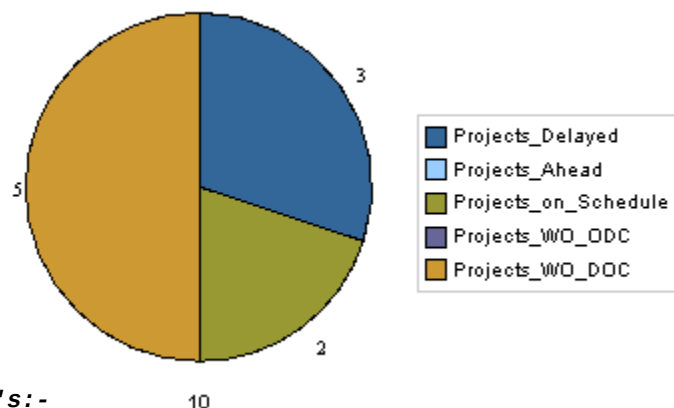


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 4910.75 crore but this was subsequently anticipated to Rs. 5535.92 crore implying a cost overrun of 12.7%. The expenditure incurred on these projects till December, 2017 is Rs. 2068.38 crore, which is 37.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

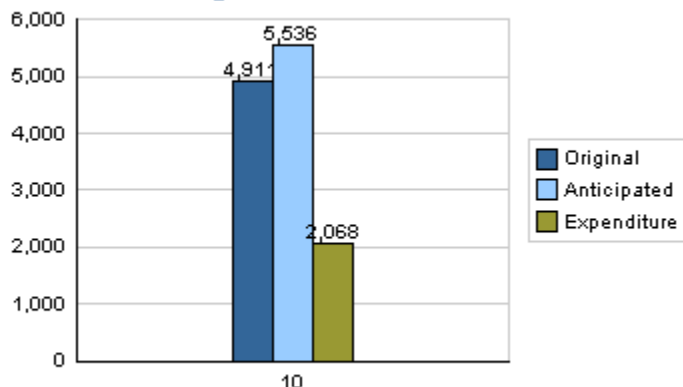

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	9
Number of Projects On Schedule	5
Number of Projects Delayed	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 1 project is ahead of schedule, 5 projects are on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

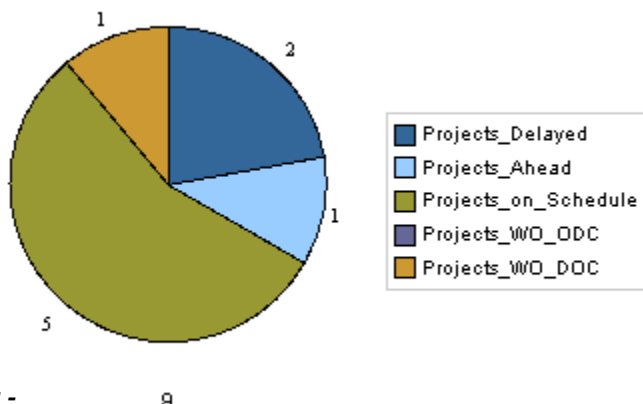


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 16952.95 crore but this was subsequently anticipated to Rs. 28189.47 crore implying a cost overrun of 66.3%. The expenditure incurred on these projects till December, 2017 is Rs. 7086.2 crore, which is 25.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

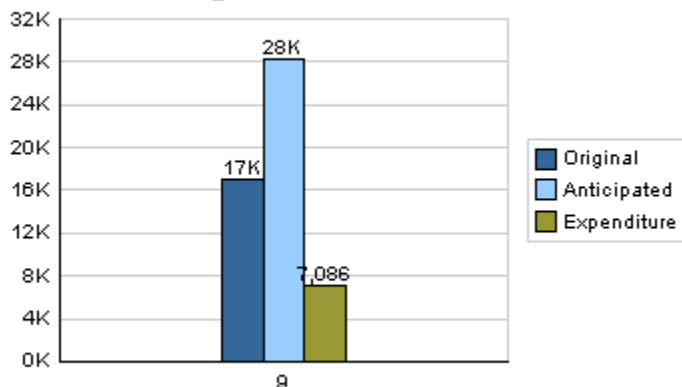

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	34
Number of Projects On Schedule	6
Number of Projects Delayed	22

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 6 projects are on schedule 22 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

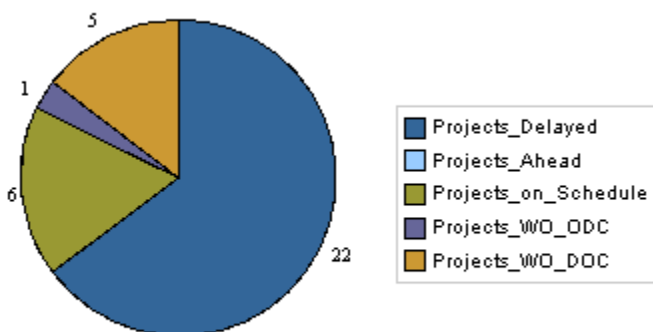


Total No Of Project's:-

34

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 138993.1 crore but this was subsequently anticipated to Rs. 144035.91 crore implying a cost overrun of 3.6%. The expenditure incurred on these projects till December, 2017 is Rs. 62590.76 crore, which is 43.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

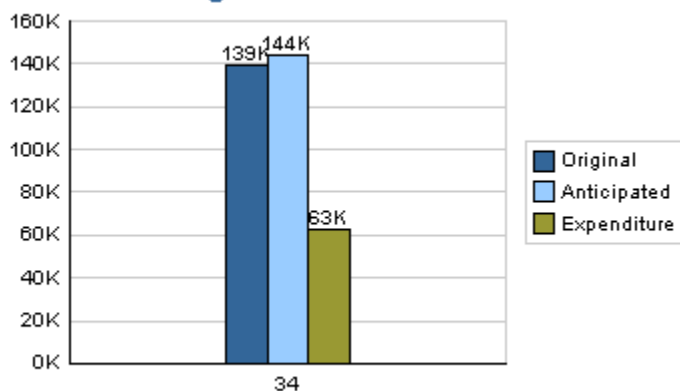

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

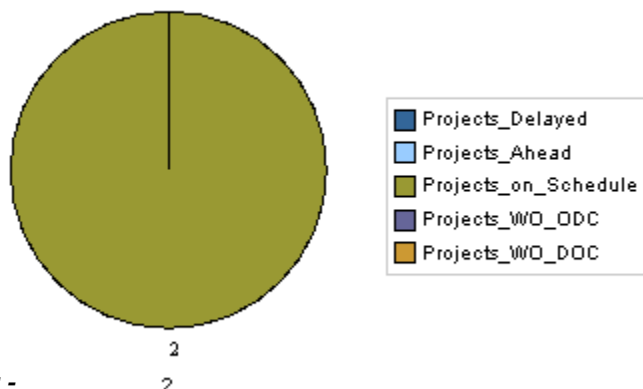


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till December, 2017 is Rs. 70.86 crore, which is 15.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

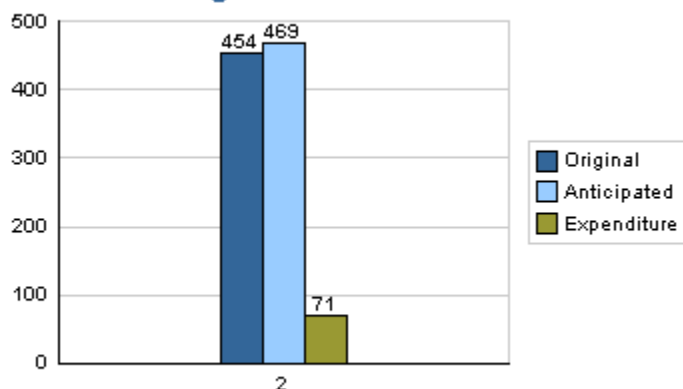

Annexure

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (DECEMBER 2017)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	26.44
2	ANDHRA PRADESH	60	97,515.51	1,01,522.54	12,388.27
3	ARUNACHAL PRADESH	31	16,602.41	33,555.84	17,566.11
4	ASSAM	48	33,455.72	49,200.77	30,110.12
5	BIHAR	79	68,372.22	85,193.29	38,970.25
6	CHHATISGARH	38	82,769.79	84,960.97	49,598.06
7	D & N HAVELI	1	6,086.08	5,479.75	2,236.63
8	DELHI	14	49,878.66	50,145.97	38,764.29
9	GOA	9	4,043.51	4,058.91	152.07
10	GUJARAT	43	38,941.93	41,578.3	16,748.56
11	HARYANA	21	14,081.22	15,967.45	1,341.9
12	HIMACHAL PRADESH	12	14,659.32	22,591.6	6,948.36
13	JAMMU AND KASHMIR	11	28,880.41	57,111.68	23,413.27
14	JHARKHAND	47	46,513.55	50,225.71	19,875.13
15	KARNATAKA	44	72,280.39	81,988.83	28,941.61
16	KERALA	21	21,774.25	27,871.82	2,589.95
17	MADHYA PRADESH	59	62,349.33	65,892.8	18,661.16
18	MAHARASHTRA	123	1,77,734.51	1,90,392.94	64,770.6
19	MANIPUR	2	944.25	9,874.69	7,037.58
20	MEGHALAYA	6	7,108.02	9,025	283.74
21	MIZORAM	5	2,001.2	6,942.57	3,293.9
22	MULTI STATE	183	3,02,573.52	3,00,732.55	92,057.02
23	NAGALAND	7	8,126.79	10,276.79	406.14
24	ODISHA	72	74,459.24	82,559.02	20,836.55
25	PUNJAB	28	15,555.77	15,561.5	2,553.4
26	RAJASTHAN	62	45,695.77	47,536.64	14,672.91
27	SIKKIM	6	2,537.08	5,585.45	931.23
28	TAMIL NADU	65	1,10,018.77	1,25,859.19	48,445.09
29	TELANGANA	36	24,952.57	27,674.71	6,249.99
30	TRIPURA	11	4,400.64	9,067.42	5,735.34
31	UTTAR PRADESH	88	1,11,448.36	1,15,138.64	36,803.67
32	UTTARAKHAND	14	17,481.68	32,916.29	7,871.63
33	WEST BENGAL	55	56,532.37	71,188.94	38,399.83
TOTAL		1,302	16,20,089.45	18,38,119.9	6,58,680.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

CIVIL AVIATION

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	522.95

COAL

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	331.06
3	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	397.54
4	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	195.09
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	259.5
6	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	477.74
7	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	687.28	-	733.23

HEAVY INDUSTRY

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	1718	-	2289

PETROLEUM

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	600.17	-	703.97
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	960

POWER

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
12	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6597.22
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	9610.95
14	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3359
15	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	5186.86
16	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	573.99	1337.76	1544.55
17	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	232.34	-	246.39

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
18	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	297.33	346.79	364.29
19	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	368.72	1329.43	1337.43
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	478.69
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
21	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	124.43	-	919.06
23	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	703.51
24	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	304	-	509.95
25	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
26	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	900.05	-	980.99
27	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	-	967.96
28	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
29	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	856.81
30	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	155.74	164.36	874.72
31	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	677.97	1062.36	1781.64
32	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	4892.39
33	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	218.24	236.41	544.2
34	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	194.07	-	548.77
35	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
36	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	876.49
37	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
38	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	919.92

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
39	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	242.42	369.7	927.68
40	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
41	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	625.3	408.76	841.57
42	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.61
43	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	733	-	2748.23
44	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	1049.69	-	3544.3
45	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	-	321.09
46	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	613.71
47	JIND-SONEPAT (NL),NR	NR	01/2004	238.56	-	722.65
48	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	944.84
49	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	301.64	-	1025.83
50	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	166.16	-	369.99
51	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	-	6985.58
52	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	364.4
53	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	120	-	210.67
54	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	279.46
55	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	183.23	-	583.08
56	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	362.24
57	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	136.62	-	379.63
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	283.95	495.4
59	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	261.7	-	343.71
60	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	743	-	1478.11
61	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	500.67

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
62	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	687.2	-	1020.64
63	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	404.19	-	1028.2
64	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1053.63
65	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	170	-	440.72
66	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	436.01
67	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	921.36
68	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	618.19
69	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	2407.41
70	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	1825.65
71	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	482	-	992.03
72	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	676.07
73	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	516.23	-	694.13
74	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	207.11
75	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	293.47
76	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	603.04	-	628.11
77	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	1389.62	-	1513.78
78	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
79	KATAKHAL TO BHAIRABI	NFR	04/1998	227.9	-	417.62
80	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	1676.31	-	7137.21
81	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	421.94
82	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	220.72
83	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	446	-	590.6
84	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	279.4	-	323.64

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
85	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	739.65	-	796.25
86	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	171.02	-	242.02
87	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	402.65
88	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
89	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	464.68
90	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	822.39	-	1673.99
91	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1495.92
92	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	590.9
93	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	283.55	-	331.37
94	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	378.76
95	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	523.17	-	1081.96
96	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	509.15
97	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	456.58
98	PEN ROHA DOUBLING	CR	04/2007	98.74	203	362.54
99	PANVEL PEN DOUBLING	CR	04/2006	96.16	260.16	274.54
100	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	179.65	-	799.73
101	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	342
102	JHARSUGUDA-RENGALI DOUBLING	ECOR	03/2006	201	-	241.95
103	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	224.64
104	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	190.1	-	297.24
105	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	836.26	-	1026.65
106	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
107	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	4300	-	4440.32

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

ROAD TRANSPORT AND HIGHWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
108	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
109	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	852	-	913.37
110	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2373.6
111	MURADABAD-BAREILY	NHAI	04/2010	1267	-	2667.96
112	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2063.52
113	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1986.56
114	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.31
115	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	622.89
116	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	3170.77
117	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1142.86
118	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2416.68
119	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	998.79	-	1945.82
120	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2724.78
121	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	320.46
122	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1850
123	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1792.9
124	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1374.5
125	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	395.72
126	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	537.71
127	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1479.14
128	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
129	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2805.32
130	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2094.55

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(DECEMBER 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
131	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	2313.68
132	TRICHY - KARUR	NHAI	03/2007	516	-	761.19
SHIPPING AND PORTS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
133	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	245.67	-	350.68
134	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12
STEEL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
135	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	17265	-	18303.09
136	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
137	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Annexure - III

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	69.04	03/2023 -	03/2021
	Total		1,186.64 -	203.82	69.04		
	<u>PETROLEUM</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	64.86	12/2020 -	08/2020
3	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.50	02/2019 -	12/2018
4	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	215.86	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	81.33	05/2019 -	12/2018
	Total		7,787.52 -	7,787.52	610.52		
	<u>POWER</u>						
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 969.97	969.97	732.28	06/2016 02/2018	12/2017
8	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	98.02	07/2018 -	01/2018
9	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	119.40	05/2018 -	03/2018
	Total		1,278.07 -	1,339.96	949.70		
	<u>RAILWAYS</u>						
10	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92	1,172.92	110.88	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	110.88		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
11	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	147.29	07/2018 -	06/2018
12	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	6.54	03/2020 -	05/2019
	Total		963.19 -	921.00	153.83		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
13	GUJARAT ACCESS (LOT 1) - [N26000111	9/2017	171.54 -	171.54	-	05/2018 -	04/2018
	Total		171.54 -	171.54	.00		
	Grand Total		12,559.88	11,596.76	1,893.97		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023
4	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	370.58	03/2021 -	03/2021
5	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.78	03/2018 -	03/2018
6	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	231.76	03/2025 -	03/2025
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021
9	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
10	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
11	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	0.04	03/2022 -	03/2022
12	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	38.57	03/2022 -	03/2022
13	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
14	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	70.86	03/2020 -	03/2020
15	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	284.27	03/2022 -	03/2022
16	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	176.03	03/2020 -	03/2020
17	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
18	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,444.26	03/2023 -	03/2023
19	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	49.19	03/2020 -	03/2020
20	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022
21	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	72.23	03/2023 02/2017	03/2023
22	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.94	03/2020 -	03/2020
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	204.93	03/2018 -	03/2018
25	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	25.13	03/2019 -	03/2019
26	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	47.29	03/2019 -	03/2019
27	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
28	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	72.65	03/2021 -	03/2021
29	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	38.29	03/2020 -	03/2020
30	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.85	03/2021 -	03/2021
31	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	430.99	03/2018 -	03/2018
32	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.62	03/2021 -	03/2021
33	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	31.42	03/2021 -	03/2021
34	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	5.69	09/2019 -	09/2019
35	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	47.85	03/2021 -	03/2021
36	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	368.02	03/2020 -	03/2020
37	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,184.47	11/2021 -	11/2021
38	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	0.57	03/2023 -	03/2023
39	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
40	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
41	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
42	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	199.31	03/2020 -	03/2020
43	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.34	12/2019 -	12/2019
44	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
45	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	12.79	03/2022 -	03/2022
47	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,563.46	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
48	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	0.42	03/2021 -	03/2021
49	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
50	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	30.12	03/2019 -	03/2019
51	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.57	03/2019 -	03/2019
	Total		66,658.54 -	66,926.41	9,854.51		
	<u>DEFENCE PRODUCTION</u>						
52	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	39.30	08/2020 -	08/2020
53	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	31.56	05/2018 -	05/2018
	Total		453.64 -	469.04	70.86		
	<u>HEALTH AND FAMILY WELFARE</u>						
54	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
55	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
56	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
57	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019
58	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
	Total		1,458.52 -	1,458.52	302.35		
	<u>MINES</u>						
59	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	286.25	01/2020 01/2020	01/2020
60	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	44.60	04/2021 04/2021	04/2021
61	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
62	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	13.88	11/2020 11/2020	11/2020
	Total		6,912.00 -	6,912.00	344.73		
	<u>PETROLEUM</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	262.60	10/2019 -	10/2019
64	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.09	12/2019 -	12/2019
65	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	88.68	03/2019 -	03/2019
66	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	1,163.47	04/2018 04/2018	04/2018
67	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.39	02/2020 -	02/2020
68	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	12.38	04/2022 -	04/2022
69	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019
70	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	16.93	07/2020 -	07/2020
71	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	157.51	09/2018 09/2018	09/2018
72	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	0.57	07/2022 -	07/2022
73	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	542.00	02/2020 -	02/2020
74	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	155.33	05/2019 05/2019	05/2019
75	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
76	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 -	11/2019
77	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
78	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
79	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	11.35	06/2020 -	06/2020
80	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
81	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,548.90	12/2018 -	12/2018
82	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	8.28	12/2020 -	12/2020
83	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,052.91	06/2018 -	06/2018
84	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	316.80	11/2019 -	11/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	127.28	12/2020 -	12/2020
86	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 -	11/2019
87	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
88	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
89	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	32.34	02/2020 -	02/2020
90	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	89.27	02/2020 -	02/2020
91	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	185.08	08/2021 -	08/2021
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	2,253.00	14.19	12/2020 -	12/2020
93	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	57.29	12/2019 -	12/2019
94	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	123.41	05/2021 -	05/2021
95	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	55.76	04/2019 -	04/2019
96	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018
97	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020
98	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
99	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,828.00	3.27	12/2020 -	12/2020
100	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	207.09	03/2026 03/2026	03/2026
101	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
102	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	124.98	03/2018 -	03/2018
103	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	24.35	08/2018 -	08/2018
104	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	26.18	12/2018 -	12/2018
105	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,212.00	6.30	12/2020 -	12/2020
106	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
107	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.06	10/2020 -	10/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	32.65	09/2019 -	09/2019
109	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	227.72	04/2018 -	04/2018
110	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	-	03/2021 -	03/2021
111	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
112	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,250.00	18.19	12/2020 -	12/2020
113	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	12.13	01/2019 -	01/2019
114	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	487.03	12/2018 -	12/2018
115	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	97.51	12/2019 -	12/2019
116	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	91.45	08/2019 -	08/2019
117	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
118	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	89.85	12/2017 -	12/2017
119	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	272.86	11/2018 -	11/2018
120	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	217.71	10/2018 -	10/2018
121	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020
122	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	39.60	09/2019 09/2019	09/2019
123	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	312.83	06/2020 -	06/2020
124	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	16.95	02/2019 -	02/2019
125	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	12.07	12/2019 -	12/2019
126	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	70.83	01/2019 -	01/2019
127	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	96.29	12/2019 -	12/2019
128	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	200.00	15.92	04/2018 -	04/2018
	Total		1,22,609.39 -	1,22,397.38	9,895.15		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
129	50 MW SOLAR POWER PROJECT - [N18000251]	6/2017	287.48 -	287.48	28.79	03/2018 -	03/2018
130	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	758.15	07/2018 -	07/2018
131	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
132	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	-	02/2019 -	02/2019
133	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	-	02/2020 -	02/2020
134	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	8.00	07/2019 -	07/2019
135	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	4.99	09/2018 -	09/2018
136	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	1,043.00	04/2019 -	04/2019
137	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	38.90	09/2020 -	09/2020
138	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]	4/2015	2,225.00 2,225.00	2,225.00	1,033.00	01/2018 -	01/2018
139	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	109.00	07/2020 -	07/2020
140	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	570.00	06/2018 -	06/2018
141	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	66.46	05/2018 -	05/2018
142	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	0.77	02/2019 -	02/2019
143	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
144	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,106.00	07/2020 -	07/2020
145	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
146	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
147	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	163.78	01/2019 -	01/2019
148	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	147.51	04/2018 -	04/2018
149	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	81.99	06/2018 -	06/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
150	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
151	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019
152	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	342.29	06/2019 -	06/2019
153	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	60.40	11/2018 -	11/2018
154	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
155	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI [N18000240]	10/2016	608.24 -	608.24	11.77	04/2019 -	04/2019
156	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
157	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	15.59	02/2019 -	02/2019
158	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	7.29	06/2019 -	06/2019
159	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	50.40	11/2018 -	11/2018
160	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	7.82	04/2019 -	04/2019
161	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	322.43	04/2020 -	04/2020
162	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	137.00	04/2019 -	04/2019
163	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	37.81	07/2018 -	07/2018
164	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	58.24	03/2018 -	03/2018
165	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	411.76	12/2018 -	12/2018
166	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
167	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	600.02	05/2019 -	05/2019
168	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	51.97	12/2018 -	12/2018
169	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	1.43	03/2019 -	03/2019
170	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	-	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
171	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239	10/2016	408.46 -	408.46	51.76	01/2019 -	01/2019
172	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200	7/2015	2,247.37 -	2,247.37	834.84	07/2018 -	07/2018
173	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195	5/2015	780.33 -	780.33	32.97	10/2018 -	10/2018
174	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179	12/2014	6,517.36 -	6,517.36	3,557.86	04/2018 -	04/2018
175	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	812.04	11/2019 -	11/2019
176	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230	7/2016	333.17 -	333.17	171.22	03/2019 -	03/2019
	Total		83,371.30 -	83,371.47	16,344.59		
	<u>RAILWAYS</u>						
177	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
178	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405	4/2015	1,765.90 -	1,765.92	-	12/2025 -	12/2025
179	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421	1/2011	493.17 -	493.17	383.20	03/2018 -	03/2018
180	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	16,216.00	549.59	12/2026 -	12/2026
181	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	750.55 -	750.56	23.63	12/2024 -	12/2024
182	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426	12/2015	346.32 -	300.00	208.87	03/2019 -	03/2019
183	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	1/2013	387.70 -	387.70	361.35	03/2018 -	03/2018
184	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00 -	1,295.42	-	03/2022 -	03/2022
185	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	810.02	50.37	03/2021 -	03/2021
186	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	977.00	798.85	03/2019 -	03/2019
187	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423	4/2012	471.82 -	471.82	20.03	03/2019 -	03/2019
188	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	728.10 -	728.10	35.23	12/2024 -	12/2024
189	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.65 -	1,485.85	718.67	12/2020 -	12/2020
190	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
191	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	0.16	12/2025 -	12/2025

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
192	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021
193	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	245.96	03/2019 -	03/2019
194	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	73.95	03/2020 -	03/2020
195	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	739.22	03/2020 -	03/2020
196	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	0.39	03/2019 -	03/2019
197	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	66.36	03/2021 -	03/2021
198	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
199	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,237.34	03/2020 -	03/2020
200	BANASPAANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	835.03	03/2019 -	03/2019
201	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	103.59	03/2019 -	03/2019
202	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
203	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
204	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021
205	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
206	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	767.18	12/2020 -	12/2020
207	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
208	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	145.79	03/2018 -	03/2018
209	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	671.78	03/2020 -	03/2020
210	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
211	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
212	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	221.08	03/2019 -	03/2019
213	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
214	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
215	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
	Total		44,682.64 -	58,420.30	9,174.82		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
216	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
217	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	200.36	06/2018 -	06/2018
218	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
219	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
220	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
221	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
222	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
223	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
224	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
225	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
226	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
227	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
228	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
229	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
230	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
231	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
232	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
233	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
234	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
236	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
237	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
238	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
239	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
240	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
241	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
242	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
243	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
244	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
245	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
246	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
247	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS (KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020
248	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	188.28	06/2018 -	06/2018
249	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
250	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	157.03	06/2018 -	06/2018
251	FOUR LANING OF PARWANOO - SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
252	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	710.31	03/2018 -	03/2018
253	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
254	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
255	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	675.07	03/2018 -	03/2018
256	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
257	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
258	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
259	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
260	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
261	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
262	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	443.77	03/2018 -	03/2018
263	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
264	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
265	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	2,805.32	01/2018 -	01/2018
266	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
267	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
268	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
269	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
270	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	116.26	06/2018 -	06/2018
271	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
272	SIX LANING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
273	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
274	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
275	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
276	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
277	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	612.73	03/2018 -	03/2018
278	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
279	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
280	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
281	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
282	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
283	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
284	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
285	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
286	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
287	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
288	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
289	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
290	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
291	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
292	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
	Total		58,533.36 -	60,381.80	6,485.27		
	SHIPPING AND PORTS						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
293	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
294	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	0.14	12/2017 -	12/2017
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
295	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
296	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
297	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
298	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
299	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019
	Total		1,706.06 -	1,706.06	453.40		
	<u>TELECOMMUNICATIONS</u>						
300	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	163.00 -	163.00	-	08/2018 -	08/2018
301	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
302	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	164.90	-	04/2018 -	04/2018
303	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	222.00	-	05/2018 -	05/2018
304	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	-	04/2018 -	04/2018
	Total		917.98 -	924.50	.00		
	<u>URBAN DEVELOPMENT</u>						
305	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
306	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
307	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	57.58	04/2019 -	04/2019
308	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019
309	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
310	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	0.61	03/2020 -	03/2020
	Total		15,712.15 -	15,566.15	5,587.96		
	Grand Total		4,03,470.08	4,19,001.96	58,513.78		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
5	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
8	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
11	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	12/2017	11.60
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		19,751.90 -	21,090.72			
	<u>DEFENCE PRODUCTION</u>						
13	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	3.16
14	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.53
	Total		453.64 -	469.04			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
16	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	02/2018	2.31
	Total		680.64 -	703.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
17	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	05/2017 -	03/2018	13.31
	Total		168.90 -	191.38			
	<u>HEAVY INDUSTRY</u>						
18	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
19	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49
21	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
22	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	03/2018	36.68
23	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
24	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
25	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	03/2018	12.15
26	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
27	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	03/2018	45.83
28	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
30	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50
31	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
32	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
33	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
34	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
35	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
36	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	03/2017	1,933.00 -	2,253.00	12/2020 -	12/2020	16.55
37	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	03/2017	1,740.00 -	1,828.00	12/2020 -	12/2020	5.06
	Total		28,273.91 -	35,027.99			
	<u>POWER</u>						
38	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,559.49	09/2010 -	-	195.28
40	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	06/2018	54.59
41	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	06/2018	5.14
42	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58
43	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	02/2018	23.65
44	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	03/2018	36.79
45	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2018	38.61
46	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	02/2014	908.08 -	969.97	06/2016 -	12/2017	6.82
47	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34
48	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	03/2018	32.69
49	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14
50	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	04/2018	86.27

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
51	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
52	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	03/2018	14.60
53	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2018	26.82
54	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92
55	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	02/2018	36.01
56	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	01/2018	46.77
57	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75
58	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
59	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91
60	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
61	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79
62	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80
63	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51
64	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	03/2018	39.30
65	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
66	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2018	31.17
67	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06
68	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37
69	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60
70	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
71	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
72	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	06/2020	73.65
73	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,329.43	07/2006 02/2015	11/2017	260.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
74	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV [N18000128]	11/2011	723.63 -	882.13	11/2014 -	03/2018	21.90
76	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	05/2018	36.74
77	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
78	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR- II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
79	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
80	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		1,04,449.62 -	1,63,275.45			
	<u>RAILWAYS</u>						
81	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
82	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	1,568.48
83	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
84	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
85	KATHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
86	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26
87	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
88	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
89	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
90	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
91	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
92	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
93	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
94	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
95	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
96	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	- -	03/2018	88.85
97	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
98	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
99	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37
100	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
101	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
102	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	157.10
103	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	12/2022	137.80
104	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	380.00	12/2007 03/2010	03/2017	178.14
105	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
106	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
107	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
108	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
109	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	- -	-	404.39
110	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
111	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
112	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
113	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
114	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
115	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02
116	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
117	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
118	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
119	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	03/2023	534.55
120	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	03/2021	185.52
121	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
122	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
123	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
124	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
125	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	03/2019	8.18
126	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	03/2022	81.31
127	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	371.85	- -	-	276.60
128	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	277.00	- -	-	188.06
129	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
130	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
131	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
132	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
133	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
134	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
135	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
136	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
137	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
138	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
139	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
140	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
141	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
142	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
143	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
144	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
145	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
146	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
147	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
148	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
149	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
150	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
151	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
152	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
153	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	03/2021	341.34
154	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
155	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
156	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
157	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
158	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
159	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
160	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
161	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
162	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
163	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
164	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
165	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
166	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	465.00	03/2011 -	10/2011	173.53
167	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2020	290.00
168	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
169	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
170	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
171	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
172	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	7,300.00	03/2009 -	11/2017	335.48
173	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
174	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	03/2020	27.24
175	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
176	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	-	147.67
177	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
178	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	827.84	- -	08/2018	101.87
179	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38
180	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
181	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
182	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
183	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
184	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,141.70	12/2012 -	-	275.56
185	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	380.00	02/2009 02/2009	06/2017	128.70
186	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
187	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
188	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
189	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
190	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
191	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
192	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
193	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
194	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
195	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
196	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
197	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
198	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
199	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
200	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
201	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
202	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
203	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
204	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
205	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
206	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322	04/2011	190.10 -	350.00	- -	03/2019	84.11
207	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	-	40.49
208	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	685.99	- -	03/2020	14.33
209	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
210	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [N220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
211	AMRAVATI-NARKHER NL(CR) - [N220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	29.56
212	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252]	10/1998	550.00 -	2,815.62	- -	01/2018	411.93
213	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
214	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	- -	08/2017	10.26
215	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	03/2018	142.44
216	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	- -	10/2018	61.80
217	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
218	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	03/2019	41.64
219	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
220	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
221	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
222	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
223	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	- -	12/2020	22.24
224	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
225	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
226	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
227	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
228	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	- -	10/2018	24.47
229	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
230	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	- -	03/2019	14.35
231	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	- -	10/2018	19.86
232	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	- -	03/2019	44.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
233	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
234	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
235	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
236	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
237	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
238	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	250.00	06/2013 -	12/2016	46.18
239	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
240	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
241	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
242	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
243	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
244	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
245	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
246	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
247	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	- -	-	147.28
248	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
249	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
250	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
251	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	- -	03/2018	120.09
252	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
253	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
254	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
255	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
256	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
257	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
258	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
259	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
260	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
261	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
262	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	03/2020	94.45
263	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
264	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38
265	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
266	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
267	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
268	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06
269	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	- -	-	199.29
270	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
271	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
272	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
273	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	- -	03/2024	120.28
274	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	- -	03/2024	25.04
275	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	03/2022	101.93
276	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	03/2023	5.33
277	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	03/2023	10.94
278	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	03/2023	21.21
279	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	-	9.32

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
280	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
281	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
282	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
283	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	08/2015	5.12
284	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
285	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	- -	03/2020	10.01
286	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
287	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
288	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
289	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
290	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
291	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
292	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
293	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	12/2026	277.53
294	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
295	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
296	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
297	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
298	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	Total		1,33,921.02 -	3,24,078.27			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
299	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
300	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
301	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
302	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99
303	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
304	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
305	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
306	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
307	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
308	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25
309	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
310	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
311	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
312	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
313	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
314	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
315	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
316	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
317	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
318	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
319	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
320	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
321	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
322	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06
323	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02
324	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
325	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
326	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
327	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
328	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
329	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
330	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
331	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
332	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
333	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
334	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
335	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
336	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
337	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
338	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
339	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48/O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
340	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
341	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		25,598.69 -	32,656.93			
	<u>SHIPPING AND PORTS</u>						
342	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
343	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	-	18.20
344	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
345	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
346	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
347	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04
348	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
349	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
350	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
351	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	Total		1,639.71 -	2,211.39			
	<u>TELECOMMUNICATIONS</u>						
352	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97
353	MAHARASHTRA ACESS (LOT 1) - [N26000109	08/2017	212.70 -	222.00	05/2018 -	05/2018	4.37

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(December 2017)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		13,546.70 -	24,886.00			
	URBAN DEVELOPMENT						
354	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	03/2018	44.75
355	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
356	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53
357	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	03/2018	37.10
358	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
359	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	Total		17,021.00 -	22,244.19			
	Grand Total		3,52,545.30	6,39,929.73			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above										(December 2017)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044] BHAVINI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,532.63	09/2010 09/2016	06/2018	93	74.68	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010] NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	11,088.00	12/2015 11/2016	11/2019	47	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027] NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,666.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028] NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	69,728.00	27,419.63					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073] AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	40.28	
	Total		314.61 -	441.33	26.44					
	<u>COAL</u>									
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151] NLC, TAMIL NADU	05/2016	687.28 -	767.00	733.23	06/2017 -	12/2017	6	11.6	
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092] MCL, ODISHA	01/2005	302.96 -	302.96	331.06	03/2010 -	03/2018	96	0	
8	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033] NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	397.54	03/2012 -	03/2018	72	87.58	
9	RKP OCP PHASE-I - [N06000079] SCCL, TELANGANA	03/2010	209.78 -	209.78	144.33	03/2015 -	03/2018	36	0	
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080] SCCL, TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	199.85	03/2014 -	03/2018	48	0	
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24	0	
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	347.32	03/2016 -	03/2018	24	0	
14	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	153.43	03/2016 -	03/2018	24	0	
15	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	121.94	06/2015 -	03/2018	33	0	
16	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	147.18	03/2016 -	03/2018	24	-3.5	
17	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,039.57	12/2015 04/2018	04/2018	28	0	
18	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	156.92	05/2014 -	04/2018	47	0	
19	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	153.87	04/2014 -	04/2018	48	0	
20	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	282.30	03/2017 -	05/2018	14	0	
21	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	405.44	03/2013 -	11/2018	68	0	
23	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	163.85	03/2012 -	03/2019	84	80.24	
24	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	195.09	03/2010 -	03/2019	108	0	
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	259.50	03/2012 -	03/2019	84	0	
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	221.47	03/2013 -	03/2019	72	0	
27	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.06	03/2012 -	03/2019	84	0	
28	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.85	03/2012 -	03/2019	84	0	
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.15	03/2014 -	03/2019	60	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
31	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	207.23	04/2015 -	04/2019	48	0	
32	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	320.01	06/2015 09/2019	09/2019	51	-51.37	
33	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	135.12	03/2015 03/2020	03/2020	60	201.44	
34	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	
35	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	0	forest clearance
36	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	.34	03/2015 -	03/2020	60	-32.3	
37	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	114.6	
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	67.63	07/2016 -	03/2020	44	0	
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	321.06	03/2018 -	03/2020	24	0	Rehabilitation of PAFs: Process of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
40	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	120.77	07/2012 03/2017	03/2021	104	0	
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	267.42	03/2015 -	03/2021	72	-2.14	Diversion of forest land
42	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	16.86	
	Total		20,254.10 -	20,473.06	12,165.38					
	<u>FERTILISERS</u>									
43	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 -	494.00	413.01	12/2017 02/2018	02/2018	2	2.31	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	103.35	11/2016 04/2019	04/2019	29	5.89	
	Total		680.64 -	703.44	516.36					
	STEEL									
45	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	196.21	05/2016 -	12/2017	19	0	
46	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	12.04	
47	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,303.09	03/2013 -	02/2018	59	0	
48	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	
49	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	528.08	12/2017 -	05/2018	5	0	
50	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	200.59	10/2017 -	07/2018	9	0	
51	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	
52	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	53.91	07/2018 -	09/2018	2	0	
53	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	13,054.00	05/2015 10/2018	10/2018	41	0	
54	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	715.85	12/2017 -	10/2018	10	-12.53	
55	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	23.78	08/2018 -	10/2018	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
56	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
57	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
58	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	63.94	09/2018 -	01/2019	4	0	
59	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	1,837.55	04/2018 -	02/2019	10	0	
60	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	234.69	10/2016 -	03/2019	29	42.39	
61	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	Total		46,561.67 -	46,373.46	36,549.27					
	<u>PETROLEUM</u>									
62	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL, TAMIL NADU	02/2016	367.11 -	367.11	244.25	04/2017 -	01/2018	9	0	
63	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA	05/2016	215.38 215.38	215.38	175.07	06/2017 01/2018	01/2018	7	0	
64	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	171.84	11/2016 -	02/2018	15	0	
65	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL, GUJARAT	02/2016	931.00 -	931.00	435.08	07/2017 -	02/2018	7	0	
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,183.39	05/2013 03/2018	03/2018	58	45.83	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
67	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 -	2,665.65	1,671.57	03/2015 03/2018	03/2018	36	29.42	
68	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 -	600.17	703.97	12/2014 03/2018	03/2018	39	0	
69	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 723.40	723.40	422.29	10/2014 03/2018	03/2018	41	133.5	
70	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 4,259.59	5,637.00	4,050.69	04/2016 03/2018	03/2018	23	36.68	
71	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	256.41	147.19	12/2016 -	03/2018	15	12.15	
72	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 -	173.28	164.86	01/2017 03/2018	03/2018	14	-4.28	
73	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018	6	0	
74	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 -	2,592.17	2,084.15	05/2014 05/2018	05/2018	48	0	
75	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,554.21	05/2017 05/2018	05/2018	12	1.87	
76	PIPELINE REPLACEMENT PROJECT - 4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018	12	-27.64	
77	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC, GUJARAT	09/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018	23	-20.81	
78	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	2,248.49	09/2017 06/2018	06/2018	9	36.22	
79	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.89	2,065.39	03/2013 09/2018	09/2018	66	-3.5	
80	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	438.84	134.50	03/2017 -	11/2018	20	24.47	

[illegible]

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
92	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,971.62	08/2014 12/2017	12/2017	40	27.6	
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 969.97	969.97	732.28	06/2016 02/2018	12/2017	18	6.82	
94	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	419.93	08/2016 10/2017	12/2017	16	0	
95	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	341.00	246.39	06/2012 -	01/2018	67	46.77	S/S almost ready since Jun'12. Line completed except 5 kms near Yelahanka, which is held up due to long pending ROW problem (high compensation agitation). ROW issues resolved with support from State Admn. through revised compensation. Work under progress.
96	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	165.34	03/2017 10/2017	01/2018	10	0	Generation project delayed. (Gen. project ant. by Feb'18). Work slowed-down to the extent possible to match Generation.
97	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,565.00	11/2017 -	01/2018	2	0	
98	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,186.86	01/2016 -	02/2018	25	61.5	
99	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,575.15	08/2013 12/2017	02/2018	54	23.65	05/08 line completed. Balance lines (linked to Gen. Proj.) to be completed matching with Generation Project. Kaneng HEP scheduled in Mar'18 and Lower Subhansiri HEP is schedule uncertain.(agitation against big dams).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
100	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,425.08	11/2012 12/2017	02/2018	63	36.01	07/08 line & 06/07 sub station completed progressively from Oct'12 to Jun'16 . Down stream 220KV line of state at Daltonganj required matching with readiness of Sasaram - Daltonganj line & Daltonganj sub station anticipated by Feb'18.
101	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	14,795.00	01/2017 07/2017	02/2018	13	0	Slow progress in execution of CHP
102	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	186.30	11/2017 -	02/2018	3	0	
103	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,099.06	12/2009 03/2018	03/2018	99	147.51	
104	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,544.55	08/2013 03/2018	03/2018	55	133.06	
105	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,488.99	01/2015 03/2018	03/2018	38	16.58	03 out of 04 line alongwith Alipurduar & Agra HVDC terminal completed. Gen. Proj.(Punatsangchu-I HEP in Bhutan) getting delayed. Also line getting completed ahead of Gen. Proj. (anticipated in 2019-20). Line proposed to be used as contingency arrangement for evacuation of power from Mangdechhu HEP. (Gen. expected by March 2018).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
106	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,589.80	12/2012 02/2018	03/2018	63	36.79	13/17 line & 05/07 S/s completed. Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Arunachal Pradesh (Tezu-Namsai line) affected due to compensation issues & land ownership disputes and further their commissioning linked to readiness of down stream system (being implemented under NER comprehensive scheme). Mizoram (Silcher-Melriat line) is affected due to tree cutting. Issue getting resolved with support of state/Distt. Admn.
107	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,357.64	09/2014 06/2017	03/2018	42	39.3	02 out of 03 line completed. Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Obstruction are being removed progressively with the help of Police protection.
108	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	364.29	08/2014 12/2017	03/2018	43	43.37	Implementation affected due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Work under progress with the help of Police protection.
109	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	136.45	09/2014 09/2017	03/2018	42	0	Supply has been completed in package. Presently there are only 02 lines balance which are under construction lines and having ROW issues.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	727.62	11/2014 06/2017	03/2018	40	21.9	ROW/tree cutting issues resolved. Completion being expedited through mobilization from other sources in Dehradun-Abdullapur line. Progress of Dulhasti-Kishenpur line, work affected due to severe ROW in Doda distt. and disturbance in J&K. Now work in progress with Police protection.
111	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	121.98	04/2016 12/2017	03/2018	23	0	
112	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	374.70	11/2016 11/2017	03/2018	16	5.34	Implementation affected due to delay in supply of transformers due to testing issues and other transportation constraints. Now transformer outsourced by M/s GE, manufacturing/supply under progress.
113	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	140.76	03/2016 07/2017	03/2018	24	32.69	Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.
114	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	231.75	02/2017 06/2017	03/2018	13	30.37	Implementation affected due to delay in Transformer supply (failure in testing). Transformer supply outsourced, mfg./supply under progress.
115	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	134.45	02/2016 08/2017	03/2018	25	14.6	Implementation affected due to delay in manufacturing of Reactors by Vendor. Reactors now supplied & being commissioned progressively. Work was under hold due to delay in availability of shut down at Rourkela. Now work in progress. Transformer supply also delayed in Gaya S/s.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
116	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	733.18	04/2017 03/2018	03/2018	11	0	Work has been slowed-down to match with Generation (ant. by Mar'18).
117	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,091.00	12/2015 -	03/2018	27	42.83	
118	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	6,860.00	09/2011 06/2017	04/2018	79	86.27	
119	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	585.89	06/2015 12/2017	05/2018	35	36.74	765KV Bay commissioned in Jan'17 matching with associated line. ICT's ready. Commissioning matching with down-stream line (under TBCB sch. Apr'19). TBCB line being expedited & now expected by May/Jun'18.
120	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	653.52	09/2010 12/2017	06/2018	93	54.59	02/03 line line completed. Severe ROW problem in balance LILO line (400KV D/C LILO at Navi Mumbai, being completed using underground cable) continue. Cable burnt/ damaged by miscreants. Also down stream network at Navi Mumbai is not ready. Critical.
121	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,489.03	10/2012 02/2018	06/2018	68	5.14	8 out of 9 lines completed progressively by Dec'16. Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & severe ROW problem also being encountered, apart from poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
122	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,048.50	12/2015 12/2017	06/2018	30	0	Generation project delayed/uncertain. Implementation also affected due to severe ROW problem & huge forest involvement. Working permission for Chattisgarh portion issued in Nov'17.
123	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,174.49	04/2016 09/2017	06/2018	26	38.61	Farakka - Gokarna portion of Rajarhat - Purnea line including both LLO's at Farakka & Gokarna commissioned in Mar'17. Implementation affected due to severe ROW problem. Work in Rajarhat S/s. area almost standstill since last 9-10 months due to protest/agitation by locals who not allowing to enter in S/s. Work resumed in Oct'17 again stopped due to protest w.e.f 01.12.17. Matter being followed up at all levels for early resolution & efforts being made to complete by Jun'18
124	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	393.44	06/2016 02/2018	06/2018	24	0	01 out of 02 completed. Implementation affected due to severe ROW problem at singrauli end. Work also affected due to poor performance by executing agency, being expedited with support from Powergrid.
125	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,707.65	03/2018 -	06/2018	3	0	Implementation affected due to delay in land acquisition & likely delay in off-shore supplies.
126	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	169.37	03/2018 -	06/2018	3	26.82	Work badly affected due to disturbance in Kashmir and delay in finalisation of compensation by PNC. To resolve compensation issue matter taken up with State Govt.. State/MoP help required. All efforts shall be made to complete Kishanganga -Amargarh line matching with Gen. (ant. by Jan'18).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
127	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	06/2018	8	0	Gen. project delayed. Work on ATS are being slowed-down to extent possible to match with Generation (ant. by Sep'19).
128	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	176.23	11/2017 -	06/2018	7	0	Generation project ant. in 2019-20/ beyond. Work slowed-down to extent possible to match the generation
129	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,296.77	04/2018 -	07/2018	3	0	Implementation affected due to severe ROW problem & forest clearance (awaited). Generation project delayed (ant. by Jul'18). Work slowed-down to the extent possible to match Generation.
130	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,969.63	11/2008 09/2018	09/2018	118	22.93	06/07 lines & 02/02 S/stn completed ahead of Generation. Implementation of balance 01 line (Edamon-Muvattupuzha line) is affected due to severe ROW problem (long pending). Problem being addressed progressively as per latest Revised G.O. of 30.07.15 (compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.). Works under progress. Site is getting police protection as per requirement from State admin.
131	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.99	06/2014 03/2018	09/2018	51	31.17	01 out of 02 lines completed. Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work re-award in Dec'17.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
132	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	477.43	09/2017 -	09/2018	12	0	
133	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,213.54	09/2017 -	09/2018	12	30.49	Khalsti & Leh S/Stn. and 220LV Leh – Khalsti line were charged on 31 Oct'17. Implementation affected due to delay in land acquisition of Kargil S/s. Land handed over by DM in Dec'16. Forest clearance received from Govt. of J&K. Tree cutting to be expedited by J&K forest deptt. in 25 locs. ROW clearance of 12 locs. to be expedited. Increased BE allocation from 250 Cr. To 820 Cr. Required.
134	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,597.22	09/2009 -	12/2018	111	114.28	
135	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,206.00	11/2016 12/2017	12/2018	25	0	
136	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	168.86	07/2017 -	12/2018	17	27.92	03 elements out of 04 elements completed. Project commissioned except Bus Reactor at Yelankha As per MoM of 40th SCPSPSR held on 19.11.16. Procurement being taken up after resolution
137	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11	5.91	
138	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	478.69	12/2016 -	12/2018	24	37.96	
139	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,892.00	06/2017 12/2017	01/2019	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
140	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	8,413.00	09/2017 03/2018	01/2019	16	0	Slow progress in sand lifting
141	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57	49.41	
142	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	0	
143	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	6,615.00	08/2018 -	03/2019	7	0	
144	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	148.06	02/2014 02/2018	03/2019	61	50.75	IInd stage forest clearance for Power Evacuation Arrangement.
145	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	243.37	01/2018 -	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through Tiger reserve area. Wildlife clearance proposal submitted. SBWL meeting yet to be held. Clearance awaited. Alternate arrangements being made for evacuation (through contingency scheme) matching with Generation.
146	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	41.97	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). However, only 400KV line bays are being made at Maharani bag. Award under progress. Expected by Jan'18.
147	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,400.00	03/2019 -	09/2019	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
148	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42	4,754.42	466.74	12/2018	12/2019	12	0	28 packages out of 44 packages award. Balance award under progress. Award have been delayed due to poor response & high prices quoted by bidders. Out of 116 Sub stations land for only 53 nos land available. Non-availability of 27 nos. land for awarded Sub-station. Critical. Approval of new elements proposed by Govt. of Arunachal Pradesh.
149	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33	5,111.33	386.29	12/2018	12/2019	12	0	47 packages out of 55 packages award. Balance award under progress). Award have delayed due to poor response & high prices quoted by bidders.
150	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48	3,846.30	3,359.00	03/2013 06/2019	03/2020	84	29.14	
151	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,932.00	01/2011 05/2018	06/2020	113	73.65	
152	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58	14,366.58	5,674.00	02/2019 02/2020	09/2020	19	0	
153	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58	2,491.58	1,312.24	06/2013	11/2020	89	0	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.
154	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,443.93	02/2016 09/2019	12/2020	58	137.73	Law and order problem: Dharna at crusher plant area has been called off on 17.11.17 , however, continuous support of Distt. Administration is required for maintaining law and order.
155	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 1,592.34	1,381.84	294.00	09/2019	03/2021	18	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
164	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	520.89	
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	343.00	362.24	03/2009 03/2009	12/2017	105	157.1	
166	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	555.00	500.67	03/2010 -	12/2017	93	70.82	
167	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	0	
168	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,020.64	03/2010 -	03/2018	96	49.88	
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,450.00	4,892.39	04/2008 12/2011	06/2018	122	263.33	
170	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193	1017.84	
172	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	722.31	03/2016 -	12/2018	33	0	
173	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	491.31	03/2016 -	12/2018	33	29.06	
174	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,040.00	2,748.23	12/2008 -	03/2019	123	314.73	
175	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	
176	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	1.06	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
177	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	0	
178	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	895.00	676.07	03/2014 -	06/2019	63	37.02	
179	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
180	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.07	583.08	02/2015 -	12/2019	58	556.04	
181	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	343.71	02/2006 -	12/2019	166	48.26	
182	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,143.70	514.27	03/2015 -	12/2019	57	37.84	
183	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	678.01	03/2004 -	03/2020	192	259.68	
184	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	
185	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	6,985.58	03/2011 -	03/2020	108	1227.45	
186	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,478.11	03/2008 06/2008	03/2020	144	145.63	
187	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,407.41	03/2014 -	03/2020	72	324.3	
188	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,825.65	04/2014 -	03/2020	71	642.73	
189	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
190	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-2.17	
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	406.14	03/2015 -	03/2020	60	252.94	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
192	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,541.16	03/2016 -	12/2020	57	7.78	
193	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	37.12	03/2021 -	03/2022	12	0	
194	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	22.36	03/2021 -	03/2022	12	0	
195	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
196	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	226.23	
197	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	Total		42,047.55 -	1,14,569.54	54,505.85					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
198	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	12/2017	106	28.93	
199	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	12/2017	104	92.75	
200	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	12/2017	104	0	
201	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116	0	
202	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	12/2017	101	68.99	
203	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63	114.56	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
204	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,373.60	05/2013 -	12/2017	55	0	
205	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64	0	
206	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40	0	
207	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,063.52	03/2013 -	12/2017	57	0	
208	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55	0	
209	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	0	
210	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	0	
211	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49	0	
212	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42	0	
213	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,416.68	08/2013 -	12/2017	52	0	
214	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	-	06/2014 -	12/2017	42	0	
215	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,724.78	09/2014 -	12/2017	39	0	
216	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47	0	
217	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	-	10/2013 -	12/2017	50	-11	
218	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	856.59	06/2015 -	12/2017	30	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
219	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	-	04/2015 -	12/2017	32	0	
220	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
221	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	-	01/2016 -	12/2017	23	0	
222	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	-	10/2011 -	12/2017	74	0	
223	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28	0	
224	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,479.14	07/2017 -	01/2018	6	0	
225	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117	0	
226	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15	0	
227	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	80.68	
228	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95	42.25	
229	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	106.5	
230	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	0	
231	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	0	
232	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	0	
233	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55	0	
234	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44	0	
235	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	395.20	06/2014 -	03/2018	45	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
236	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	0	
237	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,374.50	09/2016 -	03/2018	18	0	
238	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	252.39	09/2017 -	03/2018	6	0	
239	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,424.00	08/2016 -	03/2018	19	0	
240	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,094.55	06/2012 -	03/2018	69	0	
241	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
242	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	0	
243	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
244	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	0	
245	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	0	
246	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	0	
247	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
248	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	286.02	06/2016 -	06/2018	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
249	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	97.35	07/2016 -	07/2018	24	0	
250	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	730.88	11/2017 -	08/2018	9	0	
251	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
252	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	0	
253	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	0	
254	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	0	
255	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	0	
256	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	0	
257	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
258	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
259	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(December 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
260	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	Total		55,031.75 -	58,574.37	26,361.66					
	<u>SHIPPING AND PORTS</u>									
261	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141	300	
262	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
263	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20	-57.02	
	Total		1,116.39 -	1,527.36	550.92					
	<u>TELECOMMUNICATIONS</u>									
264	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	0	
265	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47	84.97	
	Total		13,752.26 -	25,082.26	6,832.30					
	<u>URBAN DEVELOPMENT</u>									
266	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	30.53	
267	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD, KERALA	07/2015	154.00 -	154.00	74.54	11/2015 -	12/2017	25	0	
268	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00 -	388.00	309.07	05/2017 02/2018	02/2018	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
269	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	0	land at few location is not available. Target will be worked out when these land pockets are available.
270	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	184.89	12/2015 03/2018	03/2018	27	0	
271	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 349.33	349.33	269.50	03/2016 12/2017	03/2018	24	44.75	
272	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72	-16.77	
273	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	0	
274	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	528.94	12/2015 -	03/2018	27	0	
275	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	479.87	414.62	03/2015 12/2017	03/2018	36	37.1	
276	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD, MADHYA PRADESH	12/2016	164.00 -	164.00	69.25	01/2018 05/2018	05/2018	4	0	
277	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	122.43	08/2016 -	06/2018	22	0	
278	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	126.71	11/2014 -	10/2018	47	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(December 2017)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
279	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
280	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	38.76	03/2016 -	12/2018	33	0	
281	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	39.73	04/2018 -	05/2019	13	0	
282	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
283	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
284	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21	0	
285	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	land acquisition
286	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,283.30	1,592.00	157.53	10/2019 -	03/2020	5	30.58	
287	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	.20	06/2017 06/2020	06/2020	36	.57	
	Total		99,001.16 -	1,04,189.97	56,611.49					
	Grand Total		6,27,769.77	7,65,358.56	4,39,112.58					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(December 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69	93
	Total		3,492.00 -	6,100.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>South-Eastern Coal Fields Limited</u>							
3	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Singareni Colliers Company Limited</u>							
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60	60
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24	84
	<u>Northern Coal Fields Limited</u>							
6	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
	<u>Singareni Colliers Company Limited</u>							
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>Neyveli Lignite Corporation</u>							
8	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	12/2017	11.60	6
	Total		1,929.87 -	3,000.82				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
10	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	02/2016	482.85 -	494.00	12/2017 -	02/2018	2.31	2
	Total		680.64 -	703.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
11	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	191.38	05/2017 -	03/2018	13.31	10
	Total		168.90 -	191.38				
	<u>HEAVY INDUSTRY</u>							
	<u>Natrip Implementation Society</u>							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
	<u>Oil & Natural Gas Corporation Limited</u>							
13	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
	<u>Oil India Limited</u>							
14	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	03/2018	12.15	15
	<u>Hindustan Petroleum Corporation Limited</u>							
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	03/2018	133.50	41
	<u>Oil India Limited</u>							
16	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47	20
	<u>Indian Oil Corporation Limited</u>							
17	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
	<u>Oil & Natural Gas Corporation Limited</u>							
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	03/2018	45.83	58
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Indian Oil Corporation Limited</u>							
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22	9
	<u>Oil & Natural Gas Corporation Limited</u>							
21	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	03/2018	36.68	23
22	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	Total		17,529.25 -	22,025.87				
	<u>POWER</u>							
	<u>Power Grid Corporation Of India Limited</u>							
23	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	03/2018	32.69	24
	<u>Thdc India Limited</u>							
24	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
	<u>Power Grid Corporation Of India Limited</u>							
25	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	03/2018	14.60	25
26	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92	17
27	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	01/2018	46.77	67
28	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2018	26.82	3
29	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37	13
30	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37	43
	<u>Satluj Jal Vidyut Nigam Limited</u>							
31	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	<u>Power Grid Corporation Of India Limited</u>							
32	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	06/2018	54.59	93
33	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2018	31.17	51
34	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	05/2018	36.74	35

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
35	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164 <u>North East Electric Power Corporation</u>	05/2014	522.29 -	550.18	11/2016 -	03/2018	5.34	16
36	PARE HYDRO ELECTRIC PROJECT - [N18000045 <u>Power Grid Corporation Of India Limited</u>	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06	55
37	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	882.13	11/2014 -	03/2018	21.90	40
38	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159	02/2014	908.08 -	969.97	06/2016 -	12/2017	6.82	18
39	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83	27
40	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	07/2010	1,272.80 -	1,731.10	11/2012 -	02/2018	36.01	63
41	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155 <u>Thdc India Limited</u>	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2018	38.61	26
42	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010 <u>Power Grid Corporation Of India Limited</u>	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73	58
43	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60	40
44	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
45	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
46	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	09/2011	1,940.13 -	2,702.65	09/2014 -	03/2018	39.30	42
47	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080 <u>North East Electric Power Corporation</u>	02/2010	2,144.00 -	2,932.88	12/2012 -	03/2018	36.79	63
48	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239 <u>National Thermal Power Corporation</u>	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51	99
49	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014 <u>National Hydro-Electric Power Corporation</u>	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14	84
50	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50	25
51	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>National Thermal Power Corporation</u>							
52	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	04/2018	86.27	79
	<u>Power Grid Corporation Of India Limited</u>							
53	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	03/2018	16.58	38
54	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	06/2018	5.14	68
	<u>National Thermal Power Corporation</u>							
55	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41	57
56	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	06/2020	73.65	113
	<u>Power Grid Corporation Of India Limited</u>							
57	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	02/2018	23.65	54
	<u>National Thermal Power Corporation</u>							
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91	11
	Total		85,911.47 -	1,23,456.70				
	<u>RAILWAYS</u>							
	<u>Rail Vikas Nigam Ltd.</u>							
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	157.10	105
	<u>South Central Railway</u>							
60	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
	<u>Rail Vikas Nigam Ltd.</u>							
61	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04	58
	<u>West Central Railway</u>							
62	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Rail Vikas Nigam Ltd.</u>							
63	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26	166
	<u>Western Railway</u>							
64	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
	<u>Rail Vikas Nigam Ltd.</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
65	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82	93
	<u>South East Central Railway</u>							
66	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
	<u>Metropolitan Rapid Transport Projects</u>							
67	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
	<u>North East Frontier Railway</u>							
68	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
	<u>North Central Railway</u>							
69	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
	<u>Rail Vikas Nigam Ltd.</u>							
70	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06	33
	<u>North Western Railway</u>							
71	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02	63
	<u>Rail Vikas Nigam Ltd.</u>							
72	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88	96
	<u>North East Frontier Railway</u>							
73	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
74	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73	123
	<u>Rail Vikas Nigam Ltd.</u>							
75	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
	<u>North East Frontier Railway</u>							
76	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
	<u>North Western Railway</u>							
77	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84	57
	<u>North East Frontier Railway</u>							
78	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
	<u>Eastern Railways</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
79	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
	<u>North Central Railway</u>							
80	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
	<u>North East Frontier Railway</u>							
81	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
82	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33	122
	<u>Northern Railway</u>							
83	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84	193
	<u>Rail Vikas Nigam Ltd.</u>							
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78	57
	<u>Metropolitan Rapid Transport Projects</u>							
85	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		27,085.68 -	99,616.22				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
86	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
87	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68	112
88	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99	101
89	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75	104
90	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25	95
91	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93	106
92	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76
93	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		3,804.49 -	7,347.92				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>SHIPPING AND PORTS</u>							
	<u>Port Trust</u>							
94	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00	141
	<u>Mumbai Port Trust</u>							
95	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		516.39 -	1,269.46				
	<u>STEEL</u>							
	<u>Hindustan Steelwork Construction Limited</u>							
96	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04	12
	<u>Rastriya Ispat Nigam Limited</u>							
97	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39	29
	Total		545.61 -	715.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
98	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97	47
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
99	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
100	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	03/2018	44.75	24
101	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	03/2018	37.10	36
102	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(December 2017)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
103	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	<u>Chennai Metro Rail Ltd</u>							
104	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53	24
	Total		17,021.00 -	22,244.19				
	Grand Total		1,74,051.91	3,15,604.03				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	10/2017
	Total		309.46 -		
	<u>COAL</u>				
	<u>Eastern Coal Fields Limited</u>				
2	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	05/2017
	<u>Singareni Colliers Company Limited</u>				
3	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	<u>Bharat Coking Coal Limited</u>				
4	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	Total		1,595.80 -		
	<u>STEEL</u>				
	<u>Hindustan Steelwork Construction Limited</u>				
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
6	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
7	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
8	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
9	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
10	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Steel Authority Of India Limited (Sail)</u>				
11	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
12	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		6,774.27 -		
	<u>PETROLEUM</u>				
	<u>Oil India Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above				(December 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	03/2015 -	11/2017
	<u>Indian Oil Corporation Limited</u>				
14	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	12/2016 06/2017	06/2017
15	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL, JHARKHAND	04/2011	191.96 -	05/2015 06/2017	06/2017
16	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA	03/2014	238.50 -	03/2017 10/2017	10/2017
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	11/2017
	<u>Chennai Petroleum Corporation Limited</u>				
18	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	03/2013	3,110.36 -	11/2015 -	11/2017
	<u>Hindustan Petroleum Corporation Limited</u>				
19	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL, RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Bharat Petroleum Corporation Limited</u>				
20	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	Total		8,186.17 -		
	<u>POWER</u>				
	<u>Damodar Valley Corporation</u>				
21	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
	<u>National Thermal Power Corporation</u>				
22	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 12/2016	12/2016
	<u>Damodar Valley Corporation</u>				
23	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,138.41	12/2011 03/2016	02/2017
	<u>National Thermal Power Corporation</u>				
24	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	09/2016 03/2017	03/2017
	<u>North East Electric Power Corporation</u>				
25	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,329.43	07/2006 11/2017	11/2017
	<u>National Hydro-Electric Power Corporation</u>				
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>North East Electric Power Corporation</u>				
27	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-
	<u>National Thermal Power Corporation</u>				
28	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 1,801.07	08/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
29	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>National Hydro-Electric Power Corporation</u>				
30	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	02/2016 -	-
	Total		30,862.10 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
31	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 09/2017	09/2017
32	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-
33	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		749.18 -		
	<u>RAILWAYS</u>				
	<u>North East Frontier Railway</u>				
34	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009
35	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011
36	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
37	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	03/2014
38	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	11/2014
	<u>East Coast Railway</u>				
39	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015
	<u>North East Frontier Railway</u>				
40	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	08/2015
41	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016
42	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	05/2016
	<u>Rail Vikas Nigam Ltd.</u>				
43	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016
44	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	03/2017
	<u>Metropolitan Rapid Transport Projects</u>				
45	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 495.74	06/2013 -	03/2017
	<u>Rail Vikas Nigam Ltd.</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
46	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	06/2017
	<u>North Eastern Railway</u>				
47	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2017
	<u>North East Frontier Railway</u>				
48	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	11/2017
	<u>North Central Railway</u>				
49	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
	<u>South Central Railway</u>				
50	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-
	<u>Central Railways</u>				
51	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
52	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
	<u>Southern Railway</u>				
53	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
	<u>Northern Railway</u>				
54	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
	<u>Southern Railway</u>				
55	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
	<u>South Western Railway</u>				
56	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
	<u>North Eastern Railway</u>				
57	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-
	<u>South Eastern Railway</u>				
58	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
59	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
	<u>South Central Railway</u>				
60	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
	<u>East Central Railways</u>				
61	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
	<u>North Central Railway</u>				
62	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
	<u>North East Frontier Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
	<u>South Central Railway</u>				
64	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-
	<u>North Eastern Railway</u>				
65	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
	<u>East Central Railways</u>				
66	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
	<u>Northern Railway</u>				
67	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
	<u>Southern Railway</u>				
68	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
	<u>Metropolitan Rapid Transport Projects</u>				
69	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
	<u>South Central Railway</u>				
70	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-
	<u>Eastern Railways</u>				
71	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
	<u>South Western Railway</u>				
72	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
	<u>Northern Railway</u>				
73	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
	<u>East Central Railways</u>				
74	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
75	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
76	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
77	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
	<u>North Eastern Railway</u>				
78	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
	<u>North Central Railway</u>				
79	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>South East Central Railway</u>				
80	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>East Central Railways</u>				
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
	<u>Southern Railway</u>				
82	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
83	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
84	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-
	<u>Northern Railway</u>				
85	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
	<u>Eastern Railways</u>				
86	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
	<u>Railway Electrification</u>				
87	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Eastern Railway</u>				
88	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
	<u>South Western Railway</u>				
89	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
	<u>North Western Railway</u>				
92	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
	<u>Eastern Railways</u>				
93	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
94	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
95	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-
96	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
97	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-
	<u>Western Railway</u>				
98	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
99	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
	<u>North Eastern Railway</u>				
100	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
101	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
	<u>Western Railway</u>				
102	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
103	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
104	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
	<u>North Western Railway</u>				
105	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
106	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
107	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
108	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
	<u>South Eastern Railway</u>				
109	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
110	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
111	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
112	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
113	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
114	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
	<u>East Central Railways</u>				
115	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
	<u>East Coast Railway</u>				
116	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
117	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
118	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
119	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
120	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
	<u>East Central Railways</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
121	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
122	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
123	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
124	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
125	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
126	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
127	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
128	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
129	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
130	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
	<u>Southern Railway</u>				
131	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-
132	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
133	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
134	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
135	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
136	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
137	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
138	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
139	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
	<u>North East Frontier Railway</u>				
140	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
	<u>Metropolitan Rapid Transport Projects</u>				
141	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
142	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>Southern Railway</u>				
143	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
	<u>Eastern Railways</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
144	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
145	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
146	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
147	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-
148	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-
149	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
150	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
151	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
152	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
153	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
154	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
155	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
156	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
157	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
158	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
159	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
160	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
161	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
162	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
163	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
164	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
165	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
166	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above				(December 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
167	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
168	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
	<u>Central Railways</u>				
169	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- -	-
170	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-
	<u>South Western Railway</u>				
171	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
172	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
173	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
	<u>South Central Railway</u>				
174	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
175	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
176	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
177	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
	<u>Northern Railway</u>				
178	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
179	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
180	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
181	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
182	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
183	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
184	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
	<u>South Western Railway</u>				
185	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
186	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
187	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
188	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above				(December 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>South Western Railway</u>				
189	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
	<u>Northern Railway</u>				
190	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
	<u>South Central Railway</u>				
191	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
192	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
193	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
194	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
	<u>Northern Railway</u>				
195	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
196	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
197	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
198	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
199	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
200	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
201	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
202	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
	<u>South Western Railway</u>				
203	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
204	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
205	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
	<u>Eastern Railways</u>				
206	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
207	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>South Central Railway</u>				
208	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
	<u>South Eastern Railway</u>				
209	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
	<u>South Western Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
210	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
	<u>South Eastern Railway</u>				
211	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
	<u>East Coast Railway</u>				
212	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
	<u>North Eastern Railway</u>				
213	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
	<u>South Eastern Railway</u>				
214	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
	<u>South Western Railway</u>				
215	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
	<u>East Central Railways</u>				
216	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
	<u>North Western Railway</u>				
217	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
218	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
	<u>South Western Railway</u>				
219	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
	<u>North Eastern Railway</u>				
220	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
221	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
	<u>South Central Railway</u>				
222	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
223	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
224	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
225	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
226	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>East Central Railways</u>				
227	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Southern Railway</u>				
228	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
229	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
	<u>South Eastern Railway</u>				
230	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	Total		1,88,796.53 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Public Works Dept Of State</u>				
231	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
232	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
233	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
234	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
235	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
236	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
237	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
	<u>Ministry Of Road Transport And Highways</u>				
238	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014
239	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
	<u>Public Works Dept Of State</u>				
240	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
	<u>National Highways Development Project</u>				
241	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
	<u>Public Works Dept Of State</u>				
242	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
243	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
244	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
	<u>National Highways Development Project</u>				
245	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
	<u>Ministry Of Road Transport And Highways</u>				
246	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
247	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
	<u>Public Works Dept Of State</u>				
248	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
249	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
250	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
	<u>National Highways Development Project</u>				
251	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
	<u>Ministry Of Road Transport And Highways</u>				
252	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
253	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
	<u>Public Works Dept Of State</u>				
254	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
255	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
	<u>Ministry Of Road Transport And Highways</u>				
256	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
257	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
	<u>Public Works Dept Of State</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above				(December 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
259	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
	<u>Ministry Of Road Transport And Highways</u>				
260	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
	<u>Public Works Dept Of State</u>				
261	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
262	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
	<u>Ministry Of Road Transport And Highways</u>				
263	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
	<u>National Highways Development Project</u>				
265	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
	<u>Ministry Of Road Transport And Highways</u>				
266	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
	<u>National Highways Development Project</u>				
267	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
	<u>Public Works Dept Of State</u>				
268	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
	<u>Ministry Of Road Transport And Highways</u>				
269	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
270	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
	<u>National Highways Development Project</u>				
271	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
272	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
	<u>Public Works Dept Of State</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
273	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
274	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
275	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016
	<u>Public Works Dept Of State</u>				
276	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
277	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
278	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
	<u>Ministry Of Road Transport And Highways</u>				
279	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
	<u>Public Works Dept Of State</u>				
280	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
281	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
282	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
283	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
284	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
285	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
	<u>National Highways Authority Of India</u>				
286	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017
	<u>National Highways Development Project</u>				
287	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
	<u>Public Works Dept Of State</u>				
288	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways Development Project</u>				
289	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
290	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
	<u>Ministry Of Road Transport And Highways</u>				
291	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
292	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017
293	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
294	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
	<u>Public Works Dept Of State</u>				
295	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	05/2017
	<u>National Highways Development Project</u>				
296	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017
	<u>Public Works Dept Of State</u>				
297	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017
	<u>National Highways Development Project</u>				
298	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017
299	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017
	<u>National Highways Authority Of India</u>				
300	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017
	<u>National Highways Development Project</u>				
301	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017
	<u>Ministry Of Road Transport And Highways</u>				
302	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017
	<u>National Highways Authority Of India</u>				
303	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
304	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	07/2017
	<u>National Highways Development Project</u>				
305	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017
	<u>National Highways Authority Of India</u>				
306	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017
307	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017
308	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017
309	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017
	<u>Public Works Dept Of State</u>				
310	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	08/2017
311	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017
	<u>National Highways Authority Of India</u>				
312	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	09/2017
313	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017
314	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017
315	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017
	<u>Public Works Dept Of State</u>				
316	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017
	<u>National Highways Authority Of India</u>				
317	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017
318	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017
319	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017
320	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017
321	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2017
322	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017
323	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017
324	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017
325	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways Development Project</u>				
326	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	10/2017
	<u>Public Works Dept Of State</u>				
327	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017
	<u>Ministry Of Road Transport And Highways</u>				
328	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017
329	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017
330	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
331	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017
	<u>National Highways Authority Of India</u>				
332	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	11/2017
333	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017
334	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017
335	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017
	<u>Public Works Dept Of State</u>				
336	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017
	<u>Ministry Of Road Transport And Highways</u>				
337	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017
338	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017
	<u>National Highways Authority Of India</u>				
339	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017
340	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017
341	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017
342	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
343	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017
	<u>Public Works Dept Of State</u>				
344	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017
	<u>National Highways Authority Of India</u>				
345	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
346	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
347	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
348	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
349	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
350	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
351	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
352	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
353	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
354	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-
	<u>Public Works Dept Of State</u>				
355	REHABILITATION AND UPGRADE OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
356	REHABILITATION AND UPGRADE OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
357	YAN TO NIRMAL SEREHALITATION AND UPGRADE OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
358	REHABILITATION AND UPGRADE OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
359	REHABILITATION AND UPGRADE OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
360	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
	<u>Dept Of Road Transport & Highways</u>				
361	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
362	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
363	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
364	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Public Works Dept Of State</u>				
365	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
366	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
367	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
368	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
369	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
370	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
	<u>Public Works Dept Of State</u>				
371	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
372	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
373	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
374	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
	<u>Public Works Dept Of State</u>				
375	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
376	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
377	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
378	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
	<u>Ministry Of Road Transport And Highways</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
379	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
380	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
381	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
382	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
383	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
384	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
	<u>Public Works Dept Of State</u>				
385	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
386	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
387	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
388	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
389	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
390	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
391	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
392	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
393	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
	<u>Ministry Of Road Transport And Highways</u>				
394	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
395	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
396	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
397	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways Authority Of India</u>				
398	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-
399	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-
400	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
401	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
	<u>Public Works Dept Of State</u>				
402	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
403	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
404	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
	<u>National Highways Development Project</u>				
405	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
406	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
407	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
	<u>Public Works Dept Of State</u>				
408	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
409	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
410	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
411	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
412	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
413	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
	<u>National Highways Development Project</u>				
414	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
	<u>Public Works Dept Of State</u>				
415	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
416	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
	<u>National Highways Authority Of India</u>				
417	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
418	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
419	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
420	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
	<u>National Highways Authority Of India</u>				
421	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
422	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
423	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
424	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
425	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
426	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
427	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
428	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
429	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
430	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
431	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
432	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
433	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
	<u>Public Works Dept Of State</u>				
434	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
435	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
	<u>National Highways Authority Of India</u>				
436	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
	<u>Ministry Of Road Transport And Highways</u>				
437	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
	<u>Public Works Dept Of State</u>				
438	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
439	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
440	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
	<u>National Highways Authority Of India</u>				
441	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
442	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
443	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
444	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
445	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
446	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
447	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
448	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
449	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
450	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
451	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
452	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
453	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
454	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
455	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
456	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
457	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
458	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
459	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
460	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
461	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
462	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
	<u>Public Works Dept Of State</u>				
463	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
464	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	<u>National Highways Authority Of India</u>				
465	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
466	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
467	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
468	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
469	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
470	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
471	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
472	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
473	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
474	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
	<u>National Highways Authority Of India</u>				
475	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-
476	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
477	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
478	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
479	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
480	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
481	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
482	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
483	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
484	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
485	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-
486	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
	<u>Ministry Of Road Transport And Highways</u>				
487	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
	<u>National Highways Authority Of India</u>				
488	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
489	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
490	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
491	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
492	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
493	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
494	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
495	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
496	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
497	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
498	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
499	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
500	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
501	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
	<u>National Highways Authority Of India</u>				
502	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
503	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
504	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU	08/2017	652.55 -	08/2017 -	-
505	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
506	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
507	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
508	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
509	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
510	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
511	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
512	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
513	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
514	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
515	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
516	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
517	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
518	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
519	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
520	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
521	REHABILITATION AND UPGRADE OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
522	REHABILITATION AND UPGRADE OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
523	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
524	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
525	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
526	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
527	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
528	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
529	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-
	Public Works Dept Of State				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above					(December 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
530	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
	<u>National Highways Authority Of India</u>				
531	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
	Total		1,70,446.05 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Port Trust</u>				
532	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
533	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
	<u>Kamarajar Port Limited</u>				
534	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU	10/2013	198.94 -	06/2017 -	-
535	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 -	04/2017 -	-
	<u>Shipping Crp. Of India</u>				
536	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER - [N25000069]SHIPP.,MAHARASHTRA	03/2017	193.00 -	04/2017 -	-
	Total		3,339.86 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
537	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	Total		2,111.17 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
538	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	11/2017
539	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
540	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				
541	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>Central Public Works Department</u>				

Details of Projects Without Date of Commissioning

Costing Rs.150Crore and above				(December 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
542	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
	Total		24,082.46 -		
	Grand Total		4,37,253.05		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	175.00	1.83	- -	12/2017	-	0/0
	Total		175.00 -	175.00	1.83				0/0
	<u>RAILWAYS</u>								
	<u>South Eastern Railway</u>								
2	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	365.00	98.37	- -	12/2017	-	0/0
	<u>Southern Railway</u>								
3	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	189.24	6.28	- -	12/2017	-	0/0
4	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 -	2,815.62	240.68	- -	01/2018	-	0/0
	<u>North Eastern Railway</u>								
5	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	412.05	364.40	- -	03/2018	-	0/0
6	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	474.30	421.94	- -	03/2018	-	0/0
7	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	199.75	220.72	- -	03/2018	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
8	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE	04/2008	822.39 -	1,810.00	1,673.99	- -	03/2018	-	0/1
	<u>North East Frontier Railway</u>								
9	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	630.00	590.90	- -	03/2018	-	0/0
10	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	1,871.00	1,081.96	- -	03/2018	-	0/0
	<u>North Western Railway</u>								
11	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	420.48	35.80	- -	05/2018	-	0/0
12	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	827.84	375.56	- -	08/2018	-	0/0
	<u>North Eastern Railway</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (December 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
13	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	109.01	- -	10/2018	-	0/0
	<u>North Western Railway</u>								
14	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	109.39	- -	10/2018	-	0/0
15	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 335.53	346.35	199.68	- -	10/2018	-	0/0
	<u>Eastern Railways</u>								
16	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	47.63	- -	11/2018	-	0/0
	<u>East Central Railways</u>								
17	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	678.54	-	- -	12/2018	-	0/38
	<u>South Central Railway</u>								
18	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	525.00	544.20	- -	03/2019	-	0/0
	<u>Eastern Railways</u>								
19	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	111(R1)	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
20	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.99	1,025.83	- 09/2009	03/2019	114(R1)	0/0
	<u>North Western Railway</u>								
21	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	43.98	- -	03/2019	-	0/0
	<u>Western Railway</u>								
22	RAJKOT-VERAVAL,WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR- SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	-	- -	03/2019	-	0/0
23	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	590.60	- -	03/2019	-	0/0
	<u>North Western Railway</u>								
24	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	105.69	- -	03/2019	-	0/0
25	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	349.00	144.37	- -	03/2019	-	0/0
	<u>North East Frontier Railway</u>								
26	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
27	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	450.00	331.37	- -	03/2019	-	0/0
28	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	535.00	509.15	- -	03/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (December 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
29	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	398.93	115.62	- -	03/2019	-	0/0
	<u>Central Railways</u>								
30	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 199.12	199.12	146.86	- -	03/2019	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
31	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL, HIMACHAL PRADESH	04/2008	1,046.88 -	4,500.00	110.45	- -	03/2019	-	0/0
32	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL, KARNATAKA	04/2010	2,127.00 -	2,127.00	847.70	- -	03/2019	-	0/1
33	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	350.00	297.24	- -	03/2019	-	0/0
	<u>North Eastern Railway</u>								
34	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	718.54	279.46	- -	05/2019	-	0/0
	<u>North East Frontier Railway</u>								
35	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	580.00	-	- -	07/2019	-	2/3
36	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	614.00	261.71	- -	03/2020	-	0/0
37	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	780.00	436.01	- -	03/2020	-	0/0
38	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	2,135.00	921.36	- -	03/2020	-	0/0
39	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 -	360.00	3.13	- -	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
40	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	567.18 -	975.62	361.26	- -	03/2020	-	0/0
	<u>North East Frontier Railway</u>								
41	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	33.53	- -	03/2020	-	0/0
42	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
43	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	471.00	52.57	- -	03/2020	-	0/0
44	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	450.00	122.81	- -	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (December 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
45	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	566.74	- -	03/2020	-	0/0
	<u>East Coast Railway</u>								
46	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	466.17	- -	03/2020	-	1/1
47	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	155.28	- -	03/2020	-	0/0
	<u>North Western Railway</u>								
48	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	2.88	- -	03/2020	-	0/0
	<u>South Western Railway</u>								
49	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	325.13	- -	03/2020	-	0/0
50	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	324.71	- 11/2015	03/2020	52(R3)	0/2
	<u>North East Frontier Railway</u>								
51	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	612.00	-	- -	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
52	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	644.38	36.97	- -	12/2020	-	0/0
53	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	1,548.66	442.97	- -	12/2020	-	0/0
	<u>Central Railways</u>								
54	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	2,271.50	1,386.59	- -	03/2021	-	0/0
	<u>South Central Railway</u>								
55	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	2,125.18	14.17	- -	03/2021	-	0/0
	<u>West Central Railway</u>								
56	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	2,713.09	-	- -	03/2021	-	0/0
	<u>North East Frontier Railway</u>								
57	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	6,000.00	255.59	- -	03/2021	-	0/0
	<u>Central Railways</u>								
58	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	792.89	213.92	- -	03/2021	-	0/0
	<u>East Coast Railway</u>								
59	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	1,579.27	605.54	- -	03/2021	-	0/0
60	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	843.04	47.24	- -	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above (December 2017)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>South Central Railway</u>								
61	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	.14	- -	03/2021	-	0/0
	<u>North East Frontier Railway</u>								
62	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	871.00	25.71	- -	03/2021	-	0/0
	<u>Western Railway</u>								
63	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	-	- -	03/2021	-	0/0
	<u>East Coast Railway</u>								
64	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	3,004.90	944.84	- -	06/2021	-	0/0
	<u>South Central Railway</u>								
65	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	1,160.47	1.74	- -	03/2022	-	0/1
	<u>Western Railway</u>								
66	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	331.91	- -	03/2022	-	0/0
	<u>Central Railways</u>								
67	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	540.02	123.73	- -	03/2022	-	0/0
68	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	1,272.19	57.85	- -	03/2022	-	0/0
69	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	637.95	2.37	- -	03/2022	-	0/0
	<u>North East Frontier Railway</u>								
70	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.00	68.44	- -	03/2022	-	0/0
	<u>East Coast Railway</u>								
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	478.29	- -	12/2022	-	0/0
	<u>Central Railways</u>								
72	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	3,168.29	734.00	- -	03/2023	-	0/0
73	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	2,449.91	18.91	- -	03/2023	-	0/0
74	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	2,081.27	-	- -	03/2023	-	0/0
75	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	1,035.16	2.04	- -	03/2023	-	0/0
76	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	8,857.98	.74	- -	03/2024	-	0/0
77	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	5,341.68	1.99	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
78	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	3,438.51	-	- -	03/2024	-	0/0
79	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	3,627.47	17.13	- -	03/2024	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
80	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	2,335.67	44.95	- -	12/2024	-	0/0
	<u>South Western Railway</u>								
81	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	1,141.00	481.99	- 03/2020	-	-	0/5
	Total		77,101.13 -	1,13,461.20	21,799.11				3/52
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
82	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	-	- -	12/2017	-	0/0
83	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	-	- -	12/2017	-	0/0
84	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	1,665.00	2,313.68	- -	12/2017	-	0/0
85	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
86	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
87	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	-	- -	01/2018	-	0/0
88	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
89	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	771.18	-	- -	03/2018	-	0/0
	<u>National Highways Development Project</u>								
90	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
	<u>National Highways Authority Of India</u>								
91	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
92	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
93	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	-	- -	04/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
95	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	105.63	- -	05/2018	-	0/0
96	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	57.86	- -	05/2018	-	0/0
97	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	-	- -	05/2018	-	0/0
98	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	101.53	- -	05/2018	-	0/0
99	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	-	- -	05/2018	-	0/0
100	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
101	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	-	- -	05/2018	-	0/0
102	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	-	- -	05/2018	-	0/0
103	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	06/2018	-	3/3
104	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
105	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	07/2018	-	0/0
106	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	-	- -	07/2018	-	0/0
107	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	- -	07/2018	-	0/0
108	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	-	- -	07/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	FOUR LANE OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	576.00	- -	08/2018	-	0/0
110	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	129.75	- -	08/2018	-	0/0
111	FOUR LANE OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	19.87	- -	08/2018	-	0/0
112	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	87.78	- -	08/2018	-	0/0
113	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	-	- -	10/2018	-	0/0
114	FOUR LANE OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	-	0/0
115	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	268.10	- -	11/2018	-	0/0
116	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	35.17	- -	11/2018	-	0/0
117	6 LANE OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	355.00	- -	01/2019	-	0/0
118	FOUR LANE OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	-	- -	01/2019	-	0/0
119	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	-	- -	01/2019	-	0/0
120	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	-	- -	01/2019	-	0/0
121	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	-	- -	02/2019	-	0/0
122	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	11.42	- -	03/2019	-	0/0
123	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	302.45	- -	03/2019	-	0/0
124	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	-	- -	03/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
125	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	-	-	03/2019	-	0/0
126	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	90.43	-	03/2019	-	0/0
127	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	-	-	03/2019	-	0/0
128	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	-	-	03/2019	-	0/0
129	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	-	-	04/2019	-	0/0
130	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	1,041.10	-	-	04/2019	-	0/0
131	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	-	-	04/2019	-	0/0
132	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	676.73	71.78	-	04/2019	-	0/0
133	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	1,587.49	14.24	-	04/2019	-	0/0
134	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	-	-	04/2019	-	0/0
135	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	-	-	04/2019	-	0/0
136	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	-	05/2019	-	0/0
137	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	-	05/2019	-	0/0
138	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	701.12	-	-	05/2019	-	0/0
139	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	-	-	05/2019	-	0/0
140	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	1,004.67	-	-	05/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
141	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	244.90	29.50	- -	05/2019	-	0/0
142	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
143	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	07/2019	-	0/0
144	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	07/2019	-	0/0
145	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	950.69	-	- -	08/2019	-	0/0
146	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	-	0/0
147	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	1,664.20	49.55	- -	04/2020	-	0/0
	Total		54,072.65 -	54,072.14	5,476.60				3/4
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
148	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD, DELHI	06/2015	197.33 -	197.33	4.06	- -	04/2019	-	0/2
	Total		197.33 -	197.33	4.06				0/2
	Grand Total		1,31,546.11	1,67,905.67	27,281.60				6/58

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs.150 Crore and Above				(December 2017)		
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>ATOMIC ENERGY</u>					
	<u>Nuclear Power Corporation Of India Limited</u>					
1	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	11/2020 -	11/2023	0/0
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	10/2017	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	06/2017 -	12/2017	0/0
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
	<u>Western Coal Fields Limited</u>					
7	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
	<u>Northern Coal Fields Limited</u>					
8	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09 -	03/2021 -	03/2021	0/0
	<u>Neyveli Lignite Corporation</u>					
9	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Western Coal Fields Limited</u>					
10	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>South-Eastern Coal Fields Limited</u>					
11	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH	05/2017	976.95 -	03/2026 -	03/2026	0/0
	<u>MINES</u>					
	<u>National Aluminum Company Limited (Nalco)</u>					
12	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	04/2021 04/2021	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>STEEL</u>					
	<u>Hindustan Steelwork Construction Limited</u>					
13	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017	0/0
14	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
15	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
16	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
17	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
18	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
19	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
20	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
21	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
22	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
23	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
24	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
25	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
26	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL, ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
27	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Steel Authority Of India Limited (Sail)</u>					
28	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Indian Strategic Petroleum Reserves Ltd</u>					
29	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	11/2017	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
30	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA	05/2016	215.38 215.38	06/2017 01/2018	01/2018	0/0
	<u>Oil India Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
31	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	12/2016 -	03/2018	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
32	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 -	01/2017 03/2018	03/2018	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
33	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	09/2017 03/2018	03/2018	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
34	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
35	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2018	05/2018	0/0
	<u>Bharat Petroleum Corporation Limited</u>					
36	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL, KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
	<u>Indian Oil Corporation Limited</u>					
37	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT	10/2014	279.00 -	08/2018 -	08/2018	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
38	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
39	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH	04/2017	420.76 -	09/2018 09/2018	09/2018	0/0
	<u>Bharat Petroleum Corporation Limited</u>					
40	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
	<u>Oil India Limited</u>					
41	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	03/2017 -	11/2018	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
42	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	12/2018	0/0
	<u>Bharat Petroleum Corporation Limited</u>					
43	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL, MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
44	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0
45	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
46	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	03/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
47	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC, MAHARASHTRA	01/2017	474.15 474.15	05/2019 05/2019	05/2019	0/0
48	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 06/2019	06/2019	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
49	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
50	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 5,479.75	05/2019 10/2019	10/2019	0/0
51	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC, MAHARASHTRA	02/2017	546.15 546.15	11/2019 11/2019	11/2019	0/0
52	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC, MAHARASHTRA	02/2017	511.30 511.30	11/2019 -	11/2019	0/0
53	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC, MAHARASHTRA	02/2017	968.61 -	11/2019 -	11/2019	0/0
	<u>Oil India Limited</u>					
54	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL, MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
	<u>Indian Oil Corporation Limited</u>					
55	LPG BP PROJECT KHORDHA - [N16000283]IOCL, ODISHA	12/2016	161.59 -	12/2019 -	12/2019	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
56	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
	<u>Gas Authority Of India Limited</u>					
57	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
	<u>Bharat Petroleum Corporation Limited</u>					
58	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL, MAHARASHTRA	02/2016	554.00 -	02/2020 -	02/2020	0/0
59	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA	02/2016	3,313.00 -	02/2020 -	02/2020	0/0
	<u>Indian Oil Corporation Limited</u>					
60	SITARGANJ LPG PROJECT - [N16000282]IOCL, UTTARAKHAND	02/2017	160.10 -	02/2020 -	02/2020	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
61	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
62	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC, ASSAM	07/2016	249.85 250.00	05/2020 05/2020	05/2020	0/0
	<u>Indian Oil Corporation Limited</u>					
63	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
64	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH <u>Indian Oil Corporation Limited</u>	03/2016	34,012.00 -	06/2020 06/2020	06/2020	0/0
65	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT <u>Oil India Limited</u>	09/2016	208.35 -	07/2020 -	07/2020	0/0
66	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE <u>Indian Oil Corporation Limited</u>	05/2016	406.00 -	10/2020 -	10/2020	0/0
67	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
68	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
69	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
70	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
71	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
72	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
73	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH <u>Hindustan Petroleum Corporation Limited</u>	07/2014	247.00 -	03/2021 -	03/2021	0/0
74	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE <u>Oil & Natural Gas Corporation Limited</u>	09/2017	2,677.00 -	03/2021 -	03/2021	0/0
75	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 -	05/2021 -	05/2021	0/0
76	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND <u>Gas Authority Of India Limited</u>	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0
77	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH	04/2017	287.49 -	04/2022 -	04/2022	0/0
78	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA <u>Oil & Natural Gas Corporation Limited</u>	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
79	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT <u>Bharat Petroleum Corporation Limited</u>	02/2017	1,162.56 1,162.56	03/2026 03/2026	03/2026	0/0
80	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
81	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>POWER</u>					
	<u>National Thermal Power Corporation</u>					
82	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 12/2016	12/2016	0/0
	<u>Power Grid Corporation Of India Limited</u>					
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 10/2017	01/2018	0/0
84	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	01/2018	0/0
85	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	11/2017 -	01/2018	0/0
86	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	01/2018 -	01/2018	0/0
87	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 09/2017	03/2018	0/0
88	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	03/2018	0/0
89	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
90	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	03/2018	0/0
	<u>National Hydro-Electric Power Corporation</u>					
91	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU	06/2017	287.48 -	03/2018 -	03/2018	0/0
	<u>Power Grid Corporation Of India Limited</u>					
92	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	12/2015 -	03/2018	0/0
93	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
94	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
95	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	06/2018	0/0
96	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
97	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	06/2018	0/0
98	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
99	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
100	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
101	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2018	0/0
102	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
103	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 -	09/2018	0/0
104	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0
105	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
106	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
107	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
108	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
109	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
110	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
111	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
112	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL, MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
113	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
115	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	03/2019	0/0
116	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
117	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
118	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL, MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
119	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
120	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL, MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0
121	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
122	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
123	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
124	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL, BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
125	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL, MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
126	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
127	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0
128	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
129	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
130	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
131	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
132	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
133	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
134	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
135	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
136	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
137	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
138	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
139	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	12/2021 -	12/2021	0/0
	<u>Chenab Valley Power Projects [P] Limited</u>					
140	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 12/2017	06/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
141	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Natrip Implementation Society</u>					
142	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Hospital Services Consultancy Corporation Ltd</u>					
143	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
144	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Hospital Services Consultancy Corporation</u>					
145	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
146	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
147	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 08/2019	08/2019	0/0
148	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0
149	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	<u>RAILWAYS</u>					
	<u>North East Frontier Railway</u>					
150	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009	0/0
151	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011	0/0
152	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
153	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	03/2014	0/0
154	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	11/2014	0/0
	<u>East Coast Railway</u>					
155	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015	0/0
	<u>North East Frontier Railway</u>					
156	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	08/2015	0/0
157	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016	0/0
158	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	05/2016	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
159	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
160	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	03/2017	0/0
	<u>North Eastern Railway</u>					
161	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2017	0/0
	<u>North East Frontier Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
162	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	11/2017	0/0
	<u>South Central Railway</u>					
163	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	12/2017	0/0
	<u>Western Railway</u>					
164	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	12/2017	0/0
	<u>South Eastern Railway</u>					
165	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
	<u>Southern Railway</u>					
166	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24 -	- -	12/2017	0/0
167	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 -	- -	01/2018	0/0
	<u>North Eastern Railway</u>					
168	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	- -	03/2018	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
169	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	03/2018	0/0
	<u>North Eastern Railway</u>					
170	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
171	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	03/2018	0/0
	<u>North East Frontier Railway</u>					
172	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
173	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
	<u>Container Corporation Of India</u>					
174	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
175	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
176	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
	<u>North Western Railway</u>					
177	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	- -	05/2018	0/0
	<u>North East Frontier Railway</u>					
178	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Metropolitan Rapid Transport Projects</u>					
179	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
	<u>North Western Railway</u>					
180	DAUSA-GANGAPUR CITY (NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	08/2018	0/0
	<u>North Eastern Railway</u>					
181	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	10/2018	0/0
	<u>North Western Railway</u>					
182	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	10/2018	0/0
183	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 335.53	- -	10/2018	0/0
	<u>Eastern Railways</u>					
184	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER, MULTI STATE	04/2010	157.94 -	- -	11/2018	0/0
	<u>Northern Railway</u>					
185	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	11/2002 -	12/2018	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
187	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	03/2016 -	12/2018	0/0
	<u>South Central Railway</u>					
188	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2019	0/0
	<u>North East Frontier Railway</u>					
189	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
	<u>Eastern Railways</u>					
190	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	03/2019	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
191	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
192	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
	<u>Western Railway</u>					
193	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
	<u>North Western Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
194	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	03/2019	0/0
	<u>Western Railway</u>					
195	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
196	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
	<u>North Western Railway</u>					
197	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	03/2019	0/0
198	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 281.03	- -	03/2019	0/0
	<u>North East Frontier Railway</u>					
199	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
200	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2019	0/0
201	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2019	0/0
202	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
	<u>Central Railways</u>					
203	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	03/2019	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
204	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	03/2019	0/0
205	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
206	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
207	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
	<u>East Central Railways</u>					
208	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
	<u>Container Corporation Of India</u>					
209	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
210	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0
211	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
212	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
213	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
214	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
	<u>North Eastern Railway</u>					
215	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
	<u>North Western Railway</u>					
216	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	03/2014 -	06/2019	0/0
	<u>South East Central Railway</u>					
217	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
218	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0
	<u>North Western Railway</u>					
219	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	12/2019	0/0
	<u>North East Frontier Railway</u>					
220	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	- -	03/2020	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
221	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
	<u>Eastern Railways</u>					
222	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0
	<u>North East Frontier Railway</u>					
223	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
224	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
	<u>North East Frontier Railway</u>					
225	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086]NFR, ASSAM	09/2006	200.00 -	- -	03/2020	0/0
226	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]NFR, BIHAR	09/2006	300.00 -	- -	03/2020	0/0
227	AGARTALA SABROOM, NL, NEFR - [N220000099]NFR, TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
228	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
229	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
230	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
	<u>Western Railway</u>					
231	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
	<u>North East Frontier Railway</u>					
232	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
233	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
	<u>North East Frontier Railway</u>					
234	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
235	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
236	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	03/2020	0/0
237	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2020	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
238	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
	<u>East Coast Railway</u>					
239	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
	<u>North Western Railway</u>					
240	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	03/2020	0/0
	<u>South Western Railway</u>					
241	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0
	<u>East Coast Railway</u>					
242	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2020	0/0
	<u>North East Frontier Railway</u>					
243	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	03/2020	0/0
	<u>South Eastern Railway</u>					
244	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
245	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
246	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
247	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
	<u>East Central Railways</u>					
248	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
	<u>East Coast Railway</u>					
249	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR, ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
250	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
251	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
252	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
253	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
254	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
	<u>Central Railways</u>					
255	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 2,271.50	- -	03/2021	0/0
	<u>South Central Railway</u>					
256	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	03/2021	0/0
	<u>West Central Railway</u>					
257	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2021	0/0
	<u>North East Frontier Railway</u>					
258	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
	<u>Central Railways</u>					
259	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	277.70 792.89	- -	03/2021	0/0
	<u>East Coast Railway</u>					
260	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 1,111.99	- -	03/2021	0/0
261	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	03/2021	0/0
	<u>South Central Railway</u>					
262	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	- -	03/2021	0/0
	<u>East Coast Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
263	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2021 -	03/2021	0/0
264	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
	<u>North East Frontier Railway</u>					
265	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
	<u>Western Railway</u>					
266	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
	<u>South Eastern Railway</u>					
267	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
	<u>East Coast Railway</u>					
268	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	06/2021	0/0
	<u>South Eastern Railway</u>					
269	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0
270	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
	<u>South East Central Railway</u>					
271	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
	<u>Western Railway</u>					
272	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	03/2022	0/0
	<u>Central Railways</u>					
273	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	03/2022	0/0
	<u>North Eastern Railway</u>					
274	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
	<u>Central Railways</u>					
275	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	03/2022	0/0
276	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	- -	03/2022	0/0
	<u>East Coast Railway</u>					
277	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2021 -	03/2022	0/0
278	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2021 -	03/2022	0/0
	<u>North East Frontier Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
279	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2022	0/0
	<u>South Central Railway</u>					
280	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
	<u>East Coast Railway</u>					
281	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	- -	12/2022	0/0
	<u>North Central Railway</u>					
282	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
283	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0
	<u>Central Railways</u>					
284	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- -	03/2023	0/0
285	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	- -	03/2023	0/0
286	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	- -	03/2023	0/0
287	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	- -	03/2023	0/0
288	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	03/2024	0/0
289	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	03/2024	0/0
290	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	03/2024	0/0
291	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	- -	03/2024	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
292	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
293	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
294	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	12/2024	0/0
295	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
296	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
297	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
	<u>North Central Railway</u>					
298	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>South Central Railway</u>					
299	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-	0/0
	<u>Central Railways</u>					
300	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
301	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
	<u>Southern Railway</u>					
302	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
	<u>Northern Railway</u>					
303	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
	<u>Southern Railway</u>					
304	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
	<u>South Western Railway</u>					
305	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
	<u>North Eastern Railway</u>					
306	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	-	0/0
	<u>South Eastern Railway</u>					
307	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
308	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
	<u>South Central Railway</u>					
309	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
	<u>East Central Railways</u>					
310	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
	<u>North Central Railway</u>					
311	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
	<u>North East Frontier Railway</u>					
312	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
	<u>East Central Railways</u>					
313	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Northern Railway</u>					
314	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
315	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
	<u>South Central Railway</u>					
316	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
	<u>Eastern Railways</u>					
317	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
	<u>South Western Railway</u>					
318	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
	<u>Northern Railway</u>					
319	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
	<u>East Central Railways</u>					
320	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
321	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
322	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
323	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
	<u>North Eastern Railway</u>					
324	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
	<u>North Central Railway</u>					
325	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>South East Central Railway</u>					
326	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
	<u>East Central Railways</u>					
327	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
	<u>Southern Railway</u>					
328	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
329	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
330	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-	0/0
	<u>Northern Railway</u>					
331	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
	<u>Railway Electrification</u>					
332	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Eastern Railway</u>					
333	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
	<u>South Western Railway</u>					
334	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
335	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
336	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
	<u>North Western Railway</u>					
337	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
	<u>Eastern Railways</u>					
338	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
339	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
340	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
341	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
342	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
	<u>Western Railway</u>					
343	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
344	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
	<u>North Eastern Railway</u>					
345	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
346	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
	<u>Western Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
347	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
348	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
349	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
	<u>North Western Railway</u>					
350	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
	<u>South Eastern Railway</u>					
351	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
352	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
353	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
354	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
355	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
356	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
	<u>East Central Railways</u>					
357	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
	<u>East Coast Railway</u>					
358	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
359	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
360	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
361	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
362	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
	<u>East Central Railways</u>					
363	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
364	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
365	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
366	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
367	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
368	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
369	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
370	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
371	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
372	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
	<u>Southern Railway</u>					
373	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-	0/0
374	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
375	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
376	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
377	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
378	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
379	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
380	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
381	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
382	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
383	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
384	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>Southern Railway</u>					
385	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
	<u>Eastern Railways</u>					
386	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
387	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
388	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
389	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
390	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
391	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
392	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
393	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
394	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
395	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
396	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
397	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
398	BARIAPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
399	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
400	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
401	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
402	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
403	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
404	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
405	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
406	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
407	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
408	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
409	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
410	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
	<u>Central Railways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
411	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- -	-	0/0
412	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-	0/0
	<u>South Western Railway</u>					
413	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
	<u>South Central Railway</u>					
414	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
415	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
	<u>Northern Railway</u>					
416	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
417	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
418	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
419	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
420	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
421	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
422	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
	<u>South Western Railway</u>					
423	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
424	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
425	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
426	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
	<u>Northern Railway</u>					
427	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
428	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
429	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
430	JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
431	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
432	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
433	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
434	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
435	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
	<u>South Western Railway</u>					
436	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
437	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
438	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
	<u>Eastern Railways</u>					
439	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
440	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>South Central Railway</u>					
441	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
	<u>South Eastern Railway</u>					
442	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
	<u>South Western Railway</u>					
443	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
	<u>South Eastern Railway</u>					
444	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
	<u>East Coast Railway</u>					
445	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
	<u>North Eastern Railway</u>					
446	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
	<u>South Eastern Railway</u>					
447	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
	<u>South Western Railway</u>					
448	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
	<u>East Central Railways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Antici Pated	
1	2	3	4	5	6	7
449	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
	<u>North Western Railway</u>					
450	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
451	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
	<u>South Western Railway</u>					
452	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
	<u>North Eastern Railway</u>					
453	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
454	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
	<u>South Central Railway</u>					
455	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
456	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
457	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
458	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>East Central Railways</u>					
459	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>Southern Railway</u>					
460	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
461	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
	<u>South Eastern Railway</u>					
462	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Public Works Dept Of State</u>					
463	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
464	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
465	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
466	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
467	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
468	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
469	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
	<u>Ministry Of Road Transport And Highways</u>					
470	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
471	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0
	<u>Public Works Dept Of State</u>					
472	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
	<u>National Highways Development Project</u>					
473	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
	<u>Public Works Dept Of State</u>					
474	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
475	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
476	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
	<u>National Highways Development Project</u>					
477	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
	<u>Ministry Of Road Transport And Highways</u>					
478	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
479	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
	<u>Public Works Dept Of State</u>					
480	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
	<u>National Highways Development Project</u>					
481	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
482	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
483	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
	<u>Public Works Dept Of State</u>					
484	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					
485	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
486	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
	<u>Public Works Dept Of State</u>					
487	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
488	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					
489	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
490	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
	<u>National Highways Development Project</u>					
491	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					
492	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
	<u>National Highways Development Project</u>					
493	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
	<u>Public Works Dept Of State</u>					
494	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					
495	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
496	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
	<u>Public Works Dept Of State</u>					
497	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
	<u>Ministry Of Road Transport And Highways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
498	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH, BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
	<u>Public Works Dept Of State</u>					
499	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
500	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD, ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
501	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
	<u>National Highways Authority Of India</u>					
502	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
	<u>National Highways Development Project</u>					
503	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
	<u>Public Works Dept Of State</u>					
504	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD (NH-52B) (NEW NH NO.215) FROM KM 0.00 TO KM 68.30 IN THE STATE - [N24000373]PWD, UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
	<u>National Highways Development Project</u>					
505	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
506	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
	<u>Ministry Of Road Transport And Highways</u>					
507	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
508	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017	0/0
509	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
	<u>National Highways Development Project</u>					
510	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
	<u>Public Works Dept Of State</u>					
511	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B (EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
	<u>National Highways Development Project</u>					
512	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
513	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
	<u>National Highways Authority Of India</u>					
514	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Ministry Of Road Transport And Highways</u>					
515	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
	<u>National Highways Authority Of India</u>					
516	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
	<u>National Highways Development Project</u>					
517	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
	<u>National Highways Authority Of India</u>					
518	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
519	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017	0/0
520	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017	0/0
521	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
	<u>Public Works Dept Of State</u>					
522	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
	<u>National Highways Authority Of India</u>					
523	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
524	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017	0/0
525	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
	<u>Public Works Dept Of State</u>					
526	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
	<u>National Highways Authority Of India</u>					
527	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
528	TWO LANE WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0
529	2 LANE WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
530	FOUR LANE OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0
531	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	10/2017	0/0
532	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
533	2 LANE OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
534	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017	0/0
535	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
	<u>Public Works Dept Of State</u>					
536	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
	<u>Ministry Of Road Transport And Highways</u>					
537	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
538	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
539	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
540	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017	0/0
	<u>National Highways Authority Of India</u>					
541	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	11/2017	0/0
542	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
543	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017	0/0
544	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
	<u>Public Works Dept Of State</u>					
545	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
	<u>Ministry Of Road Transport And Highways</u>					
546	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
547	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
	<u>National Highways Authority Of India</u>					
548	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017	0/0
549	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017	0/0
550	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
551	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
552	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
	<u>Public Works Dept Of State</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
553	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
	<u>National Highways Authority Of India</u>					
554	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2017	0/0
555	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017	0/0
556	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	12/2017	0/0
557	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2017	0/0
558	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	12/2017	0/0
559	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017	0/0
560	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017	0/0
561	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
562	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0
563	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
564	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
565	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
566	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
567	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0
568	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017	0/0
569	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017	0/0
570	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017	0/0
571	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017	0/0
572	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
573	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
574	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
575	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
576	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
	<u>National Highways Development Project</u>					
577	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
	<u>National Highways Authority Of India</u>					
578	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
579	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	12/2017	0/0
580	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2017	0/0
581	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
582	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0
583	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
584	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	12/2017	0/0
	<u>Ministry Of Road Transport And Highways</u>					
585	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
	<u>National Highways Authority Of India</u>					
586	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
587	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
588	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
589	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
590	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	02/2018	0/0
591	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
592	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
593	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
594	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
	<u>Public Works Dept Of State</u>					
595	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
596	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>National Highways Authority Of India</u>					
597	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
598	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2018	0/0
599	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	03/2018	0/0
600	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	03/2018	0/0
601	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	03/2018	0/0
602	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	03/2018	0/0
603	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	03/2018	0/0
604	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
605	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	03/2018	0/0
606	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2018	0/0
607	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	03/2018	0/0
608	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	03/2018	0/0
609	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
	<u>National Highways Development Project</u>					
610	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHAI,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
	<u>Ministry Of Road Transport And Highways</u>					
611	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
	<u>National Highways Authority Of India</u>					
612	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
613	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
614	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
615	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
616	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
617	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	03/2018	0/0
	<u>National Highways Development Project</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
618	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
	<u>National Highways Authority Of India</u>					
619	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
620	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
	<u>Public Works Dept Of State</u>					
621	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
	<u>National Highways Authority Of India</u>					
622	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	- -	03/2018	0/0
623	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2018	0/0
624	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
625	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2018	0/0
626	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
627	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	- -	04/2018	0/0
628	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	- -	04/2018	0/0
629	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	- -	04/2018	0/0
630	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	04/2018	0/0
	<u>Ministry Of Road Transport And Highways</u>					
631	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH, ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
632	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH, ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
	<u>National Highways Authority Of India</u>					
633	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	- -	05/2018	0/0
634	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	- -	05/2018	0/0
635	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	- -	05/2018	0/0
636	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	05/2018	0/0
637	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, HARYANA	11/2015	867.66 -	- -	05/2018	0/0
638	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	- -	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
639	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
640	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	05/2018	0/0
641	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
<u>Ministry Of Road Transport And Highways</u>						
642	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
<u>National Highways Authority Of India</u>						
643	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	06/2018	0/0
644	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	06/2018	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
645	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
<u>National Highways Authority Of India</u>						
646	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
647	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
648	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
<u>National Highways Development Project</u>						
649	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
<u>National Highways Authority Of India</u>						
650	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
651	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
652	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
653	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
654	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	- -	06/2018	0/0
655	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
656	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
657	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
658	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
659	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI, MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
660	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI, UTTARAKHAND	11/2012	605.84 -	- -	07/2018	0/0
661	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2018	0/0
662	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	08/2018	0/0
663	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
664	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
665	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
666	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	- -	08/2018	0/0
667	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
668	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
669	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
670	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
	<u>Ministry Of Road Transport And Highways</u>					
671	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
	<u>National Highways Authority Of India</u>					
672	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
673	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2018	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
674	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
	<u>National Highways Authority Of India</u>					
675	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
676	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
677	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
678	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN	08/2016	320.30 -	- -	01/2019	0/0
679	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
680	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	02/2019	0/0
681	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
682	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
683	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
684	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
685	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	03/2019	0/0
686	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	03/2019	0/0
687	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	03/2019	0/0
688	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	- -	03/2019	0/0
689	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
690	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
691	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0
692	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
693	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	04/2019	0/0
694	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	04/2019	0/0
695	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	04/2019	0/0
696	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	04/2019	0/0
697	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	04/2019	0/0
698	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
699	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
700	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
701	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
702	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
703	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	05/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
704	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
705	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
706	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
707	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
708	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
709	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
710	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
711	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
712	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	08/2019	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
713	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
714	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
715	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
	<u>National Highways Authority Of India</u>					
716	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	09/2019	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
717	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
	<u>National Highways Authority Of India</u>					
718	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
719	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
720	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
721	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
722	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
723	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
724	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
725	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0
726	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
727	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
728	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
729	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
730	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
731	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
732	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
733	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	03/2020	0/0
734	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
735	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
736	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
737	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
738	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]NHAI,KARNATAKA	03/2017	985.41 -	03/2020 -	03/2020	0/0
739	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	03/2020	0/0
740	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	03/2020	0/0
741	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	-	04/2020	0/0
742	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
743	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
744	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
745	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
746	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
747	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
748	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
749	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
750	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
751	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
752	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
753	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
754	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
755	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
756	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
757	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
<u>Public Works Dept Of State</u>						
758	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
759	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
760	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
761	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
<u>Public Works Dept Of State</u>						
762	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
763	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
764	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
765	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
766	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
767	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
768	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
769	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
770	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
771	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
	<u>Public Works Dept Of State</u>					
772	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
773	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
774	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
775	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
776	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
777	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
778	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
779	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
780	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
	<u>Ministry Of Road Transport And Highways</u>					
781	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
782	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
783	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
784	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					
785	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-	0/0
786	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
787	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
788	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
	<u>Public Works Dept Of State</u>					
789	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
790	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
791	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
	<u>National Highways Development Project</u>					
792	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
793	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
	<u>Ministry Of Road Transport And Highways</u>					
794	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
	<u>Public Works Dept Of State</u>					
795	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
796	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
797	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
798	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
799	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
800	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
	<u>National Highways Development Project</u>					
801	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
	<u>Public Works Dept Of State</u>					
802	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
803	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					
804	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0
805	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
806	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
	<u>Ministry Of Road Transport And Highways</u>					
807	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
808	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
809	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
810	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
811	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
812	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
813	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
814	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
815	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
816	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
817	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
818	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
819	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
820	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
<u>Public Works Dept Of State</u>						
821	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
822	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
<u>National Highways Authority Of India</u>						
823	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
824	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
<u>Public Works Dept Of State</u>						
825	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
826	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
<u>Ministry Of Road Transport And Highways</u>						
827	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>National Highways Authority Of India</u>					
828	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
829	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
830	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
831	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
832	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
833	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
834	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
835	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
836	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
837	FOUR LANNING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
838	FOUR LANNING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
839	FOUR LANNING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
840	FOUR LANNING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
841	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
842	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
	<u>Ministry Of Road Transport And Highways</u>					
843	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
844	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
845	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
846	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
847	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
848	FOUR LANNING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
849	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
	<u>Public Works Dept Of State</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
850	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
851	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					
852	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
853	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
854	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
855	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
856	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
857	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
858	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
859	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
860	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
861	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					
862	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-	0/0
863	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
864	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
865	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
866	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
867	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
868	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
869	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
870	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
871	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-	0/0
872	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
873	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
	<u>Ministry Of Road Transport And Highways</u>					
874	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH, ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
	<u>National Highways Authority Of India</u>					
875	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
876	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-	0/0
877	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
878	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
879	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
880	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
881	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
882	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
883	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
884	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
885	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
886	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
887	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL, NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
888	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
	<u>National Highways Authority Of India</u>					
889	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI, BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
890	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI, TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
891	TWO LANE WITH PS OF KARAIKUDI-RAMANATHPURAM - [N24000698]NHAI,TAMIL NADU	08/2017	652.55 -	08/2017 -	-	0/0
892	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
893	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
894	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
895	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-	0/0
896	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
897	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
898	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
899	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
900	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
901	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
902	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
903	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
904	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
905	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
906	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-	0/0
907	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
908	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
909	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
910	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0
911	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
912	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
913	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
914	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
915	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
916	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
	<u>Public Works Dept Of State</u>					
917	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
	<u>National Highways Authority Of India</u>					
918	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Port Trust</u>					
919	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2017	0/0
	<u>Kamarajar Port Limited</u>					
920	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
	<u>Mumbai Port Trust</u>					
921	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
	<u>Kamarajar Port Limited</u>					
922	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	08/2019	0/0
	<u>Port Trust</u>					
923	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
924	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-	0/0
	<u>Shipping Crp. Of India</u>					
925	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER - [N25000069]SHIPP.,MAHARASHTRA	03/2017	193.00 -	04/2017 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Mahanagar Telephone Nigam Limited</u>					
926	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	03/2018	0/0
	<u>Bharat Sanchar Nigam Limited</u>					
927	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 159.30	04/2018 -	04/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above (December 2017)

			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
928	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 164.90	04/2018 -	04/2018	0/0
929	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	05/2018 -	04/2018	0/0
930	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	212.70 222.00	05/2018 -	05/2018	0/0
931	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 -	05/2018 -	05/2018	0/0
932	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH	11/2017	163.00 -	08/2018 -	08/2018	0/0
<u>Department Of Telecommunication</u>						
933	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	06/2019	0/0
<u>URBAN DEVELOPMENT</u>						
<u>Central Public Works Department</u>						
934	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	11/2017	0/0
935	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	11/2015 -	12/2017	0/0
<u>Delhi Metro Rail Corporation Ltd</u>						
936	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	03/2018	0/0
<u>Central Public Works Department</u>						
937	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2015 03/2018	03/2018	0/0
938	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	03/2018	0/0
939	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	03/2015 12/2017	03/2018	0/0
<u>Chennai Metro Rail Ltd</u>						
940	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2018	0/0
<u>Lucknow Metro Rail Corporation Limited</u>						
941	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
<u>Central Public Works Department</u>						
942	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
<u>Kochi Metro Rail Corporation Ltd</u>						
943	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
<u>Nagpur Metro Rail Corporation Ltd</u>						
944	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs.150 Crore and Above				(December 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Central Public Works Department</u>					
945	RESIDENTIAL QUARTERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 -	02/2020	0/0
	<u>Bangalore Metro Rail Corporation Limited</u>					
946	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
947	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,283.30	10/2019 -	03/2020	0/0
948	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 06/2020	06/2020	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
949	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
950	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0
	Total		10,39,406.52 -			0/0
	Grand Total		10,39,406.52			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Annexure - XI

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	69.04	03/2023 -	03/2021
	Total		1,186.64 -	203.82	69.04		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
2	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	64.86	12/2020 -	08/2020
3	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	53.50	02/2019 -	12/2018
	<u>Hindustan Petroleum Corporation Limited</u>						
4	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL [N16000252]	5/2016	664.00 -	664.00	215.86	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	81.33	05/2019 -	12/2018
	Total		7,787.52 -	7,787.52	610.52		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159]	2/2014	908.08 969.97	969.97	732.28	06/2016 02/2018	12/2017
8	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	98.02	07/2018 -	01/2018
9	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	119.40	05/2018 -	03/2018
	Total		1,278.07 -	1,339.96	949.70		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>East Coast Railway</u>						
10	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92	1,172.92	110.88	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	110.88		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
11	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	147.29	07/2018 -	06/2018
12	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	6.54	03/2020 -	05/2019
	Total		963.19 -	921.00	153.83		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
13	GUJARAT ACCESS (LOT 1) - [N26000111	9/2017	171.54 -	171.54	-	05/2018 -	04/2018
	Total		171.54 -	171.54	.00		
	Grand Total		12,559.88	11,596.76	1,893.97		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	135.12	03/2015 03/2020	03/2020
	<u>Eastern Coal Fields Limited</u>						
2	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	284.27	03/2022 -	03/2022
	<u>South-Eastern Coal Fields Limited</u>						
3	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.73	03/2023 -	03/2023
4	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	28.74	03/2022 -	03/2022
	<u>Neyveli Lignite Corporation</u>						
5	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	320.01	06/2015 09/2019	09/2019
	<u>South-Eastern Coal Fields Limited</u>						
6	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
	<u>Western Coal Fields Limited</u>						
7	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	7.72	03/2020 -	03/2020
	<u>Bharat Coking Coal Limited</u>						
8	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Mahanadi Coal Fields Limited</u>						
9	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	25.13	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
10	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
11	GOKUL - [N06000120]	11/2014	267.67 -	267.67	204.93	03/2018 -	03/2018
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	138.85	03/2021 -	03/2021
13	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	368.02	03/2020 -	03/2020
	<u>Mahanadi Coal Fields Limited</u>						
14	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	370.58	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
15	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
16	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	30.12	03/2019 -	03/2019
17	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026
	<u>South-Eastern Coal Fields Limited</u>						
18	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	49.19	03/2020 -	03/2020
	<u>Neyveli Lignite Corporation</u>						
19	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	5,039.57	12/2015 04/2018	04/2018
	<u>South-Eastern Coal Fields Limited</u>						
20	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,563.46	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
21	PENGANGA OCP(REVISED) - [N060000066]	9/2014	441.82 -	441.82	176.03	03/2020 -	03/2020
	<u>Northern Coal Fields Limited</u>						
22	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	430.99	03/2018 -	03/2018
	<u>South-Eastern Coal Fields Limited</u>						
23	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N060000008]	8/2013	7,612.33 -	7,612.33	1,444.26	03/2023 -	03/2023
24	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	.57	03/2023 -	03/2023
25	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	38.29	03/2020 -	03/2020
26	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
27	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
	<u>Central Coal Fields Limited</u>						
28	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	175.94	03/2020 -	03/2020
	<u>Western Coal Fields Limited</u>						
29	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	231.76	03/2025 -	03/2025
30	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	72.65	03/2021 -	03/2021
31	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	70.86	03/2020 -	03/2020
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
32	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129] <u>Western Coal Fields Limited</u>	5/2015	397.09 -	442.42	47.29	03/2019 -	03/2019
33	NEW MAJRI UG TO OC - [N06000128] <u>South-Eastern Coal Fields Limited</u>	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
34	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	34.39	03/2021 -	03/2021
35	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.62	03/2021 -	03/2021
36	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	48.78	03/2018 -	03/2018
37	VIJAY WEST OPENCASE PROJECT - [N06000158] <u>Western Coal Fields Limited</u>	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
38	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	47.85	03/2021 -	03/2021
39	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	-	03/2022 -	03/2022
40	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	.04	03/2022 -	03/2022
41	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	12.79	03/2022 -	03/2022
42	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.57	03/2019 -	03/2019
43	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149] <u>South-Eastern Coal Fields Limited</u>	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
44	AMADAND OPENCASE EXPANSION PROJECT - [N06000148] <u>Singareni Colliers Company Limited</u>	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
45	KALYANIKHANI 6 INCLINE PROJECT - [N06000147] <u>Neyveli Lignite Corporation</u>	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
46	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	167.34	12/2019 -	12/2019
47	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144] <u>Eastern Coal Fields Limited</u>	3/2015	522.45 -	522.45	5.69	09/2019 -	09/2019
48	HURA - C OC (3 MTY) - [N06000143] <u>Western Coal Fields Limited</u>	10/2015	359.69 -	359.69	38.57	03/2022 -	03/2022
49	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	.42	03/2021 -	03/2021
50	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	199.31	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Northern Coal Fields Limited</u>						
51	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	31.42	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
52	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,184.47	11/2021 -	11/2021
	<u>South-Eastern Coal Fields Limited</u>						
53	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.06	03/2023 -	03/2023
	Total		73,988.31 -	73,592.39	15,276.98		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
54	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	31.56	05/2018 -	05/2018
55	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	39.30	08/2020 -	08/2020
	Total		453.64 -	469.04	70.86		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
56	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	103.35	11/2016 04/2019	04/2019
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	413.01	12/2017 02/2018	02/2018
	Total		680.64 -	703.44	516.36		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
58	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	21.00	05/2018 08/2019	08/2019
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation</u>						
61	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Hospital Services Consultancy Corporation Ltd</u>						
62	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
63	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
	Total		1,822.51 -	1,822.51	323.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
64	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	44.60	04/2021 04/2021	04/2021
65	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
66	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	13.88	11/2020 11/2020	11/2020
67	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	286.25	01/2020 01/2020	01/2020
	Total		6,912.00 -	6,912.00	344.73		
	<u>PETROLEUM</u>						
	<u>Oil & Natural Gas Corporation Limited</u>						
68	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	2,065.39	03/2013 09/2018	09/2018
69	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	5,637.00	4,050.69	04/2016 03/2018	03/2018
	<u>Indian Oil Corporation Limited</u>						
70	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	1,546.59	09/2017 12/2018	12/2018
71	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	4,190.00	2,248.49	09/2017 06/2018	06/2018
	<u>Bharat Petroleum Corporation Limited</u>						
72	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	89.27	02/2020 -	02/2020
73	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	12.13	01/2019 -	01/2019
74	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	97.51	12/2019 -	12/2019
75	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	32.34	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Oil India Limited</u>						
76	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.09	12/2019 -	12/2019
77	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.06	10/2020 -	10/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
78	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	57.29	12/2019 -	12/2019
79	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	88.68	03/2019 -	03/2019
80	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	55.76	04/2019 -	04/2019
	<u>Indian Oil Corporation Limited</u>						
81	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.80	12/2019 -	12/2019
82	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	20.39	02/2020 -	02/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
83	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018
84	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	207.09	03/2026 03/2026	03/2026
85	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020
	<u>Indian Oil Corporation Limited</u>						
86	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	70.83	01/2019 -	01/2019
87	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
	<u>Gas Authority Of India Limited</u>						
88	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,828.00	3.27	12/2020 -	12/2020
89	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,212.00	6.30	12/2020 -	12/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
90	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	123.41	05/2021 -	05/2021
	<u>Hindustan Petroleum Corporation Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
91	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	-	03/2021 -	03/2021
	<u>Chennai Petroleum Corporation Limited</u>						
92	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	96.29	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
93	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 -	11/2019
94	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 -	11/2019
95	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
96	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	155.33	05/2019 05/2019	05/2019
	<u>Gas Authority Of India Limited</u>						
97	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	.57	07/2022 -	07/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	12.38	04/2022 -	04/2022
	<u>Indian Oil Corporation Limited</u>						
99	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
100	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
101	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	16.93	07/2020 -	07/2020
	<u>Gas Authority Of India Limited</u>						
102	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,250.00	18.19	12/2020 -	12/2020
103	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	2,253.00	14.19	12/2020 -	12/2020
104	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	12.07	12/2019 -	12/2019
	<u>Indian Oil Corporation Limited</u>						
105	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
106	ADDITIONAL FACILITIES AT VIJAYAWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
107	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
108	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
	<u>Bharat Petroleum Corporation Limited</u>						
109	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	24.35	08/2018 -	08/2018
	<u>Indian Oil Corporation Limited</u>						
110	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	11.35	06/2020 -	06/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
111	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	5.87	03/2023 03/2022	03/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
112	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	312.83	06/2020 -	06/2020
113	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	422.29	10/2014 03/2018	03/2018
	<u>Indian Oil Corporation Limited</u>						
114	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,052.91	06/2018 -	06/2018
	<u>Oil & Natural Gas Corporation Limited</u>						
115	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	703.97	12/2014 03/2018	03/2018
116	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	2,084.15	05/2014 05/2018	05/2018
117	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,671.57	03/2015 03/2018	03/2018
118	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,183.39	05/2013 03/2018	03/2018
119	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	5.63	01/2014 11/2019	11/2019
	<u>Gas Authority Of India Limited</u>						
120	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,548.90	12/2018 -	12/2018
	<u>Oil & Natural Gas Corporation Limited</u>						
121	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	593.82	03/2019 05/2020	05/2020
122	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,237.43	05/2017 05/2018	05/2018
123	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	367.84	11/2019 12/2018	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,479.75	2,236.63	05/2019 10/2019	10/2019
125	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,306.72	04/2019 03/2019	03/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
126	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	39.60	09/2019 09/2019	09/2019
	<u>Indian Oil Corporation Limited</u>						
127	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	91.45	08/2019 -	08/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
128	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
	<u>Gas Authority Of India Limited</u>						
129	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	200.00	15.92	04/2018 -	04/2018
130	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	124.98	03/2018 -	03/2018
131	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	487.03	12/2018 -	12/2018
	<u>Bharat Petroleum Corporation Limited</u>						
132	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	1,025.00	08/2018 05/2019	05/2019
133	PALAKKAD LPG PLANT - [N16000225]	2/2015	184.00 -	184.00	89.85	12/2017 -	12/2017
134	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	227.72	04/2018 -	04/2018
	<u>Indian Oil Corporation Limited</u>						
135	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	26.18	12/2018 -	12/2018
136	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	8.28	12/2020 -	12/2020
137	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	32.65	09/2019 -	09/2019
138	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	185.08	08/2021 -	08/2021
139	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY [N16000248]	7/2015	822.66 -	822.66	272.86	11/2018 -	11/2018
	<u>Oil & Natural Gas Corporation Limited</u>						
140	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246	5/2016	215.38 -	215.38	175.07	06/2017 01/2018	01/2018
	<u>Indian Oil Corporation Limited</u>						
142	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243	2/2016	2,582.00 -	2,582.00	316.80	11/2019 -	11/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
143	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242	11/2016	230.00 -	230.00	16.95	02/2019 -	02/2019
	<u>Bharat Petroleum Corporation Limited</u>						
144	HALDIA LPG IMPORT FACILITY - [N16000223	3/2015	694.00 -	694.00	217.71	10/2018 -	10/2018
	<u>Hindustan Petroleum Corporation Limited</u>						
145	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222	8/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018
	<u>Oil & Natural Gas Corporation Limited</u>						
146	SIX PIPELINE REPLACEMENT PROJECT - [N16000214	3/2009	181.02 -	173.28	164.86	01/2017 03/2018	03/2018
147	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	1,163.47	04/2018 04/2018	04/2018
148	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212	1/2015	4,619.94 -	3,961.54	3,480.50	12/2017 03/2019	03/2019
149	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211	11/2014	195.63 -	187.10	157.51	09/2018 09/2018	09/2018
	<u>Gas Authority Of India Limited</u>						
150	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	749.00	542.00	02/2020 -	02/2020
	<u>Numaligarh Refinery Limited</u>						
151	DIESEL HYDROTREATOR - [N16000207	7/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018
	<u>Indian Oil Corporation Limited</u>						
152	PARADIP LPG IMPORT FACILITY - [N16000196	1/2015	690.00 -	690.00	133.91	07/2018 08/2020	08/2020
153	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195	2/2015	890.00 -	887.00	262.60	10/2019 -	10/2019
154	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	1/2015	1,823.00 -	1,823.00	127.28	12/2020 -	12/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
155	MH NORTH REDEVELOPMENT PHASE III - [N16000188	6/2014	5,706.47 -	5,813.25	5,554.21	05/2017 05/2018	05/2018
	<u>Indian Oil Corporation Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
156	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162 <u>Oil & Natural Gas Corporation Limited</u>	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
157	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084	6/2007	736.65 -	571.47	542.65	09/2011 06/2019	06/2019
158	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25 -	160.16	106.98	07/2016 06/2018	06/2018
	Total		1,79,385.38 -	1,79,456.99	45,938.95		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
159	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077 <u>Satluj Jal Vidyut Nigam Limited</u>	4/2010	4,404.57 -	5,135.01	3,488.99	01/2015 03/2018	03/2018
160	NAITWAR MORI HEP - [N18000265 <u>Power Grid Corporation Of India Limited</u>	10/2017	648.33 -	648.33	-	12/2021 -	12/2021
161	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	8/2017	1,931.39 -	1,931.39	-	02/2020 -	02/2020
162	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263	5/2017	445.89 -	445.89	-	02/2019 -	02/2019
163	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	5/2017	186.17 -	186.17	8.00	07/2019 -	07/2019
164	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261	5/2017	175.64 -	175.64	4.99	09/2018 -	09/2018
165	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	3/2017	3,500.00 3,500.00	3,500.00	109.00	07/2020 -	07/2020
166	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI [N18000257	12/2015	3,654.00 -	3,654.00	1,043.00	04/2019 -	04/2019
167	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256	2/2015	1,750.00 -	1,750.00	570.00	06/2018 -	06/2018
168	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255	4/2015	2,225.00 2,225.00	2,225.00	1,033.00	01/2018 -	01/2018
	<u>Thdc India Limited</u>						
169	AMELIA COAL MINE - [N18000252 <u>National Hydro-Electric Power Corporation</u>	1/2017	2,104.21 -	2,104.21	38.90	09/2020 -	09/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
170	50 MW SOLAR POWER PROJECT - [N18000251] <u>Power Grid Corporation Of India Limited</u>	6/2017	287.48 -	287.48	28.79	03/2018 -	03/2018
171	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
172	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	322.43	04/2020 -	04/2020
173	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	7.45	09/2019 -	09/2019
174	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
175	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]	2/2017	235.53 -	235.53	7.29	06/2019 -	06/2019
176	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	1.43	03/2019 -	03/2019
177	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	15.59	02/2019 -	02/2019
178	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
179	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	11.77	04/2019 -	04/2019
180	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	51.76	01/2019 -	01/2019
181	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
182	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	7.82	04/2019 -	04/2019
183	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	-	06/2019 -	06/2019
184	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.56	03/2019 -	03/2019
185	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	10.95	02/2019 -	02/2019
186	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	.77	02/2019 -	02/2019
187	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	171.22	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
188	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	37.81	07/2018 -	07/2018
189	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	51.97	12/2018 -	12/2018
190	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	163.78	01/2019 -	01/2019
191	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	50.40	11/2018 -	11/2018
192	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	137.00	04/2019 -	04/2019
193	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.30	342.29	06/2019 -	06/2019
194	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	81.99	06/2018 -	06/2018
195	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	411.76	12/2018 -	12/2018
196	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P) - [N18000219]	5/2016	14,733.37 -	14,733.37	812.04	11/2019 -	11/2019
197	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	600.02	05/2019 -	05/2019
198	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	60.40	11/2018 -	11/2018
199	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	66.46	05/2018 -	05/2018
200	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	147.51	04/2018 -	04/2018
	<u>National Thermal Power Corporation</u>						
201	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,106.00	07/2020 -	07/2020
	<u>Power Grid Corporation Of India Limited</u>						
202	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	758.15	07/2018 -	07/2018
	<u>National Thermal Power Corporation</u>						
203	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	3,537.00	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						
204	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	1,969.63	11/2008 09/2018	09/2018
205	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	1,971.62	08/2014 12/2017	12/2017

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Electric Power Corporation</u>						
206	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,544.55	08/2013 03/2018	03/2018
207	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,099.06	12/2009 03/2018	03/2018
	<u>Power Grid Corporation Of India Limited</u>						
208	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	834.84	07/2018 -	07/2018
209	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	733.18	04/2017 03/2018	03/2018
210	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	58.24	03/2018 -	03/2018
211	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	41.97	05/2017 06/2019	06/2019
212	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	3,557.86	04/2018 -	04/2018
213	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	32.97	10/2018 -	10/2018
	Total		97,246.52 -	1,03,314.05	32,193.59		
	<u>RAILWAYS</u>						
	<u>North Eastern Railway</u>						
214	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	-	03/2022 -	03/2022
	<u>West Central Railway</u>						
215	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
	<u>East Coast Railway</u>						
216	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	66.36	03/2021 -	03/2021
	<u>Rail India Technical And Economic Service</u>						
217	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Container Corporation Of India</u>						
218	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	103.59	03/2019 -	03/2019
219	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	208.87	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
220	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	145.79	03/2018 -	03/2018
221	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	361.35	03/2018 -	03/2018
222	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	20.03	03/2019 -	03/2019
223	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	221.08	03/2019 -	03/2019
224	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	383.20	03/2018 -	03/2018
	<u>South East Central Railway</u>						
225	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
	<u>Rail Vikas Nigam Ltd.</u>						
226	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	549.59	12/2026 -	12/2026
227	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	-	12/2025 -	12/2025
228	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	798.85	03/2019 -	03/2019
229	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	35.23	12/2024 -	12/2024
230	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	23.63	12/2024 -	12/2024
	<u>South Eastern Railway</u>						
231	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.99	12/2021 -	12/2021
232	TAMLUK DIGHA 88.9 KM WITH MM DESHPAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	482.05	12/2021 -	12/2021
233	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	-	03/2021 -	03/2021
234	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
235	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
	<u>East Central Railways</u>						
236	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	73.95	03/2020 -	03/2020
	<u>West Central Railway</u>						
237	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
238	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
239	BINA - KOTA DOUBLING WITH RE - [N22000414	4/2011	1,485.65 -	1,485.85	718.67	12/2020 -	12/2020
240	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,183.30	767.18	12/2020 -	12/2020
241	BANASPANI- JAKHPURA - DOUBLING - [N22000412	3/2009	942.95 -	942.95	835.03	03/2019 -	03/2019
242	RAIPUR - TITLAGARH - DOUBLING - [N22000411	3/2007	758.09 -	758.09	671.78	03/2020 -	03/2020
243	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	3/2006	960.18 -	960.18	739.22	03/2020 -	03/2020
244	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	1,514.45 -	1,750.00	1,237.34	03/2020 -	03/2020
245	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	.16	12/2025 -	12/2025
	<u>South Central Railway</u>						
246	MANMAD-PARBHANI-NANDED-SECUNDERABAD- GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>Container Corporation Of India</u>						
247	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	8/2016	234.50 -	234.50	.39	03/2019 -	03/2019
248	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428	10/2013	343.00 -	343.00	245.96	03/2019 -	03/2019
	<u>East Coast Railway</u>						
249	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	4/2015	701.61 -	810.02	50.37	03/2021 -	03/2021
	<u>North Central Railway</u>						
250	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>East Central Railways</u>						
251	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
252	KIUL - GAYA DOUBLING PROJECT - [N22000349	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
	Total		44,682.64 -	58,420.30	9,174.82		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
253	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
254	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
255	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
256	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
	<u>Public Works Dept Of State</u>						
257	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
	<u>Ministry Of Road Transport And Highways</u>						
258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
	<u>National Highways Development Project</u>						
259	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
	<u>Ministry Of Road Transport And Highways</u>						
260	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
	<u>National Highways Authority Of India</u>						
261	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
262	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
263	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
264	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
265	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
	<u>National Highways Development Project</u>						
266	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
	<u>National Highways Authority Of India</u>						
267	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
268	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	157.03	06/2018 -	06/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
269	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	710.31	03/2018 -	03/2018
270	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
271	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
272	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
273	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	675.07	03/2018 -	03/2018
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
274	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
	<u>National Highways Authority Of India</u>						
275	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
276	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
277	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
278	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	2,805.32	01/2018 -	01/2018
279	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
280	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	200.36	06/2018 -	06/2018
281	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	188.28	06/2018 -	06/2018
282	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	116.26	06/2018 -	06/2018
283	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
284	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
285	FOUR LANING OF PARWANOO - SOLAN - [N24000479]	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
	<u>National Highways Development Project</u>						
286	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Highways Authority Of India</u>						
287	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
288	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
289	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
290	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
291	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
292	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
293	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
294	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	-	02/2020 -	02/2020
	<u>Ministry Of Road Transport And Highways</u>						
295	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
	<u>National Highways Authority Of India</u>						
296	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
297	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
298	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	3/2017	993.16 -	1,434.00	-	03/2020 -	03/2020
299	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	3/2017	831.58 -	1,177.00	-	03/2020 -	03/2020
300	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673]	3/2017	985.41 -	1,200.00	-	03/2020 -	03/2020
301	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	-	03/2020 -	03/2020
302	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
303	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
304	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
305	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
306	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	3/2017	1,041.62 -	1,187.10	-	03/2020 -	03/2020
307	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32 -	503.10	-	03/2020 -	03/2020
308	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
309	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
310	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
311	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
312	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
313	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
314	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	443.77	03/2018 -	03/2018
315	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	612.73	03/2018 -	03/2018
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
316	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
317	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
318	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
	<u>Ministry Of Road Transport And Highways</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
319	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
	<u>Public Works Dept Of State</u>						
320	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
	<u>National Highways Development Project</u>						
321	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
	<u>Ministry Of Road Transport And Highways</u>						
322	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
323	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
324	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
325	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
326	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
327	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
328	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
329	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
	Total		58,533.36 -	60,381.80	6,485.27		
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
330	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017
331	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		454.50 -	468.33	.14		
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
332	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
	<u>National Mineral Development Corporation (Nmhc)</u>						
333	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	13,054.00	05/2015 10/2018	10/2018
	<u>Steel Authority Of India Limited (Sail)</u>						
334	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
335	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	37.19	06/2019 -	06/2019
	<u>National Mineral Development Corporation (Nmhc)</u>						
336	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
	<u>Hindustan Steelwork Construction Limited</u>						
337	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	Total		17,231.06 -	17,231.06	13,507.40		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
338	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	-	04/2018 -	04/2018
339	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	222.00	-	05/2018 -	05/2018
340	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	164.90	-	04/2018 -	04/2018
341	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	163.00 -	163.00	-	08/2018 -	08/2018
342	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
	Total		917.98 -	924.50	.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
343	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	309.07	05/2017 02/2018	02/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Lucknow Metro Rail Corporation Limited</u>						
344	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>Central Public Works Department</u>						
345	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	69.25	01/2018 05/2018	05/2018
346	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	.61	03/2020 -	03/2020
347	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	57.58	04/2019 -	04/2019
348	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	-	02/2020 -	02/2020
349	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	2/2016	496.18 496.00	498.99	.20	06/2017 06/2020	06/2020
	<u>Chennai Metro Rail Ltd</u>						
350	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
	<u>National Building Construcion Corporation Ltd</u>						
351	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019
	<u>Central Public Works Department</u>						
352	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]	12/2012	188.87 -	188.87	184.89	12/2015 03/2018	03/2018
	Total		16,949.20 -	16,806.01	6,151.37		
	Grand Total		4,99,257.74	5,20,502.42	1,29,983.82		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Northern Coal Fields Limited</u>						
4	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
	<u>Singareni Colliers Company Limited</u>						
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
7	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
	<u>Neyveli Lignite Corporation</u>						
9	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	12/2017	11.60
10	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	Total		19,411.53 -	20,221.55			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
11	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	2.97
12	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.51
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010	02/2016	482.85 -	494.00	12/2017 -	02/2018	2.31
	Total		482.85 -	494.00			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
14	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	03/2018	13.31
	Total		168.90 -	191.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
15	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Oil India Limited</u>						
16	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Indian Oil Corporation Limited</u>						
18	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Oil & Natural Gas Corporation Limited</u>						
19	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,637.00	04/2016 -	03/2018	36.68
	<u>Oil India Limited</u>						
20	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	03/2018	12.15
	<u>Oil & Natural Gas Corporation Limited</u>						
21	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
	<u>Oil India Limited</u>						
22	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	<u>Hindustan Petroleum Corporation Limited</u>						
23	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Oil & Natural Gas Corporation Limited</u>						
24	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
25	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Gas Authority Of India Limited</u>						
26	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	03/2017	1,933.00 -	2,253.00	12/2020 -	12/2020	16.55
27	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	03/2017	1,740.00 -	1,828.00	12/2020 -	12/2020	5.06
	Total		16,634.28 -	20,510.59			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
28	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,559.49	09/2010 -	-	195.28
30	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	02/2015	302.49 302.00	302.49	02/2016 -	-	.16
	<u>National Thermal Power Corporation</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
31	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2020	29.14
	<u>Power Grid Corporation Of India Limited</u>						
32	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	03/2018	30.37
33	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	01/2018	46.77
	<u>National Thermal Power Corporation</u>						
34	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	12/2018	5.91
	<u>Satluj Jal Vidyut Nigam Limited</u>						
35	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Damodar Valley Corporation</u>						
36	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
37	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
	<u>Thdc India Limited</u>						
38	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	3,939.11	02/2016 -	12/2020	137.73
	<u>Power Grid Corporation Of India Limited</u>						
39	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37
	<u>National Hydro-Electric Power Corporation</u>						
40	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	02/2018	61.50
	<u>Power Grid Corporation Of India Limited</u>						
41	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
42	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
43	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	Total		42,972.91 -	74,402.46			
	<u>RAILWAYS</u>						
	<u>North Central Railway</u>						
44	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
45	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	123.75
	<u>Southern Railway</u>						
46	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
47	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
	<u>North East Frontier Railway</u>						
48	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
	<u>South Central Railway</u>						
49	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21
	<u>Southern Railway</u>						
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
	<u>South Central Railway</u>						
51	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
	<u>Metropolitan Rapid Transport Projects</u>						
52	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
	<u>South Central Railway</u>						
53	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
	<u>Eastern Railways</u>						
54	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
55	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
	<u>Northern Railway</u>						
56	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
	<u>Rail Vikas Nigam Ltd.</u>						
57	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
	<u>West Central Railway</u>						
58	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	273.12
	<u>North Eastern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
59	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	-	03/2018	88.85
60	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	-	-	60.34
	<u>North Central Railway</u>						
61	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
	<u>North Eastern Railway</u>						
62	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	-	05/2019	212.37
	<u>South East Central Railway</u>						
63	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	-	-	186.92
	<u>Rail Vikas Nigam Ltd.</u>						
64	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
65	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	65.70
66	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	380.00	12/2007 03/2010	03/2017	178.14
67	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
68	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
	<u>Southern Railway</u>						
69	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	-	-	412.75
70	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	-	-	210.34
71	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	-	-	404.39
	<u>Railway Electrification</u>						
72	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>North East Frontier Railway</u>						
73	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
	<u>East Central Railways</u>						
74	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
	<u>South Central Railway</u>						
75	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	-	03/2022	206.55
	<u>Rail Vikas Nigam Ltd.</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
	<u>North Western Railway</u>						
77	JAIPUR - RINGU - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02
	<u>Western Railway</u>						
78	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
79	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
	<u>North East Frontier Railway</u>						
80	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	05/2016	123.34
	<u>Central Railways</u>						
81	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	03/2023	534.55
	<u>Eastern Railways</u>						
82	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
83	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
84	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
85	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
	<u>Central Railways</u>						
86	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	371.85	- -	-	276.60
87	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	277.00	- -	-	188.06
	<u>South Western Railway</u>						
88	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
89	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
	<u>South Central Railway</u>						
90	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
91	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
	<u>Northern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
92	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
93	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
	<u>Rail Vikas Nigam Ltd.</u>						
94	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
	<u>South Western Railway</u>						
95	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
96	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
	<u>Rail Vikas Nigam Ltd.</u>						
97	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
	<u>South Western Railway</u>						
98	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
	<u>South Central Railway</u>						
99	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
	<u>Northern Railway</u>						
100	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
101	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
	<u>South Western Railway</u>						
102	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
	<u>Eastern Railways</u>						
103	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
104	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
	<u>South Central Railway</u>						
105	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	-	77.08
	<u>South Eastern Railway</u>						
106	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
107	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
	<u>Eastern Railways</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
108	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168 <u>North East Frontier Railway</u>	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
109	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201 <u>West Central Railway</u>	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
110	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232 <u>East Central Railways</u>	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
111	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240 <u>North Central Railway</u>	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
112	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243 <u>East Central Railways</u>	04/1999	108.00 -	432.72	12/2009 -	-	300.67
113	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257 <u>North East Frontier Railway</u>	04/1997	162.87 -	541.00	- -	-	232.17
114	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266 <u>East Coast Railway</u>	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
115	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284 <u>North East Frontier Railway</u>	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
116	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288 <u>East Central Railways</u>	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
117	KOSI BRIDGE (NL), ECR - [220100304 <u>Metropolitan Rapid Transport Projects</u>	04/2002	322.95 -	341.41	03/2012 -	-	5.72
118	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028 <u>North East Frontier Railway</u>	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
119	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	465.00	03/2011 -	10/2011	173.53
120	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	780.00	- -	03/2020	290.00
121	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
122	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124 <u>Metropolitan Rapid Transport Projects</u>	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>Eastern Railways</u>						
124	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
	<u>North East Frontier Railway</u>						
125	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,300.00	03/2009 -	11/2017	335.48
126	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
127	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	03/2020	27.24
128	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
	<u>North Eastern Railway</u>						
129	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	-	58.06
130	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
	<u>North Western Railway</u>						
131	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	827.84	- -	08/2018	101.87
132	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38
	<u>Northern Railway</u>						
133	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
134	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
135	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
136	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
137	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,141.70	12/2012 -	-	275.56
138	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	380.00	02/2009 02/2009	06/2017	128.70
139	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82
140	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South Central Railway</u>						
141	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
142	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
143	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
	<u>South East Central Railway</u>						
144	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
	<u>South Eastern Railway</u>						
145	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
147	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	491.33	06/2004 -	-	153.17
	<u>South Western Railway</u>						
148	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
	<u>North Eastern Railway</u>						
149	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) [N22000345	04/1997	836.26 -	1,072.52	- -	-	28.25
	<u>South Western Railway</u>						
150	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	-	81.45
	<u>Western Railway</u>						
151	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
	<u>East Coast Railway</u>						
152	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
153	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
154	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	- -	03/2020	52.77
155	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
	<u>North Eastern Railway</u>						
156	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
	<u>Rail Vikas Nigam Ltd.</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
157	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	350.00	-	03/2019	84.11
	<u>South Eastern Railway</u>						
158	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
	<u>North Western Railway</u>						
159	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	-	03/2020	14.33
160	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84
	<u>South Central Railway</u>						
161	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	-	-	711.70
	<u>Central Railways</u>						
162	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	390.00
	<u>Southern Railway</u>						
163	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	-	01/2018	411.93
	<u>North Eastern Railway</u>						
164	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	-	-	.33
165	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	-	08/2017	10.26
166	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
167	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	-	10/2018	61.80
168	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
	<u>North Western Railway</u>						
169	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	-	03/2019	41.64
	<u>Rail Vikas Nigam Ltd.</u>						
170	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	-	03/2020	72.01
171	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	-	12/2020	71.11
	<u>Western Railway</u>						
172	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	-	-	92.25
173	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	-	03/2019	24.63

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
174	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	- -	12/2020	22.24
	<u>Western Railway</u>						
175	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
176	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
	<u>North Western Railway</u>						
177	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
	<u>North Central Railway</u>						
178	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
	<u>North Western Railway</u>						
179	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	- -	10/2018	24.47
180	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
181	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	- -	03/2019	14.35
182	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	- -	10/2018	19.86
183	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	- -	03/2019	44.16
	<u>North Central Railway</u>						
184	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
	<u>South Eastern Railway</u>						
185	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
186	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
187	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
188	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
	<u>Rail Vikas Nigam Ltd.</u>						
189	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	250.00	06/2013 -	12/2016	46.18
	<u>South Eastern Railway</u>						
190	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
191	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	-	12/2017	41.36
	<u>East Coast Railway</u>						
192	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
193	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	-	-	84.98
194	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	-	-	32.80
	<u>East Central Railways</u>						
195	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91
196	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
197	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
	<u>Southern Railway</u>						
198	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	-	-	147.28
199	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	-	-	348.88
200	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
201	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
	<u>Rail Vikas Nigam Ltd.</u>						
202	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	-	03/2018	120.09
	<u>Southern Railway</u>						
203	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
	<u>North East Frontier Railway</u>						
204	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	-	03/2020	71.62
205	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007	04/2016	107.49
206	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	-	07/2019	130.16
207	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	-	03/2018	200.33
208	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	-	03/2019	58.70
	<u>Southern Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
209	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	-	-	295.05
210	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71
211	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	-	-	78.83
	<u>North East Frontier Railway</u>						
212	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	-	03/2021	46.95
213	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	-	03/2020	94.45
214	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	-	63.25
215	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	-	03/2020	171.38
216	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	-	03/2018	257.63
217	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	-	03/2019	71.41
218	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	-	03/2019	62.12
	<u>Rail Vikas Nigam Ltd.</u>						
219	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2018	29.06
	<u>Southern Railway</u>						
220	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	-	-	199.29
	<u>Eastern Railways</u>						
221	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	-	-	51.49
222	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	-	-	27.07
	<u>Central Railways</u>						
223	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024	120.28
224	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024	25.04
	<u>Rail Vikas Nigam Ltd.</u>						
225	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	-	-	9.32
	<u>East Central Railways</u>						
226	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	<u>East Coast Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
227	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
	<u>North East Frontier Railway</u>						
228	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	08/2015	5.12
229	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
230	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	03/2020	10.01
	<u>South Eastern Railway</u>						
231	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
232	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
	<u>Southern Railway</u>						
233	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
	<u>Rail Vikas Nigam Ltd.</u>						
234	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
	<u>South Eastern Railway</u>						
235	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	<u>Rail Vikas Nigam Ltd.</u>						
236	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
237	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
238	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	12/2026	277.53
239	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
240	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
241	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	Total		1,19,477.05 -	2,99,322.95			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
242	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	12/2017	28.93
243	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
244	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
245	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	12/2017	68.99
246	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
	<u>Public Works Dept Of State</u>						
247	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
	<u>National Highways Authority Of India</u>						
248	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	03/2018	42.25
249	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
250	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
251	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
	<u>Public Works Dept Of State</u>						
252	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
253	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
254	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12
255	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	.01
	<u>Dept Of Road Transport & Highways</u>						
256	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	<u>Public Works Dept Of State</u>						
257	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
	<u>National Highways Authority Of India</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
258	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
259	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
260	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
261	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
262	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
263	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
264	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
265	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
266	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
267	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	03/2020	13.97
268	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
269	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
270	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
271	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4) - [N24000673	03/2017	985.41 -	1,200.00	03/2020 -	03/2020	21.78
272	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	03/2020	41.54
273	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	03/2020	44.39
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
274	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	Total		23,165.35 -	29,854.53			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
	<u>Port Trust</u>						
275	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
	<u>Kamarajar Port Limited</u>						
276	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20
277	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
	<u>Rail Vikas Nigam Ltd.</u>						
278	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	-	66.82
	<u>Mumbai Port Trust</u>						
279	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
280	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
	<u>Rastrya Ispat Nigam Limited</u>						
281	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	<u>Hindustan Steelwork Construction Limited</u>						
282	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	Total		1,261.61 -	1,777.68			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
283	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	06/2019	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs.150 Crore and above					(December 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
284	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]	06/2010	205.00 -	170.62	03/2012 -	03/2018	-16.77
285	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
	Total		701.18 -	669.61			
	Grand Total		2,45,102.87	4,85,672.72			

List of Delayed Projects w.r.t. Latest Schedule

Annexure- XIV

Costing Rs.150 Crore and above						(December 2017)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,532.63	09/2010 09/2016	06/2018	93	21
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	11,088.00	12/2015 11/2016	11/2019	47	36
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,666.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	69,728.00	27,419.63				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	26.44				
	<u>COAL</u>								
	<u>Neyveli Lignite Corporation</u>								
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	767.00	733.23	06/2017 -	12/2017	6	-
	<u>Mahanadi Coal Fields Limited</u>								
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	331.06	03/2010 -	03/2018	96	-
	<u>Northern Coal Fields Limited</u>								
8	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	486.57	397.54	03/2012 -	03/2018	72	-
	<u>Singareni Colliers Company Limited</u>								
9	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	144.33	03/2015 -	03/2018	36	-
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	176.79	03/2012 -	03/2018	72	-
	<u>South-Eastern Coal Fields Limited</u>								
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	199.85	03/2014 -	03/2018	48	-
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2018	24	-
	<u>Central Coal Fields Limited</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	347.32	03/2016 -	03/2018	24	-
	<u>South-Eastern Coal Fields Limited</u>								
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	153.43	03/2016 -	03/2018	24	-
	<u>Singareni Colliers Company Limited</u>								
15	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	121.94	06/2015 -	03/2018	33	-
16	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	147.18	03/2016 -	03/2018	24	-
	<u>Bharat Coking Coal Limited</u>								
17	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	156.92	05/2014 -	04/2018	47	-
18	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	153.87	04/2014 -	04/2018	48	-
	<u>Mahanadi Coal Fields Limited</u>								
19	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	282.30	03/2017 -	05/2018	14	-
	<u>Bharat Coking Coal Limited</u>								
20	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
	<u>Mahanadi Coal Fields Limited</u>								
21	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	405.44	03/2013 -	11/2018	68	-
	<u>Singareni Colliers Company Limited</u>								
22	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	163.85	03/2012 -	03/2019	84	-
	<u>Mahanadi Coal Fields Limited</u>								
23	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	195.09	03/2010 -	03/2019	108	-
24	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	259.50	03/2012 -	03/2019	84	-
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	221.47	03/2013 -	03/2019	72	-
	<u>Central Coal Fields Limited</u>								
26	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.06	03/2012 -	03/2019	84	-
27	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	153.85	03/2012 -	03/2019	84	-
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.15	03/2014 -	03/2019	60	-
	<u>Singareni Colliers Company Limited</u>								
29	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
	<u>Bharat Coking Coal Limited</u>								
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	207.23	04/2015 -	04/2019	48	-
	<u>South-Eastern Coal Fields Limited</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
31	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
	<u>Central Coal Fields Limited</u>								
32	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	-
	<u>Singareni Colliers Company Limited</u>								
33	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	.34	03/2015 -	03/2020	60	-
34	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	-
35	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	67.63	07/2016 -	03/2020	44	-
	<u>Eastern Coal Fields Limited</u>								
36	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	321.06	03/2018 -	03/2020	24	-
	<u>Central Coal Fields Limited</u>								
37	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	120.77	07/2012 03/2017	03/2021	104	48
	<u>Singareni Colliers Company Limited</u>								
38	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	267.42	03/2015 -	03/2021	72	-
39	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	477.74	03/2012 -	03/2023	132	-
	<u>Western Coal Fields Limited</u>								
40	BHANEAGAN OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	72.23	03/2023 02/2017	03/2023	0	73
	Total		12,924.33 -	13,807.08	6,742.91				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (SAIL)</u>								
41	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	196.21	05/2016 -	12/2017	19	-
	<u>Hindustan Steelwork Construction Limited</u>								
42	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	12	-
	<u>Steel Authority Of India Limited (SAIL)</u>								
43	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,303.09	03/2013 -	02/2018	59	-
	<u>Hindustan Steelwork Construction Limited</u>								
44	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
	<u>Steel Authority Of India Limited (SAIL)</u>								
45	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	528.08	12/2017 -	05/2018	5	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above							(December 2017)		
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
46	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	200.59	10/2017 -	07/2018	9	-
	<u>Hindustan Steelwork Construction Limited</u>								
47	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
	<u>Rastrya Ispat Nigam Limited</u>								
48	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	53.91	07/2018 -	09/2018	2	-
49	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	715.85	12/2017 -	10/2018	10	-
50	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	23.78	08/2018 -	10/2018	2	-
	<u>Hindustan Steelwork Construction Limited</u>								
51	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
52	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
	<u>Rastrya Ispat Nigam Limited</u>								
53	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	63.94	09/2018 -	01/2019	4	-
	<u>Steel Authority Of India Limited (Sail)</u>								
54	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	1,837.55	04/2018 -	02/2019	10	-
	<u>Rastrya Ispat Nigam Limited</u>								
55	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	234.69	10/2016 -	03/2019	29	-
	<u>Hindustan Steelwork Construction Limited</u>								
56	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	Total		31,036.67 -	30,848.46	23,495.27				
	<u>PETROLEUM</u>								
	<u>Chennai Petroleum Corporation Limited</u>								
57	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	244.25	04/2017 -	01/2018	9	-
58	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	171.84	11/2016 -	02/2018	15	-
	<u>Indian Oil Corporation Limited</u>								
59	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	435.08	07/2017 -	02/2018	7	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Oil India Limited</u>								
60	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	256.41	147.19	12/2016 -	03/2018	15	-
61	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	438.84	134.50	03/2017 -	11/2018	20	-
	<u>Gas Authority Of India Limited</u>								
62	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 2,915.00	2,915.00	1,469.29	12/2012 -	02/2019	74	-
	<u>Indian Oil Corporation Limited</u>								
63	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 -	714.25	276.85	10/2017 -	03/2019	17	-
	<u>Oil & Natural Gas Corporation Limited</u>								
64	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	390.52	148.14	03/2019 -	04/2019	1	-
	Total		6,049.76 -	6,271.00	3,027.14				
	<u>POWER</u>								
	<u>Power Grid Corporation Of India Limited</u>								
65	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL, MULTI STATE	05/2014	829.98 -	829.98	419.93	08/2016 10/2017	12/2017	16	2
66	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34 -	341.00	246.39	06/2012 -	01/2018	67	-
67	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	305.04	165.34	03/2017 10/2017	01/2018	10	3
68	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL, MULTI STATE	04/2015	2,525.00 -	2,525.00	1,565.00	11/2017 -	01/2018	2	-
	<u>National Hydro-Electric Power Corporation</u>								
69	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,186.86	01/2016 -	02/2018	25	-
	<u>Power Grid Corporation Of India Limited</u>								
70	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,575.15	08/2013 12/2017	02/2018	54	2
71	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,425.08	11/2012 12/2017	02/2018	63	2
	<u>National Thermal Power Corporation</u>								
72	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	15,166.19	14,795.00	01/2017 07/2017	02/2018	13	7
	<u>Satluj Jal Vidyut Nigam Limited</u>								
73	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN, GUJARAT	11/2016	330.00 -	330.00	186.30	11/2017 -	02/2018	3	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Power Grid Corporation Of India Limited</u>								
74	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,589.80	12/2012 02/2018	03/2018	63	1
75	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,357.64	09/2014 06/2017	03/2018	42	9
76	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	364.29	08/2014 12/2017	03/2018	43	3
77	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	136.45	09/2014 09/2017	03/2018	42	6
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	727.62	11/2014 06/2017	03/2018	40	9
79	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	121.98	04/2016 12/2017	03/2018	23	3
80	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	374.70	11/2016 11/2017	03/2018	16	4
81	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	140.76	03/2016 07/2017	03/2018	24	8
82	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	231.75	02/2017 06/2017	03/2018	13	9
83	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	134.45	02/2016 08/2017	03/2018	25	7
84	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,091.00	12/2015 -	03/2018	27	-
	<u>National Thermal Power Corporation</u>								
85	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	6,860.00	09/2011 06/2017	04/2018	79	10
	<u>Power Grid Corporation Of India Limited</u>								
86	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART - C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	585.89	06/2015 12/2017	05/2018	35	5
87	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	653.52	09/2010 12/2017	06/2018	93	6
88	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,489.03	10/2012 02/2018	06/2018	68	4
89	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,048.50	12/2015 12/2017	06/2018	30	6
90	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,174.49	04/2016 09/2017	06/2018	26	9

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	393.44	06/2016 02/2018	06/2018	24	4
92	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,707.65	03/2018 -	06/2018	3	-
93	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	169.37	03/2018 -	06/2018	3	-
94	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	06/2018	8	8
95	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	176.23	11/2017 -	06/2018	7	-
96	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,296.77	04/2018 -	07/2018	3	-
97	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	485.99	06/2014 03/2018	09/2018	51	6
98	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	477.43	09/2017 -	09/2018	12	-
99	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,213.54	09/2017 -	09/2018	12	-
	<u>National Hydro-Electric Power Corporation</u>								
100	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,597.22	09/2009 -	12/2018	111	-
	<u>National Thermal Power Corporation</u>								
101	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,206.00	11/2016 12/2017	12/2018	25	12
	<u>Power Grid Corporation Of India Limited</u>								
102	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	168.86	07/2017 -	12/2018	17	-
	<u>National Thermal Power Corporation</u>								
103	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	10,084.21	01/2018 -	12/2018	11	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
104	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	478.69	12/2016 -	12/2018	24	-
	<u>National Thermal Power Corporation</u>								
105	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	8,892.00	06/2017 12/2017	01/2019	19	13
106	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	8,413.00	09/2017 03/2018	01/2019	16	10

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
107	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	7,998.00	6,838.73	05/2014 09/2017	02/2019	57	17
108	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	-
109	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	6,615.00	08/2018 -	03/2019	7	-
	<u>Thdc India Limited</u>								
110	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	148.06	02/2014 02/2018	03/2019	61	13
	<u>Power Grid Corporation Of India Limited</u>								
111	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	243.37	01/2018 -	03/2019	14	-
	<u>National Thermal Power Corporation</u>								
112	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,400.00	03/2019 -	09/2019	6	-
	<u>Power Grid Corporation Of India Limited</u>								
113	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	466.74	12/2018 -	12/2019	12	-
114	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	386.29	12/2018 -	12/2019	12	-
	<u>National Thermal Power Corporation</u>								
115	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,359.00	03/2013 06/2019	03/2020	84	9
116	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	13,932.00	01/2011 05/2018	06/2020	113	25
117	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	5,674.00	02/2019 02/2020	09/2020	19	7
	<u>Thdc India Limited</u>								
118	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,312.24	06/2013 -	11/2020	89	-
119	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	3,939.11	2,443.93	02/2016 09/2019	12/2020	58	15
	<u>National Thermal Power Corporation</u>								
120	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 1,592.34	1,381.84	294.00	09/2019 -	03/2021	18	-
	<u>Chenab Valley Power Projects [P] Limited</u>								
121	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	881.41	04/2020 12/2017	06/2023	38	66
	Total		2,09,271.72 -	2,40,687.70	1,63,520.59				
	<u>HEAVY INDUSTRY</u>								
	<u>Natrip Implementation Society</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
122	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2,289.00				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
123	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10	-
124	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13	-
125	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6	-
126	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16	-
127	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6	-
	Total		1,325.52 -	1,348.00	770.90				
	<u>RAILWAYS</u>								
	<u>South Central Railway</u>								
128	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	966.98	874.72	02/2009 -	12/2017	106	-
	<u>Rail Vikas Nigam Ltd.</u>								
129	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	343.00	362.24	03/2009 03/2009	12/2017	105	105
130	SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	555.00	500.67	03/2010 -	12/2017	93	-
	<u>Western Railway</u>								
131	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,513.78	03/2014 -	12/2017	45	-
	<u>Rail Vikas Nigam Ltd.</u>								
132	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,020.64	03/2010 -	03/2018	96	-
	<u>North East Frontier Railway</u>								
133	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,450.00	4,892.39	04/2008 12/2011	06/2018	122	78
	<u>Metropolitan Rapid Transport Projects</u>								
134	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
	<u>Northern Railway</u>								
135	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Rail Vikas Nigam Ltd.</u>								
136	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	722.31	03/2016 -	12/2018	33	-
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	491.31	03/2016 -	12/2018	33	-
	<u>North East Frontier Railway</u>								
138	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,040.00	2,748.23	12/2008 -	03/2019	123	-
	<u>Eastern Railways</u>								
139	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	-	111
	<u>Rail Vikas Nigam Ltd.</u>								
140	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.99	1,025.83	- 09/2009	03/2019	-	114
	<u>Metropolitan Rapid Transport Projects</u>								
141	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
	<u>Western Railway</u>								
142	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	37.15	03/2012 -	03/2019	84	-
	<u>East Central Railways</u>								
143	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	61.44	03/2018 -	03/2019	12	-
	<u>North Western Railway</u>								
144	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	895.00	676.07	03/2014 -	06/2019	63	-
	<u>South East Central Railway</u>								
145	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
	<u>Rail Vikas Nigam Ltd.</u>								
146	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.07	583.08	02/2015 -	12/2019	58	-
147	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	388.00	343.71	02/2006 -	12/2019	166	-
	<u>North Western Railway</u>								
148	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,143.70	514.27	03/2015 -	12/2019	57	-
	<u>Metropolitan Rapid Transport Projects</u>								
149	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	678.01	03/2004 -	03/2020	192	-
	<u>Eastern Railways</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
150	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
	<u>North East Frontier Railway</u>								
151	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	9,658.00	6,985.58	03/2011 -	03/2020	108	-
	<u>Rail Vikas Nigam Ltd.</u>								
152	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,478.11	03/2008 06/2008	03/2020	144	141
	<u>North East Frontier Railway</u>								
153	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	2,407.41	03/2014 -	03/2020	72	-
154	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	1,825.65	04/2014 -	03/2020	71	-
155	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
	<u>Western Railway</u>								
156	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	27.69	03/2013 -	03/2020	84	-
	<u>North East Frontier Railway</u>								
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	406.14	03/2015 -	03/2020	60	-
	<u>South Western Railway</u>								
158	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	324.71	- 11/2015	03/2020	-	52
	<u>Rail Vikas Nigam Ltd.</u>								
159	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,541.16	03/2016 -	12/2020	57	-
	<u>East Coast Railway</u>								
160	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	37.12	03/2021 -	03/2022	12	-
161	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	22.36	03/2021 -	03/2022	12	-
	<u>North Central Railway</u>								
162	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
163	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
	<u>West Central Railway</u>								
164	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	Total		44,498.10 -	1,17,652.86	56,613.62				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>National Highways Authority Of India</u>								
165	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	12/2017	106	-
166	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	12/2017	104	-
167	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	12/2017	104	-
168	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	12/2017	116	-
169	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	12/2017	101	-
170	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	63	-
171	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,373.60	05/2013 -	12/2017	55	-
172	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	64	-
173	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	40	-
174	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,063.52	03/2013 -	12/2017	57	-
175	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2017	55	-
176	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	-
177	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.89	10/2013 -	12/2017	50	-
178	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	49	-
179	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	42	-
180	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,416.68	08/2013 -	12/2017	52	-
181	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	-	06/2014 -	12/2017	42	-
182	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,724.78	09/2014 -	12/2017	39	-
183	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	320.46	01/2014 -	12/2017	47	-
184	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	-	10/2013 -	12/2017	50	-
185	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	856.59	06/2015 -	12/2017	30	-
186	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	-	04/2015 -	12/2017	32	-
187	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
188	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	-	01/2016 -	12/2017	23	-
189	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	-	10/2011 -	12/2017	74	-
190	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	28	-
191	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,479.14	07/2017 -	01/2018	6	-
192	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117	-
193	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15	-
194	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	-
195	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	03/2018	95	-
196	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	-
197	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	-
198	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	-
199	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	-
200	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55	-
201	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	518.12	07/2014 -	03/2018	44	-
202	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	395.20	06/2014 -	03/2018	45	-
203	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	-
204	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,374.50	09/2016 -	03/2018	18	-
205	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	252.39	09/2017 -	03/2018	6	-
206	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,424.00	08/2016 -	03/2018	19	-
207	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,094.55	06/2012 -	03/2018	69	-
	Public Works Dept Of State								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
208	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
	<u>National Highways Authority Of India</u>								
209	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	-
210	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
211	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	-
212	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	58.72	05/2017 -	06/2018	13	-
213	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92	563.92	186.50	11/2016 -	06/2018	19	-
214	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
215	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	286.02	06/2016 -	06/2018	24	-
216	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	97.35	07/2016 -	07/2018	24	-
217	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	730.88	11/2017 -	08/2018	9	-
	<u>Ministry Of Road Transport And Highways</u>								
218	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
	<u>National Highways Authority Of India</u>								
219	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	-
220	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	-
221	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	-
222	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	-
223	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above						(December 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
224	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
225	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
226	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
227	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	Total		55,031.75 -	58,574.37	26,361.66				
	<u>SHIPPING AND PORTS</u>								
	<u>Port Trust</u>								
228	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	141	-
	<u>Mumbai Port Trust</u>								
229	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	-
	<u>Kamarajar Port Limited</u>								
230	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20	-
	Total		1,116.39 -	1,527.36	550.92				
	<u>TELECOMMUNICATIONS</u>								
	<u>Mahanagar Telephone Nigam Limited</u>								
231	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	-
	<u>Department Of Telecommunication</u>								
232	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	6,660.00	07/2015 -	06/2019	47	-
	Total		13,752.26 -	25,082.26	6,832.30				
	<u>URBAN DEVELOPMENT</u>								
	<u>Chennai Metro Rail Ltd</u>								
233	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	24	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
234	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	74.54	11/2015 -	12/2017	25	-
	<u>Delhi Metro Rail Corporation Ltd</u>								
235	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	-
	<u>Central Public Works Department</u>								
236	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	269.50	03/2016 12/2017	03/2018	24	3
237	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 166.97	170.62	146.41	03/2012 -	03/2018	72	-
238	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	11
239	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	528.94	12/2015 -	03/2018	27	-
240	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	414.62	03/2015 12/2017	03/2018	36	3
241	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	122.43	08/2016 -	06/2018	22	-
242	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	126.71	11/2014 -	10/2018	47	-
243	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
244	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	38.76	03/2016 -	12/2018	33	-
245	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	39.73	04/2018 -	05/2019	13	-
246	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
247	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
248	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
249	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs.150 Crore and above								(December 2017)	
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Central Public Works Department</u>								
250	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 2,283.30	1,592.00	157.53	10/2019 -	03/2020	5	-
	Total		97,764.11 -	1,02,950.11	56,048.08				
	Grand Total		5,41,923.22	6,72,745.83	3,73,698.46				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492	93
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	12/2017	687.28	6
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
9	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
10	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
11	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60
12	MURADIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
13	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	96
14	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
16	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
17	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
18	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
19	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72
20	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
22	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
23	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
25	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
26	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
27	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
28	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2018	289.45	47
29	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2018	269.82	48
30	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
38	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
39	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
40	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
42	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	6
46	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.9	10
47	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	6
48	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2018	204.44	13

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A	ONGC	05/2016	06/2017	01/2018	215.38	7
52	NEW 250 TMTPL LPG PLANT AT PANAGARH	HPCL	08/2014	09/2017	03/2018	190.45	6
53	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
54	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
55	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
56	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12
57	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
58	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	03/2018	181.02	14
59	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY	CPCL	02/2016	04/2017	01/2018	367.11	9
60	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	66
62	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	93
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	11/2018	352.56	20
64	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
65	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	23
66	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
67	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
68	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
69	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	15
70	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	08/2020	690	25
71	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
72	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	02/2018	257.87	15
73	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
74	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2018	861.79	58
75	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
76	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	41
77	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7
78	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
80	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	55
81	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2018	297.33	43
82	SYSTEM STRENGTHENING IN NORTH AND	PGCIL	12/2011	08/2014	12/2017	1746.65	40

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH						
83	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	25
84	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
85	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	06/2020	8692.97	113
86	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	03/2018	198.63	42
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	03/2018	723.63	40
88	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	02/2018	15166.19	13
89	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
90	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	03/2019	12532.44	7
91	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	09/2020	14366.58	19
92	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	03/2021	1381.84	18
93	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	06/2018	871.62	8
94	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	12/2018	203.28	17
95	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	02/2018	1272.8	63
96	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	09/2018	1071.24	12
97	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	01/2018	232.34	67
98	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
99	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
100	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353	57
101	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24
102	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	03/2018	1479.3	11
103	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	06/2018	307.18	7
104	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2018	522.29	16
105	AUGMENTATION OF TRANSFORMERS IN	PGCIL	03/2014	03/2016	03/2018	155.57	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NORTHERN REGION - PART B						
106	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	03/2020	2978.48	84
107	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	04/2018	4375.35	79
108	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	03/2018	288.49	13
109	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	03/2018	196.58	25
110	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	06/2023	8112.12	38
111	SOLAPUR STPP	NTPC	03/2012	11/2016	12/2018	9395.18	25
112	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	01/2019	11846	19
113	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	05/2018	514.2	35
114	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2018	2514.88	30
115	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	01/2018	305.04	10
116	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
117	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
118	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
119	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955	27
120	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12/2018	12964.6	11
121	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	02/2019	9750.89	26
122	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
123	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2018	477.69	93
124	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	06/2018	4824.12	68
125	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	38
126	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	01/2019	11638.55	16
127	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	02/2018	11130.19	54
128	TRANSMISSION SYSTEM ASSOCIATED WITH	PGCIL	02/2010	12/2012	03/2018	2144	63

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	PALLATANA GBPP and BPTS.						
129	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2018	1364.52	26
130	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2018	374.63	23
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	06/2018	539.82	24
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	12/2017	908.08	18
133	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION	PGCIL	05/2014	08/2016	12/2017	829.98	16
134	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	89
135	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.9	99
136	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	03/2018	1940.13	42
137	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657	58
138	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2018	487.49	51

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
139	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
140	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
141	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
142	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
143	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
144	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
145	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
146	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
148	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	106
149	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45
151	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
152	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2017	133.41	105
153	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
154	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.2	96
155	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
156	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
158	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	63
159	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
160	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
161	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
162	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
163	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
164	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
165	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
166	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
167	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	57
168	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
169	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	12
170	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	33
171	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
172	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
174	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	50
175	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	45
176	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	03/2018	709	6
177	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2018	1387.11	9
178	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	12/2017	523.85	23
179	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	12/2018	563.92	12
180	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	13
181	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	06/2018	563.92	19
182	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
183	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	12/2017	1078.84	52
184	4-LANING OF BRAHMAPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
185	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	12/2017	1047	42
186	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2017	1396.18	39
187	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	12/2017	291.36	47
188	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2017	1928.22	32
189	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
190	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2018	1655.01	19
191	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	12/2017	1673.7	74
192	4-LANING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
193	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	12/2017	511.54	49
194	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.7	42
195	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	44
196	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479	30
197	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108	76
198	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.2	49
199	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2017	617	64
200	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	12/2017	1724.55	57
201	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	07/2018	641.17	24
202	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
203	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
204	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	12/2017	2498.76	40
205	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
206	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
207	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
208	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
209	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536	50
210	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	12/2017	1585	55
211	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
212	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2018	1266.6	18
213	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.1	63
214	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250	60
215	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
216	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
217	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2018	1410	42
218	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2017	280	106
219	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2017	199.81	104
220	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	112
221	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2017	200	104
222	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2018	160	117
223	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2017	196	101
224	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	03/2018	217.61	95
225	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2017	208	116
226	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
227	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
228	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	12/2017	1232	28
229	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
230	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
231	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
232	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
233	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
234	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
235	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	08/2019	600	20
236	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150	141

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
237	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
238	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2018	2858	10
239	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
240	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	02/2018	17265	59
241	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HSC	12/2007	06/2016	03/2018	253.92	21
242	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSC	05/2015	03/2017	08/2018	189	17
243	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSC	12/2007	12/2016	12/2017	202.61	12
244	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	12/2017	245.67	19
245	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSC	04/2014	09/2017	12/2018	151.33	15
246	IRRIGATION WORK OF BAGMATI	HSC	10/2005	03/2015	03/2021	956	72
247	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSC	02/2014	12/2016	12/2018	787.29	24
248	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2018	15525	41
249	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	07/2018	1034.01	9
250	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
251	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	MTNL	06/2016	06/2017	03/2018	418.26	9
252	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2019	13334	47

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
253	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
254	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	CPWD	07/2015	11/2015	12/2017	154	25
255	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
256	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600	24
257	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
258	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	03/2018	241.33	24
259	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2018	270.83	47
260	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2015	03/2018	188.87	27
261	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2018	350.02	36
262	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
263	NSG AT KOLKATA	CPWD	10/2014	04/2018	05/2019	162.88	13
264	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
265	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	02/2018	388	9
266	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	06/2018	156.57	22
267	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	33
268	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2018	205	72
269	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	03/2018	884.3	27
270	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
271	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	03/2018	38585	24
272	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
8	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	1933	2253	320
13	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
19	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
20	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
21	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
22	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	5637	1512.65

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
24	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18559.49	12274.16
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5882.01	2239.97
29	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	426.29	128.96
31	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
32	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	3939.11	2282.11
34	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
36	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
37	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
38	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
41	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	723.63	882.13	158.5
42	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
43	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1329.43	960.71
44	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
45	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
46	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
47	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
48	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	232.34	341	108.66
49	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
50	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
51	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
52	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
53	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
54	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
55	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
56	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	4404.57	5135.01	730.44

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
58	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	N.A.	36.8	614	577.2
59	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
60	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
62	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
63	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
64	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	380	243.38
65	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
66	KHURDA ROAD - BARANG 3RD LINE (DL)(ECOR)	RVNL	04/2000	03/2009	133.41	343	209.59
67	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.07	1018.84
68	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
69	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
70	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
71	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	412.05	193.86
72	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
73	GUDUR-DURGARAJPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
74	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
75	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
76	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
77	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
78	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	277	180.84
79	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	371.85	273.11
80	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
81	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
82	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5450	3950

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	MANDARHILL -DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	900.05	1125.89	225.84
84	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTPT	03/1996	03/2004	495.44	1781.98	1286.54
85	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
86	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
87	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
88	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
89	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
90	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
91	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
92	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
93	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7300	5623.69
94	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	5300	7986.04	2686.04
96	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
97	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2135	1835
98	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
99	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	465	295
100	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	900	4131.9	3231.9
101	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
102	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
103	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
104	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	03/2021	701.61	810.02	108.41
105	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
107	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	3246.26	3548.67	302.41
108	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16
109	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
110	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
111	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
112	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	N.A.	2750	3438.51	688.51
113	PUNE-NASIK (265 KM)	CR	02/2016	N.A.	2425	5341.68	2916.68
114	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
115	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1800	1198.57
116	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
117	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
118	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	535	222.88
119	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
120	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
121	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
122	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
123	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
124	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
125	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
126	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
127	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	283.55	450	166.45
128	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	630	420.23

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
130	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
131	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
132	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1810	987.61
133	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
134	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
135	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
136	ATTIPPATTU PUTTUR	SR	04/2008	N.A.	446.87	1105	658.13
137	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
138	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
139	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
140	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
141	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
142	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
143	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
144	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
145	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
146	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
147	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
148	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	N.A.	242.09	349	106.91
149	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
150	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
151	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
153	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	N.A.	1266.89	1548.66	281.77
154	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
155	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
156	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
157	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
158	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31
159	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
160	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	2815.62	2265.62
161	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.97	195.96
162	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
163	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1143.7	313.96
164	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
165	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
166	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
167	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
168	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
170	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	555	230.1
171	RAJATGARH-BARANG(LD), ECR	RVNL	04/1999	02/2009	166.16	380	213.84
172	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	1141.7	837.7
173	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
174	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	1514.45	1750	235.55

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2026	4295.3	16216	11920.7
176	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
177	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	350	159.9
178	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
179	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
180	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
181	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
182	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
183	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	227	2135	1908
184	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	194.07	491.33	297.26
185	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
186	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
187	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	NR	03/2002	06/2007	625.3	876.1	250.8
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	2500	27946	25446
189	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2100	1650
190	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
191	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	410.08	827.84	417.76
192	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
193	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
194	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	732.89	237.15
195	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
196	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
197	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	733	3040	2307

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
199	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
200	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
201	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
202	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
203	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
204	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
205	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
206	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
207	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
208	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	4500	3453.12
209	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
210	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
211	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
212	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
213	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	2300	1844
214	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
215	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
216	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	1030	342.8
217	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
218	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
219	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
220	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
222	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	509	281.1
223	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
224	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	895	241.81
225	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
226	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
227	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
228	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
229	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
230	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
231	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
232	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.99	884.35

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
233	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
234	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
235	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
236	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)	NHAI	03/2017	03/2020	985.41	1200	214.59
237	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
238	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
239	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
240	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
241	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
242	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
244	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
245	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
246	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
247	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
248	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
249	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
250	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
251	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
252	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
253	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
254	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
255	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
256	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79
257	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
258	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
259	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492.00	6100.00	2608	93

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	186.52	60
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
5	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	199.83	84

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	723.40	413.59	41
9	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
10	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
11	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12
12	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	5637.00	1512.65	23

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
14	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1114	9
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	03/2018	861.79	1256.72	394.93	58

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
16	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	545.3	12
17	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	03/2018	723.63	882.13	158.5	40
18	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	05/2018	514.20	703.10	188.9	35
19	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
20	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	2228.71	482.06	40
21	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	1337.76	763.77	55
22	TRANSMISSION SYSTEM ASSOCIATED WITH IPPTS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955.00	1364.00	409	27
23	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12/2018	1,2964.60	1,3731.26	766.66	11
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
25	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	02/2018	1272.80	1731.10	458.3	63
26	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	01/2018	232.34	341.00	108.66	67
27	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353.00	7998.00	2645	57
28	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	165.76	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.90	6179.96	3683.06	99
30	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	03/2018	1940.13	2702.65	762.52	42
31	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	3939.11	2282.11	58
32	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2018	487.49	639.46	151.97	51
33	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2018	297.33	426.29	128.96	43
34	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2018	477.69	738.48	260.79	93
35	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	06/2018	4824.12	5071.94	247.82	68
36	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	5135.01	730.44	38
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	02/2018	1,1130.19	1,3762.80	2632.61	54
38	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2018	2144.00	2932.88	788.88	63
39	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2018	1364.52	1891.41	526.89	26
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	03/2020	2978.48	3846.30	867.82	84
41	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	04/2018	4375.35	8150.00	3774.65	79
42	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	5882.01	2239.97	25
43	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	06/2020	8692.97	1,5095.67	6402.7	113

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
44	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2018	632.68	816.55	183.87	33

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS
OF RS.100 CRORE AND ABOVE
(DECEMBER 2017)**

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
46	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	1143.70	313.96	57
47	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
48	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
49	MANDARHILL -DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
50	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	3950	122
51	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2307	123
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
54	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
55	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
56	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
57	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
58	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	2,7946.00	25446	193
59	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	555.00	230.1	93
60	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	307.5	57
61	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.07	1018.84	58
62	KHURDA ROAD - BARANG 3RD LINE	RVNL	04/2000	03/2009	12/2017	133.41	343.00	209.59	105

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	(DL) (ECOR)								
63	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	126.3	166
64	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	1030.00	342.8	96
65	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
66	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
67	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	895.00	241.81	63
68	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
69	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
70	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2017	196.00	331.23	135.23	101
71	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	12/2017	1509.10	3237.87	1728.77	63
72	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	1180	76
73	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2017	199.81	385.13	185.32	104
74	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	280.13	125.09	112

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96
76	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150.00	600.00	450	141

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(DECEMBER 2017)

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
77	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	145.4	29

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
78	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2019	1,3334.00	2,4664.00	11330	47

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
79	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
80	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2018	350.02	479.87	129.85	36
81	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	1,4600.00	1,9058.00	4458	24
82	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	03/2018	241.33	349.33	108	24

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF STATE-WISE CENTRAL SECTOR PROJECTS SHOWING TIME & COST OVERRUNS (as on 01.01.2018)

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
ANDAMAN & NICOBAR ISLANDS										
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	26.44	40.28	21
ANDHRA PRADESH										
2	REVAMPING OF SINTER MACHINES -	RINL	12/2009	10/2016	03/2019	343.00	488.40	234.69	42.39	29
3	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1478.11	145.63	144
4	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	874.72	520.89	106
ARUNACHAL PRADESH										
5	PARE HYDRO ELECTRIC	NEEPCO	12/2008	08/2013	03/2018	573.99	1337.76	1544.55	133.06	55
6	KAMENG HYDROELECTRIC PROJECT	NEEPCO	12/2004	12/2009	03/2018	2496.90	6179.96	6099.06	147.51	99
7	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM.	NHIDCL	12/2016	01/2017	01/2020	138.93	155.00	0.00	11.57	36
ASSAM										
8	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	4892.39	263.33	122
9	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2017	280.00	361.00	0.00	28.93	106
10	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	03/2018	217.61	309.56	0.00	42.25	95
11	MAIBANG TO LUMDING (AS-24), KM.111.000 TO	NHAI	12/2003	11/2008	03/2018	155.04	280.13	0.00	80.68	112
12	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	12/2017	196.00	331.23	0.00	68.99	101
13	MAIBANG TO LUMDING (AS-25), KM.83.400 TO	NHAI	12/2003	04/2009	12/2017	199.81	385.13	0.00	92.75	104
14	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	04/2018	4375.35	8150.00	6860.00	86.27	79
15	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	256.41	147.19	12.15	15

[illegible]

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
29	PARBATI HEP (4X200 MW) (NHPC)	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	6597.22	114.28	111
	JAMMU & KASHMIR									
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	02/2018	3642.04	5882.01	5186.86	61.50	25
31	UDHAMPUR-SRINAGAR-	NR	03/1995	11/2002	12/2018	2500.00	27946.00	16131.46	1017.84	193
32	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	1213.54	30.49	12
	JHARKHAND									
33	MANDARHILL-DUMKA-	ER	04/1995	12/2011	03/2020	900.05	1125.89	980.99	25.09	99
34	GOELKERA-MANOHARPUR,(LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	343.71	48.26	166
	KERALA									
35	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	276.85	17.66	17
	MADHYA PRADESH									
36	NIGAH I OC EXPANSION PROJECT 10 MTY	NCL	10/2007	03/2012	03/2018	259.40	486.57	397.54	87.58	72
37	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	1030.00	1020.64	49.88	96
	MAHARASHTRA									
38	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	03/2018	241.33	349.33	269.50	44.75	24
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	678.01	259.68	192
40	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2423.55	50.68	60
41	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON PORT	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	411.12	82.72	96
42	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	5554.21	1.87	12
43	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPU)	ONGC	03/2011	05/2013	03/2018	861.79	1256.72	1183.39	45.83	58

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
44	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	1671.57	29.42	36
45	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	06/2018	477.69	738.48	653.52	54.59	93
46	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR	RCF	02/2016	12/2017	02/2018	482.85	494.00	413.01	2.31	2
47	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	209.44	103.35	5.89	29
MANIPUR										
48	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	6985.58	1227.45	108
MIZORAM										
49	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	1825.65	642.73	71
MULTI STATE										
50	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	06/2019	13334.00	24664.00	6660.00	84.97	47
51	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	723.40	422.29	133.50	41
52	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2289.00	122.78	75
53	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANGAL	NCR	04/2010	02/2019	12/2022	622.41	2030.50	10.34	226.23	46
54	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	1.92	226.98	34
55	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2748.23	314.73	123
56	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHURAN	OIL	07/2011	03/2017	11/2018	352.56	438.84	134.50	24.47	20

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
57	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	5637.00	4050.69	36.68	23
58	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2018	522.29	550.18	374.70	5.34	16
59	EASTERN REGION STRENGTHENING SCHEME -IX	PGCIL	02/2014	02/2016	03/2018	196.58	225.28	134.45	14.60	25
60	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION PART B	PGCIL	03/2014	03/2016	03/2018	155.57	206.42	140.76	32.69	24
61	SYSTEM STRENGTHENING IN SOUTHERN REGION XXIII	PGCIL	01/2015	07/2017	12/2018	203.28	260.03	168.86	27.92	17
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	12/2017	908.08	969.97	732.28	6.82	18
63	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA	PGCIL	01/2015	03/2018	06/2018	268.80	340.88	169.37	26.82	3
64	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	03/2018	288.49	376.09	231.75	30.37	13
65	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	01/2018	232.34	341.00	246.39	46.77	67
66	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2018	297.33	426.29	364.29	43.37	43
67	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2018	487.49	639.46	485.99	31.17	51
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	03/2018	723.63	882.13	727.62	21.90	40
69	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA AND PART C	PGCIL	03/2013	06/2015	05/2018	514.20	703.10	585.89	36.74	35
70	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER	PGCIL	10/2008	10/2012	06/2018	4824.12	5071.94	4489.03	5.14	68

[illegible]

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
84	SEVOK RANGPO,	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	383.92	204.95	51
	TAMIL NADU									
85	PROTOTYPE FAST BREEDER REACTOR (BHAVINI,	BHAVNI	09/2003	09/2010	06/2018	3492.00	6100.00	5532.63	74.68	93
86	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600.00	19058.00	14784.59	30.53	24
87	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	12/2017	687.28	767.00	733.23	11.60	6
88	KUNADANKULAM APP TRANS	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	1969.63	22.93	118
89	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED	PGCIL	09/2011	09/2014	03/2018	1940.13	2702.65	2357.64	39.30	42
90	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	12/2017	150.00	600.00	139.80	300.00	141
	TELANGANA									
91	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II	RVNL	04/2012	03/2016	12/2018	632.68	816.55	491.31	29.06	33
92	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	489.62	477.74	16.86	132
93	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	1.31	114.60	60
94	SHANTIKHANI LONGWALL PROJ-	SCCL	10/2006	03/2012	03/2019	249.03	448.86	163.85	80.24	84
	TRIPURA									
95	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY	HSCL	12/2007	12/2016	12/2017	202.61	227.00	199.95	12.04	12
96	AGARTALA SABROOM, NL,	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2407.41	324.30	72
	UTTAR PRADESH									
97	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	294.60	148.06	50.75	61
	UTTARAKHAND									
98	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF	CPWD	12/2008	12/2013	10/2019	114.26	266.00	0.00	132.80	70
99	TAPOVAN-VISHNUGAD HEP	NTPC	11/2006	03/2013	03/2020	2978.48	3846.30	3359.00	29.14	84

SN	PROJECT	IMPLIMENTING AGENCY	DATE OF APPROVAL (month/year)	ORIGINAL DATE OF COMMISSIONING (month/year)	ANTICIPATED DATE OF COMMISSIONING (month/year)	COST ORIGINAL (Rs. In crore)	COST ANTICIPATED (Rs. In crore)	REPORTED CUMULATIVE EXPENDITURE (Rs. In crore)	COST OVERRUN (Rs. In crore)	TIME OVERRUN (MONTHS)
100	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	3939.11	2443.93	137.73	58
WEST BENGAL										
101	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.90	191.38	110.00	13.31	10
102	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	2248.49	36.22	9
103	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2018	4404.57	5135.01	3488.99	16.58	38
104	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJABHAT (MTD)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	1541.16	7.78	57
