


केन्द्रीय क्षेत्र की परियोजनाओं
CENTRAL SECTOR PROJECTS
₹150 करोड़ और अधिक लागत वाली
(₹ 150 Crore and above)
364वीं फ्लैश रिपोर्ट / 364th Flash Report
फरवरी, 2016 / February, 2016

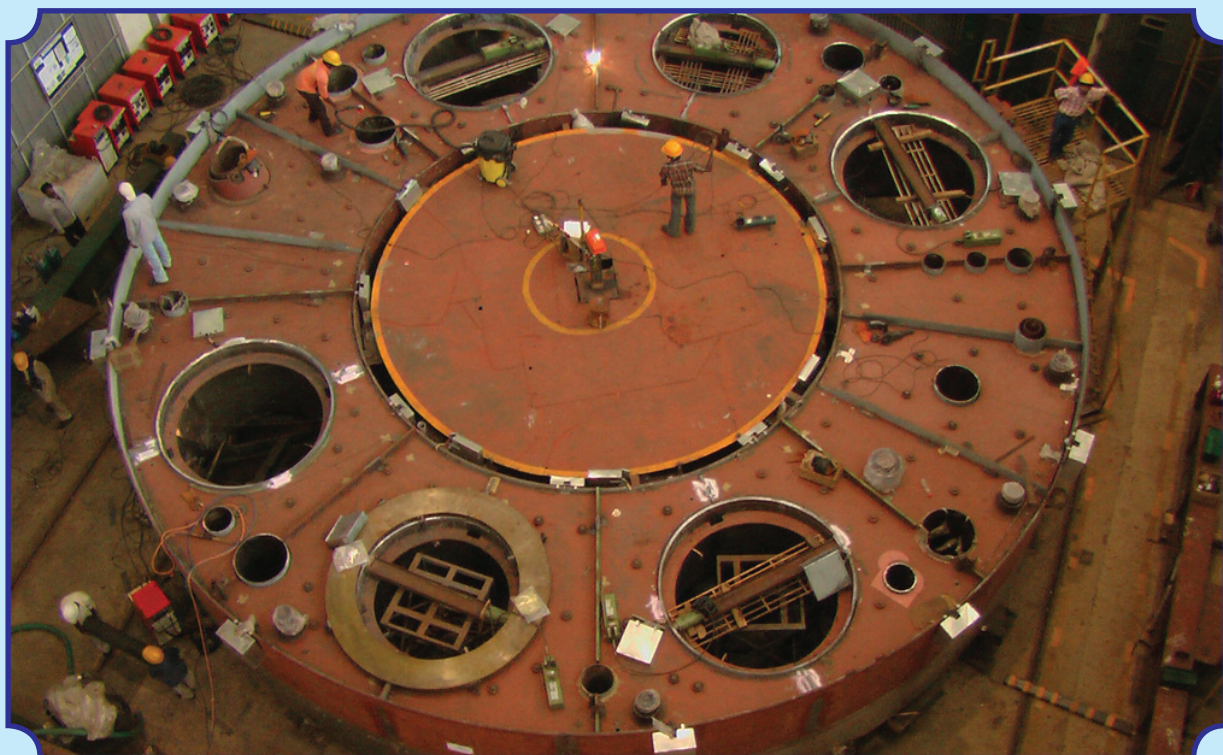

भारत सरकार / Government of India
सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय
Ministry of Statistics and Programme Implementation
आधारी संरचना और परियोजना प्रबोधन प्रभाग
Infrastructure and Project Monitoring Division
सरदार पटेल भवन, संसद मार्ग
Sardar Patel Bhavan, Sansad Marg,
नई दिल्ली / New Delhi-110001
वेबसाइट / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-22
Executive Summary English	23-41
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-2016	42-46
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2015-2016	47-48
Summary of projects	49-63
Graphical Presentation of All Projects	64-76
Sector wise Analysis of Projects	77-130
Sector wise Graph	131-143
Annexures	144-144
Status of central sector projects costing Rs.150 Crore and above	145-145
List of projects in which expenditure is more than approved cost	146-155
Details of Projects Ahead of Schedule w.r.t. Original Schedule	156-156
Details of On Schedule Projects w.r.t. Original Schedule	157-169
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	170-181
Details of Delayed Projects w.r.t. Original and Revised Schedule	182-213
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	214-218
Details of Projects Without Date of Commissioning	215-238
Details of projects without original Date of Commissioning	239-240
Details of projects without Milestones w.r.t. original schedule	241-274
List of Projects Ahead of Schedule w.r.t. Latest Schedule	275-275
List of Projects on schedule w.r.t. Latest Schedule	276-291
List of ongoing projects having cost overrun w.r.t. to revised schedule	290-301
List of Delayed Projects w.r.t. Latest Schedule	302-317
Details of Central Sector Projects Showing Time overruns of 6 Months and More	318-332
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	333-341
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More and cost overruns of Rs. 100 Crore and above	342-362
Details of 20 Railways Projects	363-348

कार्यकारी सारांश

1. फरवरी, 2016 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1071 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। फरवरी 2016 के दौरान, 2 परियोजनाओं (कोयला तथा पेट्रोलियम क्षेत्र में प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 1071 परियोजनाओं में से, 341 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 38 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 38 परियोजनाओं में से, 11 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	411	130	4	0
2.	रेलवे	298	32	0	0
3.	विद्युत	111	60	12	6
4.	कोयला	88	43	3	1
5.	पेट्रोलियम	66	36	10	3
6.	इस्पात	34	15	5	1
7.	शहरी विकास	30	11	2	0
8.	स्वास्थ्य और परिवार कल्याण	9	4	2	0
9.	पोत परिवहन एवं पत्तन	8	2	0	0
10.	नागर विमानन	4	1	0	0
11.	परमाणु ऊर्जा	4	4	0	0
12.	खान	3	0	0	0
13.	दूरसंचार	2	2	0	0
14.	उर्वरक	1	0	0	0
15.	पेट्रोरसायन	1	0	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1071	341	38	11

3. 1071 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 12,66,248.36 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 14,26,985.93 करोड़ होने की संभावना है, जो ₹ 1,60,737.57 करोड़ (मूल लागत का 12.69%) की समग्र लागत वृद्धि को दर्शाता है। फरवरी, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,66,058.05 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 39.67% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(29.02.2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	लागत वृद्धि (%)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी, 500 मेगावाट)	09/2003	3492.00	5677.00	62.57
नागर विमानन					
1	56 विभिन्न हवाई अड्डों पर ओपन स्कूल एयरफील्ड दमकल की आपूर्ति	10/2012	217.60	244.10	12.18
कोयला					
1	अद्वियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	निगही ओसी विस्तार परियोजना के लिए 15 10 एमटीवाई को एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
3	रामागुंडम ओसी-द्वितीय विस्तार	12/2009	418.97	489.62	16.86
4	मनुगुरु ओसी परियोजना की आरएफआर	11/2012	430.45	486.27	12.97
उर्वरक					
1	नया सीवेज उपचार संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	209.44	5.89
भारी उद्योग					
1	राष्ट्रीय ऑटोमोटिव परीक्षण और सड़क बुनियादी ढांचा परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
पेट्रोलियम					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	82.49
पेट्रोलियम					
1	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
2	मंगलौर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	732.00	1227.00	67.62

3	कोरबा में विपणन टोप	01/2011	141.86	232.00	63.54
4	उरन चाकन / शिकरपूर एलपीजी पाइपलाइन	12/2009	309.81	462.79	49.38
5	मोबाइल ऑफशोर उत्पादन इकाई के लिए रिग सागर सम्राट के रूपांतरण (एमओपीएस)	03/2011	861.79	1256.72	45.83
विद्युत					
1	तुरियल जल विद्युत परियोजना (60 मेगावाट)	07/1998	368.72	1381.71	274.73
2	सुबानसिरी लोअर एचईपी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	18063.89	187.40
3	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	147.51
4	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.57	139.32
5	रघुनाथपुर थर्मल पावर स्टेशन चरण-	04/2007	4122.00	9606.82	133.06
रेलवे					
1	एकलाखी-बालुरघाट सहित गाजोल-इटहर से नई बीजी रेलवे लाइन (एनएल) एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुड़ा - दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	ललितपुर-सतना-रीवा-सिंगरौली नाथन, (एनसीआर)	09/1998	247.66	3500.00	1313.23
4	अकोला-खंडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
5	बंगलौर - सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन (96 किमी/387.1 किलोमीटर)	05/2009	1108.00	2288.00	106.50
2	अरुणाचल प्रदेश पैकेज के तहत अरुणाचल प्रदेश में युपिआ-एचओजे सेक्शन के दो लाइनिंग (20.40 किमी)	12/2009	104.00	201.00	93.27
3	मैबंग से लुमडिंग (एएस 25), 83.400किमी से 111.000किमी	12/2003	199.81	385.13	92.75
4	मैबंग से लुमडिंग (एएस 24), 111.000किमी से 126.450किमी	12/2003	155.04	280.13	80.68
5	अरुणाचल प्रदेश के तहत अरुणाचल प्रदेश में खोंसा -तिस्सा -लौंगडिंग (एनएच 52ख) (42.50 किलोमीटर) - के दो लेनिंग	12/2011	156.63	276.00	76.21
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ /ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00

2	मुंबई में बीओटी आधार पर ऑफशोर कंटेनर बर्थ के निर्माण और कंटेनर टर्मिनल के विकास	01/2007	366.39	669.46	82.72
3	कोचीन पोर्ट ट्रस्ट में वल्लारपादम के आईसीटीटी के लिए रेल कनक्टिविटी	03/2007	245.67	409.83	66.82
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	5.66
इस्पात					
1	सिंटर मशीन - 1 और 2 के सुधार	12/2009	343.00	488.40	42.39
2	गुलबर्गा में मेडिकल कॉलेज और अस्पताल के निर्माण	05/2005	768.88	1070.97	39.29
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत ग्रामीण सड़क के निर्माण और रखरखाव	10/2011	175.49	206.71	17.79
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़क के निर्माण और रखरखाव	03/2007	149.73	175.94	17.50
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़क के निर्माण और रखरखाव	12/2007	202.61	227.00	12.04
शहरी विकास					
1	बैंगलुरु मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53
2	बिहटा के आईआईटी पटना के लिए आवासीय परिसर और अन्य परिसरों	02/2012	171.10	202.00	18.06

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार हैं:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(29.02.2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	सीओआर (रु.करोड़ में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी, 500 मेगावाट)	09/2003	3492.00	5677.00	2185.00
नागर विमानन					
1	56 विभिन्न हवाई अड्डों पर ओपन स्कूल एयरफील्ड दमकल की आपूर्ति	10/2012	217.60	244.10	26.50
कोयला					
1	अद्वियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगही ओसी विस्तार परियोजना के लिए 15 10 एमटीवाई को एमटीवाई , सिंगरौली	10/2007	259.40	486.57	227.17
4	रामागुंडम ओसी-द्वितीय विस्तार	12/2009	418.97	489.62	70.65
5	मनुगुरु ओसी परियोजना की आरएफआर	11/2012	430.45	486.27	55.82
उर्वरक					
1	नया सीवेज उपचार संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	209.44	11.65
भारी उद्योग					
1	राष्ट्रीय ऑटोमोटिव परीक्षण और सड़क बुनियादी ढांचा परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	9965.00	4504.39
पेट्रोलियम					
1	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
2	एकीकृत रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
3	पादुर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	993.00	1693.00	700.00
4	बी-127 क्षेत्रों के समन्वित विकास	12/2011	2059.63	2665.65	606.02
5	मंगलौर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	732.00	1227.00	495.00
विद्युत					

1	सुबानसिरी लोअर एचईपी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	18063.89	11778.56
2	बाढ़ एसटीपीपी (3X660एमडब्ल्यू), एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन चरण-I	04/2007	4122.00	9606.82	5484.82
4	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) द्वितीय	09/2002	3919.59	8398.76	4479.17
5	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6179.96	3683.06
रेलवे					
1	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	20000.00	17500.00
2	जिरीबाम से इंफाल (तुपुई) (एनएल) (एनईएफआर)	04/2003	727.56	6570.75	5843.19
3	लुमडिंग-सिलचर जिरीबाम, बदरपुर-बरइग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
4	बोगिबिल और लिंक लाइनों पर ब्रह्मपुत्र पुल एनईएफआर	09/1997	1500.00	4996.19	3496.19
5	ललितपुर-सतना-रीवा-सिंगरुली एनएल , (एनसीआर)	09/1998	247.66	3500.00	3252.34
सड़क परिवहन एवं राजमार्ग					
1	पानीपत-जालंधर 6 लेन (96किमी से 387.1 किलोमीटर)	05/2009	1108.00	2288.00	1180.00
2	मैबंग से लुमडिंग (एस 25), 83.400 किमी से 111.000किमी	12/2003	199.81	385.13	185.32
3	हरगंजो से मैबंग , एनएच 54	12/2003	196.00	331.23	135.23
4	मैबंग से लुमडिंग (एस 24), 111.000 किमी से 126.450 किमी	12/2003	155.04	280.13	125.09
5	एलडब्ल्यू के तहत राष्ट्रीय राजमार्ग -202 पर अप्रोच रोड सहित वैकटपुरम के पास गोदावरी नदी पुल के निर्माण	03/2011	218.31	339.82	121.51
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ / ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में बीओटी आधार पर ऑफशोर कंटेनर बर्थ के निर्माण और कंटेनर टर्मिनल के विकास	01/2007	366.39	669.46	303.07

3	कोचीन पोर्ट ट्रस्ट में वल्लारपादम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	409.83	164.16
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	13.83
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल के निर्माण	05/2005	768.88	1070.97	302.09
2	सिंटर मशीन - 1 और 2 के सुधार	12/2009	343.00	488.40	145.40
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VII के तहत ग्रामीण सड़क के निर्माण और रखरखाव	10/2011	175.49	206.71	31.22
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़क के निर्माण और रखरखाव	03/2007	149.73	175.94	26.21
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़क के निर्माण और रखरखाव	12/2007	202.61	227.00	24.39
शहरी विकास					
1	बैंगलुरु मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00
2	बिहार में आईआईटी पटना के परिसर के लिए आवासीय और अन्य परिसरों	02/2012	171.10	202.00	30.90

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1071 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 258 समय पर तथा 341 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 305 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 34 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 433 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 341 विलंबित परियोजनाओं में से, 65 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 66 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 138 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 72 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(29.02.2016 की स्थिति के अनुसार)**

क्र. सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	05/2016	89
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी, 500 मेगावाट)	09/2003	09/2010	09/2016	72
3	राजस्थान परमाणु विद्युत परियोजना -7 और 8 (2X700 मेगावाट)	10/2009	12/2016	12/2019	36
4	काकरापार परमाणु बिजली परियोजना - 3 और 4	10/2009	12/2015	11/2018	35
नागर विमानन					
1	पकयोंग हवाई अड्डे में नए हवाई अड्डे के निर्माण (सिक्किम)	01/2009	01/2011	09/2017	80
कोयला					
1	रामागुंडम ओसी -II विस्तार	12/2009	03/2012	03/2023	132
2	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	07/2012	03/2021	104
3	कुलड़ा ओसीपी (महानदी कोलफील्ड्स लिमिटेड)	01/2005	03/2010	03/2017	84
4	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
5	अशोक ईएसपीएन ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
स्वास्थ्य और परिवार कल्याण					
1	एम्स रायबरेली आवास	10/2013	11/2013	06/2016	31
2	एलजीबीआरआईएमएच -तेजपुर, असम	07/2012	12/2014	03/2016	15
3	सफदरजंग अस्पताल पुनर्विकास और अन्य सुपर स्पेशलिटी ब्लॉक	09/2013	12/2015	03/2016	3
4	सफदरजंग अस्पताल, नई दिल्ली-पुनर्विकास और अन्य आपातकालीन ब्लॉक	11/2013	01/2016	04/2016	3
भारी उद्योग					
1	राष्ट्रीय ऑटोमोटिव परीक्षण और सड़क बुनियादी ढांचा परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
पेट्रोलियम					
1	कोच्चि-बेंगलूर कूटनाड मंगलौर पाइपलाइन परियोजना	06/2009	12/2012	02/2019	74
2	फूलपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	12/2018	71
3	12 अपतटीय आपूर्ति पोत का निर्माण (ओएसवी)	06/2007	09/2011	10/2016	61

4	वीकेपीएल उन्नयन और स्पेरलाइन बिछाने (भीलवाड़ा और चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
5	मंगलौर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	10/2011	03/2016	53
विद्युत					
1	तुरियल हाइड्रो इलेक्ट्रिक प्रोजेक्ट (60एमडब्ल्यू)	07/1998	07/2006	10/2016	123
2	पार्वती एचईपी (4X200 मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
3	कुडनकुलम एपीपी पारेषण प्रणाली (पीजीसीआईएल)	05/2005	11/2008	12/2016	97
4	बाढ़ एसटीपीपी (3X660 एमडब्ल्यू), एनटीपीसी	02/2005	01/2011	05/2018	88
5	तीस्ता लो डैम एचईपी, चरण IV (4X40 मेगावाट) (एनएचपीसी)	09/2005	09/2009	09/2016	84
रेलवे					
1	गोंदिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	11/2002	12/2017	181
3	बांकुड़ा - दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	06/2005	12/2019	174
5	बेलापुर-सीवुड -उरान विद्युतीकृत डबल लाइन (एमटीपी)	03/1996	03/2004	03/2016	144
सड़क परिवहन एवं राजमार्ग					
1	बिजनी से असम / पश्चिम बंगाल सीमा चरण. II, 0.00 से 30.00किमी , एनएच 31ग	12/2003	06/2005	12/2016	138
2	हरगंजो से मैबंग , एनएच 54, 164.08-190.587किमी एनएच 54	12/2003	09/2007	12/2016	111
3	नलबाड़ी से बिजनी (एस-7)	12/2003	04/2008	01/2017	105
4	आगरा-बाईपास (एन एस -1 / उ प्र-1), एनएच 2,3	12/2003	09/2007	03/2016	102
5	सोनापुर गुवाहाटी (एस -3)	12/2003	03/2008	07/2016	100
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ /ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	03/2006	03/2016	120
2	कोचीन पोर्ट ट्रस्ट में वल्लारपादम में आईसीटीटी के लिए रेल संपर्क	03/2007	04/2009	08/2016	88
3	मुंबई में बीओटी आधार पर ऑफशोर कंटेनर बर्थ के निर्माण और कंटेनर टर्मिनल के विकास	01/2007	12/2010	01/2016	61
इस्पात					
1	भिलाई इस्पात संयंत्र के विस्तार	08/2010	03/2013	11/2016	44
2	अन्य संबद्ध सुविधाओं के साथ 45 एमवीए सैफ टी की स्थापना	12/2011	10/2013	06/2016	32
3	गुलबर्गा में मेडिकल कॉलेज और अस्पताल के निर्माण	05/2005	02/2014	03/2016	25
4	एसएमएस -1 कन्वर्टर्स के सुधार	05/2012	07/2015	06/2017	23

5	रावघाट डेपोसिट पर 21 स्थानों पर स्थायी बैरकों का विकास	04/2014	04/2015	12/2016	20
दूरसंचार					
1	इनटेलीजेंट फाइबर ऑप्टिक सी के एक भाग के पैकेज एफ और जी, ओएफसी लाईग परियोजना के लिए स्पेक्ट्रम (एनएफएस) नेटवर्क	09/2014	09/2014	03/2017	30
2	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	03/2017	20
शहरी विकास					
1	नागपुर महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज के उन्नयन	06/2010	03/2012	03/2017	60
2	आईआईएसईआर कोलकाता के लिए पश्चिम बंगाल हरींघंटा कल्याणी में आवासीय सह शैक्षिक परिसर	01/2009	06/2012	05/2016	47
3	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	06/2016	37
4	भोपाल पुलिस ट्रेनिंग (सीएपीटी) के लिए केंद्रीय अकादमी के निर्माण	12/2012	12/2014	03/2017	27
5	आईआईएसईआर कोलकाता के लिए हरींघंटा कल्याणी नादिया में स्थायी आवासीय परिसर	02/2014	09/2015	04/2017	19

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 758 परियोजनाओं में से, 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि फरवरी 2016 के दौरान, 1071 परियोजनाओं में से, 238 परियोजनाओं के संबंध में लागतवृद्धि तथा 341 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है। अप्रैल 2015 की तुलना में, लागतवृद्धि दर्शाने वाले परियोजनाओं की संख्या 30.47% से घटकर 22.22% हो गई, जबकि समयवृद्धि दर्शाने वाले परियोजनाओं के संबंध में 42.61% से घटकर 31.84% हो गई है।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची

प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (29.02.2016 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पकयोंग में नए हवाई अड्डे के निर्माण (सिक्किम)	01/2009	309.46	309.46	412.95	01/2011	09/2017
2	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	318.00	305.01	05/2012	03/2015
3	विभिन्न हवाई अड्डों पर 56 एयरफील्ड फ़ाइर निविदाओं की आपूर्ति	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	वीएसआई हवाई अड्डों में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	21.76	एन.ए.	09/2018
कोयला							
1	मदन नगर ओसीपी	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
उर्वरक							
1	नया सीवेज उपचार संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	209.44	49.27	11/2016	11/2016
स्वास्थ्य और परिवार कल्याण							
1	एलजीबीआरआईएमए च	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	एलएचएमसी - अस्पताल	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	सफदरजंग एसएसबी	09/2013	444.70	444.70	268.07	12/2015	03/2016
4	रायबरेली-आवास	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	सफदरजंग अस्पताल, नई	11/2013	196.70	196.70	157.61	01/2016	01/2016

	दिल्ली-पुनर्विकास और अन्य आपातकालीन ब्लॉक						
	भारी उद्योग						
1	राष्ट्रीय ऑटोमोटिव परीक्षण और आरडी बुनियादी ढांचा परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
	खान						
1	भूमिगत खदान के मलाजखंड खान- विकास के विस्तार	09/2011	1856.00	1176.00	4.59	09/2017	04/2020
2	डब्ल्यूपीपीएमएच	12/2015	355.13	355.13	0.00	11/2016	11/2016
3	डब्ल्यूपीपीआरजे	12/2015	344.50	344.50	0.00	11/2016	11/2016
	पेट्रोलियम						
1	मंगलौर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	732.00	1227.00	1074.73	10/2011	03/2016
2	पादुर में सामरिक कच्चे तेल संग्रहण परियोजना	01/2006	993.00	1693.00	1447.43	01/2012	05/2016
3	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
4	12 अपतटीय आपूर्ति पोत का निर्माण (ओएसवी)	06/2007	736.65	736.65	499.19	09/2011	10/2016
5	बीस फीडर गैस लाइनों	03/2009	228.64	214.19	140.71	12/2016	12/2016
	विद्युत						
1	सुबानसिरी लोअर एचईपी (8X250 मेगावाट) (एनटीपीसी)	09/2003	6285.33	18063.89	7969.14	09/2010	एन.ए.
2	बीटीपीएस-ए	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	आरटीपीएस पीएच-1	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	उत्तरी में फाइबर ऑप्टिक संचार प्रणाली की स्थापना	03/2012	198.63	198.63	94.63	09/2014	06/2016
5	यूआरटीडीएसएम पहले चरण -I	01/2014	374.63	374.63	16.20	04/2016	11/2016
	रेलवे						

1	हावड़ा-आमता – चंपदंगा एनएल (एसईआर)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	नांगल बांध-तलवाड़ा (एनएल), एन.आर.	03/1981	450.00	2100.00	391.95	07/2012	एन.ए.
3	इकलाखी -बालुरघाट जी सहित नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	255.55	एन.ए.	03/2019
4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	गुना-इटावा वाया शिवपुरी-ग्वालियर - भिंड एनएल , (एनसीआर)	04/1986	158.77	608.02	602.10	03/1994	03/2015
सड़क परिवहन एवं राजमार्ग							
1	"मधुगिरी-मुल्बगल (400.330 किलोमीटर 483.151 किमी) एलओटी।।	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	अनीसाबाद- औरंगाबाद-हरिहरगंज (0.000 किलोमीटर 62.000 किमी) - एलओटी	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	अनीसाबाद- औरंगाबाद-हरिहरगंज (62.000 किमी से 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	बख्तियारपुर - मोकामा	01/1991	1167.45	1167.45	0.00	एन.ए.	एन.ए.
5	बंकूरा - पुरलिया (0.000 किमी से 84.000 किलोमीटर)	01/1991	322.00	322.00	0.00	03/2018	03/2018
पोत परिवहन एवं पत्तन							
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ / ओ स्पेशल पर्पज व्हीकल	10/2002	150.00	600.00	139.80	03/2006	03/2016
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	2427.40	2427.40	841.02	10/2008	एन.ए.

3	अपतटीय कंटेनर बर्थ के निर्माण और विकास	01/2007	366.39	669.46	415.80	12/2010	01/2016
4	कोचीन पोर्ट ट्रस्ट में वल्लारपादम में आईसीटी के लिए रेल संपर्क	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	रोरो-II	09/2015	210.00	210.00	0.00	01/2018	01/2018
इस्पात							
1	गुलबर्गा में मेडिकल कॉलेज एवं अस्पताल का निर्माण	05/2005	768.88	1060.00	1070.97	02/2014	03/2016
2	बैगमती का सिंचाई कार्य	10/2005	956.00	956.00	648.16	03/2015	03/2017
3	ग्रामीण सड़क के अंतर्गत निर्माण और प्रबंधन	03/2007	149.73	173.00	175.94	12/2015	03/2017
4	प्रधानमंत्री ग्राम सड़क योजना चरण-के तहत ग्रामीण सड़क के निर्माण और रखरखाव	12/2007	202.61	227.00	195.51	12/2016	12/2016
5	गिरीडीह में सड़क और पुल का निर्माण, कोडरमा	12/2007	200.00	200.00	126.15	03/2018	03/2018
दूरसंचार							
1	स्पेक्ट्रम के लिए नेटवर्क	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
शहरी विकास							
1	सैन्य एम में शादी आवास के निर्माण	08/2005	191.24	191.24	0.00	08/2007	एन.ए.
2	सीवरेज परियोजना	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
3	संसद भवन एनेक्सी के लिए भवन विस्तार कार्य	05/2009	261.85	261.85	168.00	05/2013	06/2016
4	एनआईटी कालिकट केरल के लिए मेगा	01/2010	165.23	165.23	0.00	10/2012	एन.ए.

	छात्रावास का निर्माण						
5	आईआईटी हौज खास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	162.90	162.90	160.00	07/2012	12/2015

एन.ए. : उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरुआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (29.02.2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	21077.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी, 500 मेगावाट)	09/2003	3492.00	0.00	5150.14
	नागर विमानन				
1	पकयोंग में नए हवाई अड्डे के निर्माण	01/2009	309.46	0.00	412.95
	कोयला				
1	अनंत ओसी विस्तार पीएच-III (15.0 एमटीवाई)	08/2008	207.28	0.00	207.70
2	रामागुंडम ओसी-II विस्तार	12/2009	418.97	0.00	453.18
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	8920.00	9175.15
	पेट्रोलियम				
1	कोरबा में विपणन शीर्ष	01/2011	141.86	0.00	164.35
	विद्युत				
1	पार्वती एचईपी -II (4X200 मेगावाट) (एनएचपीसी)	09/2002	3919.59	0.00	5398.46
2	सुबानसिरी लोअर एचईपी (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7969.14

3	तीस्ता लो डैम एचईपी, स्टेज IV (4X40 मेगावाट) (एनएचपीसी)	09/2005	1061.38	0.00	1956.52
4	किशनगंगा जलविद्युत परियोजना (3X110 मेगावाट)	01/2009	3642.04	0.00	4402.95
5	उत्तर क्षेत्र प्रणाली सुदृढीकरण-VII	02/2009	509.66	0.00	528.56
रेलवे					
1	गाजोल इटहर सहित एकलाखी बालुरघाट से नई रेलवे बीजी लाइन	04/1983	36.80	36.38	255.55
2	वीरमगाम-भीलड़ी (डब्ल्यू आर), जीसी	04/1990	155.66	0.00	201.26
3	पेद्दापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	12/1994	124.43	0.00	712.02
4	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	0.00	10722.72
5	कटक - बारंग (एलडी)	04/1995	127.13	0.00	193.37
सड़क परिवहन एवं राजमार्ग					
1	हरगंजो से मैबंग ,(एस 23), 126.450किमी 140.700 किमी	12/2003	280.00	0.00	392.60
2	सोनापुर के धरमतूल 205-183किमी (एस 20)	12/2003	160.00	0.00	197.40
3	गुवाहाटी नलबाड़ी (एस 5)	12/2003	198.16	0.00	242.40
4	नलबाड़ी से बिजनी (एस-7)	12/2003	208.00	230.00	295.20
5	बिजनी से असम पश्चिम बंगाल सीमा (एनएच 31.सी) (1) बिजनी (एनएचएआई)	12/2003	195.00	0.00	278.96
पोत परिवहन एवं पत्तन					
1	मुंबई में बीओटी आधार पर ऑफशोर कंटेनर बर्थ के निर्माण और कंटेनर टर्मिनल के विकास	01/2007	366.39	0.00	415.80
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल के निर्माण	05/2005	768.88	1060.00	1070.97
2	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़क के निर्माण और रखरखाव	03/2007	149.73	173.00	175.94
शहरी विकास					
1	बेंगलुरु मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	13525.81

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (29.02.2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर 56 एयरफील्ड फ़ाइर निविदाओं की आपूर्ति	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	झल्लाराम शाफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
स्वास्थ्य और परिवार कल्याण					
1	एलएचएमसी नई दिल्ली-पुनर्विकास	02/2013	11/2013	एन.ए.	11/2014
पेट्रोलियम					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2013	12/2015
पेट्रोलियम					
1	एन्नोर में नई मार्केटिंग टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
2	कोची-कूटनद-बंगलौर-मंगलौर पाइपलाइन परियोजना	06/2009	12/2012	एन.ए.	06/2015
3	एक ईटीपी और तीन ईटीपी सह वाटर इंजेक्शन संयंत्रों का निर्माण (डब्ल्यूआईपी)	06/2010	01/2014	एन.ए.	एन.ए.
4	टाटा नगर और राची डिपो से खूटी का रिसाइटमेंट (झारखंड)	04/2011	05/2015	एन.ए.	एन.ए.
5	एन्नोर-त्रिची मद्रुरै एलपीजी पाइपलाइन	05/2013	एन.ए.	एन.ए.	एन.ए.
विद्युत					
1	सुबानसिरी लोअर एचईपी (8X250 मेगावाट) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	एसआर का प्रणाली सुदृढीकरण XII	02/2010	06/2012	एन.ए.	एन.ए.

3	आंध्र प्रदेश भाग-क1 की वेमगिरि क्षेत्र में आईएसजीएस परियोजनाओं से संबंधित सामान्य प्रणाली	03/2012	06/2014	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा-अमटा-चम्पादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	03/2015
2	नांगल बांध-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर -भिंड एनएल , (एनसीआर)	04/1986	03/1994	एन.ए.	03/2015
4	नामखाना-चंद्रनगर, काकद्वीप-बुदाखली और चंद्र नाग के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	वीरमगाम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	एन.ए.	03/2010	एन.ए.
सड़क परिवहन एवं राजमार्ग					
1	एनएच 66 के टिंडीवनम अनुभाग के लिए पांडिचेरी	01/1991	01/2008	एन.ए.	एन.ए.
2	पुनर्वास और 2 लाइन्स -2 पेल्ड शोल्डर विन्यास और मजबूत बनाने ओ के साथ लेन करने के लिए उन्नयन	01/1991	04/2014	एन.ए.	एन.ए.
3	पेल्ड शोल्डर के साथ 2 लेन का उन्नयन तथा पुनर्विकास, बिरपुर-बिहपुर के विन्यास तथा सुदृढीकरण,	01/1991	एन.ए.	एन.ए.	एन.ए.
4	ईपीसी आधार पर एनएच 37 की नगांव बाईपास की सीमा से रांगगारा तक 4 लेनिंग (278.60 किमी से 297.00 किमी.)	01/1991	एन.ए.	एन.ए.	एन.ए.

5	4 लेन का किलोमीटर एनएच 52 के 264.10 किमी से राष्ट्रीय राजमार्ग 52क के 20.37 किमी तक गोहपुर से होलौंगी तक 4 लाइनिंग	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
इस्पात					
1	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खदान परियोजना (एनएमडीसी)	02/2011	05/2013	01/2015	08/2015
2	1.2 एमटीपीए पेलेट संयंत्र परियोजना, डोनिमलई (एनएमडीसी)	04/2011	04/2013	09/2014	06/2015
3	नेशनल इंस्टिट्यूट ऑफ फार्मास्यूटिकल एजुकेशन एंड रिसर्च के लिए परिसर और भवन का निर्माण	01/2013	एन.ए.	एन.ए.	एन.ए.
4	राजीव गांधी के अंतर्गत इनडोर खेल हॉल के लिए तेलंगाना में 123 ब्लॉकों तथा आंध्र प्रदेश में 167 ब्लॉकों का निर्माण	07/2014	01/1999	एन.ए.	एन.ए.
शहरी विकास					
1	रक्षा मंत्रालय में सैन्य स्टेशन मामुन पंजाब में विवाहित आवासीय के निर्माण	08/2005	08/2007	एन.ए.	एन.ए.
2	मूसी के दक्षिण पर पुरानी शहरी क्षेत्र में सीवरेज प्रणाली को मजबूत बनाना तथा पुनर्वास (2 जोन में)	08/2007	एन.ए.	एन.ए.	एन.ए.
3	आईआईटी हौज खास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	12/2015	12/2015
4	एनआईटी कालीकट केरल	01/2010	10/2012	एन.ए.	एन.ए.

	के लिए मेगा छात्रावास द्वितीय का निर्माण				
5	नागपुर महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज के उन्नयन	06/2010	03/2012	एन.ए.	एन.ए.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

i) **विद्युत क्षेत्र में,** 111 परियोजनाओं में से, 60 परियोजनाएं विलंबित हैं । माह के दौरान 12 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 12 परियोजनाओं में से, 6 परियोजनाएं मेगा परियोजनाएं हैं । दो परियोजनाएं 'कमेग जलविद्युत परियोजना ,नीपको ' तथा उत्तर क्षेत्रीय प्रणाली सुदृढीकरण योजना -XIX, पीजीसीआईएल' के संबंध में क्रमशः आकस्मिक बाढ़ तथा डैम पैरामीटरों के रिडिजाइनिंग के कारण प्रत्ये 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएं 'उत्तरी क्षेत्रीय पारेषण सुदृढीकरण योजना,पीजीसीआईएल' तथा 'उत्तरी क्षेत्र की पारेषण प्रणाली सुदृढीकरण योजना-XXI, पीजीसीआईएल', के संबंध में क्रमशः कृषक आंदोलन तथा आरओडब्ल्यू समस्याओं के कारण 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'सासन तथा मुंदरा के लिए एनआर में प्रणाली सुदृढीकरण (यूएमपीपी) ,पीजीसीआईएल' तथा झारखंड तथा पश्चिम बंगाल भाग क 1 में जेनेरेशन परियोजनाओं के लिए पारेषण प्रणाली ,पीजीसीआईएल' के संबंध में क्रमशः संविदात्मक मुद्दों तथा भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।परियोजना 'छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए डब्ल्यूआर के उत्तर /पश्चिम में प्रणाली सुदृढीकरण,पीजीसीआईएल' के संबंध में वन संबंधी अनुमति में देरी होने के कारण 6 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;एक परियोजना 'जैसलमर में लख्खमना पर पवन विद्युत परियोजना ,50मेवा ,एनएचपीसी ' के संबंध में 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है;तीन परियोजनाएं 'एनआर/डब्ल्यूआर के लिए सिक्किम में जेनेरेशन परियोजनाएं से विद्युत के हस्तांतरण के लिए पारेषण प्रणाली ,पीजीसीआईएल ' उत्तर क्षेत्रीय भाग ख में ट्रान्सफोर्मर्स की स्थापना पीजीसीआईएल' तथा 'बोकारो ताप विद्युत स्टेशन -क ,डीवीसी ' के संबंध में प्रत्येक में 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । तथा एक परियोजना 'छत्तीसगढ़ में आईपीपीएस जेनेरेशन परियोजनाओं डब्ल्यूआर के पश्चिम भाग में पारेषण प्रणाली सुदृढीकरण' पीजीसीआईएल' के संबंध में 6 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।(तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

ii) **पेट्रोलियम क्षेत्र में,** 66 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं । माह के दौरान, 10 परियोजनाओं के संबंध में 1-44 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 10 परियोजनाओं में से 3 मेगा परियोजनाएं हैं। एक परियोजना 'पारादीप-राईपूर -रांची पाइपलाइन 'आईओसीएल' के संबंध

में संविदात्मक मुद्दों के कारण 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'मौंडेड बुलेट परियोजना ,सीपीसीएल' तथा 'गुजरात रिफ़ाइनरी में ईटीपी के लिए रिवर्स ओसमोसिस संयंत्र ,आईओसीएल' के संबंध में क्रमशः एचटी प्रसारण में बाधा तथा ठेकेदार द्वारा धीमी प्रगति के कारण प्रत्येक में 2 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'एसएमपीएल के डी-बोटलनेकिंग ,आईओसीएल' तथा 'ईटीपी 6 के निर्माणओएनजीसी' के संबंध में क्रमशः ठेकेदार द्वारा कम निष्पादन तथा सिविल कार्यों में धीमी प्रगति के कारण प्रत्येक में 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'परदीप हल्दीया बरौनी पाइपलाइन आईओसीएल' तथा 'कोक चेम्बरों का प्रतिस्थापन आईओसीएल' के संबंध में क्रमशः भूमि अधिग्रहण समस्याएँ तथा पारिस्थितिक अनुमति में विलंब के कारण प्रत्येक में 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;एक परियोजना 'कोरबा में मार्केटिंग टोप ,आईओसीएल' के संबंध में ठेकेदार द्वारा कम निष्पादन के कारण 6 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;एक परियोजना 'कोच्चि -कूटनाड बांगलूर मांगलूर पाइपलाइन परियोजना ,गेल' के संबंध में किसानों और जमीन मालिकों से कड़े प्रतिरोध के कारण 44 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'मधुबन में निर्जलीकरण सुविधाओं के साथ माध्यमिक टैंक फार्म तथा उपचार प्रवाह संयंत्र ,ऑइल' के संबंध में 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iii) **इस्पात क्षेत्र में**, 34 परियोजनाओं में से 15 परियोजनाएं विलंबित हैं । माह के दौरान 5 परियोजनाओं के संबंध में 1-7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 15 परियोजनाओं में से 1 मेगा परियोजनाएं हैं। एक परियोजना 'भिलाई इस्पात संयंत्र के विस्तार ,सेल ' के संबंध में आर एवं आर समस्याएँ तथा अपर्याप्त संसाधन जुटाने के संबंध में 5 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'आरएसपी में ब्लास्ट फरनेस -1 का उन्नयन ,सेल' तथा 'बीएसपी में कोक ओवेन बाटेरी के कोल्ड रिपेयर ,सेल' के संबंध में क्रमशः 1 तथा 2 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'संबंधित अन्य सुविधाओं के साथ 45 एमवीए साफ टी के स्थापना,सेल' तथा बीएसएल में सीओबी-7 के पुनर्निर्माण 'के संबंध में क्रमशः 3 तथा 7 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।(तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iv) **सड़क परिवहन एवं राजमार्ग क्षेत्र में**, 411 परियोजनाओं में से, 130 परियोजनाएं विलंबित हैं । माह के दौरान 4 परियोजनाओं के संबंध में 11-21 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । एक परियोजना 'सितागंज बरेली पीएस के साथ 2 लाइनिंग ,एनएचएआई ' के संबंध में 11 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ;दो परियोजनाएं 'तिरुचि-कराईकुडी तथा तिरुचि बाइपास ,एनएचएआई' तथा 'जलंधर -अमृतसर एनएचएआई' के संबंध में प्रत्येक में 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा एक परियोजना 'तिरुपति-तिरुथनी-चेन्नई एनएचएआई' के संबंध में 21 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है ।(तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) **कोयला क्षेत्र में**, 88 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं। माह के दौरान 3 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 3 परियोजनाओं में से 1 मेगा परियोजनाएं हैं। 1 परियोजना 'सोनेपूर बाजारी (समन्वय) ओसीपी (8.0एमटीवाई) ईसीएल' संबंध में सीएचपी के निविदाओं में देरी के कारण 1 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है; दो परियोजनाएं 'कुलड़ा ओसीपी, एमसीएल' तथा 'पूर्णादीह ओसीपी (3.0एमटीवाई), सीसीएल' के संबंध में प्रत्येक में कोयला निकासी समस्या तथा भूमि अधिग्रहण समस्या के कारण क्रमशः 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है।

vi) **शहरी विकास क्षेत्र में**, 30 परियोजनाओं में से, 11 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाएं 'आईआईएसईआर कोलकत्ता के लिए पश्चिम बंगाल हरीघंटा कल्याणी में आवासीय सह शैक्षिक परिसर सीपीडब्ल्यूडी' तथा भोपाल (सीएपीटी) पुलिस प्रशिक्षण केलिए केंद्रीय अकादमी के निर्माण सीपीडब्ल्यूडी' के संबंध में क्रमशः 2 तथा 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vii) **स्वास्थ्य और परिवार कल्याण में**, 9 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाएं 'सफदरजंग आस्पताल, नई दिल्ली - पूनर्विकास तथा अन्य एमेर्जेंसी ब्लॉक, एचएससीसी टीएटीएचए 'एम्स - रायबरेली आवासीय एचएससीसी' के संबंध में क्रमशः निधि की कमी तथा स्थानीय समस्याओं के कारण 3 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है।

12. रेल मंत्रालय ने 1 जनवरी, 2015 से इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी जारी परियोजनाओं पर मासिक स्थिति रिपोर्टें प्रस्तुत करने की परंपरा को समाप्त कर दिया है। रेल मंत्रालय ने अपनी 20 परियोजनाओं के संबंध में नवीनतम जानकारी प्रदान की है, केवल इन्हीं परियोजनाओं को सां. और कार्य. कार्या. मंत्रालय स्तर पर निगरानी के लिए पहचान किया गया है। अतः उपलब्ध सूचना/आंकड़े का (जनवरी 2015 की स्थिति के अनुसार) रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में उपयोग किया गया है।

13. सड़क परिवहन एवं राजमार्ग मंत्रालय (एमओआरटीएच) तथा भारतीय राष्ट्रीय राजमार्ग प्राधिकरण (एनएचएआई) ने जून, 2015 से अपनी परियोजनाओं संबंधी आंकड़े प्रदान करना बंद कर दिया है। तथापि, एमओआरटीएच व एनएचएआई ने फरवरी 2016 माह (रिपोर्टिंग माह दिसंबर, 2015) से अपनी सभी चल रही परियोजनाओं को स्वैच्छिक रूप से फिर से अद्यतन करना शुरू किया है। एमओआरटीएच तथा एनएचएआई दोनों ने रिपोर्टिंग माह दिसंबर, 2015 के दौरान सड़क के अंतर्गत 251 नई परियोजनाओं को शामिल किया है। यह मंत्रालय एनएचएआई के द्वारा दी गई जानकारी के अनुसार पीपीपी/बीओटी परियोजनाओं को अलग-अलग रूप से वर्गीकृत कर रहा है।

14. दिनांक 29.02.2016 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।

15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for February 2016 contains information on the status of the 1071 Central Sector Infrastructure Projects costing ₹150 crore and above. During February 2016, 2 projects (1 project each in Coal and Petroleum sector) have reported completion.

2. During the reference month, out of 1071 projects, 341 projects are delayed with respect to original schedule and 38 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 38 projects, 11 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	411	130	4	0
2	RAILWAYS	298	32	0	0
3	POWER	111	60	12	6
4	COAL	88	43	3	1
5	PETROLEUM	66	36	10	3
6	STEEL	34	15	5	1
7	URBAN DEVELOPMENT	30	11	2	0
8	HEALTH AND FAMILY WELFARE	9	4	2	0
9	SHIPPING AND PORTS	8	2	0	0
10	CIVIL AVIATION	4	1	0	0
11	ATOMIC ENERGY	4	4	0	0
12	MINES	3	0	0	0
13	TELECOMMUNICATIONS	2	2	0	0
14	FERTILISERS	1	0	0	0
15	PETROCHEMICALS	1	0	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		1071	341	38	11

3. Total original cost of implementation of the 1071 projects was ₹12,66,248.36 crore and their anticipated completion cost is likely to be ₹14,26,985.93 crore, which reflects overall cost overruns of ₹1,60,737.57 crore (12.69% of original cost). The expenditure incurred on these projects till February 2016 is ₹5,66,058.05 crore, which is 39.67% of the anticipated cost of the projects. The

sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns(as on 29-02-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
3	MARKETING TOP AT KORBA	01/2011	141.86	232.00	63.54
4	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	12/2009	309.81	462.79	49.38
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	187.40
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
4	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.57	139.32
5	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	133.06
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
2	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
3	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	1313.23
4	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01

ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
2	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
5	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	156.63	276.00	76.21
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
STEEL					
1	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	39.29
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53
2	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	202.00	18.06

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 29-02-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00

2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
COAL					
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
4	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
5	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
PETROLEUM					
1	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
2	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
4	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	495.00
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	11778.56
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.76	4479.17
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	3683.06
RAILWAYS					
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	3252.34
ROAD TRANSPORT AND HIGHWAYS					
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
3	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23

4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	302.09
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00
2	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHAR	02/2012	171.10	202.00	30.90

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1071 projects, 5 projects are ahead of schedule, 258 are on schedule and 341 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 305 if delay is calculated on the basis of latest schedule of completion. Further, 34 projects have been sanctioned without original commissioning schedule date and for 433 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 341 delayed projects, 65 projects have overall delay in the range of 1 to 12 months, 66 projects have delay in the range of 13 to 24 months, 138 projects have delay in the range of 25 to 60 months and 72 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 29-02-2016)

SN	PROJECT	DOA	DOC ORIGIN AL	DOC ANTICIPAT ED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	05/2016	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12/2016	12/2019	36
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11/2018	35
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
COAL					
1	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
2	MAGADH OC 20 MTY (CCL)	08/2008	07/2012	03/2021	104
3	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
4	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2017	84
5	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
HEALTH AND FAMILY WELFARE					
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	06/2016	31
2	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2016	15
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK	09/2013	12/2015	03/2016	3
4	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	01/2016	04/2016	3
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
PETROLEUM					
1	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	02/2019	74
2	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	12/2018	71
3	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	10/2016	61
4	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	10/2011	03/2016	53
POWER					
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2016	97
4	BARH STPP(3X660MW) NTPC	02/2005	01/2011	05/2018	88
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	09/2009	09/2016	84
RAILWAYS					
1	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2017	181
3	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174

5	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2016	144
ROAD TRANSPORT AND HIGHWAYS					
1	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2016	138
2	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12/2003	09/2007	12/2016	111
3	NALBARI T BIJNI (AS-7)	12/2003	04/2008	01/2017	105
4	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	03/2016	102
5	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	07/2016	100
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	03/2016	120
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
STEEL					
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	11/2016	44
2	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	06/2016	32
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	03/2016	25
4	SMS-1 CONVERTERS REVAMPING	05/2012	07/2015	06/2017	23
5	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	12/2016	20
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	09/2014	03/2017	30
2	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2017	20
URBAN DEVELOPMENT					
1	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	03/2017	60
2	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	05/2016	47
3	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37
4	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	12/2014	03/2017	27
5	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	02/2014	09/2015	04/2017	19

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during February 2016, out of 1071 projects, 238 projects reported cost overruns and 341 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **22.22%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **31.84%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 29-02-2016)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIR	01/2009	309.46	309.46	412.95	01/2011	09/2017
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.01	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	21.76	N.A.	09/2018
COAL							
1	MADANNAGAR OCP	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	49.27	11/2016	11/2016
HEALTH AND FAMILY WELFARE							
1	LGBRIMH	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	LHMC - HOSPITAL	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	SAFDARJUNG SSB	09/2013	444.70	444.70	268.07	12/2015	03/2016

4	RAEBARELI-HOUSING	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	157.61	01/2016	01/2016
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1176.00	4.59	09/2017	04/2020
2	WPPMH	12/2015	355.13	355.13	0.00	11/2016	11/2016
3	WPPRJ	12/2015	344.50	344.50	0.00	11/2016	11/2016
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1074.73	10/2011	03/2016
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1447.43	01/2012	05/2016
3	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	499.19	09/2011	10/2016
5	TWENTY NOS. FEEDER GAS LINES	03/2009	228.64	214.19	140.71	12/2016	12/2016
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	7969.14	09/2010	N.A.
2	BTPS-A	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	RTPS PH-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	94.63	09/2014	06/2016
5	URTD SM PHASE-I	01/2014	374.63	374.63	16.20	04/2016	11/2016
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGAL (SER)	04/1974	393.46	1026.00	181.48	03/2007	03/2015

2	NANGALDAM-TALWARA(NL),N R	03/1981	450.00	2100.00	391.95	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	255.55	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	602.10	03/1994	03/2015
ROAD TRANSPORT AND HIGHWAYS							
1	"MADHUGIRI-MULBAGAL (KM 400.330 TO KM 483.151) - LOT-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	ANISABAD-AURANGABAD-HARIHARGANJ (KM 0.000 TO KM 62.000)- LOT	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	ANISABAD-AURANGABAD-HARIHARGANJ (KM 62.000 TO KM 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	BAKHTIYARPUR - MOKAMA	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
5	BANKUARA-PURULIA (KM 0.000 TO KM 84.000)	01/1991	322.00	322.00	0.00	03/2018	03/2018
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	03/2016
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	841.02	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	415.80	12/2010	01/2016
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	RORO-II	09/2015	210.00	210.00	0.00	01/2018	01/2018
STEEL							
1	MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97	02/2014	03/2016
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	648.16	03/2015	03/2017

3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER	03/2007	149.73	173.00	175.94	12/2015	03/2017
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER	12/2007	202.61	227.00	195.51	12/2016	12/2016
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERM	12/2007	200.00	200.00	126.15	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY M	08/2005	191.24	191.24	0.00	08/2007	N.A.
2	SEWEWORAGE PROJECT	08/2007	246.90	246.90	0.00	N.A.	N.A.
3	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEX	05/2009	261.85	261.85	168.00	05/2013	06/2016
4	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KER	01/2010	165.23	165.23	0.00	10/2012	N.A.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	160.00	07/2012	12/2015

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 29-02-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	21077.00

2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5150.14
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	412.95
COAL					
1	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	207.70
2	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	453.18
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	9175.15
PETROLEUM					
1	MARKETING TOP AT KORBA	01/2011	141.86	0.00	164.35
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5398.46
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7969.14
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1956.52
4	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4402.95
5	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	02/2009	509.66	0.00	528.56
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	36.38	255.55
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	0.00	201.26
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	0.00	712.02
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	0.00	10722.72
5	CUTTACK - BARANG (LD)	04/1995	127.13	0.00	193.37
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	392.60
2	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	197.40
3	GUWAHATI TO NALBARI (AS-5)	12/2003	198.16	0.00	242.40
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	230.00	295.20
5	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	195.00	0.00	278.96
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	415.80
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97
1	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	175.94
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	13525.81

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 29-02-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2013	12/2015
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	N.A.	06/2015
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	SYSTEM STRENGTHENING XII OF SR	02/2010	06/2012	N.A.	N.A.
3	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	N.A.	03/2015

4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.A.	03/2010	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	PONDICHERRY TO TINDIVANAM SECTION OF NH-66	01/1991	01/2008	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF PRATAPGARH PADI SECTION	01/1991	04/2014	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
4	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	01/1991	N.A.	N.A.	N.A.
5	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	01/1991	N.A.	N.A.	N.A.
SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	01/2015	08/2015
2	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	09/2014	06/2015
3	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH	01/2013	N.A.	N.A.	N.A.
4	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GANDHI KHEL ABHIYAN(RGKA) SCHEME	07/2014	01/1999	N.A.	N.A.

URBAN DEVELOPMENT					
1	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.A.	N.A.
2	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
3	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	12/2015	12/2015
4	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
5	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Power Sector**, out of 111 projects, 60 projects are delayed. During the month, 12 projects have reported additional delay in the range of 1-6 months. Out of 12 projects, 6 are mega projects. Two projects 'Kameng Hydroelectric Project, NEEPCO' and 'Northern Region System Strengthening Scheme-XIX, PGCIL' have reported additional delay of 1 month each due to flash flood and redesigning of dam parameter respectively; two projects 'Northern Region Transmission Strengthening Scheme, PGCIL' and 'Northern Region System Strengthening Scheme-XXI, PGCIL' have reported additional delay of 1 month each due to farmer agitation and RoW problem respectively; two projects 'System Strengthening in NR For Sasan and Mundra (UMPP), PGCIL' and 'Transmission System for Phase-1 Generation Projects in Jharkhand and West Bengal-Part-A1, PGCIL' have reported additional delay of 3 months each due to contractual issue and land acquisition issue respectively; the project 'System Strengthening in North/West Part of WR for IPP Projects in Chattisgarh, PGCIL' has reported additional delay of 6 months due to delay in forest clearance; one project 'Wind Power Project at Lakhmana in Jaisalmer, 50MW, NHPC' have reported additional delay of 1 month; three projects 'Transmission System for Transfer of Power from Generation Projects in Sikkim to NR/WR Part-A, PGCIL', 'Augmentation of Transformers in Northern Region-Part BPGCIL' and 'Bokaro Thermal Power Station-A, DVC' have reported additional delay of 3 months each and one project 'Transmission System Strengthening in Western Part of WR For IPPS Generation Projects in Chattisgarh, PGCIL' has reported additional

delay of 6 month (however, no specific reason has been reported by the project implementing agency for the delay in these projects).

- ii) In the **Petroleum Sector**, out of 66 projects, 36 projects are delayed. During the month, 10 projects have reported additional delays in the range of 1-44 months. Out of 10 projects, 3 projects are mega projects. One project 'Paradip-Raipur-Ranchi Pipeline IOCL' has reported additional delay of 1 month due to contractual problem; two projects 'Mounded Bullet Project, CPCL' and 'Reverse Osmosis Plant for ETP at Gujarat Refinery, IOCL' have reported additional delay of 2 months each due to hindrance in HT transmission and slow progress by contractor respectively; two projects 'De-Bottlenecking of SMPL, IOCL' and 'Construction of 6 ETPs, ONGC' have reported additional delay of 3 months each due to poor performance of contractor and slow progress in civil works respectively; two projects 'Augmentation of Paradip Haldia Barauni Pipeline, IOCL' and 'Replacement of Coke Chambers IOCL' have reported additional delay of 3 months each due to land acquisition problem and delay in environmental clearances respectively; one project 'Marketing TOP at Korba, IOCL' has reported additional delay of 6 months due to poor performance of contractor; one project 'Kochi-Kootanad Bangalore Mangalore Pipeline Project GAIL' has reported additional delay of 44 months due to stiff resistance from farmers and land owners and one project 'Secondary Tank Farm With Dehydration Facility and Effluent Treatment Plantat Madhuban, OIL' has reported additional delay of 12 months; (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- iii) In the **Steel Sector**, out of 34 projects, 15 projects are delayed. During the month, 5 projects have reported additional delay in the range of 1-7 months. Out of 5 projects, 1 projects\ is mega project. One project 'Expansion of Bhilai Steel Plant, SAIL' has reported additional delay of 5 months due to R&R problem and inadequate resource mobilization; two projects 'Upgradation of Blast Furnace-1 at RSP SAIL' and 'Cold Repair of Coke Oven Battery-9 at BSP, Bhilai, SAIL' have reported additional delay of 1 and 2 months respectively; two projects 'Installation of 45MVA Saft With Other Associated Facilities SAIL' and 'Rebuilding of COB-7 at BSL SAIL' have reported additional delay of 3 and 7 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- iv) In the **Road Transport & Highways Sector**, out of 411 projects, 130 projects are delayed. During the month, 4 projects have reported additional delay in the range of 11-

21 months. One project '2-Laning With PS Sitarganj Bareilly Section NHAI' has reported additional delay of 11 months; two projects 'Two Laning of Trichy - Karaikudi and Trychi Bypass, NHAI' and 'Jalandhar-Amritsar NHAI' have reported additional delay of 12 months each and one project 'Tirupati - Tiruthani - Chennai NHAI' has reported additional delay of 21 months (however, no specific reason has been reported by the project implementing agency for the delay in these projects).

- v) In the **Coal Sector**, out of 88 projects, 43 projects are delayed. During the month, 3 projects have reported additional delay in the range of 1-12 months. Out of 3 projects, 1 project is mega project. One project 'Sonepur Bazari (Comb) OCP (8.0 MTY) ECL' has reported additional delay of 1 month due to delay in tendering of CHP; two projects 'Kulda OCP, MCL' and 'Purnadih OCP (3.0 MTY), CCL' have reported additional delay of 12 months each due to coal evacuation problem and land acquisition problem respectively.
- vi) In the **Urban Development Sector**, out of 30 projects, 11 projects are delayed. During the month, 2 projects 'Academic cum Residential Campus at Haringhanta Kalyani WB For IISER Kolkata, CPWD' and 'Construction of Central Academy For Police Training (CAPT) Bhopal, CPWD' have reported additional delay of 2 and 3 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- vii) In the **Health and Family Welfare**, out of 9 projects, 4 projects are delayed. During the month, 2 projects 'Safdarjung Hospital, New Delhi-Redevelopment and Others-Emergency Block, HSCC and 'AIIMS-Raebareli-Housing HSCC' have reported additional delay of 3 months each due to fund constraint and local problem respectively.

12. Ministry of Railways has **discontinued** the practice of furnishing monthly status reports on all its on-going projects to this Ministry w.e.f 1st January 2015. The Ministry of Railways have provided latest information of their 20 projects only which have been identified by them to be monitored at MoSPI level. Therefore, the available information/data (**as on January 2015**) has been used in respect of remaining projects of Railways sector.

13. Ministry of Road Transport & Highways (MoRTH) & National Highways Authority of India (NHAI) had stopped providing data on their project w.e.f. June 2015. However, MoRTH & NHAI have voluntarily resumed updating of all their on-going projects from the month of February 2016 (Reporting month December 2015). Both MoRTH and NHAI have

added 251 new projects under Road sector during reporting month of December 2015. This Ministry is separately classifying PPP/BOT projects as per information given by NHAI.


14. The status as on 29.02.2016 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

15. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	411	4
2	RAILWAYS	298	0
3	POWER	111	12
4	COAL	88	3
5	PETROLEUM	66	10
6	STEEL	34	5
7	URBAN DEVELOPMENT	30	2
8	HEALTH AND FAMILY WELFARE	9	2
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	0
12	MINES	3	0
13	TELECOMMUNICATIONS	2	0
14	FERTILISERS	1	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	1071	38

Sectoral break up of on-going infrastructure projects

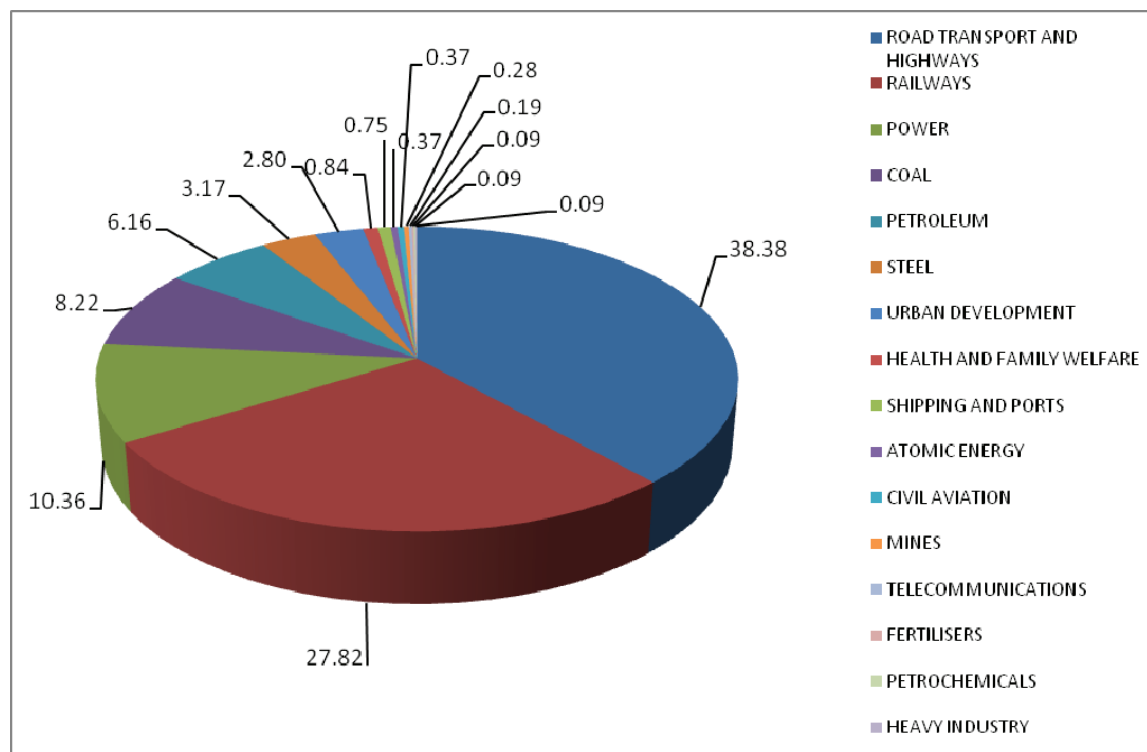

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00
	September,2015			
	<u>STEEL</u>			
29	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000018]	607.17	12/2011	394.89
30	EXPANSION OF BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000055]	6,325.00	12/2011	5,256.65
	<u>PETROLEUM</u>			
31	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000132]	5,608.40	05/2015	4,457.47
	<u>POWER</u>			
32	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000124]	213.78	03/2014	204.54
33	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000154]	1,315.90	10/2016	632.97
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000156]	296.87	12/2014	318.66
	October,2015			
	<u>CIVIL AVIATION</u>			
35	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000070]	452.00	03/2015	449.41
	<u>STEEL</u>			
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) (RASTRIYA ISPAT NIGAM LIMITED) - [120100067]	8,692.00	10/2009	11,483.12
37	CAPTIVE POWER PLANT - 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000087]	677.00	09/2013	537.19

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
38	102 MW WIND POWER PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000119]	1,106.00	06/2012	437.69
	<u>POWER</u>			
39	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100246]	588.25	12/2007	1,020.81
40	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000093]	2,743.19	12/2013	2,827.00
	<u>URBAN DEVELOPMENT</u>			
41	FARIDABAD EXTENSION (DELHI METRO RAIL CORPORATION LTD) - [N28000057]	2,494.00	09/2014	1,311.53
	November,2015			
	<u>POWER</u>			
42	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N16000144]	1,508.74	03/2015	1,211.48
	December,2015			
	<u>CIVIL AVIATION</u>			
43	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000072]	344.28	03/2014	80.60
	<u>COAL</u>			
44	CHURCHA ROUG(1.35MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000046]	462.35	03/2014	497.01
	<u>PETROLEUM</u>			
45	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000142]	1,419.00	12/2014	1,291.63
46	REWARI KANPUR PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000145]	1,210.64	11/2015	1,249.03
47	MARKETING TERMINAL AT PARADEEP (INDIAN OIL CORPORATION LIMITED) - [N16000168]	199.75	07/2013	211.72
48	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000182]	429.06	10/2014	439.02
	<u>POWER</u>			
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000160]	243.53	08/2016	185.63

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
50	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN(SHIPPING CRP. OF INDIA) - [N25000064]	994.82	11/2013	427.54
	<u>TELECOMMUNICATIONS</u>			
51	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS (BHARAT SANCHAR NIGAM LIMITED) - [N26000096]	384.00	10/2010	74.74
	January,2016			
	<u>COAL</u>			
52	BLOCK-B OCP NCL (3.5 MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000009]	746.04	03/2015	550.32
	<u>STEEL</u>			
53	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000079]	237.09	12/2014	221.88
54	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000080]	313.05	06/2015	319.91
55	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000082]	160.48	09/2014	143.89
	<u>POWER</u>			
56	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000087]	2,074.86	03/2013	1,975.94
	<u>URBAN DEVELOPMENT</u>			
57	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000078]	2,727.89	03/2010	2,709.00
	February,2016			
	<u>COAL</u>			
58	DIPKA EXPANSION OCP (SECL) (20-25) MTY (SOUTH-EASTERN COAL FIELDS LIMITED) - [060100094]	1,943.66	03/2014	2,121.76
	<u>PETROLEUM</u>			
59	DEVELOPMENT OF WO-16 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000105]	2,523.00	01/2014	1,792.85

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2016			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000103]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000120]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000121]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000122]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000181]	2,913.10	05/2016	13.86
	June,2016			
7	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
8	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N26000065]	1,077.00	03/2009	.00
	August,2016			
	<u>SHIPPING AND PORTS</u>			
9	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21
10	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	October,2016			
	<u>PETROLEUM</u>			
11	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>SHIPPING AND PORTS</u>			
12	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	December,2016			
	<u>PETROLEUM</u>			
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	667.40
15	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000270]	297.78	02/2015	37.72
17	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000271]	297.78	02/2015	37.72
18	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T(PUBLIC WORKS DEPT OF STATE) - [N24000285]	297.78	02/2015	37.72
19	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(PUBLIC WORKS DEPT OF STATE) - [N24000400]	282.41	08/2016	.00
	<u>SHIPPING AND PORTS</u>			
20	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL (MUMBAI PORT TRUST) - [N25000016]	1,228.00	12/2010	1,038.00


Summary of projects in the Flash Report for the month of February, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1063
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects Added in Current Month	10
Number of Projects in Current Month	1071


Brief Analysis

Project Status with respect to Original Schedule: Out of 1071 projects, 5 projects are ahead of schedule, 258 projects are on schedule 341 projects are delayed. 433 projects do not have fixed dates of commissioning. 34 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

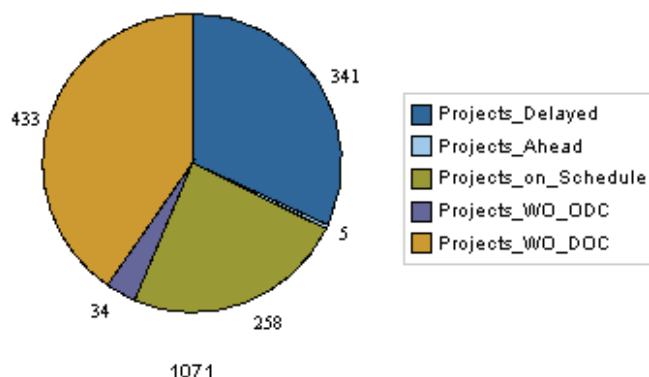

Investment Scenario

Total original cost of implementation of 1071 projects when sanctioned, was of the order of Rs. 1266248.36 crore but this was subsequently revised to Rs. 1426985.93 crore implying a cost overrun of 12.7%. The expenditure incurred on these projects till February, 2016 is Rs. 566058.05 crore, which is 39.7% of the revised cost of the projects.

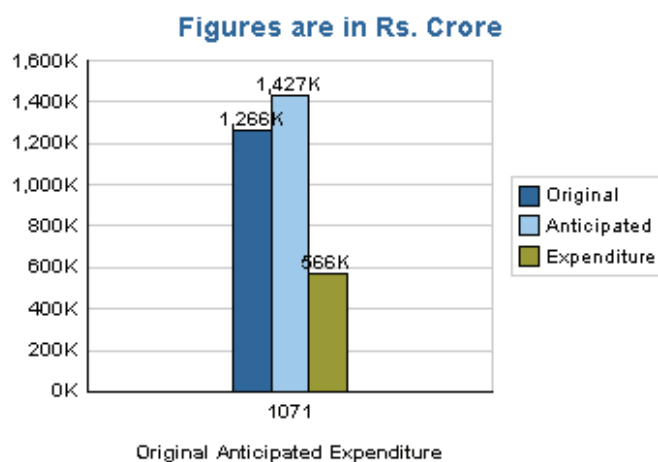

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1063
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	10
No of Projects in Current Month	1071

Project status

Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	341	5	258	34	433	1071	31.84
Latest Approved (Date)	305	7	292	34	433	1071	28.48

Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	938	10,72,470.83	11,29,161.77	3,79,097.94	33.60	56,690.94	5.30
Project with Revision in Cost	133	2,59,675.96	2,97,824.16	1,86,960.11	62.80	38,148.20	14.70
Total	1,071	13,32,146.79	14,26,985.93	5,66,058.05	39.67	94839.14	7.12
Original Cost of All Projects							
Original Cost	1071	12,66,248.36	14,26,985.93	5,66,058.05	39.67	1,60,737.57	12.69

Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	341	543,616.01	660,111.49	409,867.13	62.10	116,495.48	21.40
Latest Approved (RCE)	305	500,365.62	566,026.73	365,313.10	64.50	65,661.11	13.10

Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	38	48,346.46	71,989.69	50,856.30	70.60	23,643.23	48.90

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	60,408.62	61,521.55	1.84	4	1,321.16	2,690.85	103.67
4	FERTILISERS	1	197.79	209.44	5.89	1	197.79	209.44	5.89
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0.00
6	STEEL	34	54,044.86	54,574.30	0.98	6	1,964.58	2,494.02	26.95
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	66	137,131.44	145,764.07	6.30	15	59,284.75	69,863.51	17.84
9	POWER	111	304,580.02	353,192.66	15.96	22	61,522.84	110,199.09	79.12
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	298	254,176.67	329,512.54	29.64	161	82,833.35	214,601.52	159.08
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,520.01	0.95	18	5,171.67	7,634.21	47.62
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	4	1,006.56	1,937.62	92.50
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	30	134,055.93	139,282.13	3.90	2	6,566.10	11,811.00	79.88
Total		1071	1,266,248.36	1,426,985.93	12.69	238	243,928.01	463,616.66	90.06

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	5	1,263.14	3,108.40	146.09
2	ARUNACHAL PRADESH	14	11,758.70	28,124.97	139.18	5	9,616.85	25,983.12	170.18
3	ASSAM	50	28,795.71	44,498.17	54.53	14	15,918.17	31,722.22	99.28
4	BIHAR	64	57,872.84	72,300.43	24.93	16	13,908.83	29,122.47	109.38
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	31	30,605.81	31,660.45	3.45	6	3,425.92	4,607.88	34.50
7	HARYANA	20	13,986.73	15,957.35	14.09	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,966.47	11,365.75	128.85
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	2	6,142.04	25,751.47	319.27
10	KARNATAKA	42	72,113.99	87,378.98	21.17	19	14,794.54	30,065.56	103.22
11	KERALA	16	25,825.82	30,300.97	17.33	8	17,335.36	21,810.51	25.82
12	MADHYA PRADESH	52	54,020.18	56,591.41	4.76	5	2,404.35	5,184.88	115.65
13	MAHARASHTRA	73	121,026.10	129,786.02	7.24	12	17,419.89	27,446.77	57.56
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	4,083.02	5,307.90	30.00
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	325.27
17	NAGALAND	3	6,420.00	8,757.12	36.40	2	5,124.00	7,461.12	45.61
18	ODISHA	47	71,450.12	80,688.81	12.93	12	33,164.89	42,424.92	27.92
19	PUNJAB	23	11,714.51	11,712.84	-0.01	1	573.96	605.00	5.41
20	RAJASTHAN	60	40,960.69	41,503.63	1.33	7	2,884.16	3,512.63	21.79
21	SIKKIM	5	2,149.08	4,999.32	132.63	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	57	68,769.74	88,418.98	28.57	21	23,753.56	43,402.80	82.72
23	TRIPURA	9	3,776.07	7,489.01	98.33	7	2,909.18	6,622.12	127.63
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	8	2,576.25	6,510.63	152.72
25	WEST BENGAL	46	49,513.36	62,924.88	27.09	13	8,617.64	24,280.63	181.76
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	16	49,963.05	49,963.05	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	40	86,425.52	87,703.17	1.48	5	3,343.98	4,621.63	38.21
29	JHARKHAND	44	41,826.84	44,389.59	6.13	6	3,485.18	6,089.67	74.73
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	0.00	0	0.00	0.00	0.00
32	TELANGANA	32	12,335.70	15,282.09	23.89	9	2,836.21	5,870.81	106.99
33	MULTI STATE	176	267,786.62	245,109.97	-8.47	42	33,836.45	65,015.75	92.15
Total		1071	1,266,248.36	1,426,985.93	12.69	238	243,928.01	463,616.66	90.06

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	60,408.62	61,521.55	1.84	43	24,273.96	25,595.39	4 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	-
6	STEEL	34	54,044.86	54,574.30	0.98	15	38,472.11	38,977.16	3 - 44
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	66	137,131.44	145,764.07	6.30	36	77,227.77	84,051.74	1 - 74
9	POWER	111	304,580.02	353,192.66	15.96	60	161,214.48	197,310.03	1 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	976.47	976.47	3 - 31
12	RAILWAYS	298	254,176.67	329,512.54	29.64	32	37,635.20	93,472.32	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,520.01	0.95	130	90,119.92	91,945.85	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88 - 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	30	134,055.93	139,282.13	3.90	11	55,385.80	55,372.77	8 - 60
Total		1071	1,266,248.36	1,426,985.93	12.69	341	543,616.01	660,111.49	

Extent of time overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	18	9,281.00	9,426.40	5 - 50
2	ARUNACHAL PRADESH	14	11,758.70	28,124.97	139.18	2	3,070.89	7,442.23	35 - 79
3	ASSAM	50	28,795.71	44,498.17	54.53	25	15,059.37	25,717.56	15 - 138
4	BIHAR	64	57,872.84	72,300.43	24.93	16	24,575.79	34,273.78	8 - 90
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	-
6	GUJARAT	31	30,605.81	31,660.45	3.45	9	18,913.80	18,894.11	5 - 45
7	HARYANA	20	13,986.73	15,957.35	14.09	5	3,130.20	4,310.20	14 - 69
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,190.42	8,669.59	16 - 111
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	6	13,202.50	32,811.93	10 - 181
10	KARNATAKA	42	72,113.99	87,378.98	21.17	9	18,509.13	19,478.43	2 - 53
11	KERALA	16	25,825.82	30,300.97	17.33	4	2,462.73	3,434.08	4 - 88
12	MADHYA PRADESH	52	54,020.18	56,591.41	4.76	9	5,076.62	5,566.59	11 - 87
13	MAHARASHTRA	73	121,026.10	129,786.02	7.24	22	40,866.25	45,635.62	1 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	536.00	536.00	29 - 29
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	47 - 123
17	NAGALAND	3	6,420.00	8,757.12	36.40	1	850.00	2,973.42	60 - 60
18	ODISHA	47	71,450.12	80,688.81	12.93	16	36,085.96	41,288.32	5 - 91
19	PUNJAB	23	11,714.51	11,712.84	-0.01	1	523.85	523.85	12 - 12
20	RAJASTHAN	60	40,960.69	41,503.63	1.33	14	20,093.07	20,134.26	1 - 89
21	SIKKIM	5	2,149.08	4,999.32	132.63	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	57	68,769.74	88,418.98	28.57	19	51,712.00	64,046.03	5 - 120
23	TRIPURA	9	3,776.07	7,489.01	98.33	4	2,033.56	4,500.90	7 - 108
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	19	19,506.39	21,717.77	7 - 102
25	WEST BENGAL	46	49,513.36	62,924.88	27.09	17	31,897.56	40,299.35	3 - 177
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
27	DELHI	16	49,963.05	49,963.05	0.00	5	39,893.26	39,893.26	3 - 37
28	CHHATISGARH	40	86,425.52	87,703.17	1.48	16	55,283.72	55,826.42	7 - 93
29	JHARKHAND	44	41,826.84	44,389.59	6.13	18	8,309.00	10,507.23	3 - 104
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	4	7,605.57	9,794.74	33 - 78
31	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	0.00	0	0.00	0.00	-
32	TELANGANA	32	12,335.70	15,282.09	23.89	13	4,422.52	5,748.91	8 - 132
33	MULTI STATE	176	267,786.62	245,109.97	-8.47	60	97,074.21	105,302.26	1 - 261
Total		1071	1,266,248.36	1,426,985.93	12.69	341	543,616.01	660,111.49	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	88	60,408.62	61,521.55	1.84	39	15,419.01	16,513.27	4 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	-
6	STEEL	34	54,044.86	54,574.30	0.98	14	22,947.11	23,452.16	3 - 44
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	66	137,131.44	145,764.07	6.30	20	49,747.78	56,003.16	1 - 74
9	POWER	111	304,580.02	353,192.66	15.96	53	142,291.24	168,202.11	1 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	4	976.47	976.47	3 - 31
12	RAILWAYS	298	254,176.67	329,512.54	29.64	30	31,485.20	82,512.86	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,520.01	0.95	124	88,850.19	90,584.17	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88 - 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	30	134,055.93	139,282.13	3.90	11	55,385.80	55,372.77	8 - 60
Total		1071	1,266,248.36	1,426,985.93	12.69	305	465,413.10	566,026.73	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	88	60,379.03	61,521.55	1.89	3	1,061.76	2,204.28	107.61
4	FERTILISERS	1	209.44	209.44	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0.00
6	STEEL	34	54,415.36	54,574.30	0.29	3	1,576.00	1,735.31	10.11
7	PETROCHEMICALS	1	8,920.00	9,965.00	11.72	1	8,920.00	9,965.00	11.72
8	PETROLEUM	66	143,178.74	145,764.07	1.81	4	15,590.77	18,386.55	17.93
9	POWER	111	332,768.53	353,192.66	6.14	7	28,130.05	48,554.18	72.61
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	298	275,766.45	329,512.54	19.49	151	85,193.36	195,587.58	129.58
13	ROAD TRANSPORT AND HIGHWAYS	411	250,231.68	250,520.01	0.12	12	3,669.32	5,544.33	51.10
14	SHIPPING AND PORTS	8	4,258.80	5,048.81	18.55	4	1,147.61	1,937.62	68.84
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	30	134,018.53	139,282.13	3.93	2	6,537.37	11,800.97	80.52
Total		1071	1,332,146.79	1,426,985.93	7.12	191	174,523.84	327,926.22	87.90

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	0	0.00	0.00	0- 0
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	60,408.62	61,521.55	1.84	1	259.40	486.57	60- 60
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0- 0
6	STEEL	34	54,044.86	54,574.30	0.98	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	66	137,131.44	145,764.07	6.30	4	1,892.87	2,385.12	4- 43
9	POWER	111	304,580.02	353,192.66	15.96	6	18,370.80	28,498.48	35- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	298	254,176.67	329,512.54	29.64	1	5,300.00	7,986.04	60- 60
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,520.01	0.95	2	425.61	517.56	77- 105
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	30	134,055.93	139,282.13	3.90	0	0.00	0.00	0- 0
Total		1071	1266248.36	1426985.93	12.69	14	26248.68	39873.77	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	88	60,408.62	61,521.55	1.84	4	1,321.16	2,690.85	24- 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	2,555.63	0.00	0	0.00	0.00	0- 0
6	STEEL	34	54,044.86	54,574.30	0.98	5	1,761.97	2,267.02	3- 25
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	66	137,131.44	145,764.07	6.30	11	37,540.20	45,433.04	4- 53
9	POWER	111	304,580.02	353,192.66	15.96	19	54,329.01	90,488.17	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	298	254,176.67	329,512.54	29.64	26	22,458.31	77,795.14	3- 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,520.01	0.95	8	2,586.46	4,438.02	55- 90
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	2	395.67	1,009.83	88- 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	30	134,055.93	139,282.13	3.90	0	0.00	0.00	0- 0
Total		1071	1266248.36	1426985.93	12.69	78	138773.78	256088.37	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	DIPKA EXPANSION OCP (SECL) (20-25) MTY	12/2009	1,943.66	03/2014	1,943.66	03/2016	2,121.76
	<u>PETROLEUM</u>						
2	DEVELOPMENT OF WO-16 CLUSTER FIELDS	06/2010	2,523.00	01/2014	2,523.00	01/2016	1,792.85

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	522.45	9/2019	522.45	9/2019
2	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	513.63	12/2019	513.63	12/2019
3	KOYAGUDEM OPENCAST PROJECT	10/2015	426.79	3/2018	426.79	3/2018
	<u>PETROLEUM</u>					
4	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	749.00	2/2020	749.00	2/2020
5	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM	1/2015	4,619.94	12/2017	4,619.94	12/2017
6	SIX PIPELINE REPLACEMENT PROJECT	3/2009	181.02	1/2017	181.02	1/2017
7	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	3,190.69	4/2018	3,190.69	4/2018
8	NAWAGAM-KOYALI PIPELINE PROJECT	11/2014	195.63	9/2018	195.63	9/2018
	<u>RAILWAYS</u>					
9	DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	81,459.00	/	28,181.00	-
	<u>STEEL</u>					
10	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER	8/2012	185.37	3/2016	185.37	3/2016

Milestones (Cumulative due & achieved)


Total	3936
Achieved up to month	1840

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	SONEPUR BAZARI (COMB) OCP (8.0 MTY) ECL	1,055.05	1,055.05	03/2018	06/2018	07/2018	1
2	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2016	03/2017	12
3	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2016	03/2017	12
	<u>STEEL</u>						
4	UPGRADATION OF BLAST FURNACE-1 AT RSP SAIL	708.91	708.91	04/2016	08/2016	09/2016	1
5	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	01/2016	03/2016	2
6	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES SAIL	187.33	187.33	10/2013	03/2016	06/2016	3
7	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	06/2016	11/2016	5
8	REBUILDING OF COB-7 AT BSL SAIL	245.67	245.67	05/2016	05/2016	12/2016	7
	<u>PETROLEUM</u>						
9	PARADIP-RAIPUR- RANCHI PIPELINE IOCL	1,793.00	1,793.00	09/2012	05/2016	06/2016	1
10	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	01/2016	03/2016	2
11	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY IOCL	160.00	160.00	02/2016	05/2016	07/2016	2
12	DE-BOTTLENECKING OF SMPL IOCL	1,584.00	1,584.00	08/2015	03/2016	06/2016	3
13	CONSTRUCTION OF 6 ETPS ONGC	317.64	240.95	09/2012	03/2016	06/2016	3
14	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	08/2015	03/2016	06/2016	3
15	REPLACEMENT OF COKE CHAMBERS IOCL	480.00	422.00	02/2016	07/2016	10/2016	3
16	MARKETING TOP AT KORBA IOCL	141.86	232.00	09/2016	03/2016	09/2016	6
17	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	352.56	450.55	03/2017	03/2017	03/2018	12


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
18	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT GAIL	2,915.00	2,915.00	12/2012	06/2015	02/2019	44
	<u>POWER</u>						
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	6,179.96	12/2009	06/2016	07/2016	1
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	02/2016	03/2016	1
21	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	02/2016	03/2016	1
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI PGCIL	1,677.57	1,677.57	04/2013	02/2016	03/2016	1
23	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW NHPC	302.49	302.49	02/2016	02/2016	03/2016	1
24	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	03/2016	06/2016	3
25	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A PGCIL	250.03	250.03	01/2013	02/2016	05/2016	3
26	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	558.26	558.26	11/2013	03/2016	06/2016	3
27	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B PGCIL	155.57	155.57	03/2016	03/2016	06/2016	3
28	BOKARO THERMAL POWER STATION-A DVC	2,313.00	4,237.67	12/2011	03/2016	06/2016	3
29	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	06/2016	12/2016	6
30	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH PGCIL	1,746.65	2,228.71	08/2014	06/2016	12/2016	6
	<u>HEALTH AND FAMILY WELFARE</u>						
31	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK HSCC	196.70	196.70	01/2016	01/2016	04/2016	3
32	AIIMS-RAEBARELI-HOUSING HSCC	159.50	159.50	11/2013	03/2016	06/2016	3

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
33	2-LANING WITH PS SITARGANJ BAREILY SECTION NHAI	301.04	301.04	01/2016	01/2016	12/2016	11
34	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS NHAI	374.00	374.00	05/2013	12/2016	12/2017	12
35	JALANDHAR - AMRITSAR NHAI	523.85	523.85	01/2016	01/2016	01/2017	12
36	TIRUPATI - TIRUTHANI - CHENNAI NHAI	571.00	571.00	10/2013	03/2016	12/2017	21
	<u>URBAN DEVELOPMENT</u>						
37	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA CPWD	225.81	225.81	06/2012	03/2016	05/2016	2
38	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL CPWD	188.87	188.87	12/2014	12/2016	03/2017	3

Graphical Presentation of All Projects w.r.t. Original Schedule

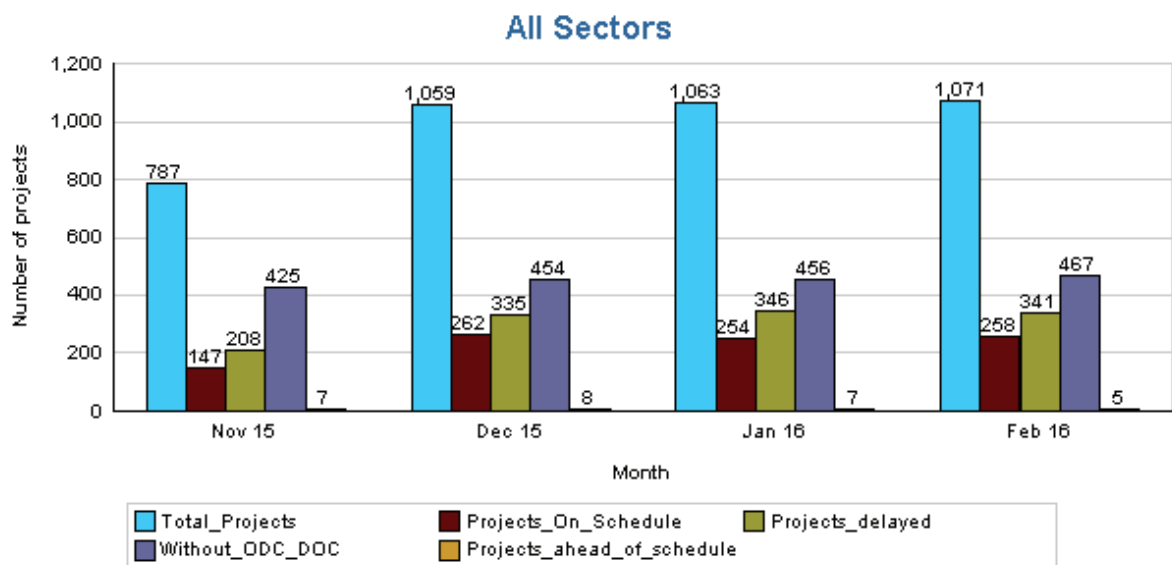


Break-up of 341 Delayed projects in February 2016

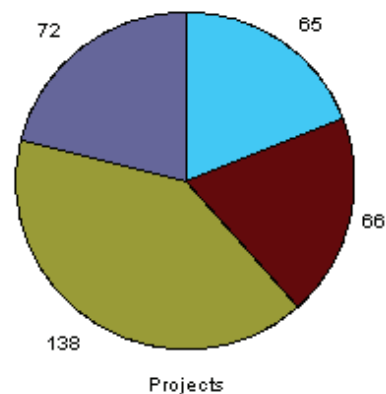


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

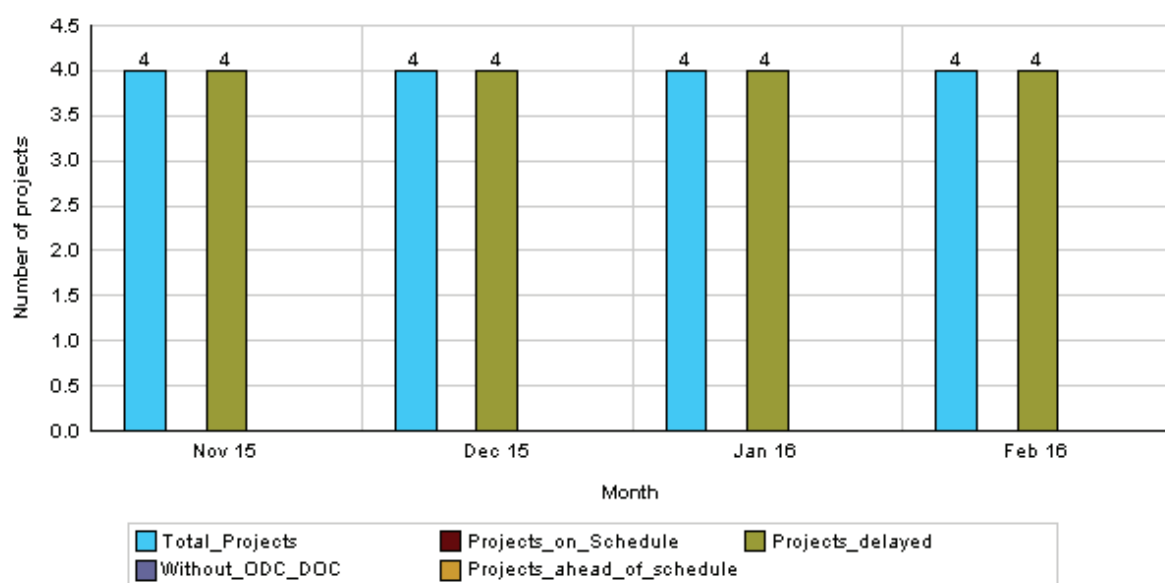


Break-up of 4 Delayed projects in February 2016

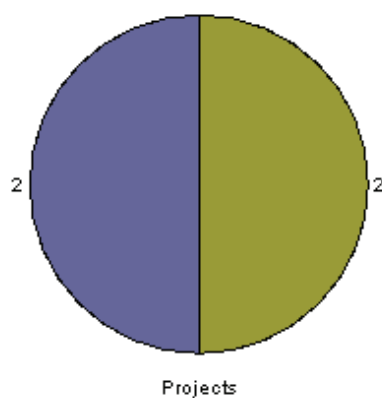


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12				
13-24				
25-60				
MORE THAN 60				


Graphical Presentation of CIVIL AVIATION Sector

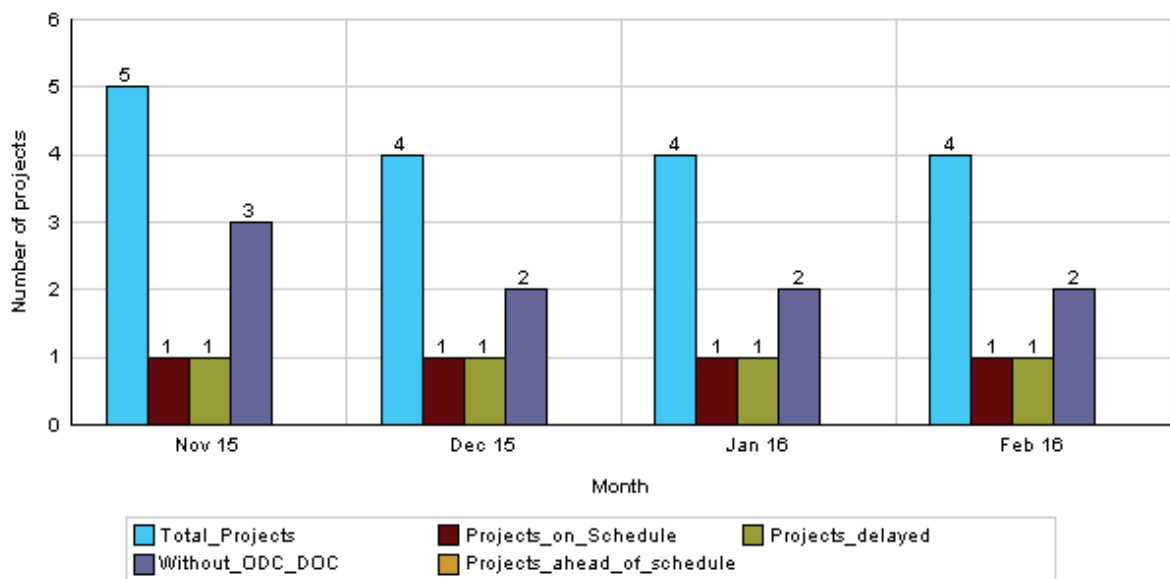


Break-up of 1 Delayed projects in February 2016

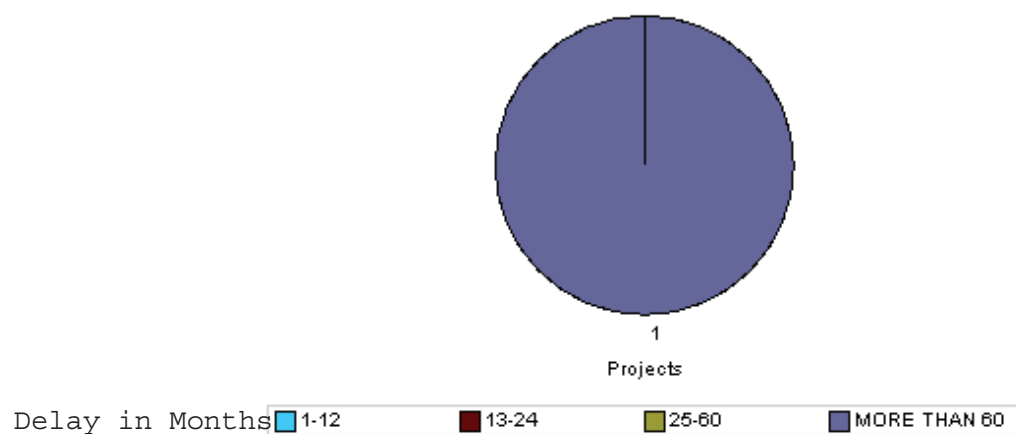


Graphical Presentation of COAL Sector

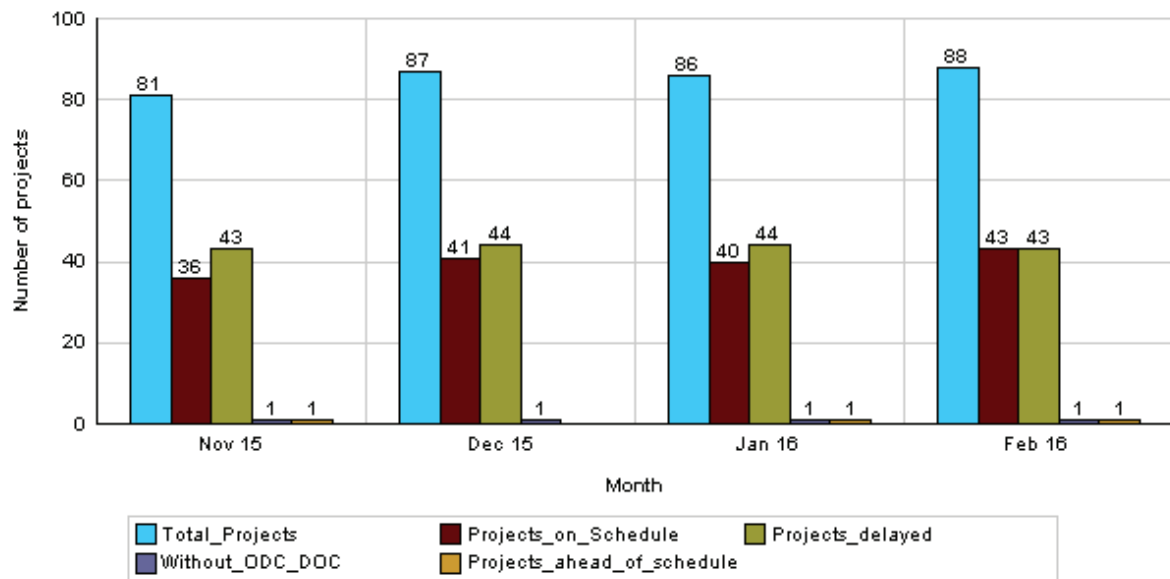


Break-up of 43 Delayed projects in February 2016

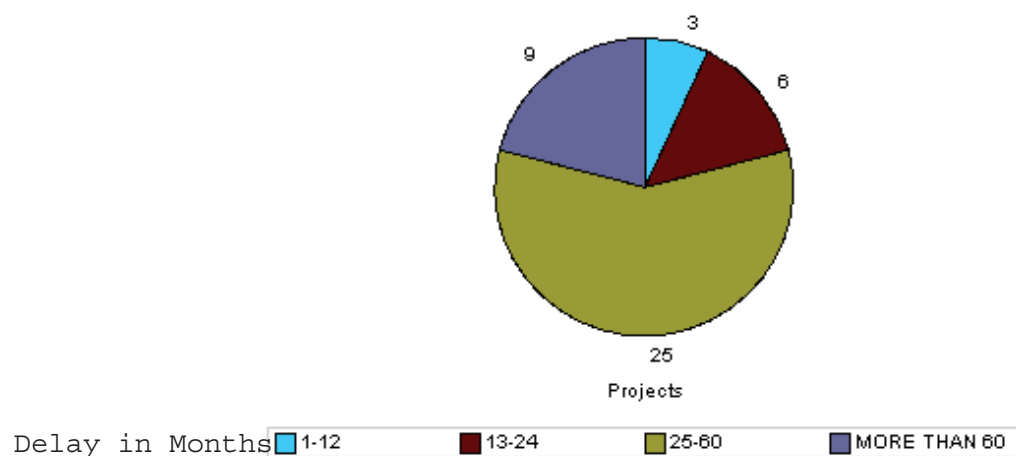


Graphical Presentation of STEEL Sector

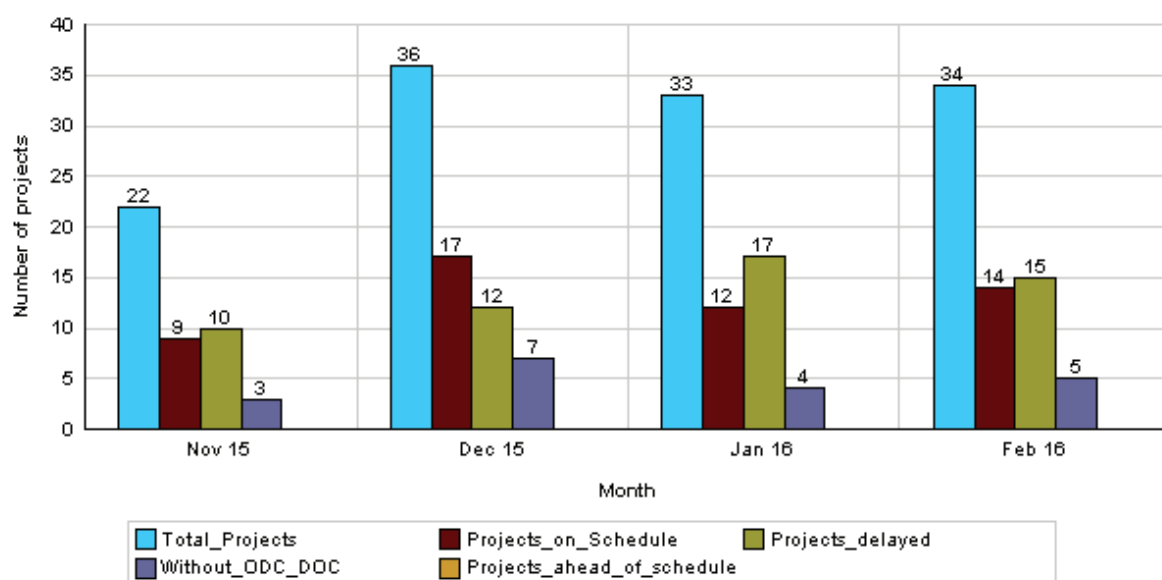


Break-up of 15 Delayed projects in February 2016

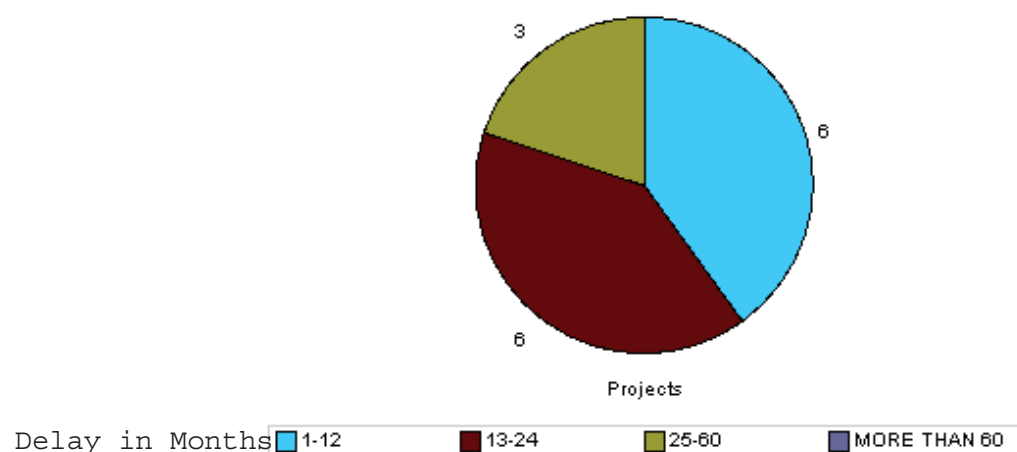

Graphical Presentation of PETROLEUM Sector

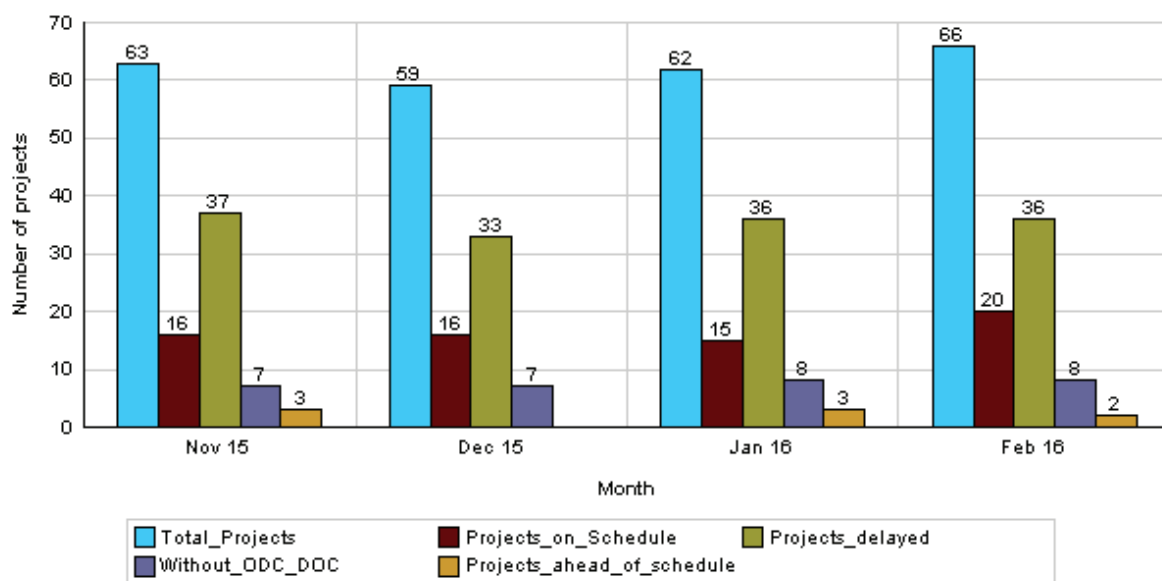


Break-up of 36 Delayed projects in February 2016

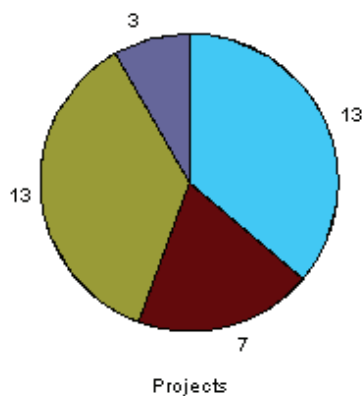


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of POWER Sector

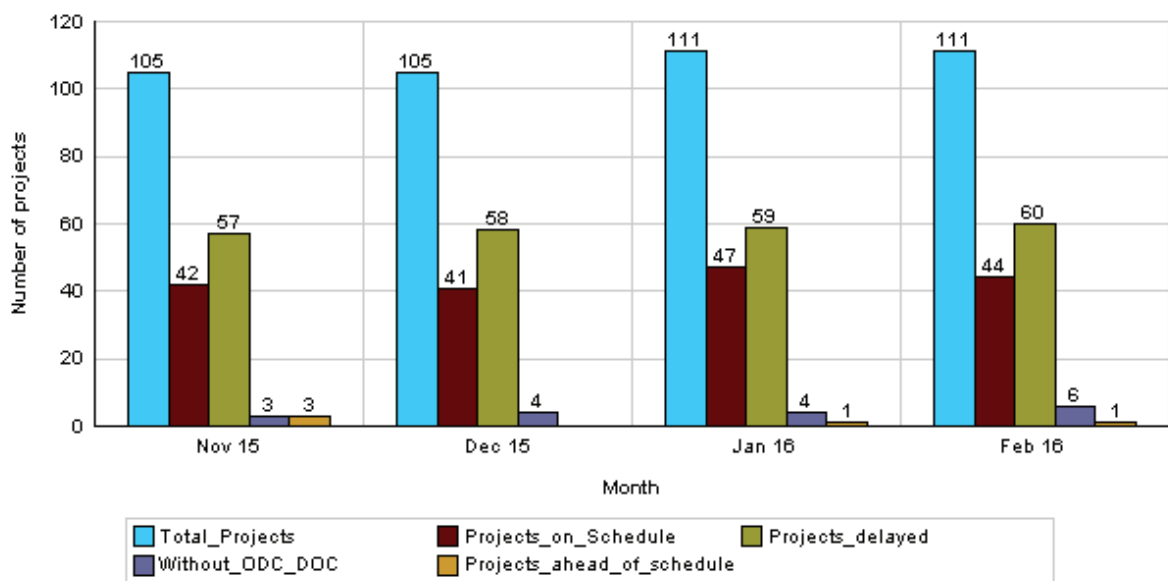


Break-up of 60 Delayed projects in February 2016

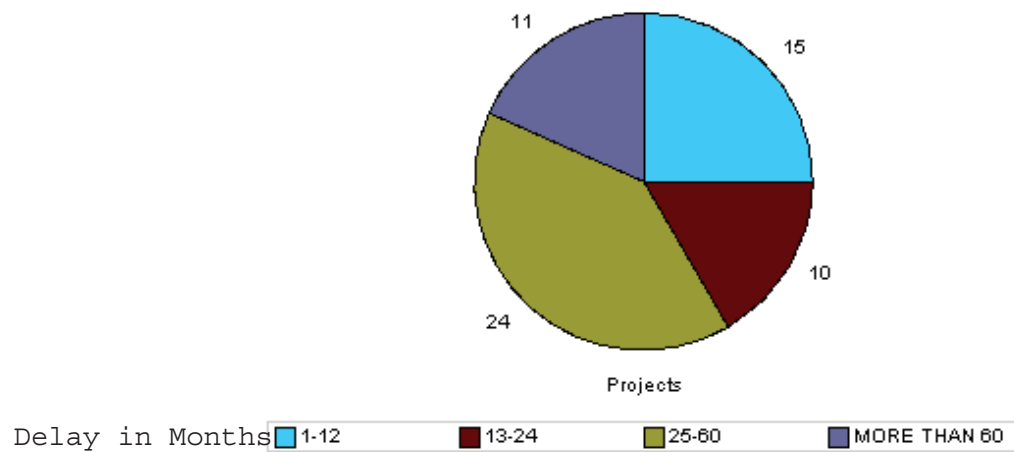

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

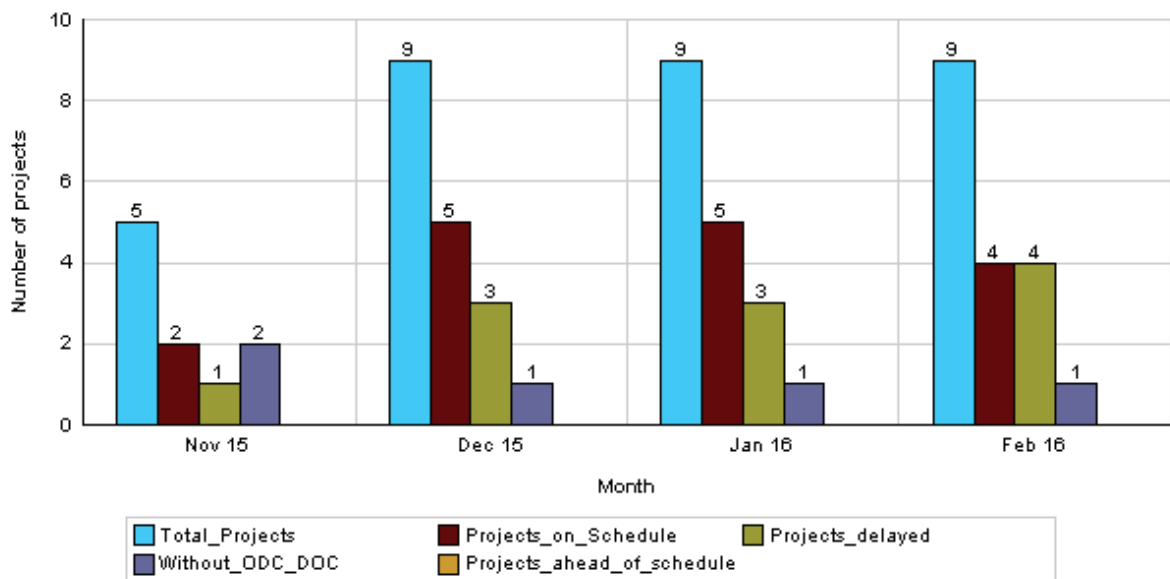


Break-up of 4 Delayed projects in February 2016

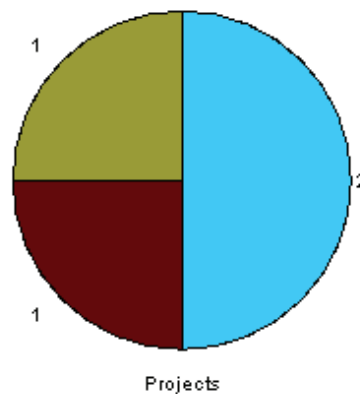


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of RAILWAYS Sector

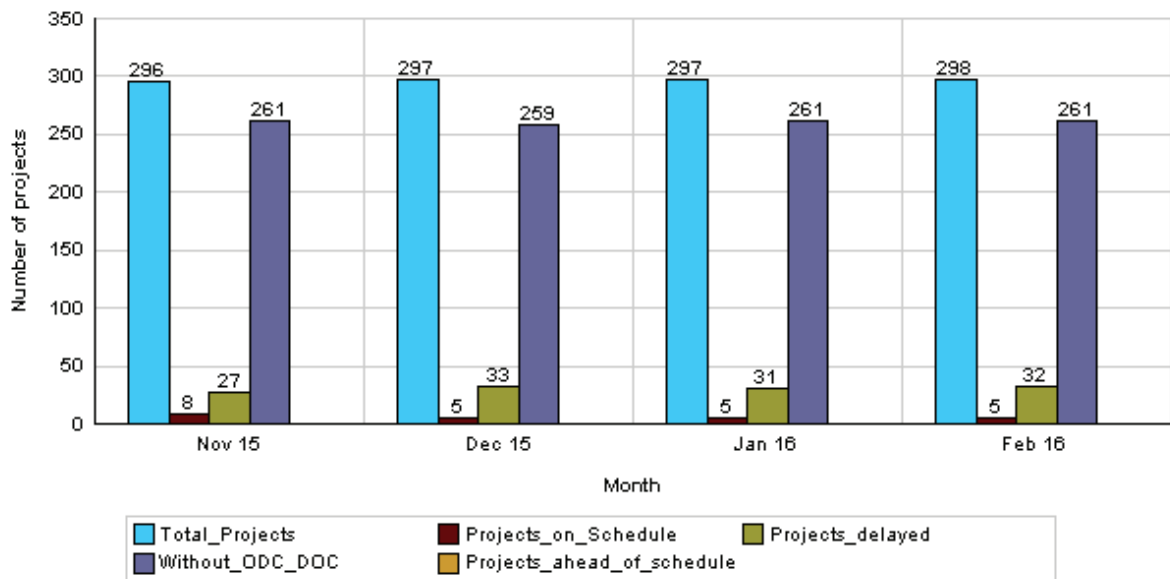


Break-up of 32 Delayed projects in February 2016

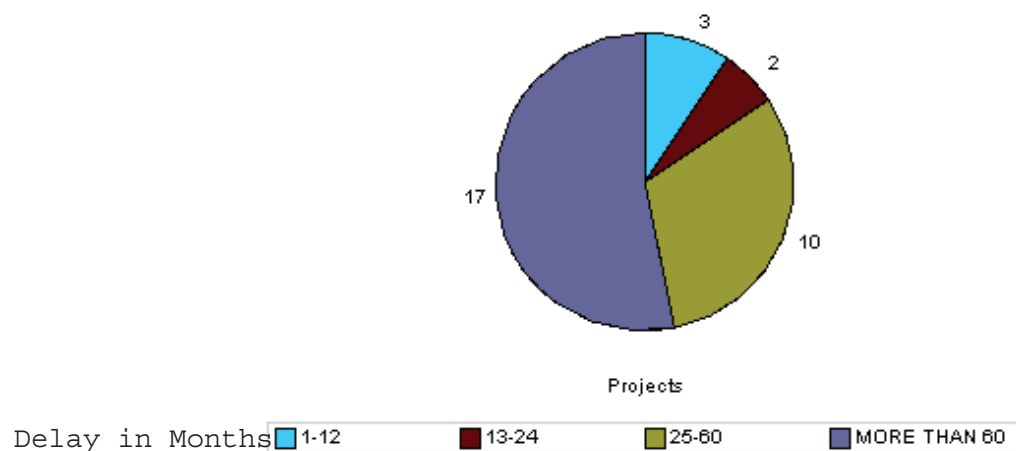


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

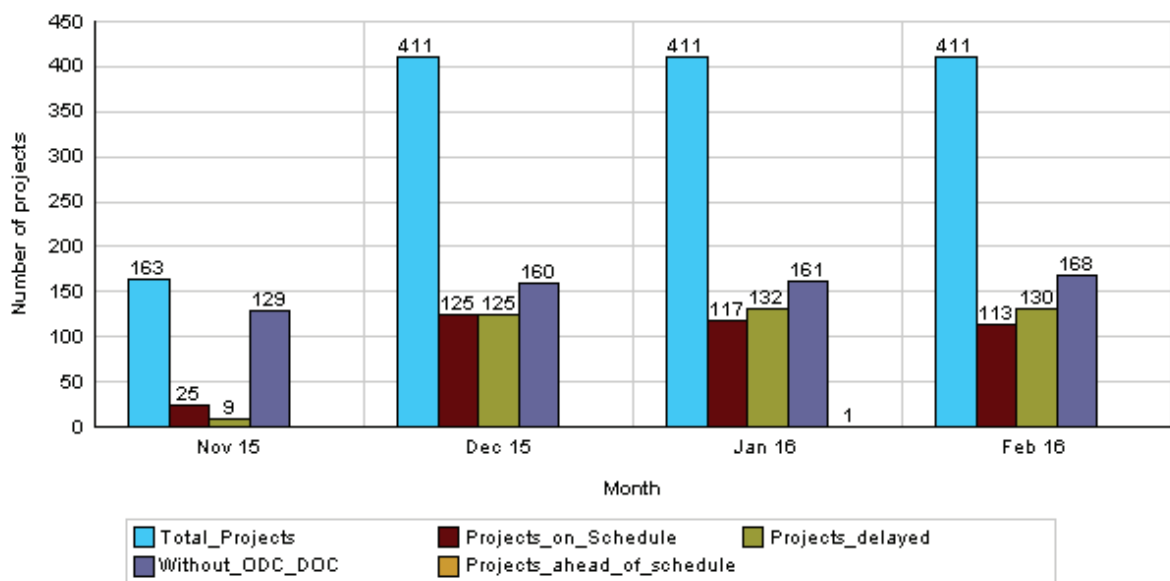


Break-up of 130 Delayed projects in February 2016

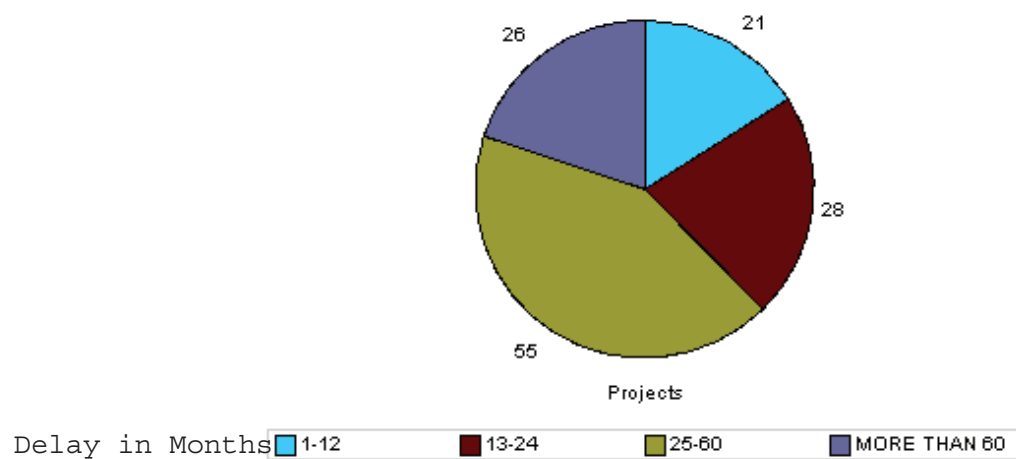


Graphical Presentation of SHIPPING AND PORTS Sector

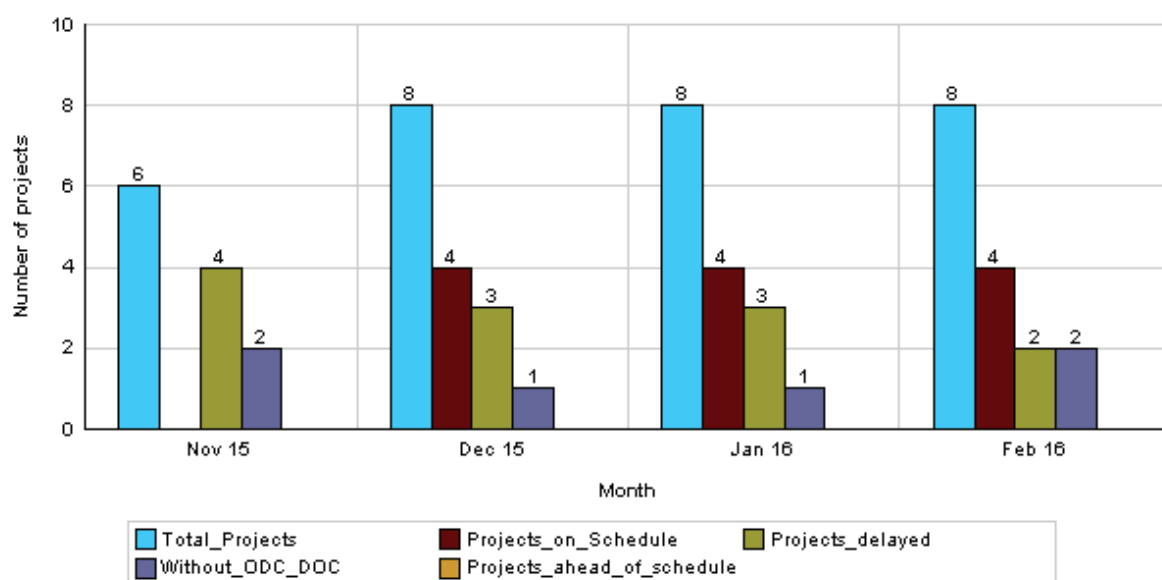


Break-up of 2 Delayed projects in February 2016

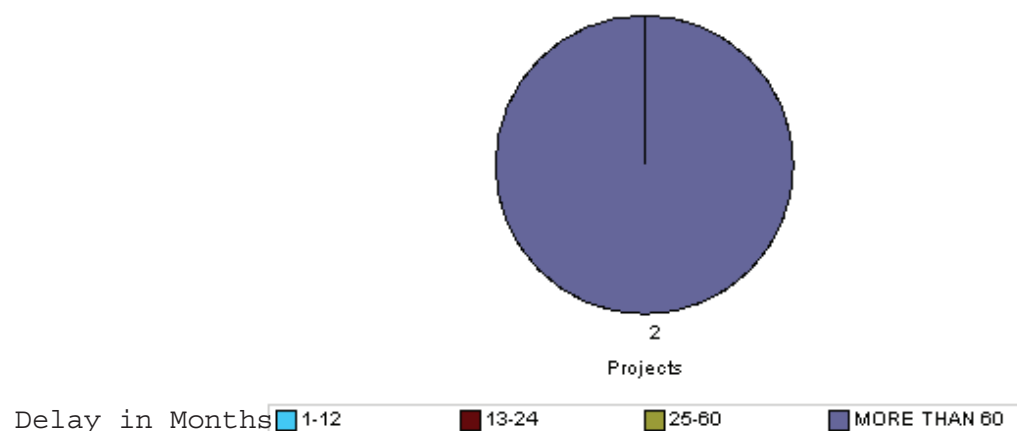

Graphical Presentation of TELECOMMUNICATIONS Sector

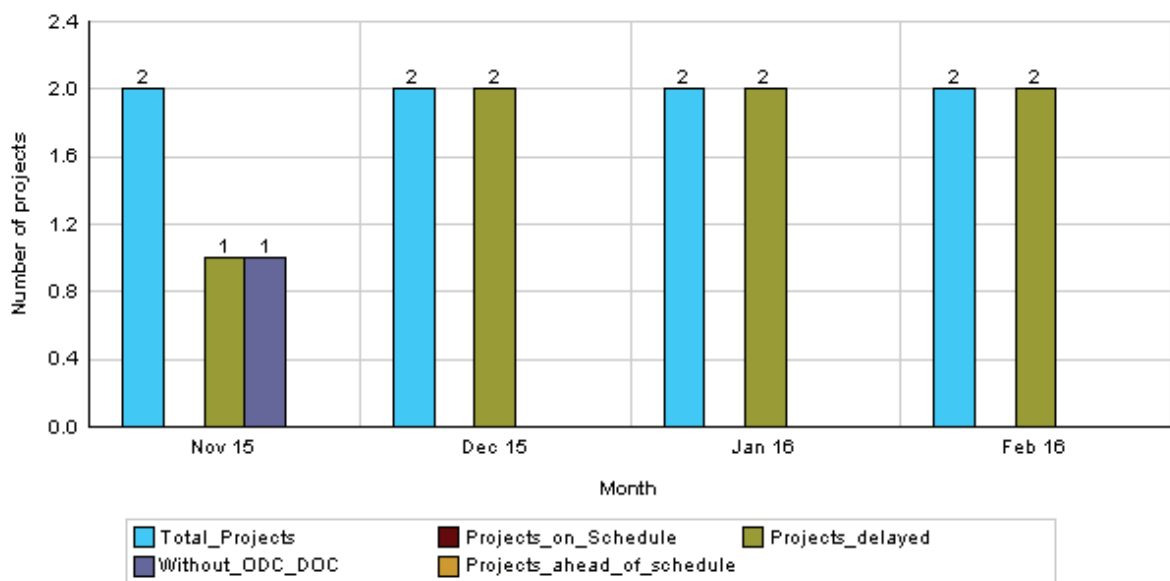


Break-up of 2 Delayed projects in February 2016

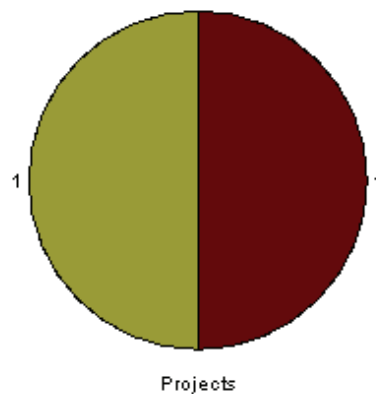


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

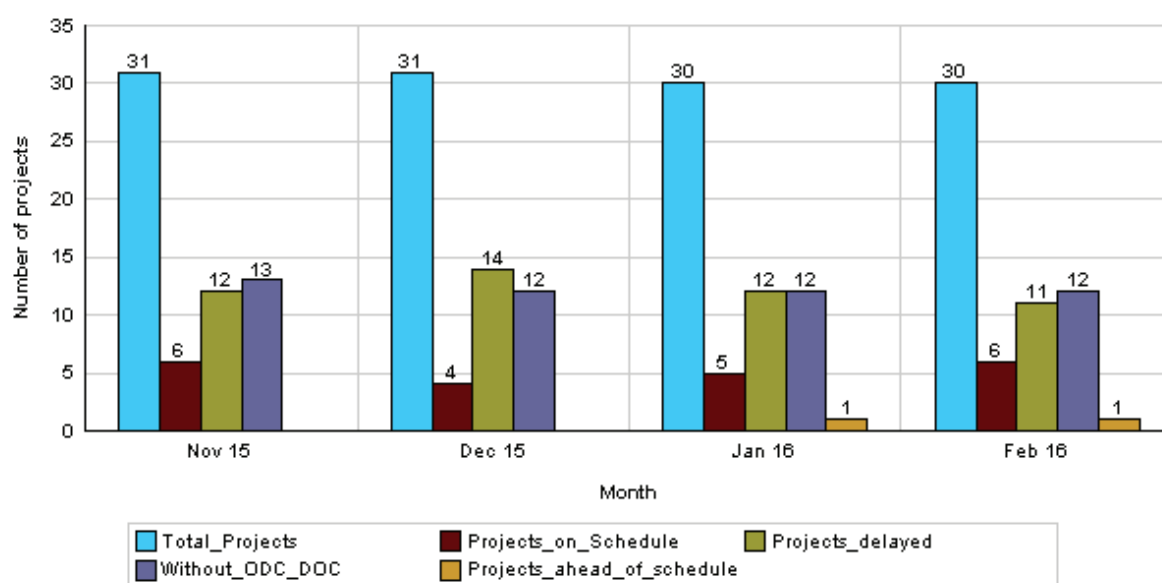

Break-up of 11 Delayed projects in February 2016

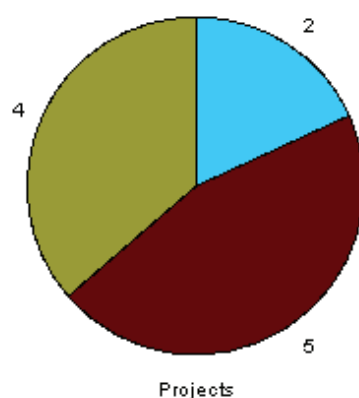

Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	39,893.65
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	776.37
COAL	88	60,408.62	60,379.03	61,521.55	13,803.48
FERTILISERS	1	197.79	209.44	209.44	52.22
MINES	3	2,555.63	2,555.63	2,555.63	6.61
STEEL	34	54,044.86	54,415.36	54,574.30	30,103.02
PETROCHEMICALS	1	5,460.61	8,920.00	9,965.00	9,241.36
PETROLEUM	66	137,131.44	143,178.74	145,764.07	68,558.74
POWER	111	304,580.02	332,768.53	353,192.66	185,284.79
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	1,018.40
RAILWAYS	298	254,176.67	275,766.45	329,512.54	93,586.56
ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,231.68	250,520.01	81,738.36
SHIPPING AND PORTS	8	4,117.75	4,258.80	5,048.81	1,826.73
TELECOMMUNICATIONS	2	15,445.17	15,445.17	15,345.17	2,720.00
URBAN DEVELOPMENT	30	134,055.93	134,018.53	139,282.13	37,447.76
Grand total	1071	1,266,248.36	1,332,146.79	1,426,985.93	566,058.05

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(February 2016)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU , .	12/2001	13,171.00 17,270.00	22,462.00	21,160.00	12/2008 10/2013	05/2016	89(O) 31(R)	54/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , .	09/2003	3,492.00 -	5,677.00	5,166.65	09/2010 -	09/2016	72(O) -	12/88
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT , .	10/2009	11,459.00 -	11,459.00	7,917.00	12/2015 10/2016	11/2018	35(O) 25(R)	41/70
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , .	10/2009	12,320.00 -	12,320.00	5,650.00	12/2016 03/2017	12/2019	36(O) 33(R)	29/69
	Total		40,442.00 -	51,918.00	39,893.65				136/329
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA , .	05/2010	335.61 -	318.00	305.01	05/2012 -	03/2015	-	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , .	01/2009	309.46 -	309.46	417.66	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE , .	10/2012	217.60 -	244.10	30.74	03/2015 -	09/2015	-	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , .	10/2013	314.61 -	314.61	22.96	09/2018 -	09/2018	0(O) -	0/0
	Total		1,177.28 -	1,186.17	776.37				0/0
	COAL								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA , .	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , .	01/2005	302.96 -	302.96	302.92	03/2010 -	03/2017	84(O) -	8/10
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH , .	06/2010	2,675.67 -	2,675.67	2,006.46	03/2014 -	03/2016	24(O) -	11/16
12	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND , .	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72(O) -	2/5
13	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH , .	06/2011	789.88 741.62	741.62	504.99	03/2013 -	03/2016	36(O) -	2/5
14	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , .	08/2013	7,612.33 7,612.33	7,612.33	800.01	03/2023 03/2023	03/2023	0(O) 0(R)	2/17
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH , .	12/2009	1,352.04 1,143.54	1,143.54	820.31	03/2016 -	03/2016	0(O) -	4/6
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , .	08/2008	706.40 -	706.40	79.03	07/2012 -	03/2021	104(O) -	1/3

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA , .	12/2009	212.34 -	1,228.39	869.37	03/2013 -	03/2016	36(O) -	21/22
18	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , .	10/2006	249.03 -	249.03	118.02	03/2012 -	03/2018	72(O) -	30/42
19	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL , .	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72(O) -	9/15
20	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , .	10/2007	259.40 486.57	486.57	91.86	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , .	12/2007	490.10 -	490.10	205.40	03/2017 -	03/2017	0(O) -	11/11
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , .	12/2007	457.77 -	457.77	210.87	03/2013 -	03/2017	48(O) -	8/9
23	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA , .	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
24	TALABIRA OCP - [N06000043]MCL,ODISHA , .	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
25	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , .	12/2007	172.08 -	172.08	152.05	03/2010 -	03/2017	84(O) -	2/4
26	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , .	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
27	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , .	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51(O) -	11/44
28	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH , .	08/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023	0(O) -	1/9
29	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , .	09/2014	441.82 -	441.82	141.38	03/2020 -	03/2020	0(O) -	5/13
30	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , .	08/2008	207.28 -	207.28	207.71	03/2012 -	03/2017	60(O) -	4/5
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , .	11/2008	479.53 -	479.53	185.34	03/2013 -	03/2017	48(O) -	4/8
32	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , .	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/6
33	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , .	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
34	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , .	12/2009	418.97 -	489.62	457.41	03/2012 -	03/2023	132(O) -	0/2
35	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , .	03/2010	209.78 -	209.78	85.26	03/2015 -	03/2016	12(O) -	8/31
36	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , .	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48(O) -	5/6
37	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , .	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48(O) -	4/7
38	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , .	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016	0(O) -	3/7
39	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND , .	08/2007	163.51 -	163.51	36.16	03/2011 -	03/2016	60(O) -	0/3
40	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND , .	12/2007	179.87 -	179.87	94.84	03/2012 -	03/2017	60(O) -	3/3
41	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND , .	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48(O) -	4/4

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , .	08/2008	264.68 -	264.68 -	146.05 -	03/2012 -	03/2016	48(O) -	2/4
43	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , .	12/2009	510.85 -	510.85 -	224.70 -	03/2016 -	03/2016	0(O) -	2/4
44	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , .	06/2009	162.46 -	162.46 -	70.25 -	03/2014 -	03/2017	36(O) -	3/4
45	KISTARAM OCP - [N06000089]SCCL,TELANGANA , .	11/2010	242.29 -	242.29 -	8.03 -	03/2015 -	03/2018	36(O) -	0/5
46	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , .	06/2011	1,131.28 1,131.28	1,131.28 -	165.06 -	03/2018 -	03/2018	0(O) -	6/9
47	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , .	07/2011	162.76 -	162.76 -	1.31 -	03/2015 -	03/2018	36(O) -	4/29
48	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , .	07/2011	447.06 -	447.06 -	77.44 -	03/2015 -	03/2018	36(O) -	4/13
49	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , .	02/2011	339.88 -	339.88 -	12.46 -	04/2014 -	03/2016	23(O) -	4/7
50	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , .	04/2012	258.56 -	258.56 -	102.72 -	03/2016 -	03/2018	24(O) -	3/6
51	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , .	06/2012	365.01 -	365.01 -	6.56 -	06/2015 -	03/2017	21(O) -	18/51
52	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , .	07/2012	417.33 -	417.33 -	25.28 -	07/2016 -	03/2017	8(O) -	6/28
53	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , .	11/2012	430.45 -	486.27 -	93.51 -	03/2016 -	03/2018	24(O) -	7/39
54	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , .	02/2012	858.11 -	858.11 -	109.63 -	03/2020 -	03/2020	0(O) -	3/3
55	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , .	12/2013	610.63 -	610.63 -	- -	03/2022 -	03/2022	0(O) -	1/7
56	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , .	02/2014	555.52 -	555.52 -	3.52 -	03/2021 -	03/2017	-48(O) -	0/2
57	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , .	04/2012	364.75 -	364.75 -	196.19 -	10/2014 -	03/2016	17(O) -	8/10
58	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , .	05/2014	164.49 -	164.49 -	76.43 -	03/2020 -	03/2020	0(O) -	3/6
59	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , .	05/2014	479.15 -	479.15 -	10.89 -	03/2019 -	03/2019	0(O) -	1/9
60	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , .	05/2014	3,756.36 -	3,756.36 -	620.96 -	03/2026 -	03/2026	0(O) -	3/15
61	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , .	05/2014	337.66 -	337.66 -	0.74 -	03/2019 -	03/2019	0(O) -	2/6
62	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , .	06/2014	289.03 -	289.03 -	- -	03/2018 -	03/2018	0(O) -	1/5
63	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , .	11/2014	1,375.38 -	1,375.38 -	179.12 -	03/2021 -	03/2021	0(O) -	1/9
64	DINESH OCP - [N06000118]WCL,MAHARASHTRA , .	11/2014	611.16 -	611.16 -	224.02 -	03/2020 -	03/2020	0(O) -	3/15
65	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , .	09/2014	266.23 -	266.23 -	101.81 -	03/2021 -	03/2021	0(O) -	4/14
66	GOKUL - [N06000120]WCL,MAHARASHTRA , .	11/2014	267.67 -	267.67 -	185.72 -	03/2018 -	03/2018	0(O) -	2/8

Sector Wise Details

(February 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
67	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA , .	02/2015	187.94 -	187.94	53.93	03/2023 -	03/2023	0(O) -	6/10
68	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , .	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
69	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , .	02/2015	335.97 -	335.97	34.09	03/2018 -	03/2018	0(O) -	1/4
70	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , .	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021	0(O) -	0/7
71	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , .	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021	0(O) -	0/6
72	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , .	05/2015	295.56 -	295.56	73.30	03/2019 -	03/2019	0(O) -	4/14
73	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA , .	05/2015	397.09 -	397.09	0.05	03/2019 -	03/2019	0(O) -	5/18
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , .	06/2015	205.49 -	205.49	1.37	03/2020 -	03/2020	0(O) -	4/12
75	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , .	06/2015	483.69 -	483.69	48.58	03/2021 -	03/2021	0(O) -	3/8
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , .	08/2015	727.28 -	727.28	66.37	03/2025 -	03/2025	0(O) -	3/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , .	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	3/9
78	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , .	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
79	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH , .	07/2015	316.10 -	316.10	16.87	03/2020 -	03/2020	0(O) -	0/5
80	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH , .	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	0/8
81	MALACHUA OPENCAS PROJECT - [N06000139]SECL,MADHYA PRADESH , .	10/2015	488.33 -	488.33	-	03/2023 -	03/2023	0(O) -	0/8
82	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH , .	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/0
83	KAMPTTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , .	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/9
84	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , .	11/2015	498.42 -	498.42	-	03/2018 -	03/2018	0(O) -	1/9
85	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , .	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022	0(O) -	0/24
86	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	0(O) -	0/0
87	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , .	06/2011	5,907.11 -	5,907.11	1,499.01	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
88	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , .	08/2011	1,230.27 -	1,230.27	48.66	04/2015 04/2019	04/2019	48(O) 0(R)	1/6
89	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , .	08/2011	988.35 -	988.35	45.27	04/2017 -	04/2017	0(O) -	0/3
90	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL , .	08/2012	1,055.05 -	1,055.05	206.70	03/2018 -	07/2018	4(O) -	5/15
91	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , .	04/2013	1,458.17 -	1,458.17	21.91	06/2015 08/2019	08/2019	50(O) 0(R)	1/7

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
92	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND , .	09/2009	153.82 -	153.82	75.24	03/2014 -	09/2016	30(O) -	6/9
93	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.56	09/2019 -	09/2019	0(O) -	0/0
94	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND , .	08/2010	289.45 -	289.45	104.25	05/2014 -	10/2016	29(O) -	0/8
95	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND , .	10/2012	269.82 -	269.82	69.89	04/2014 -	11/2016	31(O) -	0/10
96	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	67.23	12/2019 -	12/2019	0(O) -	0/0
	Total		60,408.62 -	61,521.55	13,803.48				324/1016
	<u>FERTILISERS</u>								
97	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA , .	10/2014	197.79 209.44	209.44	52.22	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	209.44	52.22				0/0
	<u>MINES</u>								
98	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL, MADHYA PRADESH , .	09/2011	1,856.00 -	1,856.00	6.61	09/2017 -	09/2017	0(O) -	0/0
99	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO, MAHARASHTRA , Private	12/2015	355.13 -	355.13	-	11/2016 -	11/2016	0(O) -	0/0
100	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO, RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 -	344.50	-	11/2016 -	11/2016	0(O) -	0/0
	Total		2,555.63 -	2,555.63	6.61				0/0
	<u>STEEL</u>								
101	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL, ANDHRA PRADESH , .	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
102	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL, GUJARAT , .	01/2013	175.00 -	175.00	-	- -	-	-	0/0
103	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR , .	10/2005	956.00 -	956.00	-	03/2015 -	-	-	0/0
104	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATTISGARH , .	07/2012	332.65 -	332.65	233.55	08/2014 -	03/2016	19(O) -	4/5
105	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL, JHARKHAND , .	03/2015	255.19 -	255.19	22.05	03/2018 -	03/2018	0(O) -	0/0
106	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA , .	03/2007	149.73 173.00	175.94	175.94	12/2015 -	03/2017	15(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , .	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014 -	03/2016	25(O) -	0/0
108	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , .	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3(O) -	0/0
109	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , .	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
110	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , .	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
111	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	-	03/2016 -	03/2016	0(O) -	0/0
112	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , .	04/2015	3,127.30 -	3,127.30	303.25	04/2018 -	04/2018	0(O) -	0/0
113	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , .	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
114	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA , .	04/2011	572.00 -	572.00	488.54	04/2013 09/2014	06/2015	-	18/19
115	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA , .	12/2011	187.33 -	187.33	174.45	10/2013 -	06/2016	32(O) -	2/5
116	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH , .	05/2012	404.16 -	404.16	285.39	07/2015 -	06/2017	23(O) -	0/1
117	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , .	12/2009	343.00 -	488.40	39.17	10/2016 -	06/2017	8(O) -	0/0
118	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , .	12/2007	253.92 254.00	253.92	193.97	06/2016 -	06/2016	0(O) -	0/0
119	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , .	10/2011	175.49 207.00	206.71	134.61	12/2016 -	07/2017	7(O) -	0/0
120	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA , .	02/2011	898.55 -	898.55	418.89	05/2013 01/2015	08/2015	-	19/20
121	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , .	07/2011	877.73 -	877.73	454.15	07/2015 -	08/2016	13(O) -	2/2
122	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA , .	06/2014	708.91 -	708.91	326.57	04/2016 -	09/2016	5(O) -	2/2
123	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , .	12/2009	280.00 -	280.00	28.55	09/2016 -	09/2016	0(O) -	1/1
124	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , .	04/2014	151.33 -	151.33	4.84	09/2017 -	09/2017	0(O) -	0/0
125	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , .	03/2015	1,034.01 -	1,034.01	26.98	10/2017 -	10/2017	0(O) -	0/0
126	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , .	08/2010	17,265.00 -	17,265.00	15,636.77	03/2013 -	11/2016	44(O) -	32/35

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
127	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , .	10/2013	245.67 -	245.67	98.57	05/2016 -	12/2016	7(O) -	1/3
128	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , .	04/2014	188.93 -	188.93	60.23	04/2015 -	12/2016	20(O) -	2/3
129	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH , .	01/2010	15,525.00 -	15,525.00	8,727.80	05/2015 12/2016	12/2016	19(O) 0(R)	32/81
130	3RD CONVERTER AND 4TH CASTER - [N12000088]JINL,ANDHRA PRADESH , .	07/2011	974.76 -	974.76	234.67	07/2016 -	12/2016	5(O) -	0/1
131	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND , .	05/2015	1,154.18 -	1,154.18	28.20	12/2017 -	12/2017	0(O) -	0/0
132	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA , .	12/2007	202.61 227.00	227.00	196.12	12/2016 -	12/2016	0(O) -	0/0
133	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , .	02/2014	787.29 -	787.29	251.53	12/2016 -	12/2016	0(O) -	0/0
134	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , .	02/2014	4,749.00 -	4,749.00	3.63	09/2017 -	09/2017	0(O) -	0/0
	Total		54,044.86 -	54,574.30	30,103.02				115/178
	<u>PETROCHEMICALS</u>								
135	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM , .	04/2006	5,460.61 8,920.00	9,965.00	9,241.36	04/2012 12/2013	12/2015	-	23/26
	Total		5,460.61 -	9,965.00	9,241.36				23/26
	<u>PETROLEUM</u>								
136	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU , .	05/2013	711.00 -	711.00	7.70	- -	-	-	0/0
137	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU , .	11/2006	171.83 -	171.83	-	- -	-	-	0/0
138	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE , .	01/2015	1,823.00 -	1,823.00	1.34	- -	-	-	0/0
139	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE , .	01/2015	2,321.00 -	2,321.00	2.04	- -	-	-	0/0
140	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE , .	02/2015	890.00 -	890.00	1.92	- -	-	-	0/0
141	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE , .	04/2010	270.00 -	251.66	172.53	06/2012 -	01/2016	-	0/0
142	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	24.29	01/2018 -	01/2018	0(O) -	0/61
143	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	181.02	78.73	01/2017 -	01/2017	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
144	PARADIP REFINERY PROJECT - [N1600058]IOCL,ODISHA , .	02/2009	29,777.00 34,555.00	34,555.00	31,300.53	11/2012 11/2013	02/2016	39(O) 27(R)	96/100
145	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE , .	06/2009	2,915.00 -	2,915.00	1,381.31	12/2012 -	02/2019	74(O) -	7/14
146	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA , .	10/2015	607.06 714.25	714.25	84.88	10/2017 02/2018	02/2018	4(O) 0(R)	21/48
147	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	41.18	02/2020 -	02/2020	0(O) -	0/0
148	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM , .	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
149	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE , .	12/2009	463.32 -	463.32	322.07	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
150	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA , .	03/2012	2,592.17 2,592.17	2,592.17	1,130.50	05/2014 03/2017	03/2017	34(O) 0(R)	0/21
151	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU , .	12/2012	279.00 -	279.00	187.05	12/2014 -	03/2016	15(O) -	58/58
152	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE , .	12/2009	309.81 462.79	462.79	265.72	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
153	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA , .	01/2006	732.00 1,227.00	1,227.00	1,091.39	10/2011 -	03/2016	53(O) -	0/0
154	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE , .	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2018	12(O) -	0/0
155	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA , .	11/2014	6,068.80 -	6,068.80	826.03	04/2019 -	03/2019	-1(O) -	0/0
156	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI , .	08/2014	6,086.08 -	6,086.08	673.95	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
157	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA , .	03/2014	238.50 -	238.50	7.30	03/2017 -	03/2017	0(O) -	0/0
158	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA , .	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
159	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 -	500.00	-	03/2017 -	03/2017	0(O) -	0/0
160	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA , .	03/2011	861.79 1,256.72	1,256.72	1,011.65	05/2013 04/2016	04/2016	35(O) 0(R)	1/5
161	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU , .	05/2015	257.87 -	257.87	34.87	11/2016 -	04/2017	5(O) -	10/22
162	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018	0(O) -	0/0
163	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA , .	12/2011	2,059.63 2,665.65	2,665.65	1,325.28	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
164	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE , .	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
165	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE , .	01/2012	352.49 -	352.49	138.84	03/2014 05/2016	05/2016	26(O) 0(R)	0/3

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
166	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA , .	03/2012	14,225.00 -	16,504.00	10,366.19	05/2016 -	05/2016	0(O) -	0/30
167	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA , .	03/2013	1,138.50 686.58	686.58	586.26	04/2015 05/2016	05/2016	13(O) 0(R)	0/0
168	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA , .	01/2006	993.00 1,693.00	1,693.00	1,449.53	01/2012 -	05/2016	52(O) -	0/0
169	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE , .	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
170	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA , .	06/2014	5,706.47 5,813.25	5,813.25	2,954.21	05/2017 05/2017	05/2017	0(O) 0(R)	6/16
171	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , .	02/2015	2,899.93 2,098.43	2,098.43	641.31	05/2017 -	05/2017	0(O) -	0/0
172	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE , .	08/2009	1,793.00 -	1,793.00	1,327.98	09/2012 -	06/2016	45(O) -	6/7
173	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA , .	12/2009	1,584.00 -	1,584.00	1,321.77	08/2015 -	06/2016	10(O) -	3/12
174	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT , .	03/2009	317.64 -	240.95	127.15	09/2012 06/2016	06/2016	45(O) 0(R)	0/5
175	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE , .	08/2011	586.00 -	586.00	433.56	08/2015 -	06/2016	10(O) -	3/12
176	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH , .	07/2014	419.04 -	419.04	314.92	01/2017 -	06/2016	-7(O) -	13/16
177	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , .	09/2011	202.25 -	160.16	75.40	07/2016 -	07/2016	0(O) -	5/12
178	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM , .	02/2014	163.88 -	163.00	58.18	07/2016 -	07/2016	0(O) -	4/6
179	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT , .	12/2011	160.00 -	160.00	51.55	02/2016 02/2016	07/2016	5(O) 5(R)	0/0
180	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , .	09/2012	871.35 -	1,200.00	559.57	03/2015 11/2015	08/2016	17(O) 9(R)	0/5
181	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , .	03/2014	3,150.00 -	3,150.00	112.97	09/2017 -	09/2017	0(O) -	0/0
182	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH , .	01/2011	141.86 -	232.00	170.03	09/2016 -	09/2016	0(O) -	0/12
183	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	195.63	-	09/2018 -	09/2018	0(O) -	0/0
184	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , .	06/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016	61(O) 0(R)	0/0
185	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR , .	04/2013	480.00 -	422.00	179.18	02/2016 -	10/2016	8(O) -	5/6
186	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , .	11/2011	310.00 370.00	370.00	0.37	03/2013 10/2016	10/2016	43(O) 0(R)	0/0
187	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA , .	02/2012	666.00 838.08	838.08	579.21	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
188	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , .	02/2011	3,110.36 -	3,110.36	1,494.16	11/2015 07/2016	11/2016	12(O) 4(R)	47/52
189	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , .	05/2015	1,671.22 1,881.22	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
190	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , .	07/2009	3,957.00 3,561.00	3,561.00	85.47	01/2013 12/2018	12/2018	71(O) 0(R)	11/38
191	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , .	02/2011	913.00 -	913.00	493.61	08/2015 -	12/2016	16(O) -	0/0
192	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , .	05/2013	4,124.35 4,124.35	4,124.35	633.74	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
193	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , .	03/2014	3,076.00 -	3,076.00	212.27	09/2017 03/2018	12/2017	3(O) -3(R)	0/0
194	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE , .	03/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018	0(O) -	3/8
195	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , .	03/2009	228.64 -	214.19	142.35	12/2016 -	12/2016	0(O) -	0/0
196	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , .	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5(O) -	1/39
197	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE , .	10/2011	725.00 -	725.00	147.98	11/2016 -	12/2016	1(O) -	0/14
198	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , .	05/2015	2,443.00 -	2,443.00	120.23	12/2017 -	12/2017	0(O) -	0/0
199	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	4,619.94	420.28	12/2017 -	12/2017	0(O) -	0/0
200	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , .	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
201	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , .	04/2011	191.96 -	191.96	105.94	05/2015 -	-	-	0/12
	Total		137,131.44 -	145,764.07	68,558.74				371/776
	POWER								
202	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , .	02/2010	232.34 -	232.34	215.89	06/2012 -	-	-	1/4
203	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , .	10/2011	487.49 639.46	639.46	436.52	06/2014 03/2016	-	-	10/12
204	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH , .	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
205	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND , .	07/2012	1,527.00 -	1,527.00	143.00	08/2017 -	-	-	0/9
206	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , .	07/2009	421.01 1,007.57	1,007.57	961.14	07/2013 01/2016	01/2016	-	25/26
207	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , .	01/2013	12,964.60 -	12,964.60	5,361.60	01/2018 -	01/2018	0(O) -	23/25
208	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , .	08/2014	288.49 -	288.49	71.60	02/2017 -	02/2017	0(O) -	0/12

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
209	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , .	02/2014	14,366.58 -	14,366.58	2,449.00	02/2019 -	02/2019	0(O) -	11/13
210	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , .	05/2011	195.42 -	195.42	55.26	02/2014 -	02/2018	48(O) -	1/1
211	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , .	01/2008	4,375.35 6,749.18	6,749.18	5,824.00	09/2011 -	03/2017	66(O) -	19/37
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE , .	02/2009	410.29 -	410.29	366.37	02/2012 -	03/2016	49(O) -	7/10
213	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL , .	04/2010	4,404.57 -	4,404.57	2,498.65	01/2015 -	03/2017	26(O) -	8/16
214	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE , .	03/2010	965.58 -	965.58	766.74	11/2012 -	03/2016	40(O) -	7/10
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE , .	08/2010	1,677.57 -	1,677.57	1,463.52	04/2013 -	03/2016	35(O) -	9/11
216	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE , .	03/2011	1,585.12 -	1,585.12	1,609.36	11/2013 -	03/2016	28(O) -	8/12
217	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , .	07/2010	1,272.80 -	1,272.80	1,254.53	11/2012 -	03/2017	52(O) -	8/13
218	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE , .	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	03/2016	19(O) -	9/14
219	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT , .	12/2011	552.44 609.44	609.44	590.10	02/2014 03/2016	03/2016	25(O) 0(R)	8/10
220	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE , .	02/2012	1,927.16 -	1,927.16	1,600.27	10/2014 -	03/2016	17(O) -	5/7
221	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , .	01/2012	15,166.19 -	15,166.19	10,325.00	01/2017 -	03/2017	2(O) -	30/39
222	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE , .	09/2012	524.40 -	524.40	333.82	05/2015 -	03/2016	10(O) -	8/12
223	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , .	06/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018	0(O) -	8/12
224	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH , .	08/2014	188.75 -	188.75	74.10	02/2017 -	03/2016	-11(O) -	0/2
225	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , .	09/2014	9,188.98 -	9,188.98	1,056.00	03/2019 -	03/2019	0(O) -	14/15
226	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE , .	01/2015	268.80 -	268.80	23.30	03/2018 -	03/2018	0(O) -	0/3
227	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , .	03/2015	197.40 -	197.40	-	03/2018 -	03/2018	0(O) -	0/0
228	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , .	03/2015	550.06 -	550.06	21.10	03/2018 -	03/2018	0(O) -	0/3

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
229	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR , .	03/2010	3,984.03 -	3,984.03	3,198.14	01/2013 -	03/2016	38(O) -	0/1
230	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL , .	04/2007	4,122.00 8,781.30	9,606.82	8,222.09	02/2011 -	03/2016	61(O) -	24/26
231	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , .	02/2015	302.49 302.00	302.49	268.27	02/2016 -	03/2016	1(O) -	0/1
232	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , .	01/2016	305.04 -	305.04	-	03/2017 -	03/2017	0(O) -	0/0
233	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE , .	06/2014	400.47 -	400.47	46.70	04/2017 -	04/2017	0(O) -	0/3
234	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , .	10/2014	8,112.12 -	8,112.12	121.97	04/2020 -	04/2020	0(O) -	0/0
235	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , .	12/2014	6,517.36 -	6,517.36	345.30	04/2018 -	04/2018	0(O) -	3/12
236	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , .	04/2015	3,705.61 -	3,705.61	258.10	04/2018 -	04/2018	0(O) -	4/9
237	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , .	04/2015	1,479.30 -	1,479.30	84.40	04/2017 -	04/2017	0(O) -	2/8
238	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , .	02/2005	8,692.97 15,095.67	15,095.67	11,241.00	01/2011 10/2014	05/2018	88(O) 43(R)	27/48
239	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE , .	05/2010	250.03 -	250.03	236.20	01/2013 -	05/2016	40(O) -	10/15
240	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE , .	09/2013	1,575.30 -	1,575.30	779.10	05/2016 -	05/2016	0(O) -	8/13
241	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA , .	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5(O) -	6/8
242	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE , .	01/2015	3,662.02 -	3,662.02	387.90	05/2018 -	05/2018	0(O) -	0/5
243	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , .	03/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017	0(O) -	0/9
244	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH , .	05/2015	312.94 -	312.94	26.50	05/2016 -	05/2016	0(O) -	0/0
245	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , .	01/2016	162.11 -	162.11	-	05/2018 -	05/2018	0(O) -	0/0
246	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE , .	02/2009	509.66 -	509.66	541.66	11/2011 -	06/2016	55(O) -	8/11
247	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE , .	12/2009	1,216.83 -	1,216.83	1,071.59	08/2012 -	06/2016	46(O) -	3/5
248	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE , .	07/2010	752.64 689.03	689.03	554.02	07/2013 11/2015	06/2016	35(O) 7(R)	7/9

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
249	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH, . .	05/2011	1,961.87 -	1,961.87	1,801.75	05/2014 -	06/2016	25(O) -	8/12
250	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU, . .	09/2011	1,940.13 -	1,940.13	1,959.76	09/2014 -	06/2016	21(O) -	8/13
251	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND, .	10/2011	558.26 -	558.26	537.51	11/2013 -	06/2016	31(O) -	8/12
252	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE, . .	12/2011	297.33 346.79	346.79	306.27	08/2014 06/2015	06/2016	22(O) 12(R)	8/10
253	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH, . .	01/2012	1,422.85 -	1,422.85	1,436.82	01/2015 -	06/2016	17(O) -	9/11
254	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE, . .	03/2012	198.63 -	198.63	96.23	09/2014 -	06/2016	21(O) -	0/0
255	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH, . .	03/2012	9,569.76 -	9,569.76	5,841.39	06/2015 -	06/2016	12(O) -	21/30
256	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE, . .	11/2011	723.63 -	723.63	598.32	11/2014 -	06/2016	19(O) -	7/10
257	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE, . .	02/2012	3,201.44 -	3,201.44	3,089.11	10/2014 -	06/2016	20(O) -	8/17
258	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATTISGARH, . .	12/2012	11,846.00 -	11,846.00	5,713.00	06/2017 -	06/2017	0(O) -	23/40
259	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE, . .	09/2013	680.69 -	680.69	466.89	03/2016 -	06/2016	3(O) -	10/12
260	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE, . .	10/2013	1,364.52 -	1,364.52	479.74	04/2016 -	06/2016	2(O) -	8/12
261	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL, MULTI STATE, . .	02/2014	539.82 -	539.82	125.20	06/2016 -	06/2016	0(O) -	8/11
262	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL, MULTI STATE, . .	02/2014	908.08 -	908.08	236.90	06/2016 -	06/2016	0(O) -	9/18
263	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE, .	03/2014	155.57 -	155.57	5.40	03/2016 -	06/2016	3(O) -	1/6
264	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE, . .	02/2014	196.58 -	196.58	25.30	02/2016 -	06/2016	4(O) -	7/17
265	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND, . .	08/2006	2,313.00 4,138.41	4,237.67	3,247.07	12/2011 03/2016	06/2016	54(O) 3(R)	12/13
266	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL, ODISHA, . .	01/2016	187.04 -	187.04	-	06/2018 -	06/2018	0(O) -	0/0
267	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH, . .	12/2004	2,496.90 6,179.96	6,179.96	4,401.09	12/2009 07/2016	07/2016	79(O) 0(R)	16/27
268	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH, . .	12/2008	573.99 1,262.27	1,262.27	1,111.17	08/2013 07/2016	07/2016	35(O) 0(R)	29/38

Sector Wise Details

(February 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
269	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE , .	05/2014	303.07 -	303.07	19.70	07/2016 -	07/2016	0(O) -	3/9
270	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE , .	01/2015	203.28 -	203.28	18.38	07/2017 -	07/2017	0(O) -	0/5
271	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI , .	05/2015	780.33 -	780.33	0.90	07/2017 -	07/2017	0(O) -	0/0
272	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE , .	07/2015	2,247.37 -	2,247.37	16.20	07/2018 -	07/2018	0(O) -	0/0
273	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT , .	01/2016	244.19 -	244.19	-	07/2018 -	07/2018	0(O) -	0/0
274	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE , .	01/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018	0(O) -	0/0
275	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH , .	01/2016	207.88 -	207.88	-	07/2018 -	07/2018	0(O) -	0/0
276	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA , .	03/2012	9,395.18 -	9,395.18	5,991.00	11/2016 -	08/2017	9(O) -	26/30
277	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE , .	03/2013	514.20 -	514.20	345.40	06/2015 -	08/2016	14(O) -	7/10
278	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE , .	06/2012	1,909.24 -	1,909.24	1,044.13	06/2015 -	08/2016	14(O) -	3/5
279	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , .	05/2014	829.98 -	829.98	101.40	08/2016 -	08/2016	0(O) -	1/4
280	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , .	02/2014	12,532.44 -	12,532.44	2,829.00	08/2018 -	08/2018	0(O) -	18/18
281	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL , .	09/2005	1,061.38 -	2,193.08	1,986.06	09/2009 -	09/2016	84(O) -	3/6
282	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , .	07/2006	1,657.00 2,978.86	2,978.86	1,644.81	02/2016 09/2019	09/2019	43(O) 0(R)	11/21
283	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , .	03/2013	11,638.55 -	11,638.55	5,025.00	09/2017 -	09/2017	0(O) -	20/41
284	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , .	09/2014	1,381.84 -	1,381.84	163.00	09/2019 -	09/2019	0(O) -	4/5
285	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , .	03/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017	0(O) -	0/0
286	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , .	01/2007	5,353.00 -	5,353.00	5,347.06	05/2014 -	09/2017	40(O) -	0/4
287	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , .	04/2012	9,750.89 -	9,750.89	4,664.54	12/2016 -	09/2017	9(O) -	25/28
288	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , .	03/2015	9,870.51 -	9,870.51	1,473.00	09/2019 -	09/2019	0(O) -	7/7
289	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NPEPCO,MIZORAM , .	07/1998	368.72 1,381.71	1,381.71	972.25	07/2006 10/2016	10/2016	123(O) 0(R)	5/13
290	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT , .	02/2014	378.71 -	378.71	120.00	10/2016 -	10/2016	0(O) -	8/11

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
291	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , ,	01/2015	871.62 -	871.62	6.20	10/2017 -	10/2017	0(O) -	0/5
292	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT , ,	10/2015	315.00 -	315.00	-	10/2016 -	10/2016	0(O) -	0/1
293	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , ,	01/2009	3,642.04 -	5,751.47	4,433.49	01/2016 -	11/2016	10(O) -	7/9
294	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , ,	01/2014	374.63 -	374.63	16.30	04/2016 -	11/2016	7(O) -	0/0
295	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , ,	05/2014	522.29 -	522.29	96.20	11/2016 -	11/2016	0(O) -	2/12
296	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE , ,	11/2014	972.42 -	972.42	67.80	11/2017 -	11/2017	0(O) -	0/3
297	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , ,	07/2015	307.18 -	307.18	12.70	11/2017 -	11/2017	0(O) -	0/0
298	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , ,	09/2002	3,919.59 -	8,398.76	5,460.85	09/2009 -	12/2018	111(O) -	2/3
299	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , ,	05/2005	1,779.29 2,187.32	2,187.32	1,904.95	11/2008 01/2016	12/2016	97(O) 11(R)	20/22
300	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , ,	11/2006	2,978.48 3,846.30	3,846.30	2,724.00	03/2013 -	12/2018	69(O) -	3/15
301	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , ,	12/2007	477.69 738.48	738.48	597.69	09/2010 01/2016	12/2016	75(O) 11(R)	4/8
302	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , ,	08/2008	2,491.58 -	2,491.58	814.10	06/2013 -	12/2019	78(O) -	5/8
303	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , ,	10/2008	4,824.12 -	4,824.12	4,256.58	10/2012 -	12/2016	50(O) -	7/11
304	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , ,	02/2009	11,130.19 13,762.80	13,762.80	11,605.20	08/2013 12/2017	12/2017	52(O) 0(R)	17/26
305	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , ,	02/2010	2,144.00 2,932.88	2,932.88	2,293.90	12/2012 12/2016	12/2016	48(O) 0(R)	11/23
306	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH , ,	11/2011	2,127.51 -	2,127.51	2,338.43	07/2014 -	12/2016	29(O) -	6/8
307	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH , ,	12/2011	1,746.65 2,228.71	2,228.71	1,482.93	08/2014 12/2015	12/2016	28(O) 12(R)	7/11
308	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , ,	03/2012	7,921.47 -	7,921.47	4,968.00	09/2016 -	12/2016	3(O) -	31/35
309	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , ,	03/2013	2,514.88 -	2,514.88	1,049.05	12/2015 -	12/2016	12(O) -	15/18
310	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , ,	07/2013	3,363.12 -	3,363.12	1,121.00	12/2016 -	12/2016	0(O) -	19/20

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
311	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR, .	05/2015	436.68 -	436.68	436.90	12/2016 -	12/2016	0(O) -	0/1
312	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH, .	09/2003	6,285.33 -	18,063.89	8,188.23	09/2010 -	-	-	0/0
	Total		304,580.02 -	353,192.66	185,284.79				829/1296
	HEAVY INDUSTRY								
313	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE, .	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	HEALTH AND FAMILY WELFARE								
314	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI, .	09/2013	444.70 -	444.70	285.20	12/2015 -	03/2016	3(O) -	0/0
315	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM, .	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15(O) -	0/0
316	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA, .	09/2014	505.58 -	505.58	14.38	03/2018 -	03/2018	0(O) -	0/0
317	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI, .	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3(O) -	0/0
318	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI, .	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017	0(O) -	0/0
319	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI, .	08/2014	293.65 -	293.65	67.84	05/2017 -	05/2017	0(O) -	0/0
320	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL, .	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017	0(O) -	0/0
321	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH, .	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31(O) -	0/0
322	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI, .	02/2013	414.11 -	414.11	210.91	11/2013 -	11/2014	-	0/0
	Total		2,563.15 -	2,563.15	1,018.40				0/0
	RAILWAYS								
323	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND, .	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
324	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE, .	09/1998	247.66 3,500.00	3,500.00	1,007.95	05/2008 -	-	-	0/0
325	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA, .	04/1996	301.64 -	1,185.64	577.84	- 09/2009	-	-	0/0
326	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR, .	04/2001	624.47 -	2,921.00	2,521.72	10/2007 -	-	-	0/0
327	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA, .	04/1998	183.23 -	1,202.70	185.46	02/2015 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
328	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT , .	04/2013	1,266.89	1,266.89	-	-	-	-	0/0
329	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE , .	04/2008	822.39	1,280.83	1,031.83	-	-	-	0/0
330	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , .	04/2012	1,054.35	2,200.00	51.67	-	-	-	0/0
331	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA , .	04/2010	2,127.00	2,127.00	325.00	-	-	-	0/0
332	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA , .	03/2011	679.27	1,111.99	60.31	-	-	-	0/0
333	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH , .	04/1997	836.26	1,072.51	-	-	-	-	0/0
334	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00	28,181.00	-	-	-	-	0/0
335	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL , .	04/2010	171.02	171.00	166.84	06/2013	01/2015	-	0/0
336	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , .	04/2006	96.16	260.16	240.21	-	01/2015	-	0/0
337	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , .	12/1994	124.43	925.30	712.02	-	02/2014	-	0/0
338	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , .	02/1996	240.00	579.37	599.40	-	02/2012	-	0/0
339	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , .	04/2011	1,176.09	3,845.60	2.33	02/2020	02/2020	0(O)	0/0
340	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , .	04/2010	622.41	2,030.50	3.61	02/2019	02/2019	0(O)	0/0
341	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , .	04/1986	158.77	608.02	602.10	03/1994	03/2015	-	0/0
342	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , .	04/1983	36.80	1,336.57	255.55	-	03/2019	-	0/0
343	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , .	03/1996	495.44	1,781.98	440.08	03/2004	03/2016	144(O)	0/0
344	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , .	03/1996	155.74	883.00	755.50	02/2009	03/2015	-	0/0
345	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , .	03/1997	677.97	1,651.54	1,621.40	-	03/2018	-	0/0
346	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , .	04/1997	218.24	645.00	309.19	-	03/2015	-	0/0
347	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL , .	04/1974	393.46	1,026.00	181.48	03/2007	03/2015	-	0/0
348	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR , .	09/2001	492.98	1,727.27	743.74	12/2010	03/2018	87(O)	0/0
349	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA , .	02/1998	242.42	844.00	798.87	-	03/2015	-	0/0
350	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE , .	04/1999	744.71	744.71	576.86	-	03/2016	-	1/1

Sector Wise Details

(February 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
351	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE , .	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
352	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR , .	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
353	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND , .	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0
354	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR , .	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84(O) -	0/0
355	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH , .	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
356	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH , .	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
357	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU , .	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
358	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM , .	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
359	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR , .	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
360	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA , .	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
361	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH , .	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
362	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA , .	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
363	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM , .	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
364	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR , .	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
365	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM , .	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
366	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN , .	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	-	0/0
367	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND , .	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
368	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM , .	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
369	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM , .	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84(O) -	0/0
370	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND , .	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
371	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE , .	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
372	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL , .	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
373	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA , .	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
374	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , .	04/2012	252.00 -	886.65 -	-	- -	03/2018	- -	0/0
375	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , .	04/2013	4,274.00 -	4,487.70 -	-	- -	03/2020	- -	0/0
376	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL , .	04/2011	209.77 190.39	441.45 -	85.78 -	- -	03/2018	- -	0/0
377	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL , .	04/2012	283.55 278.21	288.81 -	11.74 -	- -	03/2018	- -	0/0
378	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRI - [N22000202]SR,TAMIL NADU , .	04/2007	247.00 -	951.24 -	619.87 -	- -	03/2015	- -	0/0
379	NEW BG LINE FROM BYRNHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA , .	04/2010	4,083.02 -	5,307.90 -	7.79 -	- 03/2016	03/2020	- 48(R)	0/0
380	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , .	04/2010	242.22 171.00	679.57 -	40.41 -	- -	03/2018	- -	0/0
381	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , .	04/2010	241.52 210.00	394.28 -	233.46 -	- -	03/2017	- -	0/0
382	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , .	04/2011	165.82 165.82	435.58 -	0.56 -	- -	03/2018	- -	0/0
383	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATKHOWA-JAI - [N22000209]NFR,MULTI STATE , .	04/1999	523.17 380.60	1,653.55 -	1,040.11 -	- -	03/2018	- -	0/0
384	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , .	04/2011	312.12 257.93	453.10 -	134.79 -	- -	03/2018	- -	0/0
385	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , .	04/2012	246.07 246.07	364.06 -	0.30 -	- -	03/2019	- -	0/0
386	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , .	04/2012	714.10 -	714.10 -	65.93 -	04/2016 -	03/2017	11(O) -	0/0
387	PLASSEY-JAGANJ DOUBLING - [N22000220]ER,MULTI STATE , .	04/2011	248.07 -	248.07 -	29.10 -	03/2015 -	03/2015	- -	0/0
388	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , .	04/2011	299.60 -	299.60 -	- -	03/2017 -	03/2017	0(O) -	0/0
389	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE , .	04/2009	257.42 -	257.42 -	67.97 -	03/2014 -	03/2014	- -	0/0
390	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , .	04/2010	423.66 -	423.66 -	163.59 -	03/2017 -	03/2017	0(O) -	0/0
391	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , .	04/2007	98.74 -	203.00 -	227.84 -	- -	03/2015	- -	0/0
392	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , PPP (BOT)	03/2012	1,503.71 -	1,503.71 -	175.26 -	- -	03/2020	- -	0/0
393	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , .	12/2012	826.57 -	1,143.60 -	189.12 -	- -	03/2018	- -	0/0
394	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , .	04/1999	166.16 -	325.50 -	349.36 -	02/2009 02/2009	04/2016	86(O) 86(R)	0/0
395	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , .	09/1997	1,500.00 -	4,996.19 -	4,102.70 -	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
396	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , .	04/1999	108.00 427.21	432.72 -	436.85 -	12/2009 03/2011	06/2015	- -	0/0

Sector Wise Details

(February 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , .	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
398	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , .	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87(O) -	0/0
399	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL , .	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
400	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL , .	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
401	AMRAVATI-NARKHER (NL) (CR) - [220100118]CR,MAHARASHTRA , .	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
402	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , .	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
403	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , .	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	-	0/0
404	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL , .	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	-	0/0
405	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , .	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
406	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , .	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	-	0/0
407	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA , .	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
408	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , .	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91(O) 91(R)	0/0
409	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL , .	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
410	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , .	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181(O) -	0/0
411	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , .	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
412	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , .	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	-	0/0
413	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL , .	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
414	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , .	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
415	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , .	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93(O) -	0/0
416	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL , .	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
417	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL , .	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57(O) -	0/0
418	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL , .	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
419	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , .	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
420	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , .	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
421	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , .	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	- -	0/0
422	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA , .	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21(O) -	0/0
423	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , .	03/2012	155.81 -	155.81	18.25	- -	12/2016	- -	0/0
424	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , .	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
425	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE , .	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
426	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH , .	04/1995	304.00 -	631.78	238.82	12/2012 -	-	-	0/0
427	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , .	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
428	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA , .	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
429	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , .	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
430	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , .	02/1997	410.08 -	410.08	297.58	- -	-	-	0/0
431	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , .	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
432	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , .	02/1997	155.55 -	800.00	800.70	- -	-	-	0/0
433	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , .	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0
434	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , .	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
435	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , .	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
436	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , .	04/1997	162.87 -	541.00	158.58	- -	-	-	0/0
437	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , .	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
438	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , .	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
439	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , .	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
440	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , .	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
441	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL , .	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
442	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , .	04/1998	92.63 -	270.00	376.18	02/2011 02/2011	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
443	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL, .	04/2000	1,188.91	1,188.91	687.63	-	-	-	0/0
444	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER, MULTI STATE, .	04/2000	607.09	607.09	561.14	12/2009	-	-	0/0
445	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA, .	04/1996	138.00	1,382.78	2.81	-	-	-	0/0
446	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA, .	04/1994	470.21	1,995.25	355.02	-	-	-	0/0
447	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR, .	04/2003	528.65	324.66	227.03	-	-	-	0/0
448	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR, .	04/2002	322.95	341.41	325.36	03/2012	-	-	0/0
449	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND, .	04/2002	459.91	418.17	260.67	-	-	-	0/0
450	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR, .	04/2001	406.92	339.00	204.83	-	-	-	0/0
451	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR, .	04/2003	218.19	343.00	216.17	-	-	-	0/0
452	HATHUA-BHATNI (NL) (NER) - [220100319]NER, MULTI STATE, .	04/2005	230.03	230.03	172.58	-	-	-	0/0
453	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA, .	04/2005	810.78	810.80	160.80	-	-	-	0/0
454	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH, .	04/2003	136.62	360.00	357.91	12/2007	-	-	0/0
455	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR, .	04/1996	332.92	477.88	498.37	03/2012	-	-	0/0
456	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA, .	04/2006	378.56	791.59	5.41	-	-	-	0/0
457	GOELKERA-MANOHPUR, (LD)(SER) - [N22000045]SER, JHARKHAND, .	03/1997	261.70	360.00	253.92	02/2006	-	-	0/0
458	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH, .	07/2006	743.00	732.81	770.18	03/2008	-	-	0/0
459	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU, .	09/2007	404.19	1,383.45	457.88	-	-	-	0/0
460	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE, .	12/2006	170.00	485.00	417.70	03/2011	-	-	0/0
461	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU, .	09/2006	125.00	490.00	67.57	-	-	-	0/0
462	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU, .	09/2006	456.00	1,080.00	194.61	-	-	-	0/0
463	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH, .	04/2006	325.00	2,434.00	419.45	03/2010	03/2017	84(O)	0/0
464	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL, .	04/2007	1,106.62	1,106.62	244.99	12/2010	-	-	0/0
465	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL, .	04/2010	2,298.42	1,655.68	38.46	03/2014	-	-	0/0
466	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN, PPP (BOT)	04/2008	653.19	653.55	258.78	03/2014	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
467	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , .	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
468	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , .	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
469	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL , .	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
470	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL , .	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
471	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , .	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
472	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , .	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
473	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , .	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
474	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , .	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
475	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , .	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
476	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH , .	03/2013	307.00 -	307.00	-	- -	-	-	0/0
477	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , .	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
478	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , .	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
479	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , .	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0
480	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , .	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
481	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , .	03/2013	643.00 -	643.00	-	- -	-	-	0/0
482	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , .	04/2012	246.08 -	246.08	4.20	- -	-	-	0/0
483	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , .	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
484	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , .	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
485	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT , .	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
486	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT , .	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
487	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , .	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
488	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , .	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
489	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , .	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
490	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , .	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
491	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , .	04/2011	2,082.75 -	3,500.00	54.23	- -	-	-	0/0
492	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , .	04/2013	236.93 -	262.00	0.41	- -	-	-	0/0
493	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , .	04/2013	822.00 -	822.00	-	- -	-	-	0/0
494	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , .	04/2013	323.00 -	323.00	-	- -	-	-	0/0
495	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , .	04/2013	456.00 -	855.16	557.82	- -	-	-	0/0
496	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , .	04/2010	739.65 -	872.22	794.11	- -	-	-	0/0
497	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , .	04/2011	239.73 -	179.32	75.76	- -	-	-	0/0
498	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , .	04/2011	213.39 -	218.39	23.63	- -	-	-	0/0
499	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , .	04/2012	288.97 -	288.97	1.09	- -	-	-	0/0
500	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , .	04/2013	242.09 -	242.09	0.39	- -	-	-	0/0
501	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , .	04/2010	267.37 -	434.00	35.90	- -	-	-	0/0
502	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , .	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
503	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , .	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
504	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR , .	04/2008	620.57 -	620.57	-	- -	-	-	0/0
505	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]JECR,BIHAR , .	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
506	GAYA-CHATRA (NL) - [N22000169]JECR,MULTI STATE , .	04/2008	415.67 -	415.67	14.00	- -	-	-	0/0
507	BIHTA-AURANGABAD (NL) - [N22000170]JECR,BIHAR , .	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
508	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR,BIHAR , .	04/1999	175.69 -	325.00	259.31	- -	-	-	0/0
509	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECR,BIHAR , .	04/2006	285.07 -	378.56	111.87	- -	-	-	0/0
510	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]JECR,BIHAR , .	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
511	MOTIHARI-SITAMARHI (NL) - [N22000174]JECR,BIHAR , .	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
512	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]JECR,BIHAR , .	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
513	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR , .	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
514	ARARIA-SUPAUL (NL) - [N22000177]JECR,BIHAR , .	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
515	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , .	04/2008	192.56 -	192.56	0.38	-	-	-	0/0
516	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , .	04/2008	281.30 -	281.30	0.58	-	-	-	0/0
517	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , .	04/2004	372.14 -	355.81	294.07	-	-	-	0/0
518	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , .	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
519	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , .	04/2013	213.01 -	367.17	17.19	-	-	-	0/0
520	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU , .	04/2008	446.87 -	528.00	2.96	-	-	-	0/0
521	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , .	04/2008	523.52 -	1,200.00	2.07	-	-	-	0/0
522	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , .	04/2013	839.00 -	1,500.00	0.01	-	-	-	0/0
523	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU , .	04/1999	198.68 -	556.64	268.56	-	-	-	0/0
524	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , .	04/1998	271.24 -	520.00	462.69	-	-	-	0/0
525	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , .	04/2007	270.14 -	346.15	14.61	-	-	-	0/0
526	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , .	04/2011	252.96 -	252.96	1.48	-	-	-	0/0
527	ERODE-PALANI - [N22000199]SR,TAMIL NADU , .	04/2008	288.57 -	603.22	1.64	-	-	-	0/0
528	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , .	04/2008	164.41 -	450.00	16.97	-	-	-	0/0
529	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , .	04/2006	191.72 -	222.95	112.40	-	-	-	0/0
530	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , .	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
531	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL , .	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
532	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , .	04/2011	601.43 -	800.00	0.69	-	-	-	0/0
533	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , .	04/1987	406.99 -	406.99	141.55	-	-	-	0/0
534	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , .	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
535	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , .	04/2010	172.03 -	172.03	5.86	-	-	-	0/0
536	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , .	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
537	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , .	04/2011	288.35 -	288.35	9.60	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
538	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , .	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
539	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE , .	04/2000	157.17 -	157.17	76.90	-	-	-	0/0
540	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , .	04/2001	923.52 -	923.52	208.10	-	-	-	0/0
541	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , .	04/2005	595.91 -	595.91	89.60	-	-	-	0/0
542	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , .	04/2010	174.56 -	174.56	63.08	-	-	-	0/0
543	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , .	04/2010	277.28 -	277.28	67.82	-	-	-	0/0
544	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , .	04/2010	296.44 -	296.44	4.55	-	-	-	0/0
545	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , .	04/2010	157.94 -	157.94	43.34	-	-	-	0/0
546	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , .	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
547	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , .	04/2011	277.70 -	279.70	4.73	-	-	-	0/0
548	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , .	04/2007	450.55 -	450.55	13.53	-	-	-	0/0
549	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , .	04/2010	365.17 -	365.17	1.35	-	-	-	0/0
550	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , .	04/2011	267.09 -	267.09	1.50	-	-	-	0/0
551	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , .	04/2011	193.44 -	193.44	53.01	-	-	-	0/0
552	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , .	04/2011	175.80 -	175.80	1.46	-	-	-	0/0
553	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , .	04/2010	494.54 -	494.54	31.20	-	-	-	0/0
554	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , .	04/2000	297.47 -	297.47	51.82	-	-	-	0/0
555	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE , .	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
556	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , .	04/2009	493.96 -	493.96	121.27	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
557	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , .	04/2011	184.06 -	184.06	15.23	-	-	-	0/0
558	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , .	04/2010	268.52 -	268.52	78.81	-	-	-	0/0
559	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , .	04/2011	166.89 -	166.89	0.02	-	-	-	0/0
560	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , .	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
561	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , .	04/2011	913.00 -	1,801.01	1.47	-	-	-	0/0
562	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , .	04/2007	179.65 -	1,350.91	380.62	-	-	-	0/0
563	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , .	04/2010	377.93 -	986.30	100.76	-	-	-	0/0
564	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , .	04/2013	1,112.00 -	1,112.00	-	-	-	-	0/0
565	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE , .	04/2013	723.00 -	723.00	-	-	-	-	0/0
566	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE , .	04/2008	184.26 -	2,000.00	17.32	-	-	-	0/0
567	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , .	04/2012	923.23 -	923.23	1.01	-	-	-	0/0
568	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH , .	04/2011	283.54 -	283.54	0.31	-	-	-	0/0
569	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , .	04/2012	377.44 -	377.44	7.50	-	-	-	0/0
570	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB , .	04/2009	396.04 -	369.00	188.93	-	-	-	0/0
571	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , .	04/1999	156.65 -	156.65	53.00	-	-	-	0/0
572	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , .	04/2013	654.00 -	654.00	-	-	-	-	0/0
573	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , .	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
574	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , .	04/2012	287.00 -	576.18	3.40	-	-	-	0/0
575	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH , .	04/2008	1,046.88 -	2,966.99	40.80	-	-	-	0/0
576	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , .	04/2007	336.91 -	336.91	144.25	-	-	-	0/0
577	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , .	04/2013	558.00 -	692.43	-	-	-	-	0/0
578	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , .	04/2013	296.00 -	466.65	-	-	-	-	0/0
579	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , .	04/2011	562.74 -	832.47	0.94	-	-	-	0/0
580	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE , .	04/2007	970.34 -	1,743.00	359.06	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
581	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , .	04/2011	341.05 -	348.85 -	0.34 -	-	-	-	0/0
582	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , .	04/2012	295.68 -	295.68 -	0.86 -	-	-	-	0/0
583	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , .	04/2013	829.00 -	829.00 -	-	-	-	-	0/0
584	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA , .	04/2011	390.60 -	390.60 -	4.69 -	-	-	-	0/0
585	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , .	04/2011	1,313.48 -	1,313.48 -	5.13 -	-	-	-	0/0
586	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , .	04/2010	337.49 -	337.50 -	0.21 -	-	-	-	0/0
587	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , .	04/2008	2,050.00 -	2,050.00 -	194.45 -	-	-	-	0/0
588	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND , .	04/2012	219.83 -	329.97 -	2.38 -	-	-	-	0/0
589	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , .	04/2010	338.54 -	338.54 -	129.14 -	-	-	-	0/0
590	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , .	04/2008	162.96 -	162.96 -	143.62 -	-	-	-	0/0
591	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , .	04/2013	400.00 -	400.00 -	-	-	-	-	0/0
592	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , .	04/2013	876.00 -	876.00 -	-	-	-	-	0/0
593	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH , .	04/2012	380.00 -	380.00 -	1.38 -	-	-	-	0/0
594	QADIAN-BEAS - [N22000295]NR,PUNJAB , .	04/2011	205.22 -	205.22 -	1.54 -	-	-	-	0/0
595	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , .	04/2007	328.14 -	328.14 -	0.31 -	-	-	-	0/0
596	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , .	04/2011	146.75 -	167.50 -	0.32 -	-	-	-	0/0
597	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , .	04/2013	1,117.00 -	1,922.00 -	1.89 -	-	-	-	0/0
598	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , .	04/2013	327.25 -	367.77 -	-	-	-	-	0/0
599	MONIGRAM- NIMITITA - [N22000301]ER,MULTI STATE , .	04/2012	250.93 -	250.93 -	0.14 -	-	-	-	0/0
600	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL , .	04/2012	255.64 -	255.64 -	-	-	-	-	0/0
601	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU , .	04/1999	460.94 -	1,030.00 -	-	01/1999 -	-	-	0/0
602	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , .	04/2007	313.24 -	313.24 -	230.62 -	01/1999 -	-	-	0/0
603	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , .	04/2008	466.48 -	800.00 -	0.83 -	01/1999 -	-	-	0/0
604	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , .	04/2012	285.57 -	279.54 -	1.38 -	01/1999 -	-	-	0/0
605	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL , .	04/2011	276.69 -	426.00 -	-	01/1999 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
606	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA , .	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
607	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA , .	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
608	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA , .	03/2011	165.16 -	234.71	137.01	03/2015 -	-	-	0/0
609	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH , .	04/2014	182.92 -	197.73	-	-	-	-	0/0
610	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR, TAMIL NADU , .	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
611	HUBLI- CHIKAJAJUR - [N22000325]SWR, KARNATAKA , .	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
612	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE , .	05/2015	600.00 -	600.00	-	-	-	-	0/0
613	MIRAJ-LONDA - [N22000327]SWR, MULTI STATE , .	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
614	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE , .	05/2015	860.43 -	860.43	-	-	-	-	0/0
615	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR , .	05/2015	380.00 -	380.00	-	-	-	-	0/0
616	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN , .	05/2015	873.71 -	873.71	-	-	-	-	0/0
617	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR, HARYANA , .	05/2015	400.00 -	400.00	-	-	-	-	0/0
618	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA , .	03/2015	960.00 -	960.00	-	-	-	-	0/0
619	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE , .	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
620	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE , .	05/2015	720.00 -	720.00	-	-	-	-	0/0
	Total		254,176.67 -	329,512.54	93,586.56				1/7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
621	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM , .	12/2003	157.47 -	157.47	-	09/2007 -	-	-	0/0
622	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR , .	12/2003	300.00 -	300.00	-	10/2008 -	-	-	0/0
623	RAJMARG CHORHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH , .	12/2003	251.03 -	251.03	-	10/2008 -	-	-	0/0
624	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL , .	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0
625	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
626	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
627	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
628	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI,KERALA , .	03/2005	557.00 -	557.00 -	932.30 -	02/2010 -	-	-	0/0
629	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75 -	-	08/2011 -	-	-	2/2
630	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH , .	05/2009	572.30 -	572.30 -	761.40 -	10/2011 -	-	-	0/0
631	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN , PPP (BOT)	06/2010	792.06 -	792.06 -	1,983.00 -	12/2012 -	02/2016	38(O)	0/0
632	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , .	09/2010	946.00 -	946.00 -	-	-	-	-	3/3
633	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00 -	1,655.00 -	-	09/2013 -	-	-	0/0
634	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00 -	1,055.94 -	11/2013 -	-	-	0/0
635	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND , .	08/2010	625.07 -	625.07 -	-	01/2013 -	-	-	0/0
636	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA , .	02/2010	390.56 -	390.56 -	-	02/2012 -	06/2013	-	0/0
637	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA , PPP (BOT)	09/2010	671.00 -	671.00 -	-	-	-	-	2/3
638	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA , .	04/2011	807.00 -	807.00 -	-	10/2014 -	-	-	0/0
639	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA , .	12/2010	453.00 -	453.00 -	487.90 -	-	-	-	1/1
640	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA , .	12/2010	480.00 -	480.00 -	438.00 -	-	-	-	2/2
641	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA , .	11/2010	680.00 -	680.00 -	-	-	-	-	2/2
642	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT , PPP (BOT)	03/2011	785.50 -	785.50 -	-	08/2013 -	-	-	0/3
643	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA , .	02/2011	226.00 -	226.00 -	-	02/2014 -	-	-	0/0
644	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR , .	12/2011	325.51 -	325.00 -	160.20 -	05/2014 -	-	-	0/0
645	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH , .	10/2011	209.00 -	209.00 -	-	01/2013 -	-	-	0/0
646	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA , .	11/2011	909.00 -	909.00 -	844.10 -	05/2014 -	-	-	0/0
647	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH , .	07/1999	635.90 -	635.90 -	-	07/2012 -	-	-	0/0
648	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA , .	04/2011	682.00 -	682.00 -	34.81 -	10/2013 -	-	-	0/0
649	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH , .	10/2012	250.50 -	250.50 -	-	10/2014 -	-	-	0/0
650	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH , .	01/2013	373.47 -	373.47 -	358.30 -	07/2014 -	08/2015	-	0/0
651	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH , .	09/2013	606.00 -	606.00 -	-	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
652	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA , .	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
653	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN , .	01/2014	177.32 -	177.32	86.65	01/2016 -	-	-	0/0
654	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , .	03/2011	218.31 339.82	339.82	282.02	12/2015 -	-	-	0/3
655	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33 -	298.33	-	-	-	-	0/4
656	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	-	-	-	-	0/4
657	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	-	-	-	-	0/4
658	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	71.38	02/2015 -	-	-	0/4
659	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , .	01/2014	361.30 -	361.30	-	07/2014 -	-	-	0/1
660	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	-	-	-	0/1
661	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	-	-	-	0/4
662	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	-	-	-	0/0
663	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	-	-	-	0/0
664	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	50.94	-	-	-	0/0
665	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	-	-	-	-	0/0
666	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	20.70	03/2015 -	-	-	0/0
667	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	5.26	03/2015 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
668	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD, CHHATISGARH , EPC	11/2014	262.54 -	262.54	10.14	03/2015 -	-	-	0/0
669	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	12/2015 -	-	-	0/0
670	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD, CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	111.73	12/2012 -	-	-	0/0
671	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD, CHHATISGARH , EPC	12/2014	394.20 -	394.20	96.04	- -	-	-	0/0
672	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
673	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH , EPC	03/2015	422.34 -	422.34	8.89	03/2015 -	-	-	0/0
674	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD, PUNJAB , EPC	03/2015	435.90 -	435.90	15.50	- -	-	-	0/0
675	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD, PUNJAB , EPC	01/2015	279.68 -	279.68	29.39	- -	-	-	0/0
676	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD, PUNJAB , EPC	11/2014	463.65 546.00	463.65	256.48	- -	-	-	0/0
677	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD, PUNJAB , EPC	11/2014	573.96 605.00	605.00	198.10	- -	-	-	0/0
678	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH, ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
679	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH, RAJASTHAN , EPC	10/2014	269.22 -	269.22	27.00	01/2015 -	-	-	0/0
680	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH, RAJASTHAN , EPC	10/2014	257.09 -	257.09	15.17	01/2015 -	-	-	0/0
681	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH, RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
682	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH, RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	171.16	04/2014 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
683	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	131.09	03/2015 -	-	-	0/0
684	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM , ITEM RATE	08/2010	186.96 -	186.96	132.80	- -	-	-	0/0
685	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	219.50	03/2011 -	-	-	0/0
686	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	140.75	02/2012 -	-	-	0/0
687	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	122.00	10/2010 -	-	-	0/0
688	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	4.39	03/2011 -	-	-	0/0
689	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	12.66	05/2012 -	-	-	0/0
690	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM , .	04/2013	151.59 -	151.59	7.19	08/2013 -	-	-	0/0
691	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
692	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	49.42	02/2013 -	-	-	0/0
693	WIDENING OF 2(TWO) LANING OF LONGLENG- CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
694	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	20.80	08/2015 -	-	-	0/0
695	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 161.70	161.70	2.55	07/2015 -	-	-	0/0
696	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 158.35	154.14	2.55	08/2015 -	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
697	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74	629.74	-	-	-	-	0/0
698	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81	225.81	-	-	-	-	0/0
699	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38	483.38	45.64	-	-	-	0/0
700	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36	616.36	25.87	-	-	-	0/0
701	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74	486.74	89.68	-	-	-	0/0
702	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51	390.51	-	02/2015	-	-	0/0
703	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26	704.26	-	05/2015	-	-	0/0
704	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80	257.80	-	02/2016	02/2016	0(0)	0/0
705	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00	675.00	-	-	-	-	0/0
706	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79	312.79	-	-	-	-	0/0
707	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80	319.80	51.28	-	-	-	0/0
708	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36	766.36	12.08	-	-	-	0/0
709	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16	264.16	-	-	-	-	0/0
710	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02	847.02	299.55	-	-	-	0/0
711	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48	1,494.48	2,090.00	02/2011	-	-	0/0
712	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24	889.24	388.43	-	-	-	0/0
713	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80	257.00	-	05/2015	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
714	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20	470.20	7.97	02/2011	-	-	0/0
715	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38	578.38	-	-	-	-	0/0
716	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83	789.83	72.79	-	-	-	0/0
717	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21	333.21	-	11/2015	-	-	0/0
718	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04	195.04	157.22	10/2010	10/2010	-	0/0
719	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00	165.00	135.01	09/2010	-	-	0/0
720	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00	201.00	-	09/2010	-	-	0/0
721	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18	2,288.18	-	-	-	-	0/0
722	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , .	07/2015	1,282.94	1,282.94	-	-	-	-	0/0
723	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	01/1991	225.02	225.02	-	-	-	-	0/0
724	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	01/1991	223.30	223.30	-	-	-	-	0/0
725	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01	520.01	-	-	-	-	0/0
726	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , .	09/2015	414.51	414.00	-	-	-	-	0/0
727	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH , .	06/2015	583.79	583.79	-	-	-	-	0/0
728	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL , .	10/2015	531.13	531.13	-	-	-	-	0/0
729	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL , .	10/2015	361.15	361.15	-	-	-	-	0/0
730	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	01/1991	289.99	289.99	-	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
731	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	-	-	-	0/0
732	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , .	10/2015	593.26 -	593.26	-	-	-	-	0/0
733	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , .	12/2015	649.50 -	649.50	-	-	-	-	0/0
734	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	-	-	-	0/0
735	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	-	02/2015 -	-	-	0/0
736	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	-	-	0/0
737	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , .	08/2015	505.00 -	505.00	-	-	-	-	0/0
738	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	-	-	-	-	0/0
739	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,012.90 -	1,012.90	-	-	-	-	0/0
740	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , .	06/2015	845.24 -	845.24	-	-	-	-	0/0
741	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU , .	01/1991	285.00 -	285.00	-	01/2008 -	-	-	0/0
742	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
743	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , .	03/2015	795.76 -	795.76	-	-	-	-	0/0
744	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , .	03/2015	794.30 -	794.30	-	-	-	-	0/0
745	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	-	-	0/0
746	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA , .	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
747	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , .	08/2015	556.07 -	556.07	-	-	-	-	0/0
748	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS , .	09/2015	273.06 -	273.06	-	-	-	-	0/0
749	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , .	12/2015	1,041.10 -	1,041.10	-	-	-	-	0/0
750	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR , .	08/2015	814.04 -	814.04	-	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
751	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , .	12/2015	752.28 -	752.28	-	-	-	-	0/0
752	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL , .	12/2015	1,423.96 -	1,423.96	-	-	-	-	0/0
753	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , .	03/2015	928.83 -	928.83	-	-	-	-	0/0
754	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00 -	1,388.00	-	-	-	-	0/0
755	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , .	12/2015	596.67 -	596.67	-	-	-	-	0/0
756	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , .	08/2015	322.09 -	322.09	-	-	-	-	0/0
757	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , .	12/2015	509.13 -	509.13	-	-	-	-	0/0
758	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , .	03/2015	810.22 -	810.22	-	-	-	-	0/0
759	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	-	-	0/0
760	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , .	01/1991	642.41 -	642.41	-	-	-	-	0/0
761	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , .	01/1991	1,167.45 -	1,167.45	-	-	-	-	0/0
762	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , .	12/2015	726.67 -	726.67	-	-	-	-	0/0
763	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
764	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	-	-	-	0/0
765	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	-	-	-	0/0
766	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , .	12/2015	479.20 -	479.20	-	-	-	-	0/0
767	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , .	08/2015	399.54 -	399.54	-	-	-	-	0/0
768	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR , .	01/1991	478.35 -	478.35	-	-	-	-	0/0
769	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN , .	08/2015	275.90 -	275.90	-	-	-	-	0/0
770	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR , .	08/2015	516.13 -	516.13	18.48	-	-	-	0/0
771	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	14.70	-	-	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
772	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	13.13	-	-	-	0/0
773	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	-	07/2008 -	-	-	0/0
774	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
775	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	-	-	-	0/0
776	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	-	-	-	0/0
777	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM , .	12/2003	208.00 230.00	208.00	295.20	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
778	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU , PPP (BOT)	06/2011	535.00 -	535.00	-	12/2013 -	01/2016	-	0/0
779	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT , PPP (BOT)	09/2010	805.39 -	805.39	1,384.61	03/2013 -	01/2016	-	0/0
780	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
781	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	-	01/2019 -	01/2019	0(O) -	0/0
782	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB , .	01/2014	523.85 -	523.85	62.37	01/2016 -	01/2017	12(O) -	0/0
783	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU , .	07/2014	401.11 -	401.11	-	01/2017 -	01/2017	0(O) -	0/0
784	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
785	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
786	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2016 -	01/2016	-	0/0
787	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	-	10/2011 -	01/2016	-	0/0
788	FOUR LANING OF KATHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	876.68	-	01/2018	-	0/0
789	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,055.00	-	11/2015 -	01/2016	-	0/0
790	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2019 -	01/2016	-	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
791	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34	1,871.34	1,125.73	01/2018	01/2018	0(O)	0/0
792	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM , .	12/2003	264.72	264.72	-	06/2008	02/2016	92(O)	0/0
793	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00	486.00	468.41	05/2010	02/2016	69(O)	0/0
794	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10	1,509.10	2,891.15	09/2012	02/2016	41(O)	2/3
795	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16	702.16	391.77	07/2014	02/2017	31(O)	0/0
796	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN , PPP (ANNUITY)	03/2012	333.51	333.51	225.26	09/2014	02/2016	17(O)	0/0
797	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47	313.27	12.80	02/2017	02/2017	0(O)	0/1
798	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH , .	02/2015	241.61	241.61	37.55	02/2017	02/2017	0(O)	0/1
799	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78	330.00	15.47	02/2017	02/2017	0(O)	0/0
800	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55	251.55	27.87	02/2015	02/2017	24(O)	0/1
801	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN , .	08/2015	538.08	538.08	-	02/2018	02/2018	0(O)	0/0
802	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , .	08/2015	723.54	723.54	161.76	02/2018	02/2018	0(O)	0/0
803	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN , .	08/2015	482.27	482.27	16.90	02/2018	02/2018	0(O)	0/0
804	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22	176.22	106.61	02/2018	02/2018	0(O)	0/0
805	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31	218.31	-	02/2018	02/2018	0(O)	0/0
806	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN , EPC	03/2012	914.50	914.50	1,097.62	10/2015	02/2016	4(O)	0/0
807	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH , .	12/2003	155.00	201.66	242.00	09/2008	03/2016	90(O)	0/0
808	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , .	12/2003	280.00	361.00	-	02/2009	03/2016	85(O)	0/0
809	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , .	12/2003	199.81	385.13	-	04/2009	03/2016	83(O)	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
810	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , .	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88(O) -	0/0
811	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , .	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88(O) -	0/0
812	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83(O) -	0/0
813	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM , .	12/2003	195.00 -	195.00	-	06/2008 -	03/2016	93(O) -	0/0
814	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM , .	12/2003	237.80 -	237.80	-	06/2008 -	03/2016	93(O) -	0/0
815	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR , .	12/2003	332.94 -	332.94	493.27	09/2008 -	03/2016	90(O) -	0/0
816	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN , .	12/2003	275.00 -	250.39	274.11	10/2008 -	03/2016	89(O) -	0/0
817	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , .	12/2003	196.00 -	331.23	-	07/2009 -	03/2016	80(O) -	0/0
818	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH , .	12/2003	348.16 -	348.16	342.49	09/2007 -	03/2016	102(O) -	0/0
819	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN , PPP (BOT)	11/2009	795.00 -	795.00	1,607.78	05/2012 -	03/2016	46(O) -	0/0
820	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35(O) -	0/0
821	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55(O) -	0/0
822	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33(O) -	0/0
823	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19(O) -	0/0
824	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	03/2016	34(O) -	0/0
825	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28(O) -	0/0
826	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	-	08/2013 -	03/2017	43(O) -	0/0
827	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	609.00	02/2014 -	03/2016	25(O) -	0/0
828	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	761.49	03/2014 -	03/2016	24(O) -	0/0
829	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , .	10/2011	375.09 -	375.09	352.00	04/2014 -	03/2016	23(O) -	0/0
830	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	03/2016	28(O) -	0/0
831	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND , .	02/2012	398.00 -	398.00	-	02/2014 -	03/2016	25(O) -	0/0
832	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA , PPP (BOT)	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26(O) -	0/0
833	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31(O) -	0/0
834	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN , .	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
835	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN , PPP (BOT)	12/2011	2,388.51 -	2,388.00	2,472.00	06/2014 -	03/2016	21(O) -	0/0
836	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21(O) -	0/0
837	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA , PPP (BOT)	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17(O) -	0/0
838	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE , .	12/2011	942.69 -	942.69	229.16	06/2014 -	03/2016	21(O) -	0/0
839	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE , PPP (BOT)	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7(O) -	0/0
840	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	-	11/2015 -	03/2017	16(O) -	0/0
841	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , .	03/2014	240.10 -	240.10	147.69	03/2016 -	03/2016	0(O) -	0/0
842	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016	0(O) -	3/4
843	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016	0(O) -	3/4
844	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016	0(O) -	1/4
845	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(O) -	0/2
846	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	50.85	03/2016 -	03/2016	0(O) -	1/4
847	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	03/2015	829.00 -	829.00	-	03/2018 -	03/2018	0(O) -	0/4
848	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018	0(O) -	0/4
849	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	31.64	03/2016 -	03/2016	0(O) -	0/0
850	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR , .	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88(O) -	0/0
851	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , .	09/2015	567.51 -	567.51	42.79	03/2018 -	03/2018	0(O) -	0/0
852	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
853	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017	0(O) -	0/0
854	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
855	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , EPC	01/1991	322.00 -	322.00	-	03/2018 -	03/2018	0(O) -	0/0
856	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	-	03/2017 -	03/2017	0(O) -	0/0
857	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	0(O) -	0/0
858	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , .	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(O) -	0/0
859	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , .	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(O) -	0/0
860	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , .	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(O) -	0/0
861	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,HARYANA , .	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
862	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , .	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
863	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	-	03/2018 -	03/2018	0(O) -	0/0
864	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , .	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
865	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH , .	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7(O) -	0/0
866	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , .	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016	0(O) -	0/0
867	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7(O) -	0/0
868	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA , .	02/2010	650.00 -	650.00	813.91	-	03/2016	-	0/0
869	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
870	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM, .	12/2003	198.16 -	198.16	242.40	04/2008 04/2016	04/2016	96(O) 0(R)	0/0
871	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI, ASSAM, .	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016	94(O) 0(R)	0/0
872	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE, .	12/2003	232.45 -	232.45	-	09/2010 -	04/2016	67(O) -	0/0
873	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA, PPP (BOT)	03/2005	940.00 -	940.00	1,409.36	07/2012 -	04/2016	45(O) -	3/3
874	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN, PPP (BOT)	01/2011	593.00 -	593.00	1,006.79	07/2013 -	04/2016	33(O) -	0/0
875	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH, PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32(O) -	0/0
876	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE, PPP (BOT)	09/2011	2,848.00 -	2,848.00	542.01	03/2014 -	04/2017	37(O) -	0/0
877	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE, PPP (BOT)	10/2012	1,928.22 -	1,928.22	822.96	04/2015 -	04/2016	12(O) -	0/0
878	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN, PPP (BOT)	10/2013	677.79 -	677.79	604.72	04/2016 -	04/2016	0(O) -	0/0
879	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP, GOA, EPC	03/2015	297.00 -	297.00	36.02	- -	04/2018	- -	0/1
880	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL, TRIPURA, EPC	05/2014	497.89 -	497.89	49.78	04/2017 -	04/2017	0(O) -	0/3
881	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI, RAJASTHAN, .	10/2014	206.12 -	206.12	105.78	04/2017 -	04/2017	0(O) -	0/0
882	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN, .	10/2014	264.72 -	264.72	85.17	04/2017 -	04/2017	0(O) -	0/0
883	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 2) - [N24000358]NHAI, HARYANA, .	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
884	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH, BOT (TOLL)	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12(O) -	0/0
885	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN, PPP (BOT)	08/2014	822.90 -	822.90	37.00	04/2018 -	04/2018	0(O) -	0/0
886	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN, .	12/2003	275.00 -	281.31	162.47	02/2010 -	05/2017	87(O) -	0/0
887	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR, PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
888	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE, PPP (BOT)	02/2011	580.43 -	580.43	222.75	08/2013 -	05/2017	45(O) -	0/0
889	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL, PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,310.32	09/2014 -	05/2016	20(O) -	0/0
890	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE, PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	480.44	06/2015 -	05/2017	23(O) -	0/0
891	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN, .	01/2014	158.04 -	158.04	117.97	12/2015 -	05/2016	5(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
892	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	0/4
893	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018	0(O) -	0/4
894	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	-	05/2018 -	05/2018	0(O) -	0/4
895	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , .	11/2014	279.14 -	279.14	60.87	05/2017 -	05/2017	0(O) -	0/0
896	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , .	05/2015	261.09 -	261.09	5.00	05/2017 -	05/2017	0(O) -	0/0
897	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	0(O) -	0/0
898	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017	0(O) -	0/0
899	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	-	05/2017 -	05/2017	0(O) -	0/0
900	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	-	05/2016 -	05/2016	0(O) -	0/0
901	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , .	01/1991	229.41 -	229.41	-	05/2018 -	05/2018	0(O) -	0/0
902	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13(O) -	0/0
903	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	28.86	05/2018 -	05/2018	0(O) -	0/4
904	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , .	02/2015	327.32 -	327.32	-	05/2017 -	05/2017	0(O) -	0/0
905	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH , .	11/2015	867.66 -	867.66	52.60	11/2015 -	05/2018	30(O) -	0/0
906	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37 -	353.37	-	10/2011 -	06/2016	56(O) -	0/0
907	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,619.94	11/2011 -	06/2016	55(O) -	0/0
908	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
909	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11(O) -	0/0
910	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35(O) -	0/0
911	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50	-	06/2013 -	06/2016	36(O) -	0/3
912	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , .	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36(O) -	0/0
913	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35(O) -	0/0
914	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29(O) -	0/0
915	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,503.31	05/2014 -	06/2016	25(O) -	0/0
916	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24(O) -	0/0
917	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	902.06	03/2013 -	06/2016	39(O) -	0/0
918	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,844.50	09/2015 -	06/2016	9(O) -	0/0
919	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	06/2016	6(O) -	0/3
920	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21(O) -	0/3
921	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN , .	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5(O) -	0/0
922	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	-	- -	06/2017	- -	0/4
923	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24(O) -	0/4
924	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	10/2014	437.39 -	437.39	-	06/2018 -	06/2018	0(O) -	0/4
925	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	10/2014	463.49 -	463.49	-	06/2018 -	06/2018	0(O) -	0/4
926	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/0
927	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
928	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI,TAMIL NADU , .	12/2014	451.58 -	451.58	-	06/2017 -	06/2017	0(O) -	0/0
929	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH , PPP (ANNUITY)	06/2014	569.38 -	569.38	737.51	06/2016 -	06/2016	0(O) -	0/0
930	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA , .	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
931	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]DORTH,HARYANA , PPP (BOT)	03/2013	959.25 -	959.25	-	06/2016 -	06/2016	0(O) -	0/0
932	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH , .	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
933	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL , .	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
934	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR , .	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
935	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	-	06/2018 -	06/2018	0(O) -	0/0
936	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH , .	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
937	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH , .	01/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018	0(O) -	0/0
938	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH , .	12/2015	667.00 -	667.00	-	06/2018 -	06/2018	0(O) -	0/0
939	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , .	12/2003	245.00 -	245.00	214.17	03/2008 07/2016	07/2016	100(O) 0(R)	0/0
940	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE , PPP (BOT)	02/2011	998.79 -	998.79	1,655.11	08/2013 -	07/2017	47(O) -	0/0
941	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , .	11/2011	478.51 -	478.00	277.41	10/2013 -	07/2016	33(O) -	0/0
942	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	-	07/2016 -	07/2016	0(O) -	0/0
943	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24(O) -	0/1
944	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	-	07/2017 -	07/2017	0(O) -	0/0
945	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN , .	07/2015	455.60 -	455.60	26.50	07/2017 -	07/2017	0(O) -	0/0
946	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , .	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
947	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	934.81	07/2017 -	07/2017	0(O) -	0/0
948	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , .	09/2014	479.00 -	479.00	349.60	- -	07/2016	- -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
949	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , .	06/2016	667.00 -	667.00	-	07/2018 -	07/2018	0(O) -	0/0
950	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
951	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM , .	12/2003	175.96 -	175.96	304.17	04/2008 08/2016	08/2016	100(O) 0(R)	0/0
952	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , .	12/2003	160.00 -	160.00	197.40	05/2008 07/2016	08/2016	99(O) 1(R)	0/0
953	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	1,070.90	05/2013 -	08/2016	39(O) -	0/0
954	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE , PPP (BOT)	02/2011	1,078.84 -	1,078.84	1,876.89	08/2013 -	08/2016	36(O) -	0/0
955	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,313.00	02/2014 -	08/2016	30(O) -	2/2
956	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDON - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23(O) -	0/4
957	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , .	03/2014	503.16 -	503.16	-	08/2016 -	08/2016	0(O) -	0/0
958	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	-	08/2016 -	08/2016	0(O) -	0/0
959	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11(O) -	0/0
960	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	233.96	08/2016 -	08/2016	0(O) -	0/0
961	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00	-	08/2016 -	08/2016	0(O) -	0/0
962	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	-	08/2016 -	08/2016	0(O) -	0/0
963	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA , .	04/2010	1,170.52 -	1,170.52	1,579.15	06/2012 -	08/2016	50(O) -	0/0
964	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	-	08/2017 -	08/2017	0(O) -	0/0
965	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM , .	12/2003	217.61 309.56	309.56	370.66	04/2010 09/2016	09/2016	77(O) 0(R)	0/0
966	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40(O) -	0/0
967	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	211.68	01/2014 -	09/2016	32(O) -	0/0
968	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
969	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017	0(O) -	0/0
970	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA , .	05/2015	709.00 -	709.00	-	09/2017 -	09/2017	0(O) -	0/0
971	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND , .	09/2015	341.61 -	341.61	89.15	09/2017 -	09/2017	0(O) -	0/0
972	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN , .	09/2014	425.19 -	425.19	184.07	09/2016 -	09/2016	0(O) -	0/0
973	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH , .	04/2014	351.34 -	351.34	133.92	01/2016 -	09/2016	8(O) -	0/0
974	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH , .	09/2015	368.73 -	368.73	58.64	09/2016 -	09/2017	12(O) -	0/0
975	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13(O) -	0/0
976	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA , .	12/2012	438.75 -	438.75	-	09/2016 -	09/2016	0(O) -	0/0
977	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	994.21	- -	09/2016	- -	0/0
978	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25(O) -	0/0
979	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	-	- -	10/2017	- -	0/4
980	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
981	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	19.72	10/2018 -	10/2018	0(O) -	0/4
982	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016	0(O) -	0/0
983	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , .	04/2014	495.78 -	495.78	195.93	01/2016 -	10/2016	9(O) -	0/0
984	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , .	01/1991	269.26 -	269.26	-	10/2016 -	10/2016	0(O) -	0/0
985	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	0(O) -	0/0
986	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	-	10/2017 -	10/2017	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
987	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH, BIHAR , ITEM RATE	01/1991	358.22 -	358.22	-	10/2016 -	10/2016	0(O) -	0/0
988	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP, UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	0(O) -	0/0
989	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD, ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	0(O) -	0/0
990	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN , .	10/2015	597.00 -	597.00	-	10/2017 -	10/2017	0(O) -	0/0
991	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,253.44	11/2016 -	11/2016	0(O) -	0/0
992	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP, MAHARASHTRA , EPC	06/2014	260.39 -	260.39	-	11/2016 -	11/2016	0(O) -	0/4
993	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP, MAHARASHTRA , EPC	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(O) -	0/4
994	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA , EPC	01/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017	0(O) -	0/0
995	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
996	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD, ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	28.66	11/2014 -	11/2016	24(O) -	0/4
997	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM , EPC	03/2015	168.39 -	168.39	-	11/2018 -	11/2018	0(O) -	0/4
998	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM , EPC	10/2014	588.95 -	588.95	-	11/2018 -	11/2018	0(O) -	0/4
999	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA , EPC	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24(O) -	0/0
1000	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA , EPC	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24(O) -	0/0
1001	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU , .	05/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017	0(O) -	0/0
1002	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU , .	11/2014	563.92 -	563.92	-	11/2016 -	11/2016	0(O) -	0/0
1003	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA , EPC	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017	0(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1004	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM , .	12/2003	230.00 -	230.00 -	-	06/2005 -	12/2016	138(O) -	0/0
1005	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM , .	12/2003	212.00 -	212.00 -	-	09/2007 -	12/2016	111(O) -	0/0
1006	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA , .	02/2011	193.45 -	193.45 -	30.63	11/2012 -	12/2016	49(O) -	0/0
1007	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00 -	-	09/2013 -	12/2016	39(O) -	0/0
1008	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55 -	1,778.42	03/2013 -	12/2016	45(O) -	0/0
1009	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30 -	880.14	02/2013 -	12/2016	46(O) -	0/0
1010	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00 -	-	12/2013 -	12/2016	36(O) -	0/0
1011	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00 -	303.94	05/2013 -	12/2017	55(O) -	0/0
1012	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00 -	622.74	10/2013 -	12/2017	50(O) -	0/0
1013	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00 -	604.57	07/2013 -	12/2016	41(O) -	0/0
1014	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA , PPP (BOT)	07/2011	586.00 -	586.00 -	-	01/2014 -	12/2016	35(O) -	0/0
1015	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00 -	437.14	09/2013 -	12/2016	39(O) -	0/0
1016	2-LANING WITH PAVED SHOULDER OF MUZZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR , PPP (BOT)	07/2012	356.40 -	356.40 -	347.00	07/2014 -	12/2017	41(O) -	0/0
1017	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE , PPP (ANNUITY)	04/2012	624.00 -	624.00 -	343.75	04/2014 -	12/2016	32(O) -	0/0
1018	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00 -	278.17	02/2015 -	12/2017	34(O) -	0/0
1019	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA , PPP (BOT)	10/2013	283.25 -	283.25 -	176.11	10/2015 -	12/2016	14(O) -	0/0
1020	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD, TELANGANA , EPC	10/2014	244.30 156.09	156.09	61.17	12/2016 -	12/2016	0(O) -	0/4
1021	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH , .	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12(O) -	0/2
1022	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH , .	07/2015	333.21 -	333.21 -	-	12/2015 -	12/2016	12(O) -	0/0
1023	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU , .	06/2015	563.92 -	563.92 -	-	12/2017 -	12/2017	0(O) -	0/0
1024	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH , .	06/2014	301.04 -	301.04 -	32.54	01/2016 -	12/2016	11(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1025	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA , .	06/2015	996.37 -	996.37	-	12/2017 -	12/2017	0(O) -	0/0
1026	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	-	12/2017 -	12/2017	0(O) -	0/0
1027	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	283.72	11/2016 -	12/2016	1(O) -	0/0
1028	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , .	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	0(O) -	0/0
1029	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , .	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
1030	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB , .	10/2015	447.29 -	447.29	-	12/2017 -	12/2017	0(O) -	0/0
1031	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , .	08/2015	854.80 -	854.80	-	-	-	-	0/0
	Total		248,173.44 -	250,520.01	81,738.36				27/166
	<u>SHIPPING AND PORTS</u>								
1032	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	841.02	10/2008 -	-	-	0/0
1033	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	415.80	12/2010 -	01/2016	-	0/0
1034	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , .	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1035	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120(O) 2(R)	0/0
1036	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , .	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017	0(O) -	0/1
1037	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017	0(O) -	0/2
1038	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , .	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1039	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017	0(O) -	0/1
	Total		4,117.75 -	5,048.81	1,826.73				0/4
	<u>TELECOMMUNICATIONS</u>								
1040	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , .	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20(O) -	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1041	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17	2,011.17	1,360.00	09/2014	03/2017	30(O)	0/70
	Total		15,445.17	15,345.17	2,720.00				0/70
	<u>URBAN DEVELOPMENT</u>								
1042	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , .	05/2006	6,395.00	11,609.00	-	06/2011	-	-	3/3
1043	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB , .	08/2005	191.24	185.57	173.21	08/2007	-	-	0/0
1044	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , .	07/2012	884.30	884.30	238.19	08/2014	-	-	0/0
1045	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU , .	12/2015	209.00	209.00	-	-	-	-	0/0
1046	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA , .	02/2014	26,405.14	26,405.14	-	02/2019	02/2019	0(O)	0/0
1047	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , .	12/2012	188.87	188.87	91.53	12/2014	03/2017	27(O)	0/1
1048	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , .	11/2012	270.83	270.83	-	11/2014	03/2016	16(O)	0/0
1049	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA , .	06/2010	205.00	191.97	119.44	03/2012	03/2017	60(O)	0/0
1050	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , .	06/2014	157.84	157.84	30.67	03/2017	03/2017	0(O)	0/0
1051	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA , .	08/2014	8,680.00	8,680.00	74.92	03/2018	03/2018	0(O)	0/0
1052	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL , .	02/2014	156.57	156.57	29.17	09/2015	04/2017	19(O)	0/7
1053	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , .	05/2012	405.01	405.01	-	12/2014	04/2016	16(O)	0/3
1054	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL , .	01/2009	225.81	225.81	139.88	06/2012	05/2016	47(O)	10/16
1055	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , .	09/2012	171.86	171.86	12.23	03/2016	05/2017	14(O)	0/6
1056	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI , .	05/2009	261.85	261.85	171.26	05/2013	06/2016	37(O)	0/0
1057	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA , .	07/2012	5,181.79	5,181.79	2,562.95	07/2017	06/2017	-1(O)	0/0

Sector Wise Details									
(February 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1058	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR , .	02/2012	171.10 202.00	202.00	191.99	09/2014 07/2015	07/2015	-	0/0
1059	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , .	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
1060	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU , .	02/2009	14,600.00 14,600.00	14,600.00	11,776.56	12/2015 -	08/2016	8(O) -	1/24
1061	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU , .	04/2014	332.72 -	332.72	93.89	09/2016 -	09/2016	0(O) -	0/0
1062	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA , .	12/2012	315.00 315.00	315.00	176.16	06/2015 08/2016	10/2016	16(O) 2(R)	0/0
1063	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , .	06/2012	4,264.00 -	4,264.00	1,162.27	11/2019 -	11/2019	0(O) -	0/7
1064	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , .	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9(O) -	0/0
1065	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI , .	01/2010	162.90 -	162.90	160.00	07/2012 12/2015	12/2015	-	0/0
1066	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA , .	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1067	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA , .	11/2012	238.43 -	238.43	-	02/2015 -	-	-	0/0
1068	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , .	02/2011	241.33 -	241.33	70.64	11/2014 -	-	-	0/0
1069	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , .	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
1070	REHABILITATION AND STRENGTHENING OF SEWORAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH , .	08/2007	246.90 -	246.90	-	- -	-	-	0/0
1071	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , .	02/2014	388.00 -	388.00	-	01/2015 -	-	-	0/1
	Total		134,055.93 -	139,282.13	37,447.76				14/68
	Grand Total		1,266,248.36	1,426,985.93	566,058.05				1840/3936


Summary of projects in the Flash Report for the month of February, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1063
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects Added in Current Month	10
Number of Projects in Current Month	1071


Brief Analysis

Project Status with respect to Original Schedule: Out of 1071 projects, 5 projects are ahead of schedule, 258 projects are on schedule 341 projects are delayed. 433 projects do not have fixed dates of commissioning. 34 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

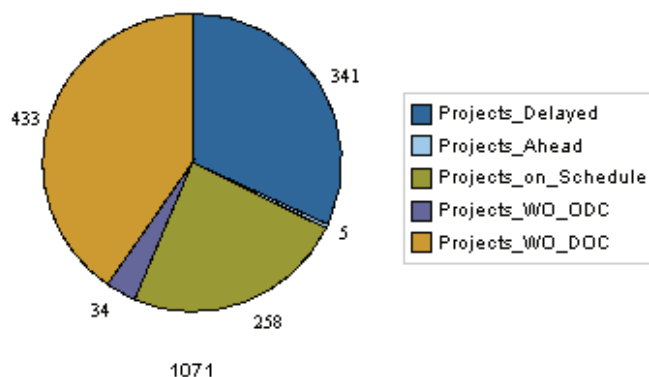

Investment Scenario

Total original cost of implementation of 1071 projects when sanctioned, was of the order of Rs. 1266248.36 crore but this was subsequently revised to Rs. 1426985.93 crore implying a cost overrun of 12.7%. The expenditure incurred on these projects till February, 2016 is Rs. 566058.05 crore, which is 39.7% of the revised cost of the projects.

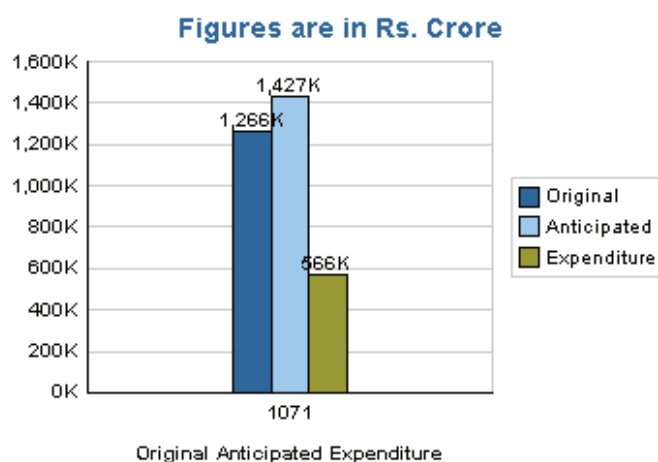

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

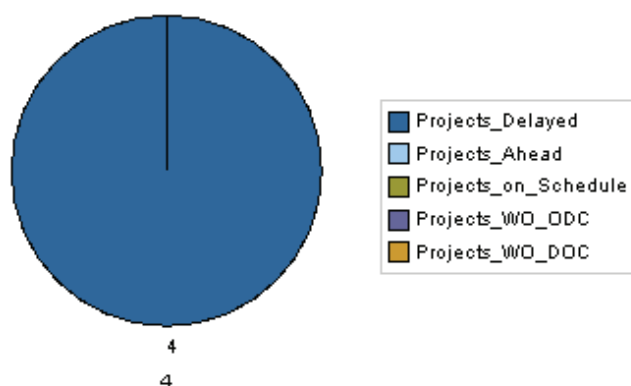

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till February, 2016 is Rs. 39893.65 crore, which is 76.8% of the revised cost of the projects.

Figures are in Rs. Crore

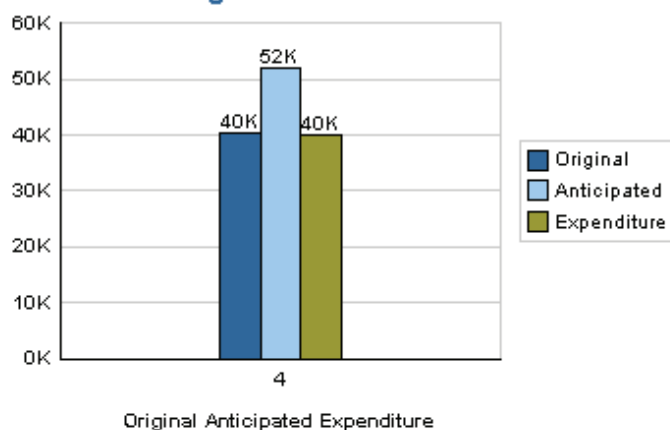

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 1 project is delayed. 2 projects do not have fixed dates of commissioning.

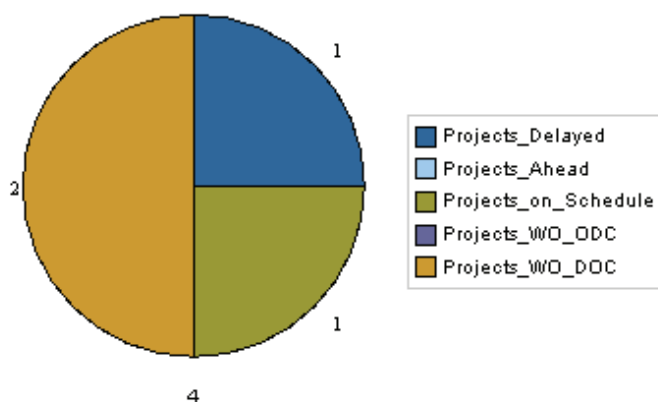

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till February, 2016 is Rs. 776.37 crore, which is 65.5% of the revised cost of the projects.

Figures are in Rs. Crore

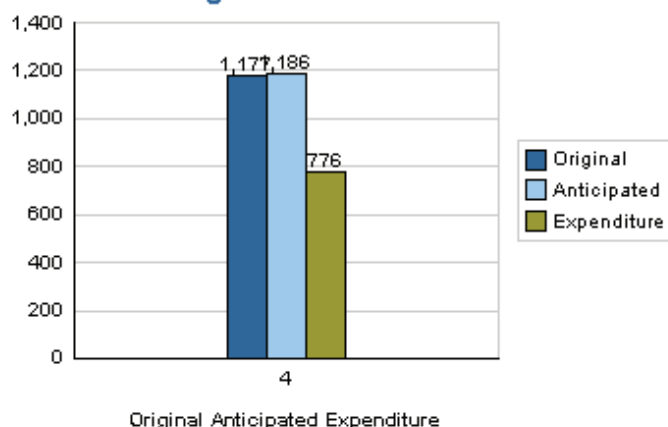

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	88
Number of Projects On Schedule	43
Number of Projects Delayed	43
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 88 projects, 1 project is ahead of schedule, 43 projects are on schedule 43 projects are delayed. 1 project does not have fixed dates of commissioning.

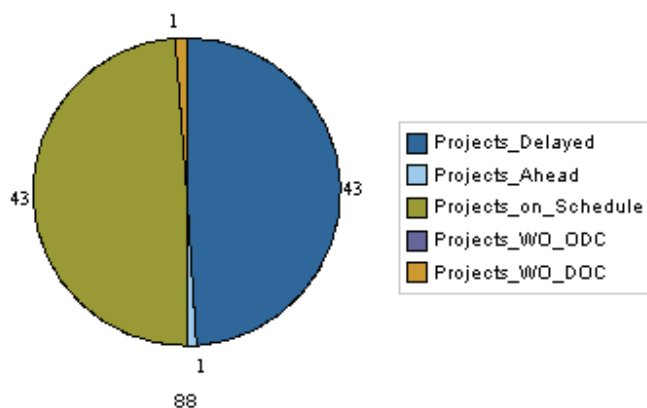

Investment Scenario

Total original cost of implementation of 88 projects when sanctioned, was of the order of Rs. 60408.62 crore but this was subsequently anticipated to Rs. 61521.55 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till February, 2016 is Rs. 13803.48 crore, which is 22.4% of the revised cost of the projects.

Figures are in Rs. Crore

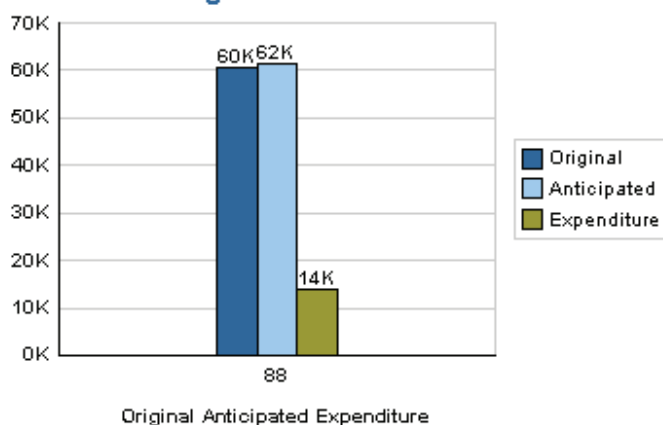

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	34
Number of Projects On Schedule	14
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning 5


Brief Analysis

Project Status with respect to Original Schedule: Out of 34 projects, 14 projects are on schedule 15 projects are delayed. 5 projects do not have fixed dates of commissioning.

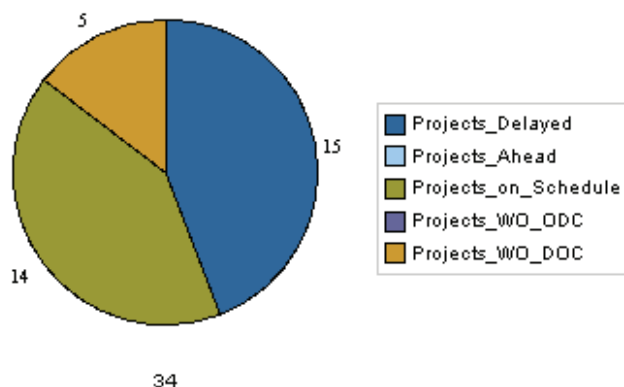

Investment Scenario

Total original cost of implementation of 34 projects when sanctioned, was of the order of Rs. 54044.86 crore but this was subsequently anticipated to Rs. 54574.3 crore implying a cost overrun of 1%. The expenditure incurred on these projects till February, 2016 is Rs. 30103.02 crore, which is 55.2% of the revised cost of the projects.

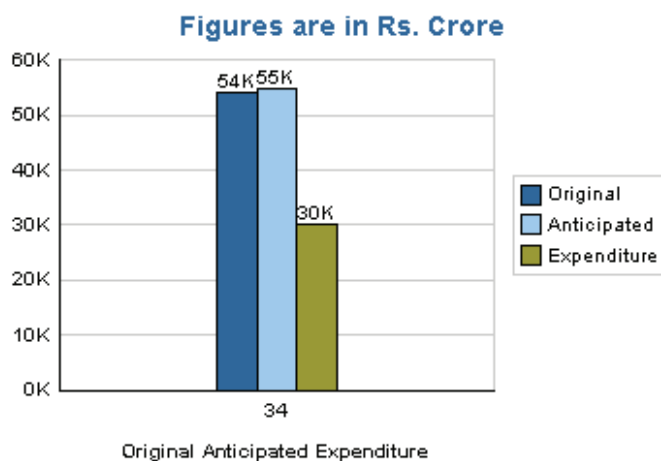

Sector wise current status of projects on the Flash Report

PETROLEUM


Current Status:

Number of Projects	66
Number of Projects On Schedule	20
Number of Projects Delayed	36
Number of Projects Ahead	2

Number of Projects Without Date Of Commissioning	8
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 66 projects, 2 projects are ahead of schedule, 20 projects are on schedule 36 projects are delayed. 8 projects do not have fixed dates of commissioning.

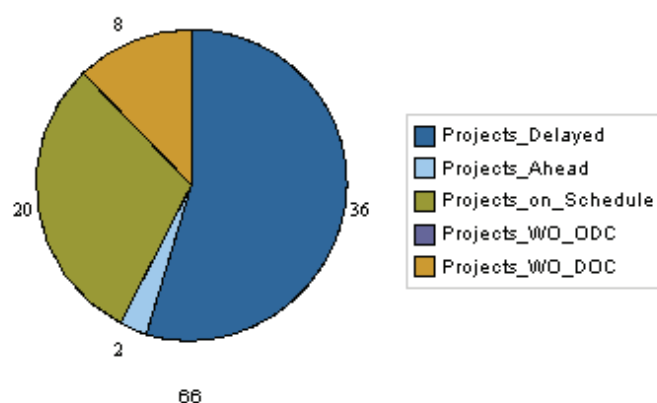

Investment Scenario

Total original cost of implementation of 66 projects when sanctioned, was of the order of Rs. 137131.44 crore but this was subsequently anticipated to Rs. 145764.07 crore implying a cost overrun of 6.3%. The expenditure incurred on these projects till February, 2016 is Rs. 68558.74 crore, which is 47% of the revised cost of the projects.

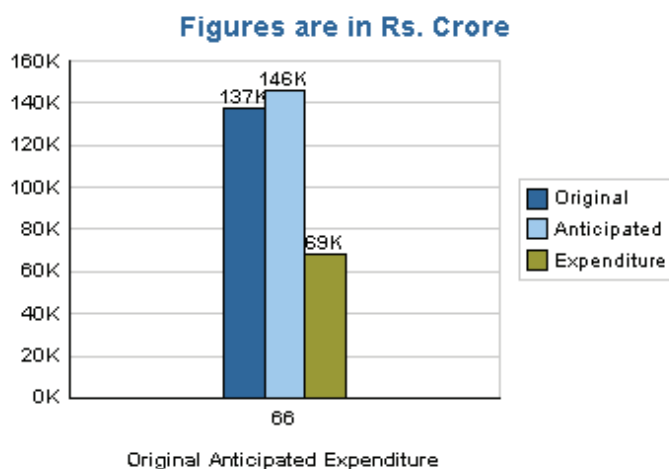

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	111
Number of Projects On Schedule	44
Number of Projects Delayed	60
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 111 projects, 1 project is ahead of schedule, 44 projects are on schedule 60 projects are delayed. 6 projects do not have fixed dates of commissioning.

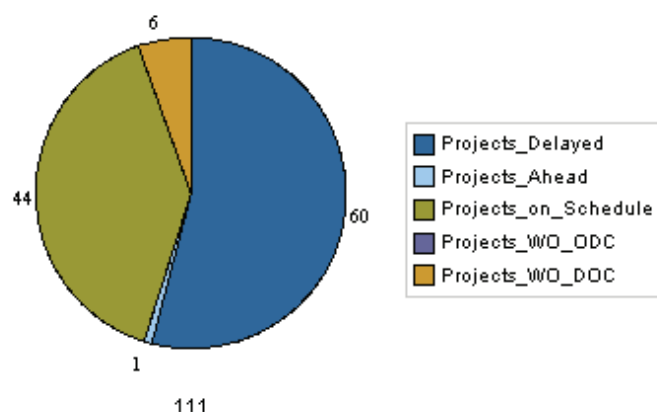

Investment Scenario

Total original cost of implementation of 111 projects when sanctioned, was of the order of Rs. 304580.02 crore but this was subsequently anticipated to Rs. 353192.66 crore implying a cost overrun of 16%. The expenditure incurred on these projects till February, 2016 is Rs. 185284.79 crore, which is 52.5% of the revised cost of the projects.

Figures are in Rs. Crore

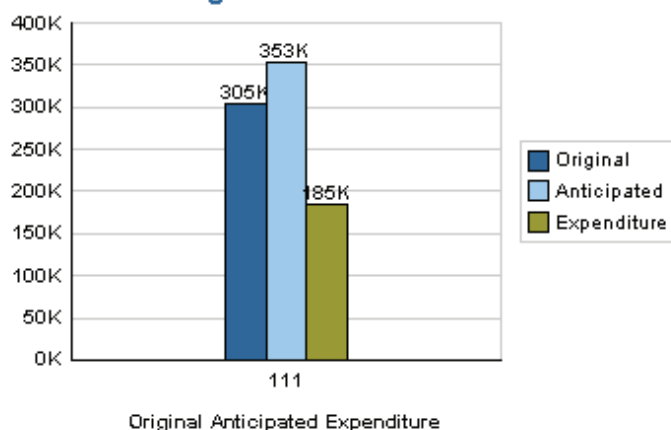

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	9
Number of Projects On Schedule	4
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 4 projects are on schedule 4 projects are delayed. 1 project does not have fixed dates of commissioning.

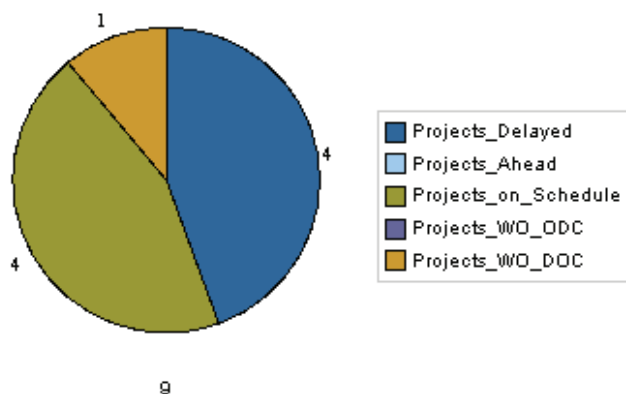

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 2563.15 crore but this was subsequently anticipated to Rs. 2563.15 crore. The expenditure incurred on these projects till February, 2016 is Rs. 1018.4 crore, which is 39.7% of the revised cost of the projects.

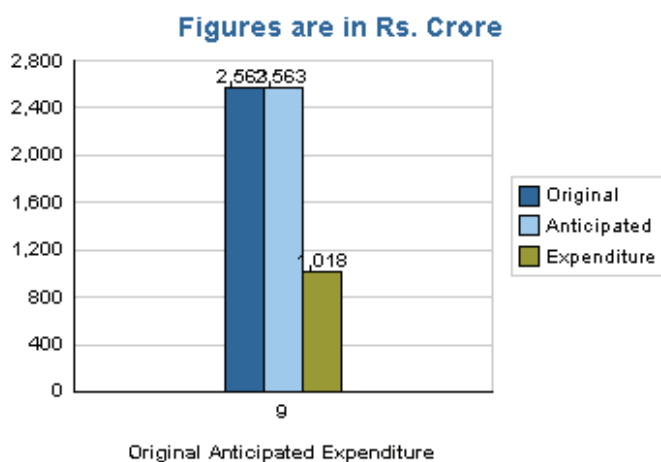

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	298
Number of Projects On Schedule	5
Number of Projects Delayed	32
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	234


Brief Analysis

Project Status with respect to Original Schedule: Out of 298 projects, 5 projects are on schedule 32 projects are delayed. 234 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

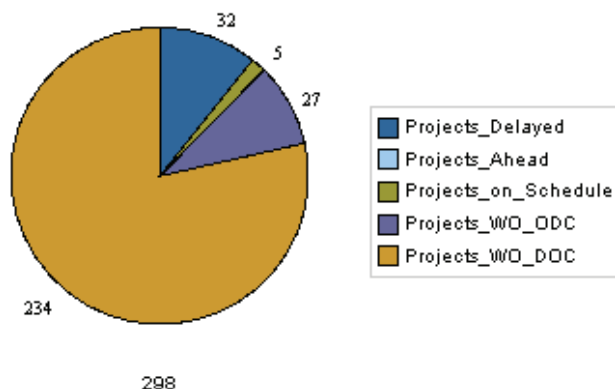

Investment Scenario

Total original cost of implementation of 298 projects when sanctioned, was of the order of Rs. 254176.67 crore but this was subsequently anticipated to Rs. 329512.54 crore implying a cost overrun of 29.6%. The expenditure incurred on these projects till February, 2016 is Rs. 93586.56 crore, which is 28.4% of the revised cost of the projects.

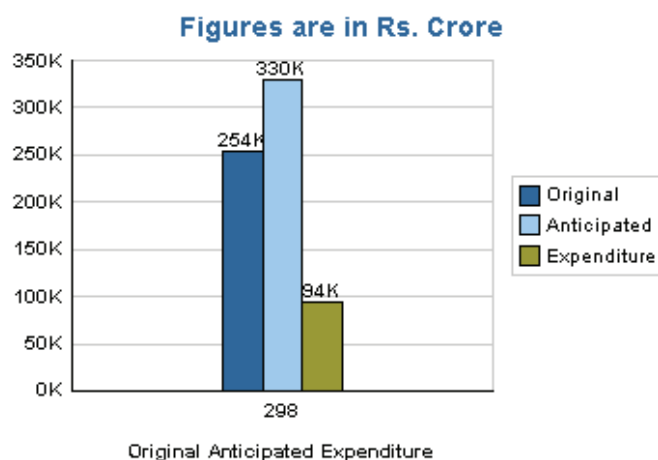

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	411
Number of Projects On Schedule	113
Number of Projects Delayed	130
Number of Projects Without Original Date of Commissioning	7
Number of Projects Without Date Of Commissioning	161


Brief Analysis

Project Status with respect to Original Schedule: Out of 411 projects, 113 projects are on schedule 130 projects are delayed. 161 projects do not have fixed dates of commissioning. 7 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

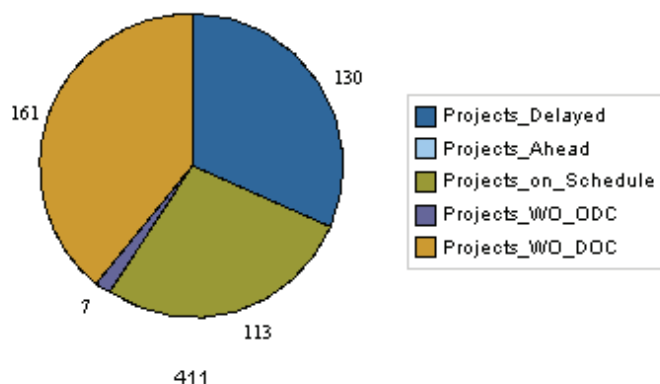

Investment Scenario

Total original cost of implementation of 411 projects when sanctioned, was of the order of Rs. 248173.44 crore but this was subsequently anticipated to Rs. 250520.01 crore implying a cost overrun of .9%. The expenditure incurred on these projects till February, 2016 is Rs. 81738.36 crore, which is 32.6% of the revised cost of the projects.

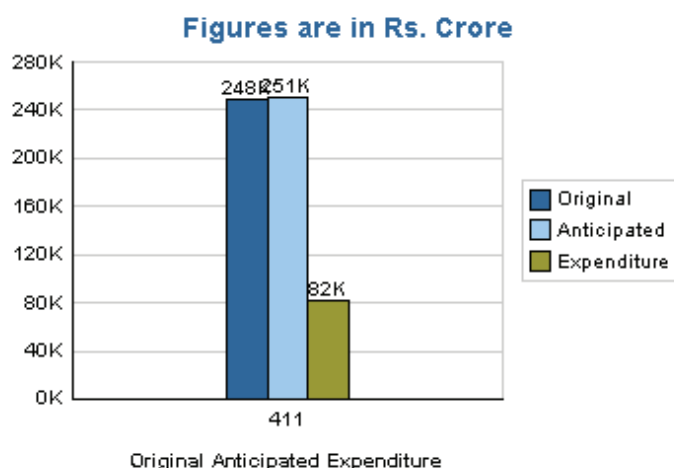

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

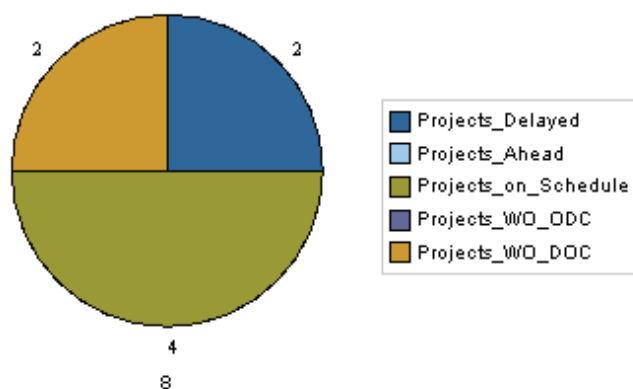

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5048.81 crore implying a cost overrun of 22.6%. The expenditure incurred on these projects till February, 2016 is Rs. 1826.73 crore, which is 36.2% of the revised cost of the projects.

Figures are in Rs. Crore

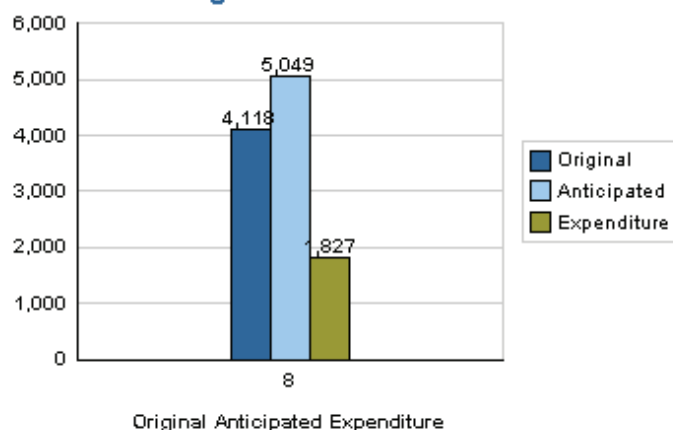

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

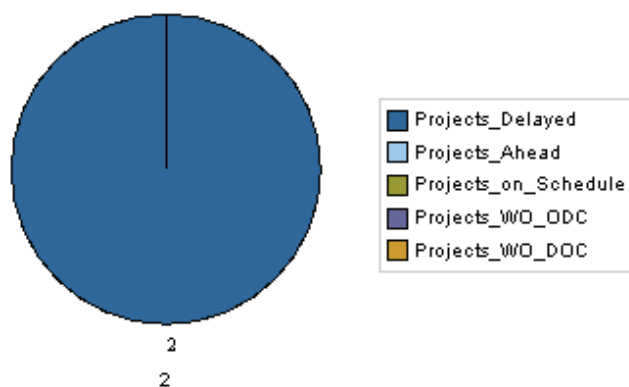

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 15445.17 crore but this was subsequently anticipated to Rs. 15345.17 cr The expenditure incurred on these projects till February, 2016 is Rs. 2720 crore, which is 17.7% of the revised cost of the projects.

Figures are in Rs. Crore

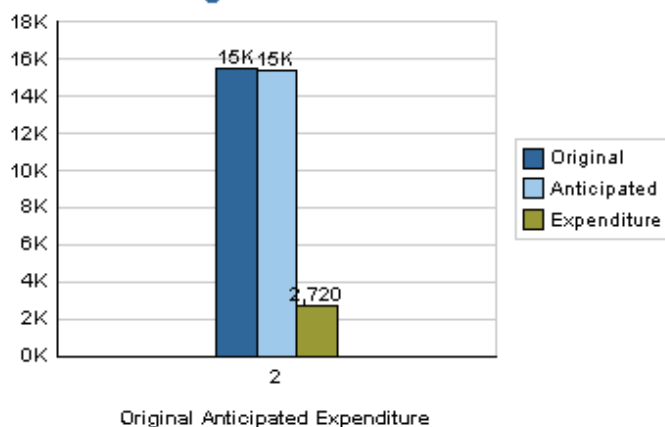

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	30
Number of Projects On Schedule	6
Number of Projects Delayed	11
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	12

Brief Analysis


Project Status with respect to Original Schedule: Out of 30 projects, 1 project is ahead of schedule, 6 projects are on schedule 11 projects are delayed. 12 projects do not have fixed dates of commissioning.

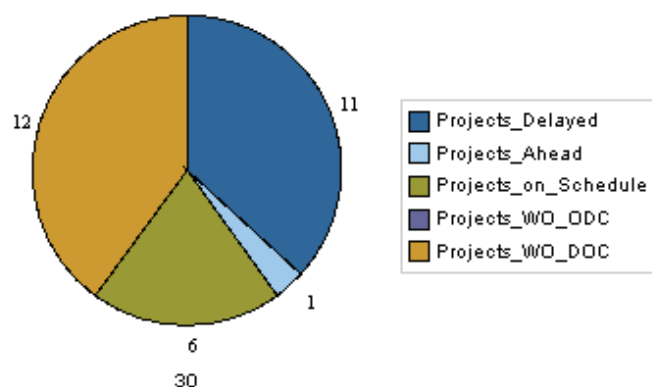

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 134055.93 crore but this was subsequently anticipated to Rs. 139282.13 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till February, 2016 is Rs. 37447.76 crore, which is 26.9% of the revised cost of the projects.

Figures are in Rs. Crore

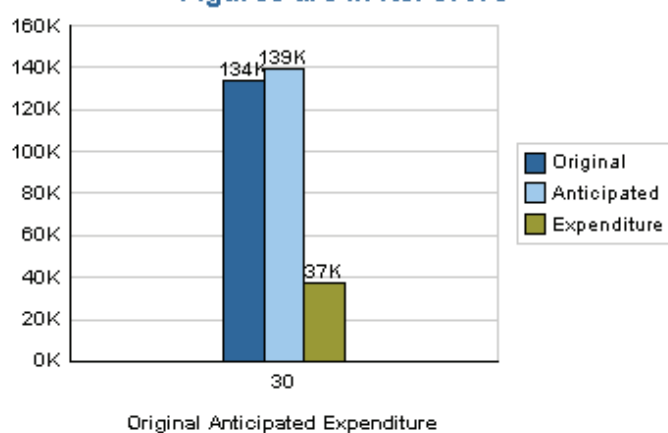

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	22.96
2	ANDHRA PRADESH	47	21,226.93	23,061.97	8,962.84
3	ARUNACHAL PRADESH	14	11,758.7	28,124.97	14,041.88
4	ASSAM	50	28,795.71	44,498.17	29,340.33
5	BIHAR	64	57,872.84	72,300.43	39,167.53
6	CHHATISGARH	40	86,425.52	87,703.17	47,878.41
7	D & N HAVELI	1	6,086.08	6,086.08	673.95
8	DELHI	16	49,963.05	49,963.05	22,727.07
9	GOA	8	3,925.48	3,907.87	341.03
10	GUJARAT	31	30,605.81	31,660.45	15,448.63
11	HARYANA	20	13,986.73	15,957.35	7,605.33
12	HIMACHAL PRADESH	5	8,088.55	14,487.83	6,755.09
13	JAMMU AND KASHMIR	9	25,620.25	45,229.68	15,278.18
14	JHARKHAND	44	41,826.84	44,389.59	13,211.78
15	KARNATAKA	42	72,113.99	87,378.98	19,005.73
16	KERALA	16	25,825.82	30,300.97	16,066.24
17	MADHYA PRADESH	52	54,020.18	56,591.41	10,006.28
18	MAHARASHTRA	73	1,21,026.1	1,29,786.02	39,783.5
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	6	6,970.03	8,194.91	2,102.63
21	MIZORAM	6	2,188.16	5,402.06	1,803.08
22	MULTI STATE	176	2,67,786.62	2,45,109.97	74,935.14
23	NAGALAND	3	6,420	8,757.12	10.44
24	ODISHA	47	71,450.12	80,688.81	40,630.62
25	PUNJAB	23	11,714.51	11,712.84	2,215.48
26	RAJASTHAN	60	40,960.69	41,503.63	20,516.78
27	SIKKIM	5	2,149.08	4,999.32	562.83
28	TAMIL NADU	57	68,769.74	88,418.98	52,733.41
29	TELANGANA	32	12,335.7	15,282.09	4,221.08
30	TRIPURA	9	3,776.07	7,489.01	3,406.97
31	UTTAR PRADESH	60	52,378.07	56,264.19	19,912.64
32	UTTARAKHAND	6	9,352.4	11,651.71	5,605.7
33	WEST BENGAL	46	49,513.36	62,924.88	28,296.5
TOTAL		1,071	12,66,248.36	14,26,985.93	5,66,058.05

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	21,160
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	5,166.65
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,460.85
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	8,188.23
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,986.06
6	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	RAILWAYS	03/1995	2,500	-	10,722.72
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) ,SWR	RAILWAYS	02/1997	295	-	1,092.98
12	GONDIA-JABALPUR (GC) , (SECR)	RAILWAYS	02/1997	386.3	-	590.26
13	KARUR-SALEM (NL) ,SR	RAILWAYS	02/1997	155.55	-	800.7
14	NANDYAL-YERRAGUNTALA (NL) ,SCR	RAILWAYS	03/1996	155.74	164.36	755.5

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	KANPUR KASGANJ MATHURA (GC) NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4
16	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	-	4,102.7
17	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
18	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
21	KATI HAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
22	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
28	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	376.18

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIND-SONEPAT (NL) ,NR	RAILWAYS	01/2004	238.56	-	639.77
30	HARIDASPUR-PARADEEP (NL)	RAILWAYS	04/1996	301.64	-	577.84
31	RAJATGARH-BARANG (LD) , ECR	RAILWAYS	04/1999	166.16	-	349.36
32	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
33	KOSI BRIDGE (NL) , ECR	RAILWAYS	04/2002	322.95	-	325.36
34	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,521.72
35	ETAWAH-MAINPURI (NL) ,NCR	RAILWAYS	04/1997	120	245.39	249.33
36	SUKINDA ROAD - ANGUL (NL) (ECOR)	RAILWAYS	04/1998	183.23	-	185.46
37	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	322.75
39	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	357.91
40	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	242
41	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	493.27
42	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	417.66

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	-	869.37
44	ANANTA OC EXPANSION PH-III (15.0 MTY)	COAL	08/2008	207.28	-	207.71
45	RAMAGUNDAM OC-II EXTENSION	COAL	12/2009	418.97	-	457.41
46	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	STEEL	03/2007	149.73	173	175.94
47	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	STEEL	05/2005	768.88	1060	1,070.97
48	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	8920	9,241.36
49	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	170.03
50	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,433.49
51	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	POWER	02/2009	509.66	-	541.66
52	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	POWER	03/2011	1,585.12	-	1,609.36
53	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	POWER	09/2011	1,940.13	-	1,959.76
54	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH	POWER	11/2011	2,127.51	-	2,338.43
55	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2	POWER	12/2011	2,422.66	-	2,448.76
56	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	POWER	01/2012	1,422.85	-	1,436.82

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	POWER	05/2015	436.68	-	436.9
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
59	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RAILWAYS	07/2006	743	-	770.18
60	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RAILWAYS	09/2006	324.9	-	351.79
61	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	896.75
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
63	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
64	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
65	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
66	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
67	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
68	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
70	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,769.59

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
72	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
73	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	259.31
74	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
75	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
76	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
77	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	1,047.1
78	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
79	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
80	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
81	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
82	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
83	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
84	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	304.17

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
86	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	311.13
87	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	295.2
88	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.4
89	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	370.66
90	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
91	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,409.36
92	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	2782.54	2,891.15
93	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,607.78
94	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
95	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,619.94
96	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
97	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,055.94
98	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	863.58

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	1,006.79
100	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
101	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
102	PUNE-SATARA (NH-4)	ROAD TRANSPORT AND HIGHWAYS	10/2010	1,724.55	-	1,778.42
103	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	453.58
104	PATNA-MUZZAFFARPUR	ROAD TRANSPORT AND HIGHWAYS	08/2010	671.3	-	880.14
105	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	830.97
106	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,911.64
107	TIRUPATI - TIRUTHANI - CHENNAI	ROAD TRANSPORT AND HIGHWAYS	04/2011	571	-	622.74
108	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	1,384.61
109	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,503.31
110	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	761.49
111	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	604.57
112	PUNE-SHOLAPUR, PKG-II	ROAD TRANSPORT AND HIGHWAYS	09/2011	835	-	1,684

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
114	BEAWAR PALI PINDWARA	ROAD TRANSPORT AND HIGHWAYS	12/2011	2,388.51	-	2,472
115	MUZAFFARNAGAR-HARIDWAR	ROAD TRANSPORT AND HIGHWAYS	09/2011	754	-	902.06
116	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,876.89
117	4-LANING OF BRAHAMPUR-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,655.11
118	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	2,310.32
119	ETAWAH CHAKERI	ROAD TRANSPORT AND HIGHWAYS	03/2013	1,573	-	1,844.5
120	KOTWA TO DEWAPUR (LMNHP-10)	ROAD TRANSPORT AND HIGHWAYS	11/2005	240	-	295.38
121	2 LANING OF SHILLONG NONGSTON SECTION OF NH 44 AND NONGSTON TURA STATE ROAD UNDER PHASE A OF SA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,494.48	-	2,090
122	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR	ROAD TRANSPORT AND HIGHWAYS	06/2014	569.38	-	737.51
123	4 LANING OF GOMTI CHAURAH - UDAIPUR	ROAD TRANSPORT AND HIGHWAYS	03/2012	914.5	-	1,097.62
124	NAGPUR - KONDHALI	ROAD TRANSPORT AND HIGHWAYS	09/2005	168	-	226.24
125	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,170.52	-	1,579.15
126	ROHTAK - BAWAL (APPROVED LENGTH 97 KM)	ROAD TRANSPORT AND HIGHWAYS	02/2010	650	-	813.91

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	SHIPPING AND PORTS	01/2007	366.39	-	415.8

Annexure - III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(February 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
2	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	74.10	02/2017 -	03/2016
	Total		188.75 -	188.75	74.10		
	<u>PETROLEUM</u>						
3	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	314.92	01/2017 -	06/2016
	Total		419.04 -	419.04	314.92		
	<u>URBAN DEVELOPMENT</u>						
4	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						
5	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	826.03	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	826.03		
	Grand Total		12,413.90	12,413.90	3,781.52		

Annexure - IV

Details of On Schedule Projects w.r.t. Original Schedule

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	314.61	22.96	09/2018 -	09/2018
	Total		314.61 -	314.61	22.96		
	<u>COAL</u>						
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016
4	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	179.12	03/2021 -	03/2021
6	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	205.40	03/2017 -	03/2017
8	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	66.37	03/2025 -	03/2025
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.96	03/2026 -	03/2026
10	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
11	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017
12	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	101.81	03/2021 -	03/2021
13	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
14	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
15	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
16	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	141.38	03/2020 -	03/2020
17	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	800.01	03/2023 03/2023	03/2023
18	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
19	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	224.02	03/2020 -	03/2020
20	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016

							(February 2016)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
22	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
23	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	820.31	03/2016 -	03/2016
24	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
25	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	73.30	03/2019 -	03/2019
26	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
27	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	109.63	03/2020 -	03/2020
28	GOKUL - [N06000120]	11/2014	267.67 -	267.67	185.72	03/2018 -	03/2018
29	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
30	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.89	03/2019 -	03/2019
31	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
32	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
33	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	48.58	03/2021 -	03/2021
34	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	165.06	03/2018 -	03/2018
35	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.23	12/2019 -	12/2019
36	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
37	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
38	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
39	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
40	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019
41	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
42	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
43	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	53.93	03/2023 -	03/2023
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
	Total		35,111.36 -	34,902.86	4,556.33		

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
45	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	52.22	11/2016 -	11/2016
	Total		197.79 -	209.44	52.22		
	<u>HEALTH AND FAMILY WELFARE</u>						
46	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	14.38	03/2018 -	03/2018
47	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	67.84	05/2017 -	05/2017
48	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017
49	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017
	Total		1,172.57 -	1,172.57	122.02		
	<u>MINES</u>						
50	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	6.61	09/2017 -	09/2017
51	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]	12/2015	355.13 -	355.13	-	11/2016 -	11/2016
52	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	-	11/2016 -	11/2016
	Total		2,555.63 -	2,555.63	6.61		
	<u>PETROLEUM</u>						
53	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	641.31	05/2017 -	05/2017
54	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	120.23	12/2017 -	12/2017
55	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	24.29	01/2018 -	01/2018
56	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018
57	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	4,619.94	420.28	12/2017 -	12/2017
58	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
59	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	195.63	-	09/2018 -	09/2018
60	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	181.02	78.73	01/2017 -	01/2017
61	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	41.18	02/2020 -	02/2020

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
63	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	112.97	09/2017 -	09/2017
64	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	75.40	07/2016 -	07/2016
65	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	170.03	09/2016 -	09/2016
66	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	10,366.19	05/2016 -	05/2016
67	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	142.35	12/2016 -	12/2016
68	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018
69	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,954.21	05/2017 05/2017	05/2017
70	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	7.30	03/2017 -	03/2017
71	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.00	58.18	07/2016 -	07/2016
72	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
	Total		46,834.10 -	48,661.10	15,811.91		
	<u>POWER</u>						
73	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,121.00	12/2016 -	12/2016
74	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
75	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
76	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	12.70	11/2017 -	11/2017
77	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018
78	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	258.10	04/2018 -	04/2018
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	236.90	06/2016 -	06/2016
80	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	21.10	03/2018 -	03/2018
81	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	120.00	10/2016 -	10/2016
82	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
83	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	-	05/2018 -	05/2018

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.20	07/2018 -	07/2018
85	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,713.00	06/2017 -	06/2017
86	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	436.90	12/2016 -	12/2016
87	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	101.40	08/2016 -	08/2016
88	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	121.97	04/2020 -	04/2020
89	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	67.80	11/2017 -	11/2017
90	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	71.60	02/2017 -	02/2017
91	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,473.00	09/2019 -	09/2019
92	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
93	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	5,361.60	01/2018 -	01/2018
94	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,829.00	08/2018 -	08/2018
95	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
96	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
97	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	96.20	11/2016 -	11/2016
98	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	779.10	05/2016 -	05/2016
99	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	387.90	05/2018 -	05/2018
100	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016
101	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,056.00	03/2019 -	03/2019
102	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
103	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	23.30	03/2018 -	03/2018
104	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	5,025.00	09/2017 -	09/2017
105	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	163.00	09/2019 -	09/2019
106	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	-	06/2018 -	06/2018
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	125.20	06/2016 -	06/2016

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62	871.62	6.20	10/2017	10/2017
109	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47	400.47	46.70	04/2017	04/2017
110	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58	14,366.58	2,449.00	02/2019	02/2019
111	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19	244.19	-	07/2018	07/2018
112	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33	780.33	0.90	07/2017	07/2017
113	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36	6,517.36	345.30	04/2018	04/2018
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94	312.94	26.50	05/2016	05/2016
115	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30	1,479.30	84.40	04/2017	04/2017
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04	305.04	-	03/2017	03/2017
	Total		134,017.18	134,017.18	29,319.85		
	<u>RAILWAYS</u>						
117	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41	2,030.50	3.61	02/2019	02/2019
118	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77	209.00	2.64	12/2016	12/2016
119	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66	423.66	163.59	03/2017	03/2017
120	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60	299.60	-	03/2017	03/2017
121	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09	3,845.60	2.33	02/2020	02/2020
	Total		2,670.53	6,808.36	172.17		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
122	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00	667.00	-	06/2018	06/2018
123	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]	7/2014	401.11	401.11	-	01/2017	01/2017
124	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12	206.12	105.78	04/2017	04/2017
125	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23	239.23	-	12/2017	12/2017
126	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53	1,027.53	-	06/2018	06/2018
127	PADI - DAHOD - [N24000353]	11/2014	279.14	279.14	60.87	05/2017	05/2017

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
128	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
129	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017
130	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342	5/2015	709.00 -	709.00	-	09/2017 -	09/2017
131	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
132	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	16.90	02/2018 -	02/2018
133	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
134	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	85.17	04/2017 -	04/2017
135	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	26.50	07/2017 -	07/2017
136	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61 -	241.61	37.55	02/2017 -	02/2017
137	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
138	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
139	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
140	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
141	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
142	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
143	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240	3/2014	240.10 -	240.10	147.69	03/2016 -	03/2016
144	VADODARA-SURAT SECTION - [N24000361	3/2014	503.16 -	503.16	-	08/2016 -	08/2016
145	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	5.00	05/2017 -	05/2017
146	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
147	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344	9/2014	425.19 -	425.19	184.07	09/2016 -	09/2016
148	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368	11/2014	563.92 -	563.92	-	11/2016 -	11/2016

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
150	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	89.15	09/2017 -	09/2017
151	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
152	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016
153	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	-	08/2016 -	08/2016
154	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
155	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
156	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]	3/2013	959.25 -	959.25	-	06/2016 -	06/2016
157	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	233.96	08/2016 -	08/2016
158	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,253.44	11/2016 -	11/2016
159	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	37.00	04/2018 -	04/2018
160	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
161	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
162	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	10/2014	437.39 -	437.39	-	06/2018 -	06/2018
163	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
164	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
165	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
166	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
167	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	12.80	02/2017 -	02/2017
168	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
169	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	-	05/2018 -	05/2018

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
170	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	10/2014	463.49 -	463.49	-	06/2018 -	06/2018
171	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
172	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
173	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
174	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	61.17	12/2016 -	12/2016
175	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
176	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
177	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
178	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
179	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
180	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
181	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
182	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
183	REHABILATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
184	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
185	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016
186	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
187	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
188	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	-	08/2016 -	08/2016

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
189	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
191	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
192	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
193	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
194	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
195	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
196	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	3/2015	829.00 -	829.00	-	03/2018 -	03/2018
197	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
198	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
199	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016
200	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
201	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
202	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
203	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
204	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
205	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
206	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
207	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
208	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
209	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
210	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
211	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
212	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
213	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
214	YAN TO NIRMAL SEREHAABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016
215	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
216	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
217	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
218	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]	6/2014	569.38 -	569.38	737.51	06/2016 -	06/2016
219	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	604.72	04/2016 -	04/2016
220	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,125.73	01/2018 -	01/2018
221	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	934.81	07/2017 -	07/2017
222	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
223	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
225	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
226	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
227	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
228	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
229	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
230	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
231	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
232	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
233	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	161.76	02/2018 -	02/2018
234	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
	Total		61,579.87 -	61,719.25	7,657.02		
	<u>SHIPPING AND PORTS</u>						
235	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017
236	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
237	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017
238	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017
	Total		928.29 -	942.12	63.91		
	<u>STEEL</u>						
239	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	3.63	09/2017 -	09/2017
240	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	26.98	10/2017 -	10/2017
241	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	196.12	12/2016 -	12/2016
242	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
243	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
244	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111	2/2014	787.29 -	787.29	251.53	12/2016 -	12/2016
245	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
246	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	28.55	09/2016 -	09/2016
247	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096	5/2015	1,154.18 -	1,154.18	28.20	12/2017 -	12/2017
248	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018

						(February 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
249	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	303.25	04/2018 -	04/2018
250	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]	8/2012	185.37 -	185.37	-	03/2016 -	03/2016
251	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	193.97	06/2016 -	06/2016
252	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	Total		12,739.20 -	12,763.59	1,279.18		
	<u>URBAN DEVELOPMENT</u>						
253	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
254	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	74.92	03/2018 -	03/2018
255	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	1,162.27	11/2019 -	11/2019
256	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017
257	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
258	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	93.89	09/2016 -	09/2016
	Total		41,058.91 -	41,058.91	1,361.75		
	Grand Total		339,180.04	345,125.62	60,425.93		

Annexure - V
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,321.16 -	2,690.85			
	<u>FERTILISERS</u>						
8	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	11/2016	5.89
	Total		197.79 -	209.44			
	<u>HEAVY INDUSTRY</u>						
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						
11	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2018	27.79
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49
13	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66
14	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
15	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
16	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83
18	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2016	16.05
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
20	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
22	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62
24	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
25	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	10/2016	19.35
	Total		59,284.75 -	69,863.51			
	<u>POWER</u>						
26	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28
27	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
28	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
29	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2016	54.59
30	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
31	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79
32	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
33	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
34	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21
35	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
36	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	07/2016	147.51
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
38	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	-	31.17
39	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91
40	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
41	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	06/2016	16.63
42	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2016	27.60
43	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
44	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93
45	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
46	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
47	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32
	Total		61,522.84 -	110,199.09			
	<u>RAILWAYS</u>						
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
49	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
50	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
51	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
52	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
53	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
54	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
55	KOTLALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
56	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
57	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
58	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
59	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
60	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
61	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	3,040.00	03/2009 -	03/2016	230.08
62	RAMGANJMUDDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
63	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
64	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
65	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
66	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
67	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
68	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
69	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
70	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
71	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56
72	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
73	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	-	-	242.28
74	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	-	03/2016	166.63
75	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	-	-	292.00
76	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	-	-	136.84
77	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012	03/2016	60.77
78	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014	03/2018	355.36
79	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012	-	43.54
80	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	-	-	252.06
81	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	-	-	109.11
82	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014	-	0.06
83	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012	-	135.68
84	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011	-	67.82
85	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012	03/2016	45.41
86	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	-	-	400.91
87	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	-	-	0.72
88	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	-	03/2015	105.59
89	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	-	01/2015	170.55
90	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	-	-	97.26
91	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	-	-	651.97
92	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	-	-	160.97
93	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	-	-	108.66
94	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	-	-	985.42
95	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	-	-	100.76

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
96	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99 -	- -	- -	183.41
97	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	- -	24.09
98	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	- -	57.65
99	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	- -	47.93
100	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	- -	79.63
101	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	- -	2.29
102	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50 -	- -	- -	0.00
103	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97 -	- -	- -	50.10
104	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	- -	14.14
105	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	- -	72.07
106	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	- -	12.38
107	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	- -	123.46
108	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00 -	01/1999 -	- -	71.50
109	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	01/1999 -	- -	53.96
110	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00 -	- -	- -	447.91
111	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98 -	03/2004 -	03/2016 -	259.68
112	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19 -	04/2008 12/2011	06/2017 -	233.08
113	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	3,500.00 -	05/2008 -	- -	1,313.23
114	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56 -	03/2012 -	- -	108.01
115	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015 -	300.67
116	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00 -	- -	- -	232.17
117	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34 -	12/2008 -	03/2018 -	245.34
118	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25 -	- -	- -	324.33
119	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75 -	03/2011 -	03/2019 -	803.12

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
120	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
121	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	-	367.76
122	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
123	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
124	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
125	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
126	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
127	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
128	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
129	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
130	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
131	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
132	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
133	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
134	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	2,434.00	03/2010 -	-	648.92
136	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
137	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
138	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
139	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
140	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
141	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
142	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
143	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
144	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
145	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
146	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
147	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.51	- -	-	28.25
148	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
149	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
150	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
151	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
152	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
153	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
154	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
155	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
156	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
157	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
158	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
159	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
160	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
161	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
162	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
163	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
164	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63
165	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147	04/2011	2,082.75 -	3,500.00	- -	-	68.05

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
166	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
167	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
168	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
169	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
170	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
171	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
172	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
173	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
174	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
175	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
176	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
177	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
178	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
179	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
180	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
181	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
182	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
183	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
184	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
185	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
186	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
187	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
188	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	-	-	55.74
189	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
190	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	-	03/2019	154.33
191	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007	03/2016	38.80
192	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	-	03/2018	251.85
193	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	-	03/2020	5.00
194	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	-	03/2018	110.44
195	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	-	03/2018	1.86
196	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	-	-	109.04
197	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71
198	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	-	03/2015	285.12
199	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	-	-	16.29
200	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	-	03/2020	30.00
201	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	-	03/2018	180.56
202	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	03/2017	63.25
203	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	-	03/2018	162.68
204	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	-	03/2018	216.06
205	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	-	03/2018	45.17
206	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	-	03/2019	47.95
207	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016	12/2017	29.06
208	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	-	-	33.02
	Total		82,833.35 -	214,601.52			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
209	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009	03/2016	28.93

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
210	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
211	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
212	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
213	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2016	106.50
214	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
215	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
216	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
217	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	161.70	07/2015 -	-	2.88
218	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25
219	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2016	30.10
220	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
221	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
222	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
223	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
224	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
225	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
226	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		5,171.67 -	7,634.21			
	<u>SHIPPING AND PORTS</u>						
227	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	03/2016	300.00

(February 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
228	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
229	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
230	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
231	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
232	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
233	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
234	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	07/2011	324.87 324.87	325.00	12/2015 -	03/2016	0.04
235	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
236	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50
	Total		1,964.58 -	2,494.02			
	<u>URBAN DEVELOPMENT</u>						
237	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
238	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]	02/2012	171.10 -	202.00	09/2014 -	07/2015	18.06
	Total		6,566.10 -	11,811.00			
	Grand Total		243,928.01	463,616.66			

Annexure - VI

Details of Delayed Projects w.r.t. Original Schedule

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,160.00	12/2008 10/2013	05/2016	89	70.54	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,166.65	09/2010 -	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	7,917.00	12/2015 10/2016	11/2018	35	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,650.00	12/2016 03/2017	12/2019	36	0	
	Total		40,442.00 -	51,918.00	39,893.65					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	417.66	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	417.66					
	<u>COAL</u>									
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	2,006.46	03/2014 -	03/2016	24	0	
7	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	504.99	03/2013 -	03/2016	36	-6.11	
8	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 -	1,228.39	869.37	03/2013 -	03/2016	36	478.5	
9	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	85.26	03/2015 -	03/2016	12	0	
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48	0	
11	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL, JHARKHAND	08/2007	163.51 -	163.51	36.16	03/2011 -	03/2016	60	0	
12	TAPIN OCP (2.5 MTY) - [N06000086]JCL, JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
13	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.46	04/2014 -	03/2016	23	0	
14	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	196.19	10/2014 -	03/2016	17	0	
15	RAJMAHAL OC EXP. - [N06000056]JCL,JHARKHAND	09/2009	153.82 -	153.82	75.24	03/2014 -	09/2016	30	0	1) Delay in clearance of Title cases pending at CBA Tribunals and authentication of GTs(genealogical Tree). 2) Delay/ non issuance of 'Patta' for land/plots allotted to PAFs shifted and being shifted in the area acquired under CBA Act.
16	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	104.25	05/2014 -	10/2016	29	0	
17	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	69.89	04/2014 -	11/2016	31	0	
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.92	03/2010 -	03/2017	84	0	
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	0	
20	JHANJRA R-VI SEAM PSLW - [N06000020]JCL, WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	0	Processing of FC stage-I and stage-II was delayed by State Forest Deptt. and State Govt.
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	91.86	03/2012 03/2018	03/2017	60	87.58	
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	210.87	03/2013 -	03/2017	48	0	
23	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	152.05	03/2010 -	03/2017	84	0	
24	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51	0	
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	207.71	03/2012 -	03/2017	60	0	
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	185.34	03/2013 -	03/2017	48	0	
27	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	94.84	03/2012 -	03/2017	60	0	Authentication of village potanga, Court cases
28	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	0	
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	70.25	03/2014 -	03/2017	36	0	Authentication of land of village

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
30	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	0	
31	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	25.28	07/2016	03/2017	8	0	Aquisition of non forest land and R&R
32	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03	249.03	118.02	03/2012	03/2018	72	0	
33	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	211.06	03/2014	03/2018	48	0	
34	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	8.03	03/2015	03/2018	36	0	
35	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2018	36	0	
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	77.44	03/2015	03/2018	36	0	
37	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56	258.56	102.72	03/2016	03/2018	24	0	
38	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45	486.27	93.51	03/2016	03/2018	24	12.97	
39	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11	5,907.11	1,499.01	12/2015 04/2018	04/2018	28	0	
40	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05	1,055.05	206.70	03/2018	07/2018	4	0	
41	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	48.66	04/2015 04/2019	04/2019	48	0	
42	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17	1,458.17	21.91	06/2015 08/2019	08/2019	50	0	
43	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	0	
44	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	0	
45	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	0	
46	MAGADH OC 20 MTY (CCL) - [N06000015]JCL, JHARKHAND	08/2008	706.40	706.40	79.03	07/2012	03/2021	104	0	
47	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	0	
48	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97	489.62	457.41	03/2012	03/2023	132	16.86	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		24,273.96	25,595.39	9,240.78					
			-							
	STEEL									
49	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	233.55	08/2014	03/2016	19	0	
50	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014	03/2016	25	39.29	
51	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015	03/2016	3	.04	
52	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	174.45	10/2013	06/2016	32	0	
53	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]JRLN, ANDHRA PRADESH	07/2011	877.73	877.73	454.15	07/2015	08/2016	13	0	
54	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91	708.91	326.57	04/2016	09/2016	5	0	
55	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	15,636.77	03/2013	11/2016	44	0	
56	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67	245.67	98.57	05/2016	12/2016	7	0	
57	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93	188.93	60.23	04/2015	12/2016	20	0	
58	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00	15,525.00	8,727.80	05/2015 12/2016	12/2016	19	0	
59	3RD CONVERTER AND 4TH CASTER - [N12000088]JRLN, ANDHRA PRADESH	07/2011	974.76	974.76	234.67	07/2016	12/2016	5	0	
60	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	175.94	175.94	12/2015	03/2017	15	17.5	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
61	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	285.39	07/2015 -	06/2017	23	0	
62	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	39.17	10/2016 -	06/2017	8	42.39	
63	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 207.00	206.71	134.61	12/2016 -	07/2017	7	17.79	
	Total		38,472.11 -	38,977.16	27,916.41					
	PETROLEUM									
64	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	31,300.53	11/2012 11/2013	02/2016	39	16.05	
65	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	322.07	06/2011 03/2012	03/2016	57	0	
66	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	187.05	12/2014 -	03/2016	15	0	
67	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,091.39	10/2011 -	03/2016	53	67.62	issues faced with local elements in the RoU.
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,011.65	05/2013 04/2016	04/2016	35	45.83	
69	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,325.28	03/2015 05/2016	05/2016	14	29.42	
70	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	
71	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	138.84	03/2014 05/2016	05/2016	26	0	
72	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	586.26	04/2015 05/2016	05/2016	13	-39.69	
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,449.53	01/2012 -	05/2016	52	70.49	Progress is slow due to heavy rains during the period, RoU issue

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
74	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,327.98	09/2012 -	06/2016	45	0	
75	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,321.77	08/2015 -	06/2016	10	0	
76	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	127.15	09/2012 06/2016	06/2016	45	-24.14	
77	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	433.56	08/2015 -	06/2016	10	0	
78	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	51.55	02/2016 02/2016	07/2016	5	0	
79	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	559.57	03/2015 11/2015	08/2016	17	37.72	space constraint in few locations, obstructions, retendering, poor performance of contractor, torrential rain, delay in award
80	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016	61	0	
81	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	422.00	179.18	02/2016 -	10/2016	8	-12.08	
82	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	370.00	0.37	03/2013 10/2016	10/2016	43	19.35	
83	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	579.21	11/2015 11/2016	11/2016	12	25.84	
84	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,494.16	11/2015 07/2016	11/2016	12	0	
85	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	493.61	08/2015 -	12/2016	16	0	Dealy in grant of 2nd Stage forest clerances for Odisha.
86	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	147.98	11/2016 -	12/2016	1	0	
87	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48	-3.5	
88	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,130.50	05/2014 03/2017	03/2017	34	0	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
89	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	265.72	10/2014 03/2017	03/2017	29	49.38	1.Pipeline laying along SH-55: Application submitted on 12.09.2013. Approval received and payment made in May 2014. Working permission for the laying of 13.7 kms of pipeline along SH-55 is awaited from PWD which is kept on hold due to their road widening project. Govt. of Maharashtra has directed to CE, PWD to resolve the issue. . Secretary PWD has directed CE, PWD to submit revised proposal based on HPCL's new proposal. Proposal originated. The proposal had been reviewed by CE, PWD Pune and forwarded to PWD Department, Mantralaya on 13th April 2015. Demand note for working permission received and payment made. Final working permission received only on 10.06.2015.After obtaining Permission from PWD authorities, works stopped by local villagers at Pimple Jagtap, Khed Taluk, Pune District. They are opposing the pipeline laying along SH 55 stating that a) Existing SH55 road is not acquired by PWD Dept b) Pipeline laying on the new 4 lane road is not acceptable as this portion is yet to be acquired by PWD. Requested assistance from State Govt. / PWD authorities to provide the suitable documents confirming the ownership of RO 2.ROU: As per the recent amendment in LARR Act April 2015 issued by GOI, the compensation under P & MP Act.1963 as well as 12 other acts listed schedule 4 of the LARR act has to be as per schedule 1 of the act. We requested for the expediting finalisation of multiplication factor for acquisition of land so that the ROU compensation can be finalized and we can open the ROU. Govt. of Maharashtra has issued Gazette Notification on

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
90	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	34.87	11/2016 -	04/2017	5	0	
91	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	
92	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,124.35	4,124.35	633.74	04/2016 12/2017	12/2017	20	0	
93	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	212.27	09/2017 03/2018	12/2017	3	0	
94	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	84.88	10/2017 02/2018	02/2018	4	17.66	
95	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2018	12	27.79	Cost incurred till date is only the cost against EPCM contract. The award of EPC contract is pending due to litigation accordingly the expenditure is remaining constant for last few months. Court Cases
96	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	85.47	01/2013 12/2018	12/2018	71	-10.01	
97	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	0	
98	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.31	12/2012 -	02/2019	74	0	
99	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	673.95	05/2019 03/2020	03/2020	10	0	
	Total		77,227.77 -	84,051.74	51,311.46					
	<u>POWER</u>									
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	366.37	02/2012 -	03/2016	49	0	ROW problem resolved. Completion matching with Bagpat Sub station.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
101	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	766.74	11/2012 -	03/2016	40	0	Balance LILO at Saharanpur & Saharanpur S/S is severely affected due to severe ROW problem in Western UP (farmers agitation) & high compensation demand. Keeping in view severe ROW problem, State Admn. has advised to review the scheme. LILO line proposed for deletion as advised by state Govt. (matter referred to CEA for deletion of line & revised of proj. scope). The balance s/s is planned to be commissioned alongwith Roorkee-Saharanpur line (Covered under NRSS-XXI).
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,463.52	04/2013 -	03/2016	35	0	Implementation of balance line affected due to severe ROW problem in Roorkee-Saharanpur line in western UP due to farmers agitation & high compensation demand. ROW being address with support from State admn. & MoP. 02 locations hold-up. Critical
103	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,609.36	11/2013 -	03/2016	28	0	03/05 lines & 02/02 sub station completed. Completion affected due to delay in land acquisition of Kishanganj S/stn (changed from West Bengal to Bihar & acquired in Aug 13). Completion of LILO-out portion (LILO of Teesta-III – Kishanganj 400KV D/C at Rangpo) earlier deferred being proposed to be dropped.
104	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	03/2016	19	0	Gen. Project delayed (ant. in 2016-17 & beyond). Implementation affected due to delay in land acquisition of Varansai S/S (land acquired in Jun 14). ROW (Nexalite) problem faced in Gaya-Varanasi line. Repeated stoppage of work seriously affected progress.

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
105	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 609.44	609.44	590.10	02/2014 03/2016	03/2016	25	10.32	Generation project uncertain. Implementation affected due to severe ROW problem being encountered. 09 fdn., 10 Tower erection & 3.5 Kms stgg. hold due to non-finalisation of gantry by Essar power.
106	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,600.27	10/2014 -	03/2016	17	0	02/05 line & 02/03 sub station completed ahead of schedule. Further 02 lines & 01 S/S. completed in Feb 15. Severe ROW problem are being faced in balance LIFO line.
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	333.82	05/2015 -	03/2016	10	0	Implementation affected due to delay in acquisition of land for Varansai S/stn. (land acquired progressively by Jun 14). Completion matching with readiness of Varansai S/S being expedited.
108	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	3,198.14	01/2013 -	03/2016	38	0	
109	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	9,606.82	8,222.09	02/2011 -	03/2016	61	133.06	Balance Land acquisition and to maintain Law & order
110	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC, RAJASTHAN	02/2015	302.49 302.00	302.49	268.27	02/2016 -	03/2016	1	0	
111	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	236.20	01/2013 -	05/2016	40	0	Completion affected due to delay in land acquisition of Kishanganj S/S. Alternate land acquired in Bihar in Aug 13. Completion matching with S/S. Work under progress. 01 ICT under erection & IInd in transit.
112	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL, KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5	0	Completion matching with associated lines being executed under TBCB rout.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	541.66	11/2011 -	06/2016	55	0	Severe ROW problem in Western U.P. (near Bagpat etc.) initially due to farmers agitations & high compensation demand. ROW problem continues. ROW being addressed with support from State Admn. & Ministry of power
114	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,071.59	08/2012 -	06/2016	46	0	Balance one lines (Sikar-Jaipur) delayed due to contractual/ legal issues arising out of change of ownership & poor performance of the executing contractor. Contract revived by assigning the balance works to the JV Partner and being executed with support by POWERGRID. ROW problem faced.
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	554.02	07/2013 11/2015	06/2016	35	-8.45	Project completed except Kishenpur - New Wanpoo line. Implementation of balance line affected due to delay final forest clearance. Forest clearance received in Oct 15 after cabinet meeting. NBWL clearance received on 28.11.14. Limited working period due to snow-bound area & floods affecting implementation. Critical
116	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,801.75	05/2014 -	06/2016	25	0	Project completed except balance ICT s at Champa S/stn. Land acquisition for Champa S/S was delayed. (acquired in Apr 13). Balance work of Champa S/stn. shall be completed matching with HVDC link to Kurakshetra (ant. by Jun 16).
117	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND INDBARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,959.76	09/2014 -	06/2016	21	0	01 line completed but charging awaited. Completion of balance line delayed due to severe ROW problem faced in Karnataka & contractual issues involved in Salam - Tuticorin line. Issues resolved. Work under progress.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
118	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	537.51	11/2013 -	06/2016	31	0	Generation Project delayed (ant. in 2016-17 & beyond). Completion affected due to delay in land acquisition of Chandwa s/s. (land acquired in Apr 13). Also project involves huge forest (Stage-I received in Dec 14 & permission to work received in May 15). Repeated stoppage of work by extremists affecting progress.
119	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	306.27	08/2014 06/2015	06/2016	22	16.63	Completion delayed due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Efforts being made to complete the project earlier through intervention of State Govt. & Ministry of Power for regulation of compensation issue. But issue still un-resolved.
120	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,436.82	01/2015 -	06/2016	17	0	Completion delayed due to delay in forest clearance. (stage-I obtained in Jun 15, involves 295 Ha. forest). Permission to work obtained in Jul 15. Work in forest area taken up after tree cutting.
121	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	96.23	09/2014 -	06/2016	21	0	- During the installation of OPGW, RoW problems are being encountered across the TL, which hampered the progress. Work is also delayed due to heavy fog in NR and snowfall in hilly area. - Mostly OPGW is being laid on charged transmission line and many times PTW(Permit to Work) is not being issued in time due to Power System constraints which affects the work progress.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
122	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76	9,569.76	5,841.39	06/2015	06/2016	12	0	Implementation affected due to delay in land acquisition of Champa Sub station (land acquired in Apr 13). Forest clearance awaited in HVDC line. Stage-I for WR portion obtained in Jun 15. Permission to work obtained in Sep 15. Completion matching with HVDC Station.
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63	723.63	598.32	11/2014	06/2016	19	0	Severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. Implementation affected of Dulhasti-Kishenpur line due to delay in forest clearance (received in Feb 15) & affected due to floods/cloud bursts.
124	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44	3,201.44	3,089.11	10/2014	06/2016	20	0	Gen. Proj. delayed (ant. in 2016-17 & beyond). Implementation affected due to delay in land acquisition of Kanpur S/stn. (land acquired in Jun 13). Final forest clearance awaited. Permission to work obtained in Jan 16. Completion matching with Sub station.
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE	09/2013	680.69	680.69	466.89	03/2016	06/2016	3	0	02 out of 03 lines completed. Completion delayed due to severe ROW problem at Bhiwani end. Bay at Jaipur (RRV/PNL) earlier planned for execution through RRV/PNL being awarded by Powergrid (under process).
126	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52	1,364.52	479.74	04/2016	06/2016	2	0	Completion likely to be delayed due to delay in land acquisition (land acquired in Feb 14). ROW issues being faced in Jharkhand. Progress being expedited.
127	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL, MULTI STATE	03/2014	155.57	155.57	5.40	03/2016	06/2016	3	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
128	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	25.30	02/2016 -	06/2016	4	0	Completion delay due to delay in manufacturing of Reactors by M/s. BHEL. Yet to be taken up.
129	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,247.07	12/2011 03/2016	06/2016	54	83.21	NIL
130	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	4,401.09	12/2009 07/2016	07/2016	79	147.51	
131	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,262.27	1,262.27	1,111.17	08/2013 07/2016	07/2016	35	119.91	
132	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	345.40	06/2015 -	08/2016	14	0	Commissioning linked to Angul – Srikakulam line & readiness of Srikakulam – Vemagiri line being executed under TBCB route (sch Aug 16) Progress being expedited.
133	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,044.13	06/2015 -	08/2016	14	0	Stage – I forest clearance & working permission received. 01 pkg. re-awarded in Jun 15. Commissioning of line linked to readiness of Srikakulam – Vemagiri line being implemented under TBCB route sch. Aug 16) being expedited. Efforts being made to complete earlier
134	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	2,193.08	1,986.06	09/2009 -	09/2016	84	106.63	
135	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	972.25	07/2006 10/2016	10/2016	123	274.73	
136	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,751.47	4,433.49	01/2016 -	11/2016	10	57.92	
137	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	16.30	04/2016 -	11/2016	7	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
138	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,904.95	11/2008 01/2016	12/2016	97	22.93	Project completed except 01 line (Edaman-Muvattupuza line) getting delayed due to severe ROW problem in Kerala. Work to start after assessment of compensation & payment by State Govt./KSEB. (G.O. with enhanced compensation issued in Jan 15, again revised on 30.07.15) which is compensation to be paid land value, to be finalised by concerned DC, which is under process.
139	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	597.69	09/2010 01/2016	12/2016	75	54.59	Completion affected due to severe ROW problem in balance 02 lines, (400KV D/C Vapi-Navi Mumbai line & LILO at Navi Mumbai). LILO line is being completed using underground cable, however, ROW problem for laying of cable continue. Critical. Vapi-Navi Mumbai line now decided to be terminated at Kudus S/S of MSETCL. Stage-I forest clearance received in Aug 15. Further, its commissioning is linked to readiness of Kudus S/s. which is critical.
140	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,256.58	10/2012 -	12/2016	50	0	Balance Navsari-Boisar line affected due to severe ROW problem & delay in forest clearance awaited. 1200KV Wardha - Aurangabad affected due to delay in implementation arising out of complexities involved (1200KV tower) & ROW problem also encountered, subsequent contractual issues. 01 pkg. terminated & re-awarded in Dec 14/ Feb 15. Remaining 01 pkg. also terminated in Aug 15. However, contract was revived in Feb 16.

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (AS Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
141	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,293.90	12/2012 12/2016	12/2016	48	36.79	Implementing of balance lines affected due to stiff resistance/ local disturbances & geographical constraints in NER. 03 nos. lines under re-tendering due to poor performance by contractor. 03 lines in Arunachal Pradesh affected due to issue arising out of compensation to forest clearance & land ownership disputes. Issue getting resolved with support of state/Distt. Admn.
142	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,338.43	07/2014 -	12/2016	29	0	01/02 line & 01/01 S/stn. completed. Balance Aurangabad-Boisor line affected due to delay in forest clearance (Stage-I received in Aug 15). Permission to work received in Oct 15 & severe ROW in routing of line through grape garden. Critical
143	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,482.93	08/2014 12/2015	12/2016	28	27.6	01/03 lines completed. Implementation affected due to delay in forest clearance and NOC for wildlife (awaited for Aurangabad – Padghe) & anticipated delay in completion Kudus (Padghe) S/stn. being executed by MSETCL. Critical
144	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,968.00	09/2016 -	12/2016	3	0	
145	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,049.05	12/2015 -	12/2016	12	0	Implementation affected due to severe ROW problems in Odisha & Huge forest involvement in Chattisgarh. Involvement of additional forest area reported by State Govt., under process. Stage-I forest clearance awaited. Critical
146	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,824.00	09/2011 -	03/2017	66	54.25	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
147	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	2,498.65	01/2015	03/2017	26	0	Gen. Proj. (Punatsangchu HEP in Bhutan) getting delayed. Project getting completed ahead of Gen. Proj. now anticipated in 2017-18. Work slowed down to the extent feasible to match Gen. Wild life clearance (NBWL) for Punatsangchu - Alipurduar line received in Nov 15 & forwarded to state for further processing for forest clearance, awaited. LILO of HVDC line matching with HVDC terminal
148	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80	1,272.80	1,254.53	11/2012	03/2017	52	0	Completion affected due to delay in land acquisition of Daltonganj (land acquired in May 15) & Change of location of Ultra S/stn. to Pandiabil due to local resistance. ROW problem being faced in LILO line. Further Daltonganj S/S pkg. under re-tender.
149	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19	15,166.19	10,325.00	01/2017	03/2017	2	0	
150	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18	9,395.18	5,991.00	11/2016	08/2017	9	0	
151	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00	5,353.00	5,347.06	05/2014	09/2017	40	0	
152	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89	9,750.89	4,664.54	12/2016	09/2017	9	0	
153	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19	13,762.80	11,605.20	08/2013	12/2017	52	23.65	05/08 line completed Implementation affected due to agitation against Big Dam proj. affecting the construction works in Assam and adverse law & order situation in NER. Lower Subhanshri- B'Chariyali line in almost standstill since Dec 11 due to agitation. Gen. Proj. are also getting delayed. Kameng HEP is ant. in FY 2016-17. Project expected completed progressively by Dec 17 matching with Gen. Proj.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
154	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	55.26	02/2014 -	02/2018	48	0	
155	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,241.00	01/2011 10/2014	05/2018	88	73.65	
156	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.76	5,460.85	09/2009 -	12/2018	111	114.28	
157	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,724.00	03/2013 -	12/2018	69	29.14	
158	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,644.81	02/2016 09/2019	09/2019	43	79.77	4.668 Ha. Land diversion case for dumping area at Village Chopra
159	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	814.10	06/2013 -	12/2019	78	0	Post Award: 1.Hindrances by local villagers. Work was stopped by villagers from 18.02.16 to 29.02.16 at Dam site. Post Award: 1. Minor hindrances by local villagers.
	Total		161,214.48 -	197,310.03	145,902.09					
	HEAVY INDUSTRY									
160	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	NATRIP is a temporary organization is the major hurdle of the project. NATRIP is first of its kind of project for which no train manpower was available in the country.
	Total		1,718.00 -	3,827.30	.00					
	HEALTH AND FAMILY WELFARE									
161	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	285.20	12/2015 -	03/2016	3	0	Fund Constraints.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
162	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15	0	i) Delay in issuance of labour licence from labour Deptt. ii) Frequent bandhs and heavy rain iii) Obstruction of work by locals. iv) Difficulty in procurement of sand and aggregates due to ban of forest produce.
163	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3	0	Fund Constraints.
164	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31	0	Local disturbances.
	Total		976.47 -	976.47	685.47					
	<u>RAILWAYS</u>									
165	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	03/2017	84	648.92	
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]JMRT, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	259.68	
167	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR, BIHAR	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84	230.08	
168	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defrozen and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut-Saharanpur).
169	KATAKHAL TO BHAIIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
170	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	228.1	
171	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	
172	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	38.8	
173	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	95.9	Contractual issues
174	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
175	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	138.61	Contractual issues
176	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
177	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	
178	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	233.08	
179	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	38.24	
180	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	700	
181	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	18.66	Contractual issue, land acquisition, non finalisation of alignment of flyover at Bilaspur
182	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	29.06	land acquisition & hurdle clearances like drains etc. by GHMC authorities.
183	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
184	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [N22000266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
185	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
186	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
187	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	
188	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-28.09	Non-handing over of land of Joka Depot
189	JIRIBAM TO IMPHAL (TUPU) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
190	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
191	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261	299.79	
192	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
193	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
194	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
195	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
196	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-20	land acquisition problem

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		37,635.20	93,472.32	39,981.54					
			-							
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
197	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06	792.06	1,983.00	12/2012	02/2016	38	0	
198	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72	264.72	-	06/2008	02/2016	92	0	
199	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00	486.00	468.41	05/2010	02/2016	69	0	
200	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	2,891.15	09/2012	02/2016	41	0	
201	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51	333.51	225.26	09/2014	02/2016	17	0	
202	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH, RAJASTHAN	03/2012	914.50	914.50	1,097.62	10/2015	02/2016	4	0	
203	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00	201.66	242.00	09/2008	03/2016	90	30.1	
204	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00	361.00	-	02/2009	03/2016	85	28.93	
205	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81	385.13	-	04/2009	03/2016	83	92.75	
206	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64	167.64	-	11/2008	03/2016	88	0	
207	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04	280.13	-	11/2008	03/2016	88	80.68	
208	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00	200.00	-	04/2009	03/2016	83	0	
209	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00	195.00	-	06/2008	03/2016	93	0	
210	BIJUNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80	237.80	-	06/2008	03/2016	93	0	
211	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94	332.94	493.27	09/2008	03/2016	90	0	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
212	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	274.11	10/2008 -	03/2016	89	-8.95	
213	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2016	80	68.99	
214	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	348.16	342.49	09/2007 -	03/2016	102	0	
215	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,607.78	05/2012 -	03/2016	46	0	
216	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35	0	
217	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33	0	
218	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19	0	
219	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	329.40	05/2013 -	03/2016	34	0	
220	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28	0	
221	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	609.00	02/2014 -	03/2016	25	0	
222	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	761.49	03/2014 -	03/2016	24	0	
223	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	352.00	04/2014 -	03/2016	23	0	
224	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	03/2016	28	0	
225	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	-	02/2014 -	03/2016	25	0	
226	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	0	
227	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31	0	
228	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37	0	
229	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,472.00	06/2014 -	03/2016	21	-02	
230	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
231	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19	484.19	455.26	10/2014	03/2016	17	0	
232	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69	942.69	229.16	06/2014	03/2016	21	0	
233	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00	1,232.00	927.19	08/2015	03/2016	7	0	
234	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI, BIHAR	11/2005	240.00	240.00	295.38	11/2008	03/2016	88	0	
235	FOUR LANING OF ORISSA/CHATTISHGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00	1,232.00	-	08/2015	03/2016	7	0	
236	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54	164.54	-	08/2015	03/2016	7	0	
237	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16	198.16	242.40	04/2008 04/2016	04/2016	96	0	
238	NALBARI TO BIJUNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00	225.00	311.13	06/2008 04/2016	04/2016	94	0	
239	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45	232.45	-	09/2010	04/2016	67	0	
240	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00	940.00	1,409.36	07/2012	04/2016	45	0	
241	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00	593.00	1,006.79	07/2013	04/2016	33	0	
242	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00	1,141.00	1,911.64	08/2013	04/2016	32	0	
243	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22	1,928.22	822.96	04/2015	04/2016	12	0	
244	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHAI, MADHYA PRADESH	01/2012	381.86	381.86	-	04/2015	04/2016	12	0	
245	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00	2,159.00	-	06/2015	05/2016	11	0	
246	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18	1,396.18	2,310.32	09/2014	05/2016	20	0	
247	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN	01/2014	158.04	158.04	117.97	12/2015	05/2016	5	0	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
248	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD, ANDHRA PRADESH	02/2015	224.83	224.83	13.17	04/2015	05/2016	13	0	
249	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37	353.37	-	10/2011	06/2016	56	0	
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00	2,288.00	3,619.94	11/2011	06/2016	55	106.5	
251	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00	852.00	863.58	03/2013	06/2016	39	0	
252	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11	0	
253	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76	1,813.76	-	07/2013	06/2016	35	0	
254	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50	1,008.50	-	06/2013	06/2016	36	0	
255	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00	600.00	307.41	06/2013	06/2016	36	0	
256	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88	953.88	-	07/2013	06/2016	35	0	
257	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00	536.00	-	01/2014	06/2016	29	0	
258	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00	1,535.00	2,503.31	05/2014	06/2016	25	0	
259	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70	1,100.70	-	06/2014	06/2016	24	0	
260	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00	754.00	902.06	03/2013	06/2016	39	0	
261	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00	1,573.00	1,844.50	09/2015	06/2016	9	0	
262	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24	2,125.24	-	12/2015	06/2016	6	0	
263	4 LANNING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00	828.00	-	09/2014	06/2016	21	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
264	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN	01/2014	368.15	368.15	184.28	01/2016	06/2016	5	0	
265	REHABILITATION AND UPGRADE OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD, ANDHRA PRADESH	02/2014	417.61	417.61	112.85	06/2014	06/2016	24	0	
266	SONAPUR TO GUWAHATI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00	245.00	214.17	03/2008 07/2016	07/2016	100	0	
267	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51	478.00	277.41	10/2013	07/2016	33	-11	
268	REHABILITATION AND UPGRADE OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD, ANDHRA PRADESH	02/2014	258.99	258.99	64.65	07/2014	07/2016	24	0	
269	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96	175.96	304.17	04/2008 08/2016	08/2016	100	0	
270	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00	160.00	197.40	05/2008 07/2016	08/2016	99	0	
271	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00	1,585.00	1,070.90	05/2013	08/2016	39	0	
272	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84	1,078.84	1,876.89	08/2013	08/2016	36	0	
273	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20	1,348.20	1,313.00	02/2014	08/2016	30	0	
274	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH	11/2011	871.15	871.15	-	09/2015	08/2016	11	0	
275	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52	1,170.52	1,579.15	06/2012	08/2016	50	0	
276	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61	309.56	370.66	04/2010 09/2016	09/2016	77	42.25	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
277	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40	0	
278	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	211.68	01/2014 -	09/2016	32	0	
279	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	133.92	01/2016 -	09/2016	8	0	
280	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	0	
281	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	0	
282	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	195.93	01/2016 -	10/2016	9	0	
283	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	0	
284	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	28.66	11/2014 -	11/2016	24	0	
285	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	12/2016	138	0	
286	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	12/2016	111	0	
287	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	0	
288	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	0	
289	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,778.42	03/2013 -	12/2016	45	0	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
290	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30	671.30	880.14	02/2013	12/2016	46	0	
291	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00	1,250.00	-	12/2013	12/2016	36	0	
292	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00	575.00	604.57	07/2013	12/2016	41	0	
293	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00	586.00	-	01/2014	12/2016	35	0	
294	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00	1,046.00	437.14	09/2013	12/2016	39	0	
295	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00	624.00	343.75	04/2014	12/2016	32	0	
296	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25	283.25	176.11	10/2015	12/2016	14	0	
297	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD, ANDHRA PRADESH	07/2015	333.21	333.21	14.12	12/2015	12/2016	12	0	
298	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21	333.21	-	12/2015	12/2016	12	0	
299	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04	301.04	32.54	01/2016	12/2016	11	0	
300	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04	923.04	283.72	11/2016	12/2016	1	0	
301	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00	208.00	295.20	04/2008	01/2017	105	0	
302	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85	523.85	62.37	01/2016	01/2017	12	0	
303	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16	702.16	391.77	07/2014	02/2017	31	0	
304	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD, ANDHRA PRADESH	07/2014	251.55	251.55	27.87	02/2015	02/2017	24	0	

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
305	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55	0	
306	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	-	08/2013 -	03/2017	43	0	
307	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	03/2017	16	0	
308	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	542.01	03/2014 -	04/2017	37	0	
309	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	162.47	02/2010 -	05/2017	87	2.29	
310	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	222.75	08/2013 -	05/2017	45	0	
311	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	1,479.00	480.44	06/2015 -	05/2017	23	0	
312	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	
313	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,655.11	08/2013 -	07/2017	47	0	
314	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	0	
315	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	58.64	09/2016 -	09/2017	12	0	
316	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	
317	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	0	

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
318	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPUR - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	0	
319	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2017	55	0	
320	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	12/2017	50	0	
321	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	347.00	07/2014 -	12/2017	41	0	
322	BARSAAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	
323	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	0	
324	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	867.66	52.60	11/2015 -	05/2018	30	0	
325	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
326	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	
	Total		90,119.92 -	91,945.85	58,603.04					
	<u>SHIPPING AND PORTS</u>									
327	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120	300	Relocating of fishing stalls for a length about 300m in fishing harbour.
328	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	66.82	
	Total		395.67 -	1,009.83	506.00					

(February 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>TELECOMMUNICATIONS</u>									
329	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	0	
330	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-4.74	
	Total		15,445.17 -	15,345.17	2,720.00					
	<u>URBAN DEVELOPMENT</u>									
331	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	03/2016	16	0	
332	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	
333	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	139.88	06/2012 03/2016	05/2016	47	0	
334	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	171.26	05/2013 10/2015	06/2016	37	0	
335	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,776.56	12/2015 -	08/2016	8	0	
336	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	315.00	176.16	06/2015 08/2016	10/2016	16	0	
337	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9	0	Rehabilitation & Resettlement, Land acquisition and Delay in technical approval from M/o Railways delays the project.

(February 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
338	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	91.53	12/2014 12/2016	03/2017	27	0	
339	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	119.44	03/2012 08/2016	03/2017	60	-6.36	
340	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	29.17	09/2015 07/2016	04/2017	19	0	
341	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	0	
	Total		55,385.80 -	55,372.77	32,689.03					
	Grand Total		543,616.01	660,111.49	409,867.13					

Annexure - VII

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54	89
	Total		16,663.00 -	28,139.00				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58	60
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97	24
	Total		1,321.16 -	2,690.85				
	<u>HEAVY INDUSTRY</u>							
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38	29
9	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	10/2016	19.35	43
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2018	27.79	12
11	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66	4
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84	12

(February 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62	53
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83	35
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72	17
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49	52
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
18	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2016	16.05	39
	Total		37,540.20 -	45,433.04				
	<u>POWER</u>							
19	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	06/2016	16.63	22
20	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
21	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2016	54.59	75
22	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32	25
23	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91	35
24	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63	84
25	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
26	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2016	27.60	28
27	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93	97
28	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79	48
29	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21	54
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	07/2016	147.51	79
31	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69
32	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92	10

(February 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
33	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28	111
34	RAGHUNATHPUR THERMAL POWER STATION PHASE-I [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06	61
35	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
36	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
37	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		54,329.01 -	90,488.17				
	<u>RAILWAYS</u>							
38	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61	91
40	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
41	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90	86
42	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
43	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
44	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
45	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
46	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66	93
47	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
48	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
49	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
50	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
51	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
52	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87

(February 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56	6,570.75	03/2011	03/2019	803.12	96
54	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00	2,531.34	12/2008	03/2018	245.34	111
55	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34	2,876.00	03/2014	03/2018	253.60	48
56	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00	2,973.42	03/2015	03/2020	249.81	60
57	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00	1,242.25	03/2007	03/2016	38.80	108
58	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00	3,040.00	03/2009	03/2016	230.08	84
59	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48	4,190.00	12/2015	03/2020	212.81	51
60	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00	4,996.19	04/2008	06/2017	233.08	110
61	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31	5,500.00	03/2009	03/2016	228.10	84
62	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00	20,000.00	11/2002	12/2017	700.00	181
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00	7,986.04	03/2014	03/2019	50.68	60
	Total		22,458.31	77,795.14				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
64	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00	201.66	09/2008	03/2016	30.10	90
65	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04	280.13	11/2008	03/2016	80.68	88
66	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00	331.23	07/2009	03/2016	68.99	80
67	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81	385.13	04/2009	03/2016	92.75	83
68	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61	309.56	04/2010	09/2016	42.25	77
69	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00	281.31	02/2010	05/2017	2.29	87
70	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	361.00	02/2009	03/2016	28.93	85
71	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00	2,288.00	11/2011	06/2016	106.50	55
	Total		2,586.46	4,438.02				

(February 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>SHIPPING AND PORTS</u>							
72	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	03/2016	300.00	120
73	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82	88
	Total		395.67 -	1,009.83				
	<u>STEEL</u>							
74	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50	15
75	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
76	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	07/2011	324.87 324.87	325.00	12/2015 -	03/2016	0.04	3
77	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39	8
78	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29	25
	Total		1,761.97 -	2,267.02				
	Grand Total		138,773.78	256,088.37				

Annexure - VIII

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		467.78 -		
	<u>STEEL</u>				
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
5	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	05/2013 01/2015	08/2015
6	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
7	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
8	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-
	Total		2,833.55 -		
	<u>PETROCHEMICALS</u>				
9	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	04/2012 12/2013	12/2015
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
10	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016
11	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
12	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
14	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
15	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
16	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
17	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
	Total		6,581.73 -		
	<u>POWER</u>				
18	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.57	07/2013 01/2016	01/2016
19	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
20	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	06/2014 03/2016	-
21	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
22	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	Total		9,159.61 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
24	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
	Total		414.11 -		
	<u>RAILWAYS</u>				
25	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
26	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
27	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
28	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
29	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
30	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N220000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
31	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
32	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	- -	02/2014
33	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
34	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014
35	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
36	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015
37	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
38	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
39	MUNEERABAD-MAHABOONAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015
40	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
41	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
42	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
43	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015
44	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
45	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015
46	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
47	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015
48	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
49	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	09/2015
50	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
51	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015
52	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
53	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-
54	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-
55	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23	02/2015	-
57	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89	-	-
58	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39	-	-
59	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35	-	-
60	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00	-	-
61	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27	-	-
62	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH	04/1997	836.26	-	-
63	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00	-	-
64	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66	-	-
65	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00	12/2012	-
66	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05	12/2011	-
67	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68	-	-
68	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00	-	-
69	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08	-	-
70	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00	07/2012	-
71	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55	-	-
72	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00	-	-
73	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69	03/2012	-
74	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00	-	-
75	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87	-	-
76	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30	06/2007	-
77	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00	-	-
78	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00	-	-
79	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00	-	-
80	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69	12/2006	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
82	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
83	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
84	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
85	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
86	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
87	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
88	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
89	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
90	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
91	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
92	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
93	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
94	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
95	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
96	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
97	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
98	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
99	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
100	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
101	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
102	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
104	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
105	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
107	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
108	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
109	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
110	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
111	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
112	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
113	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
114	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
115	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
116	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
117	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
118	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
119	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
120	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
121	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
122	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
123	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
124	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
125	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
126	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
127	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
128	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
130	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
131	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
132	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
133	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
134	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
135	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
136	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
137	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
138	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
139	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
140	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
141	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
142	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
143	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
144	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
145	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
146	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
147	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
148	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
149	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
150	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
151	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
152	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
153	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
154	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
155	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
156	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
158	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
159	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
160	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
161	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
162	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
163	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
164	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
165	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
166	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
167	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
168	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
169	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
170	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
171	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
172	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
173	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
174	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
175	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
176	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
177	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
178	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
179	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
180	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
181	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
182	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
183	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
184	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
185	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
186	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
187	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
188	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
189	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
190	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
191	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
192	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
193	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
194	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
195	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
196	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
197	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
198	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
199	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
200	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
201	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
202	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
203	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
204	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
205	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
206	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
207	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
208	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
209	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
210	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
211	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
212	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
213	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
214	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
215	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
216	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
217	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
218	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
219	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
220	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
221	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
222	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
223	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
224	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
225	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
226	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
227	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
228	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
229	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
230	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
231	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
232	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
233	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
234	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
235	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
236	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
237	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
238	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
239	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
240	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
241	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
242	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
243	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
244	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
245	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
246	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-
247	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
248	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
249	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
250	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
251	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
252	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
253	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
254	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
255	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
257	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
258	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-
	Total		194,280.06 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
259	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
260	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	08/2015
261	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
262	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
263	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	01/2016
264	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	01/2016
265	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2016 -	01/2016
266	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	01/2016
267	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	01/2016
268	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2019 -	01/2016
269	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-
270	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
271	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
272	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
273	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
274	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
275	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
276	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
277	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
279	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
280	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
281	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
282	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	-
283	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	- -	-
284	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	10/2014 -	-
285	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	-
286	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	- -	-
287	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	- -	-
288	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	-
289	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, MEGHALAYA	02/2011	226.00 -	02/2014 -	-
290	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI, BIHAR	12/2011	325.51 -	05/2014 -	-
291	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
292	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	05/2014 -	-
293	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
294	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	10/2013 -	-
295	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
296	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-
297	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-
298	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI, RAJASTHAN	01/2014	177.32 -	01/2016 -	-
299	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD, TELANGANA	03/2011	218.31 339.82	12/2015 -	-
300	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH, GOA	03/2015	298.33 -	- -	-
301	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH, GOA	03/2015	184.05 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
302	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
303	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
304	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
305	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
306	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
307	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
308	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
309	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
310	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
311	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
312	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
313	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
314	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	12/2015 -	-
315	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
316	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
317	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
318	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	03/2015 -	-
319	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
320	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
321	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
322	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
323	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
324	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
325	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
326	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
327	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
328	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
329	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-
330	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
331	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
332	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
333	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
334	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
335	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
336	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
337	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
338	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
339	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
340	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 161.70	07/2015 -	-
341	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 158.35	08/2015 -	-
342	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
343	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
344	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
345	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
346	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
347	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	02/2015 -	-
348	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
349	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
350	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
351	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
352	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
353	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
354	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
355	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
356	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
357	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
358	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
359	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
360	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
361	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
362	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
363	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
364	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
365	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
366	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	01/1991	225.02 -	- -	-
367	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	01/1991	223.30 -	- -	-
368	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
369	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-
370	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-
371	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL	10/2015	531.13 -	- -	-
372	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL	10/2015	361.15 -	- -	-
373	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	01/1991	289.99 -	- -	-
374	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-
375	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-
376	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-
377	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
378	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
379	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-
380	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-
381	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-
382	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-
383	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-
384	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	-
385	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
386	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
387	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
388	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
389	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
390	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-
391	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-
392	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR	08/2015	814.04 -	- -	-
393	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
394	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL	12/2015	1,423.96 -	- -	-
395	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
396	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	-
397	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-
398	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-
399	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-
400	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
401	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
402	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
403	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-
404	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-
405	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
406	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
407	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
408	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-
409	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-
410	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
411	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-
412	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	-
413	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
414	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
415	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
416	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
417	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
418	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
419	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
	Total		91,374.58 -		
	SHIPPING AND PORTS				
420	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	01/2016
421	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		2,793.79		
			-		
	<u>URBAN DEVELOPMENT</u>				
422	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 202.00	09/2014 07/2015	07/2015
423	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 12/2015	12/2015
424	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015
425	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
426	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 185.57	08/2007 -	-
427	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-
428	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
429	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-
430	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-
431	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
432	REHABILITATION AND STRENGTHENING OF SEWEWRAE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
433	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	-
	Total		32,429.43 -		
	Grand Total		346,348.46		

Annexure - IX

Details of Projects Without Original Date of Commissioning

(February 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	RAILWAYS								
1	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	-	0/1
2	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2016	-	0/0
3	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	12/2016	-	0/0
4	RAMGANJMUDDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	-	0/0
5	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
6	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
7	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N220000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
8	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
9	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2018	-	0/0
10	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
11	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	886.65	-	- -	03/2018	-	0/0
12	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
13	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
14	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
15	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
16	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
17	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
18	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0

(February 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
19	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [N220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
20	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
21	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
22	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
23	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
24	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
25	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
26	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
27	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	175.26	- -	03/2020	-	0/0
	Total		19,590.88 -	30,884.76	5,992.51				0/1
	ROAD TRANSPORT AND HIGHWAYS								
28	ROHTAK - BAWAL (APPROVED LENGTH 97 KM) - [N24000525]NHAI, HARYANA	02/2010	650.00 -	650.00	813.91	- -	03/2016	-	0/0
29	FOUR LANNING OF LUDHIYANA - TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	479.00	349.60	- -	07/2016	-	0/0
30	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	994.21	- -	09/2016	-	0/0
31	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/4
32	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/4
33	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	1,393.00	876.68	- -	01/2018	-	0/0
34	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL. FOUR LANE KHINDEAPAR BRIDGE - [N24000251]NHDP, GOA	03/2015	297.00 -	297.00	36.02	- -	04/2018	-	0/1
	Total		5,099.07 -	5,099.07	3,070.42				0/9
	Grand Total		24,689.95	35,983.83	9,062.93				0/10

Annexure - X

Details of Projects Without Milestones w.r.t. Original Schedule

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	03/2018 -	03/2018	0/0
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
8	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	03/2024 -	03/2024	0/0
	Total		3,338.19 -			0/0
	<u>FERTILISERS</u>					
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
10	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 -	11/2016 -	11/2016	0/0
11	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 -	11/2016 -	11/2016	0/0
12	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		2,555.63 -			0/0
	<u>STEEL</u>					

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	02/2014 -	03/2016	0/0
14	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	12/2015 -	03/2016	0/0
15	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0
16	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 254.00	06/2016 -	06/2016	0/0
17	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
18	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
20	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
21	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	06/2017	0/0
22	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	12/2016 -	07/2017	0/0
23	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
24	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
25	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
26	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
27	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
28	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
29	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
30	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
31	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
32	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-	0/0
33	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
	Total		15,584.17 -			0/0
	<u>PETROLEUM</u>					
34	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016	0/0

			(February 2016)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	03/2016	0/0
36	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 05/2016	05/2016	0/0
37	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	05/2016	0/0
38	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	07/2016	0/0
39	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 10/2016	10/2016	0/0
40	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	03/2013 10/2016	10/2016	0/0
41	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	12/2016	0/0
42	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
43	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 -	01/2017	0/0
44	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
45	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT	11/2015	500.00 -	03/2017 -	03/2017	0/0
46	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017 -	05/2017	0/0
47	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
48	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 03/2018	12/2017	0/0
49	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA	05/2015	2,443.00 -	12/2017 -	12/2017	0/0
50	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 -	12/2017	0/0
51	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2018	0/0
52	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 -	04/2018	0/0
53	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 -	09/2018	0/0
54	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
55	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
56	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 1,881.22	11/2019 -	11/2019	0/0
57	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
58	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
60	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
61	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
62	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
63	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		49,639.87 -			0/0
	<u>POWER</u>					
64	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
65	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
67	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 -	03/2017	0/0
68	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
69	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
70	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
71	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
72	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
73	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA	01/2016	187.04 -	06/2018 -	06/2018	0/0
74	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
75	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
76	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
77	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
78	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
79	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		22,448.90 -			0/0

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>HEAVY INDUSTRY</u>					
80	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
81	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
82	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	03/2016	0/0
83	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
84	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	04/2016	0/0
85	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	06/2016	0/0
86	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	05/2017	0/0
87	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	05/2017	0/0
88	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	05/2017	0/0
89	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
	Total		2,563.15 -			0/0
	<u>RAILWAYS</u>					
90	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 2,434.00	03/2010 -	03/2017	0/0
91	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
92	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
93	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
94	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
95	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
96	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTPT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
97	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
98	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
99	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
100	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
101	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
102	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
103	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
104	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
105	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
106	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
107	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
108	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
109	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
110	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
111	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
112	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
113	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
114	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
115	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
116	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
117	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
118	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	03/2004 -	03/2016	0/0
119	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 3,040.00	03/2009 -	03/2016	0/0
120	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
121	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
122	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
123	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
124	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
125	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
126	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	02/2009 02/2009	04/2016	0/0
127	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
128	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	10/2016	0/0
129	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
130	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	12/2016	0/0
131	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
132	RAMGANJUMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
133	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
134	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
135	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
136	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
137	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
138	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER, MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
139	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2017	0/0
140	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
141	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2017	0/0
142	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017	0/0
143	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
144	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
145	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
146	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
147	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
148	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
149	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
150	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
151	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
152	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
153	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
154	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
155	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
156	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJBHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
157	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
158	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
161	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
162	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
163	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
164	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
165	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
166	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
167	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
168	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
169	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
170	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
171	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
172	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
173	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
174	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
175	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
176	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
177	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
178	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
180	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
181	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-	0/0
182	HARIDASPUR-PARADEEP (NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
183	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 -	-	0/0
184	SUKINDA ROAD - ANGUL (NL) (ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
185	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
186	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 -	- -	-	0/0
187	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,054.35 2,200.00	- -	-	0/0
188	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR, KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
189	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-	0/0
190	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR, UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
191	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
192	VIRAMGAM-BHILDI (WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
193	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATTISGARH	04/1995	304.00 -	12/2012 -	-	0/0
194	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
196	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0
197	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
198	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
199	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
200	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
201	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
202	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
203	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
204	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
205	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
206	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
207	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
208	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
209	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
210	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
211	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
212	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
213	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
214	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
215	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
216	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
217	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0
218	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
220	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
221	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
222	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
223	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
224	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
225	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
226	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
227	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
228	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
229	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
230	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
231	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
232	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
233	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
234	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
235	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
236	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
237	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
238	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
239	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
240	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
241	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
242	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
244	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
245	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
246	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
247	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
248	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
249	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
250	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
251	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
252	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
253	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
254	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
255	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
256	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
257	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
258	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
259	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
260	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
261	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
262	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
263	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
264	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
265	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
266	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
268	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
269	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
270	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
271	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
272	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
273	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
274	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
275	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
276	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
277	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
278	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
279	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-	0/0
280	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-	0/0
281	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-	0/0
282	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-	0/0
283	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-	0/0
284	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-	0/0
285	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-	0/0
286	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-	0/0
287	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-	0/0
288	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	- -	-	0/0
289	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 -	- -	-	0/0
290	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR, MULTI STATE	04/2007	270.14 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
292	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
293	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
294	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
295	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
296	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
297	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
298	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
299	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
300	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
301	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
302	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
303	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
304	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
305	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
306	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
307	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
308	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
309	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
310	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
311	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
312	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
313	BARIARPIUR-MANANPUR VIA KHARAGPUR, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
314	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
316	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
317	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
318	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
319	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
320	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
321	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
322	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
323	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
324	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
325	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
326	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
327	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
328	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
329	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
330	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
331	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
332	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
333	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
334	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]JNR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
335	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]JNR,PUNJAB	04/2009	396.04 -	- -	-	0/0
336	GRADE SEPERATOR AT DAYABASTI - [N22000269]JNR,DELHI	04/1999	156.65 -	- -	-	0/0
337	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]JNR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
338	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]JNR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
340	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
341	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
342	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
343	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
344	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
345	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
346	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
347	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
348	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
349	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
350	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
351	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
352	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
353	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
354	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
355	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
356	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
357	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
358	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
359	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
360	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
361	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
362	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
364	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
365	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-	0/0
366	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
367	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
368	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
369	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
370	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
371	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-	0/0
372	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-	0/0
373	DELANG-PURI DOUBLING - [N22000320]ECOR, ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
374	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
375	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
376	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
377	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
378	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
379	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
380	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
381	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-	0/0
382	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
383	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
384	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
385	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		253,151.96 -			0/0

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
386	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	02/2016	0/0
387	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP, MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
388	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
389	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	07/2014 -	08/2015	0/0
390	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD, MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
391	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
392	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	12/2013 -	01/2016	0/0
393	SAMA KHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	03/2013 -	01/2016	0/0
394	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI, MADHYA PRADESH	03/2015	830.36 -	01/2016 -	01/2016	0/0
395	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	01/2016	0/0
396	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	01/2016	0/0
397	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI, MADHYA PRADESH	03/2015	830.36 -	01/2019 -	01/2016	0/0
398	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	06/2008 -	02/2016	0/0
399	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	02/2016	0/0
400	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	02/2016	0/0
401	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH, RAJASTHAN	03/2012	914.50 -	10/2015 -	02/2016	0/0
402	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	09/2008 -	03/2016	0/0
403	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	03/2016	0/0
404	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	03/2016	0/0
405	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	03/2016	0/0
406	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	03/2016	0/0
407	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	04/2009 -	03/2016	0/0
408	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	06/2008 -	03/2016	0/0
409	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	06/2008 -	03/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
410	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	09/2008 -	03/2016	0/0
411	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	10/2008 -	03/2016	0/0
412	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	03/2016	0/0
413	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	09/2007 -	03/2016	0/0
414	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	05/2012 -	03/2016	0/0
415	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	03/2016	0/0
416	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2016	0/0
417	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	03/2016	0/0
418	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	03/2016	0/0
419	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	03/2016	0/0
420	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	03/2016	0/0
421	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	03/2016	0/0
422	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	03/2016	0/0
423	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	03/2016	0/0
424	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	02/2014 -	03/2016	0/0
425	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2016	0/0
426	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	03/2016	0/0
427	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	03/2016	0/0
428	BEAWAR PALI PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.51 -	06/2014 -	03/2016	0/0
429	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
430	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
431	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	06/2014 -	03/2016	0/0
432	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
433	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
434	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
435	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	11/2008 -	03/2016	0/0
436	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
437	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2016	0/0
438	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	03/2016	0/0
439	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	- -	03/2016	0/0
440	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 04/2016	04/2016	0/0
441	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2016	04/2016	0/0
442	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	04/2016	0/0
443	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	04/2016	0/0
444	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	04/2016	0/0
445	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2016	0/0
446	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
447	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2016	0/0
448	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2016	0/0
449	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2016	0/0
450	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	05/2016	0/0
451	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016	0/0
452	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
453	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
454	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2016	0/0
455	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2016	0/0
456	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
457	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
458	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	06/2016	0/0
459	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2016	0/0
460	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2016	0/0
461	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2016	0/0
462	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2016	0/0
463	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	06/2016	0/0
464	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	06/2016	0/0
465	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	06/2016	0/0
466	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH	06/2014	569.38 -	06/2016 -	06/2016	0/0
467	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]NHAI,HARYANA	03/2013	959.25 -	06/2016 -	06/2016	0/0
468	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 07/2016	07/2016	0/0
469	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2016	0/0
470	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016	0/0
471	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	07/2016	0/0
472	GUWAHTI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 08/2016	08/2016	0/0
473	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2016	08/2016	0/0
474	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	08/2016	0/0
475	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	08/2016	0/0
476	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	08/2016	0/0
477	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]NHAI,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
478	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
479	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
480	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
481	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
482	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	08/2016	0/0
483	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	09/2016	0/0
484	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
485	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
486	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
487	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
488	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	09/2016	0/0
489	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
490	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA	12/2012	438.75 -	09/2016 -	09/2016	0/0
491	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	09/2016	0/0
492	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2016	0/0
493	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
494	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	10/2016	0/0
495	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
496	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
497	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
498	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
499	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
500	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
501	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
502	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
503	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	12/2016	0/0
504	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2016	0/0
505	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
506	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
507	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
508	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2016	0/0
509	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
510	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
511	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
512	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	12/2016	0/0
513	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2016	0/0
514	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
515	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
516	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
517	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
518	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
519	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	01/2017	0/0
520	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
521	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
522	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
523	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
524	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
525	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	03/2017	0/0
526	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	03/2017	0/0
527	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
528	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
529	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
530	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
531	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
532	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI, RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
533	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
534	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
535	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	05/2017	0/0
536	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	06/2015 -	05/2017	0/0
537	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
538	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
539	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
540	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
541	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
542	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
543	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI, TAMIL NADU	12/2014	451.58 -	06/2017 -	06/2017	0/0
544	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	08/2013 -	07/2017	0/0
545	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
546	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
547	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2017	0/0
548	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD, MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
549	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
550	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
551	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI, JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
552	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
553	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
554	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
555	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
556	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
557	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
558	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
559	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
560	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
561	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
562	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
563	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	12/2017	0/0
564	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
565	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
566	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
567	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
568	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
569	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2017	0/0
570	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
571	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
572	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
573	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
574	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
575	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
576	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
577	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
578	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
579	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
580	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
581	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
582	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
583	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
584	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, HARYANA	09/2015	788.51 -	03/2018 -	03/2018	0/0
585	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
586	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
587	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
588	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
589	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA - BARWALA - PANCHKULA (PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
590	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
591	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH, ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
592	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - 2 - [N24000492]NHAI, MADHYA PRADESH	11/2015	867.66 -	11/2015 -	05/2018	0/0
593	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
594	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
595	4 LANING OF AMBALA - KAITHAL - PACKAGE - 1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
596	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
597	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
598	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
599	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
600	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
601	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
602	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
603	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0
604	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
605	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
606	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0
607	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
608	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 -	-	0/0
609	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
610	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
611	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
612	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
613	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
614	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
615	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
616	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
617	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
618	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
619	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
620	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-	0/0
621	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-	0/0
622	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.51 -	05/2014 -	-	0/0
623	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
624	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
625	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
626	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-	0/0
627	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
628	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
629	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
630	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	-	0/0
631	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
632	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
633	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
634	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
635	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
636	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
637	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
638	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	12/2015 -	-	0/0
639	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
640	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
641	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
642	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	03/2015 -	-	0/0
643	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
644	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
645	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
646	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
647	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
648	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
649	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
650	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
651	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
652	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
653	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-	0/0
654	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
655	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
656	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
657	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
658	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
659	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
660	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
661	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
662	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROAD - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
663	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
664	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 161.70	07/2015 -	-	0/0
665	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 158.35	08/2015 -	-	0/0
666	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
667	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
668	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
669	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
670	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
671	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	02/2015 -	-	0/0
672	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
673	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
674	CONST.OF 4 LANES WITH PAVED SHOULDERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
675	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOU LA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
676	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
677	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
678	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
679	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
680	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
681	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	-	0/0
682	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
683	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
684	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
685	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
686	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
687	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
688	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
689	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
690	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	01/1991	225.02 -	- -	-	0/0
691	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	01/1991	223.30 -	- -	-	0/0
692	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
693	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-	0/0
694	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-	0/0
695	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL	10/2015	531.13 -	- -	-	0/0
696	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL	10/2015	361.15 -	- -	-	0/0
697	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	01/1991	289.99 -	- -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
698	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
699	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-	0/0
700	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
701	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
702	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
703	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-	0/0
704	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-	0/0
705	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-	0/0
706	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-	0/0
707	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-	0/0
708	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	-	0/0
709	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
710	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
711	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
712	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
713	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
714	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-	0/0
715	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-	0/0
716	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR	08/2015	814.04 -	- -	-	0/0
717	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
718	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL	12/2015	1,423.96 -	- -	-	0/0
719	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
720	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	-	0/0
721	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-	0/0

			(February 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
722	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	- -	-	0/0
723	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	- -	-	0/0
724	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE - IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
725	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	-	0/0
726	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-	0/0
727	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	01/1991	1,167.45 -	- -	-	0/0
728	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	- -	-	0/0
729	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
730	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH, GOA	12/2015	773.98 -	- -	-	0/0
731	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH, GOA	12/2015	819.95 -	- -	-	0/0
732	TWO LANING WITH PS OF JOWAI - MEHALAYA / ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	- -	-	0/0
733	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	- -	-	0/0
734	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR	01/1991	478.35 -	- -	-	0/0
735	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-	0/0
736	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	-	0/0
737	WIDENING STG. OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB	06/2015	892.17 -	- -	-	0/0
738	WIDENING STG. OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD, PUNJAB	06/2015	899.21 -	- -	-	0/0
739	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
740	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
741	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD, BIHAR	01/1991	154.62 -	- -	-	0/0
742	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD, BIHAR	01/1991	319.68 -	- -	-	0/0
743	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-	0/0
	Total		222,760.17 -			0/0
	SHIPPING AND PORTS					

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
744	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	01/2016	0/0
745	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 01/2016	03/2016	0/0
746	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
747	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
748	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
749	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	03/2017	0/0
	Total		13,334.00 -			0/0
	<u>URBAN DEVELOPMENT</u>					
750	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 202.00	09/2014 07/2015	07/2015	0/0
751	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 12/2015	12/2015	0/0
752	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
753	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	03/2016	0/0
754	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 10/2015	06/2016	0/0
755	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0
756	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	06/2015 08/2016	10/2016	0/0
757	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
758	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	03/2012 08/2016	03/2017	0/0
759	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
760	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
761	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
762	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
763	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
764	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 185.57	08/2007 -	-	0/0
765	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
766	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-	0/0
767	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-	0/0
768	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-	0/0
769	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
770	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JhNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		107,260.81 -			0/0
	Grand Total		699,129.38			0/0

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

							(February 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	91.86	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	91.86		
	<u>PETROLEUM</u>						
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	212.27	09/2017 03/2018	12/2017
	Total		3,076.00 -	3,076.00	212.27		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
4	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	74.10	02/2017 -	03/2016
	Total		188.75 -	188.75	74.10		
	<u>PETROLEUM</u>						
5	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	314.92	01/2017 -	06/2016
	Total		419.04 -	419.04	314.92		
	<u>URBAN DEVELOPMENT</u>						
6	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						
7	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	826.03	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	826.03		
	Grand Total		15,749.30	15,976.47	4,085.65		

Annexure - XII

List of Projects on schedule w.r.t. Latest Schedule

						(February 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073	10/2013	314.61 -	314.61	22.96	09/2018 -	09/2018
	Total		314.61 -	314.61	22.96		
	<u>COAL</u>						
2	ADASA UG TO OC - [N06000133	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	224.70	03/2016 -	03/2016
4	MALACHUA OPENCAST PROJECT - [N06000139	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
5	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
6	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
7	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	179.12	03/2021 -	03/2021
8	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	205.40	03/2017 -	03/2017
9	AMALGAMATED YEKONA-I YEKONA-II - [N06000132	8/2015	727.28 -	727.28	66.37	03/2025 -	03/2025
10	MAKARDHOKRA I OC - [N06000119	9/2014	266.23 -	266.23	101.81	03/2021 -	03/2021
11	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	48.66	04/2015 04/2019	04/2019
12	HURA - C OC (3 MTY) - [N06000143	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
13	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
14	SINGHORI OC MINE - [N06000130	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
15	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	141.38	03/2020 -	03/2020
16	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	800.01	03/2023 03/2023	03/2023
17	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
18	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	620.96	03/2026 -	03/2026

						(February 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
19	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
20	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
21	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019
22	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
23	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
24	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	53.93	03/2023 -	03/2023
25	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
26	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	109.63	03/2020 -	03/2020
27	GOKUL - [N06000120]	11/2014	267.67 -	267.67	185.72	03/2018 -	03/2018
28	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	67.23	12/2019 -	12/2019
29	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
30	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.56	09/2019 -	09/2019
31	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	224.02	03/2020 -	03/2020
32	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
33	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.89	03/2019 -	03/2019
34	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
35	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
36	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	48.58	03/2021 -	03/2021
37	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
38	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.27	04/2017 -	04/2017
39	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	165.06	03/2018 -	03/2018
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	1,458.17	21.91	06/2015 08/2019	08/2019
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,499.01	12/2015 04/2018	04/2018
42	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
43	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
44	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
45	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	820.31	03/2016 -	03/2016
46	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
47	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	73.30	03/2019 -	03/2019
	Total		43,706.91 -	43,498.41	6,125.91		
	<u>FERTILISERS</u>						
48	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	52.22	11/2016 -	11/2016
	Total		197.79 -	209.44	52.22		
	<u>HEALTH AND FAMILY WELFARE</u>						
49	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	14.38	03/2018 -	03/2018
50	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	67.84	05/2017 -	05/2017
51	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	36.17	05/2017 -	05/2017
52	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	168.90	3.63	05/2017 -	05/2017
	Total		1,172.57 -	1,172.57	122.02		
	<u>MINES</u>						
53	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	6.61	09/2017 -	09/2017
54	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR [N10000008]	12/2015	355.13 -	355.13	-	11/2016 -	11/2016
55	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	-	11/2016 -	11/2016
	Total		2,555.63 -	2,555.63	6.61		
	<u>PETROLEUM</u>						
56	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	586.26	04/2015 05/2016	05/2016

							(February 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	673.95	05/2019 03/2020	03/2020
58	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
59	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	633.74	04/2016 12/2017	12/2017
60	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	84.88	10/2017 02/2018	02/2018
61	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	170.03	09/2016 -	09/2016
62	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
63	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	10,366.19	05/2016 -	05/2016
64	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,325.28	03/2015 05/2016	05/2016
65	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	142.35	12/2016 -	12/2016
66	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018
67	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,954.21	05/2017 05/2017	05/2017
68	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	7.30	03/2017 -	03/2017
69	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016
70	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES [N16000205]	5/2015	2,443.00 -	2,443.00	120.23	12/2017 -	12/2017
71	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY [N16000180]	2/2014	163.88 -	163.00	58.18	07/2016 -	07/2016
72	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	0.37	03/2013 10/2016	10/2016
73	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
74	IOR OF B-173A FIELD - [N16000140]	1/2012	352.49 -	352.49	138.84	03/2014 05/2016	05/2016
75	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,130.50	05/2014 03/2017	03/2017
76	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	112.97	09/2017 -	09/2017
77	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	7/2009	3,957.00 -	3,561.00	85.47	01/2013 12/2018	12/2018
78	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	579.21	11/2015 11/2016	11/2016

						(February 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	1,256.72	1,011.65	05/2013 04/2016	04/2016
80	CONSTRUCTION OF 6 ETPS - [N16000117	3/2009	317.64 -	240.95	127.15	09/2012 06/2016	06/2016
81	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25 -	160.16	75.40	07/2016 -	07/2016
82	DIESEL HYDROTREATOR - [N16000207	7/2015	1,031.37 -	1,031.37	24.29	01/2018 -	01/2018
83	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,190.69	-	04/2018 -	04/2018
84	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212	1/2015	4,619.94 -	4,619.94	420.28	12/2017 -	12/2017
85	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
86	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211	11/2014	195.63 -	195.63	-	09/2018 -	09/2018
87	SIX PIPELINE REPLACEMENT PROJECT - [N16000214	3/2009	181.02 -	181.02	78.73	01/2017 -	01/2017
88	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	749.00	41.18	02/2020 -	02/2020
89	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	462.79	265.72	10/2014 03/2017	03/2017
90	PIPELINE REPLACEMENT PROJECT -4 - [N16000203	2/2015	2,899.93 -	2,098.43	641.31	05/2017 -	05/2017
	Total		71,238.09 -	73,633.68	22,954.12		
	<u>POWER</u>						
91	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080	2/2010	2,144.00 -	2,932.88	2,293.90	12/2012 12/2016	12/2016
92	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174	7/2013	3,363.12 -	3,363.12	1,121.00	12/2016 -	12/2016
93	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201	7/2015	307.18 -	307.18	12.70	11/2017 -	11/2017
95	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208	1/2016	1,455.47 -	1,455.47	-	07/2018 -	07/2018
96	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198	5/2015	312.94 -	312.94	26.50	05/2016 -	05/2016
97	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209	1/2016	162.11 -	162.11	-	05/2018 -	05/2018

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.20	07/2018 -	07/2018
99	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,713.00	06/2017 -	06/2017
100	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	609.44	590.10	02/2014 03/2016	03/2016
101	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	5/2015	436.68 -	436.68	436.90	12/2016 -	12/2016
102	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	1,111.17	08/2013 07/2016	07/2016
103	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	101.40	08/2016 -	08/2016
104	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	345.30	04/2018 -	04/2018
105	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	258.10	04/2018 -	04/2018
106	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	84.40	04/2017 -	04/2017
107	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	4,401.09	12/2009 07/2016	07/2016
108	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	-	03/2017 -	03/2017
109	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	1,056.00	03/2019 -	03/2019
110	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	-	07/2018 -	07/2018
111	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180]	1/2015	268.80 -	268.80	23.30	03/2018 -	03/2018
112	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	5,025.00	09/2017 -	09/2017
113	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	163.00	09/2019 -	09/2019
114	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	2,978.86	1,644.81	02/2016 09/2019	09/2019
115	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211]	1/2016	187.04 -	187.04	-	06/2018 -	06/2018
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 -	539.82	125.20	06/2016 -	06/2016
117	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	6.20	10/2017 -	10/2017

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	972.25	07/2006 10/2016	10/2016
119	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC [N18000167]	6/2014	400.47 -	400.47	46.70	04/2017 -	04/2017
120	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	11,605.20	08/2013 12/2017	12/2017
121	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	121.97	04/2020 -	04/2020
122	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	67.80	11/2017 -	11/2017
123	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	71.60	02/2017 -	02/2017
124	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	1,473.00	09/2019 -	09/2019
125	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,449.00	02/2019 -	02/2019
126	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
127	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	96.20	11/2016 -	11/2016
128	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	779.10	05/2016 -	05/2016
129	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	387.90	05/2018 -	05/2018
130	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII [N18000159]	2/2014	908.08 -	908.08	236.90	06/2016 -	06/2016
132	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	21.10	03/2018 -	03/2018
133	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	120.00	10/2016 -	10/2016
134	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
135	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
136	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
137	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	5,361.60	01/2018 -	01/2018
139	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,829.00	08/2018 -	08/2018
140	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
141	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
	Total		152,940.42 -	163,125.10	51,938.37		
	<u>RAILWAYS</u>						
142	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
143	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
144	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
145	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
146	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
147	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
148	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
	Total		8,820.53 -	17,767.82	2,626.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
149	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
150	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	370.66	04/2010 09/2016	09/2016
151	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	37.55	02/2017 -	02/2017
152	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
153	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	105.78	04/2017 -	04/2017
154	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016

							(February 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	GUWAHATI TO NALBARI (AS-5) - [N24000046	12/2003	198.16 -	198.16	242.40	04/2008 04/2016	04/2016
156	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	85.17	04/2017 -	04/2017
157	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	26.50	07/2017 -	07/2017
158	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
159	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	-	01/2017 -	01/2017
160	FOUR LANING OF KHARAR - KURALI SECTION OF NH- 21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
161	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
162	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	60.87	05/2017 -	05/2017
163	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
164	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	89.15	09/2017 -	09/2017
165	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
166	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
167	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
168	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	161.76	02/2018 -	02/2018
169	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
170	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428	6/2014	569.38 -	569.38	737.51	06/2016 -	06/2016
171	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236	10/2013	677.79 -	677.79	604.72	04/2016 -	04/2016
172	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508	7/2015	1,871.34 -	1,871.34	1,125.73	01/2018 -	01/2018
173	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453	1/2015	972.50 -	972.50	934.81	07/2017 -	07/2017
174	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	674.20	09/2016 -	09/2016
175	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	-	08/2016 -	08/2016
176	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457	2/2012	912.00 -	912.00	-	08/2016 -	08/2016

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
177	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
178	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
179	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
180	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
181	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
182	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
183	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
184	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	10/2014	437.39 -	437.39	-	06/2018 -	06/2018
185	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
186	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
187	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
188	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
189	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
191	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
192	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
193	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
194	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
195	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	3/2015	829.00 -	829.00	-	03/2018 -	03/2018
196	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
197	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
198	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
199	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
200	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
201	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
202	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
203	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	116.28	03/2016 -	03/2016
204	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	13.79	09/2017 -	09/2017
205	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
206	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
207	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242	12/2013	158.65 -	158.65	103.55	03/2016 -	03/2016
208	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
209	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	2.79	11/2017 -	11/2017
210	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
211	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
212	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
213	REHABILITATION AND UPGADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
214	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DSIGN KM 490.800 TO KM 5 - [N24000320	10/2014	463.49 -	463.49	-	06/2018 -	06/2018
215	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
216	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
217	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
218	REHABILITATION AND UPGADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	156.09	61.17	12/2016 -	12/2016
219	UMARIYA TO SHAHOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
220	REHABILITATION AND UPGADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
221	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
222	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
223	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
225	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
226	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
227	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
228	REHABILITATION AND UPGADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	12.80	02/2017 -	02/2017

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
229	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
230	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
231	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTON) TO TW - [N24000243	12/2013	244.08 -	244.08	114.72	03/2016 -	03/2016
232	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
233	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
234	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456	3/2013	959.25 -	959.25	-	06/2016 -	06/2016
235	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	233.96	08/2016 -	08/2016
236	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,253.44	11/2016 -	11/2016
237	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	37.00	04/2018 -	04/2018
238	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
239	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
240	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
241	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
242	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
243	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
245	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
246	FOUR LANING OF CHADIGARH - KHARAR - [N24000503	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
247	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
248	GUWHATI TO NALBARI (AS-4) - [N24000038	12/2003	175.96 -	175.96	304.17	04/2008 08/2016	08/2016

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
249	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10	240.10	147.69	03/2016	03/2016
250	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56	768.56	-	03/2018	03/2018
251	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]	1/1991	269.26	269.26	-	10/2016	10/2016
252	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32	327.32	-	05/2017	05/2017
253	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51	788.51	-	03/2018	03/2018
254	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08	538.08	-	02/2018	02/2018
255	VADODARA-SURAT SECTION - [N24000361]	3/2014	503.16	503.16	-	08/2016	08/2016
256	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09	261.09	5.00	05/2017	05/2017
257	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	295.20	04/2008 01/2017	01/2017
258	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28	815.28	-	06/2018	06/2018
259	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19	425.19	184.07	09/2016	09/2016
260	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92	563.92	-	11/2016	11/2016
261	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90	1,012.90	-	03/2016	03/2016
262	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31	789.31	-	03/2018	03/2018
263	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11	1,387.11	-	11/2017	11/2017
264	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00	709.00	-	09/2017	09/2017
265	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37	996.37	-	12/2017	12/2017
266	JAISALMER - BARMER - [N24000348]	8/2015	482.27	482.27	16.90	02/2018	02/2018
267	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	214.17	03/2008 07/2016	07/2016
	Total		62,849.60	63,080.93	9,394.75		

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
268	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017
269	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017
270	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	2/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017
271	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		928.29 -	942.12	63.91		
	<u>STEEL</u>						
272	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	3.63	09/2017 -	09/2017
273	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]	8/2012	185.37 -	185.37	-	03/2016 -	03/2016
274	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 253.92	253.92	193.97	06/2016 -	06/2016
275	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	196.12	12/2016 -	12/2016
276	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
277	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103]	4/2014	151.33 -	151.33	4.84	09/2017 -	09/2017
278	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]	2/2014	787.29 -	787.29	251.53	12/2016 -	12/2016
279	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
280	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	28.55	09/2016 -	09/2016
281	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	28.20	12/2017 -	12/2017
282	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	26.98	10/2017 -	10/2017
283	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	8,727.80	05/2015 12/2016	12/2016
284	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	303.25	04/2018 -	04/2018

(February 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
285	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
286	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
	Total		28,264.20 -	28,288.59	10,006.98		
	<u>URBAN DEVELOPMENT</u>						
287	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
288	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017
289	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	1,162.27	11/2019 -	11/2019
290	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
291	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	74.92	03/2018 -	03/2018
292	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	93.89	09/2016 -	09/2016
	Total		41,058.91 -	41,058.91	1,361.75		
	Grand Total		414,047.55	435,647.81	104,675.83		

Annexure - XIII**List of ongoing projects having cost overrun w.r.t. to revised schedule**

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,061.76 -	2,204.28			
	<u>HEAVY INDUSTRY</u>						
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
8	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	450.55	03/2017 -	03/2018	27.79
10	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86 -	232.00	09/2016 -	09/2016	63.54
11	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
12	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
	Total		15,590.77 -	18,386.55			
	<u>POWER</u>						
13	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28
14	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
15	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63
16	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203	02/2015	302.49 302.00	302.49	02/2016 -	03/2016	0.00
17	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	06/2016	83.21
18	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	03/2016	133.06
19	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
	Total		21,645.83 -	48,554.18			
	<u>RAILWAYS</u>						
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
21	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
22	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
23	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
24	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
26	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
28	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
29	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
30	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
31	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
32	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
33	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
34	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
35	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
36	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
38	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
39	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
40	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	360.00	02/2006 -	-	37.56
41	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
42	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
43	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	03/2016	166.63
44	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	490.00	- -	-	292.00
45	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	1,080.00	- -	-	136.84
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
47	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
48	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
49	VIRAMGAM-BHILD(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
50	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
51	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
52	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
53	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
54	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
55	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
56	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
57	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
58	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
59	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
60	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
61	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
62	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
63	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
64	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
65	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
66	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
67	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
68	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
69	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
70	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
71	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
72	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
73	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
75	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	800.00	01/1999 -	-	71.50
76	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00	01/1999 -	-	53.96
77	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	-	-	447.91
78	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
79	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
80	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
82	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	-	-	232.17
83	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
84	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	-	-	324.33
85	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
86	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
87	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	-	367.76
88	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
89	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	-	03/2017	148.12
90	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	827.73	-	03/2019	175.91
91	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
93	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
94	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
95	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	-	03/2018	99.75

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
96	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
97	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
98	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
99	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
100	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
101	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
102	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
103	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
104	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
105	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
106	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
107	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
108	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
109	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
110	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
111	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
112	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26 -	1,072.51	- -	-	28.25
113	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
114	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
115	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
116	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
117	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
118	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
120	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
121	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
122	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
123	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
124	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
125	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
126	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
127	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
128	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
130	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
131	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
132	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
133	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
134	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
135	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
136	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
137	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
138	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
139	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	926.09	- -	-	338.91
143	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	367.17	- -	-	72.37
144	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
145	ATTIPPATTU-PUTTUR - [N22000184	04/2008	446.87 -	528.00	- -	-	18.16
146	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,200.00	- -	-	129.22
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
148	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
149	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1998	271.24 -	520.00	- -	-	91.71
150	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	- -	-	55.74
151	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14
152	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	563.13	- -	03/2019	154.33
153	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
154	AGARTALA-AKHAURA NL - [N22000195	04/2012	252.00 -	886.65	- -	03/2018	251.85
155	DIMAPUR-TIZIT NL - [N22000196	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
156	NEW COOCHBEHAR TO SAMUKTALA - [N22000197	04/2011	209.77 -	441.45	- -	03/2018	110.44
157	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198	04/2012	283.55 -	288.81	- -	03/2018	1.86
158	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.22	- -	-	109.04
159	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71
160	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	03/2015	285.12
161	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29
162	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
163	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	679.57	- -	03/2018	180.56
164	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	394.28	- -	03/2017	63.25

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
166	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
167	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
168	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
169	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
170	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
	Total		77,770.05 -	195,587.58			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
171	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93
172	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
173	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
174	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
175	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2016	106.50
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2016	30.10
177	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
178	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
179	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
180	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
181	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	0.00
182	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		3,492.35 -	5,544.33			

(February 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
183	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	03/2016	300.00
184	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
185	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
186	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
187	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,070.97	02/2014 -	03/2016	39.29
188	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
189	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50
	Total		1,261.61 -	1,735.31			
	<u>URBAN DEVELOPMENT</u>						
190	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
191	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]	06/2010	205.00 -	191.97	03/2012 -	03/2017	-6.36
	Total		6,600.00 -	11,800.97			
	Grand Total		152,488.14	327,926.22			

Annexure-XIV

List of Delayed Projects w.r.t. Latest Schedule

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,160.00	12/2008 10/2013	05/2016	89	31
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,166.65	09/2010 -	09/2016	72	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	7,917.00	12/2015 10/2016	11/2018	35	25
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,650.00	12/2016 03/2017	12/2019	36	33
	Total		40,442.00 -	51,918.00	39,893.65				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	417.66	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	417.66				
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	2,006.46	03/2014 -	03/2016	24	-
7	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	504.99	03/2013 -	03/2016	36	-
8	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 -	1,228.39	869.37	03/2013 -	03/2016	36	-
9	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	85.26	03/2015 -	03/2016	12	-
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	83.51	03/2012 -	03/2016	48	-
11	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	36.16	03/2011 -	03/2016	60	-
12	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	-
13	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.46	04/2014 -	03/2016	23	-
14	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	196.19	10/2014 -	03/2016	17	-
15	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	75.24	03/2014 -	09/2016	30	-
16	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	104.25	05/2014 -	10/2016	29	-
17	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	69.89	04/2014 -	11/2016	31	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96	302.96	302.92	03/2010	03/2017	84	-
19	ASHOK EXPN OCP CCL (10 MTY) - [N060100096]CCL, JHARKHAND	12/2007	341.63	341.63	126.41	03/2011	03/2017	72	-
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18	287.18	226.26	03/2011	03/2017	72	-
21	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77	457.77	210.87	03/2013	03/2017	48	-
22	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08	172.08	152.05	03/2010	03/2017	84	-
23	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63	453.63	120.89	12/2012	03/2017	51	-
24	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28	207.28	207.71	03/2012	03/2017	60	-
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	479.53	185.34	03/2013	03/2017	48	-
26	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	94.84	03/2012	03/2017	60	-
27	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98	210.98	150.78	03/2013	03/2017	48	-
28	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	70.25	03/2014	03/2017	36	-
29	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	-
30	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	25.28	07/2016	03/2017	8	-
31	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03	249.03	118.02	03/2012	03/2018	72	-
32	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	211.06	03/2014	03/2018	48	-
33	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	8.03	03/2015	03/2018	36	-
34	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76	162.76	1.31	03/2015	03/2018	36	-
35	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	77.44	03/2015	03/2018	36	-
36	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56	258.56	102.72	03/2016	03/2018	24	-
37	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45	486.27	93.51	03/2016	03/2018	24	-
38	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05	1,055.05	206.70	03/2018	07/2018	4	-
39	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	24.72	03/2015	03/2020	60	-
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	0.30	03/2014	03/2020	72	-
42	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40	706.40	79.03	07/2012	03/2021	104	-
43	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	-

(February 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
44	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	457.41	03/2012 -	03/2023	132	-
	Total		15,419.01 -	16,513.27	7,579.34				
	STEEL								
45	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	233.55	08/2014 -	03/2016	19	-
46	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	1,070.97	1,070.97	02/2014 -	03/2016	25	-
47	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3	-
48	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	174.45	10/2013 -	06/2016	32	-
49	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	454.15	07/2015 -	08/2016	13	-
50	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	326.57	04/2016 -	09/2016	5	-
51	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,636.77	03/2013 -	11/2016	44	-
52	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	98.57	05/2016 -	12/2016	7	-
53	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	60.23	04/2015 -	12/2016	20	-
54	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	234.67	07/2016 -	12/2016	5	-
55	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	175.94	12/2015 -	03/2017	15	-
56	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	285.39	07/2015 -	06/2017	23	-
57	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	39.17	10/2016 -	06/2017	8	-
58	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	206.71	134.61	12/2016 -	07/2017	7	-
	Total		22,947.11 -	23,452.16	19,188.61				
	PETROLEUM								
59	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	31,300.53	11/2012 11/2013	02/2016	39	27
60	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	322.07	06/2011 03/2012	03/2016	57	48
61	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	187.05	12/2014 -	03/2016	15	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]JSPL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,091.39	10/2011 -	03/2016	53	-
63	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
64	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]JSPL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,449.53	01/2012 -	05/2016	52	-
65	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,327.98	09/2012 -	06/2016	45	-
66	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,321.77	08/2015 -	06/2016	10	-
67	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	433.56	08/2015 -	06/2016	10	-
68	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	51.55	02/2016 02/2016	07/2016	5	5
69	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	559.57	03/2015 11/2015	08/2016	17	9
70	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	422.00	179.18	02/2016 -	10/2016	8	-
71	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,494.16	11/2015 07/2016	11/2016	12	4
72	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	493.61	08/2015 -	12/2016	16	-
73	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	147.98	11/2016 -	12/2016	1	-
74	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48	12
75	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	34.87	11/2016 -	04/2017	5	-
76	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2018	12	-
77	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	-
78	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,381.31	12/2012 -	02/2019	74	-
	Total		49,747.78 -	56,003.16	43,956.98				
	<u>POWER</u>								
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	366.37	02/2012 -	03/2016	49	-
80	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	766.74	11/2012 -	03/2016	40	-
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,463.52	04/2013 -	03/2016	35	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
82	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,609.36	11/2013 -	03/2016	28	-
83	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,448.76	08/2014 -	03/2016	19	-
84	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,600.27	10/2014 -	03/2016	17	-
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	333.82	05/2015 -	03/2016	10	-
86	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]JNTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,198.14	01/2013 -	03/2016	38	-
87	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.30	9,606.82	8,222.09	02/2011 -	03/2016	61	-
88	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN	02/2015	302.49 302.00	302.49	268.27	02/2016 -	03/2016	1	-
89	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	236.20	01/2013 -	05/2016	40	-
90	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5	-
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	541.66	11/2011 -	06/2016	55	-
92	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,071.59	08/2012 -	06/2016	46	-
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	554.02	07/2013 11/2015	06/2016	35	7
94	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,801.75	05/2014 -	06/2016	25	-
95	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,959.76	09/2014 -	06/2016	21	-
96	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	537.51	11/2013 -	06/2016	31	-
97	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	306.27	08/2014 06/2015	06/2016	22	12
98	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,436.82	01/2015 -	06/2016	17	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
99	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	96.23	09/2014 -	06/2016	21	-
100	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	5,841.39	06/2015 -	06/2016	12	-
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	598.32	11/2014 -	06/2016	19	-
102	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	3,089.11	10/2014 -	06/2016	20	-
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	466.89	03/2016 -	06/2016	3	-
104	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	479.74	04/2016 -	06/2016	2	-
105	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	5.40	03/2016 -	06/2016	3	-
106	EASTERN REGION STRENGTHENING SCHEME-IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	25.30	02/2016 -	06/2016	4	-
107	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,237.67	3,247.07	12/2011 03/2016	06/2016	54	3
108	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	345.40	06/2015 -	08/2016	14	-
109	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,044.13	06/2015 -	08/2016	14	-
110	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	2,193.08	1,986.06	09/2009 -	09/2016	84	-
111	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,751.47	4,433.49	01/2016 -	11/2016	10	-
112	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	16.30	04/2016 -	11/2016	7	-
113	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,904.95	11/2008 01/2016	12/2016	97	11
114	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	597.69	09/2010 01/2016	12/2016	75	11
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,256.58	10/2012 -	12/2016	50	-
116	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,338.43	07/2014 -	12/2016	29	-
117	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,482.93	08/2014 12/2015	12/2016	28	12

(February 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
118	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,968.00	09/2016 -	12/2016	3	-
119	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,049.05	12/2015 -	12/2016	12	-
120	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,824.00	09/2011 -	03/2017	66	-
121	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,498.65	01/2015 -	03/2017	26	-
122	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80 -	1,272.80	1,254.53	11/2012 -	03/2017	52	-
123	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	10,325.00	01/2017 -	03/2017	2	-
124	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,991.00	11/2016 -	08/2017	9	-
125	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	5,347.06	05/2014 -	09/2017	40	-
126	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	4,664.54	12/2016 -	09/2017	9	-
127	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	55.26	02/2014 -	02/2018	48	-
128	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,241.00	01/2011 10/2014	05/2018	88	43
129	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.76	5,460.85	09/2009 -	12/2018	111	-
130	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,724.00	03/2013 -	12/2018	69	-
131	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	814.10	06/2013 -	12/2019	78	-
	Total		142,291.24 -	168,202.11	123,283.57				
	HEAVY INDUSTRY								
132	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	HEALTH AND FAMILY WELFARE								
133	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	285.20	12/2015 -	03/2016	3	-
134	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	15	-
135	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	196.70	165.97	01/2016 -	04/2016	3	-
136	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	120.80	11/2013 -	06/2016	31	-

(February 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		976.47	976.47	685.47				
	RAILWAYS								
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	03/2017	84	-
138	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	-
139	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84	-
140	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
141	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
142	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	-
143	DANGOPOSI-RAJAKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
144	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	-
145	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	86
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	91
148	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
149	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
150	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	66
151	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	-
152	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	-
153	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	-
154	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	-
155	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
156	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
157	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
158	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
159	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
160	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-
161	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
162	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,544.40	590.26	03/1998 -	12/2019	261	-
163	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
164	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
165	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-
	Total		31,485.20 -	82,512.86	37,527.48				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
167	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38	-
168	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	02/2016	92	-
169	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	468.41	05/2010 -	02/2016	69	-
170	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 2,782.54	1,509.10	2,891.15	09/2012 -	02/2016	41	-
171	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	225.26	09/2014 -	02/2016	17	-
172	4 LANING OF GOMTI CHAURAH - UDAIPUR - [N24000455]DORTH, RAJASTHAN	03/2012	914.50 -	914.50	1,097.62	10/2015 -	02/2016	4	-
173	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	242.00	09/2008 -	03/2016	90	-
174	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	03/2016	85	-
175	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	03/2016	83	-
176	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88	-
177	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88	-
178	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00	195.00	-	06/2008	03/2016	93	-
180	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80	237.80	-	06/2008	03/2016	93	-
181	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94	332.94	493.27	09/2008	03/2016	90	-
182	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00	250.39	274.11	10/2008	03/2016	89	-
183	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00	331.23	-	07/2009	03/2016	80	-
184	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16	348.16	342.49	09/2007	03/2016	102	-
185	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00	795.00	1,607.78	05/2012	03/2016	46	-
186	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00	1,175.00	-	04/2013	03/2016	35	-
187	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00	1,267.00	2,425.00	06/2013	03/2016	33	-
188	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76	2,498.76	-	08/2014	03/2016	19	-
189	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54	351.54	329.40	05/2013	03/2016	34	-
190	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00	650.00	830.97	11/2013	03/2016	28	-
191	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00	664.00	609.00	02/2014	03/2016	25	-
192	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	574.00	761.49	03/2014	03/2016	24	-
193	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09	375.09	352.00	04/2014	03/2016	23	-
194	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54	511.54	-	11/2013	03/2016	28	-
195	4-LANNING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00	398.00	-	02/2014	03/2016	25	-
196	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00	835.00	1,684.00	01/2014	03/2016	26	-
197	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29	500.29	-	08/2013	03/2016	31	-
198	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81	267.81	699.60	02/2013	03/2016	37	-
199	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51	2,388.00	2,472.00	06/2014	03/2016	21	-
200	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00	1,047.00	-	06/2014	03/2016	21	-
201	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	455.26	10/2014	03/2016	17	-
202	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69	942.69	229.16	06/2014	03/2016	21	-
203	FOUR LANNING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00	1,232.00	927.19	08/2015	03/2016	7	-
204	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00	240.00	295.38	11/2008	03/2016	88	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7	-
206	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	-
207	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	-	09/2010 -	04/2016	67	-
208	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,409.36	07/2012 -	04/2016	45	-
209	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,006.79	07/2013 -	04/2016	33	-
210	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32	-
211	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	822.96	04/2015 -	04/2016	12	-
212	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	-
213	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
214	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,310.32	09/2014 -	05/2016	20	-
215	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	158.04	117.97	12/2015 -	05/2016	5	-
216	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	-
217	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	-	10/2011 -	06/2016	56	-
218	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,619.94	11/2011 -	06/2016	55	-
219	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39	-
220	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
221	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35	-
222	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	06/2016	36	-
223	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	307.41	06/2013 -	06/2016	36	-
224	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35	-
225	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29	-
226	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,503.31	05/2014 -	06/2016	25	-
227	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
228	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	902.06	03/2013 -	06/2016	39	-
229	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,844.50	09/2015 -	06/2016	9	-
230	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	-	12/2015 -	06/2016	6	-
231	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21	-
232	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGAN-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5	-
233	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	-
234	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.41	10/2013 -	07/2016	33	-
235	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	-
236	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.40	05/2008 07/2016	08/2016	99	1
237	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,070.90	05/2013 -	08/2016	39	-
238	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,876.89	08/2013 -	08/2016	36	-
239	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,313.00	02/2014 -	08/2016	30	-
240	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	-
241	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	1,579.15	06/2012 -	08/2016	50	-
242	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	453.58	05/2013 -	09/2016	40	-
243	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	211.68	01/2014 -	09/2016	32	-
244	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	133.92	01/2016 -	09/2016	8	-
245	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	-
246	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	-
247	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	195.93	01/2016 -	10/2016	9	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
248	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	-
249	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	28.66	11/2014 -	11/2016	24	-
250	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	-	06/2005 -	12/2016	138	-
251	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	-	09/2007 -	12/2016	111	-
252	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	-
253	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	-
254	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,778.42	03/2013 -	12/2016	45	-
255	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	880.14	02/2013 -	12/2016	46	-
256	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	-	12/2013 -	12/2016	36	-
257	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.57	07/2013 -	12/2016	41	-
258	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35	-
259	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	437.14	09/2013 -	12/2016	39	-
260	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	343.75	04/2014 -	12/2016	32	-
261	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	176.11	10/2015 -	12/2016	14	-
262	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12	-
263	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	-
264	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	301.04	32.54	01/2016 -	12/2016	11	-
265	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	283.72	11/2016 -	12/2016	1	-
266	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	62.37	01/2016 -	01/2017	12	-
267	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	-

(February 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
268	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	27.87	02/2015 -	02/2017	24	-
269	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55	-
270	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	-	08/2013 -	03/2017	43	-
271	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	03/2017	16	-
272	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	542.01	03/2014 -	04/2017	37	-
273	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	162.47	02/2010 -	05/2017	87	-
274	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	222.75	08/2013 -	05/2017	45	-
275	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	480.44	06/2015 -	05/2017	23	-
276	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
277	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,655.11	08/2013 -	07/2017	47	-
278	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	-
279	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	58.64	09/2016 -	09/2017	12	-
280	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
281	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	-
282	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	-
283	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	303.94	05/2013 -	12/2017	55	-
284	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	622.74	10/2013 -	12/2017	50	-
285	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	347.00	07/2014 -	12/2017	41	-
286	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-

(February 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
287	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	-
288	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, MADHYA PRADESH	11/2015	867.66 -	867.66	52.60	11/2015 -	05/2018	30	-
289	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
290	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
	Total		88,850.19 -	90,584.17	56,865.31				
	<u>SHIPPING AND PORTS</u>								
291	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120	2
292	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	77
	Total		395.67 -	1,009.83	506.00				
	<u>TELECOMMUNICATIONS</u>								
293	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	-
294	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-
	Total		15,445.17 -	15,345.17	2,720.00				
	<u>URBAN DEVELOPMENT</u>								
295	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	03/2016	16	-
296	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
297	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	139.88	06/2012 03/2016	05/2016	47	2
298	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	171.26	05/2013 10/2015	06/2016	37	8
299	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,776.56	12/2015 -	08/2016	8	-

(February 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
300	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 315.00	315.00	176.16	06/2015 08/2016	10/2016	16	2
301	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9	-
302	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	91.53	12/2014 12/2016	03/2017	27	3
303	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 142.37	191.97	119.44	03/2012 08/2016	03/2017	60	7
304	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	29.17	09/2015 07/2016	04/2017	19	9
305	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	-
	Total		55,385.80 -	55,372.77	32,689.03				
	Grand Total		465,413.10	566,026.73	365,313.10				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2019	12320	36
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2018	11459	35
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	13171	89
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
10	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
11	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
12	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
13	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
14	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
15	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
16	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
17	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
18	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
19	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
20	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
22	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
23	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
24	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
25	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
26	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	09/2016	153.82	30
27	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
28	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
29	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
30	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
31	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
32	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
33	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
34	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
35	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
36	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
37	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
38	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
39	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
41	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	03/2016	364.75	17
42	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
43	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
45	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
46	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
47	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	03/2016	175.57	15
49	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	06/2016	159.5	31

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	10/2016	310	43
52	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	17
53	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732	53
54	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	06/2016	586	10
55	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
56	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
57	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	05/2016	1138.5	13
58	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	10/2016	736.65	61
59	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2018	352.56	12
60	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993	52
61	INTEGRATED DEVELOPMENT OF VASHISTA	ONGC	05/2013	04/2016	12/2017	4124.35	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AND S-1 FIELDS						
62	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
63	REPLACEMENT OF COKE CHAMBERS	IOCL	04/2013	02/2016	10/2016	480	8
64	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
65	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	06/2016	317.64	45
66	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	35
68	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	06/2016	1793	45
69	DE-BOTTLENECKING OF SMPL	IOCL	12/2009	08/2015	06/2016	1584	10
70	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	02/2016	29777	39
71	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
72	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	02/2019	2915	74
73	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
74	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	11/2016	3110.36	12
75	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
76	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2017	2592.17	34
77	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
78	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	12/2016	913	16
79	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29
80	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	03/2016	279	15

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
82	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN	PGCIL	03/2012	09/2014	06/2016	198.63	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	REGION						
83	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	03/2016	552.44	25
84	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	06/2016	297.33	22
85	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	12/2011	08/2014	12/2016	1746.65	28
86	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
87	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97
88	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
89	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
90	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
91	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	03/2016	1927.16	17
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
93	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	05/2016	250.03	40
94	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	03/2017	1272.8	52
95	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
96	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
97	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
98	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
99	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	06/2016	2313	54
100	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	03/2016	4122	61
101	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
102	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	84
103	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	75
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
105	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
107	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	03/2016	965.58	40
108	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	03/2016	1585.12	28
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
110	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2017	4404.57	26
111	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
112	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	06/2016	1216.83	46
113	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144	48
114	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
115	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
116	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	03/2016	2422.66	19
117	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	07/2016	2496.9	79
118	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	06/2016	558.26	31
119	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
120	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43
121	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	12/2016	2127.51	29
122	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	35
123	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
124	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
125	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
126	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
128	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
129	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	03/2016	524.4	10
131	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14
132	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	12/2016	2514.88	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
133	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
134	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
135	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
136	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	03/2016	921	84
137	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
138	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
139	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
140	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
141	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
142	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
143	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2017	2500	181
144	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
145	RAJATGARH-BARANG (LD), ECR	RVNL	04/1999	02/2009	04/2016	166.16	86
146	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
148	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
149	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
151	KATAKHAL TO BHAIKABI	NFR	04/1998	12/2012	03/2016	227.9	39
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTPT	03/1996	03/2004	03/2016	495.44	144
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733	111
155	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
156	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
157	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2019	5300	60
158	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
159	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
160	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	06/2018	4874.58	27
161	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	MRTPT	04/2012	03/2016	12/2017	632.68	21
162	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
163	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	08/2016	1170.52	50
164	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	NHAI	11/2015	11/2015	05/2018	867.66	30
165	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	03/2016	1232	7
166	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
167	ETAWAH CHAKERI	NHAI	03/2013	09/2015	06/2016	1573	9
168	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	06/2016	2125.24	6
169	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
170	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
171	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	03/2016	280	85

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
172	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	83
173	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	03/2016	167.64	88
174	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	88
175	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	03/2016	200	83
176	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	03/2016	574	24
177	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	03/2016	835	26
178	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
179	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2016	500.29	31
180	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	10/2016	1410	25
181	BEAWAR PALI PINDWARA	NHAI	12/2011	06/2014	03/2016	2388.51	21
182	BAREILLY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
183	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	06/2016	754	39
184	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
185	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	24
186	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
187	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
188	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
189	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
190	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU	PWD	03/2015	09/2015	08/2017	309.01	23
191	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
192	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	24
193	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
194	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM	MORTH	03/2015	11/2015	11/2017	159.12	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM.56.00 TO 106.00 OF NH-218 BIJAPUR						
195	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	PWD	02/2015	04/2015	05/2016	224.83	13
196	WIDENING WITH PS AND STRONG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	03/2016	164.54	7
197	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHAMAPUR-TAPTA)	PWD	12/2011	08/2015	03/2018	191.08	31
198	SATANA-BELA SECTION OF NH-75 (4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
199	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11
200	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	04/2016	381.86	12
201	REENGUS SIKAR	NHAI	03/2012	09/2014	02/2016	333.51	17
202	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
203	4 LANNING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2016	2498.76	19
204	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
205	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
206	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	06/2016	1813.76	35
207	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
208	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	03/2016	351.54	34
209	TWO LANNING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
210	2 LANNING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	03/2017	485	43
211	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2016	536	29
212	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	03/2016	664	25
213	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
214	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	03/2016	511.54	28
215	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	06/2016	1100.7	24
216	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
217	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM)	NHAI	04/2012	04/2014	12/2016	624	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
218	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
219	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	02/2016	486	69
220	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	03/2016	795	46
221	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108	55
222	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593	33
223	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	06/2016	828	21
224	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
225	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
226	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
227	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
228	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2016	1267	33
229	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
230	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
231	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	06/2016	852	39
232	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	08/2016	1585	39
233	4-LANING OF ROHATAK JIND (LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2016	283.25	14
234	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	02/2016	1509.1	41
235	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	03/2016	1175	35
236	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	04/2016	940	45
237	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	02/2016	792.06	38
238	CHENNAI-TADA (SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
239	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	06/2016	1008.5	36
240	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2016	650	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
241	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	04/2016	1141	32
242	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
243	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2016	953.88	35
244	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
245	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
246	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2016	1535	25
247	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
248	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
249	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
250	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2016	1396.18	20
251	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
252	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
253	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	12/2017	356.4	41
254	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	03/2016	1232	7
255	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	03/2016	348.16	102
256	DHARAMTUL TO SONAPUR, KM 205-183 (AS- 20)	NHAI	12/2003	05/2008	08/2016	160	99
257	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2016	175.96	100
258	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	03/2016	332.94	90
259	HARANGAJO TO MAIBANG, KM 164.08- 190.587 NH-54	NHAI	12/2003	09/2007	12/2016	212	111
260	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196	80
261	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
262	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	06/2016	600	36
263	BIJUNI TO ASSAM /WB.BORDER (NH-	NHAI	12/2003	06/2008	03/2016	237.8	93

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	31.C) (NHAI)						
264	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2016	375.09	23
265	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	03/2016	398	25
266	JAIPUR-REENGUS	NHAI	08/2010	02/2013	03/2016	267.81	37
267	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2016	478.51	33
268	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2016	942.69	21
269	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
270	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	10/2016	495.78	9
271	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	02/2016	264.72	92
272	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	07/2016	245	100
273	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	09/2016	217.61	77
274	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
275	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2016	225	94
276	BIJNI TO ASSAM WB BORDER (NH- 31.C) (1) (NHAI)	NHAI	12/2003	06/2008	03/2016	195	93
277	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	03/2016	155	90
278	KOTA BYPASS, RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	03/2016	275	89
279	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
280	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	12
281	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
282	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	04/2016	198.16	96
283	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49
284	2-LANING WITH PS SITARGANJ BAREILY SECTION	NHAI	06/2014	01/2016	12/2016	301.04	11
285	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH- 125	NHAI	09/2015	09/2016	09/2017	368.73	12
286	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	09/2016	351.34	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
287	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	01/2017	523.85	12
288	KOTWA TO DEWAPUR (LMNHP-10)	NHAI	11/2005	11/2008	03/2016	240	88

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
289	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
290	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	03/2016	150	120

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
291	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	03/2016	332.65	19
292	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	06/2017	404.16	23
293	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
294	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	12/2016	245.67	7
295	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	07/2017	175.49	7
296	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	03/2016	768.88	25
297	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	11/2016	17265	44
298	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	12/2016	188.93	20
299	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	08/2016	877.73	13
300	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343	8
301	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	06/2016	187.33	32
302	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	03/2017	149.73	15

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
303	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2017	13334	20
304	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF	ITI	09/2014	09/2014	03/2017	2111.17	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	INTELLIGENT FIBER OPTIC C						

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
305	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
306	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2016	270.83	16
307	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	05/2016	225.81	47
308	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	03/2017	188.87	27
309	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	04/2017	156.57	19
310	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	05/2017	171.86	14
311	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
312	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	10/2016	315	16
313	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
314	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	03/2017	205	60
315	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
8	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.76	4479.17
20	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18063.89	11778.56
21	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
22	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
23	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	2193.08	1131.7
24	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
25	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
26	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
27	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
28	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
29	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5751.47	2109.43
30	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
31	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1262.27	688.28
32	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
35	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
36	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
37	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
38	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
40	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
41	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
42	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	800	644.45
43	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
44	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
45	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
46	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
47	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
48	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
49	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
50	JIND-SONEPAT (NL) ,NR	NR	01/2004	03/2012	238.56	740	501.44
51	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
52	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	3040	2119
53	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
54	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
55	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
56	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
57	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
58	KATAKHAL TO BHAI RABI	NFR	04/1998	12/2012	227.9	331.4	103.5
59	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
60	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
61	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
63	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
64	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
65	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
66	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
67	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
68	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
69	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
70	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
71	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
72	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
73	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
74	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
75	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
76	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
77	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
78	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
79	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
80	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
81	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	632.68	816.55	183.87
82	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
83	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
84	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA- NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
85	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
86	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
87	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
88	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
89	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
90	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
91	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
92	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
93	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
94	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
95	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
96	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
97	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
98	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
99	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
100	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
101	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
102	HAIJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
103	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
104	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
105	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
106	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
107	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
108	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
109	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
110	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
111	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
112	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
113	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
114	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
115	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
116	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
117	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
118	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
119	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	WCR	04/1997	N.A.	836.26	1072.51	236.25
120	HUBLI-ANKOLA (NL), SWR	SWR	04/1997	N.A.	227	2135	1908
121	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	194.07	335	140.93
122	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
123	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
124	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
125	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
126	MUNEERABAD-MAHABOONNAGAR (NL), SCR	SCR	04/1997	N.A.	218.24	645	426.76
127	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
128	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
129	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
130	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
131	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
132	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
133	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
134	NANDYAL-YERRAGUNTLA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
135	RAJATGARH-BARANG (LD) , ECR	RVNL	04/1999	02/2009	166.16	325.5	159.34
136	DALLI-RAJHARA - RAOGHAT (PART OF DALLI- RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	2434	2109
138	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
139	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	20000	17500
140	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
141	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1651.54	973.57
142	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
143	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
144	KHURDA ROAD-BOLANGIR (NL) ECR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
145	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
146	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
148	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
149	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	3500	3252.34
150	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
151	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
152	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
153	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
154	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
155	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
156	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
157	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
158	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
159	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
160	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
161	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
162	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
163	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
164	RAICHUR-GUNTAKAL(DL) (SCR)	RVNL	04/2003	12/2007	136.62	360	223.38
165	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	318.33	184.92
166	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
167	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
168	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
169	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
170	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
171	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
172	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
173	MAIBANG TO LUMDING (AS-25) , KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
174	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
175	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
177	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
178	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
179	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
180	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMBAI	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
181	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
182	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1070.97	302.09
183	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
184	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	6395	11609	5214

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	1,3171.00	2,2462.00	9291	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	1200.00	328.65	17
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732.00	1227.00	495	53
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993.00	1693.00	700	52
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	1256.72	394.93	35
12	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
13	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	02/2016	2,9777.00	3,4555.00	4778	39

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
14	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
15	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	1262.27	688.28	35
16	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
17	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
18	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	06/2016	2313.00	4237.67	1924.67	54
19	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	03/2016	4122.00	9606.82	5484.82	61
20	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	07/2016	2496.90	6179.96	3683.06	79
21	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
22	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2016	1746.65	2228.71	482.06	28
23	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.76	4479.17	111
25	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	2193.08	1131.7	84
26	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	738.48	260.79	75
27	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
28	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144.00	2932.88	788.88	48
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2187.32	408.03	97
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5751.47	2109.43	10

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
32	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
33	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
34	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	2434.00	2109	84
35	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
36	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
37	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
38	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
39	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	03/2016	921.00	3040.00	2119	84
40	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	318.33	184.92	91
41	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
42	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
43	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
44	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
45	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
46	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
47	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
48	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
49	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
50	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
51	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
52	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2017	2500.00	2,0000.00	17500	181
53	RAJATGARH-BARANG(LD), ECR	RVNL	04/1999	02/2009	04/2016	166.16	325.50	159.34	86
54	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
55	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196.00	331.23	135.23	80
56	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	385.13	185.32	83
57	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108.00	2288.00	1180	55
58	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	280.13	125.09	88

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
59	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88
60	ENORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	03/2016	150.00	600.00	450	120

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
61	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343.00	488.40	145.4	8

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	03/2016	768.88	1070.97	302.09	25

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure-XVIII

Details of 20 Railways Projects [as identified by Ministry of Railways vide letter no. 2011/w-1 /Genl / MoSPI dated 28/10/2015] to be monitored at MoSPI level

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>RAILWAYS</u>					
1	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 2,434.00 2,434.00	03/2010 -	03/2017	0/0
2	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 3,040.00 3,040.00	03/2009 -	03/2016	0/0
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 - 5,500.00	03/2009 -	03/2016	0/0
4	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 - 1,242.25	03/2007 -	03/2016	0/0
5	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 - 4,996.19	04/2008 12/2011	06/2017	0/0
6	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 - 20,000.00	11/2002 -	12/2017	0/0
7	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36 1,651.54	- -	03/2018	0/0
8	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 - 1,143.60	- -	03/2018	0/0
9	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 - 1,544.40	03/1998 -	12/2019	0/0
10	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 - 2,957.21	07/2005 -	-	0/0
11	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 3,500.00 3,500.00	05/2008 -	-	0/0
12	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 - 1,185.64	- 09/2009	-	0/0
13	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 - 2,921.00	10/2007 -	-	0/0
14	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 - 1,202.70	02/2015 -	-	0/0

			(February 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 - 1,266.89	- -	-	0/0
16	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 - 1,280.83	- -	-	0/0
17	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 2,200.00 2,200.00	- -	-	0/0
18	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 - 2,127.00	- -	-	0/0
19	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 - 1,111.99	- -	-	0/0
20	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]WCR,UTTAR PRADESH	04/1997	836.26 - 1,072.51	- -	-	0/0
	Total		20,808.52 -			0/0
	Grand Total		20,808.52			0/0
