

388th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
February 2018



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI Airport Authority of India Ltd.
AERB Atomic Energy Regulatory Board
AIBP Accelerated Irrigation Benefit Programme
AIR All India Radio
APW Active Process Water
ATU Atomic Treating Unit
BCM Billion Cubic Meter
BHEL Bharat Heavy Electricals Ltd.
BHPV Bharat Heavy Plates & Vessel Ltd.
BLU Boiler Light Up
BOLT Build , Operate, Lease & Transfer
BPST Bureau of Parliamentary Studies & Training
CCEA Cabinet Committee on Economic Affairs
CCU Catalytic Cracking Unit
CDS Crude Distribution System
CDU Crude Distillation Unit
CEA Central Electricity Authority
CEC Central Empowered Committee
CHP Coal Handling Plant
CLW Chittaranjan Locomotive Works
CMPDI Central Mine Planning & Design Institute
COS Committee of Secretaries
COR Cost Overrun
CPP Captive Power Plant
CRIS Centre for Railway Information System
CRL Cochin Refinery Ltd.
CSL Cochin Shipyard Ltd.
CTU Crude Topping Unit
DAE Department of Atomic Energy
DB Dumb Barges
DCME Digital Circuit Multiplexing Equipment
DGMS Director General Mines Safety
DHDS Diesel Hydro Desulphurisation project
DOA Date of Approval
DOC Date of Commissioning
DOT Department of Telecommunication
DVC Damodar Valley Corporation
ECL Eastern Coalfields Ltd.
EIL Engineers India Ltd.
EMP Environment Management Plan
EOT Electrical Overhead Travelling crane
ESP Electrostatic Precipitator
FCCU Fluidised Catalytic Cracker Unit
ERP Enterprise Resource Planning
FE Foreign Exchange
FOIS Freight Operation Information System
FPU Feed Preparation Unit
GAIL Gas Authority of India Ltd.
GC Gauge Conversion
GDS Gateway Digital Switch
GIS Gas Insulated Station
GT Gas Turbine
GTPP Gas Turbine Power Plant
HCU Hydro- cracker Unit
HEC Heavy Engineering Corporation
HEMM Heavy Equipment & Mining Machinery
HEP Hydro Electric Project
HPCL Hindustan Petroleum Corporation Ltd.
HRT Head Race Tunnel
HSCL Hindustan Steel Construction Ltd.
HVDC High Voltage Direct Current
IAAI International Airport Authority of India
ICT Inter Connecting Transformer
IDC Interest During construction
IFFCO Indian Farmer Fertilizer Co-operative Ltd.
IMG Inter Ministerial Group
IOC Indian Oil Corporation Ltd.
IPCL Indian Petrochemicals Ltd.
KV Kilo Volts.

L&T Larsen & Toubro
LEP Life Extension Program
LOI Letter of Intent
LPG Liquefied Petroleum Gas
LSTK Lump sum Turnkey contract
MAMC Mining & Allied Machinery Corporation.
MFL Madras Fertilizer Ltd.
MGCL Madras Gas Cracker Complex
MIS Management Information System
MMSCMD Million Metric Standard Cubic Meter day
MMT Million Metric Tonnes
MOE&F Ministry of Environment & Forest
MT Metric Tonnes
MTY Metric Tonne per year
MU Million Unit
MW Mega Watts
NAC New Anticipated Cost
NALCO National Aluminium Company
NBCC National Building Construction Corporation.
NCL Northern Coalfields Ltd
NEC North East Council
NEEPCO North-Eastern Electric Power Corporation Ltd.
NFL National Fertilizer Ltd.
NH National Highway
NHPC National Hydro-Electric Power Corporation
NIRE National Institute of Renewable Energy
NIT Notice Inviting Tender
NJPC Nathpa Jhakri Power Corporation Ltd.
NGN Next Generation Network
NLC Neyveli Lignite Corporation Ltd.
NMDC National Mineral Development Corporation Ltd.
NPC Nuclear Power Corporation Ltd.
NRL Numaligarh Refinery Ltd.
OB Over Burden
OC Opencast
OECD Overseas Economic Co-operation Fund
ONGC Oil & Natural Gas Commission
OPGC Orissa Power Generation Corporation
P & M Plant & Machinery
PERT Project Evaluation & Review Technique
PSTN Public Switched Telephone Network
PHT Primary Heat Transport
PIB Public Investment Board
PSLW Powered Support Longwall
QRC Quick Roll Changer
RAPP Rajasthan Atomic Power Plant
RCE Revised Cost Estimates
RCF Railway Coach Factory
ROB Road Over Bridge
ROH Regular Overhauling
RTU Remote Terminal Unit
SAIL Steel Authority of India Ltd.
SCI Shipping Corporation of India Ltd.
SDH Synchronous Digital Hierarchy
SG Steam Generator
SP Self Propelled
ST Steam Turbine
STPS Super Thermal Power Station
SUR Sulphur Recovery Unit
SWSU Sour Water Stripping Unit
TBM Tunnel Boring Machine
TG Turbo Generator
TPA Tonnes Per Annum
TPS Thermal Power Station
TOR Time Overrun
TPY Tonnes per year
UG Under Ground
ULDCS Unified Load Despatch & Communication Scheme
VDU Vacuum Distillation Unit
WHRB Waste Heat Recovery Boiler
WO_DOC With out Date of Commissioning
WO_ODC With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for February 2018 contains information on the status of the 1304 Central Sector Infrastructure Projects costing ₹ 150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 47 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 47 projects, 14 are **Mega** Projects costing ₹ 1000 crore and above.

(ii). Total original cost of implementation of the 1304 projects was Rs. 16,21,994.63 crore and their anticipated completion cost is likely to be Rs. 18,38,702.43 crore, which reflects overall cost overruns of Rs. 2,16,707.80 crore (13.36% of original cost). The expenditure incurred on these projects till February 2018 is Rs. 6,36,212.47 crore, which is 34.60% of the anticipated cost of the projects.

(iii). Out of a total of 1304 projects, 29 projects have reported completion and 33 new projects have been initiated on the monitor of this ministry during the current month. Of these, 14 projects are ahead of schedule, 307 are on schedule, 262 are delayed, 343 projects are showing cost overrun and 100 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 222 if delay is calculated with reference to latest revised schedules of completion. For 721 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 262 delayed projects, 53 projects have overall delay in the range of 1 to 12 months, 55 projects have delay in the range of 13 to 24 months, 83 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above.

(v). Further, out of the 262 delayed projects, 100 projects have cost overruns. Out of these, the cost for 41 projects has been revised and for 59 projects the cost has not yet been revised. Of the 41 projects where cost has been revised, the anticipated cost of 6 projects has again exceeded the revised cost. Out of 262 delayed projects, 122 projects have not provided any milestones and for 32 projects the date of milestone has been lapsed.

(vi). In addition to above there are 244 projects which though on schedule but are having cost overruns. Of these, the cost for 72 projects has since been revised. Of the 72 projects where cost has been revised, the anticipated cost of 29 projects has exceeded even the revised costs. Out of these 244 projects, 151 projects have not provided any milestones and for 1 project the date of milestone has been lapsed

(vii) Out of 1304 projects, 241 projects are facing time overrun of 6 months and more, 249 projects are facing cost overrun of 100 crore and above and 78 projects are facing both time overrun of 6 months and more and cost overrun of 100 crore and above.

3. The implementation status of **Central Sector Mega Projects** (costing Rs.1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1302 projects 388 are mega projects. Total original cost of implementation of these 388 projects was Rs. 12,46,584.61 crore and their anticipated completion cost is likely to be Rs. 14,38,868.91 crore, which reflects overall cost overruns of Rs. 1,92,284.30 crore (15.42% of original cost). The expenditure incurred on these projects till February 2018 is Rs. 5,37,999.41 crore, which is 37.39% of the anticipated cost of the projects. Out of the 388 mega projects, 151 projects have cost overruns with respect to original cost and the number of such projects decreases to 117 when cost overrun is calculated on the basis of revised cost.

(ii) Further, out of the 116 delayed mega projects, 58 projects have cost overruns. Out of these, the cost for 21 projects has been revised and for 37 projects the cost has not yet been revised. Of the 21 projects where cost has been revised, the anticipated cost of 4 projects has again exceeded the revised cost. Out of 116 delayed projects, 56 projects have not provided any milestones and for 19 projects the dates of milestone have been lapsed.

(iii) In addition to above there are 93 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 28 projects has since been revised and for 65 projects cost has not been revised. Of the 28 projects where cost has been revised, the anticipated cost of 11 projects has exceeded even the revised costs. Out of these 93 projects, 53 projects have not provided any milestones for 1 project the dates of milestone have been lapsed.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land

acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.

7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 28.02.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at [www.cspm.gov.in /publication](http://www.cspm.gov.in/publication).

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	522	5
2	RAILWAYS	334	4
3	POWER	121	21
4	PETROLEUM	118	7
5	COAL	92	3
6	URBAN DEVELOPMENT	38	4
7	STEEL	30	0
8	HEALTH AND FAMILY WELFARE	14	0
9	TELECOMMUNICATIONS	9	2
10	SHIPPING AND PORTS	8	0
11	FERTILISERS	5	1
12	ATOMIC ENERGY	4	0
13	MINES	4	0
14	CIVIL AVIATION	2	0
15	DEFENCE PRODUCTION	2	0
16	HEAVY INDUSTRY	1	0
	Total	1304	47

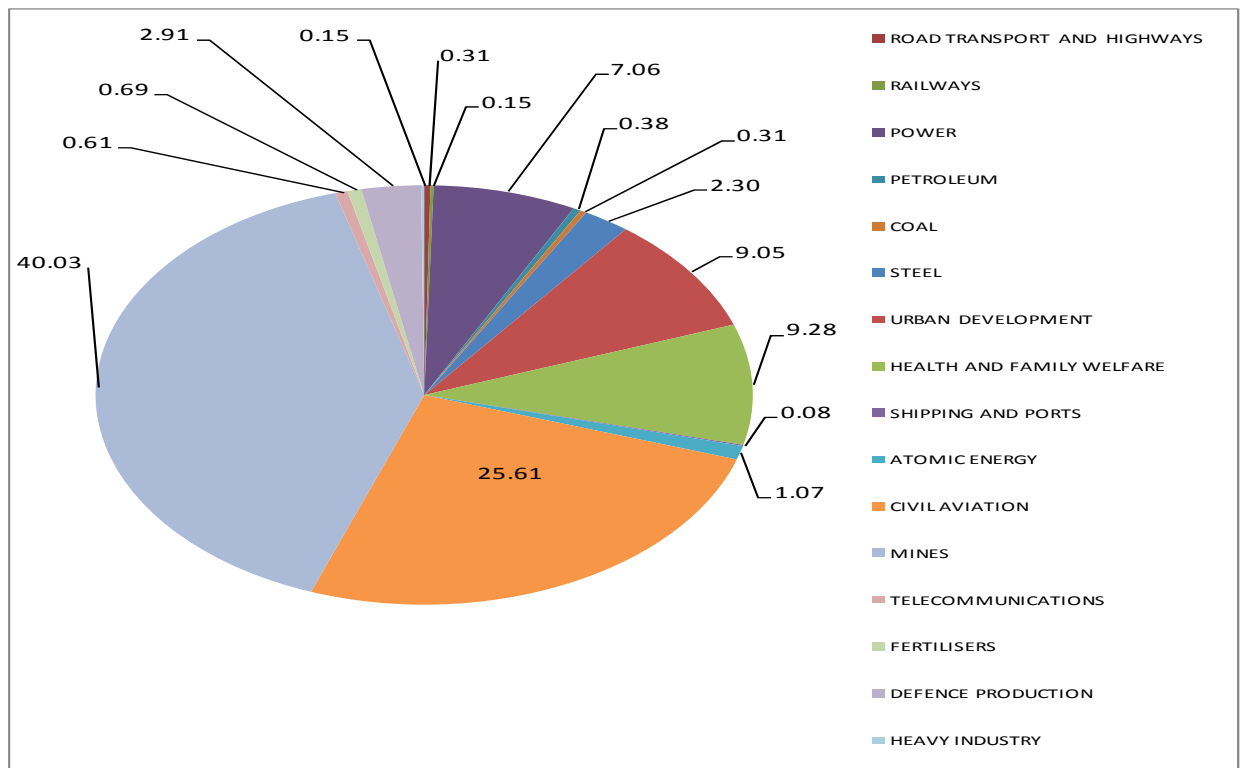


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2017			
	<u>PETROCHEMICALS</u>			
1	ASSAM GAS CRACKER PROJECT (BRAHMAPUTRA CRECKER & POLYMER LTD.) - [N16000106]	5,460.61	04/2012	9,895.05
	<u>POWER</u>			
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000053]	509.66	11/2011	566.26
3	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000081]	1,216.83	08/2012	1,074.89
4	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000101]	1,961.87	05/2014	1,817.05
5	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000117]	1,422.85	01/2015	1,490.42
6	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000145]	1,909.24	06/2015	1,093.03
7	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000163]	303.07	07/2016	48.50
8	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000173]	972.42	11/2017	92.20

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissionin g	Cumulative Expenditure (Rs. crore)
	May,2017			
	<u>CIVIL AVIATION</u>			
9	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000071]	217.60	03/2015	196.94
	June,2017			
	<u>STEEL</u>			
10	SMS-1 CONVERTERS REVAMPING (RASTRIYA ISPAT NIGAM LIMITED) - [N12000090]	404.16	07/2015	394.74
	<u>POWER</u>			
11	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000166]	378.71	10/2016	257.90
12	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000167]	400.47	04/2017	265.20
13	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000211]	187.04	06/2018	54.60
	July,2017			
14	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000094]	752.64	07/2013	633.62
15	WARDHA-HYDERABAD 765 KV LINK (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000183]	3,662.02	05/2018	2,302.40
	August,2017			
16	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000153]	1,575.30	05/2016	1,328.51
	September,2017			
	<u>ATOMIC ENERGY</u>			
17	KUDANKULAM APP (NPCIL) (NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100040]	13,171.00	12/2008	22,340.00
	<u>CIVIL AVIATION</u>			
18	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000069]	335.61	05/2012	305.59
	<u>PETROLEUM</u>			
19	DE-BOTTLENECKING OF SMPL (INDIAN OIL CORPORATION LIMITED) - [N16000089]	1,584.00	03/2017	1,355.45
20	INTEGRATED REFINERY EXPANSION PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000143]	16,504.00	03/2017	15,090.99
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000146]	666.00	11/2015	606.13
22	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000149]	586.00	08/2015	440.20
23	MARKETING TOP AT KORBA (INDIAN OIL CORPORATION LIMITED) - [N16000186]	141.86	09/2016	174.37

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
24	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000205]	1,714.00	06/2017	1,067.89
	<u>POWER</u>			
25	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000112]	2,127.51	07/2014	2,582.69
26	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000125]	9,569.76	06/2015	7,311.17
27	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000191]	3,984.03	01/2013	3,290.44
	October,2017			
	<u>COAL</u>			
28	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU (NEYVELI LIGNITE CORPORATION) - [N06000110]	364.75	10/2014	333.05
	<u>STEEL</u>			
29	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS (RASTRIYA ISPAT NIGAM LIMITED) - [N12000089]	877.73	07/2015	747.81
30	TURBO BLOWER - 5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000092]	280.00	09/2016	157.09
	<u>PETROLEUM</u>			
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000180]	163.88	07/2016	82.45
32	50 MW 10 PERSENT WIND ENERGY POWER PROJECT Central Sector Projects(OIL INDIA LIMITED) - [N16000208]	500.00	03/2017	368.24
33	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) (INDIAN OIL CORPORATION LIMITED) - [N16000217]	150.00	07/2014	251.90
	<u>RAILWAYS</u>			
34	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR (SOUTH WESTERN RAILWAY) - [220100183]	295.00	-	1,509.88
35	GURIYA-MARWAR AND KARJODA-PALANPUR (NORTH WESTERN RAILWAY) - [N22000154]	239.73	-	195.42
36	HOSADURGA - CHICKJAJUR (28.89 KM) (SOUTH WESTERN RAILWAY) - [N22000324]	203.40	-	282.69
	<u>URBAN DEVELOPMENT</u>			
37	BANGALORE METRO RAIL PROJECT (METROPOLITAN RAPID TRANSPORT PROJECTS) - [N28000008]	6,395.00	06/2011	14,200.11
38	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000074]	315.00	06/2015	302.82
39	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000077]	405.01	12/2014	349.54
	November,2017			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2017-2018

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissionin g	Cumulative Expenditure (Rs. crore)
	<u>MINES</u>			
40	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra Private(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000008]	355.13	11/2016	355.13
41	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT RAJASTHAN PPP (ANNUITY)(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [N10000009]	344.50	11/2016	344.50
	<u>POWER</u>			
42	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000186]	550.06	03/2018	470.07
43	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000207]	244.19	07/2018	123.33
	December,2017			
	<u>COAL</u>			
44	PURNADIH OCP (3.0 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000085]	210.98	03/2013	206.80
	<u>STEEL</u>			
45	3RD CONVERTER AND 4TH CASTER (RASTRIYA ISPAT NIGAM LIMITED) - [N12000088]	974.76	07/2016	676.93
	<u>HEALTH AND FAMILY WELFARE</u>			
46	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000004]	444.70	12/2015	326.30
47	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000005]	196.70	01/2016	170.00
	January,2018			
	<u>STEEL</u>			
48	REBUILDING OF COB-7 AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000083]	245.67	05/2016	196.21
	<u>POWER</u>			
49	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000159]	908.08	06/2016	741.63
50	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000162]	829.98	08/2016	423.52
51	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000203]	302.49	02/2016	270.77
	<u>SHIPPING AND PORTS</u>			
52	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST (RAIL VIKAS NIGAM LTD.) - [N25000059]	245.67	04/2009	350.68
53	ACQUISITION OF SECONDHAND/ RESALE OF VLGC (SHIPPING CRP. OF INDIA) - [N25000071]	215.00	09/2017	0.01

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissionin g	Cumulative Expenditure (Rs. crore)
	February,2018			
	<u>PETROLEUM</u>			
54	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000136]	600.17	12/2014	707.33
55	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY Central Sector Projects(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000218]	367.11	04/2017	251.63
56	PALAKKAD LPG PLANT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000225]	184.00	12/2017	100.20
	<u>POWER</u>			
57	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000116]	1,746.65	08/2014	1,977.30
58	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000119]	368.72	07/2006	1,341.24
	<u>RAILWAYS</u>			
59	KANPUR KASGANJ MATHURA(GC) NER (NORTH EASTERN RAILWAY) - [220100197]	677.97	-	1,781.64
60	RAJATGARH-BARANG(LD),ECOR (RAIL VIKAS NIGAM LTD.) - [220100286]	166.16	02/2009	371.62
61	RAICHUR-GUNTAKAL(DL)(SCR) (RAIL VIKAS NIGAM LTD.) - [220100329]	136.62	12/2007	379.62
62	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000082]	170.00	03/2011	440.72
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) (SOUTH WESTERN RAILWAY) - [N22000107]	482.00	03/2013	992.61
64	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) (NORTH WESTERN RAILWAY) - [N22000114]	516.23	03/2014	694.13
65	KATAKHAL TO BHAIRABI (NORTH EAST FRONTIER RAILWAY) - [N22000126]	227.90	12/2012	426.94
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT (NORTH EAST FRONTIER RAILWAY) - [N22000127]	1,676.31	03/2009	7,241.49
67	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) (NORTH WESTERN RAILWAY) - [N22000153]	739.65	-	796.25
68	TAMLUK-BASULYA-SUTAHATA DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000163]	171.02	06/2013	241.76
69	PEN ROHA DOUBLING (CENTRAL RAILWAYS) - [N22000254]	98.74	-	366.50
70	PANVEL PEN DOUBLING (CENTRAL RAILWAYS) - [N22000255]	96.16	-	274.54
71	JHARSUGUDA-RENGALI DOUBLING (EAST COAST RAILWAY) - [N22000317]	201.00	-	243.26
72	ROHTAK - BHIWANI DOUBLING (NORTH WESTERN RAILWAY) - [N22000331]	400.00	-	0.10
73	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) (NORTH EASTERN RAILWAY) - [N22000345]	836.26	-	1,026.65
74	DUDHNOI-MENDHIPATHAR (NORTH EAST FRONTIER RAILWAY) - [N22000378]	315.64	-	313.45
75	HARMUTI-NAHARLAGUN (NORTH EAST FRONTIER RAILWAY) - [N22000382]	614.54	-	564.68

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissionin g	Cumulative Expenditure (Rs. crore)
76	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000385]	971.22	-	834.11
77	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS (NORTH EAST FRONTIER RAILWAY) - [N22000386]	4,300.00	-	4,465.80
78	NEW GUWAHATI-DIGARU-PATCH DOUBLING (NORTH EAST FRONTIER RAILWAY) - [N22000387]	180.09	-	157.12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
79	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000144]	852.00	03/2013	913.37
80	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000343]	341.61	09/2017	319.04
	<u>SHIPPING AND PORTS</u>			
81	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER Central Sector Projects(SHIPPING CRP. OF INDIA) - [N25000069]	193.00	04/2017	193.00
	<u>URBAN DEVELOPMENT</u>			
82	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000059]	188.87	12/2015	193.29

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2018			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000123]	940.00	07/2012	1,415.36
2	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000153]	359.00	09/2013	2.74
3	BHUBANESWAR TO PURI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000195]	500.29	08/2013	869.91
4	4-LANING OF RAIGANJ-DALKOLA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000204]	580.43	08/2013	226.67
5	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000225]	828.00	09/2014	870.15
6	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000366]	996.37	12/2017	0.00
7	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000588]	725.95	06/2019	0.00
	September,2018			
	<u>POWER</u>			
8	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [180100261]	358.42	12/2008	0.00
9	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000099]	1,585.12	11/2013	1,452.46
10	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000114]	552.44	02/2014	501.60
11	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000170]	188.75	02/2017	0.00
12	PATAN WIND FARM SITE, GUJARAT 50 MW (THDC INDIA LIMITED) - [N18000204]	315.00	10/2016	311.96
13	KANDORNA AND BHANWAD WIND FARM (THDC INDIA LIMITED) - [N18000234]	415.49	03/2017	415.50
	October,2018			
14	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM CUDDALORE AREA – PACKAGE A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000259]	955.00	12/2015	74.00
15	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000260]	2,525.00	11/2017	564.00
	February,2018			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	BARSAT-KRISHNANAGAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000229]	867.00	02/2015	278.17

Month wise List of Deleted Projects Costing Rs. 150 Crore and above during				
2017-2018				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
17	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000673]	985.41	03/2020	0.10
18	TWO LANE WITH PS OF KARAIKUDI-RAMANATHPURAM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000698]	652.55	08/2017	0.10


Summary of projects in the Flash Report for the month of February, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1304
Number of Projects completed/dropped/frozen in Current Month	32
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	33
Number of Projects in Current Month	1304

Brief Analysis

Project Status with respect to Original Schedule: Out of 1304 projects, 14 projects are ahead of schedule, 307 projects are on schedule 262 projects are delayed. 581 projects do not have fixed dates of commissioning. 140 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

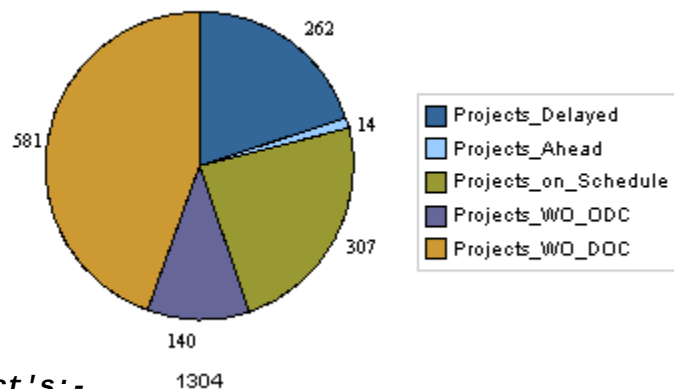

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1304 projects when sanctioned, was of the order of Rs. 1621994.63 crore but this was subsequently revised to Rs. 1838702.43 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till February, 2018 is Rs. 636212.47 crore, which is 34.6% of the anticipated cost of the projects.

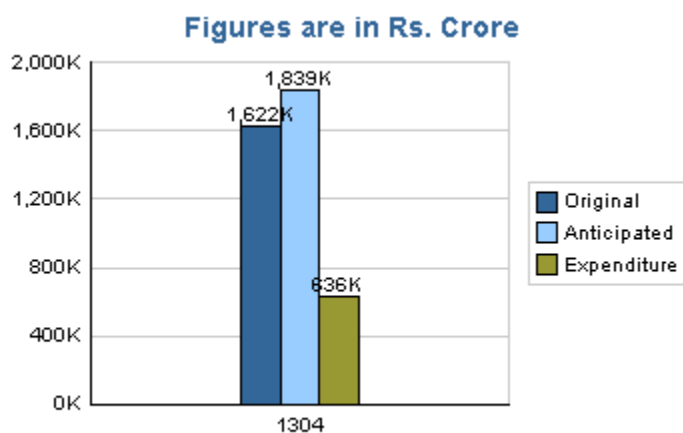


TABLE-4**Projects Added / Completed / Dropped / Frozen Rs. 150****Crore and above**

No of Projects in Previous Month	1304
No of Projects Completed/Dropped/Frozen in Current Month	32
No of Projects added in Current Month	33
No of Projects in Current Month	1304

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	262 (20.09%)	14 (1.07%)	307 (23.54%)	140 (10.74%)	581 (44.56%)	1304
Latest Approved (Date)	222 (17.02%)	11 (.84%)	354 (27.15%)	135 (10.35%)	582 (44.63%)	1304

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1136	14,11,051.59	15,36,788.27	4,60,645.51	30.00	1,25,736.68	8.90
Project with Revision in Cost	168	2,83,273.95	3,01,914.16	1,75,566.96	58.20	18,640.21	6.60
Total	1,304	16,94,325.54	18,38,702.43	6,36,212.47	34.60	1,44,376.89	8.52
Original Cost of All Projects							
Original Cost	1,304	16,21,994.63	18,38,702.43	6,36,212.47	34.60	2,16,707.80	13.36

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	262	6,01,037.76	7,36,994.63	4,04,760.35	54.90	1,35,956.87	22.60
Latest Approved (RCE)	222	4,37,094.24	5,08,769.38	2,56,085.93	50.30	71,675.14	16.40

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	47	64,542.12	84,353.84	50,120.21	59.40	19,811.72	30.70
Total	47	64,542.12	84,353.84	50,120.21	59.42	19,811.72	30.70

TABLE-5

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	89,695.08	89,199.09	-0.55	9	19,751.90	21,090.72	6.78
4	FERTILISERS	5	1,355.20	1,366.85	0.86	1	197.79	209.44	5.89
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	30	54,971.33	55,185.01	0.39	5	1,639.71	2,211.39	34.86
7	PETROLEUM	118	2,03,764.02	2,05,332.56	0.77	17	24,600.91	31,035.49	26.16
8	POWER	121	3,37,506.49	4,04,972.96	19.99	48	1,80,865.02	2,48,331.49	37.30
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	334	3,41,263.79	4,61,201.56	35.15	203	1,24,325.95	3,04,734.19	145.11
12	ROAD TRANSPORT AND HIGHWAYS	522	3,48,802.18	3,54,959.79	1.77	42	24,613.28	31,456.93	27.80
13	SHIPPING AND PORTS	8	4,472.08	4,933.09	10.31	4	959.83	1,762.94	83.67
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	38	1,42,480.14	1,47,511.23	3.53	6	17,021.00	22,244.19	30.69
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	2	453.64	469.04	3.39
Total		1304	16,21,994.63	18,38,702.43	13.36	343	4,13,766.00	6,99,323.36	69.01

[^]- Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above									
(All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun ^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	61	97,970.05	1,01,733.70	3.84	8	6,440.94	11,230.74	74.36
2	ARUNACHAL PRADESH	31	16,602.41	34,492.69	107.76	6	9,755.78	27,646.06	183.38
3	ASSAM	44	26,450.20	36,075.50	36.39	14	9,855.89	19,638.74	99.26
4	BIHAR	81	69,841.31	86,662.38	24.08	21	33,916.51	51,033.53	50.47
5	GOA	9	4,043.51	4,058.91	0.38	2	453.64	469.04	3.39
6	GUJARAT	45	39,141.62	42,701.82	9.10	10	6,584.92	11,436.06	73.67
7	HARYANA	21	13,897.14	15,783.37	13.57	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	2	4,966.47	12,898.75	159.72
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	355.99
10	KARNATAKA	41	70,570.56	80,140.31	13.56	17	23,776.18	34,509.71	45.14
11	KERALA	19	21,344.58	27,277.99	27.80	6	2,771.69	8,705.10	214.07
12	MADHYA PRADESH	61	64,127.43	70,184.36	9.45	10	27,629.06	34,669.61	25.48
13	MAHARASHTRA	126	1,79,252.77	1,92,299.71	7.28	30	40,091.42	57,557.16	43.56
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	642.73
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	252.94
18	ODISHA	79	81,238.38	89,983.41	10.76	19	19,508.27	28,269.59	44.91
19	PUNJAB	30	16,014.41	16,020.14	0.04	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	59	44,137.40	45,593.70	3.30	11	4,055.49	5,547.71	36.80
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	65	1,09,383.31	1,25,212.01	14.47	21	27,563.13	44,494.76	61.43
23	TRIPURA	11	4,400.64	9,067.42	106.05	7	2,909.18	7,575.96	160.42
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	18	28,085.24	31,019.93	10.45
25	WEST BENGAL	54	55,657.37	70,146.96	26.03	21	23,044.77	38,132.46	65.47
26	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
27	DELHI	17	52,999.22	53,266.53	0.50	2	1,375.86	1,789.17	30.04
28	CHHATISGARH	38	84,027.14	86,630.08	3.10	5	13,453.90	16,056.84	19.35
29	JHARKHAND	47	47,354.89	51,864.52	9.52	11	23,813.89	28,327.30	18.95
30	UTTARAKHAND	14	17,481.68	34,951.18	99.93	8	13,425.90	30,895.91	130.12
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	36	24,952.57	27,674.71	10.91	11	3,122.03	6,035.26	93.31
33	MULTI STATE	176	2,99,440.21	2,97,340.08	-0.70	67	67,641.86	1,21,423.06	79.51
Total		1304	16,21,994.63	18,38,702.43	13.36	343	4,13,766.00	6,99,323.36	69.01

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

<u>Extent of time overrun in projects with respect to original schedule</u>						Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	89,695.08	89,199.09	-0.55	37	20,254.10	20,473.06	8 - 132
4	FERTILISERS	5	1,355.20	1,366.85	0.86	2	680.64	692.29	4 - 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	30	54,971.33	55,185.01	0.39	15	46,113.39	45,900.79	2 - 72
7	PETROLEUM	118	2,03,764.02	2,05,332.56	0.77	29	53,922.23	56,788.55	1 - 93
8	POWER	121	3,37,506.49	4,04,972.96	19.99	65	2,36,398.29	2,81,055.60	1 - 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	6	1,689.51	1,711.99	6 - 16
11	RAILWAYS	334	3,41,263.79	4,61,201.56	35.15	29	39,411.20	1,10,498.39	12 - 261
12	ROAD TRANSPORT AND HIGHWAYS	522	3,48,802.18	3,54,959.79	1.77	48	35,576.13	38,136.91	2 - 119
13	SHIPPING AND PORTS	8	4,472.08	4,933.09	10.31	2	966.39	927.36	20 - 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	2	13,752.26	25,082.26	9 - 57
15	URBAN DEVELOPMENT	38	1,42,480.14	1,47,511.23	3.53	22	84,839.01	85,558.10	2 - 75
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	-
Total		1304	16,21,994.63	18,38,702.43	13.36	262	6,01,037.76	7,36,994.63	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	97,970.05	1,01,733.70	3.84	8	8,842.84	9,857.72	2 - 144
2	ARUNACHAL PRADESH	31	16,602.41	34,492.69	107.76	3	3,209.82	7,672.72	36 - 99
3	ASSAM	44	26,450.20	36,075.50	36.39	15	10,931.37	19,158.21	8 - 122
4	BIHAR	81	69,841.31	86,662.38	24.08	8	30,145.73	40,128.66	13 - 123
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	45	39,141.62	42,701.82	9.10	7	13,962.41	13,787.38	3 - 84
7	HARYANA	21	13,897.14	15,783.37	13.57	3	2,216.53	3,396.53	6 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	3	6,107.21	10,586.37	15 - 135
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	5	18,029.57	46,260.84	12 - 193
10	KARNATAKA	41	70,570.56	80,140.31	13.56	6	45,760.08	48,314.80	2 - 30
11	KERALA	19	21,344.58	27,277.99	27.80	5	10,696.37	10,803.56	9 - 65
12	MADHYA PRADESH	61	64,127.43	70,184.36	9.45	7	14,248.11	16,045.45	4 - 96
13	MAHARASHTRA	126	1,79,252.77	1,92,299.71	7.28	21	53,086.89	57,762.61	2 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 50
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	4	2,049.11	4,199.11	36 - 60
18	ODISHA	79	81,238.38	89,983.41	10.76	14	25,222.81	27,449.44	5 - 108
19	PUNJAB	30	16,014.41	16,020.14	0.04	4	1,282.24	1,282.24	2 - 16
20	RAJASTHAN	59	44,137.40	45,593.70	3.30	7	15,246.13	15,931.75	6 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	65	1,09,383.31	1,25,212.01	14.47	18	61,959.21	64,714.55	1 - 118
23	TRIPURA	11	4,400.64	9,067.42	106.05	1	813.34	3,451.00	72 - 72
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	7	22,219.45	22,318.63	4 - 61
25	WEST BENGAL	54	55,657.37	70,146.96	26.03	13	24,037.28	26,211.69	6 - 57
26	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
27	DELHI	17	52,999.22	53,266.53	0.50	7	42,999.38	43,372.17	5 - 27
28	CHHATISGARH	38	84,027.14	86,630.08	3.10	9	48,749.52	49,950.40	1 - 72
29	JHARKHAND	47	47,354.89	51,864.52	9.52	18	23,046.78	24,196.39	11 - 166
30	UTTARAKHAND	14	17,481.68	34,951.18	99.93	4	7,241.32	12,303.81	58 - 93
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	36	24,952.57	27,674.71	10.91	13	15,416.24	15,770.36	3 - 132
33	MULTI STATE	176	2,99,440.21	2,97,340.08	-0.70	43	83,162.94	1,16,173.90	3 - 261
Total		1304	16,21,994.63	18,38,702.43	13.36	262	6,01,037.76	7,36,994.63	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21 - 21
3	COAL	92	88,491.95	89,199.09	0.80	35	13,146.07	13,807.08	0 - 132
4	FERTILISERS	5	1,366.85	1,366.85	0.00	0	0.00	0.00	-
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	30	55,352.30	55,185.01	-0.30	14	30,588.39	30,375.79	2 - 72
7	PETROLEUM	118	2,07,134.59	2,05,332.56	-0.87	11	5,606.57	5,700.03	1 - 66
8	POWER	121	3,68,815.14	4,04,972.96	9.80	49	1,34,522.12	1,48,563.80	1 - 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	5	1,325.52	1,348.00	6 - 16
11	RAILWAYS	334	3,72,447.70	4,61,201.56	23.83	33	61,034.99	1,14,376.72	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	522	3,49,376.20	3,54,959.79	1.60	48	35,591.90	38,136.91	2 - 119
13	SHIPPING AND PORTS	8	4,143.58	4,933.09	19.05	2	624.39	927.36	20 - 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	418.26	418.26	9 - 9
15	URBAN DEVELOPMENT	38	1,47,327.55	1,47,511.23	0.12	19	84,616.42	84,946.10	5 - 75
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	-
Total		1304	16,94,325.54	18,38,702.43	8.52	222	4,37,094.24	5,08,769.38	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest schedule RS. 150 Crore and above									
						(All Cost/ Expenditure in Rs. Crore)			
						Projects with cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	92	88,491.95	89,199.09	0.80	7	19,411.53	20,221.55	4.17
4	FERTILISERS	5	1,366.85	1,366.85	0.00	0	0.00	0.00	0.00
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	30	55,352.30	55,185.01	-0.30	3	1,586.97	1,777.68	12.02
7	PETROLEUM	118	2,07,134.59	2,05,332.56	-0.87	9	8,819.93	10,792.59	22.37
8	POWER	121	3,68,815.14	4,04,972.96	9.80	24	1,35,524.30	1,71,682.12	26.68
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	13.31
11	RAILWAYS	334	3,72,447.70	4,61,201.56	23.83	180	1,26,531.94	2,73,569.85	116.21
12	ROAD TRANSPORT AND HIGHWAYS	522	3,49,376.20	3,54,959.79	1.60	32	22,196.30	28,654.53	29.10
13	SHIPPING AND PORTS	8	4,143.58	4,933.09	19.05	4	973.33	1,762.94	81.12
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	38	1,47,327.55	1,47,511.23	0.12	2	1,715.21	2,090.99	21.91
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	2	454.00	469.04	3.31
Total		1304	16,94,325.54	18,38,702.43	8.52	269	3,38,735.48	5,46,798.83	61.42

^ Cost Overrun = Anticipated Cost minus Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	88,491.95	89,199.09	0.80	5	1,777.44	2,541.33	8- 132
4	FERTILISERS	5	1,366.85	1,366.85	0.00	0	0.00	0.00	0- 0
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	30	55,352.30	55,185.01	-0.30	1	343.00	488.40	29- 29
7	PETROLEUM	118	2,07,134.59	2,05,332.56	-0.87	3	1,188.26	1,409.50	17- 20
8	POWER	121	3,68,815.14	4,04,972.96	9.80	12	35,603.38	49,645.06	12- 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	10- 10
11	RAILWAYS	334	3,72,447.70	4,61,201.56	23.83	22	42,408.51	95,152.71	34- 261
12	ROAD TRANSPORT AND HIGHWAYS	522	3,49,376.20	3,54,959.79	1.60	8	4,823.01	7,368.02	2- 112
13	SHIPPING AND PORTS	8	4,143.58	4,933.09	19.05	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	38	1,47,327.55	1,47,511.23	0.12	2	1,715.21	2,090.99	5- 36
16	DEFENCE PRODUCTION	2	454.00	469.04	3.31	0	0.00	0.00	0- 0
Total		1304	16,94,325.54	18,38,702.43	8.52	57	94,385.71	1,66,098.18	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	CIVIL AVIATION	2	624.07	994.86	59.41	1	314.61	441.33	21- 21
3	COAL	92	89,695.08	89,199.09	-0.55	6	1,929.87	3,000.82	8- 132
4	FERTILISERS	5	1,355.20	1,366.85	0.86	1	197.79	209.44	29- 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	30	54,971.33	55,185.01	0.39	1	343.00	488.40	29- 29
7	PETROLEUM	118	2,03,764.02	2,05,332.56	0.77	10	17,529.25	22,114.37	9- 70
8	POWER	121	3,37,506.49	4,04,972.96	19.99	40	1,51,298.08	1,95,955.39	3- 135
9	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	14	3,897.21	3,919.69	0.58	1	168.90	191.38	10- 10
11	RAILWAYS	334	3,41,263.79	4,61,201.56	35.15	23	25,838.95	96,934.69	34- 261
12	ROAD TRANSPORT AND HIGHWAYS	522	3,48,802.18	3,54,959.79	1.77	9	4,961.94	7,523.02	2- 112
13	SHIPPING AND PORTS	8	4,472.08	4,933.09	10.31	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	9	16,959.40	28,189.40	66.22	1	13,334.00	24,664.00	57- 57
15	URBAN DEVELOPMENT	38	1,42,480.14	1,47,511.23	3.53	5	2,421.00	3,186.19	5- 70
16	DEFENCE PRODUCTION	2	453.64	469.04	3.39	0	0.00	0.00	0- 0
Total		1304	16,21,994.63	18,38,702.43	13.36	100	2,22,195.78	3,61,478.49	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-13

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	97,970.05	1,01,733.70	3.84	3	2,127.62	3,500.50	2 - 144
2	ARUNACHAL PRADESH	31	16,602.41	34,492.69	107.76	3	3,209.82	7,672.72	36 - 99
3	ASSAM	44	26,450.20	36,075.50	36.39	8	7,155.58	15,468.68	17 - 122
4	BIHAR	81	69,841.31	86,662.38	24.08	5	27,943.43	37,926.36	13 - 123
5	GOA	9	4,043.51	4,058.91	0.38	0	0.00	0.00	-
6	GUJARAT	45	39,141.62	42,701.82	9.10	1	318.24	321.62	84 - 84
7	HARYANA	21	13,897.14	15,783.37	13.57	1	1,108.00	2,288.00	76 - 76
8	HIMACHAL PRADESH	12	14,659.32	22,591.60	54.11	1	3,919.59	8,398.75	135 - 135
9	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	12 - 193
10	KARNATAKA	41	70,570.56	80,140.31	13.56	3	16,990.93	19,545.65	2 - 14
11	KERALA	19	21,344.58	27,277.99	27.80	1	607.06	714.25	17 - 17
12	MADHYA PRADESH	61	64,127.43	70,184.36	9.45	3	12,585.15	14,382.49	21 - 96
13	MAHARASHTRA	126	1,79,252.77	1,92,299.71	7.28	9	15,706.53	21,470.35	12 - 192
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	7	8,126.79	10,276.79	26.46	1	850.00	3,000.00	60 - 60
18	ODISHA	79	81,238.38	89,983.41	10.76	2	12,715.67	14,942.60	10 - 58
19	PUNJAB	30	16,014.41	16,020.14	0.04	0	0.00	0.00	-
20	RAJASTHAN	59	44,137.40	45,593.70	3.30	3	1,832.95	2,518.57	36 - 63
21	SIKKIM	6	2,537.08	5,585.45	120.15	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	65	1,09,383.31	1,25,212.01	14.47	4	7,898.70	11,756.97	8 - 118
23	TRIPURA	11	4,400.64	9,067.42	106.05	1	813.34	3,451.00	72 - 72
24	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	1.62	1	195.42	294.60	61 - 61
25	WEST BENGAL	54	55,657.37	70,146.96	26.03	4	11,601.45	13,775.87	9 - 57
26	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
27	DELHI	17	52,999.22	53,266.53	0.50	1	1,219.21	1,592.00	5 - 5
28	CHHATISGARH	38	84,027.14	86,630.08	3.10	2	11,998.43	13,199.31	24 - 60
29	JHARKHAND	47	47,354.89	51,864.52	9.52	3	15,528.33	16,677.94	20 - 166
30	UTTARAKHAND	14	17,481.68	34,951.18	99.93	4	7,241.32	12,303.81	58 - 93
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	36	24,952.57	27,674.71	10.91	3	830.76	1,287.76	60 - 132
33	MULTI STATE	176	2,99,440.21	2,97,340.08	-0.70	26	46,866.81	80,042.95	3 - 261
Total		1304	16,21,994.63	18,38,702.43	13.36	100	2,22,195.78	3,61,478.49	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-14

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	128	0
2	ROAD TRANSPORT AND HIGHWAYS	111	3
3	POWER	64	9
4	PETROLEUM	44	1
5	COAL	12	0
6	URBAN DEVELOPMENT	11	0
7	STEEL	9	0
8	ATOMIC ENERGY	4	0
9	TELECOMMUNICATIONS	2	1
10	MINES	1	0
11	HEAVY INDUSTRY	1	0
12	SHIPPING AND PORTS	1	0
	Total	388	14

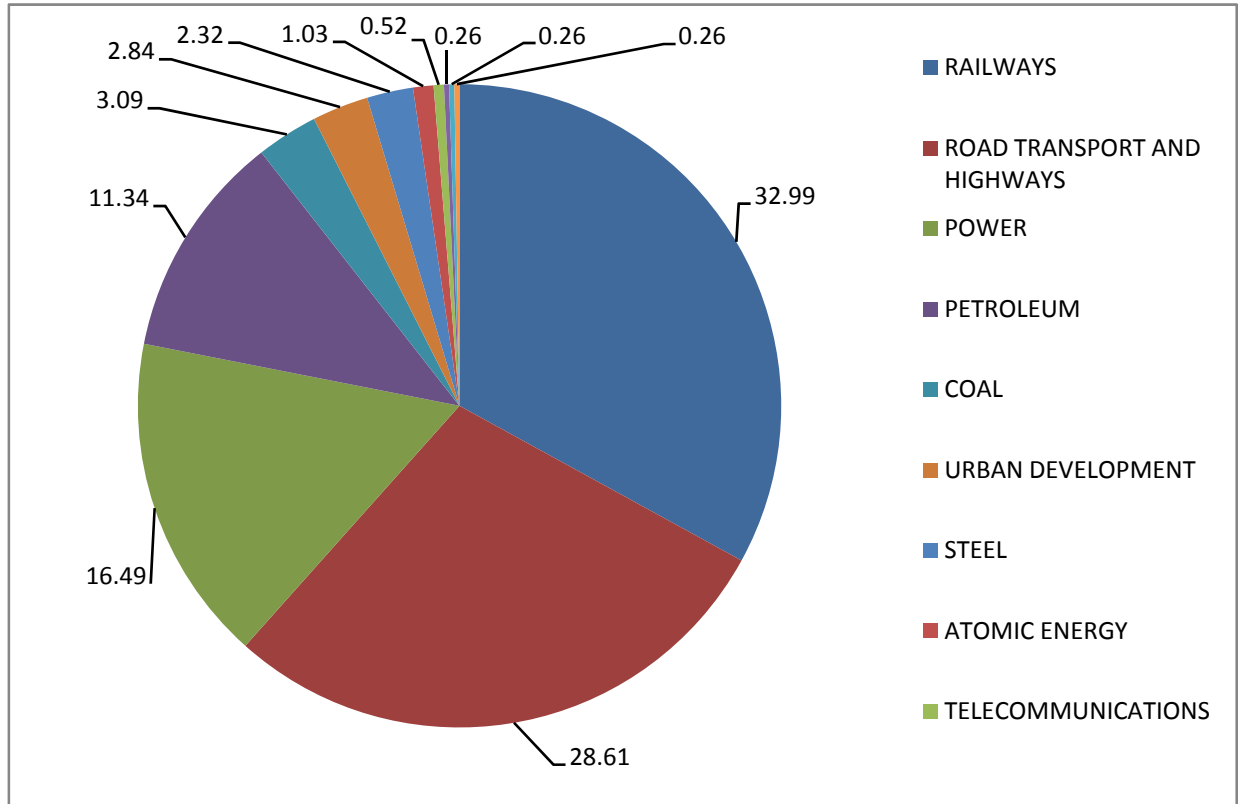


TABLE-15**Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above**

No of Projects in Previous Month	394
No of Projects Completed/Dropped/Frozen in Current Month	7
No of Projects added in Current Month	3
No of Projects in Current Month	388

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	116 (29.90%)	4 (1.03%)	77 (19.85%)	52 (13.40%)	139 (35.82%)	388
Latest Approved (Date)	86 (22.16%)	4 (1.03%)	109 (28.09%)	49 (12.63%)	140 (36.08%)	388

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	321	10,72,216.12	11,79,031.60	3,80,979.25	32.30	1,06,815.48	10.00
Project with Revision in Cost	67	2,43,152.32	2,59,837.31	1,57,020.16	60.40	16,684.99	6.90
Total	388	13,15,368.44	14,38,868.91	5,37,999.41	37.39	1,23,500.47	9.39
Original Cost of All Projects							
Original Cost	388	12,46,584.61	14,38,868.91	5,37,999.41	37.39	1,92,284.30	15.42

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	116	5,45,472.39	6,77,771.01	3,76,114.85	55.50	1,32,298.62	24.30
Latest Approved (RCE)	86	3,83,005.17	4,52,542.33	2,28,792.19	50.60	69,537.16	18.20

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	14	53,630.17	71,761.93	42,125.89	58.70	18,131.76	33.80
Total	14	53,630.17	71,761.93	42,125.89	58.70	18,131.76	33.81

TABLE-16

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs . 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with Cost overrun ^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	74.69
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROLEUM	44	1,72,351.04	1,74,960.45	1.51	9	21,796.28	27,121.31	24.43
6	POWER	64	3,15,636.62	3,81,516.33	20.87	33	1,75,075.10	2,40,954.81	37.63
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,64,554.84	3,62,509.20	37.03	88	88,983.02	2,44,821.75	175.13
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	16,427.80	21,649.27	31.78
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	2	15,819.21	20,650.00	30.54
Total		388	12,46,584.61	14,38,868.91	15.42	151	3,54,651.29	6,08,139.58	71.48

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with cost overrun ^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	4	5,360.88	8,685.95	62.02
2	ARUNACHAL PRADESH	4	10,609.32	28,267.16	166.44	3	9,356.22	27,014.06	188.73
3	ASSAM	7	15,057.54	23,024.26	52.91	3	6,746.70	14,800.00	119.37
4	BIHAR	14	39,632.94	54,365.80	37.17	7	28,983.86	43,716.72	50.83
5	GUJARAT	9	23,124.79	26,192.56	13.27	3	4,165.61	7,233.38	73.65
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	4,966.47	12,898.75	159.72
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	355.99
9	KARNATAKA	18	59,444.23	68,301.46	14.90	10	21,327.46	30,943.69	45.09
10	KERALA	7	16,657.19	22,154.71	33.00	2	1,450.00	6,947.52	379.14
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	9	27,369.66	34,183.04	24.89
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	20	36,453.02	51,807.77	42.12
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	642.73
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	25	57,615.98	65,411.17	13.53	7	16,265.64	24,060.83	47.92
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	37.84
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	10	24,589.22	39,230.47	59.54
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	6	23,760.85	25,525.55	7.43
24	WEST BENGAL	22	43,988.95	56,061.65	27.44	9	19,977.19	32,278.32	61.58
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	5	48,156.73	48,383.52	0.47	1	1,219.21	1,592.00	30.58
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	3	12,976.57	15,042.35	15.92
28	JHARKHAND	11	34,343.41	37,734.40	9.87	4	21,817.59	25,208.58	15.54
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	5	12,949.36	30,054.88	132.10
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	70	2,57,222.41	2,49,268.90	-3.09	28	54,795.85	1,01,422.83	85.09
Total		388	12,46,584.61	14,38,868.91	15.42	151	3,54,651.29	6,08,139.58	71.48

^ Cost Overrun = Anticipated Cost minus Original Cost

TABLE-18

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	4	67,120.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	3	8,192.43	8,192.43	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	7	42,646.34	42,288.34	4 - 59
5	PETROLEUM	44	1,72,351.04	1,74,960.45	1.51	14	47,963.68	50,402.81	5 - 74
6	POWER	64	3,15,636.62	3,81,516.33	20.87	43	2,27,662.95	2,70,733.67	1 - 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
8	RAILWAYS	128	2,64,554.84	3,62,509.20	37.03	24	37,255.36	1,07,979.60	12 - 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	15	21,226.49	23,338.23	2 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	57 - 57
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	5	80,071.14	80,443.93	5 - 29
Total		388	12,46,584.61	14,38,868.91	15.42	116	5,45,472.39	6,77,771.01	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	4	7,142.33	8,011.81	2 - 144
2	ARUNACHAL PRADESH	4	10,609.32	28,267.16	166.44	2	3,070.89	7,517.72	55 - 99
3	ASSAM	7	15,057.54	23,024.26	52.91	3	8,340.50	15,978.89	66 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	13 - 123
5	GUJARAT	9	23,124.79	26,192.56	13.27	1	11,459.00	11,459.00	47 - 47
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	2	5,836.38	10,315.54	15 - 135
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	5	18,029.57	46,260.84	12 - 193
9	KARNATAKA	18	59,444.23	68,301.46	14.90	5	45,051.08	47,605.80	2 - 30
10	KERALA	7	16,657.19	22,154.71	33.00	2	9,770.08	9,770.08	9 - 29
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	3	13,338.65	14,908.82	21 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	14	50,173.15	54,199.74	2 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	65,411.17	13.53	6	22,764.71	24,991.64	10 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	2	13,149.74	13,463.70	48 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	7	55,604.64	59,383.19	9 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	3	20,622.72	20,622.72	4 - 26
24	WEST BENGAL	22	43,988.95	56,061.65	27.44	7	21,657.53	23,809.46	9 - 57
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	5	48,156.73	48,383.52	0.47	3	41,198.73	41,571.52	5 - 25
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	4	47,640.00	48,533.82	1 - 59
28	JHARKHAND	11	34,343.41	37,734.40	9.87	5	18,685.09	19,708.40	11 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	58 - 93
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	11,865.58	11,865.58	3 - 18
31	MULTI STATE	70	2,57,222.41	2,49,268.90	-3.09	23	74,390.59	1,06,006.00	4 - 261
Total		388	12,46,584.61	14,38,868.91	15.42	116	5,45,472.39	6,77,771.01	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-20

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	4	69,305.00	69,728.00	36 - 93
2	COAL	12	56,404.18	56,404.98	0.00	2	2,285.32	2,285.32	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,466.31	48,150.68	-0.65	6	27,121.34	26,763.34	4 - 59
5	PETROLEUM	44	1,76,002.80	1,74,960.45	-0.59	1	1,256.72	1,256.72	66 - 66
6	POWER	64	3,45,800.20	3,81,516.33	10.33	27	1,24,641.71	1,38,241.87	1 - 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	-
8	RAILWAYS	128	2,92,578.24	3,62,509.20	23.90	26	57,097.45	1,10,484.92	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	15	21,226.49	23,338.23	2 - 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	0	0.00	0.00	-
12	URBAN DEVELOPMENT	11	1,39,921.14	1,40,147.93	0.16	5	80,071.14	80,443.93	5 - 29
Total		388	13,15,368.44	14,38,868.91	9.39	86	3,83,005.17	4,52,542.33	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-21

<u>Extent of cost overrun in projects with respect to latest schedule</u> RS. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	7.45
2	COAL	12	56,404.18	56,404.98	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROLEUM	44	1,76,002.80	1,74,960.45	-0.59	4	7,114.67	8,805.84	23.77
6	POWER	64	3,45,800.20	3,81,516.33	10.33	19	1,33,429.87	1,69,146.00	26.77
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
8	RAILWAYS	128	2,92,578.24	3,62,509.20	23.90	74	93,511.48	2,18,882.79	134.07
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	14	16,427.80	21,649.27	31.78
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	11	1,39,921.14	1,40,147.93	0.16	1	1,219.21	1,592.00	30.58
Total		388	13,15,368.44	14,38,868.91	9.39	117	2,90,740.00	4,73,018.34	62.69

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-22

Extent of time & cost overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	69,305.00	69,728.00	0.61	1	5,677.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,466.31	48,150.68	-0.65	0	0.00	0.00	0- 0
5	PETROLEUM	44	1,76,002.80	1,74,960.45	-0.59	0	0.00	0.00	0- 0
6	POWER	64	3,45,800.20	3,81,516.33	10.33	8	34,299.08	47,899.24	12- 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
8	RAILWAYS	128	2,92,578.24	3,62,509.20	23.90	19	41,175.38	93,548.09	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	4	3,974.36	6,086.10	2- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,39,921.14	1,40,147.93	0.16	1	1,219.21	1,592.00	5- 5
Total		388	13,15,368.44	14,38,868.91	9.39	33	86,345.03	1,55,225.43	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-23

Extent of time & cost overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time \$ & cost overruns ^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	69,728.00	3.89	1	3,492.00	6,100.00	93- 93
2	COAL	12	56,404.18	56,404.98	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROLEUM	44	1,72,351.04	1,74,960.45	1.51	5	15,828.24	19,651.12	9- 66
6	POWER	64	3,15,636.62	3,81,516.33	20.87	26	1,46,298.29	1,89,369.01	10- 135
7	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
8	RAILWAYS	128	2,64,554.84	3,62,509.20	37.03	20	24,605.82	95,330.07	34- 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,61,760.00	1,66,981.47	3.23	4	3,974.36	6,086.10	2- 76
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	57- 57
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,147.93	3.46	1	1,219.21	1,592.00	5- 5
Total		388	12,46,584.61	14,38,868.91	15.42	58	2,08,751.92	3,42,792.30	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$ - Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-24

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns \$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	17	83,610.97	86,209.04	3.11	2	1,784.62	3,012.10	2 - 144
2	ARUNACHAL PRADESH	4	10,609.32	28,267.16	166.44	2	3,070.89	7,517.72	55 - 99
3	ASSAM	7	15,057.54	23,024.26	52.91	2	5,875.35	13,600.00	81 - 122
4	BIHAR	14	39,632.94	54,365.80	37.17	3	27,010.57	36,824.93	13 - 123
5	GUJARAT	9	23,124.79	26,192.56	13.27	0	0.00	0.00	-
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	76 - 76
7	HIMACHAL PRADESH	6	12,226.08	20,158.36	64.88	1	3,919.59	8,398.75	135 - 135
8	JAMMU AND KASHMIR	11	28,880.41	57,111.68	97.75	3	7,930.45	36,161.72	12 - 193
9	KARNATAKA	18	59,444.23	68,301.46	14.90	3	16,990.93	19,545.65	2 - 14
10	KERALA	7	16,657.19	22,154.71	33.00	0	0.00	0.00	-
11	MADHYA PRADESH	16	39,844.82	46,658.20	17.10	2	12,325.75	13,895.92	21 - 96
12	MAHARASHTRA	45	1,46,268.44	1,57,645.05	7.78	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	65,411.17	13.53	2	12,715.67	14,942.60	10 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	8	20,933.51	21,247.47	1.50	1	829.74	1,143.70	57 - 57
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	21	91,049.44	1,05,690.69	16.08	3	7,211.42	10,989.97	48 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	31	84,597.70	85,907.82	1.55	0	0.00	0.00	-
24	WEST BENGAL	22	43,988.95	56,061.65	27.44	3	11,432.55	13,584.49	9 - 57
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	5	48,156.73	48,383.52	0.47	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	11	72,931.21	74,996.99	2.83	1	11,846.00	12,739.82	24 - 24
28	JHARKHAND	11	34,343.41	37,734.40	9.87	2	15,266.63	16,289.94	20 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	58 - 93
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	70	2,57,222.41	2,49,268.90	-3.09	13	42,314.44	73,929.85	23 - 261
Total		388	12,46,584.61	14,38,868.91	15.42	58	2,08,751.92	3,42,792.30	

\$- Time Overrun = Anticipated Date of Commissioning minus Original date of Commissioning

TABLE-25

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	04/2012	600.17	12/2014	707.34	02/2018	707.33
2	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY Central Sector Projects	02/2016	367.11	04/2017	367.11	02/2018	251.63
3	PALAKKAD LPG PLANT	02/2015	184.00	12/2017	184.00	02/2018	100.20
	<u>POWER</u>						
4	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	12/2011	1,746.65	08/2014	2,228.71	02/2018	1,977.30
5	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	07/2006	1,329.43	02/2018	1,341.24
	<u>RAILWAYS</u>						
6	RAICHUR-GUNTAKAL(DL)(SCR)	04/2003	136.62	12/2007	380.00	02/2018	379.62
7	KATAKHAL TO BHAIRABI	04/1998	227.90	12/2012	509.00	02/2018	426.94
8	PEN ROHA DOUBLING	04/2007	98.74	N.A.	371.85	02/2018	366.50
9	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	12/2006	170.00	03/2011	465.00	02/2018	440.72
10	KANPUR KASGANJ MATHURA(GC) NER	03/1997	677.97	N.A.	1,679.13	02/2018	1,781.64
11	RAJATGARH-BARANG(LD),ECOR	04/1999	166.16	02/2009	380.00	02/2018	371.62
12	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR)	04/2007	482.00	03/2013	874.57	02/2018	992.61
13	JHARSUGUDA-RENGALI DOUBLING	03/2006	201.00	N.A.	230.00	02/2018	243.26
14	ROHTAK - BHIWANI DOUBLING	05/2015	400.00	N.A.	400.00	02/2018	0.10
15	NEW GUWAHATI-DIGARU-PATCH DOUBLING	04/2007	180.09	N.A.	180.00	02/2018	157.12
16	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	04/2003	4,300.00	N.A.	4,520.00	02/2018	4,465.80
17	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM)	04/2003	971.22	N.A.	966.27	02/2018	834.11
18	HARMUTI-NAHARLAGUN	04/2006	614.54	N.A.	613.00	02/2018	564.68
19	DUDHNOI-MENDHIPATHAR	04/1992	315.64	N.A.	315.00	02/2018	313.45
20	TAMLUK-BASULYA-SUTAHATA DOUBLING	04/2010	171.02	06/2013	250.00	02/2018	241.76
21	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	04/2010	739.65	N.A.	872.22	02/2018	796.25
22	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	04/1997	836.26	N.A.	1,072.52	02/2018	1,026.65
23	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	04/2008	516.23	03/2014	735.00	02/2018	694.13
24	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL	04/1996	1,676.31	03/2009	7,300.00	02/2018	7,241.49

List of projects completed/dropped/Frozen during current month Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	PROJECT						
25	PANVEL PEN DOUBLING	04/2006	96.16	N.A.	277.00	02/2018	274.54
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
26	BARSAT-KRISHNANAGAR PPP (ANNUITY)	08/2012	867.00	02/2015	867.00	02/2018	278.17
27	TWO LANE WITH PS OF KARAUKUDI-RAMANATHPURAM Central Sector Projects	08/2017	652.55	08/2017	652.55	02/2018	0.10
28	SIX LANING AND STRENGTHENING OF KM 340+000 TO KM 403+400 OF HUBLI-HAVERI SECTION OF NH-48 (OLD NH-4)	03/2017	985.41	03/2020	1,200.00	02/2018	0.10
29	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM PPP (BOT)	09/2010	852.00	03/2013	852.00	02/2018	913.37
30	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23	09/2015	341.61	09/2017	341.61	02/2018	319.04
	<u>SHIPPING AND PORTS</u>						
31	ACQUISITION OF SECONDHAND/ RESALE OF SUEZMAX TANKER Central Sector Projects	03/2017	193.00	04/2017	193.00	02/2018	193.00
	<u>URBAN DEVELOPMENT</u>						
32	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	12/2012	188.87	12/2015	208.80	02/2018	193.29

TABLE-25

List of projects added Rs. 150 Crore and above					(February 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>FERTILISERS</u>					
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	215.92	11/2019	215.92	11/2019
2	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	218.83	11/2019	218.83	11/2019
3	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	239.81	11/2019	239.81	11/2019
	<u>PETROLEUM</u>					
4	50MW WIND ENERGY POWER PROJECT	11/2015	500.00	6/2017	500.00	7/2017
5	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	350.00	1/2019	350.00	9/2019
6	KHARAGPUR LPG BOTTLING PLANT	4/2017	163.02	4/2020	163.02	4/2020
7	RE-LIQUIFIED NATURAL GAS	8/2017	421.00	8/2020	421.00	8/2020
8	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	318.80	8/2021	318.80	8/2021
9	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	466.43	10/2020	466.43	10/2020
10	BS-VI PROJECT AT MATHURA REFINERY	1/2018	666.64	9/2019	666.64	9/2019
11	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS & HSD, ADDITIONAL TANKS FOR MS,HSD AND BI	8/2017	236.00	6/2020	236.00	6/2020
12	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	384.58	4/2021	384.58	4/2021
	<u>POWER</u>					
13	TALAIALLI COAL MINING PROJECT	9/2015	3,004.00	11/2019	3,004.00	12/2019
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
14	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	573.70	/	573.70	-
15	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	895.39	/	895.39	-
16	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	273.46	/	273.46	-
17	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	1,155.16	/	1,155.16	-
18	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	960.24	/	960.24	-
19	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	770.73	/	770.73	-
20	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	607.00	/	607.00	-
21	4-LANING FROM KARODI TO TELWADI (KM	1/2018	621.00	/	621.00	-

List of projects added Rs. 150 Crore and above					(February 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	320.104 TO 375.000)					
22	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	953.09	/	953.09	-
23	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	668.86	/	668.86	-
24	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	633.68	/	633.68	-
25	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	614.48	/	614.48	-
26	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	564.66	/	564.66	-
27	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	686.65	/	686.65	-
28	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	1,522.00	/	1,522.00	-
29	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	999.00	/	999.00	-
30	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	503.88	/	503.88	-
31	VARANASI RING ROAD PKG - I	1/2018	450.77	/	450.77	-
	<u>URBAN DEVELOPMENT</u>					
32	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	206.58	3/2019	206.58	3/2019
33	CONSTRUCTION OF CENTRAL EXCISE DEPARTMENT AT CR COLONY	11/2017	348.77	/	348.77	-

TABLE-27

Milestones (Cumulative due & achieved) Rs. 150 Crore and above

Total	3920
Achieved up to month	2146


TABLE-28

List of projects reporting additional delayed Rs . 150 Crore and above							(February 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI SOLAR POWER PROJECT 130 MW NLC	687.28	767.00	06/2017	12/2017	02/2018	2
2	AMLAI OC EXPANSION SECTOR B (1.50 MTY) SECL	198.59	198.59	03/2016	03/2018	03/2019	12
3	MANIKPUR OC EXPANSION (3.5 MTY) SECL	321.50	321.50	03/2014	03/2018	03/2020	24
	<u>FERTILISERS</u>						
4	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. RCF	482.85	482.85	12/2017	03/2018	04/2018	1
	<u>PETROLEUM</u>						
5	TWENTY NOS. FEEDER GAS LINES OIL	228.64	256.41	12/2016	03/2018	05/2018	2
6	PARADIP LPG IMPORT FACILITY IOCL	690.00	690.00	07/2018	08/2020	10/2020	2
7	SIX PIPELINE REPLACEMENT PROJECT ONGC Central Sector Projects	181.02	181.02	01/2017	03/2018	05/2018	2
8	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY CPCL	257.87	257.87	11/2016	03/2018	06/2018	3
9	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	04/2018	07/2018	3
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) ONGC	861.79	1,256.72	05/2013	03/2018	11/2018	8
11	URAN CHAKAN SHIKRAPUR LPG PIPELINE HPCL	309.81	723.40	10/2014	03/2018	02/2019	11
	<u>POWER</u>						
12	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	13,762.80	08/2013	02/2018	03/2018	1
13	SYSTEM STRENGTHENING XII OF SR PGCIL	232.34	341.00	06/2012	02/2018	03/2018	1
14	EASTERN REGION STRENGTHENING SCHEME- III PGCIL	1,272.80	1,731.10	11/2012	02/2018	03/2018	1
15	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C PGCIL	514.20	703.10	06/2015	05/2018	06/2018	1
16	EASTERN REGION STRENGTHENING SCHEME -IX PGCIL	196.58	225.28	02/2016	03/2018	04/2018	1
17	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM PGCIL	162.11	162.11	05/2018	02/2018	03/2018	1
18	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS PGCIL	207.88	207.88	07/2018	02/2018	03/2018	1


List of projects reporting additional delayed Rs . 150 Crore and above							(February 2018)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
19	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) SJVN	330.00	330.00	11/2017	02/2018	03/2018	1
20	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B PGCIL	3,705.61	3,705.61	04/2018	07/2018	09/2018	2
21	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	5,071.94	10/2012	09/2018	12/2018	3
22	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,932.88	12/2012	03/2018	06/2018	3
23	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	550.18	11/2016	03/2018	06/2018	3
24	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID PGCIL	288.49	376.09	02/2017	03/2018	06/2018	3
25	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	10/2017	06/2018	10/2018	4
26	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	2,702.65	09/2014	03/2018	09/2018	6
27	SYTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	09/2018	03/2019	6
28	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH PGCIL	5,151.37	5,151.37	03/2018	09/2018	03/2019	6
29	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B PGCIL	307.18	307.18	11/2017	06/2018	12/2018	6
30	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) PGCIL	305.04	305.04	03/2017	02/2018	09/2018	7
31	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER PGCIL	4,404.57	5,135.01	01/2015	03/2018	11/2018	8
32	RAMMAM-III HEPP (3X40 MW) NTPC	1,381.84	1,381.84	09/2019	03/2021	02/2022	11
	<u>RAILWAYS</u>						
33	MAHARAJGANJ-MASRAKH (NL) - NER NER	218.19	412.05	N.A.	03/2018	04/2018	1
34	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP NER	199.75	227.00	N.A.	03/2018	08/2018	5
35	DAUSA-GANGAPUR CITY(NL),NWR NWR	410.08	795.01	N.A.	08/2018	02/2019	6
36	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP NER	243.78	268.78	N.A.	08/2017	08/2018	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
37	BARSAT-KRISHNANAGAR NHAI PPP (ANNUITY)	867.00	867.00	02/2015	12/2017	02/2018	2

List of projects reporting additional delayed Rs . 150 Crore and above							(February 2018)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
38	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O NHA)	993.16	1,434.00	03/2020	03/2020	05/2020	2
39	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA NHA	831.58	1,177.00	03/2020	03/2020	06/2020	3
40	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHA PPP (BOT)	1,655.01	1,655.01	08/2016	03/2018	02/2019	11
41	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI NHA PPP (ANNUITY)	485.00	485.00	08/2013	12/2017	12/2018	12
	<u>TELECOMMUNICATIONS</u>						
42	GUJARAT ACCESS (LOT 1) BSNL Central Sector Projects	171.54	171.54	05/2018	04/2018	05/2018	1
43	NETWORK FOR SPECTRUM DOT	13,334.00	24,664.00	07/2015	06/2019	04/2020	10
	<u>URBAN DEVELOPMENT</u>						
44	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	321.00	09/2016	03/2018	04/2018	1
45	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA CPWD	241.33	349.33	03/2016	03/2018	04/2018	1
46	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB CPWD	294.00	294.00	04/2019	04/2019	06/2019	2
47	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA CPWD	205.00	170.62	03/2012	03/2018	06/2018	3

Graphical Presentation of All Projects w.r.t. Original Schedule

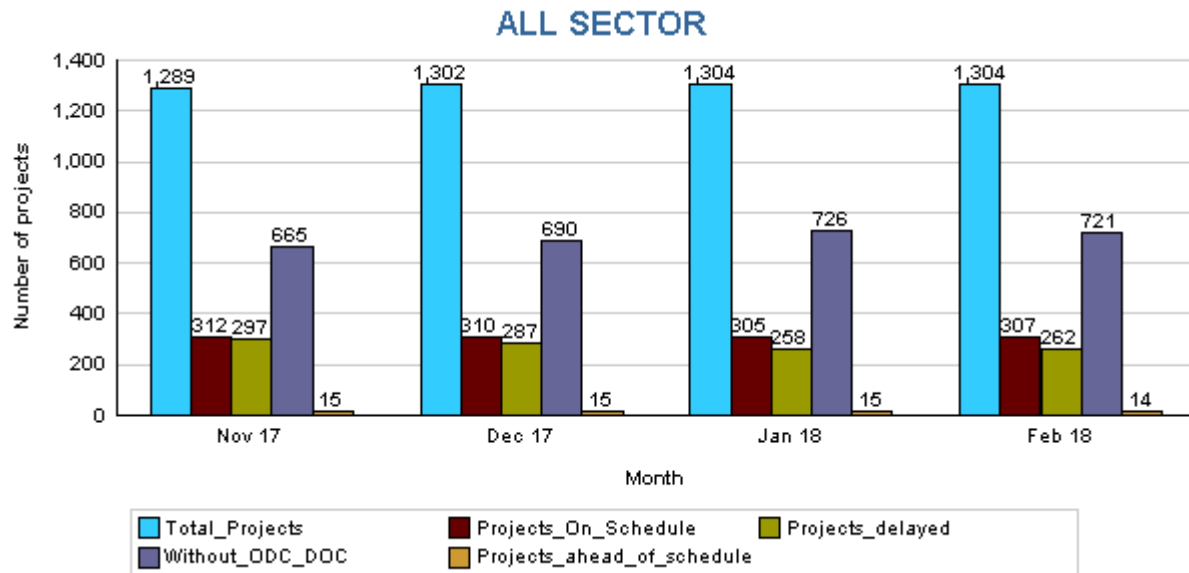


Break-up of 262 Delayed projects in February 2018

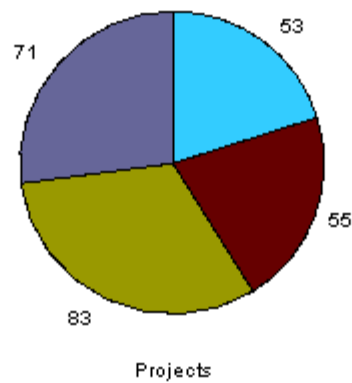


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

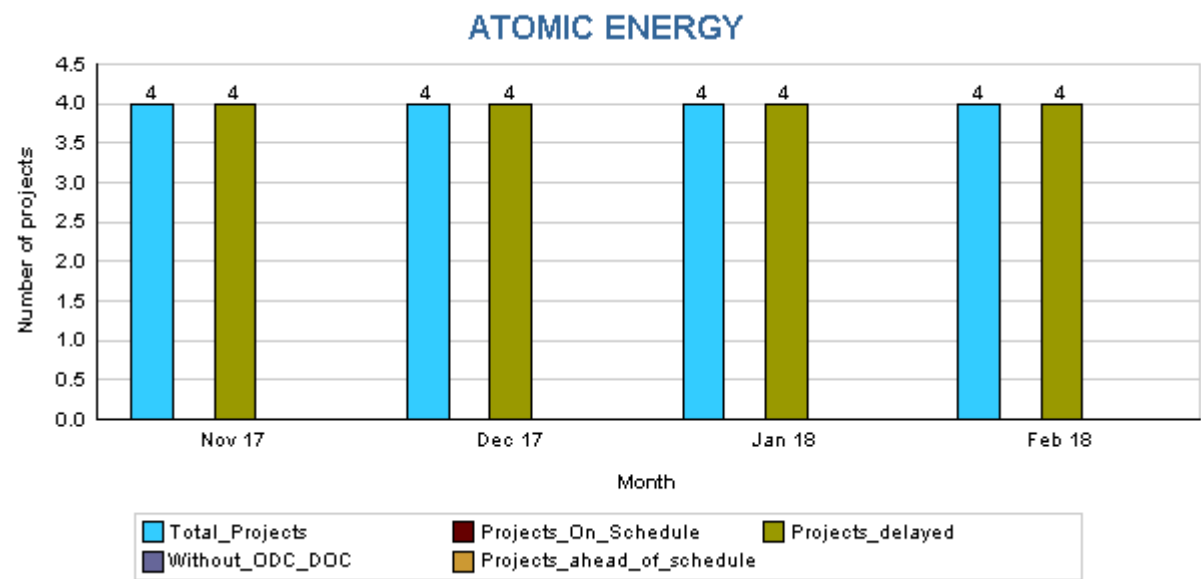


Break-up of 4 Delayed projects in February 2018

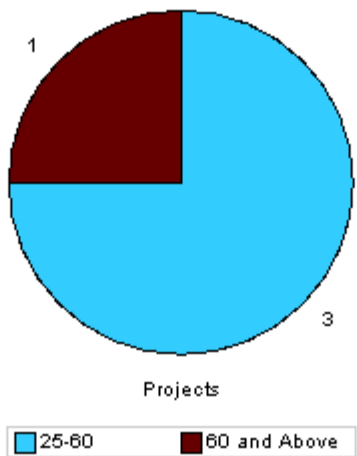


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

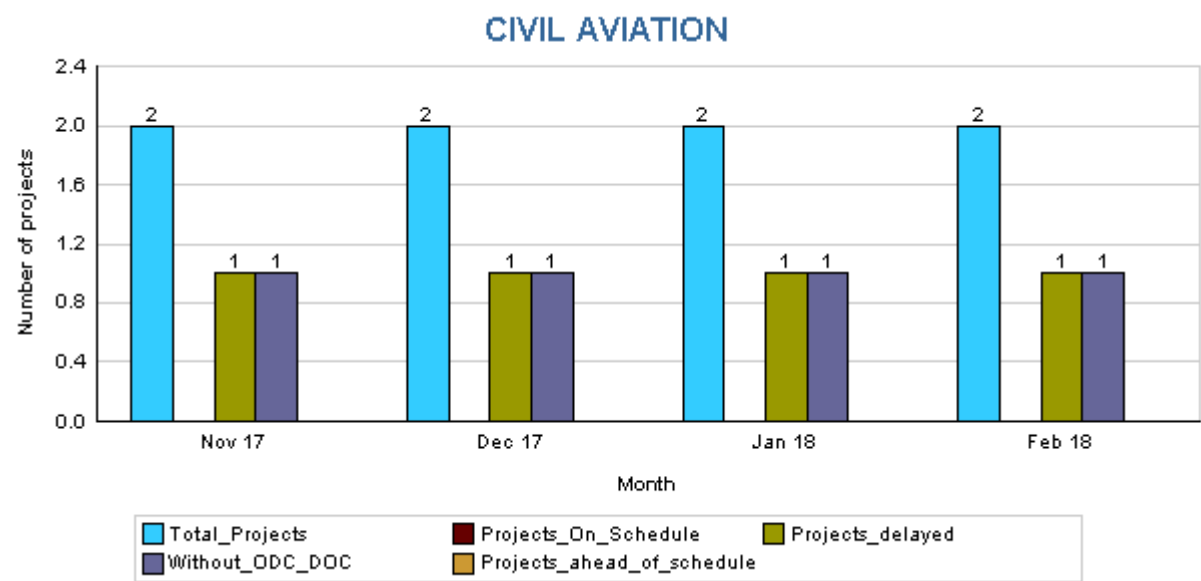


Break-up of 1 Delayed projects in February 2018

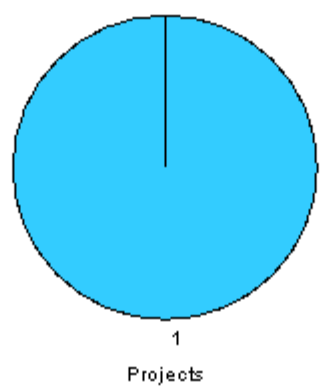


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

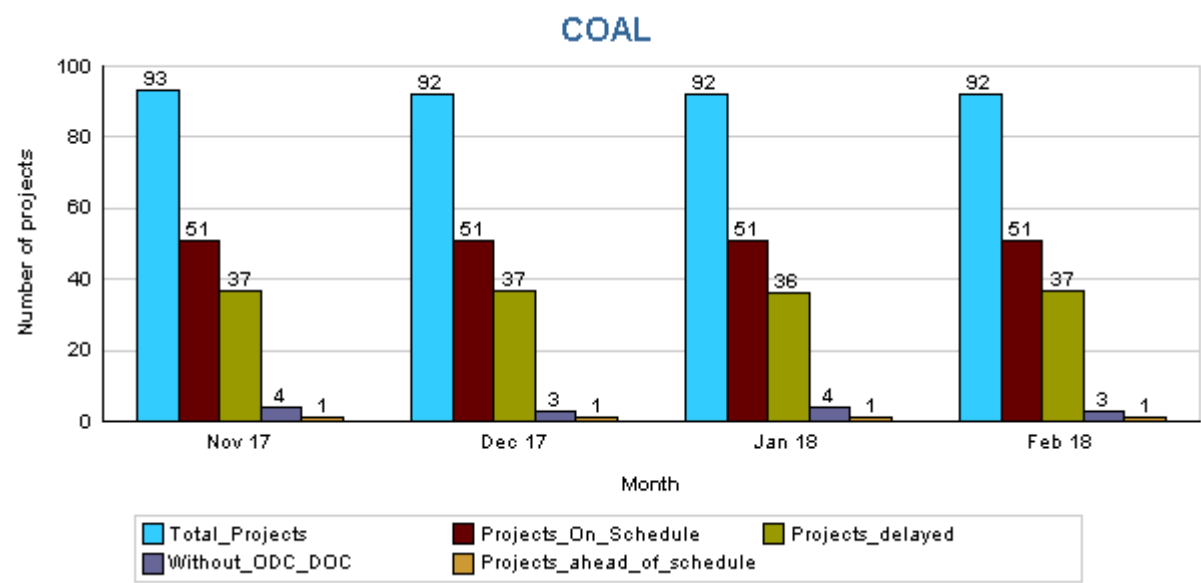


Break-up of 37 Delayed projects in February 2018

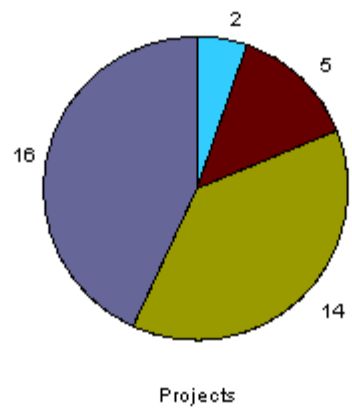


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

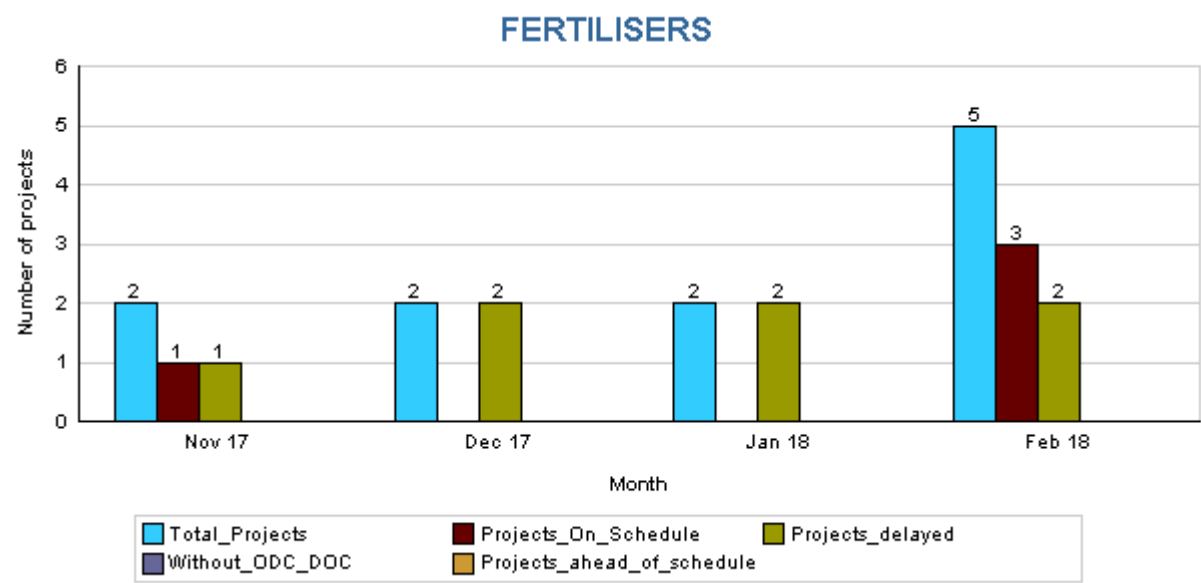


Break-up of 2 Delayed projects in February 2018

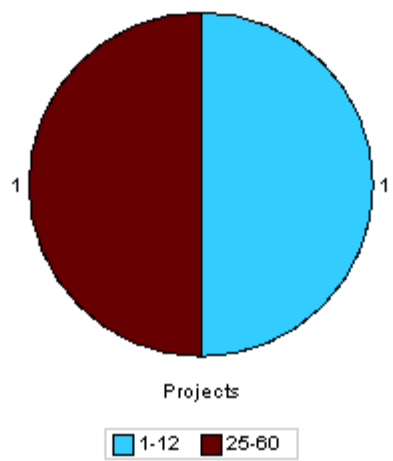


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

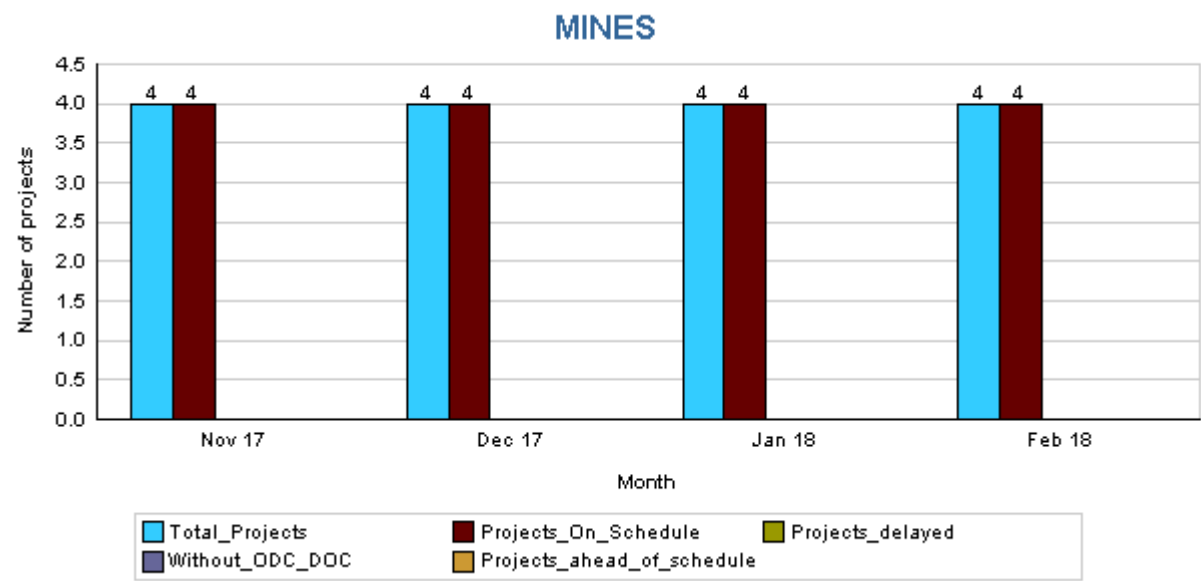


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

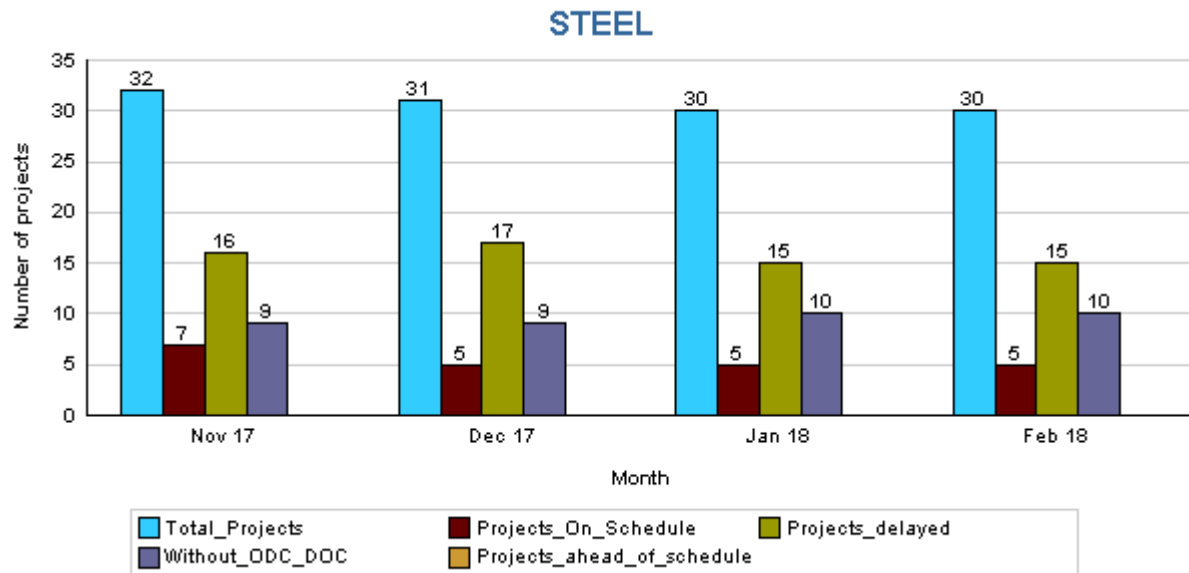


Break-up of 15 Delayed projects in February 2018

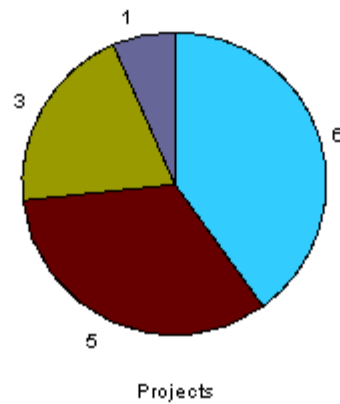


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

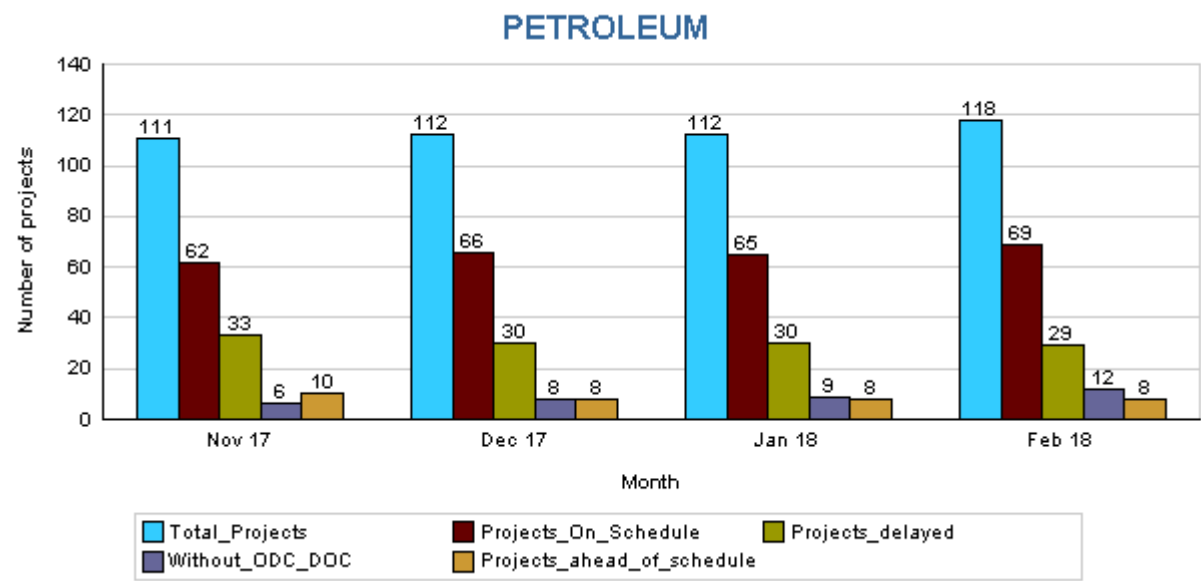


Break-up of 29 Delayed projects in February 2018

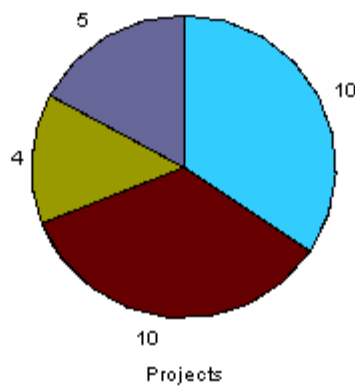


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Original Schedule

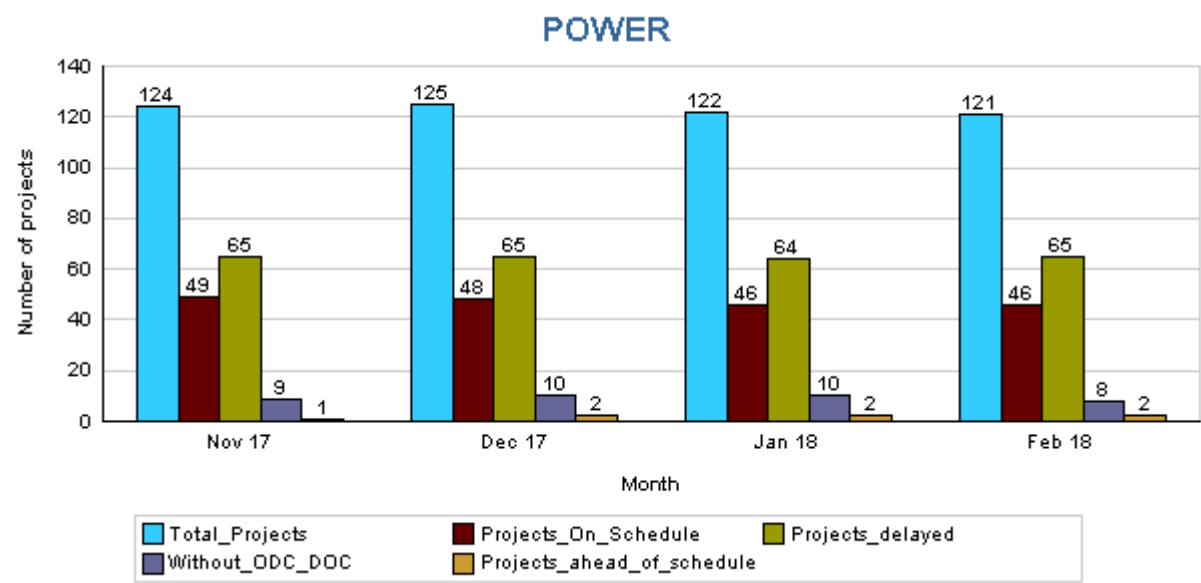


Break-up of 65 Delayed projects in February 2018

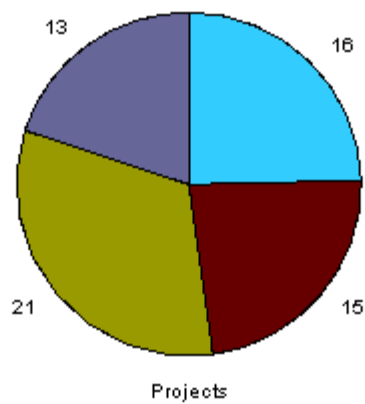

Delay in Months


1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

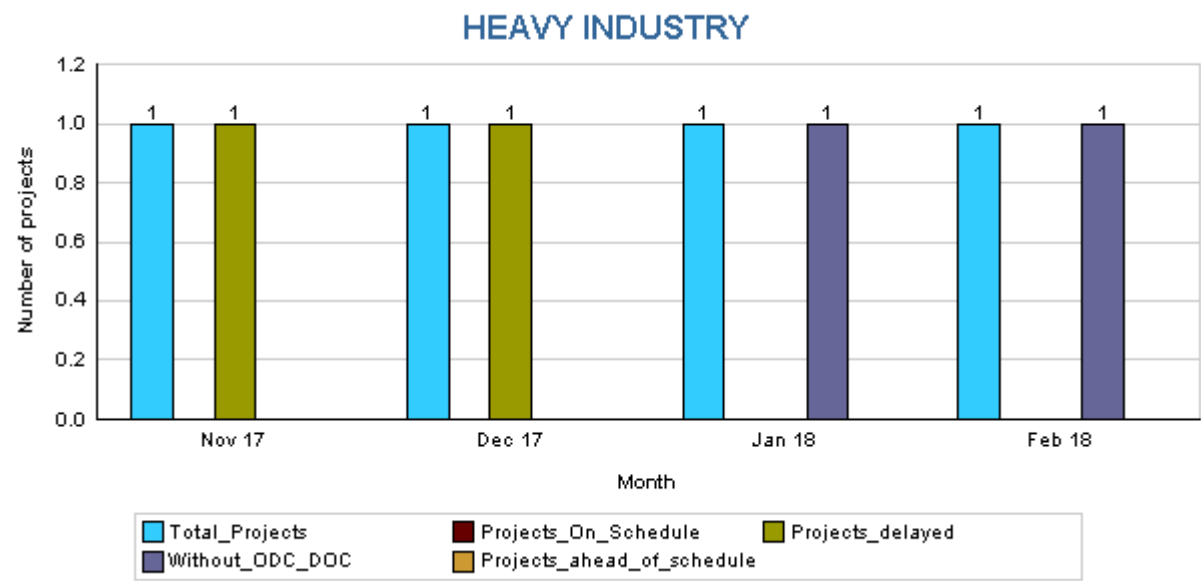


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

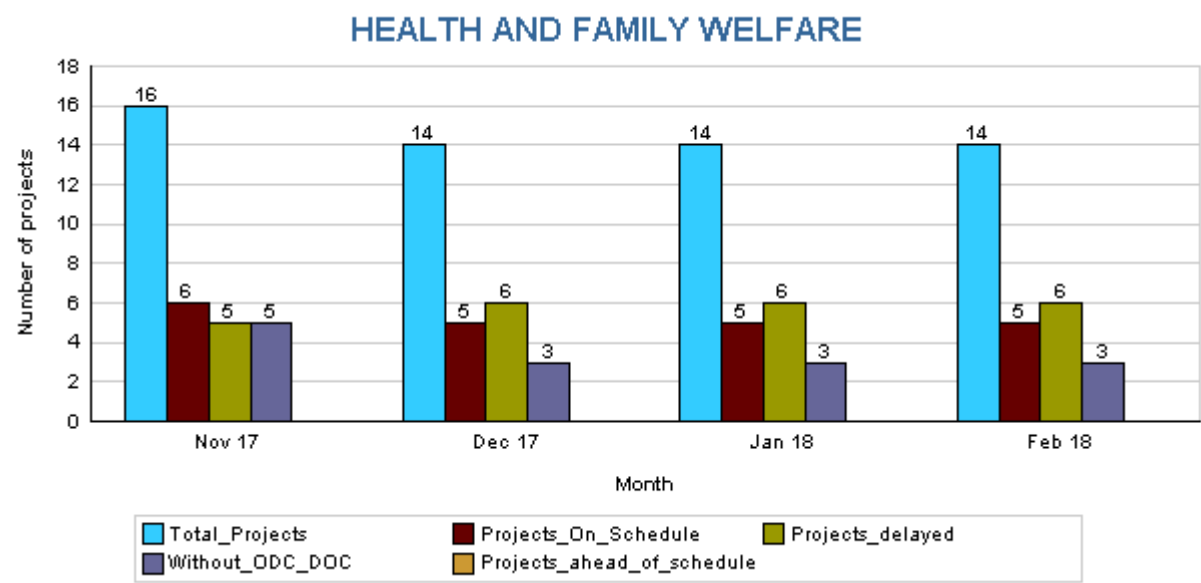


Break-up of 6 Delayed projects in February 2018

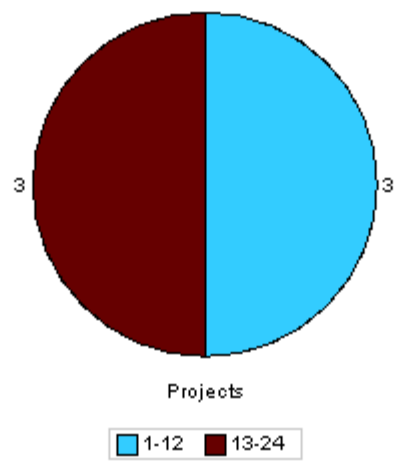


Graphical Presentation of All Projects w.r.t. Original Schedule

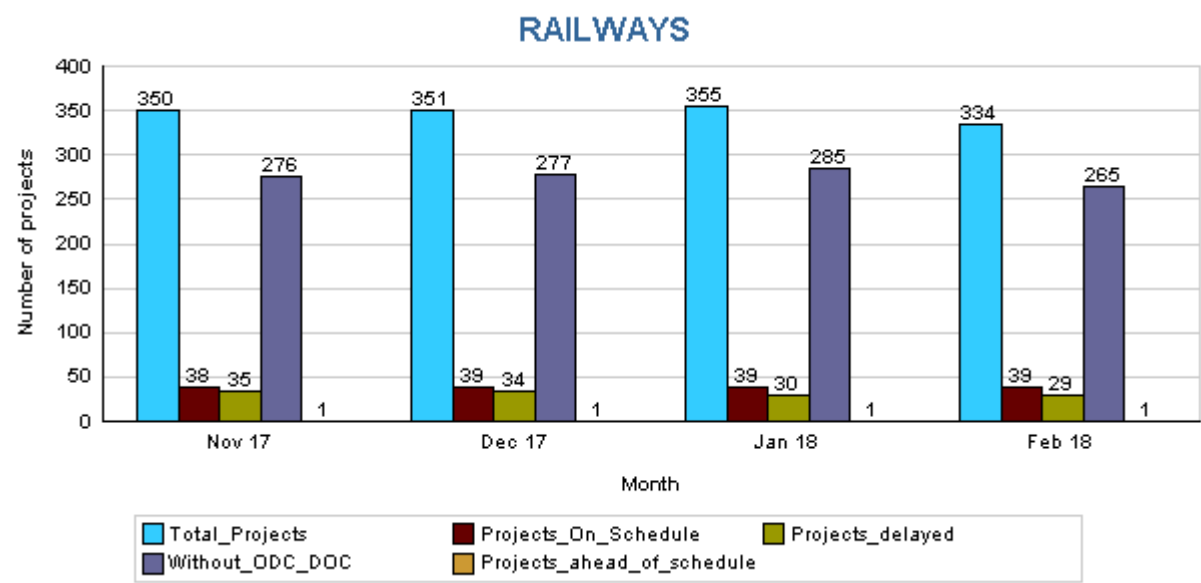


Break-up of 29 Delayed projects in February 2018

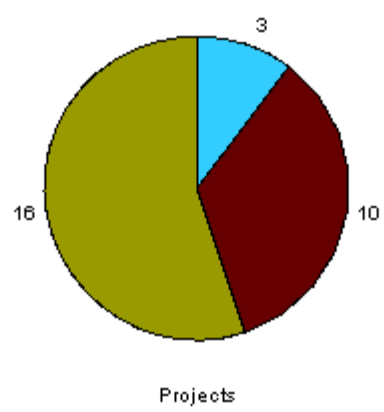


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

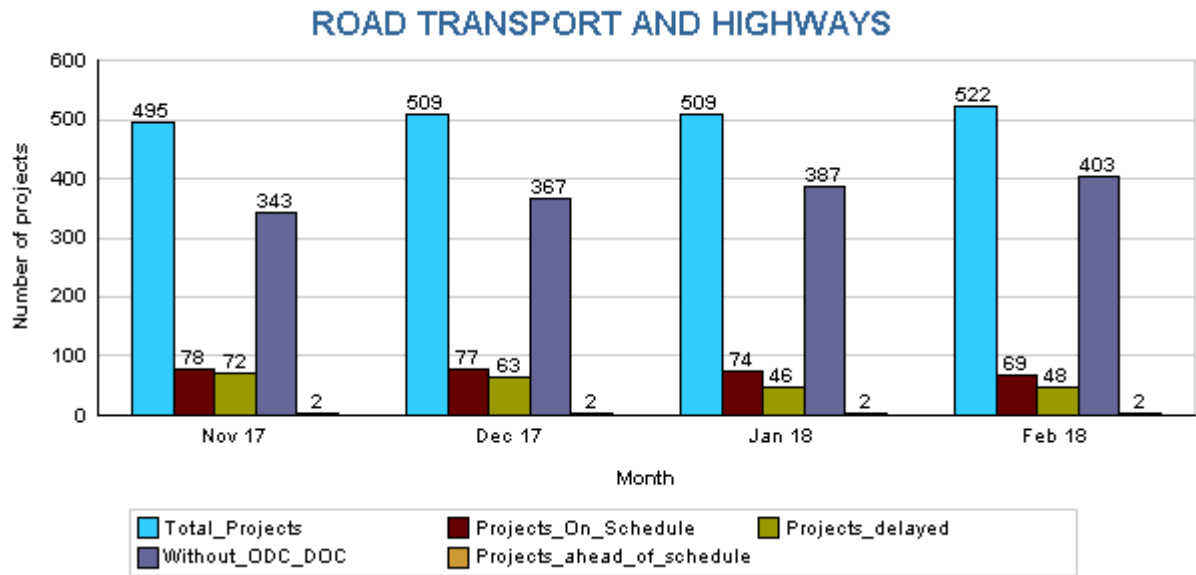


Break-up of 48 Delayed projects in February 2018

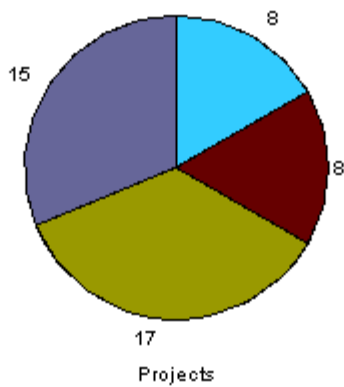


Delay in Months 1-12 13-24 25-60 60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

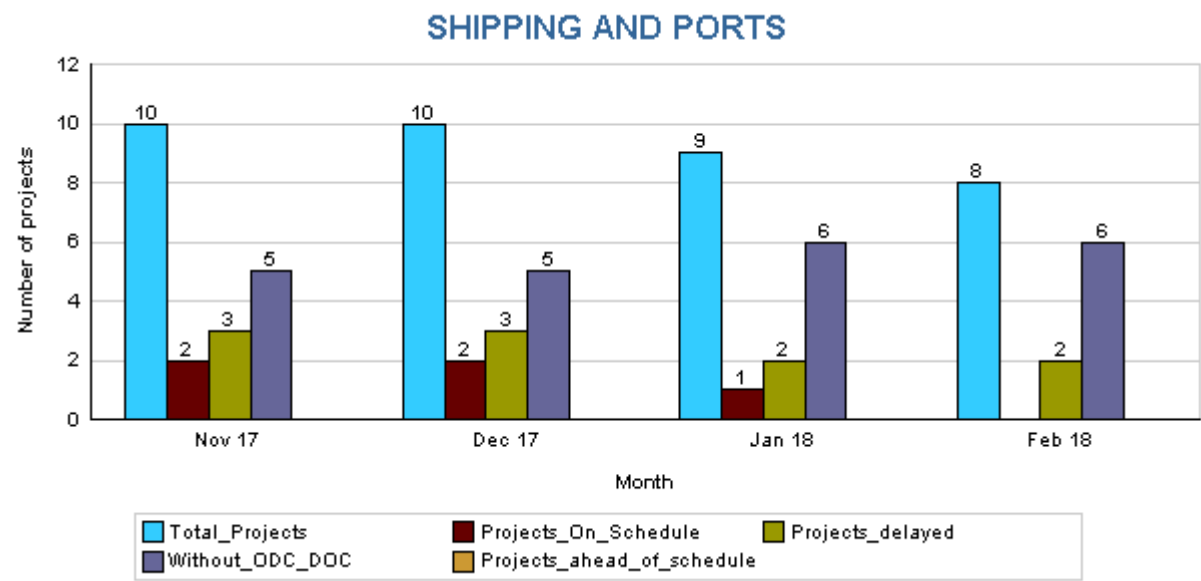


Break-up of 2 Delayed projects in February 2018

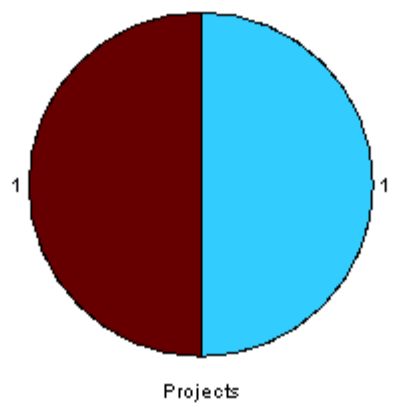


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

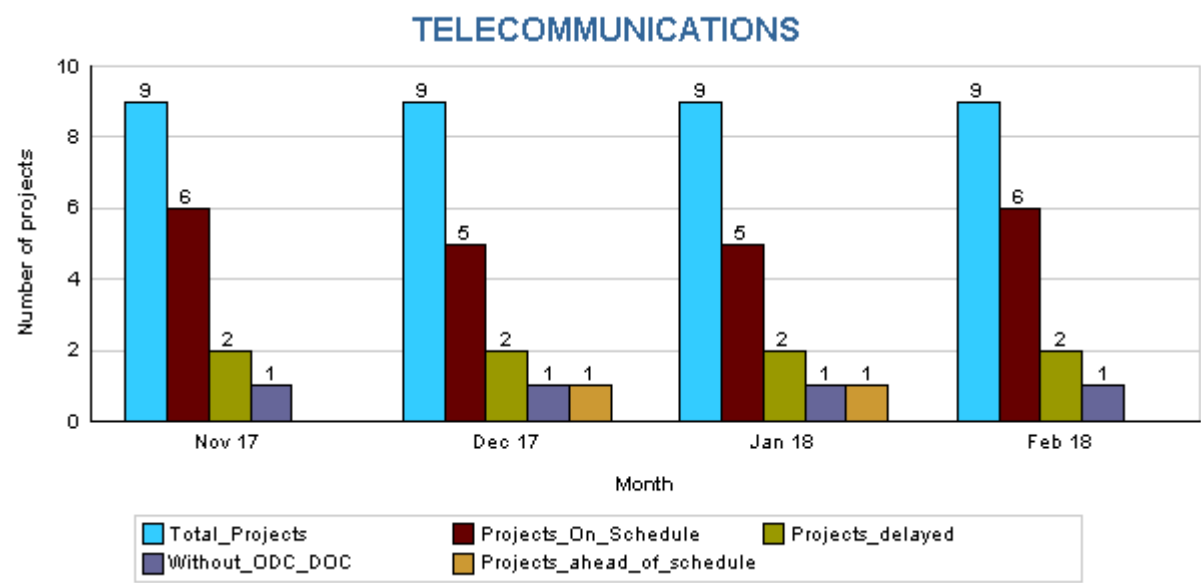


Break-up of 2 Delayed projects in February 2018

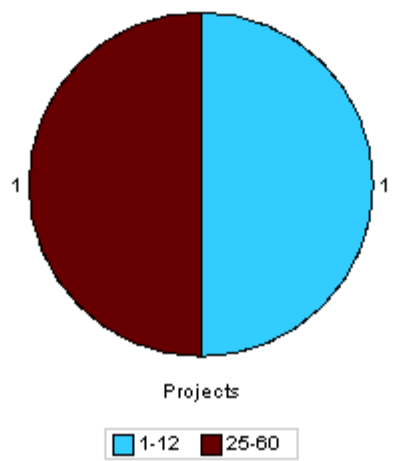


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

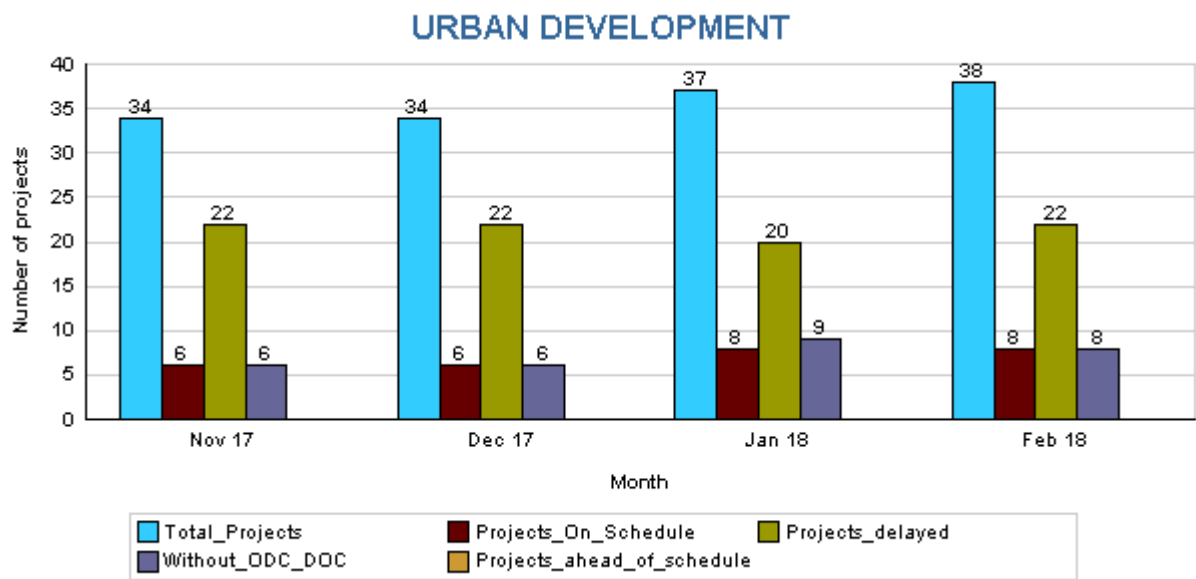


Break-up of 22 Delayed projects in February 2018

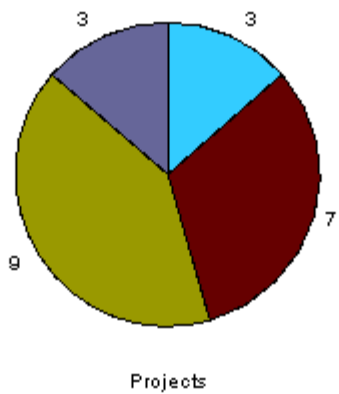

Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

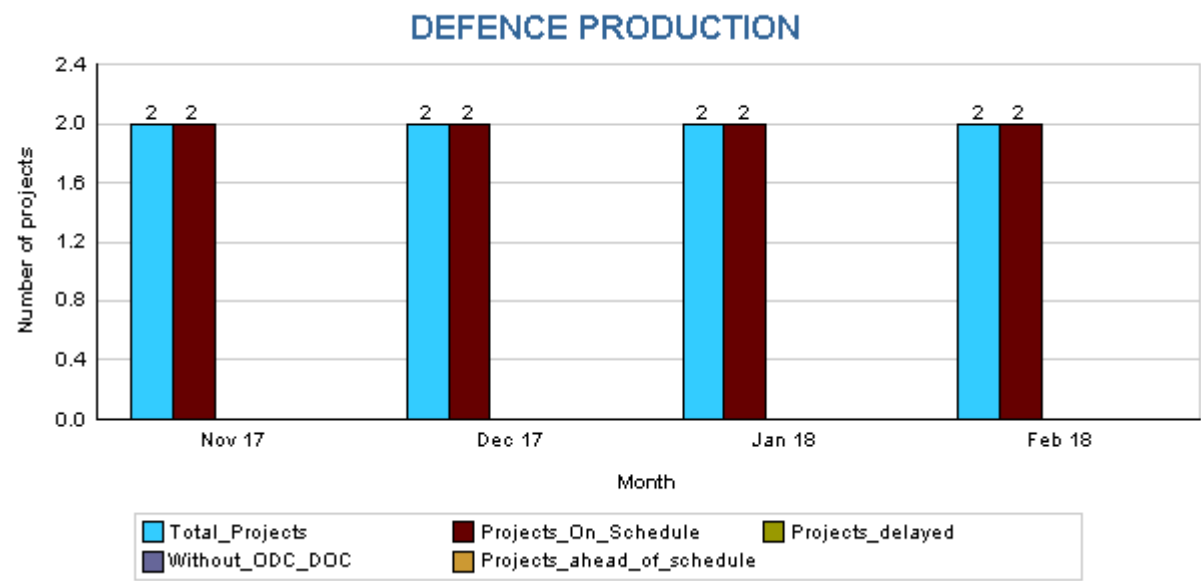

Delay in Months

TABLE-29

<u>Sector wise analysis of projects</u> Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	693,05.00	69,728.00	27,871.79
CIVIL AVIATION	2	624.07	6,24.07	994.86	549.39
COAL	92	89,695.08	884,91.95	89,199.09	22,736.55
FERTILISERS	5	1,355.20	13,66.85	1,366.85	510.95
MINES	4	6,912.00	69,12.00	6,912.00	346.92
STEEL	30	54,971.33	553,52.30	55,185.01	39,907.62
PETROLEUM	118	2,03,764.02	2,071,34.59	2,05,332.56	60,072.60
POWER	121	3,37,506.49	3,688,15.14	4,04,972.96	2,25,943.04
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	14	3,897.21	38,97.21	3,919.69	1,507.40
RAILWAYS	334	3,41,263.79	3,724,47.70	4,61,201.56	1,25,375.67
ROAD TRANSPORT AND HIGHWAYS	522	3,48,802.18	3,493,76.20	3,54,959.79	56,826.05
SHIPPING AND PORTS	8	4,472.08	41,43.58	4,933.09	1,524.70
TELECOMMUNICATIONS	9	16,959.40	169,59.40	28,189.40	8,068.20
URBAN DEVELOPMENT	38	1,42,480.14	1,473,27.55	1,47,511.23	62,587.40
DEFENCE PRODUCTION	2	453.64	4,54.00	469.04	95.19
Grand total	1304	16,21,994.63	16,94,325.54	18,38,702.43	6,36,212.47

TABLE-30

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	11,285.00	12/2015 11/2016	11/2019	47(O) 36(R)	47/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	8,887.00	12/2016 03/2017	12/2020	48(O) 45(R)	35/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,100.00	5,566.79	09/2010 09/2016	06/2018	93(O) 21(R)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT- 3&4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36(O) -	0/0
	Total		67,120.00 -	69,728.00	27,871.79				165/225
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21(O) -	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	522.95	01/2011 09/2017	10/2017	-	0/0
	Total		624.07 -	994.86	549.39				0/0
	<u>COAL</u>								
7	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,634.97	03/2023 -	03/2023	0(O) -	14/17
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,669.22	03/2023 -	03/2023	0(O) -	4/19
9	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023	0(O) -	1/11
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	135.60	03/2015 03/2020	03/2020	60(O) 0(R)	3/8
11	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	1/7
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72(O) -	0/3
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36(O) -	7/8
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2018	24(O) -	4/7
15	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	29.37	03/2022 -	03/2022	0(O) -	2/8
16	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	51.12	03/2020 -	03/2020	0(O) -	3/7
17	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	50.54	03/2018 -	03/2018	0(O) -	1/6
18	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	44.19	03/2020 -	03/2020	0(O) -	0/5
19	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	.99	03/2023 -	03/2023	0(O) -	1/9
20	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/3
21	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	120.77	07/2012 -	03/2021	104(O) -	3/4
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	05/2017	-	6/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108(O) -	2/4
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84(O) -	2/4
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	154.01	03/2012 -	03/2019	84(O) -	3/4
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	347.96	03/2016 -	03/2018	24(O) -	2/4
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60(O) -	3/4
29	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
30	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	273.25	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	182.02	03/2020 -	03/2020	0(O) -	5/5
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	161.38	05/2014 -	04/2018	47(O) -	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	163.95	04/2014 -	04/2018	48(O) -	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	41.80	03/2022 -	03/2022	0(O) -	1/21
37	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 -	486.57	399.01	03/2012 -	03/2018	72(O) -	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 203.82	203.82	77.18	03/2023 03/2021	03/2021	-24(O) 0(R)	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021	0(O) -	2/8
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021	0(O) -	1/7
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	1/6
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	111.56	03/2021 -	03/2021	0(O) -	2/3
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	15.30	03/2022 -	03/2022	0(O) -	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	28.21	03/2021 -	03/2021	0(O) -	0/0
47	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	178.26	03/2020 -	03/2020	0(O) -	7/11
48	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	371.19	03/2020 -	03/2020	0(O) -	2/8
49	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	139.76	03/2021 -	03/2021	0(O) -	9/12

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
50	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018	0(O) -	7/7
51	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	86.03	03/2023 02/2017	03/2023	0(O) 73(R)	7/11
52	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	88.13	03/2019 -	03/2019	0(O) -	10/13
53	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	94.00	03/2020 -	03/2020	0(O) -	5/10
54	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	73.88	03/2021 -	03/2021	0(O) -	2/6
55	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	231.76	03/2025 -	03/2025	0(O) -	3/13
56	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
57	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021	0(O) -	2/6
58	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	46.91	03/2020 -	03/2020	0(O) -	2/6
59	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	39.89	03/2019 -	03/2019	0(O) -	2/9
60	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	126.84	03/2019 -	03/2019	0(O) -	2/8
61	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	237.08	03/2020 -	03/2020	0(O) -	0/0
62	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	.04	03/2022 -	03/2022	0(O) -	0/3
63	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	.13	03/2022 -	03/2022	0(O) -	0/12
64	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	86.78	03/2021 -	03/2021	0(O) -	1/6
65	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	331.07	03/2010 -	03/2018	96(O) -	9/10
66	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	299.61	03/2017 -	05/2018	14(O) -	11/12
67	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	478.12	03/2013 -	11/2018	68(O) -	8/9
68	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	201.18	03/2010 -	03/2019	108(O) -	3/4
69	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	209.07	03/2012 -	03/2019	84(O) -	4/5
70	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	222.60	03/2013 -	03/2019	72(O) -	6/8
71	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	25.64	03/2019 -	03/2019	0(O) -	2/9
72	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026	0(O) -	3/15
73	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	30.12	03/2019 -	03/2019	0(O) -	3/6
74	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	2/5
75	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	371.19	03/2021 -	03/2021	0(O) -	3/9
76	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	6.22	09/2019 -	09/2019	0(O) -	0/0
77	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	168.58	12/2019 -	12/2019	0(O) -	0/0
78	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	5,170.78	12/2015 04/2018	04/2018	28(O) 0(R)	19/35

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
79	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	340.71	06/2015 09/2019	09/2019	51(O) 0(R)	4/7
80	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 -	767.00	749.25	06/2017 12/2017	02/2018	8(O) 2(R)	0/0
81	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	448.86	185.65	03/2012 -	03/2019	84(O) -	32/42
82	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
83	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132(O) -	0/2
84	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36(O) -	29/31
85	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72(O) -	5/6
86	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60(O) -	0/5
87	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60(O) -	4/29
88	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	437.51	-	03/2015 -	03/2021	72(O) -	5/13
89	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33(O) -	27/36
90	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	417.33	114.71	07/2016 -	03/2020	44(O) -	19/28
91	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	149.50	03/2016 -	03/2018	24(O) -	33/39
92	KAKATIYAKHANI OPENCASST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	72.81	03/2019 -	03/2019	0(O) -	6/18
93	KOYAGUDEM OPENCASST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12(O) -	0/9
94	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
95	KHADIA EXPANSION OPENCASST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	434.36	03/2018 -	03/2018	0(O) -	6/10
96	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	1,309.20	11/2021 -	11/2021	0(O) -	0/0
97	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	288.00	03/2022 -	03/2022	0(O) -	7/12
98	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	336.18	03/2018 -	03/2020	24(O) -	9/16
	Total		89,695.08 -	89,199.09	22,736.55				419/901
	<u>FERTILISERS</u>								
99	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	-	11/2019 -	11/2019	0(O) -	0/0
100	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	97.94	11/2016 04/2019	04/2019	29(O) 0(R)	1/13
101	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	413.01	12/2017 04/2018	04/2018	4(O) 0(R)	0/1
102	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	-	11/2019 -	11/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
103	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	-	11/2019 -	11/2019	0(O) -	0/0
	Total		1,355.20 -	1,366.85	510.95				1/14
	<u>MINES</u>								
104	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	44.60	04/2021 04/2021	04/2021	0(O) 0(R)	2/2
105	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	288.44	01/2020 01/2020	01/2020	0(O) 0(R)	1/2
106	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 355.00	355.00	13.88	11/2020 11/2020	11/2020	0(O) 0(R)	1/1
107	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	-	04/2021 04/2021	04/2021	0(O) 0(R)	0/0
	Total		6,912.00 -	6,912.00	346.92				4/5
	<u>STEEL</u>								
108	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	236.32	10/2016 -	03/2019	29(O) -	1/2
109	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
110	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	786.45	12/2017 -	10/2018	10(O) -	2/2
111	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	37.04	08/2018 -	10/2018	2(O) -	1/2
112	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	120.00	07/2018 -	09/2018	2(O) -	0/3
113	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
114	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	18,560.44	03/2013 -	02/2018	59(O) -	35/38
115	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	119.94	04/2015 -	-	-	4/5
116	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	13,298.64	05/2015 10/2018	10/2018	41(O) 0(R)	56/86
117	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020	0(O) -	4/12
118	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	12/2017	-	0/0
119	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND ,	03/2015	255.19 -	255.19	168.02	03/2018 -	03/2018	0(O) -	1/2
120	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	213.12	10/2017 -	12/2018	14(O) -	0/2
121	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	614.96	12/2017 -	11/2018	11(O) -	1/2
122	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	83.50	09/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
123	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21(O) -	0/0
124	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018	0(O) -	0/0
125	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24(O) -	0/0
126	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
127	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	38.51	06/2019 -	06/2019	0(O) -	0/1
128	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
129	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
130	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15(O) -	0/0
131	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,018.18	04/2018 -	02/2019	10(O) -	2/3
132	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17(O) -	0/0
133	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
134	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	12/2017	-	0/0
135	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
136	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	178.10	09/2018 -	01/2019	4(O) -	1/3
137	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		54,971.33 -	55,185.01	39,907.62				108/163
	PETROLEUM								
138	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0(O) -	0/1
139	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	52.19	09/2019 -	09/2019	0(O) -	19/27
140	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020	0(O) 0(R)	0/0
141	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	-	03/2021 -	03/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
142	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	-	03/2021 -	03/2021	0(O) -	0/0
143	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
144	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	6.02	04/2021 -	04/2021	0(O) -	0/0
145	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	88.97	02/2019 -	12/2018	-2(O) -	3/10
146	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.89	2,067.29	03/2013 09/2018	09/2018	66(O) 0(R)	5/15
147	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	8.45	01/2014 11/2019	11/2019	70(O) 0(R)	0/2
148	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM ,	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17(O) -	0/0
149	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	01/2018	-	46/61
150	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	117.83	08/2019 -	08/2019	0(O) -	2/13
151	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	445.91	11/2019 -	11/2019	0(O) -	6/17
152	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020	0(O) 0(R)	0/0
153	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8(O) -	0/0
154	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	961.00	03/2015 -	11/2017	-	0/5
155	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	390.95	11/2018 -	11/2018	0(O) -	5/8
156	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	240.15	12/2020 -	02/2020	-10(O) -	1/2
157	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	32.47	06/2020 -	06/2020	0(O) -	2/2
158	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	2,477.21	05/2019 10/2019	10/2019	5(O) 0(R)	0/0
159	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT ,	09/2011	202.25 -	160.16	115.36	07/2016 06/2018	06/2018	23(O) 0(R)	5/12
160	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	384.58	11/2019 12/2018	12/2018	-11(O) 0(R)	0/0
161	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	161.79	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
162	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	144.58	03/2018 -	03/2018	0(O) -	18/22
163	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	47.80	04/2018 -	07/2018	3(O) -	16/20
164	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT ,	02/2016	931.00 -	931.00	470.76	07/2017 -	02/2018	7(O) -	7/7
165	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	216.56	03/2026 03/2026	03/2026	0(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	26.19	07/2020 -	07/2020	0(O) -	0/0
167	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018	0(O) -	0/0
168	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	109.51	05/2019 -	12/2018	-5(O) -	3/13
169	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	34.75	09/2019 -	09/2019	0(O) -	2/2
170	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 06/2017	06/2017	-	8/12
171	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	8.14	03/2023 03/2022	03/2022	-12(O) 0(R)	0/0
172	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,L,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	11/2017	-	0/0
173	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	564.98	02/2020 -	02/2020	0(O) -	0/0
174	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	66.12	04/2019 -	04/2019	0(O) -	5/8
175	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 170.70	170.70	96.38	03/2019 -	03/2019	0(O) -	4/11
176	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	80.45	12/2019 -	12/2019	0(O) -	7/9
177	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	315.63	10/2017 -	03/2019	17(O) -	38/52
178	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	4,588.29	1,145.97	08/2018 05/2019	05/2019	9(O) 0(R)	0/20
179	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,313.00	107.18	02/2020 -	-	-	0/0
180	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA ,	05/2015	337.06 -	337.06	65.87	08/2018 -	08/2018	0(O) -	0/0
181	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 181.02	181.02	168.93	01/2017 03/2018	05/2018	16(O) 2(R)	0/0
182	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS & HSD, ADDITIONAL TANKS FOR MS,HSD AND BI - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	-	06/2020 -	06/2020	0(O) -	0/0
183	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,188.01	05/2013 03/2018	11/2018	66(O) 8(R)	1/5
184	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 -	2,665.65	1,729.04	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
185	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA ,	03/2012	2,592.17 -	2,592.17	2,039.15	05/2014 05/2018	05/2018	48(O) 0(R)	0/21
186	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	5,578.73	05/2017 05/2018	05/2018	12(O) 0(R)	9/16
187	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,316.24	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
188	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,504.61	1,237.43	05/2017 05/2018	05/2018	12(O) 0(R)	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	779.10	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
190	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	3,721.54	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
191	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	1,314.87	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
192	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	282.15	08/2021 -	08/2021	0(O) -	2/2
193	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	45.12	02/2020 -	02/2020	0(O) -	0/0
194	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	99.26	12/2019 -	12/2019	0(O) -	0/0
195	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	21.08	01/2019 -	01/2019	0(O) -	0/0
196	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0(O) -	0/0
197	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0(O) -	0/0
198	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0(O) -	0/0
199	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	0/0
200	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	140.80	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
201	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
202	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
203	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	-	11/2019 11/2019	11/2019	0(O) 0(R)	0/0
204	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 -	4,006.83	170.86	05/2021 -	05/2021	0(O) -	0/0
205	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	1,771.65	12/2018 -	12/2018	0(O) -	29/39
206	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	542.92	09/2011 06/2019	06/2019	93(O) 0(R)	0/0
207	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 06/2017	06/2017	-	8/8
208	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,103.82	06/2018 -	06/2018	0(O) -	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
209	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	449.68	10/2014 03/2018	02/2019	52(O) 11(R)	31/40
210	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20(O) -	0/0
211	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 5,725.50	5,725.50	4,290.94	04/2016 03/2018	03/2018	23(O) 0(R)	0/3
212	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	196.31	12/2020 -	12/2020	0(O) -	0/0
213	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	72.66	12/2020 -	08/2020	-4(O) -	1/2
214	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	296.05	10/2019 -	10/2019	0(O) -	2/3
215	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	134.25	07/2018 10/2020	10/2020	27(O) 0(R)	16/36
216	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	412.08	06/2020 -	06/2020	0(O) -	9/24
217	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	27.90	02/2019 -	02/2019	0(O) -	6/13
218	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	1.42	10/2020 -	10/2020	0(O) -	0/0
219	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	7.30	12/2019 -	12/2019	0(O) -	0/0
220	LAYING OF VIJAI PUR-AURAIYA PIPELINE SECTION OF VIJAI PUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,881.40	14.08	12/2019 12/2020	12/2019	0(O) -12(R)	11/24
221	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	42.30	12/2020 -	12/2020	0(O) -	11/24
222	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	11.32	12/2020 -	12/2020	0(O) -	9/24
223	KOCHI-KOOTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	2,915.00	1,621.62	12/2012 02/2019	02/2019	74(O) 0(R)	9/42
224	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	5.87	03/2021 -	03/2021	0(O) -	0/0
225	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	368.24	06/2017 -	07/2017	-	0/0
226	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	1,659.56	09/2017 12/2018	12/2018	15(O) 0(R)	5/6
227	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	199.59	03/2017 10/2017	10/2017	-	6/6
228	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	60.27	12/2020 -	12/2020	0(O) -	14/24
229	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	133.17	01/2019 -	01/2019	0(O) -	2/6
230	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	28.99	12/2019 -	12/2019	0(O) -	0/0
231	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	7.80	07/2022 -	07/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
232	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
233	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
234	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	11/2017	-	52/52
235	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU ,	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19(O) -	19/22
236	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU ,	08/2014	393.00 -	393.00	259.17	04/2018 -	04/2018	0(O) -	0/10
237	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.08	02/2017 -	-	-	0/0
238	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 -	390.52	97.34	03/2019 -	04/2019	1(O) -	0/0
239	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	74.03	12/2018 -	12/2018	0(O) -	1/2
240	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	-	06/2020 -	06/2020	0(O) -	2/2
241	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	144.26	12/2019 -	12/2019	0(O) -	0/0
242	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	1.15	08/2020 -	08/2020	0(O) -	0/0
243	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	.84	10/2020 -	10/2020	0(O) -	0/0
244	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA ,	05/2016	215.38 215.38	215.38	186.58	06/2017 01/2018	01/2018	-	0/0
245	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	750.00	514.17	12/2018 -	12/2018	0(O) -	13/20
246	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	39.40	04/2022 -	04/2022	0(O) -	0/0
247	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	-	08/2021 -	08/2021	0(O) -	0/0
248	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	-	09/2019 -	09/2019	0(O) -	0/0
249	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	23.16	02/2020 -	02/2020	0(O) -	9/26
250	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL ,	03/2014	3,076.00 4,190.00	4,190.00	2,505.63	09/2017 06/2018	06/2018	9(O) 0(R)	6/7
251	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL ,	08/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018	6(O) 0(R)	0/0
252	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 -	694.00	253.60	10/2018 -	10/2018	0(O) -	0/0
253	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	8.35	12/2020 -	12/2020	0(O) -	0/0
254	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	5.73	12/2020 -	12/2020	0(O) -	5/24
255	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	28.93	04/2020 -	04/2020	0(O) -	0/0
	Total		2,03,764.02 -	2,05,332.56	60,072.60				491/926

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
256	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	105.62	07/2018 -	03/2018	-4(O) -	0/0
257	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	9,838.43	09/2010 -	-	-	0/0
258	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,146.13	12/2009 03/2018	03/2018	99(O) 0(R)	21/30
259	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH ,	12/2008	573.99 1,337.76	1,337.76	1,556.85	08/2013 03/2018	03/2018	55(O) 0(R)	34/38
260	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	6,984.00	09/2011 06/2018	06/2018	81(O) 0(R)	31/37
261	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	14,283.00	01/2011 04/2021	04/2021	123(O) 0(R)	26/47
262	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57(O) 23(R)	2/18
263	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	-	01/2018 -	02/2019	13(O) -	27/31
264	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR ,	05/2015	436.68 -	602.44	481.23	12/2016 -	12/2018	24(O) -	10/16
265	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.30	363.47	06/2019 -	06/2019	0(O) -	0/0
266	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	9,341.00	06/2017 06/2019	06/2019	24(O) 0(R)	33/40
267	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	-	11/2019 -	12/2019	1(O) -	0/0
268	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	71.53	05/2017 06/2019	06/2019	25(O) 0(R)	4/9
269	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	96.34	10/2018 -	10/2018	0(O) -	0/0
270	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	98.07	12/2018 -	12/2018	0(O) -	0/0
271	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	197.07	11/2017 -	03/2018	4(O) -	1/4
272	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	14.44	09/2018 -	09/2018	0(O) -	0/0
273	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,652.65	09/2009 -	12/2020	135(O) -	2/3
274	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,882.01	5,233.88	01/2016 -	03/2018	26(O) -	6/6
275	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	893.51	04/2020 -	06/2023	38(O) -	0/0
276	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12(O) -	0/0
277	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	6,272.00	02/2019 10/2020	10/2020	20(O) 0(R)	20/23
278	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND ,	08/2006	2,313.00 4,138.41	4,366.64	3,484.00	12/2011 03/2016	02/2017	-	14/14
279	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,526.86	10/2017 -	12/2016	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018	14(O) 0(R)	47/48
281	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	70.63	02/2019 -	02/2019	0(O) -	0/0
282	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	8,722.00	09/2017 06/2019	06/2019	21(O) 0(R)	32/41
283	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	4,433.00	09/2019 -	09/2019	0(O) -	24/24
284	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	168.46	03/2017 10/2017	09/2018	18(O) 11(R)	0/0
285	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	90.51	06/2018 -	06/2018	0(O) -	0/0
286	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	39.79	09/2020 -	09/2020	0(O) -	9/16
287	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	761.00	06/2018 -	06/2018	0(O) -	0/0
288	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	659.02	09/2010 12/2017	12/2018	99(O) 12(R)	5/8
289	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 03/2017	03/2017	-	41/41
290	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,451.00	11/2016 03/2019	03/2019	28(O) 0(R)	34/38
291	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects	04/2015	2,225.00 2,225.00	2,225.00	1,287.00	01/2018 -	03/2018	2(O) -	0/0
292	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,507.26	10/2012 02/2018	12/2018	74(O) 10(R)	8/11
293	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,630.98	08/2013 12/2017	03/2018	55(O) 3(R)	22/26
294	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,610.29	12/2012 02/2018	06/2018	66(O) 4(R)	16/23
295	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE ,	02/2010	232.34 -	341.00	246.94	06/2012 -	03/2018	69(O) -	1/4
296	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,436.82	11/2012 12/2017	03/2018	64(O) 3(R)	10/13
297	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	487.29	06/2014 03/2018	03/2019	57(O) 12(R)	10/12
298	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 346.79	426.29	375.94	08/2014 12/2017	03/2018	43(O) 3(R)	8/10
299	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	137.13	09/2014 09/2017	03/2018	42(O) 6(R)	0/0
300	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE ,	11/2011	723.63 882.13	882.13	734.04	11/2014 06/2017	03/2018	40(O) 9(R)	8/10
301	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 703.10	703.10	587.18	06/2015 12/2017	06/2018	36(O) 6(R)	7/10

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
302	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	2,514.88	2,125.29	12/2015 12/2017	06/2018	30(O) 6(R)	15/18
303	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,183.35	04/2016 09/2017	06/2018	26(O) 9(R)	8/12
304	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	156.45	04/2016 12/2017	03/2018	23(O) 3(R)	0/0
305	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	399.39	06/2016 02/2018	06/2018	24(O) 4(R)	9/11
306	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	389.04	11/2016 11/2017	06/2018	19(O) 7(R)	8/12
307	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	143.08	03/2016 07/2017	03/2018	24(O) 8(R)	4/6
308	TRANSMISSION SYSTEM STRENGTHENING IN WR- NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	1,894.73	03/2018 -	03/2019	12(O) -	9/12
309	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 -	376.09	234.00	02/2017 06/2017	06/2018	16(O) 12(R)	7/12
310	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	142.77	02/2016 08/2017	04/2018	26(O) 8(R)	16/17
311	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36	3,707.22	04/2018 -	04/2018	0(O) -	3/12
312	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	185.89	03/2018 -	06/2018	3(O) -	1/3
313	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	10/2018	12(O) 12(R)	0/5
314	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	177.40	07/2017 -	12/2018	17(O) -	3/5
315	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	62.63	03/2018 -	03/2018	0(O) -	0/0
316	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	541.66	09/2017 -	09/2018	12(O) -	0/0
317	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,354.03	04/2018 -	09/2018	5(O) -	5/9
318	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30	833.39	04/2017 03/2018	03/2018	11(O) 0(R)	6/8
319	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	1,042.50	07/2018 -	07/2018	0(O) -	0/0
320	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	866.47	07/2018 -	07/2018	0(O) -	0/0
321	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	263.03	01/2018 -	03/2019	14(O) -	0/0
322	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	192.91	11/2018 -	11/2018	0(O) -	0/0
323	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	910.61	05/2019 -	05/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
324	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	992.21	11/2019 -	11/2019	0(O) -	0/0
325	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	455.95	12/2018 -	12/2018	0(O) -	0/0
326	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	60.44	11/2018 -	11/2018	0(O) -	0/0
327	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	48.37	07/2018 -	07/2018	0(O) -	0/0
328	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	193.70	03/2019 -	03/2019	0(O) -	0/0
329	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	75.73	02/2019 -	02/2019	0(O) -	0/0
330	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	42.66	02/2019 -	02/2019	0(O) -	0/0
331	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	18.59	03/2019 -	03/2019	0(O) -	0/0
332	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	1.76	06/2019 -	06/2019	0(O) -	0/0
333	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE ,	10/2016	167.75 -	167.75	48.78	04/2019 -	04/2019	0(O) -	0/0
334	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	7.71	11/2019 -	11/2019	0(O) -	0/0
335	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019	0(O) -	0/0
336	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	114.89	04/2019 -	04/2019	0(O) -	0/0
337	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	-	02/2020 -	02/2020	0(O) -	0/0
338	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	17.19	02/2019 -	02/2019	0(O) -	0/0
339	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	11.35	03/2019 -	03/2019	0(O) -	0/0
340	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	7.96	06/2019 -	06/2019	0(O) -	0/0
341	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	19.67	12/2019 -	12/2019	0(O) -	0/0
342	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	9.11	09/2019 -	09/2019	0(O) -	0/0
343	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
344	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	6.00	06/2019 -	06/2019	0(O) -	0/0
345	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	4,754.42	541.38	12/2018 -	12/2019	12(O) -	0/0
346	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	5,111.33	429.76	12/2018 -	12/2019	12(O) -	0/0
347	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 1,161.00	1,364.00	1,113.00	12/2015 -	03/2018	27(O) -	0/0
348	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,746.00	11/2017 -	03/2018	4(O) -	0/0
349	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	1,415.00	04/2019 -	04/2019	0(O) -	0/0
350	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	139.00	07/2020 -	07/2020	0(O) -	0/0
351	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	29.17	02/2020 -	02/2020	0(O) -	0/0
352	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	7,029.00	08/2018 06/2019	06/2019	10(O) 0(R)	26/37
353	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	183.83	04/2019 -	04/2019	0(O) -	0/0
354	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	178.76	11/2017 -	12/2018	13(O) -	0/0
355	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	290.24	01/2019 -	01/2019	0(O) -	0/0
356	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	1,988.93	11/2008 09/2018	09/2018	118(O) 0(R)	20/22
357	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,395.80	09/2014 06/2017	09/2018	48(O) 15(R)	11/13
358	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU ,	01/2016	162.11 -	162.11	124.71	05/2018 -	03/2018	-2(O) -	0/0
359	50 MW SOLAR POWER PROJECT - [N18000251]NHPC,TAMIL NADU ,	06/2017	287.48 -	287.48	110.15	03/2018 -	03/2018	0(O) -	0/0
360	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	8.59	07/2019 -	07/2019	0(O) -	0/0
361	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	1,399.00	07/2020 10/2020	10/2020	3(O) 0(R)	16/18
362	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 1,078.31	1,078.31	963.23	07/2013 -	-	-	26/26
363	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA ,	05/2016	409.19 -	409.19	191.54	05/2018 -	05/2018	0(O) -	0/0
364	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
365	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	3,918.00	03/2019 03/2019	09/2019	6(O) 6(R)	19/30
366	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	158.67	02/2014 02/2018	03/2019	61(O) 13(R)	4/5
367	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26(O) -	30/34
368	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,458.96	02/2016 09/2019	12/2020	58(O) 15(R)	16/26
369	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,446.00	03/2013 12/2020	12/2020	93(O) 0(R)	3/15
370	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,789.61	1,344.53	06/2013 -	11/2020	89(O) -	8/11
371	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	148.00	08/2017 -	-	-	0/15
372	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	85.72	12/2021 -	12/2021	0(O) -	0/0
373	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL ,	04/2010	4,404.57 5,135.01	5,135.01	3,683.22	01/2015 03/2018	11/2018	46(O) 8(R)	14/16
374	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	306.00	09/2019 02/2022	02/2022	29(O) 0(R)	5/9
375	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL ,	04/2007	4,122.00 8,781.30	9,142.58	8,300.00	02/2011 -	03/2016	-	26/26
376	EASTERN REGION STRENGTHENNING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	182.24	04/2018 -	04/2018	0(O) -	0/0
	Total		3,37,506.49 -	4,04,972.96	2,25,943.04				859/1124
	<u>HEAVY INDUSTRY</u>								
377	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	-	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
378	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	24.38	03/2019 -	03/2019	0(O) -	0/0
379	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
380	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
381	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13(O) -	0/2
382	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16(O) -	0/5
383	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6(O) -	0/2
384	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	312.99	149.00	08/2018 -	08/2018	0(O) -	0/1
385	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	29.68	03/2019 -	03/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
386	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	21.00	05/2018 08/2019	08/2019	15(O) 0(R)	0/0
387	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6(O) -	0/1
388	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	158.65	11/2013 09/2017	09/2017	-	0/8
389	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10(O) -	0/3
390	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	77.50	09/2018 -	09/2018	0(O) -	0/0
391	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	21.79	03/2019 -	03/2019	0(O) -	0/0
	Total		3,897.21 -	3,919.69	1,507.40				0/22
	<u>RAILWAYS</u>								
392	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 164.36	966.98	969.17	02/2009 -	-	-	0/0
393	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 -	2,125.18	246.34	- -	03/2021	- -	0/0
394	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	1,568.77	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
395	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	759.41	.51	- -	-	-	0/0
396	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	- -	-	-	0/1
397	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	1,313.48	216.49	- -	-	-	0/1
398	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	578.80	- -	03/2020	- -	0/0
399	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	-	- -	-	-	0/0
400	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 -	3,631.00	19.31	- -	-	-	0/0
401	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	37.25	- -	-	-	0/0
402	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	48.52	03/2021 -	03/2022	12(O) -	0/0
403	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	375.37	03/2018 -	03/2018	0(O) -	0/0
404	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	234.50	.39	03/2019 -	03/2019	0(O) -	0/0
405	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	1,500.00 -	5,450.00	4,965.44	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
406	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	780.00	450.50	- -	03/2020	- -	0/0
407	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	535.00	532.42	- -	03/2019	- -	0/0
408	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	128.77	- -	03/2019	- -	0/0
409	BONGAIGON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.00	93.15	- -	03/2022	- -	0/0
410	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	871.00	31.53	- -	03/2021	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
411	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240] ECR, BIHAR ,	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
412	KATI HAR - JOGBANI (GC)(NEFR) - [220100247] NFR, BIHAR ,	09/2001	492.98 -	1,320.00	919.32	12/2010 -	-	-	0/0
413	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR ,	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
414	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR ,	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
415	KOSI BRIDGE (NL), ECR - [220100304] ECR, BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
416	DANIAWAN-BIHARSARIF (NL), ECR - [220100311] ECR, BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
417	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, BIHAR ,	04/2003	218.19 -	412.05	349.66	- -	04/2018	-	0/0
418	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002] ECR, BIHAR ,	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
419	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087] NFR, BIHAR ,	09/2006	300.00 -	2,135.00	922.31	- -	03/2020	-	0/0
420	KISHANGANJ JALALGARH, NL, NEFR - [N22000101] NFR, BIHAR ,	04/2008	282.92 -	360.00	3.13	- -	03/2020	-	0/0
421	ARA-BHABHUA ROAD (NL) - [N22000166] SER, BIHAR ,	04/2008	490.80 -	490.80	.39	- -	-	-	0/0
422	NAWADA-LAXMIPUR (NL) - [N22000167] ECR, BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
423	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168] ECR, BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0
424	BIHTA-AURANGABAD (NL) - [N22000170] ECR, BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
425	SAKRI-HASANPUR ROAD (NL) - [N22000171] ECR, BIHAR ,	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
426	CHHAPRA-MUZAFFARPUR (NL) - [N22000172] ECR, BIHAR ,	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
427	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173] ECR, BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
428	MOTIHARI-SITAMARHI (NL) - [N22000174] ECR, BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
429	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175] ECR, BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
430	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176] ECR, BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
431	ARARIA-SUPAUL (NL) - [N22000177] ECR, BIHAR ,	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
432	KURSELA-BIHARIGANJ (NL) - [N22000178] ECR, BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
433	MUZAFFARPUR-DARBANGHA (NL) - [N22000179] ECR, BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
434	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180] ECR, BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
435	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181] ECR, BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
436	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182] ECR, BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
437	SAMASTIPUR-DARBANGHA - [N22000329] ECR, BIHAR ,	05/2015	380.00 -	380.00	-	- -	-	-	0/0
438	KIUL - GAYA DOUBLING PROJECT - [N22000349] ECR, BIHAR ,	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020	0(0) -	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
439	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020	0(O) -	1/1
440	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
441	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	1,141.70	535.96	12/2012 -	-	-	0/0
442	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	555.00	508.51	03/2010 -	12/2017	-	0/3
443	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	496.81	- -	03/2020	-	0/1
444	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	695.29	03/2020 -	03/2020	0(O) -	0/0
445	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	149.15	03/2018 -	03/2018	0(O) -	0/0
446	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
447	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
448	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 816.86	385.60	387.69	03/2013 -	03/2020	84(O) -	0/0
449	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 2,446.85	2,446.85	2,015.62	03/2014 -	-	-	0/0
450	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	81.96	03/2012 -	03/2019	84(O) -	0/0
451	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
452	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	387.97	- -	03/2020	-	0/0
453	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	44.80	- -	12/2020	-	0/0
454	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	844.10	15.89	- -	-	-	0/0
455	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.12	858.96	548.93	- -	03/2019	-	0/0
456	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,548.66	469.04	- -	12/2020	-	0/0
457	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 384.32	355.00	328.04	- -	-	-	0/0
458	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	143.70	- -	03/2021	-	0/0
459	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	257.28	03/2019 -	03/2019	0(O) -	0/0
460	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	-	- -	-	-	0/0
461	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	-	- -	-	-	0/0
462	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	-	- -	-	-	0/0
463	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
464	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	-	-	-	0/0
465	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	-	-	-	0/0
466	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	217.53	03/2019 -	03/2019	0(O) -	0/0
467	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	4,500.00	123.98	-	03/2019	-	0/0
468	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193(O) -	0/0
469	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 111(R)	0/0
470	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 -	491.33	-	06/2004 -	-	-	0/0
471	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	-	-	-	0/0
472	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	388.00	348.52	02/2006 -	12/2019	166(O) -	0/1
473	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	207.11	03/2012 -	-	-	0/0
474	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	583.00	-	12/2015 -	-	-	0/0
475	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	98.37	-	12/2017	-	0/0
476	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	-	12/2016 -	-	-	0/0
477	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021	0(O) -	0/0
478	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	133.91	-	-	-	0/0
479	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	6.12	-	-	-	0/0
480	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 -	1,801.01	3.58	-	-	-	0/0
481	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 -	1,350.91	815.65	-	-	-	0/1
482	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	278.24	-	-	-	0/1
483	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	-	-	-	0/0
484	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 -	832.47	.94	-	-	-	0/0
485	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.35	-	-	-	0/0
486	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	909.63	-	03/2019	-	0/1
487	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	-	-	-	0/0
488	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	8.35	-	-	-	0/0
489	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	-	-	-	0/0
490	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	3.95	01/1999 -	-	-	0/0
491	HUBLI- CHIKAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	521.44	-	-	-	0/5
492	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	341.68	-	03/2020	-	0/2
						11/2015		52(R)	

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
493	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 -	2,815.62	240.68	-	01/2018	-	0/0
494	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	7.74	-	-	-	0/0
495	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	378.76	-	-	-	0/0
496	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.28	-	12/2017	-	0/0
497	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	4,131.90	-	-	-	-	0/0
498	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	-	-	-	0/0
499	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 727.13	2,713.09	632.05	-	03/2021	-	0/0
500	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	-	-	-	0/0
501	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH ,	09/2007	687.20 -	1,030.00	1,027.36	03/2010	03/2018	96(O)	0/0
502	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 -	1,030.29	933.20	03/2012	-	-	0/0
503	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020	12/2020	0(O)	1/1
504	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.85	729.73	12/2020	12/2020	0(O)	0/0
505	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	-	03/2022	03/2022	0(O)	0/1
506	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	582.13	-	03/2020	03/2020	0(O)	0/1
507	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	121.35	03/2019	03/2019	0(O)	0/0
508	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.97	710.31	06/1999	-	-	0/0
509	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	801.59	03/2004	03/2020	192(O)	0/0
510	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	1,455.54	-	03/2021	-	0/0
511	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014	03/2019	60(O)	0/0
512	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016	-	-	0/0
513	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 3,168.29	3,168.29	803.55	-	03/2023	-	0/0
514	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	220.71	-	03/2021	-	0/0
515	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	152.31	-	03/2019	-	0/0
516	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	125.56	-	03/2022	-	0/0
517	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	-	-	03/2024	-	0/0
518	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.15	-	03/2024	-	0/0
519	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	-	-	03/2024	-	0/0
520	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	62.59	-	03/2022	-	0/0
521	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 2,449.91	2,449.91	34.54	-	03/2023	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
522	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	17.52	- -	03/2024	- -	0/0
523	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	.14	- -	03/2023	- -	0/0
524	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 1,035.16	1,035.16	4.00	- -	03/2023	- -	0/0
525	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 637.95	637.95	7.28	- -	03/2022	- -	0/0
526	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,750.00	1,356.10	03/2020 -	03/2020	0(O) -	0/0
527	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.16	12/2025 -	12/2025	0(O) -	0/0
528	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021	0(O) -	0/0
529	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	241.05	03/2019 -	03/2019	0(O) -	0/0
530	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	-	- -	-	- -	0/0
531	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	-	- -	-	- -	0/0
532	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 -	9,658.00	7,211.12	03/2011 -	03/2020	108(O) -	0/0
533	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	257.21	- -	03/2021	- -	0/0
534	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 -	4,600.00	1,928.11	04/2014 -	03/2020	71(O) -	0/0
535	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	- -	0/0
536	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	- -	0/0
537	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261(O) -	0/0
538	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	- -	0/0
539	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 236.41	525.00	679.98	- -	03/2019	- -	0/0
540	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/4
541	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	761.70	- -	-	- -	1/1
542	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	- -	0/0
543	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	- -	-	- -	0/6
544	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,040.00	2,842.53	12/2008 -	03/2019	123(O) -	0/0
545	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 -	350.00	320.46	02/2011 -	-	- -	0/0
546	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	973.33	613.71	12/2012 12/2012	-	- -	0/0
547	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	272.46	- -	05/2019	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
548	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	268.78	93.68	- -	08/2018	-	0/0
549	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	146.48	- -	10/2018	-	0/0
550	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	526.95	- -	-	-	0/0
551	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	455.37	- -	03/2022	-	0/0
552	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,562.27	180.73	- -	-	-	0/1
553	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0
554	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46(O) -	0/0
555	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 -	1,009.00	-	- -	-	-	0/0
556	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
557	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
558	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
559	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39 -	1,810.00	1,679.05	- -	03/2018	-	0/1
560	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	253.87	- -	-	-	0/0
561	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	53.14	- -	03/2020	-	0/0
562	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
563	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	122.81	- -	03/2020	-	0/0
564	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,084.45	- -	03/2018	-	0/0
565	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 -	1,800.00	77.17	- -	-	-	0/0
566	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	319.58	141.88	- -	-	-	0/0
567	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
568	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.60	6.42	- -	-	-	0/0
569	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 1,130.13	1,130.13	.30	- -	-	-	0/0
570	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
571	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	51.31	- -	-	-	0/0
572	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	87.22	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
573	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	227.50	- -	-	-	0/0
574	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
575	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	160.97	56.25	- -	-	-	0/0
576	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.00	92.93	- -	-	-	0/0
577	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 -	198.88	15.83	- -	-	-	0/0
578	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	47.63	- -	11/2018	-	0/0
579	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	15.66	- -	-	-	0/0
580	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
581	HANSIDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	98.15	- -	-	-	0/0
582	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 -	186.64	150.28	- -	-	-	0/0
583	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	18.54	- -	-	-	0/0
584	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.11	03/2017 -	-	-	0/0
585	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0
586	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.01	- -	-	-	0/0
587	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	186.89	62.73	- -	-	-	0/0
588	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 -	681.68	135.79	- -	-	-	0/0
589	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 -	720.59	456.58	03/2017 -	-	-	0/0
590	SANTOSHPUTR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
591	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
592	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 1,693.00	2,200.00	204.51	- -	-	-	0/0
593	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	2.40	- -	-	-	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
594	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
595	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	-	-	-	0/0
596	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	-	-	-	-	0/0
597	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	1,714.49	653.46	-	-	-	0/2
598	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	792.01	69.69	-	-	-	0/1
599	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,050.00	286.00	-	-	-	0/1
600	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	-	-	-	0/0
601	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	-	-	-	0/0
602	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	-	-	-	0/0
603	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	-	-	-	0/0
604	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	8.43	-	-	-	0/0
605	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE ,	04/2007	313.24 -	607.70	568.60	01/1999 -	-	-	0/0
606	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
607	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.05	-	03/2020	-	0/0
608	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	119.50	-	-	-	0/0
609	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	860.43	346.94	-	03/2020	-	0/0
610	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	555.23	-	-	-	0/0
611	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 -	678.54	-	-	12/2018	-	0/38
612	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	-	-	-	0/0
613	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	202.11	-	03/2021	-	0/0
614	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	-	-	-	0/0
615	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	428.38	03/2015 -	03/2020	60(O) -	0/0
616	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	-	-	03/2020	-	0/0
617	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,004.90	956.23	-	06/2021	-	0/0
618	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.99	1,078.57	-	03/2019	-	0/0
619	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.07	488.99	02/2015 -	12/2019	58(O) -	0/0
620	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	343.00	364.21	03/2009 03/2009	12/2017	-	1/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
621	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	486.05	- -	12/2022	- -	0/0
622	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	- -	0/0
623	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,111.99	1,579.27	641.37	- -	03/2021	- -	0/0
624	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 843.04	843.04	51.85	- -	03/2021	- -	0/0
625	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	156.11	- -	03/2020	- -	0/0
626	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA ,	03/2011	165.16 -	234.71	225.68	03/2015 07/2015	07/2015	-	0/0
627	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	71.55	03/2021 -	03/2021	0(O) -	0/0
628	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	34.98	03/2021 -	03/2022	12(O) -	0/0
629	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	53.02	03/2021 -	03/2021	0(O) -	0/0
630	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	122.87	03/2021 -	03/2020	-12(O) -	0/0
631	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020	0(O) -	0/0
632	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	-	12/2021 -	12/2021	0(O) -	0/0
633	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	62.27	- -	12/2024	- -	0/0
634	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	748.08	03/2020 -	03/2020	0(O) -	0/0
635	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	845.10	03/2019 -	03/2019	0(O) -	0/0
636	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0
637	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
638	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
639	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	388.59	- 02/1997	02/2019	- 264(R)	0/0
640	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,143.70	554.05	03/2015 -	12/2019	57(O) -	0/0
641	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	895.00	685.07	03/2014 -	06/2019	63(O) -	0/0
642	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	61.89	- -	03/2019	- -	0/0
643	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	114.58	- -	10/2018	- -	0/0
644	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
645	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	- -	-	-	0/0
646	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 295.02	420.08	36.19	- -	05/2018	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
647	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 218.39	244.02	126.95	- -	02/2019	- -	0/0
648	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	346.35	213.86	- -	10/2018	- -	0/0
649	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	148.53	- -	03/2019	- -	0/0
650	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	873.71	-	- -	-	-	0/0
651	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	385.61	03/2018 -	03/2018	0(O) -	0/0
652	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN ,	04/2012	471.82 -	471.82	20.03	03/2019 -	03/2019	0(O) -	0/0
653	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
654	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
655	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	732.89	390.56	06/2013 -	03/2017	-	1/4
656	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	404.19 -	2,072.50	1,048.37	- -	-	-	0/0
657	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
658	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	456.00 582.83	2,300.00	231.40	- 07/2008	-	-	0/0
659	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	446.87 527.37	1,105.00	3.34	- 01/2011	-	-	0/0
660	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
661	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
662	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
663	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	36.26	- -	-	-	0/0
664	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU ,	04/2011	190.10 -	350.00	308.90	- -	03/2018	- -	0/0
665	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 -	1,010.00	1,013.26	- -	-	-	0/0
666	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 -	480.00	3.69	07/2008 -	-	-	0/0
667	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 -	1,160.47	18.25	- -	03/2022	- -	0/1
668	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	500.53	03/2016 -	12/2017	-	0/0
669	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	1,112.00	.92	- -	-	-	0/1
670	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	-	- -	-	-	0/1
671	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
672	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	45.79	12/2024 -	12/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
673	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	-	03/2022 -	03/2022	0(0) -	0/0
674	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,451.00	2,550.24	03/2014 -	03/2020	72(0) -	0/0
675	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 -	1,857.00	1,504.50	03/2007 -	04/2016	-	0/0
676	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 -	580.00	-	- -	07/2019	- -	2/3
677	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
678	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
679	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
680	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
681	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	308.00	-	- -	-	-	0/0
682	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	474.30	424.76	- -	03/2018	- -	0/0
683	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	227.00	240.37	- -	08/2018	- -	0/0
684	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	-	- -	-	-	0/0
685	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
686	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
687	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
688	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	- -	-	-	0/0
689	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,295.42	50.86	03/2022 -	03/2022	0(0) -	0/0
690	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	-	03/2020 -	03/2020	0(0) -	0/6
691	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	750.56	22.91	12/2024 -	12/2024	0(0) -	0/0
692	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	830.06	03/2019 -	03/2019	0(0) -	0/0
693	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.92	32.37	12/2025 -	12/2025	0(0) -	0/0
694	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.30	766.30	12/2020 -	12/2020	0(0) -	0/0
695	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	119.12	03/2020 -	03/2020	0(0) -	0/0
696	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12(0) -	0/0
697	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
698	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	16,216.00	574.09	12/2026 -	12/2026	0(O) -	0/0
700	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL ,	04/1983	36.80 274.41	614.00	262.63	- -	03/2020	- -	0/0
701	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	-	03/2007 03/2007	-	-	0/0
702	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
703	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	- 111(R)	0/0
704	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	355.85	12/2010 -	-	-	3/7
705	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	-	-	0/0
706	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
707	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,070.00	40.16	03/2014 -	-	-	0/0
708	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,567.98	03/2016 -	12/2020	57(O) -	0/0
709	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	2,913.50	729.94	03/2016 -	12/2018	33(O) -	0/0
710	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	533.38 -	533.38	127.10	12/2011 -	-	-	0/0
711	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	611.03 -	611.03	146.31	12/2011 -	-	-	0/0
712	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL ,	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
713	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL ,	04/1999	207.52 -	334.87	293.47	12/2012 -	-	-	0/0
714	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
715	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	434.00	-	- -	-	-	0/0
716	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	-	- -	-	-	0/0
717	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	97.41	- -	03/2020	- -	0/0
718	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL ,	04/2011	209.77 -	630.00	613.01	- -	03/2018	- -	0/0
719	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL ,	04/2012	283.55 -	450.00	345.63	- -	03/2019	- -	0/0
720	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
721	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	.64	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
722	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
723	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	556.31 -	612.00	-	-	03/2020	-	0/0
724	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	763.18 -	1,428.00	-	12/2021 -	12/2021	0(0) -	0/0
725	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	-	03/2003 -	-	-	0/0
	Total		3,41,263.79 -	4,61,201.56	1,25,375.67				13/106
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
726	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	-	05/2013 -	12/2017	-	0/0
727	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62(0) -	0/0
728	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	-	05/2014 -	06/2017	-	0/0
729	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
730	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	02/2017	-	0/1
731	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	-	0/0
732	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 200.69	207.40	44.08	07/2014 -	-	-	0/1
733	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1
734	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	02/2017	-	0/1
735	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	-	-	-	0/1
736	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	-	-	-	0/4
737	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
738	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
739	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
740	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
741	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
742	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	-	2/4
743	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	-	0/4
744	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	-	0/0
745	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
746	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
747	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
748	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
749	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	- -	0/0
750	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	-	02/2017 -	02/2017	-	0/0
751	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0(O) -	0/0
752	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2(O) -	0/0
753	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	-	06/2017 -	-	-	0/0
754	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
755	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	-	- -	-	-	0/0
756	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	-	- -	-	-	0/0
757	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
758	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0
759	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
760	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	05/2018	0(O) -	1/4
761	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0(O) -	1/4
762	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0(O) -	1/4
763	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/3
764	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
765	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
766	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0
767	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	05/2018	0(O) -	1/4
768	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
769	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	-	06/2016 -	06/2016	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
770	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	-	- -	-	-	0/0
771	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	-	10/2016 -	10/2016	-	0/4
772	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	-	- -	-	-	0/0
773	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36(O) -	0/0
774	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	-	03/2017 -	-	-	0/0
775	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	-	04/2017 -	-	-	0/0
776	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	-	04/2017 -	-	-	0/0
777	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	-	04/2017 -	-	-	0/0
778	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	-	04/2017 -	-	-	0/0
779	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	-	04/2017 -	-	-	0/0
780	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	-	04/2017 -	-	-	0/0
781	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	-	04/2017 -	-	-	0/0
782	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	-	04/2017 -	-	-	0/0
783	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	-	04/2017 -	-	-	0/0
784	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111(O) -	0/0
785	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	-	04/2009 -	12/2017	-	0/0
786	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
787	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112(O) -	0/0
788	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114(O) -	0/0
789	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	-	03/2008 -	11/2017	-	0/0
790	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117(O) -	0/0
791	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119(O) -	0/0
792	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117(O) -	0/0
793	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104(O) -	0/0
794	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96(O) -	0/0
795	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	05/2018	0(O) -	0/4
796	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
797	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
798	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
799	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
800	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0(O) -	0/4
801	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	-	0/0
802	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
803	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
804	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
805	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
806	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
807	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	-	-	-	0/0
808	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
809	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
810	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	-	01/2016 -	01/2016	-	0/4
811	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64(O) -	0/0
812	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	-	05/2013 -	10/2017	-	0/0
813	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	-	02/2014 -	-	-	0/0
814	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	-	03/2014 -	09/2017	-	0/0
815	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	-	04/2014 -	-	-	0/0
816	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56(O) -	0/0
817	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	-	11/2013 -	12/2017	-	0/0
818	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
819	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	08/2016	-	0/0
820	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	10/2016	-	0/0
821	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	-	- -	-	-	0/0
822	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	-	- -	04/2019	-	0/0
823	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	-	- -	-	-	0/0
824	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
825	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	-	- -	-	-	0/0
826	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	-	- -	-	-	0/0
827	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
828	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	-	- -	-	-	0/0
829	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	-	- -	12/2017	-	0/0
830	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
831	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
832	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	- -	-	-	0/0
833	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	-	-	0/0
834	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	-	08/2014 -	08/2014	-	0/0
835	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	-	08/2014 -	-	-	0/0
836	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	-	07/2016 -	-	-	0/0
837	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	-	07/2016 -	-	-	0/0
838	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	-	05/2016 -	-	-	0/0
839	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	-	06/2016 -	06/2016	-	0/0
840	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	-	05/2016 -	-	-	0/0
841	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	-	-	0/0
842	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
843	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	-	11/2015 -	-	-	0/0
844	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	-	05/2017 -	-	-	0/0
845	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	-	0/0
846	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	-	03/2020 -	03/2020	0(0) -	0/0
847	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	-	03/2020 -	03/2020	0(0) -	0/0
848	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	-	08/2017 -	-	-	0/0
849	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
850	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	-	- -	-	-	0/0
851	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	-	- -	-	-	0/0
852	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
853	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
854	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
855	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	-	0/0
856	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
857	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
858	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
859	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
860	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	-	08/2015 -	12/2017	-	0/0
861	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
862	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
863	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	- -	04/2018	-	0/0
864	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	-	- -	03/2018	-	0/0
865	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
866	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
867	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
868	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
869	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	- -	-	-	0/0
870	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	- -	-	-	0/0
871	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	- -	-	-	0/0
872	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	-	09/2012 -	12/2017	-	2/3
873	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	-	07/2013 -	-	-	0/0
874	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	-	12/2015 -	07/2017	-	0/3
875	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	-	08/2016 -	-	-	0/0
876	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	-	- -	-	-	0/0
877	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	-	- -	-	-	0/0
878	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	-	- -	-	-	0/0
879	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	-	- -	-	-	0/0
880	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	-	- -	-	-	0/0
881	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	-	- -	-	-	0/0
882	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	-	- -	-	-	0/0
883	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	-	- -	-	-	0/0
884	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	-	- -	-	-	0/0
885	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020	0(O) -	0/0
886	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	-	10/2017 -	-	-	0/0
887	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	-	05/2010 -	08/2017	-	0/0
888	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76(O) -	0/0
889	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	-	11/2013 -	08/2017	-	0/0
890	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54	-	02/2018 -	02/2018	0(O) -	0/0
891	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA ,	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
892	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
893	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
894	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	- -	04/2019	- -	0/0
895	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	-	- -	01/2018	-	0/0
896	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	-	- -	05/2018	- -	0/0
897	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	-	- -	05/2018	- -	0/0
898	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	-	- -	05/2019	- -	0/0
899	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	- -	0/0
900	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	-	03/2020 -	03/2020	0(O) -	0/0
901	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15(O) -	0/0
902	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
903	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	- -	02/2019	- -	0/0
904	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	- -	-	-	0/0
905	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	-	- -	-	-	0/0
906	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	-	- -	-	-	0/0
907	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020	0(O) -	0/0
908	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44(O) -	0/0
909	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	-	-	0/0
910	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	-	07/2013 -	11/2017	-	0/0
911	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	-	06/2014 -	12/2017	-	0/0
912	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
913	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018	0(O) -	0/0
914	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
915	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	870.66	06/2015 -	12/2017	-	0/0
916	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	329.10	-	03/2019	-	0/0
917	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	-	-	-	0/0
918	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	21.26	-	08/2018	-	0/0
919	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	-	03/2020 -	03/2020	0(O) -	0/0
920	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	-	03/2020 -	03/2020	0(O) -	0/0
921	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	-	-	-	-	0/0
922	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	-	-	-	-	0/0
923	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	-	06/2018	-	3/3
924	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	-	0/0
925	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	-	0/0
926	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	283.32	09/2017 -	03/2018	6(O) -	0/0
927	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	-	0/0
928	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,476.75	08/2016 -	02/2019	30(O) -	0/0
929	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	635.26	-	08/2018	-	0/0
930	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	5.78	-	03/2019	-	0/0
931	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	2.93	-	03/2019	-	0/0
932	4-LANING OF HOSKOTE-DOBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	-	-	-	0/0
933	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH- 63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	75.54	-	04/2020	-	0/0
934	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	103.81	-	03/2019	-	0/0
935	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH- 209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	66.58	-	08/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
936	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	-	03/2020 -	06/2020	3(O) -	0/0
937	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	-	03/2020 -	05/2020	2(O) -	0/0
938	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	-	08/2012 -	12/2017	-	0/0
939	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	-	0/0
940	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	-	-	0/0
941	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	-	- -	11/2017	-	0/0
942	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
943	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	-	09/2017 -	-	-	0/0
944	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	-	04/2013 -	09/2017	-	0/0
945	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	-	05/2013 -	07/2017	-	0/0
946	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	07/2017	-	0/0
947	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	09/2016	-	0/0
948	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
949	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	-	-	0/0
950	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	02/2016	-	0/0
951	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	-	0/0
952	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	05/2017	-	0/0
953	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
954	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	08/2016	-	0/0
955	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	-	0/0
956	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
957	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
958	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	-	-	-	-	0/0
959	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	-	-	-	-	0/0
960	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	05/2017	-	0/0
961	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
962	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018	0(O) -	0/0
963	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	-	-	12/2017	-	0/0
964	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	-	11/2015 -	09/2017	-	0/0
965	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36(O) -	0/0
966	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
967	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	-	-	-	-	0/0
968	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	01/2019	-	0/0
969	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	-	0/0
970	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	-	01/2019	-	0/0
971	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	-	10/2017 -	-	-	0/0
972	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	-	09/2017 -	-	-	0/0
973	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	-	09/2017 -	-	-	0/0
974	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	-	-	-	-	0/0
975	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	-	-	-	-	0/0
976	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
977	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
978	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,070.65	03/2013 -	12/2017	-	0/0
979	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	416.83	06/2014 -	03/2018	45(O) -	0/0
980	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49(O) -	2/2
981	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	11/2016	-	0/2
982	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	-	10/2017	-	0/4
983	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	07/2016	-	0/12
984	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	-	06/2017	-	0/4
985	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	11/2016	-	0/4
986	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	-	-	-	0/0
987	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	65.16	- 03/2013	-	-	0/0
988	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	205.97	- 11/2014	11/2014	-	0/0
989	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	-	-	-	0/0
990	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	-	05/2019	-	0/0
991	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	130.04	-	05/2018	-	0/0
992	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	100.18	-	05/2018	-	0/0
993	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	-	05/2019	-	0/0
994	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	20.02	-	05/2018	-	0/0
995	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	31.47	-	03/2019	-	0/0
996	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	136.04	-	05/2018	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
997	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,479.14	07/2017 -	01/2018	-	0/0
998	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	525.02	11/2016 -	11/2017	-	0/0
999	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1000	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,848.31	01/2018 -	01/2018	-	0/0
1001	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,104.55	06/2012 -	03/2018	69(O) -	0/0
1002	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	11/2014	-	0/0
1003	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1004	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	-	- -	07/2019	- -	0/0
1005	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	-	- -	07/2019	- -	0/0
1006	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1007	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	-	- -	-	-	0/0
1008	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	-	- -	-	-	0/0
1009	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
1010	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
1011	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	-	- -	03/2019	- -	0/0
1012	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	-	- -	03/2019	- -	0/0
1013	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	-	- -	-	-	0/0
1014	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	43.29	- -	05/2019	- -	0/0
1015	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	6.00	02/2020 -	02/2020	0(O) -	0/0
1016	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	-	03/2020 -	03/2020	0(O) -	0/0
1017	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	-	03/2020 -	03/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1018	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020	0(O) -	0/0
1019	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	-	03/2020 -	03/2020	0(O) -	0/0
1020	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	-	03/2017 -	-	-	0/0
1021	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	23.87	03/2020 -	05/2019	-10(O) -	0/0
1022	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020	0(O) -	0/0
1023	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	-	- -	-	-	0/0
1024	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	-	- -	-	-	0/0
1025	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	-	- -	-	-	0/0
1026	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50(O) -	0/0
1027	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
1028	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	-	- -	05/2018	-	0/0
1029	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
1030	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
1031	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1032	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
1033	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	09/2017	-	2/2
1034	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	12/2017	-	0/0
1035	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49(O) -	0/0
1036	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,155.31	03/2013 -	11/2017	-	0/0
1037	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	-	04/2015 -	12/2017	-	0/0
1038	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1039	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
1040	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	-	- -	-	-	0/0
1041	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
1042	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36(O) -	0/0
1043	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36(O) -	0/0
1044	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36(O) -	0/0
1045	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	-	04/2017 -	-	-	0/0
1046	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42(O) -	0/0
1047	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	12/2017	-	0/0
1048	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	29.27	10/2017 -	10/2017	-	0/0
1049	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1050	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 265.35	229.41	6.65	05/2018 -	05/2018	0(O) -	0/0
1051	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	-	0/0
1052	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
1053	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	- -	-	-	0/0
1054	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	-	0/0
1055	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
1056	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
1057	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1058	REHABILITATION AND UPGRADE TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA ,	10/2016	1,008.96 -	1,008.96	-	-	-	-	0/0
1059	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH, ODISHA ,	03/2014	191.50 192.00	192.00	-	05/2016 -	06/2017	-	0/0
1060	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH, ODISHA ,	01/2015	326.63 327.00	327.00	-	04/2018 -	04/2018	0(O) -	0/0
1061	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH, ODISHA ,	02/2015	239.91 240.00	240.00	-	10/2017 -	10/2017	-	0/0
1062	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH, ODISHA ,	03/2015	226.31 226.00	226.00	-	10/2017 -	10/2017	-	0/0
1063	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH, ODISHA ,	12/2013	319.80 320.00	320.00	-	05/2016 -	03/2017	-	0/0
1064	REHABILITATION AND UPGRADE OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH, ODISHA ,	07/2014	342.05 342.00	342.00	-	01/2017 -	-	-	0/0
1065	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH, ODISHA ,	08/2013	171.96 172.00	172.00	-	06/2016 -	-	-	0/0
1066	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA ,	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1067	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH, ODISHA ,	03/2014	162.51 163.00	163.00	-	05/2016 -	03/2017	-	0/0
1068	REHABILITATION AND UPGRADE BY 4-LANE OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA ,	03/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020	0(O) -	0/0
1069	REHABILITATION AND UPGRADE OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	-	07/2017 -	-	-	0/0
1070	REHABILITATION AND UPGRADE OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA ,	12/2017	686.65 -	686.65	-	-	-	-	0/0
1071	REHABILITATION AND UPGRADE OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA ,	12/2017	417.51 -	417.51	-	-	-	-	0/0
1072	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM 206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA ,	01/2018	953.09 -	953.09	-	-	-	-	0/0
1073	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA ,	01/2018	668.86 -	668.86	-	-	-	-	0/0
1074	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA ,	01/2018	633.68 -	633.68	-	-	-	-	0/0
1075	REHABILITATION AND UPGRADE OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA ,	01/2018	614.48 -	614.48	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1076	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	-	-	-	-	0/0
1077	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	-	-	-	-	0/0
1078	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	-	-	-	-	0/0
1079	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	-	-	-	-	0/0
1080	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	-	-	-	-	0/0
1081	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	-	-	-	0/0
1082	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	-	-	-	0/0
1083	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	-	-	-	0/0
1084	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	-	-	-	0/0
1085	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	-	01/2016	12/2017	-	0/0
1086	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	-	-	-	0/0
1087	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	-	-	-	0/0
1088	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	-	-	-	0/0
1089	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	-	-	-	0/0
1090	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	-	-	-	0/0
1091	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	-	-	-	0/0
1092	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	-	-	-	0/0
1093	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	-	-	-	0/0
1094	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1095	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	-	- -	11/2017	-	0/0
1096	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	-	- -	12/2017	-	0/0
1097	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	-	12/2017 -	12/2017	-	0/0
1098	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16(0) -	0/0
1099	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1100	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1101	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	- -	0/0
1102	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	- -	-	-	0/0
1103	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	-	03/2020 -	03/2020	0(0) -	0/0
1104	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	-	02/2010 -	-	-	0/0
1105	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	-	07/2013 -	10/2017	-	0/0
1106	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	-	03/2016 -	-	-	0/0
1107	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1108	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1109	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
1110	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
1111	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1112	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(0) -	0/0
1113	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	-	02/2018 -	02/2018	0(0) -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1114	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	-	09/2016 -	09/2017	-	0/0
1115	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	-	02/2018 -	02/2018	0(O) -	0/0
1116	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	-	07/2017 -	07/2017	-	0/0
1117	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	-	05/2017 -	-	-	0/0
1118	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	-	04/2017 -	-	-	0/0
1119	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	-	03/2018 -	03/2018	0(O) -	0/0
1120	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	10/2016	-	0/0
1121	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	206.78	05/2016 -	05/2016	-	0/0
1122	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6(O) -	0/0
1123	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	-	08/2016 -	-	-	0/0
1124	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
1125	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1126	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1127	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	-	10/2011 -	12/2017	-	0/0
1128	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	-	-	02/2018	-	0/0
1129	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0
1130	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(O) -	0/0
1131	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1132	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	688.70	-	-	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1133	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	-	- -	10/2018	- -	0/0
1134	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	-	- -	01/2019	- -	0/0
1135	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	-	- -	-	-	0/0
1136	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	-	- -	-	-	0/0
1137	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	-	- -	-	-	0/0
1138	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	-	04/2020 -	04/2020	0(O) -	0/0
1139	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	-	10/2017 -	-	-	0/0
1140	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	-	- -	-	-	0/0
1141	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
1142	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
1143	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1144	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	-	10/2017 -	10/2017	-	0/0
1145	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60(O) -	0/0
1146	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	319.76	06/2013 -	-	-	0/0
1147	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67(O) -	0/0
1148	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64(O) -	0/0
1149	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1150	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
1151	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
1152	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1153	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9(O) -	0/0
1154	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12(O) -	0/0
1155	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1156	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19(O) -	0/0
1157	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1158	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	129.75	-	08/2018	-	0/0
1159	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	74.13	-	07/2018	-	0/0
1160	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	-	03/2020 -	03/2020	0(O) -	0/0
1161	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	149.66	07/2016 -	07/2018	24(O) -	0/0
1162	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	-	08/2017 -	-	-	0/0
1163	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	-	09/2017 -	-	-	0/0
1164	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	-	09/2017 -	-	-	0/0
1165	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	-	-	-	-	0/0
1166	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	03/2018	18(O) -	0/0
1167	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1168	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4
1169	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1170	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
1171	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1172	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1173	REHABILITATION AND UPGRADE OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	-	0/1
1174	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	-	0/0
1175	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1176	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	- -	0/0
1177	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
1178	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	04/2017	-	0/4
1179	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,667.96	06/2013 -	09/2017	-	0/0
1180	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	08/2017	-	0/0
1181	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	679.73	09/2013 -	10/2017	-	0/0
1182	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	326.46	01/2014 -	12/2017	-	0/0
1183	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,850.00	09/2015 -	10/2017	-	0/0
1184	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
1185	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
1186	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1187	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13(O) -	0/0
1188	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	409.92	01/2016 -	11/2017	-	0/0
1189	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	-	0/0
1190	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	-	01/2016 -	-	-	0/0
1191	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	556.52	01/2016 -	11/2017	-	0/0
1192	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	-	0/0
1193	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1194	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	-	10/2016 -	10/2016	-	0/0
1195	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(O) -	0/0
1196	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	03/2017	-	0/0
1197	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	-	10/2016 -	10/2016	-	0/0
1198	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	-	0/0
1199	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	673.79	03/2018 -	03/2018	0(O) -	0/0
1200	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	567.30	03/2018 -	03/2018	0(O) -	0/0
1201	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	743.26	03/2018 -	03/2018	0(O) -	0/0
1202	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	773.95	03/2018 -	03/2018	0(O) -	0/0
1203	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	505.00	- -	01/2019	- -	0/0
1204	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	340.37	06/2016 -	06/2018	24(O) -	0/0
1205	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	130.35	06/2018 -	06/2018	0(O) -	0/0
1206	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	218.34	06/2018 -	06/2018	0(O) -	0/0
1207	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	184.20	07/2018 -	06/2018	-1(O) -	0/0
1208	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	222.05	06/2018 -	06/2018	0(O) -	0/0
1209	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1210	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1211	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
1212	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
1213	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	- -	05/2019	- -	0/0
1214	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	- -	0/0
1215	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	115.21	- -	04/2019	- -	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1216	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	9.62	- -	-	-	0/0
1217	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	4.10	- -	-	-	0/0
1218	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	24.95	- -	04/2019	-	0/0
1219	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	- -	04/2019	-	0/0
1220	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	-	- -	-	-	0/0
1221	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	-	- -	-	-	0/0
1222	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	-	- -	-	-	0/0
1223	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	-	0/0
1224	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	47.57	- -	-	-	0/0
1225	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	102.97	- -	-	-	0/0
1226	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020	0(O) -	0/0
1227	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020	0(O) -	0/0
1228	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020	0(O) -	0/0
1229	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020	0(O) -	0/0
1230	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	-	- -	-	-	0/0
1231	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	-	- -	-	-	0/0
1232	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	-	- -	-	-	0/0

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1233	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	-	-	-	-	0/0
1234	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	-	10/2013 -	12/2017	-	0/0
1235	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	-	-	-	0/0
1236	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	-	-	-	-	0/0
1237	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	-	-	07/2018	-	0/0
1238	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,426.29	08/2013 -	12/2017	-	0/0
1239	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55(O) -	0/0
1240	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,771.80	09/2014 -	12/2017	-	0/0
1241	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	551.12	07/2014 -	03/2018	44(O) -	0/0
1242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	03/2018	0(O) -	0/0
1243	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15	-	-	01/2018	-	0/0
1244	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	179.92	06/2018 -	06/2018	0(O) -	0/0
1245	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,313.68	-	12/2017	-	0/0
1246	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37	35.17	-	11/2018	-	0/0
1247	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL ,	09/2016	767.03 -	767.03	123.13	-	08/2018	-	0/0
	Total		3,48,802.18 -	3,54,959.79	56,826.05				23/182
	<u>SHIPPING AND PORTS</u>								
1248	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96(O) -	0/0
1249	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1250	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	12/2017	-	0/0
1251	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	98.60	06/2017 -	-	-	0/1
1252	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	.14	12/2017 -	12/2017	-	0/1

Detail of ongoing Projects Costing Rs. 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1253	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU ,	12/2014	274.85 -	274.85	43.83	04/2017 -	-	-	0/1
1254	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU ,	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	-	0/0
1255	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20(O) -	0/0
	Total		4,472.08 -	4,933.09	1,524.70				0/3
	<u>TELECOMMUNICATIONS</u>								
1256	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9(O) -	0/0
1257	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT , Central Sector Projects	09/2017	171.54 -	171.54	-	05/2018 -	05/2018	0(O) -	0/0
1258	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	159.30 -	159.30	-	04/2018 -	04/2018	0(O) -	0/0
1259	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	167.68 -	167.68	-	04/2018 -	04/2018	0(O) -	0/0
1260	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	212.70 -	212.70	-	05/2018 -	05/2018	0(O) -	0/0
1261	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 -	215.30	-	05/2018 -	05/2018	0(O) -	0/0
1262	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020	57(O) 0(R)	0/0
1263	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
1264	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH ,	11/2017	169.45 -	169.45	-	08/2018 -	08/2018	0(O) -	0/0
	Total		16,959.40 -	28,189.40	8,068.20				0/70
	<u>URBAN DEVELOPMENT</u>								
1265	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	116.59	03/2017 -	-	-	2/5
1266	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	- -	-	-	0/0
1267	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	-	03/2019 -	03/2019	0(O) -	0/7
1268	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36(O) -	0/0
1269	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24(O) -	0/0
1270	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	160.53	10/2019 -	03/2020	5(O) -	0/7

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1271	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	545.04	12/2015 -	03/2018	27(O) -	0/0
1272	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019	0(O) -	1/7
1273	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	4.16	-	04/2019	-	0/2
1274	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	-	-	-	-	0/0
1275	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	-	05/2020 -	05/2020	0(O) -	0/0
1276	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	-	06/2019 -	06/2019	0(O) -	0/0
1277	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	134.18	11/2014 -	10/2018	47(O) -	0/8
1278	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	39.91	03/2016 -	12/2018	33(O) -	1/6
1279	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13(O) -	0/0
1280	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020	0(O) -	0/0
1281	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65(O) 11(R)	0/1
1282	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29(O) -	0/0
1283	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	82.18	11/2015 05/2018	05/2018	30(O) 0(R)	0/0
1284	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	12/2016	164.00 -	164.00	79.25	01/2018 05/2018	05/2018	4(O) 0(R)	6/11
1285	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	296.50	03/2016 12/2017	04/2018	25(O) 4(R)	0/13
1286	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 -	170.62	149.22	03/2012 03/2018	06/2018	75(O) 3(R)	15/20
1287	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21(O) -	0/0
1288	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	-	-	0/0
1289	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44(O) -	0/10
1290	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	316.80	05/2017 02/2018	06/2018	13(O) 4(R)	7/12
1291	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	67.24	04/2019 06/2019	06/2019	2(O) 0(R)	3/8

Detail of ongoing Projects Costing Rs. 150 Crore and above.									
(All Cost/ Expenditure in Rs. Crore)									
						Date of Commissioning		(February 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1292	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	443.73	03/2015 12/2017	03/2018	36(O) 3(R)	0/0
1293	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU ,	04/2014	332.72 -	321.00	297.34	09/2016 03/2018	04/2018	19(O) 1(R)	0/0
1294	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU ,	02/2009	14,600.00 19,058.00	19,058.00	14,784.59	12/2015 -	12/2017	-	11/24
1295	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU ,	12/2015	209.00 -	209.00	19.54	- -	10/2019	- -	0/6
1296	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL, TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018	0(O) -	0/0
1297	CONSTRUCTION OF CENTRAL EXCISE DEPARTMENT AT CR COLONY - [N28000109]CPWD, TAMIL NADU ,	11/2017	348.77 -	348.77	-	- -	-	-	0/0
1298	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD, TELANGANA ,	10/2016	209.84 -	209.84	1.21	03/2020 -	03/2020	0(O) -	0/5
1299	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0(O) -	0/0
1300	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND ,	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70(O) -	0/0
1301	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL ,	02/2014	156.57 -	156.57	126.35	08/2016 -	06/2018	22(O) -	8/13
1302	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	47.29	04/2018 -	05/2019	13(O) -	2/6
	Total		1,42,480.14 -	1,47,511.23	62,587.40				56/171
	<u>DEFENCE PRODUCTION</u>								
1303	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA ,	12/2016	167.69 168.00	172.99	50.97	05/2018 -	05/2018	0(O) -	4/5
1304	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL, GOA ,	12/2016	285.95 286.00	296.05	44.22	08/2020 -	08/2020	0(O) -	3/3
	Total		453.64 -	469.04	95.19				7/8
	Grand Total		16,21,994.63	18,38,702.43	6,36,212.47				2146/3920


Summary of projects in the Flash Report for the month of February, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1304
Number of Projects completed/dropped/frozen in Current Month	32
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	33
Number of Projects in Current Month	1304

Brief Analysis

Project Status with respect to Original Schedule: Out of 1304 projects, 14 projects are ahead of schedule, 307 projects are on schedule 262 projects are delayed. 581 projects do not have fixed dates of commissioning. 140 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

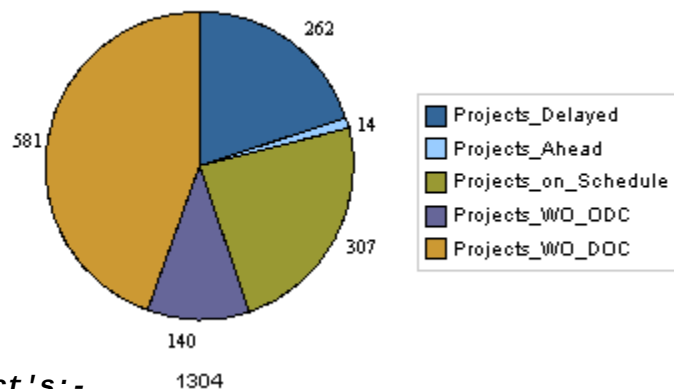


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1304 projects when sanctioned, was of the order of Rs. 1621994.63 crore but this was subsequently revised to Rs. 1838702.43 crore implying a cost overrun of 13.4%. The expenditure incurred on these projects till February, 2018 is Rs. 636212.47 crore, which is 34.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

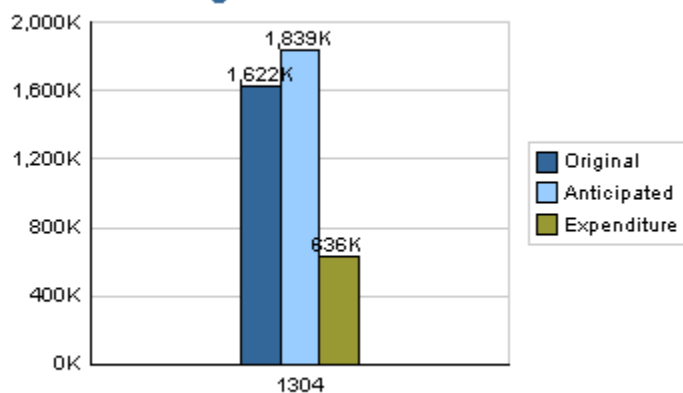

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.




Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 69728 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till February, 2018 is Rs. 27871.79 crore, which is 40% of the anticipated cost of the projects.

Figures are in Rs. Crore

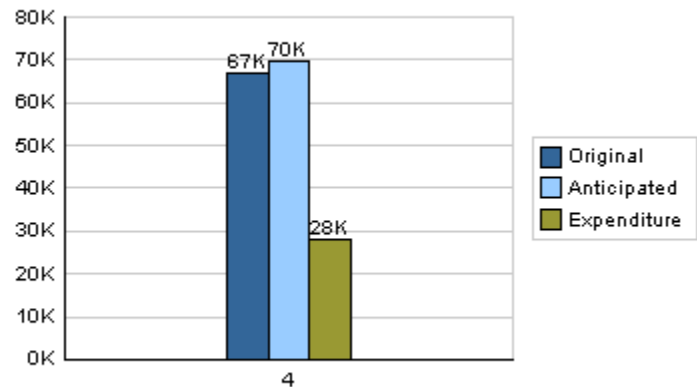

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

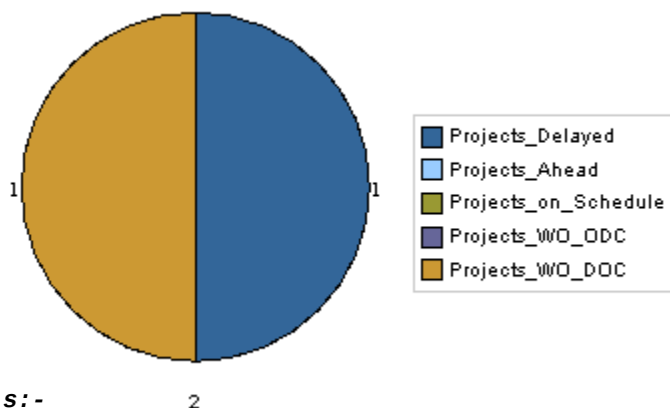


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till February, 2018 is Rs. 549.39 crore, which is 55.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

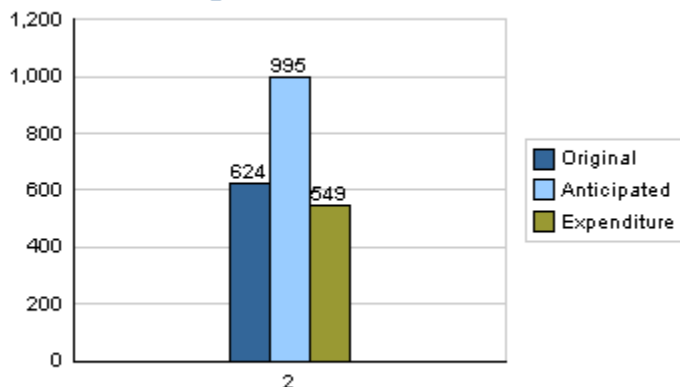

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	92
Number of Projects On Schedule	51
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 92 projects, 1 project is ahead of schedule, 51 projects are on schedule 37 projects are delayed. 3 projects do not have fixed dates of commissioning.

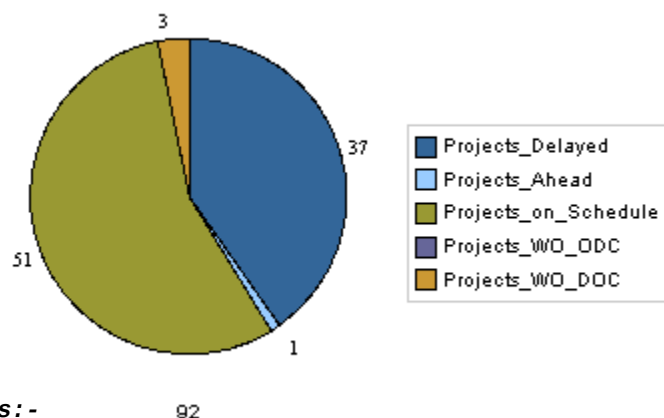


Total No Of Project's:-

92

Investment Scenario

Total original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 89695.08 crore but this was subsequently anticipated to Rs. 89199.09 cr The expenditure incurred on these projects till February, 2018 is Rs. 22736.55 crore, which is 25.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

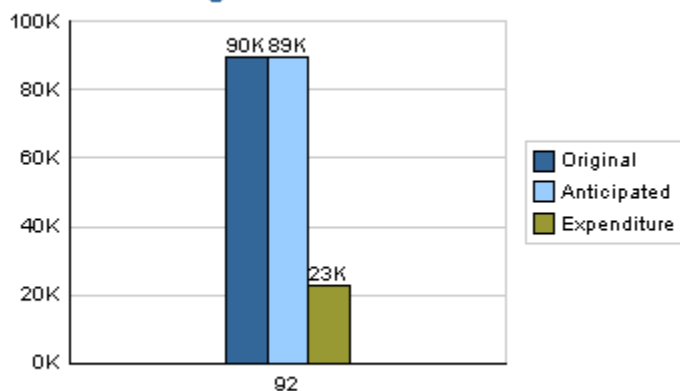

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule 2 projects are delayed.

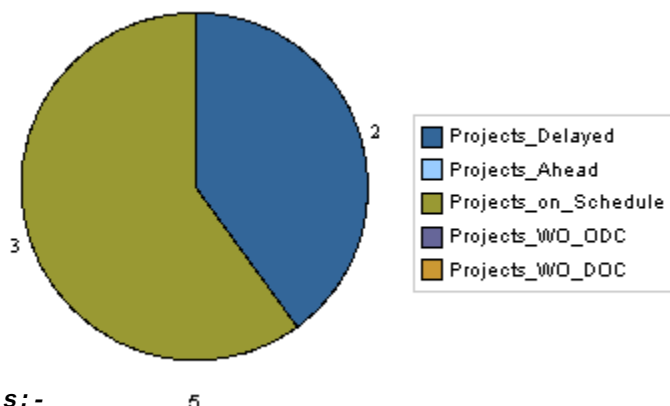


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1355.2 crore but this was subsequently anticipated to Rs. 1366.85 crore implying a cost overrun of .9%. The expenditure incurred on these projects till February, 2018 is Rs. 510.95 crore, which is 37.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

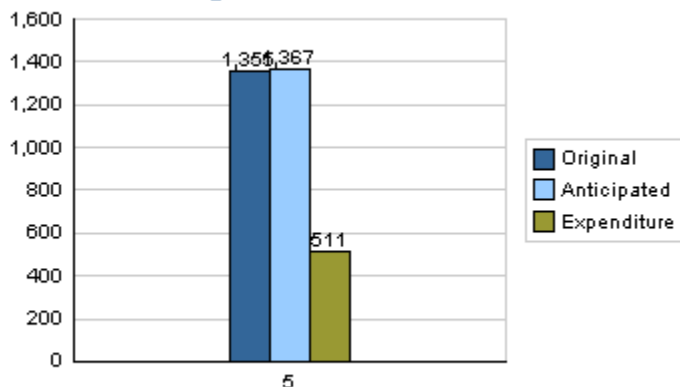

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule

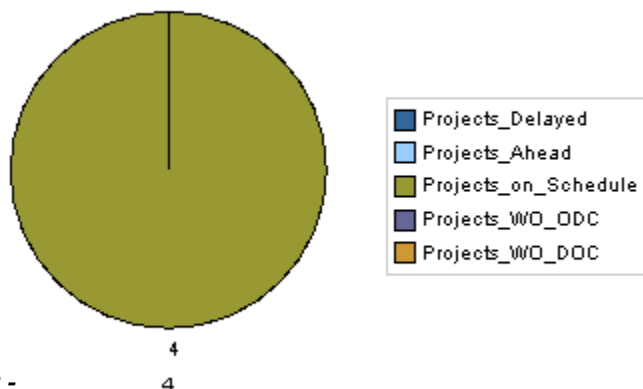


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till February, 2018 is Rs. 346.92 crore, which is 5% of the anticipated cost of the projects.

Figures are in Rs. Crore

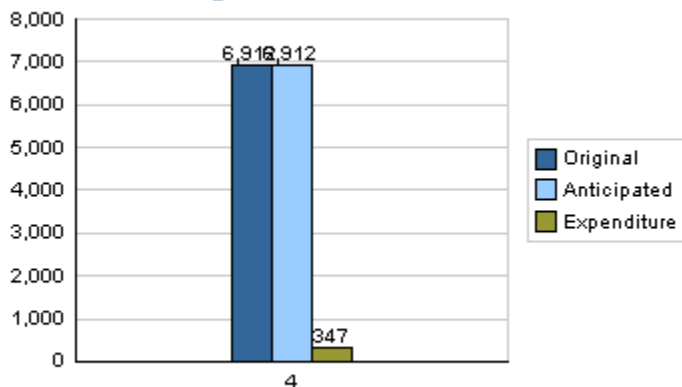

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	30
Number of Projects On Schedule	5
Number of Projects Delayed	15

Number of Projects Without Date Of Commissioning 10

Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 5 projects are on schedule 15 projects are delayed. 10 projects do not have fixed dates of commissioning.

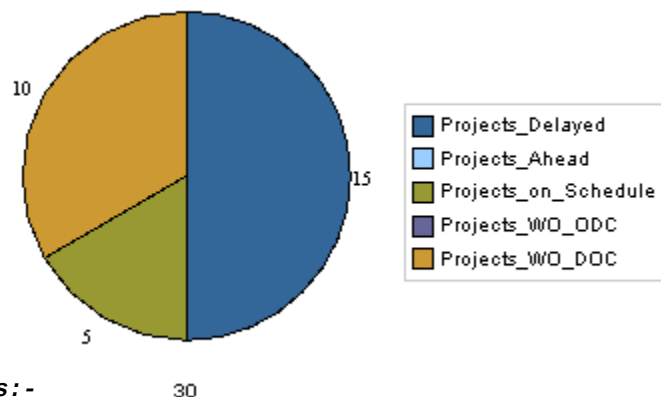


Total No Of Project's:-

30

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 54971.33 crore but this was subsequently anticipated to Rs. 55185.01 crore implying a cost overrun of .4%. The expenditure incurred on these projects till February, 2018 is Rs. 39907.62 crore, which is 72.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

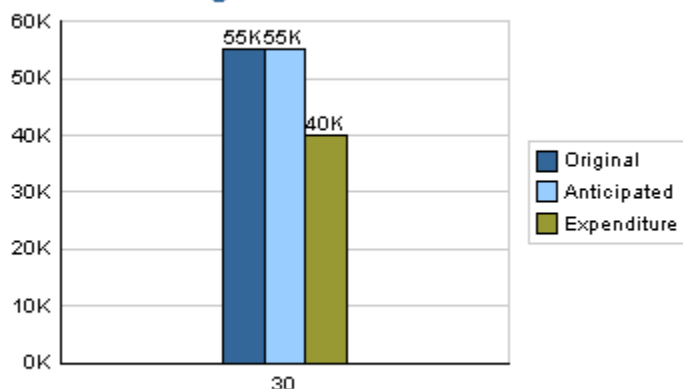

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	118
Number of Projects On Schedule	69
Number of Projects Delayed	29
Number of Projects Ahead	8
Number of Projects Without Date Of Commissioning	12

Brief Analysis

Project Status with respect to Original Schedule: Out of 118 projects, 8 projects are ahead of schedule, 69 projects are on schedule 29 projects are delayed. 12 projects do not have fixed dates of commissioning.

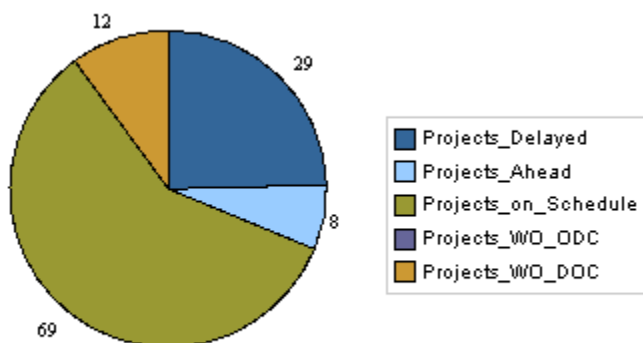


Total No Of Project's:-

118

Investment Scenario

Total original cost of implementation of 118 projects when sanctioned, was of the order of Rs. 203764.02 crore but this was subsequently anticipated to Rs. 205332.56 crore implying a cost overrun of .8%. The expenditure incurred on these projects till February, 2018 is Rs. 60072.6 crore, which is 29.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

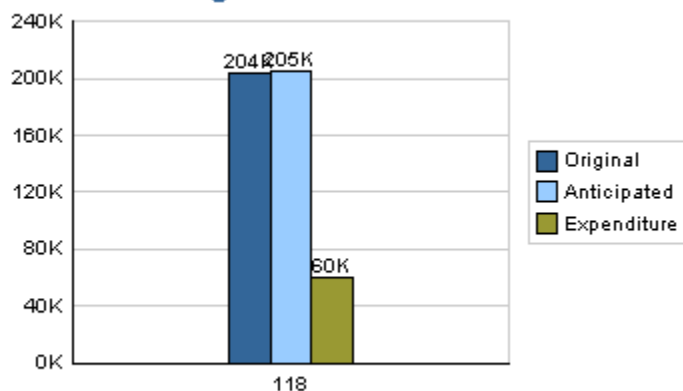

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	121
Number of Projects On Schedule	46
Number of Projects Delayed	65
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	8

Brief Analysis

Project Status with respect to Original Schedule: Out of 121 projects, 2 projects are ahead of schedule, 46 projects are on schedule 65 projects are delayed. 8 projects do not have fixed dates of commissioning.

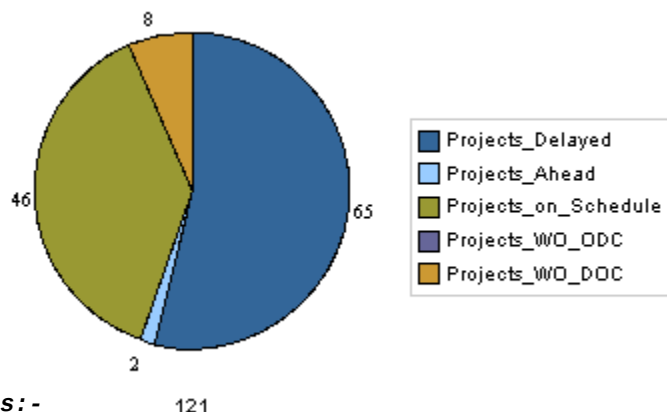


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 121 projects when sanctioned, was of the order of Rs. 337506.49 crore but this was subsequently anticipated to Rs. 404972.96 crore implying a cost overrun of 20%. The expenditure incurred on these projects till February, 2018 is Rs. 225943.04 crore, which is 55.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

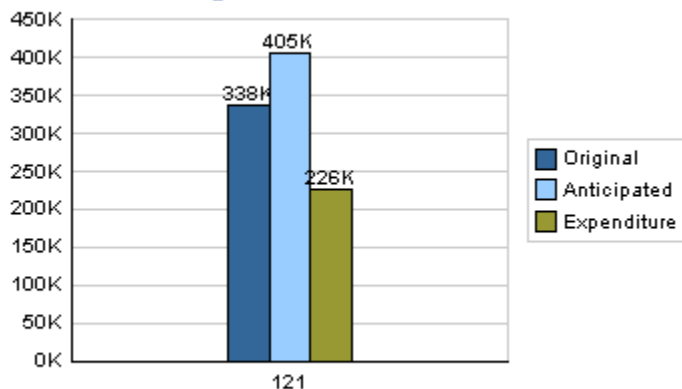

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.




Total No Of Project's:- 1

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till February, 2018 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

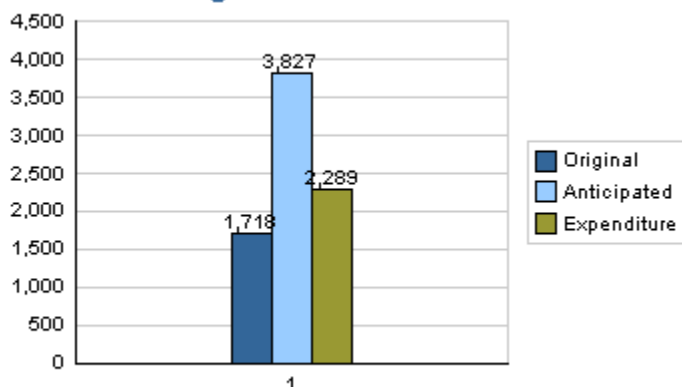

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	14
Number of Projects On Schedule	5
Number of Projects Delayed	6

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 5 projects are on schedule 6 projects are delayed. 3 projects do not have fixed dates of commissioning.

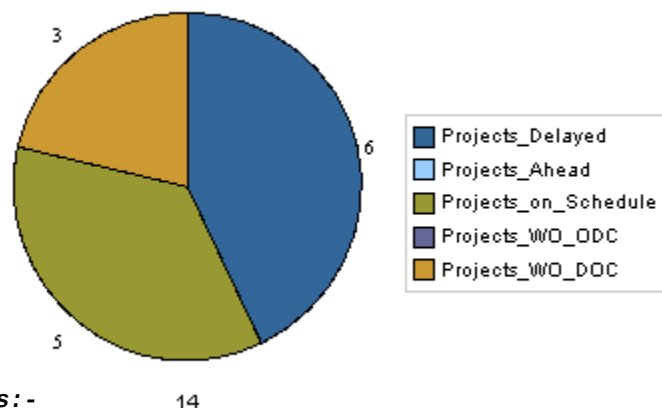


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 3897.21 crore but this was subsequently anticipated to Rs. 3919.69 crore implying a cost overrun of .6%. The expenditure incurred on these projects till February, 2018 is Rs. 1507.4 crore, which is 38.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

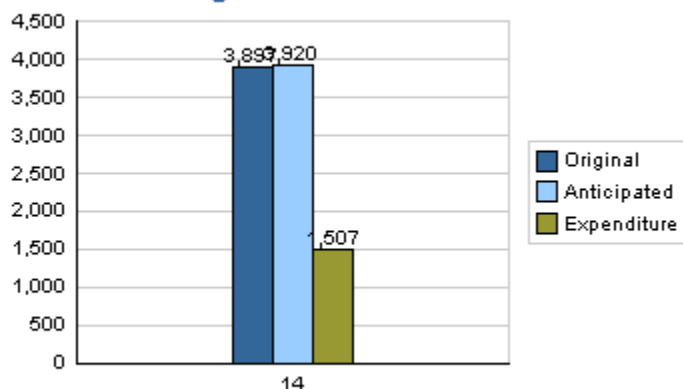

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	334
Number of Projects On Schedule	39
Number of Projects Delayed	29
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	77
Number of Projects Without Date Of Commissioning	188

Brief Analysis

Project Status with respect to Original Schedule: Out of 334 projects, 1 project is ahead of schedule, 39 projects are on schedule 29 projects are delayed. 188 projects do not have fixed dates of commissioning. 77 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

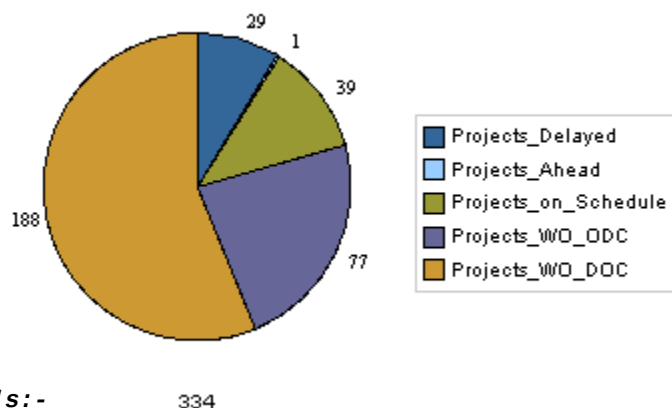


Total No Of Project's:-

334

Investment Scenario

Total original cost of implementation of 334 projects when sanctioned, was of the order of Rs. 341263.79 crore but this was subsequently anticipated to Rs. 461201.56 crore implying a cost overrun of 35.1%. The expenditure incurred on these projects till February, 2018 is Rs. 125375.67 crore, which is 27.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

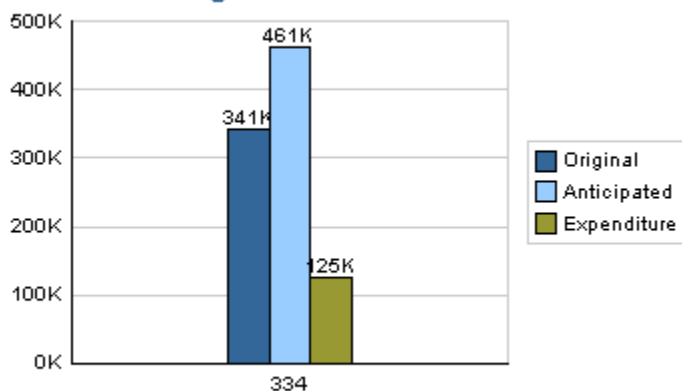

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	522
Number of Projects On Schedule	69
Number of Projects Delayed	48
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	61
Number of Projects Without Date Of Commissioning	342

Brief Analysis

Project Status with respect to Original Schedule: Out of 522 projects, 2 projects are ahead of schedule, 69 projects are on schedule 48 projects are delayed. 342 projects do not have fixed dates of commissioning. 61 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

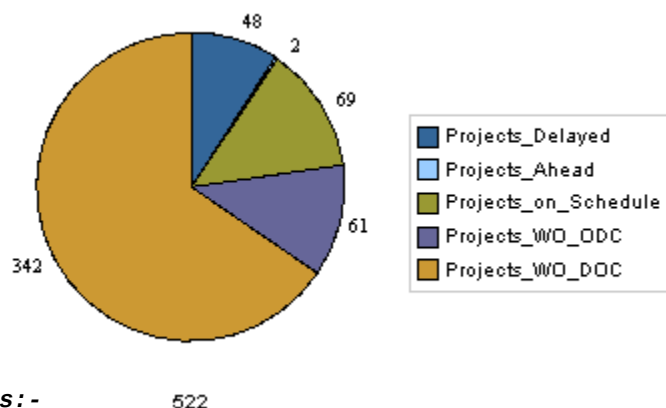


Total No Of Project's:-

522

Investment Scenario

Total original cost of implementation of 522 projects when sanctioned, was of the order of Rs. 348802.18 crore but this was subsequently anticipated to Rs. 354959.79 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till February, 2018 is Rs. 56826.05 crore, which is 16% of the anticipated cost of the projects.

Figures are in Rs. Crore

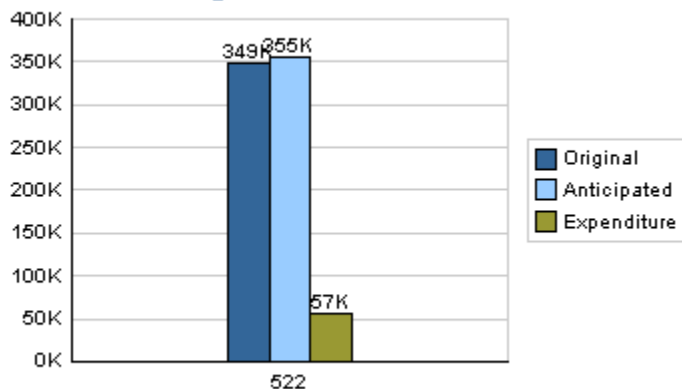

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects 8

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 6

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are delayed. 6 projects do not have fixed dates of commissioning.

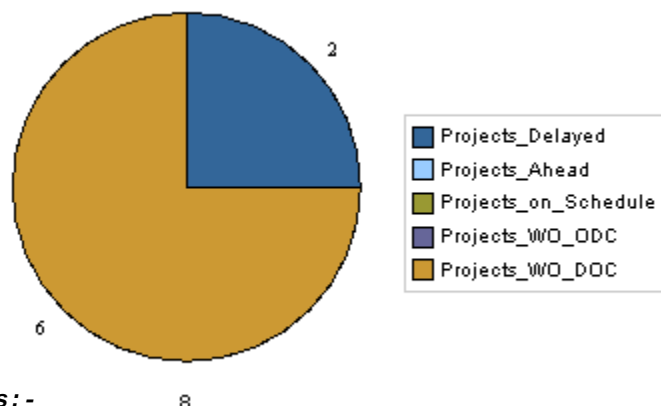


Total No Of Project's:-

8

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4472.08 crore but this was subsequently anticipated to Rs. 4933.09 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till February, 2018 is Rs. 1524.7 crore, which is 30.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

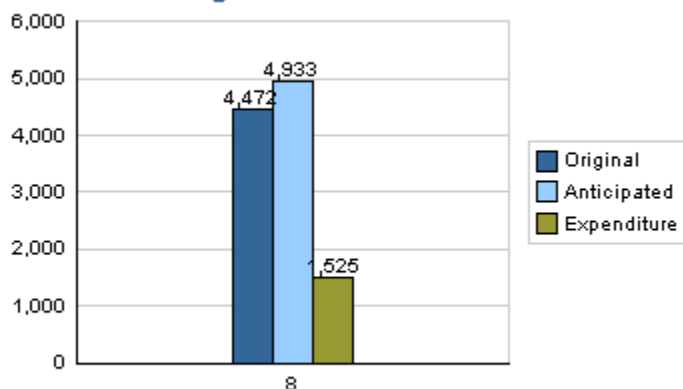

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	9
Number of Projects On Schedule	6
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 6 projects are on schedule 2 projects are delayed. 1 project does not have fixed dates of commissioning.

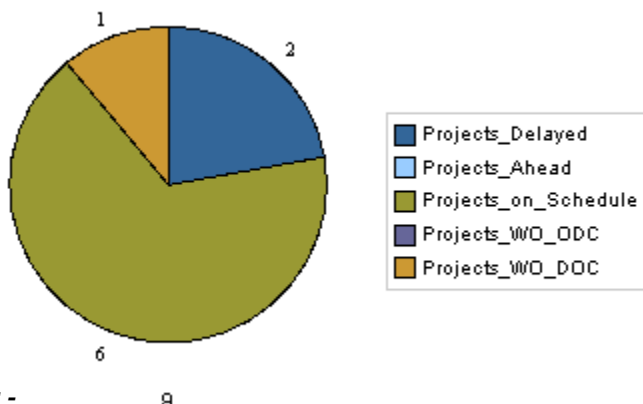


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 16959.4 crore but this was subsequently anticipated to Rs. 28189.4 crore implying a cost overrun of 66.2%. The expenditure incurred on these projects till February, 2018 is Rs. 8068.2 crore, which is 28.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

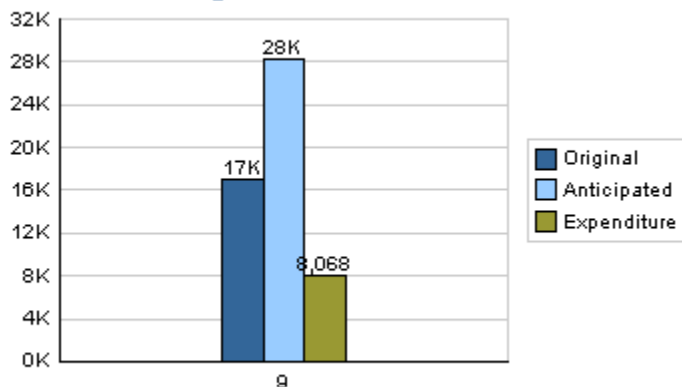

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	38
Number of Projects On Schedule	8
Number of Projects Delayed	22

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 38 projects, 8 projects are on schedule 22 projects are delayed. 6 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

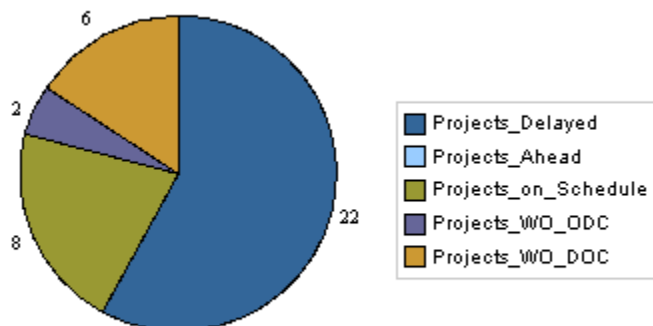


Total No Of Project's:-

38

Investment Scenario

Total original cost of implementation of 38 projects when sanctioned, was of the order of Rs. 142480.14 crore but this was subsequently anticipated to Rs. 147511.23 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till February, 2018 is Rs. 62587.4 crore, which is 42.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

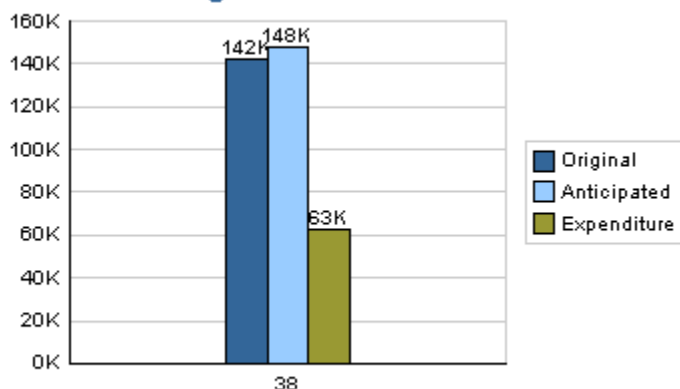

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

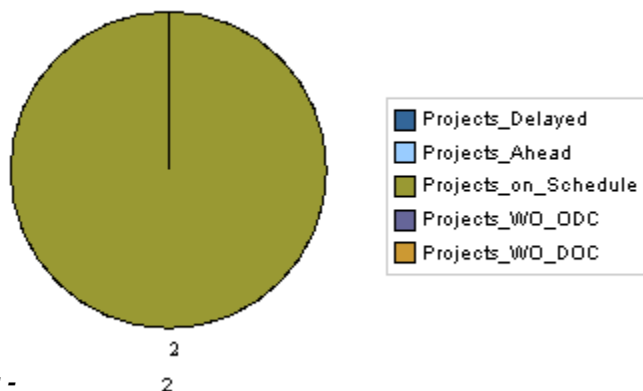


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 469.04 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till February, 2018 is Rs. 95.19 crore, which is 20.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

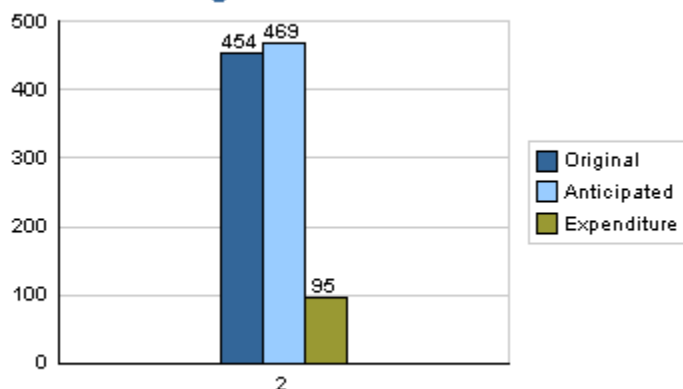

Annexure

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (FEBRUARY 2018)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	26.44
2	ANDHRA PRADESH	61	97,970.05	1,01,733.7	7,020.27
3	ARUNACHAL PRADESH	31	16,602.41	34,492.69	17,888.43
4	ASSAM	44	26,450.2	36,075.5	17,564.49
5	BIHAR	81	69,841.31	86,662.38	29,545.36
6	CHHATISGARH	38	84,027.14	86,630.08	48,982.97
7	D & N HAVELI	1	6,086.08	5,842.31	2,477.21
8	DELHI	17	52,999.22	53,266.53	38,876.42
9	GOA	9	4,043.51	4,058.91	176.4
10	GUJARAT	45	39,141.62	42,701.82	18,247.29
11	HARYANA	21	13,897.14	15,783.37	1,350.56
12	HIMACHAL PRADESH	12	14,659.32	22,591.6	7,055.07
13	JAMMU AND KASHMIR	11	28,880.41	57,111.68	23,482.39
14	JHARKHAND	47	47,354.89	51,864.52	19,442.96
15	KARNATAKA	41	70,570.56	80,140.31	28,126.12
16	KERALA	19	21,344.58	27,277.99	2,376.24
17	MADHYA PRADESH	61	64,127.43	70,184.36	20,880.65
18	MAHARASHTRA	126	1,79,252.77	1,92,299.71	66,757.08
19	MANIPUR	2	944.25	9,874.69	7,263.12
20	MEGHALAYA	6	7,108.02	9,025	285.36
21	MIZORAM	4	1,632.48	5,613.14	2,058.93
22	MULTI STATE	176	2,99,440.21	2,97,340.08	95,790.63
23	NAGALAND	7	8,126.79	10,276.79	428.38
24	ODISHA	79	81,238.38	89,983.41	21,078.19
25	PUNJAB	30	16,014.41	16,020.14	2,570.79
26	RAJASTHAN	59	44,137.4	45,593.7	13,419.94
27	SIKKIM	6	2,537.08	5,585.45	931.23
28	TAMIL NADU	65	1,09,383.31	1,25,212.01	47,994.22
29	TELANGANA	36	24,952.57	27,674.71	6,072.32
30	TRIPURA	11	4,400.64	9,067.42	6,023.34
31	UTTAR PRADESH	89	1,11,376.79	1,13,178.96	35,806.35
32	UTTARAKHAND	14	17,481.68	34,951.18	8,118.94
33	WEST BENGAL	54	55,657.37	70,146.96	38,094.38
TOTAL		1,304	16,21,994.63	18,38,702.43	6,36,212.47

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

CIVIL AVIATION

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	522.95

COAL

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	331.07
3	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	399.01
4	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	457.77	-	478.12
5	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	201.18
6	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	209.07
7	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	687.28	-	749.25

HEAVY INDUSTRY

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	1718	-	2289

PETROLEUM

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	961

POWER

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
11	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6652.65
12	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	9838.43
13	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3446
14	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	5233.88
15	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	573.99	1337.76	1556.85
16	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	232.34	-	246.94
17	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	297.33	346.79	375.94

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
18	KUDGI STPP STAGE 1	NTPC	01/2012	15166.19	-	15364
19	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	5353	-	6974.42
20	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	481.23
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
21	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	124.43	-	1013.26
23	AMRAVATI-NARKHER NL (CR)	CR	06/1994	663.01	668.34	710.31
24	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	304	-	535.96
25	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
26	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	900.05	-	980.99
27	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	-	967.96
28	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
29	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	856.94
30	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	155.74	164.36	969.17
31	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	4965.44
32	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	218.24	236.41	679.98
33	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	876.49
35	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
36	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	919.32
37	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	744.71	761.7
38	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
39	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	408.76	841.57
40	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.61
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	733	-	2842.53
42	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	1049.69	-	3544.3
43	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	-	320.46
44	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	613.71
45	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	722.65
46	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	956.23
47	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	301.64	-	1078.57
48	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	-	7211.12
49	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	349.66
50	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	120	-	210.67
51	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	272.46
52	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	183.23	-	488.99
53	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	364.21
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	283.95	495.4
55	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	261.7	-	348.52
56	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	743	-	1568.77
57	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	508.51
58	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	687.2	-	1027.36
59	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	404.19	-	1048.37
60	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1049.68
61	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	450.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
62	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	922.31
63	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	618.19
64	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	2550.24
65	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	1928.11
66	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	685.07
67	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	207.11
68	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	293.47
69	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	603.04	-	933.2
70	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
71	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	424.76
72	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	240.37
73	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
74	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	468.18
75	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	822.39	-	1679.05
76	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1504.5
77	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	613.01
78	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	283.55	-	345.63
79	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	378.76
80	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	523.17	-	1084.45
81	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	532.42
82	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	456.58
83	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	179.65	-	815.65
84	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	568.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
85	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	155.81	-	156.11
86	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	225.68
87	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	190.1	-	308.9
88	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
89	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
90	MURADABAD-BAREILY	NHAI	04/2010	1267	-	2667.96
91	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2070.65
92	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1986.56
93	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.31
94	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	582.52
95	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1155.31
96	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2426.29
97	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	998.79	-	1945.82
98	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2771.8
99	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	326.46
100	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1850
101	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1792.9
102	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1375.6
103	2-LANING WITH PAVED SHOULDERS OF RAEARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	409.92
104	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEARELI	NHAI	04/2014	495.78	-	556.52
105	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1479.14
106	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(FEBRUARY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
107	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2848.31
108	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2104.55
109	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	2313.68
110	TRICHY - KARUR	NHAI	03/2007	516	-	761.19

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
111	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12

STEEL

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
112	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	17265	-	18560.44
113	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
114	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	14.08	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	72.66	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52	247.52	88.97	02/2019 -	12/2018
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	240.15	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00	356.00	109.51	05/2019 -	12/2018
	Total		10,668.92 -	10,668.92	720.34		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	124.71	05/2018 -	03/2018
8	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	105.62	07/2018 -	03/2018
	Total		369.99 -	369.99	230.33		
	<u>RAILWAYS</u>						
	<u>East Coast Railway</u>						
9	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92	1,172.92	122.87	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	122.87		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
10	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	184.20	07/2018 -	06/2018
11	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	23.87	03/2020 -	05/2019
	Total		963.19 -	921.00	208.07		

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		13,175.02	13,132.83	1,281.61		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	182.02	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	288.00	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	41.80	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	371.19	03/2021 -	03/2021
6	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	25.64	03/2019 -	03/2019
7	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026
8	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
9	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	30.12	03/2019 -	03/2019
	<u>Neyveli Lignite Corporation</u>						
10	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,309.20	11/2021 -	11/2021
11	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	6.22	09/2019 -	09/2019
12	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	168.58	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
13	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	434.36	03/2018 -	03/2018
14	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	28.21	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
15	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
16	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	72.81	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
17	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	44.19	03/2020 -	03/2020
19	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	0.99	03/2023 -	03/2023
20	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,634.97	03/2023 -	03/2023
22	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023
23	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	51.12	03/2020 -	03/2020
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	29.37	03/2022 -	03/2022
25	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
26	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
27	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023
28	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
29	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,669.22	03/2023 -	03/2023
30	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021
31	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	50.54	03/2018 -	03/2018
32	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021
	<u>Western Coal Fields Limited</u>						
33	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
34	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021
35	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.03	03/2023 02/2017	03/2023
36	GOKUL - [N06000120]	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018
37	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	73.88	03/2021 -	03/2021
38	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	139.76	03/2021 -	03/2021
39	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	0.04	03/2022 -	03/2022
40	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	46.91	03/2020 -	03/2020
41	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	94.00	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.26	03/2020 -	03/2020
43	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	86.78	03/2021 -	03/2021
44	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	371.19	03/2020 -	03/2020
45	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	237.08	03/2020 -	03/2020
46	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
47	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
48	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.30	03/2022 -	03/2022
49	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	0.13	03/2022 -	03/2022
50	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.84	03/2019 -	03/2019
51	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	231.76	03/2025 -	03/2025
	Total		66,658.54 -	66,926.41	10,509.49		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
52	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	44.22	08/2020 -	08/2020
53	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	50.97	05/2018 -	05/2018
	Total		453.64 -	469.04	95.19		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
54	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	-	11/2019 -	11/2019
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	-	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	-	11/2019 -	11/2019
	Total		674.56 -	674.56	.00		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
57	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
58	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
60	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
61	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
	Total		1,458.52 -	1,458.52	302.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
62	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	288.44	01/2020 01/2020	01/2020
63	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	13.88	11/2020 11/2020	11/2020
64	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
65	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	44.60	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	346.92		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
66	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	21.08	01/2019 -	01/2019
67	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	259.17	04/2018 -	04/2018
68	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	65.87	08/2018 -	08/2018
69	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	45.12	02/2020 -	02/2020
70	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	99.26	12/2019 -	12/2019
71	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	253.60	10/2018 -	10/2018
	<u>Chennai Petroleum Corporation Limited</u>						
72	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	144.26	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	1.15	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
74	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	14.08	12/2019 12/2020	12/2019
75	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	42.30	12/2020 -	12/2020
76	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	11.32	12/2020 -	12/2020
77	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	1,771.65	12/2018 -	12/2018
78	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	7.80	07/2022 -	07/2022
79	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	39.40	04/2022 -	04/2022
80	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	564.98	02/2020 -	02/2020
81	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	5.73	12/2020 -	12/2020
82	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	60.27	12/2020 -	12/2020
83	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	144.58	03/2018 -	03/2018
84	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	750.00	514.17	12/2018 -	12/2018
	<u>Hindustan Petroleum Corporation Limited</u>						
85	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	27.90	02/2019 -	02/2019
86	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	52.19	09/2019 -	09/2019
87	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	412.08	06/2020 -	06/2020
88	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
89	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	5.87	03/2021 -	03/2021
	<u>Indian Oil Corporation Limited</u>						
90	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	296.05	10/2019 -	10/2019
91	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	28.93	04/2020 -	04/2020
92	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
93	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	133.17	01/2019 -	01/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
94	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	-	09/2019 -	09/2019
95	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	34.75	09/2019 -	09/2019
96	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	0.84	10/2020 -	10/2020
97	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	117.83	08/2019 -	08/2019
98	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
99	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
100	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	74.03	12/2018 -	12/2018
101	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	390.95	11/2018 -	11/2018
102	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
103	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	6.02	04/2021 -	04/2021
104	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
105	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
106	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
107	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	32.47	06/2020 -	06/2020
108	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
109	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS & HSD, ADDITIONAL TANKS FOR MS, HSD AND BI - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
110	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	8.35	12/2020 -	12/2020
111	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,103.82	06/2018 -	06/2018
112	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	445.91	11/2019 -	11/2019
113	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	23.16	02/2020 -	02/2020
114	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.99	12/2019 -	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	26.19	07/2020 -	07/2020
116	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
117	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	196.31	12/2020 -	12/2020
118	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	282.15	08/2021 -	08/2021
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
119	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	96.38	03/2019 -	03/2019
120	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	80.45	12/2019 -	12/2019
121	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	66.12	04/2019 -	04/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
122	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020
123	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018
124	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
125	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 11/2019	11/2019
126	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	1,314.87	04/2018 04/2018	04/2018
127	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	161.79	09/2018 09/2018	09/2018
128	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 11/2019	11/2019
129	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	140.80	05/2019 05/2019	05/2019
130	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020
131	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	216.56	03/2026 03/2026	03/2026
132	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	170.86	05/2021 -	05/2021
	<u>Oil India Limited</u>						
133	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.30	12/2019 -	12/2019
134	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.42	10/2020 -	10/2020
	Total		1,20,409.71 -	1,19,647.54	11,056.11		

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
135	50 MW SOLAR POWER PROJECT - [N18000251]	6/2017	287.48 -	287.48	110.15	03/2018 -	03/2018
	<u>National Thermal Power Corporation</u>						
136	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	4,433.00	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						
137	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
138	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	866.47	07/2018 -	07/2018
139	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	455.95	12/2018 -	12/2018
140	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
141	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	910.61	05/2019 -	05/2019
142	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019
143	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	1,042.50	07/2018 -	07/2018
144	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	114.89	04/2019 -	04/2019
145	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
146	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	17.19	02/2019 -	02/2019
147	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	7.96	06/2019 -	06/2019
148	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	60.44	11/2018 -	11/2018
149	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	48.78	04/2019 -	04/2019
150	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	70.63	02/2019 -	02/2019
151	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	29.17	02/2020 -	02/2020
152	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	8.59	07/2019 -	07/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
153	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	14.44	09/2018 -	09/2018
154	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	1,415.00	04/2019 -	04/2019
155	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	139.00	07/2020 -	07/2020
156	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	761.00	06/2018 -	06/2018
157	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	191.54	05/2018 -	05/2018
158	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	75.73	02/2019 -	02/2019
159	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALLAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	1.76	06/2019 -	06/2019
160	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	42.66	02/2019 -	02/2019
161	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.59	03/2019 -	03/2019
162	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	290.24	01/2019 -	01/2019
163	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	182.24	04/2018 -	04/2018
164	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	90.51	06/2018 -	06/2018
165	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	9.11	09/2019 -	09/2019
166	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	363.47	06/2019 -	06/2019
167	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	192.91	11/2018 -	11/2018
168	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
169	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	96.34	10/2018 -	10/2018
170	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	62.63	03/2018 -	03/2018
171	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	98.07	12/2018 -	12/2018
172	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH-II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	11.35	03/2019 -	03/2019
173	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020
174	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	183.83	04/2019 -	04/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
175	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	48.37	07/2018 -	07/2018
176	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	3,707.22	04/2018 -	04/2018
177	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	992.21	11/2019 -	11/2019
178	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	193.70	03/2019 -	03/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
179	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	85.72	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
180	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	39.79	09/2020 -	09/2020
	Total		70,547.32 -	71,825.84	17,911.02		
	<u>RAILWAYS</u>						
	<u>Container Corporation Of India</u>						
181	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	385.61	03/2018 -	03/2018
182	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	0.39	03/2019 -	03/2019
183	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	241.05	03/2019 -	03/2019
184	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	149.15	03/2018 -	03/2018
185	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	121.35	03/2019 -	03/2019
186	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	257.28	03/2019 -	03/2019
187	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	20.03	03/2019 -	03/2019
188	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	217.53	03/2019 -	03/2019
189	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	375.37	03/2018 -	03/2018
	<u>East Central Railways</u>						
190	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	119.12	03/2020 -	03/2020
191	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
192	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
	<u>East Coast Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
193	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
194	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	71.55	03/2021 -	03/2021
195	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	53.02	03/2021 -	03/2021
	<u>North Central Railway</u>						
196	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
197	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	50.86	03/2022 -	03/2022
	<u>Rail India Technical And Economic Service</u>						
198	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
199	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	32.37	12/2025 -	12/2025
200	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.16	12/2025 -	12/2025
201	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	729.73	12/2020 -	12/2020
202	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,356.10	03/2020 -	03/2020
203	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	766.30	12/2020 -	12/2020
204	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	695.29	03/2020 -	03/2020
205	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	748.08	03/2020 -	03/2020
206	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	845.10	03/2019 -	03/2019
207	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	830.06	03/2019 -	03/2019
208	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	45.79	12/2024 -	12/2024
209	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	22.91	12/2024 -	12/2024
210	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	574.09	12/2026 -	12/2026
	<u>South Central Railway</u>						
211	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						
212	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>South Eastern Railway</u>						
213	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	-	12/2021 -	12/2021
214	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
215	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	-	12/2021 -	12/2021
216	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021
	<u>West Central Railway</u>						
217	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
218	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
219	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
	Total		44,682.64 -	58,420.30	9,085.89		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
220	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
221	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
222	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
223	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
224	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
225	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
226	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
227	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
228	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
229	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
230	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
231	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
232	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
233	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
234	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
235	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
236	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
237	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
238	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
National Highways Authority Of India							
239	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
240	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
241	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
242	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
243	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
244	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
245	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
246	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	567.30	03/2018 -	03/2018
247	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
248	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
249	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	673.79	03/2018 -	03/2018
250	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
251	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
252	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
253	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	6.00	02/2020 -	02/2020
254	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	130.35	06/2018 -	06/2018
255	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
256	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	218.34	06/2018 -	06/2018
257	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
258	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	179.92	06/2018 -	06/2018
259	FOUR LANING OF PARWANOO - SOLAN - [N24000479]	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
260	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
261	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
262	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
263	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
264	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
265	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
266	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
267	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
268	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
269	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
270	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
271	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
272	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	222.05	06/2018 -	06/2018
273	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020
274	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
275	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
276	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	773.95	03/2018 -	03/2018
277	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
278	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	743.26	03/2018 -	03/2018
279	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
280	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
281	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
282	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
283	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
National Highways Development Project							
284	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
285	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
286	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
Public Works Dept Of State							
287	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
288	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
	Total		51,710.60 -	52,412.71	4,039.80		
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
289	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
290	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	<u>National Mineral Development Corporation (Nmhc)</u>						
291	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
292	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
293	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	38.51	06/2019 -	06/2019
	Total		1,706.06 -	1,706.06	454.72		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
294	UP (EAST) ACCESS LOT1 - [N26000112	11/2017	169.45 -	169.45	-	08/2018 -	08/2018
295	MADHYA PRADESH ACCESS (LOT1) - [N26000110	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
296	GUJARAT ACCESS (LOT 1) - [N26000111	9/2017	171.54 -	171.54	-	05/2018 -	05/2018
297	MAHARASHTRA CORE (LOT1) - [N26000108	8/2017	167.68 -	167.68	-	04/2018 -	04/2018
298	MAHARASHTRA ACCESS (LOT 1) - [N26000109	8/2017	212.70 -	212.70	-	05/2018 -	05/2018
299	MAHARASHTRA NODAL (LOT 1) - [N26000107	8/2017	159.30 -	159.30	-	04/2018 -	04/2018
	Total		1,095.97 -	1,095.97	.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
300	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108	1/2018	206.58 -	206.58	-	03/2019 -	03/2019
301	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	1.21	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
302	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020
303	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	-	06/2019 -	06/2019
304	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
	<u>Chennai Metro Rail Ltd</u>						
305	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
	<u>Lucknow Metro Rail Corporation Limited</u>						
306	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>National Building Construcion Corporation Ltd</u>						
307	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019
	Total		16,051.29 -	15,905.29	5,532.64		
	Grand Total		3,82,360.85	3,97,454.24	59,334.13		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	02/2018	11.60
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
	<u>Singareni Colliers Company Limited</u>						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
9	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
	<u>South-Eastern Coal Fields Limited</u>						
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
	Total		19,751.90 -	21,090.72			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
13	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	3.16
14	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.53
	Total		453.64 -	469.04			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	03/2018	13.31
	Total		168.90 -	191.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natip Implementation Society</u>						
17	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
18	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50
19	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
20	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
21	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
22	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	06/2018	45.67
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
24	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
25	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	5,725.50	04/2016 -	03/2018	38.82
26	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87
27	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
28	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	11/2018	45.83
29	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
30	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
31	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
32	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47
33	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	05/2018	12.15
34	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
	Total		24,600.91 -	31,035.49			
	<u>POWER</u>						
	<u>Damodar Valley Corporation</u>						
35	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202 <u>National Hydro-Electric Power Corporation</u>	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80
37	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
38	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
39	KISHANGANGA HEP (3X110 MW) - [N18000031 <u>National Thermal Power Corporation</u>	01/2009	3,642.04 -	5,882.01	01/2016 -	03/2018	61.50
40	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
41	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
42	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	8,150.00	09/2011 -	06/2018	86.27
43	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
44	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
45	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
46	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91
47	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
48	KUDGI STPP STAGE 1 - [N18000131	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
51	KHARGONE STPP STAGE I (1320 MW) - [N18000205	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
52	PAKRI BARWADIH COAL MINING PROJECT - [N18000225 <u>North East Electric Power Corporation</u>	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
53	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51
54	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06
55	TRIPURA GAS BASED POWER PROJECT - [N18000071 <u>Power Grid Corporation Of India Limited</u>	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
56	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
57	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2018	5.14
58	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]	04/2010	4,404.57 -	5,135.01	01/2015 -	11/2018	16.58
59	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2018	23.65
60	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2018	36.79
61	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2018	38.61
62	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2018	5.34
63	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	03/2018	32.69
64	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37
65	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	04/2018	14.60
66	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2018	26.82
67	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92
68	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	03/2018	36.01
69	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	03/2018	46.77
70	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30
71	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	03/2019	31.17
72	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37
73	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	882.13	11/2014 -	03/2018	21.90
75	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	06/2018	36.74
76	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
77	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
78	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	<u>Satluj Jal Vidyut Nigam Limited</u>						
79	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
80	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75
81	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	11/2020	52.10
82	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	12/2020	165.65
	Total		1,80,865.02 -	2,48,331.49			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
83	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	- -	03/2023	534.55
84	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	03/2021	185.52
85	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	03/2019	8.18
86	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	03/2022	81.31
87	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	03/2021	341.34
88	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	29.56
89	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	- -	03/2024	120.28
90	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	- -	03/2024	25.04
91	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	03/2022	101.93
92	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	03/2023	5.33
93	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	03/2023	10.94
94	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	03/2023	21.21
	<u>East Central Railways</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
95	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
96	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
97	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
98	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
99	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
100	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
101	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
102	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
<u>East Coast Railway</u>							
103	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	12/2022	137.80
104	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
105	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
106	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
107	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
108	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
109	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
110	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
111	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
112	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
<u>Eastern Railways</u>							
113	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
114	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
115	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
116	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
117	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	493.96 -	681.68	- -	-	38.00
118	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	04/2010	423.66 -	720.59	03/2017 -	-	70.09
119	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	259.23	- -	-	3.31
120	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	-	6.48
121	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
122	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119	04/1999	207.52 -	334.87	12/2012 -	-	61.37
123	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.60	- -	-	51.49
124	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	1,130.13	- -	-	23.38
125	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	332.14	- -	-	27.07
	<u>Metropolitan Rapid Transport Projects</u>						
126	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
127	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
128	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
129	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
130	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
131	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
132	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
133	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
134	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
135	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
	<u>North East Frontier Railway</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
136	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	1,568.48
137	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
138	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
139	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
140	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
141	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
142	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2020	290.00
143	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,135.00	- -	03/2020	611.67
144	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
145	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
146	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	03/2020	27.24
147	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
148	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
149	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
150	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
151	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
152	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
153	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
154	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	03/2020	94.45
155	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
156	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
157	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
158	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
159	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
160	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
161	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	03/2020	10.01
<u>North Eastern Railway</u>							
162	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	- -	04/2018	88.85
163	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
164	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37
165	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
166	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
167	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	- -	-	.33
168	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	- -	08/2018	10.26
169	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	03/2018	142.44
170	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	227.00	- -	08/2018	13.64
171	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	- -	10/2018	61.80
172	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
<u>North Western Railway</u>							
173	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02
174	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	- -	02/2019	93.87
175	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	- -	03/2020	14.33
176	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84
177	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	- -	03/2019	41.64

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
178	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	- -	-	23.02
179	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	- -	10/2018	24.47
180	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	- -	02/2019	14.35
181	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	- -	10/2018	19.86
182	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	- -	03/2019	44.16
	<u>Northern Railway</u>						
183	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
184	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
185	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
186	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
187	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
188	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
189	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
190	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
191	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
192	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
193	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
194	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	157.10
195	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
196	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
197	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
198	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
199	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
200	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,141.70	12/2012 -	-	275.56
201	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82
202	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
203	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	350.00	- -	03/2018	84.11
204	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
205	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
206	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	- -	12/2020	22.24
207	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	- -	03/2018	120.09
208	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
209	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	-	9.32
210	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
211	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
212	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
213	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	12/2026	277.53
214	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
215	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
216	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	<u>Railway Electrification</u>						
217	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
218	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
219	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
220	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
221	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
222	GUDUR-DURGARA JAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
223	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
224	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	607.70	01/1999 -	-	94.00
225	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	-	520.89
226	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
227	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	-	284.00
228	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
229	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
<u>South East Central Railway</u>							
230	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
231	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
232	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
<u>South Eastern Railway</u>							
233	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
234	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
235	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
236	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
237	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	491.33	06/2004 -	-	153.17
238	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
239	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
240	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
241	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
242	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
243	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
244	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	-	41.36
245	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
246	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
247	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	<u>South Western Railway</u>						
248	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
249	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
250	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
251	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
252	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
253	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
254	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
255	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
256	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
257	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
258	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
259	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
	<u>Southern Railway</u>						
260	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
261	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
262	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
263	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
264	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
265	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	- -	-	404.39
266	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	- -	-	411.93
267	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	- -	-	147.28
268	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
269	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
270	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
271	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
272	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
273	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
274	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
275	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	- -	-	199.29
276	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
<u>West Central Railway</u>							
277	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	476.13
278	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
<u>Western Railway</u>							
279	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
280	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
281	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	04/2008	1,389.62 -	2,446.85	03/2014 -	-	76.08
282	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
283	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	844.10	- -	-	91.89
284	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	- -	03/2019	167.87
285	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	-	27.06
	Total		1,24,325.95 -	3,04,734.19			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
286	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
287	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
288	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26
289	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
290	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
291	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06
292	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	-	.02
293	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
294	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
295	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	<u>National Highways Authority Of India</u>						
296	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2018	28.93
297	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
298	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [N240106280	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
299	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	03/2018	68.99
300	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
301	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	04/2018	42.25
302	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
303	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56
304	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
305	FOUR LANING OF GWALIOR-SHIPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
306	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
307	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
308	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
309	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
310	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
311	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
312	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
313	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
314	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
315	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
316	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
317	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
318	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
319	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
	<u>Public Works Dept Of State</u>						
320	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
321	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
322	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
323	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
324	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
325	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	31.78
326	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
327	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
	Total		24,613.28 -	31,456.93			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
328	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	-	18.20
329	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
	<u>Mumbai Port Trust</u>						
330	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
331	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		959.83 -	1,762.94			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
332	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2017	12.04
333	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
334	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
335	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Rastriya Ispat Nigam Limited</u>						
336	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,639.71 -	2,211.39			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
337	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
338	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	04/2018	44.75
339	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
340	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	03/2018	37.10
341	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
342	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Chennai Metro Rail Ltd</u>						
343	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2017	30.53
	Total		17,021.00 -	22,244.19			
	Grand Total		4,13,766.00	6,99,323.36			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (February 2018)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,566.79	09/2010 09/2016	06/2018	93	74.68	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	11,285.00	12/2015 11/2016	11/2019	47	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,887.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	69,728.00	27,871.79					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	40.28	
	Total		314.61 -	441.33	26.44					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
6	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	161.38	05/2014 -	04/2018	47	0	
7	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	163.95	04/2014 -	04/2018	48	0	
8	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
9	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	273.25	04/2015 -	04/2019	48	0	
	<u>Central Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	347.96	03/2016 -	03/2018	24	0	
11	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84	0	
12	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	154.01	03/2012 -	03/2019	84	0	
13	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60	0	
14	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	0	
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	120.77	07/2012 -	03/2021	104	0	
	<u>Eastern Coal Fields Limited</u>									
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	336.18	03/2018 -	03/2020	24	0	Rehabilitation of PAFs- Process of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
17	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	331.07	03/2010 -	03/2018	96	0	
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	299.61	03/2017 -	05/2018	14	0	
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	478.12	03/2013 -	11/2018	68	0	
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	201.18	03/2010 -	03/2019	108	0	
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	209.07	03/2012 -	03/2019	84	0	
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	222.60	03/2013 -	03/2019	72	0	
	<u>Neyveli Lignite Corporation</u>									
23	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	767.00	749.25	06/2017 12/2017	02/2018	8	11.6	
24	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	5,170.78	12/2015 04/2018	04/2018	28	0	
25	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	340.71	06/2015 09/2019	09/2019	51	-51.37	
	<u>Northern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
26	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	486.57	399.01	03/2012 -	03/2018	72	87.58	
	<u>Singareni Colliers Company Limited</u>									
27	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36	0	
28	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	0	
29	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33	0	
30	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	415.37	149.50	03/2016 -	03/2018	24	-3.5	
31	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	448.86	185.65	03/2012 -	03/2019	84	80.24	
32	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
33	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60	-32.3	
34	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	114.6	
35	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	114.71	07/2016 -	03/2020	44	0	
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	437.51	-	03/2015 -	03/2021	72	-2.14	
37	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132	16.86	
	<u>South-Eastern Coal Fields Limited</u>									
38	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2018	24	0	
39	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	0	
40	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	135.60	03/2015 03/2020	03/2020	60	201.44	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
41	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72	0	
	Total		20,254.10 -	20,473.06	11,851.64					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
43	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 482.85	482.85	413.01	12/2017 04/2018	04/2018	4	0	
44	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	97.94	11/2016 04/2019	04/2019	29	5.89	
	Total		680.64 -	692.29	510.95					
	<u>STEEL</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
45	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	0	
46	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	
47	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
48	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
49	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>National Mineral Development Corporation (Nmdc)</u>									
50	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	13,298.64	05/2015 10/2018	10/2018	41	0	
	<u>Raistriya Ispat Nigam Limited</u>									
51	ADDITIONAL WATER STORAGE RESERVOIR (KBR-II) - [N12000120]RINL, ANDHRA PRADESH	07/2015	465.85 -	465.85	120.00	07/2018 -	09/2018	2	0	No
52	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	786.45	12/2017 -	10/2018	10	-12.53	No
53	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH	08/2015	320.66 -	320.66	37.04	08/2018 -	10/2018	2	0	No
54	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	178.10	09/2018 -	01/2019	4	0	No
55	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	236.32	10/2016 -	03/2019	29	42.39	No
	<u>Steel Authority Of India Limited (Sail)</u>									
56	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,560.44	03/2013 -	02/2018	59	0	
57	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	614.96	12/2017 -	11/2018	11	0	
58	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	213.12	10/2017 -	12/2018	14	0	
59	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	2,018.18	04/2018 -	02/2019	10	0	
	Total		46,113.39 -	45,900.79	37,200.88					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
60	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	4,588.29	1,145.97	08/2018 05/2019	05/2019	9	0	
	<u>Chennai Petroleum Corporation Limited</u>									
61	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19	0	
	<u>Gas Authority Of India Limited</u>									
62	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	47.80	04/2018 -	07/2018	3	-38.98	
63	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	2,915.00	1,621.62	12/2012 02/2019	02/2019	74	0	
	<u>Hindustan Petroleum Corporation Limited</u>									
64	NEW 250 TMTPL LPG PLANT AT PANAGARH - [N16000222]HPCL,WEST BENGAL	08/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018	6	0	
65	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	449.68	10/2014 03/2018	02/2019	52	133.5	
	<u>Indian Oil Corporation Limited</u>									
66	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	470.76	07/2017 -	02/2018	7	0	
67	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	4,190.00	2,505.63	09/2017 06/2018	06/2018	9	36.22	
68	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	1,659.56	09/2017 12/2018	12/2018	15	0	
69	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	315.63	10/2017 -	03/2019	17	17.66	
70	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	134.25	07/2018 10/2020	10/2020	27	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
71	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	1,729.04	03/2015 03/2018	03/2018	36	29.42	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
72	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 5,725.50	5,725.50	4,290.94	04/2016 03/2018	03/2018	23	38.82	
73	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	2,039.15	05/2014 05/2018	05/2018	48	0	
74	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,578.73	05/2017 05/2018	05/2018	12	1.87	
75	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,504.61	1,237.43	05/2017 05/2018	05/2018	12	-13.63	
76	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 181.02	181.02	168.93	01/2017 03/2018	05/2018	16	0	
77	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	115.36	07/2016 06/2018	06/2018	23	-20.81	
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	2,067.29	03/2013 09/2018	09/2018	66	-3.5	
79	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,188.01	05/2013 03/2018	11/2018	66	45.83	
80	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	3,961.54	3,721.54	12/2017 03/2019	03/2019	15	-14.25	
81	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	97.34	03/2019 -	04/2019	1	0	
82	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	571.47	542.92	09/2011 06/2019	06/2019	93	-22.42	
83	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	2,477.21	05/2019 10/2019	10/2019	5	-4.01	
84	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	8.45	01/2014 11/2019	11/2019	70	62.78	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
85	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	779.10	03/2019 05/2020	05/2020	14	0	
	<u>Oil India Limited</u>									
86	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17	12.15	
87	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20	24.47	
88	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8	0	
	Total		53,922.23 -	56,788.55	35,019.44					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
89	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	893.51	04/2020 -	06/2023	38	0	
	<u>National Hydro-Electric Power Corporation</u>									
90	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,233.88	01/2016 -	03/2018	26	61.5	
91	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,652.65	09/2009 -	12/2020	135	114.28	
	<u>National Thermal Power Corporation</u>									
92	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018	14	11.66	
93	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	6,984.00	09/2011 06/2018	06/2018	81	86.27	
94	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57	49.41	
95	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	-	01/2018 -	02/2019	13	5.91	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	0	
97	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,451.00	11/2016 03/2019	03/2019	28	0	
98	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	9,341.00	06/2017 06/2019	06/2019	24	7.55	
99	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	8,722.00	09/2017 06/2019	06/2019	21	10.55	
100	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	7,029.00	08/2018 06/2019	06/2019	10	9.64	
101	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,918.00	03/2019 03/2019	09/2019	6	0	
102	TALAIPELLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	3,004.00	-	11/2019 -	12/2019	1	0	
103	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	6,272.00	02/2019 10/2020	10/2020	20	5.55	
104	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	1,399.00	07/2020 10/2020	10/2020	3	0	
105	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,446.00	03/2013 12/2020	12/2020	93	29.14	
106	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	14,283.00	01/2011 04/2021	04/2021	123	73.65	
107	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.84	306.00	09/2019 02/2022	02/2022	29	0	
	<u>North East Electric Power Corporation</u>									
108	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,146.13	12/2009 03/2018	03/2018	99	147.51	
109	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,556.85	08/2013 03/2018	03/2018	55	133.06	
	<u>Power Grid Corporation Of India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
110	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,630.98	08/2013 12/2017	03/2018	55	23.65	05/08 line completed. Balance lines (linked to Gen. Proj.) to be completed matching with Generation Project. Kaneng HEP scheduled in Mar'18 and Lower Subhansiri HEP is schedule uncertain.(agitation against big dams). 01 loc. under ROW affecting balance TE & stgg. Critical.
111	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	341.00	246.94	06/2012 -	03/2018	69	46.77	ROW issues resolved & line completed except LIL0 point connection awaiting CEA clearance for shut-down & charging of line (clearance linked to removal of un-authorised structures in the line corridor, to be expedited by distt. authorities).
112	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,436.82	11/2012 12/2017	03/2018	64	36.01	07/08 line & 06/07 sub station completed progressively from Oct'12 to Jun'16 . Balance elements ready for charging (except ICT-II at Daltonganj). Waiting for down stream clearance from JUSNL.
113	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	375.94	08/2014 12/2017	03/2018	43	43.37	Implementation affected due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Work under progress with the help of Police protection.
114	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	137.13	09/2014 09/2017	03/2018	42	0	Supply has been completed in package. Presently there are only 02 lines balance which are under construction lines and having ROW issues.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	734.04	11/2014 06/2017	03/2018	40	21.9	01 out of 02 elements completed. Implementation affected due to poor performance by contractor in Dehradun-Abdullapur line. Completion being expedited through mobilisation from other sources.
116	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	156.45	04/2016 12/2017	03/2018	23	0	Substation PMUs has been supplied for which installation is under progress. PDC in control center has been commissioned for WRDLC, GETCO, MPPTCL, Chattisgarh, Karnataka and Tamilnadu, Kerala, Delhi, HP, Punjab, UP & Rajasthan.
117	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	143.08	03/2016 07/2017	03/2018	24	32.69	04 out of 05 elements completed. Implementation of balance affected due to delay in equipment supply(Off-shore) & non-readiness of down stream line by State Govt. at Hamirpur.
118	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	833.39	04/2017 03/2018	03/2018	11	0	02 out of 04 line & 02 out of 03 S/S completed. Work has been slowed-down to match with Generation (ant. by Mar'18).
119	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,113.00	12/2015 -	03/2018	27	42.83	
120	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,746.00	11/2017 -	03/2018	4	0	
121	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,287.00	01/2018 -	03/2018	2	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
122	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	142.77	02/2016 08/2017	04/2018	26	14.6	Project completed except procurement of ICT (500MVA, 765/400KV) at Gaya. Transformer supply also delayed. Supply expected by Mar'18.
123	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,610.29	12/2012 02/2018	06/2018	66	36.79	13/17 line & 05/07 S/s completed. Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Arunachal Pradesh (Tezu-Namsai line) affected due to compensation issues & land ownership disputes and further their commissioning linked to readiness of down stream system (being implemented under NER comprehensive scheme). Mizoram (Silcher-Melriat line) is affected due to tree cutting. Issue getting resolved with support of state/Distt. Admn.
124	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	587.18	06/2015 12/2017	06/2018	36	36.74	765KV Bay commissioned in Jan'17 matching with associated line. ICT's ready. Commissioning matching with Srikakulam – Garivadi line (under TBCB rout).
125	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,125.29	12/2015 12/2017	06/2018	30	0	Generation project delayed/uncertain. Implementation also affected due to severe ROW problem mostly at Angul end & huge forest involvement. Working permission for Chattisgarh portion issued in Nov'17.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
126	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,183.35	04/2016 09/2017	06/2018	26	38.61	Implementation affected due to severe ROW problem at Rajarhat end as well as in Jharkhand area. Work in Rajarhat S/stn. area almost standstill since last 9-10 months due to protest/agitation by locals who not allowing to enter in S/s. Work resumed in Oct'17 again stopped due to protest w.e.f 01.12.17. Matter being followed up at all levels for early resolution & efforts being made for resumption of work complete at the earliest.
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	399.39	06/2016 02/2018	06/2018	24	0	01 out of 02 completed. Implementation affected due to severe ROW problem at singrauli end. Work also affected due to poor performance by executing agency, being expedited with support from Powergrid.
128	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	389.04	11/2016 11/2017	06/2018	19	5.34	
129	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	234.00	02/2017 06/2017	06/2018	16	30.37	
130	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	185.89	03/2018 -	06/2018	3	26.82	01 out of 02 line completed. Work badly affected due to disturbance in Kashmir and delay in finalisation of compensation by PNC. To resolve compensation issue matter taken up with State Govt.. State/MoP help required. All efforts being made to complete earlier.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
131	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,988.93	11/2008 09/2018	09/2018	118	22.93	06/07 lines & 02/02 S/stn completed ahead of Generation. Implementation of balance 01 line (Edamon-Muvattupuzha line) is affected due to severe ROW problem (long pending). Problem being addressed progressively as per latest Revised G.O. of 30.07.15 (compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.). Works under progress. Site is getting police protection as per requirement from State admn.
132	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,395.80	09/2014 06/2017	09/2018	48	39.3	02 out of 03 line completed. Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Obstruction are being removed progressively with the help of Police protection.
133	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	541.66	09/2017 -	09/2018	12	0	
134	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,354.03	04/2018 -	09/2018	5	0	01 out of 03 line completed. Implementation affected due to forest clearance (awaited). Generation project delayed (ant. by Sep'18). Work slowed-down to the extent possible to match Generation.
135	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	168.46	03/2017 10/2017	09/2018	18	0	Erection completed. Testing/rectification under progress. Commissioning matching with Generation. Generation project delayed.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
136	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12	30.49	Khalsti & Leh S/Stn. and 220LV Leh – Khalsti line were charged on 31 Oct'17. Implementation affected due to delay in land acquisition of Kargil S/s. Land handed over by DM in Dec'16. ROW clearance of 08 locs. to be expedited. Increased BE allocation from 500 Cr. To 820 Cr. Required.
137	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	10/2018	12	0	Gen. project delayed. Work on ATS are being slowed-down to extent possible to match with Generation
138	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,683.22	01/2015 03/2018	11/2018	46	16.58	03 out of 04 line alongwith Alipurduar & Agra HVDC terminal completed. Gen. Proj.(Punatsangchu-I HEP in Bhutan) getting delayed (ant in 2019-20 & beyond). Balance line completed. Line proposed to be used as contingency arrangement for evacuation of power from Mangdechhu HEP. (Gen. expected by Nov'18). Charging matching with Generation.
139	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	659.02	09/2010 12/2017	12/2018	99	54.59	02/03 line line completed. Severe ROW problem in balance LILO line (400KV D/C LILO at Navi Mumbai, being completed using underground cable) continue. Cable burnt/ damaged by miscreants. Also down stream network at Navi Mumbai is not ready. Critical.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
140	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,507.26	10/2012 02/2018	12/2018	74	5.14	8 out of 9 lines completed progressively by Dec'16. Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award. Severe ROW problem being encountered.
141	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	177.40	07/2017 -	12/2018	17	27.92	03 elements out of 04 elements completed. Project commissioned except Bus Reactor at Yelankha. As per MoM of 40th SCSPSR held on 19.11.16. Procurement being taken up after resolution of ROW issue of LILO line at Yelahanka. Now, ROW issues for LILO resolved. Procurement process for Bus Reactor is under progress. NIT done, award expected by Mar'18.
142	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	178.76	11/2017 -	12/2018	13	0	Generation project ant. in March 2020. Work slowed-down to extent possible to match the generation. Forest clearance also awaited.
143	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	487.29	06/2014 03/2018	03/2019	57	31.17	01 out of 02 lines completed. Balance 400KV Madugiri-Yelahanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work re-award in Dec'17. Work under progress.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
144	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,894.73	03/2018 -	03/2019	12	0	Implementation affected due to delay in land acquisition & likely delay in off-shore supplies.
145	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	263.03	01/2018 -	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through Tiger reserve area. Wildlife clearance proposal submitted. SBWL meeting yet to be held. Clearance awaited. Alternate arrangements made for evacuation (contingency through Punatsanghu ATS, ready) Generation project delayed (ant. by Nov'18).
146	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	71.53	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). Rajghat sub station annulled. Additional bay at Maharaniabagh in place of Rajghat S/stn. However, only 400KV line bays are being made at Maharaniabag. Award placed in Jan'18. Engg. in progress.
147	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	541.38	12/2018 -	12/2019	12	0	33 packages out of 44 packages award. Balance award under progress. Award have been delayed due to poor response & high prices quoted by bidders. Out of 116 Sub stations land for only 56 nos land available. Non-availability of 27 nos. land for awarded Sub-station. Critical. Approval of new elements proposed by Govt. of Arunachal Pradesh

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
148	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	429.76	12/2018 -	12/2019	12	0	51 packages out of 55 packages award. Balance award under progress). Award have delayed due to poor response & high prices quoted by bidders. Increased BE allocation from Rs. 282.5 Cr. to 375 Cr. required
	<u>Satluj Jal Vidyut Nigam Limited</u>									
149	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	197.07	11/2017 -	03/2018	4	0	
150	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	481.23	12/2016 -	12/2018	24	37.96	
	<u>Thdc India Limited</u>									
151	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	158.67	02/2014 02/2018	03/2019	61	50.75	Ilnd stage forest clearance for Power Evacuation Arrangement.
152	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,344.53	06/2013 -	11/2020	89	52.1	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required.
153	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,458.96	02/2016 09/2019	12/2020	58	165.65	Law and order problem: Dharna at Asena Crusher Plant since 10.02.18 is persistent till date, despite regular follow up with Distt. Administration.
	Total		2,36,398.29 -	2,81,055.60	1,74,995.17					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Hospital Services Consultancy Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
154	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10	13.31	Slow progress on account of labor and material constraints created by the localized unions /goons
155	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC, DELHI	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13	0	release of funds, smog/pollution
156	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC, PUNJAB	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6	0	Progress impacted due to shortage of construction/Building material due to Punjab Govt. Notification banning the mining /querying of aggregate and sand since 18.03.2017, Delay in submission/Mobilization of structural drawings by the agency
157	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16	0	release of funds
158	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6	0	Cyclotron area is on hold on account of clearance from AREB. non-availability of fund.
159	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	21.00	05/2018 08/2019	08/2019	15	0	
	Total		1,689.51 -	1,711.99	791.90					
	<u>RAILWAYS</u>									
	<u>East Central Railways</u>									
160	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	0	
	<u>East Coast Railway</u>									
161	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	48.52	03/2021 -	03/2022	12	0	
162	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	34.98	03/2021 -	03/2022	12	0	
	<u>Eastern Railways</u>									
163	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Metropolitan Rapid Transport Projects</u>									
164	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58	4,874.58	1,881.65	03/2016	06/2018	27	0	
165	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00	7,986.04	2,423.55	03/2014	03/2019	60	50.68	
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	801.59	03/2004	03/2020	192	259.68	
	<u>North Central Railway</u>									
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09	3,845.60	1.92	02/2020	12/2022	34	226.98	
168	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41	2,030.50	10.34	02/2019	12/2022	46	226.23	
	<u>North East Frontier Railway</u>									
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00	5,450.00	4,965.44	04/2008 12/2011	06/2018	122	263.33	
170	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00	3,040.00	2,842.53	12/2008	03/2019	123	314.73	
171	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56	9,658.00	7,211.12	03/2011	03/2020	108	1227.45	
172	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34	3,451.00	2,550.24	03/2014	03/2020	72	324.3	
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34	4,600.00	1,928.11	04/2014	03/2020	71	642.73	
174	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48	4,084.69	383.92	12/2015	03/2020	51	204.95	
175	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00	3,000.00	428.38	03/2015	03/2020	60	252.94	
	<u>North Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
176	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	895.00	685.07	03/2014 -	06/2019	63	37.02	
177	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,143.70	554.05	03/2015 -	12/2019	57	37.84	
	<u>Northern Railway</u>									
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193	1017.84	
	<u>Rail Vikas Nigam Ltd.</u>									
179	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,027.36	03/2010 -	03/2018	96	49.88	
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	729.94	03/2016 -	12/2018	33	0	
181	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.07	488.99	02/2015 -	12/2019	58	556.04	
182	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	388.00	348.52	02/2006 -	12/2019	166	48.26	
183	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,568.77	03/2008 06/2008	03/2020	144	145.63	
184	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,567.98	03/2016 -	12/2020	57	7.78	
	<u>South East Central Railway</u>									
185	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
	<u>West Central Railway</u>									
186	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	<u>Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
187	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	81.96	03/2012 -	03/2019	84	1.06	
188	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 816.86	385.60	387.69	03/2013 -	03/2020	84	-2.17	
	Total		39,411.20 -	1,10,498.39	52,006.46					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
189	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
190	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
191	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
192	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
193	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	<u>National Highways Authority Of India</u>									
194	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
195	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15	0	
196	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	80.68	
197	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117	0	
198	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119	0	
199	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104	68.99	
200	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	106.5	
201	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	0	
202	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	0	
203	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	0	
204	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55	0	
205	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	551.12	07/2014 -	03/2018	44	0	
206	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	416.83	06/2014 -	03/2018	45	0	
207	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	0	
208	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	03/2018	18	0	
209	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	709.00	283.32	09/2017 -	03/2018	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
210	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,104.55	06/2012 -	03/2018	69	0	
211	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96	42.25	
212	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	0	
213	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	0	
214	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111	28.93	
215	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	0	
216	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13	0	
217	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	0	
218	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
219	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	340.37	06/2016 -	06/2018	24	0	
220	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	149.66	07/2016 -	07/2018	24	0	
221	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9	0	
222	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118	0	
223	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
224	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	0	
225	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	0	
226	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	0	
227	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	0	
228	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	0	
229	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,476.75	08/2016 -	02/2019	30	0	
230	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	0	
231	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	0	
232	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	0	
233	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2	13.97	
234	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	-	03/2020 -	05/2020	2	44.39	
235	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	-	03/2020 -	06/2020	3	41.54	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Public Works Dept Of State</u>									
236	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	
	Total		35,576.13 -	38,136.91	14,130.38					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
237	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20	-57.02	
	<u>Mumbai Port Trust</u>									
238	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	82.72	
	Total		966.39 -	927.36	411.12					
	<u>TELECOMMUNICATIONS</u>									
	<u>Department Of Telecommunication</u>									
239	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020	57	84.97	
	<u>Mahanagar Telephone Nigam Limited</u>									
240	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	0	
	Total		13,752.26 -	25,082.26	7,814.30					
	<u>URBAN DEVELOPMENT</u>									
	<u>Bangalore Metro Rail Corporation Limited</u>									
241	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	land acquisition
	<u>Central Public Works Department</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
242	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	0	
243	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	545.04	12/2015 -	03/2018	27	0	
244	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	443.73	03/2015 12/2017	03/2018	36	37.1	
245	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	321.00	297.34	09/2016 03/2018	04/2018	19	-3.52	
246	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	296.50	03/2016 12/2017	04/2018	25	44.75	
247	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	82.18	11/2015 05/2018	05/2018	30	0	
248	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH	12/2016	164.00 -	164.00	79.25	01/2018 05/2018	05/2018	4	0	
249	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	126.35	08/2016 -	06/2018	22	0	
250	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	170.62	149.22	03/2012 03/2018	06/2018	75	-16.77	
251	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	316.80	05/2017 02/2018	06/2018	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2018)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
252	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	134.18	11/2014 -	10/2018	47	0	
253	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
254	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	39.91	03/2016 -	12/2018	33	0	
255	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	47.29	04/2018 -	05/2019	13	0	
256	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	67.24	04/2019 06/2019	06/2019	2	0	
257	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
258	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	160.53	10/2019 -	03/2020	5	30.58	
259	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36	.57	
<u>Delhi Metro Rail Corporation Ltd</u>										
260	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	0	land at few location is not available. Target will be worked out when these land pockets are available.
<u>Kochi Metro Rail Corporation Ltd</u>										
261	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
<u>Nagpur Metro Rail Corporation Ltd</u>										
262	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21	0	
Total			84,839.01 -	85,558.10	42,129.88					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Grand Total		6,01,037.76	7,36,994.63	4,04,760.35					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(February 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69	93
	Total		3,492.00 -	6,100.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
3	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	02/2018	11.60	8
	<u>Northern Coal Fields Limited</u>							
4	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58	72
	<u>Singareni Colliers Company Limited</u>							
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60	60
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24	84
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
8	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	Total		1,929.87 -	3,000.82				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		197.79	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90	191.38	05/2017	03/2018	13.31	10
	Total		168.90	191.38				
	<u>PETROLEUM</u>							
	<u>Hindustan Petroleum Corporation Limited</u>							
11	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81	723.40	10/2014	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
12	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06	714.25	10/2017	03/2019	17.66	17
13	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	03/2014	3,076.00	4,190.00	09/2017	06/2018	36.22	9
	<u>Oil & Natural Gas Corporation Limited</u>							
14	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94	330.35	01/2014	11/2019	62.78	70
15	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,256.72	05/2013	11/2018	45.83	66
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63	2,665.65	03/2015	03/2018	29.42	36
17	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35	5,725.50	04/2016	03/2018	38.82	23
18	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47	5,813.25	05/2017	05/2018	1.87	12
	<u>Oil India Limited</u>							
19	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64	256.41	12/2016	05/2018	12.15	17
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	438.84	03/2017	11/2018	24.47	20
	Total		17,529.25	22,114.37				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
21	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04	5,882.01	01/2016	03/2018	61.50	26

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
22	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28	135
	<u>National Thermal Power Corporation</u>							
23	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93
24	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41	57
25	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	06/2018	86.27	81
26	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
27	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
28	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91	13
29	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
30	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
31	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
32	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66	14
	<u>North East Electric Power Corporation</u>							
33	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	03/2018	133.06	55
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2018	147.51	99
	<u>Power Grid Corporation Of India Limited</u>							
35	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	03/2018	32.69	24
36	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	04/2018	14.60	26
37	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	12/2018	27.92	17
38	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	06/2018	26.82	3
39	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	03/2018	46.77	69
40	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37	16
41	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37	43

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
42	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	550.18	11/2016 -	06/2018	5.34	19
43	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	03/2019	31.17	57
44	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143	03/2013	514.20 -	703.10	06/2015 -	06/2018	36.74	36
45	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59	99
46	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	882.13	11/2014 -	03/2018	21.90	40
47	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83	27
48	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	07/2010	1,272.80 -	1,731.10	11/2012 -	03/2018	36.01	64
49	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	04/2016 -	06/2018	38.61	26
50	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
51	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
52	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30	48
53	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080	02/2010	2,144.00 -	2,932.88	12/2012 -	06/2018	36.79	66
54	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2018	5.14	74
55	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077	04/2010	4,404.57 -	5,135.01	01/2015 -	11/2018	16.58	46
56	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2018	23.65	55
	<u>Satluj Jal Vidyut Nigam Limited</u>							
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	<u>Thdc India Limited</u>							
58	DHUKWAN SMALL HYDRO PROJECT - [N18000189	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
59	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,789.61	06/2013 -	11/2020	52.10	89

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	12/2020	165.65	58
	Total		1,51,298.08 -	1,95,955.39				
	<u>RAILWAYS</u>							
	<u>Eastern Railways</u>							
61	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
	<u>Metropolitan Rapid Transport Projects</u>							
62	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	<u>North Central Railway</u>							
64	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
65	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
	<u>North East Frontier Railway</u>							
66	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
67	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73	123
68	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72
69	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
70	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
71	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33	122
72	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
	<u>North Western Railway</u>							
73	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02	63
74	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84	57
	<u>Northern Railway</u>							
75	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84	193
	<u>Rail Vikas Nigam Ltd.</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
76	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26	166
77	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88	96
78	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04	58
79	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
80	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78	57
<u>South East Central Railway</u>								
81	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
<u>West Central Railway</u>								
82	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
<u>Western Railway</u>								
83	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
	Total		25,838.95 -	96,934.69				
<u>ROAD TRANSPORT AND HIGHWAYS</u>								
<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
84	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
<u>National Highways Authority Of India</u>								
85	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68	112
86	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	04/2018	42.25	96
87	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2018	68.99	104
88	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2018	28.93	111
89	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
90	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
91	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39	2

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
92	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76
	Total		4,961.94 -	7,523.02				
	<u>SHIPPING AND PORTS</u>							
	<u>Mumbai Port Trust</u>							
93	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
94	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39	29
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
95	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97	57
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
96	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
97	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	04/2018	44.75	25
98	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091	08/2014	350.02 -	479.87	03/2015 -	03/2018	37.10	36
99	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36
100	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	Total		2,421.00 -	3,186.19				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Grand Total		2,22,195.78	3,61,478.49				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 09/2017	10/2017
	Total		309.46 -		
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
2	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
3	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	05/2017
	<u>Singareni Colliers Company Limited</u>				
4	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	Total		1,595.80 -		
	<u>STEEL</u>				
	<u>Hindustan Steelwork Construction Limited</u>				
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017
6	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	-	12/2017
7	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
8	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
9	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
10	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
11	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
12	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Steel Authority Of India Limited (Sail)</u>				
13	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		7,151.88 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
15	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
16	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA	02/2016	3,313.00 -	02/2020 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
17	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	11/2017
	<u>Hindustan Petroleum Corporation Limited</u>				
18	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
19	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 06/2017	06/2017
20	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 06/2017	06/2017
21	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 10/2017	10/2017
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	11/2017
	<u>Numaligarh Refinery Limited</u>				
23	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM	07/2015	1,031.37 -	01/2018 -	01/2018
	<u>Oil & Natural Gas Corporation Limited</u>				
24	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 215.38	06/2017 01/2018	01/2018
	<u>Oil India Limited</u>				
25	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	07/2017
26	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	11/2017
	Total		13,245.92 -		
	<u>POWER</u>				
	<u>Damodar Valley Corporation</u>				
27	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	12/2011 03/2016	02/2017
	<u>National Hydro-Electric Power Corporation</u>				
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
30	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016
31	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 03/2017	03/2017
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
33	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>North East Electric Power Corporation</u>				
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-
	Total		30,190.89 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
35	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation Ltd</u>				
36	AIIMS-RAE BARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 09/2017	09/2017
37	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-
38	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		749.18 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
39	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
40	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
	<u>East Central Railways</u>				
41	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
42	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
43	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
44	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
45	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
46	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
47	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
48	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
49	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
50	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
51	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
52	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
53	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
54	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
55	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
56	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
57	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
58	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
59	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
60	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>East Coast Railway</u>				
61	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015
62	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
63	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
64	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
65	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
66	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Eastern Railways</u>				
67	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
68	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
69	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-
70	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
71	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-
72	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
73	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-
74	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	- -	-
75	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER, MULTI STATE	04/2007	450.00 -	- -	-
76	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	- -	-
77	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 1,130.13	- -	-
78	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	-
79	BANDEL-BOINCHI 3RD LINE - [N22000221]ER, MULTI STATE	04/2011	288.35 -	- -	-
80	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	- -	-
81	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	- -	-
82	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.91 -	- -	-
83	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER, MULTI STATE	04/2010	174.56 -	- -	-
84	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	- -	-
85	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	296.44 -	- -	-
86	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER, MULTI STATE	04/2007	450.55 -	- -	-
87	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER, MULTI STATE	04/2010	365.17 -	- -	-
88	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
89	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
90	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
91	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
92	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
93	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
94	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
95	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
96	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
97	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
98	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
99	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
100	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
101	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
102	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 495.74	06/2013 -	03/2017
103	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
104	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
105	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
106	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
107	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
108	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016
110	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
111	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
	<u>North Eastern Railway</u>				
112	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
113	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
114	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
115	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
116	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
	<u>North Western Railway</u>				
117	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
118	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
119	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
120	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
121	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
122	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
123	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
124	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
125	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
126	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
127	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
128	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
129	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
130	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
131	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
132	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
133	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
134	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
135	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
136	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
137	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
138	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
139	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
140	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
141	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
142	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	12/2017
143	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017
144	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017
145	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
147	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	- -	-
148	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
	<u>Railway Electrification</u>				
149	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
150	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	-
151	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-
152	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
153	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
154	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
155	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,693.00	- -	-
156	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
157	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
158	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
159	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
160	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
161	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
162	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
163	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
164	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
165	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-
	<u>South East Central Railway</u>				
166	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
	<u>South Eastern Railway</u>				
167	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017
168	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
169	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
170	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
171	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
172	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
173	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
174	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
175	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
176	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
177	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
178	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
179	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-
180	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-
	<u>South Western Railway</u>				
181	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-
182	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
183	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
184	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
185	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
186	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
187	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
188	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
189	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
190	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
191	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
192	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
193	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
194	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
195	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
	<u>Southern Railway</u>				
196	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	01/2018
197	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	12/2017
198	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
199	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
200	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
201	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
202	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
203	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-
204	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-
205	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
206	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
207	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
208	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
209	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
210	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
211	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
212	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
213	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
214	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
215	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
	<u>Western Railway</u>				
216	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
217	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 -	-
218	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
219	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
220	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
221	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-
222	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
223	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
224	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
225	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
226	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		1,80,095.56 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
227	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
228	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
229	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
230	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
231	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014
232	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
233	CONSTRUCTION OF PAVED SHOULDERS INCULGING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
234	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
235	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
237	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016
238	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
239	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
240	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
242	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
243	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
244	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017
245	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017
246	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017
248	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017
249	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017
250	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017
251	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018
253	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
254	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
255	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
256	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
257	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
258	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
259	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
260	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
261	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
262	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
263	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
264	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
265	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
266	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
267	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
268	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
269	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
270	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
271	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
272	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
273	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
274	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
275	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
276	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
277	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
278	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
279	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
280	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
281	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
282	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
283	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
284	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
285	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
286	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
287	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
288	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016
289	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	04/2017
290	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017
291	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
292	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
293	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
294	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
295	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
296	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
297	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
298	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
299	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
300	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
301	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
302	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
303	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
304	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
National Highways Authority Of India					
305	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017
306	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017
307	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017
308	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	07/2017
309	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017
310	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017
311	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017
312	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017
313	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	09/2017
314	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
315	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017
316	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017
317	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017
318	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017
319	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017
320	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017
321	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017
322	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017
323	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017
324	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017
325	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017
326	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017
327	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017
328	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017
329	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017
330	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017
331	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017
332	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017
333	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	12/2017
334	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017
335	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017
336	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017
337	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017
338	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017
339	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
340	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017
341	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017
342	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017
343	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017
344	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017
345	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017
346	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017
347	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	12/2017
348	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017
349	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	12/2017
350	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI, PUNJAB	09/2014	479.00 -	- -	12/2017
351	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI, PUNJAB	12/2015	239.23 -	12/2017 -	12/2017
352	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	12/2017
353	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017
354	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	12/2017
355	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018
356	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018
357	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	- -	01/2018
358	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018
359	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	-
360	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-
361	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
362	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
363	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-
364	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
365	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
366	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
367	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
368	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-
369	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-
370	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-
371	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
372	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
373	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-
374	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
375	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
376	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
377	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
378	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
379	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
380	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
381	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
382	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
383	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
384	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
385	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
386	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
387	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
388	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
389	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
390	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
391	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
392	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
393	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
394	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
395	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
396	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
397	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
398	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
399	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
400	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
401	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
402	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
403	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
404	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
405	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
406	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
407	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
408	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
409	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
410	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
411	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
412	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
413	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
414	REHABILITATION AND UPGRADE TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
415	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
416	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
417	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-
418	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
419	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
420	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
421	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
422	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
423	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
424	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
425	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
426	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
427	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
428	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
429	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2018)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
430	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
431	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
432	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
433	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
434	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
435	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
436	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
437	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
438	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
439	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
440	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
441	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
442	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
443	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
444	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
445	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
446	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
447	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
448	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
449	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
450	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
451	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
452	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
453	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
454	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
455	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
456	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM 206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-
457	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
458	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
459	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
460	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
461	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
462	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
463	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
464	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
465	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
466	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
	<u>National Highways Development Project</u>				
467	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
468	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
469	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
470	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
471	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
472	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
473	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
474	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017
475	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017
476	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017
477	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017
478	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017
479	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017
480	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	06/2017
481	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017
482	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	10/2017
483	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017
484	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
485	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
486	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
	Public Works Dept Of State				
487	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
488	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
489	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
490	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
491	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
492	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
493	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
494	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
495	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
496	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
497	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
498	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
499	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
500	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
501	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
502	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
503	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
504	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
505	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
506	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
507	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
508	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
509	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
510	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
511	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017
512	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017
513	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017
514	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	02/2017
515	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017
516	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	02/2017
517	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017
518	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	05/2017
519	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017
520	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	08/2017
521	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017
522	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017
523	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017
524	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017
525	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
526	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTION - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
527	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
528	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
529	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
530	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
531	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-
532	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
533	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
534	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
535	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
536	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
537	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
538	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
539	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
540	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
541	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
542	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
543	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
544	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
545	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
546	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
547	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
548	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
549	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
550	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
551	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
552	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
553	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
554	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
555	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
556	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
557	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
558	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
559	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
560	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
561	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
562	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
563	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
564	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
565	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
566	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
567	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
568	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
	Total		2,09,651.35 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
569	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	12/2017
570	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018
571	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU	10/2013	198.94 -	06/2017 -	-
572	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU	12/2014	274.85 -	04/2017 -	-
	<u>Port Trust</u>				
573	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2017
574	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		3,505.69 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
575	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	Total		2,111.17 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
576	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
577	CONSTRUCTION OF CENTRAL EXCISE DEPARTMENT AT CR COLONY - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
	<u>Chennai Metro Rail Ltd</u>				
578	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 19,058.00	12/2015 -	12/2017
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
579	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				
580	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>National Building Construcion Corporation Ltd</u>				
581	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		41,183.51 -		
	Grand Total		4,91,508.41		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
1	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	199.12	152.31	- -	03/2019	-	0/0
2	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	2,271.50	1,455.54	- -	03/2021	-	0/0
3	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	792.89	220.71	- -	03/2021	-	0/0
4	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	540.02	125.56	- -	03/2022	-	0/0
5	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	1,272.19	62.59	- -	03/2022	-	0/0
6	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	637.95	7.28	- -	03/2022	-	0/0
7	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 3,168.29	3,168.29	803.55	- -	03/2023	-	0/0
8	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	2,449.91	34.54	- -	03/2023	-	0/0
9	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	2,081.27	.14	- -	03/2023	-	0/0
10	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	1,035.16	4.00	- -	03/2023	-	0/0
11	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	8,857.98	-	- -	03/2024	-	0/0
12	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	5,341.68	.15	- -	03/2024	-	0/0
13	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	3,438.51	-	- -	03/2024	-	0/0
14	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	3,627.47	17.52	- -	03/2024	-	0/0
	<u>East Central Railways</u>								
15	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	678.54	-	- -	12/2018	-	0/38
	<u>East Coast Railway</u>								
16	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	496.81	- -	03/2020	-	1/1
17	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	238.03	156.11	- -	03/2020	-	0/0
18	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	1,579.27	641.37	- -	03/2021	-	0/0
19	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 843.04	843.04	51.85	- -	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
20	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	3,004.90	956.23	- -	06/2021	-	0/0
21	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	486.05	- -	12/2022	-	0/0
	<u>Eastern Railways</u>								
22	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	47.63	- -	11/2018	-	0/0
23	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	111(R1)	0/0
	<u>North East Frontier Railway</u>								
24	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 -	630.00	613.01	- -	03/2018	-	0/0
25	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	1,871.00	1,084.45	- -	03/2018	-	0/0
26	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
27	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	450.00	345.63	- -	03/2019	-	0/0
28	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 -	535.00	532.42	- -	03/2019	-	0/0
29	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	398.93	128.77	- -	03/2019	-	0/0
30	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	580.00	-	- -	07/2019	-	2/3
31	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	614.00	262.63	- -	03/2020	-	0/0
32	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	780.00	450.50	- -	03/2020	-	0/0
33	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	2,135.00	922.31	- -	03/2020	-	0/0
34	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 -	360.00	3.13	- -	03/2020	-	0/0
35	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	380.00	97.41	- -	03/2020	-	0/0
36	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
37	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	471.00	53.14	- -	03/2020	-	0/0
38	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	450.00	122.81	- -	03/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
39	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	612.00	-	- -	03/2020	-	0/0
40	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	6,000.00	257.21	- -	03/2021	-	0/0
41	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	871.00	31.53	- -	03/2021	-	0/0
42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	2,232.00	93.15	- -	03/2022	-	0/0
<u>North Eastern Railway</u>									
43	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	474.30	424.76	- -	03/2018	-	0/0
44	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	412.05	349.66	- -	04/2018	-	0/0
45	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	268.78	93.68	- -	08/2018	-	0/0
46	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	227.00	240.37	- -	08/2018	-	0/0
47	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	146.48	- -	10/2018	-	0/0
48	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	718.54	272.46	- -	05/2019	-	0/0
<u>North Western Railway</u>									
49	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	294.90	114.58	- -	10/2018	-	0/0
50	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	346.35	213.86	- -	10/2018	-	0/0
51	DAUSA-GANGAPUR CITY (NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 780.98	795.01	388.59	- 02/1997	02/2019	264(R3)	0/0
52	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 218.39	244.02	126.95	- -	02/2019	-	0/0
53	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	348.55	61.89	- -	03/2019	-	0/0
54	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	349.00	148.53	- -	03/2019	-	0/0
55	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	685.99	3.05	- -	03/2020	-	0/0
56	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 295.02	420.08	36.19	- -	05/2018	-	0/0
<u>Rail Vikas Nigam Ltd.</u>									
57	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL, MULTI STATE	04/2008	822.39 -	1,810.00	1,679.05	- -	03/2018	-	0/1

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
58	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	350.00	308.90	- -	03/2018	-	0/0
59	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.99	1,078.57	- 09/2009	03/2019	114(R1)	0/0
60	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	4,500.00	123.98	- -	03/2019	-	0/0
61	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA	04/2010	2,127.00 -	2,127.00	909.63	- -	03/2019	-	0/1
62	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	975.62	387.97	- -	03/2020	-	0/0
63	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	578.80	- -	03/2020	-	0/0
64	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	644.38	44.80	- -	12/2020	-	0/0
65	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	1,548.66	469.04	- -	12/2020	-	0/0
66	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	2,335.67	62.27	- -	12/2024	-	0/0
<u>South Central Railway</u>									
67	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	525.00	679.98	- -	03/2019	-	0/0
68	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	2,125.18	246.34	- -	03/2021	-	0/0
69	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	202.11	- -	03/2021	-	0/0
70	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	1,160.47	18.25	- -	03/2022	-	0/1
<u>South Western Railway</u>									
71	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	860.43	346.94	- -	03/2020	-	0/0
72	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	341.68	- 11/2015	03/2020	52(R3)	0/2
73	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 1,141.00	1,141.00	521.44	- 03/2020	-	-	0/5
<u>West Central Railway</u>									
74	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	2,713.09	632.05	- -	03/2021	-	0/0
<u>Western Railway</u>									
75	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	548.93	- -	03/2019	-	0/0
76	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	143.70	- -	03/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
77	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	455.37	- -	03/2022	-	0/0
	Total		75,901.47 -	1,09,776.32	23,876.12				3/52
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
78	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	-	- -	02/2018	-	0/0
79	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	771.18	-	- -	03/2018	-	0/0
80	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	-	- -	04/2018	-	0/0
81	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	509.13	-	- -	04/2018	-	0/0
82	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	-	- -	04/2018	-	0/0
83	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	-	- -	04/2018	-	0/0
84	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	130.04	- -	05/2018	-	0/0
85	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	100.18	- -	05/2018	-	0/0
86	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	20.02	- -	05/2018	-	0/0
87	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	136.04	- -	05/2018	-	0/0
88	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	-	- -	05/2018	-	0/0
89	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- -	05/2018	-	0/0
90	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	-	- -	05/2018	-	0/0
91	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	-	- -	05/2018	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	06/2018	-	3/3
93	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0
94	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	- -	07/2018	-	0/0
95	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	74.13	- -	07/2018	-	0/0
96	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	- -	07/2018	-	0/0
97	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	-	- -	07/2018	-	0/0
98	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	635.26	- -	08/2018	-	0/0
99	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	129.75	- -	08/2018	-	0/0
100	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	21.26	- -	08/2018	-	0/0
101	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	123.13	- -	08/2018	-	0/0
102	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	-	- -	10/2018	-	0/0
103	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	-	- -	11/2018	-	0/0
104	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	-	0/0
105	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	35.17	- -	11/2018	-	0/0
106	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	505.00	- -	01/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2018)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	FOUR LANE OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	-	-	01/2019	-	0/0
108	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	-	-	01/2019	-	0/0
109	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	-	-	01/2019	-	0/0
110	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	-	-	02/2019	-	0/0
111	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	31.47	-	03/2019	-	0/0
112	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	329.10	-	03/2019	-	0/0
113	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	5.78	-	03/2019	-	0/0
114	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	2.93	-	03/2019	-	0/0
115	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	1,167.42	103.81	-	03/2019	-	0/0
116	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	-	-	03/2019	-	0/0
117	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	-	-	03/2019	-	0/0
118	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	-	-	04/2019	-	0/0
119	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	1,041.10	-	-	04/2019	-	0/0
120	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	-	-	04/2019	-	0/0
121	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	676.73	115.21	-	04/2019	-	0/0
122	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	1,587.49	24.95	-	04/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
123	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	899.00	-	- -	04/2019	-	0/0
124	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	-	- -	04/2019	-	0/0
125	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
126	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	- -	05/2019	-	0/0
127	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
128	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	-	- -	05/2019	-	0/0
129	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	1,004.67	-	- -	05/2019	-	0/0
130	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	43.29	- -	05/2019	-	0/0
131	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
132	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	-	- -	07/2019	-	0/0
133	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	-	- -	07/2019	-	0/0
134	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	-	- -	08/2019	-	0/0
135	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	66.58	- -	08/2019	-	0/0
136	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	1,388.34	-	- -	09/2019	-	0/0
137	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	1,664.20	75.54	- -	04/2020	-	0/0
National Highways Development Project									

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
138	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	38.33	- -	04/2018	-	0/1
	Total		50,900.91 -	50,900.40	3,565.50				3/4
	<u>URBAN DEVELOPMENT</u>								
	<u>Central Public Works Department</u>								
139	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	4.16	- -	04/2019	-	0/2
140	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	19.54	- -	10/2019	-	0/6
	Total		406.33 -	406.33	23.70				0/8
	Grand Total		1,27,208.71	1,61,083.05	27,465.32				6/64

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>ATOMIC ENERGY</u>					
	<u>Nuclear Power Corporation Of India Limited</u>					
1	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	11/2020 -	11/2023	0/0
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	01/2011 09/2017	10/2017	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	06/2017 12/2017	02/2018	0/0
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Northern Coal Fields Limited</u>					
8	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	03/2021 -	03/2021	0/0
	<u>South-Eastern Coal Fields Limited</u>					
9	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL, CHHATISGARH	05/2017	976.95 -	03/2026 -	03/2026	0/0
	<u>Western Coal Fields Limited</u>					
10	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL, MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
11	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL, MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>FERTILISERS</u>					
	<u>National Fertiliser Limited</u>					
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL, HARYANA	01/2018	215.92 -	11/2019 -	11/2019	0/0
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL, PUNJAB	01/2018	218.83 -	11/2019 -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 -	11/2019	0/0
	<u>MINES</u>					
	<u>National Aluminum Company Limited (Nalco)</u>					
15	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	04/2021 04/2021	04/2021	0/0
	<u>STEEL</u>					
	<u>Hindustan Steelwork Construction Limited</u>					
16	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2017	0/0
17	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
18	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	03/2018	0/0
19	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
20	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
21	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0
22	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
23	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
24	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
25	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
26	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
27	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
28	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
29	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
30	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Steel Authority Of India Limited (Sail)</u>					
31	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Bharat Petroleum Corporation Limited</u>					
32	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA	05/2015	337.06 -	08/2018 -	08/2018	0/0
33	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
34	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL, MAHARASHTRA	05/2015	193.40 -	01/2019 -	01/2019	0/0
35	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
36	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL, MAHARASHTRA	02/2016	554.00 -	02/2020 -	02/2020	0/0
37	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
38	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA	02/2016	3,313.00 -	02/2020 -	-	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
39	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
40	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
41	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
42	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL, UTTAR PRADESH	04/2017	287.49 -	04/2022 -	04/2022	0/0
43	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
44	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	09/2017 03/2018	03/2018	0/0
45	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL, MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
46	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL, MULTI STATE	09/2017	2,677.00 -	03/2021 -	03/2021	0/0
	<u>Indian Oil Corporation Limited</u>					
47	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL, GUJARAT	10/2014	279.00 -	08/2018 -	08/2018	0/0
48	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL, UTTAR PRADESH	01/2018	666.64 -	09/2019 -	09/2019	0/0
49	LPG BP PROJECT KHORDHA - [N16000283]IOCL, ODISHA	12/2016	161.59 -	12/2019 -	12/2019	0/0
50	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	04/2020 -	04/2020	0/0
51	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
52	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS & HSD, ADDITIONAL TANKS FOR MS, HSD AND BI - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
53	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL, GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
54	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 -	10/2020	0/0
55	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
56	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
57	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
58	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL, MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
59	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
60	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL, ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
61	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL, ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
62	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
63	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL, UTTAR PRADESH	08/2017	318.80 -	08/2021 -	08/2021	0/0
Indian Strategic Petroleum Reserves Ltd						
64	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KARNATAKA	01/2006	993.00 -	01/2012 -	11/2017	0/0
Oil & Natural Gas Corporation Limited						
65	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC, TRIPURA	05/2016	215.38 215.38	06/2017 01/2018	01/2018	0/0
66	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC, MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
67	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC, MAHARASHTRA	02/2015	2,899.93 -	05/2017 05/2018	05/2018	0/0
68	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC, MADHYA PRADESH	03/2009	181.02 181.02	01/2017 03/2018	05/2018	0/0
69	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC, GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
70	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC, ANDHRA PRADESH	04/2017	420.76 -	09/2018 09/2018	09/2018	0/0
71	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC, GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	12/2018	0/0
72	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0
73	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC, MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
74	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU	11/2015	390.52 -	03/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
75	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC, MAHARASHTRA	01/2017	474.15 474.15	05/2019 05/2019	05/2019	0/0
76	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 06/2019	06/2019	0/0
77	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI	08/2014	6,086.08 5,842.31	05/2019 10/2019	10/2019	0/0
78	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC, MAHARASHTRA	02/2017	546.15 546.15	11/2019 11/2019	11/2019	0/0
79	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC, MAHARASHTRA	02/2017	511.30 511.30	11/2019 11/2019	11/2019	0/0
80	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC, MAHARASHTRA	02/2017	968.61 968.61	11/2019 11/2019	11/2019	0/0
81	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
82	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC, ASSAM	07/2016	249.85 250.00	05/2020 05/2020	05/2020	0/0
83	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 06/2020	06/2020	0/0
84	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC, MAHARASHTRA	02/2017	4,006.83 -	05/2021 -	05/2021	0/0
85	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC, JHARKHAND	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0
86	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC, GUJARAT	02/2017	1,162.56 1,162.56	03/2026 03/2026	03/2026	0/0
<u>Oil India Limited</u>						
87	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL, MULTI STATE	11/2015	500.00 -	06/2017 -	07/2017	0/0
88	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL, ASSAM	03/2009	228.64 -	12/2016 -	05/2018	0/0
89	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	07/2011	352.56 -	03/2017 -	11/2018	0/0
90	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL, ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
91	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL, MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
92	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL, MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0
<u>POWER</u>						
<u>Chenab Valley Power Projects [P] Limited</u>						
93	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	06/2023	0/0
<u>National Hydro-Electric Power Corporation</u>						
94	50 MW SOLAR POWER PROJECT - [N18000251]NHPC, TAMIL NADU	06/2017	287.48 -	03/2018 -	03/2018	0/0
95	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>National Thermal Power Corporation</u>					
96	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016	0/0
97	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	12/2019	0/0
	<u>Power Grid Corporation Of India Limited</u>					
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 09/2017	03/2018	0/0
99	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	03/2018	0/0
100	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
101	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	03/2018	0/0
102	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	03/2018	0/0
103	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	12/2015 -	03/2018	0/0
104	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	11/2017 -	03/2018	0/0
105	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	01/2018 -	03/2018	0/0
106	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
107	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
108	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
109	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	06/2018	0/0
110	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
111	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
112	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
113	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2018	0/0
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 10/2017	09/2018	0/0
115	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	09/2018	0/0
117	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	10/2018 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
118	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
119	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
120	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	12/2018	0/0
121	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
122	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
123	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
124	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
125	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
126	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
127	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
128	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
129	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 -	03/2019	0/0
130	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
131	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
132	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL,MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
133	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
134	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]PGCIL,MULTI STATE	10/2016	167.75 -	04/2019 -	04/2019	0/0
135	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
136	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
137	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
138	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
139	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
140	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
141	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
142	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
143	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
144	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
145	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
146	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
147	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
148	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
149	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
150	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
151	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
152	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
153	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	12/2021 -	12/2021	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Natrip Implementation Society</u>					
154	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Hospital Services Consultancy Corporation</u>					
155	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2019	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
156	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
157	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	03/2019	0/0
158	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	03/2019	0/0
159	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 08/2019	08/2019	0/0
160	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
161	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
162	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- -	03/2019	0/0
163	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- -	03/2021	0/0
164	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- -	03/2021	0/0
165	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- -	03/2022	0/0
166	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- -	03/2022	0/0
167	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	- -	03/2022	0/0
168	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 3,168.29	- -	03/2023	0/0
169	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	- -	03/2023	0/0
170	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	- -	03/2023	0/0
171	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	- -	03/2023	0/0
172	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- -	03/2024	0/0
173	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- -	03/2024	0/0
174	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	03/2024	0/0
175	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	- -	03/2024	0/0
176	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	<u>Container Corporation Of India</u>					
177	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
178	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
179	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
180	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
181	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
182	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
183	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0
184	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
185	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	03/2019	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
186	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
	<u>East Central Railways</u>					
187	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
188	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
189	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
190	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
191	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
192	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
193	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
194	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
195	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
196	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
197	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
198	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
199	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
200	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
201	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
202	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
203	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
204	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
205	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
206	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
207	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
208	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>East Coast Railway</u>					
209	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 07/2015	07/2015	0/0
210	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
211	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2020	0/0
212	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
213	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	- -	03/2021	0/0
214	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 843.04	- -	03/2021	0/0
215	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2021 -	03/2021	0/0
216	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
217	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	06/2021	0/0
218	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2021 -	03/2022	0/0
219	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2021 -	03/2022	0/0
220	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	- -	12/2022	0/0
221	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
222	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
223	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
224	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
225	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
	<u>Eastern Railways</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
226	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	11/2018	0/0
227	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	03/2019	0/0
228	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0
229	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
230	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
231	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
232	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
233	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
234	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
235	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
236	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
237	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
238	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
239	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
240	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
241	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
242	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
243	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
244	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
245	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
246	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
247	BARIARPUUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
248	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
249	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
250	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
251	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
252	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
253	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
254	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
255	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
256	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
257	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
258	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
259	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
260	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
261	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
262	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
263	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
264	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
265	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
266	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
267	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-	0/0
268	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
269	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
270	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
271	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
272	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
273	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
<u>North East Frontier Railway</u>						
274	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	04/2016	0/0
275	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
276	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
277	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
278	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
279	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
280	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2019	0/0
281	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2019	0/0
282	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
283	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2020	0/0
284	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
285	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	- -	03/2020	0/0
286	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0
287	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
288	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
289	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	03/2020	0/0
290	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
291	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
292	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
293	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
294	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	- -	03/2020	0/0
295	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2020	0/0
296	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	- -	03/2020	0/0
297	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
298	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
299	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2022	0/0
300	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
301	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
<u>North Eastern Railway</u>						
302	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
303	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	04/2018	0/0
304	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	08/2018	0/0
305	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	08/2018	0/0
306	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	10/2018	0/0
307	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	05/2019	0/0
308	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
309	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
310	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
311	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
312	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
<u>North Western Railway</u>						
313	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	10/2018	0/0
314	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	10/2018	0/0
315	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	- 02/1997	02/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
316	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 218.39	- -	02/2019	0/0
317	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	03/2019	0/0
318	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	03/2019	0/0
319	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	06/2019	0/0
320	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	12/2019	0/0
321	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	03/2020	0/0
322	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
323	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
324	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 295.02	- -	05/2018	0/0
<u>Northern Railway</u>						
325	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	11/2002 -	12/2018	0/0
326	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
327	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
328	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
329	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
330	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
331	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
332	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
333	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
334	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
335	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
336	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
337	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
338	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
339	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
340	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
341	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
342	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
343	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
344	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
345	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
346	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
347	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
348	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	03/2018	0/0
349	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	- -	03/2018	0/0
350	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
351	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
352	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	03/2019	0/0
353	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
354	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
355	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0
356	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
357	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
358	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
359	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
360	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
361	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
362	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
363	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
364	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
365	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
366	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
367	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
368	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL, TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
369	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67 -	- -	12/2024	0/0
370	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
371	DIGHI PORT NEW LINE - [N22000408]RVNL, MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
372	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
373	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
374	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
375	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
	<u>Railway Electrification</u>					
376	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
377	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2019	0/0
378	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	03/2021	0/0
379	KAZIPET-BALHRSHA - [N22000367]SCR, MULTI STATE	04/2015	2,063.03 -	- -	03/2021	0/0
380	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
381	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	- -	-	0/0
382	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
383	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
384	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 -	-	0/0
385	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,693.00	- -	-	0/0
386	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
387	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
388	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
389	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- -	-	0/0
	<u>South East Central Railway</u>					
390	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
391	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
392	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
	<u>South Eastern Railway</u>					
393	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
394	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
395	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
396	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 -	12/2021 -	12/2021	0/0
397	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	12/2021 -	12/2021	0/0
398	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
399	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
400	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-	0/0
401	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
402	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-	0/0
403	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
404	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
405	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
406	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
407	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
408	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
409	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	-	0/0
410	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	-	0/0
	<u>South Western Railway</u>					
411	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	03/2020	0/0
412	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
413	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
414	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
415	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0
416	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
417	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
418	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
419	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
420	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
421	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
422	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
423	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
424	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0
	<u>Southern Railway</u>					
425	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 -	- -	01/2018	0/0
426	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
427	CALICUT-MANGALORE (DL) (SR) - [N220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
428	KARUR-SALEM(NL),SR - [N220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
429	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
430	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
431	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 582.83	- 07/2008	-	0/0
432	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- 01/2011	-	0/0
433	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
434	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
435	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
436	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
437	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
438	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
439	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
440	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
441	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
442	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
443	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
<u>West Central Railway</u>						
444	RAMGANJMUNDI-BHOPAL (NL),WCR - [N220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2021	0/0
<u>Western Railway</u>						
445	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
446	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	- -	03/2019	0/0
447	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 816.86	03/2013 -	03/2020	0/0
448	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
449	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	03/2022	0/0
450	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
451	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 -	-	0/0
452	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
453	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
454	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
455	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-	0/0
456	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
457	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
458	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
459	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
460	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
461	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
462	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0
463	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
464	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0
465	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
466	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
467	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
468	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
469	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
470	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
471	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
472	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
473	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0
474	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
475	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
476	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
477	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
478	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
479	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
480	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
481	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
482	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
483	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
484	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
485	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
486	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
487	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
488	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
489	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
490	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
491	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0
492	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150 (KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
493	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
494	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
495	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
496	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
497	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
498	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
499	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
500	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
501	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
503	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
504	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
505	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
506	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
507	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
508	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
509	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
510	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
511	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
512	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
513	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
514	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
515	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
516	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
517	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
518	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
519	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
520	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	10/2017	0/0
521	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
522	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
523	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
524	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
525	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
526	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
527	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
528	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
529	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
530	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
531	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
532	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
533	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
534	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
535	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
536	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
537	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
538	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
539	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
540	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0
	<u>National Highways Authority Of India</u>					
541	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	02/2017	0/0
542	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2017	0/0
543	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	07/2017	0/0
544	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
545	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	08/2017	0/0
546	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	08/2017	0/0
547	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	08/2017	0/0
548	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	09/2017	0/0
549	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	09/2017	0/0
550	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2017	0/0
551	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2017	0/0
552	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
553	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	09/2017	0/0
554	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
555	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	10/2017	0/0
556	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	10/2017	0/0
557	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	10/2017	0/0
558	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
559	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	11/2017	0/0
560	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
561	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	11/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
562	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	11/2017	0/0
563	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
564	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	11/2017	0/0
565	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
566	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	12/2017	0/0
567	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	12/2017	0/0
568	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2017	0/0
569	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	12/2017	0/0
570	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2017	0/0
571	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2017	0/0
572	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0
573	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	12/2017	0/0
574	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	12/2017	0/0
575	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	12/2017	0/0
576	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2017	0/0
577	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
578	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
579	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	12/2017	0/0
580	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	12/2017	0/0
581	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	12/2017	0/0
582	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	12/2017	0/0
583	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	12/2017	0/0
584	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
585	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	12/2017	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
586	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	12/2017	0/0
587	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	12/2017	0/0
588	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2018	0/0
589	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
590	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI, HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
591	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
592	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 -	02/2018	0/0
593	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
594	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
595	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
596	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
597	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	02/2018	0/0
598	MAIBANG TO LUMDING (AS-24), KM. 111.000 TO KM. 126.450 - [N240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	03/2018	0/0
599	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 -	03/2018	0/0
600	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	04/2008 -	03/2018	0/0
601	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	03/2018	0/0
602	PANIPAT - JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	03/2018	0/0
603	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	01/2014 -	03/2018	0/0
604	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	03/2018	0/0
605	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	03/2018	0/0
606	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
607	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	03/2018	0/0
608	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2018	0/0
609	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	03/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
610	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	03/2018	0/0
611	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
612	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
613	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
614	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
615	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
616	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
617	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
618	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
619	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	-	03/2018	0/0
620	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	04/2018	0/0
621	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2018	0/0
622	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
623	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2018	0/0
624	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
625	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	-	04/2018	0/0
626	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	-	04/2018	0/0
627	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	-	04/2018	0/0
628	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	-	04/2018	0/0
629	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	05/2018	0/0
630	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	-	05/2018	0/0
631	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	-	05/2018	0/0
632	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	-	05/2018	0/0
633	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	-	05/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
634	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	- -	05/2018	0/0
635	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	05/2018	0/0
636	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
637	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	05/2018	0/0
638	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2018	0/0
639	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	06/2018	0/0
640	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	06/2018	0/0
641	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
642	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
643	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
644	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
645	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
646	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
647	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
648	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	- -	06/2018	0/0
649	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
650	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
651	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
652	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
653	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
654	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	- -	07/2018	0/0
655	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	07/2018	0/0
656	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	08/2018	0/0
657	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
658	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
659	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
660	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	- -	08/2018	0/0
661	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
662	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	10/2018	0/0
663	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
664	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
665	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
666	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
667	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
668	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
669	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
670	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
671	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2018	0/0
672	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
673	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
674	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
675	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	01/2019	0/0
676	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
677	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	02/2019	0/0
678	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	02/2019	0/0
679	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
680	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0
681	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
682	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
683	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	03/2019	0/0
684	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	03/2019	0/0
685	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	03/2019	0/0
686	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	- -	03/2019	0/0
687	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	- -	03/2019	0/0
688	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
689	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	04/2019	0/0
690	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
691	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	04/2019	0/0
692	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	04/2019	0/0
693	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	04/2019	0/0
694	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	04/2019	0/0
695	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	04/2019	0/0
696	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
697	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	05/2019	0/0
698	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
699	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
700	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	05/2019	0/0
701	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	05/2019	0/0
702	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
703	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
704	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
705	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
706	FOUR LANNING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
707	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
708	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	07/2019	0/0
709	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	07/2019	0/0
710	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	08/2019	0/0
711	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	08/2019	0/0
712	4/6 LANNING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	09/2019	0/0
713	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	02/2020	0/0
714	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
715	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
716	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
717	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
718	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
719	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	03/2020	0/0
720	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	03/2020	0/0
721	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
722	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
723	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
724	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
725	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
726	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
727	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
728	4 LANNING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	03/2020	0/0
729	4 LANNING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
730	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2020	0/0
731	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
732	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	04/2020	0/0
733	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
734	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
735	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	05/2020	0/0
736	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0
737	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
738	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
739	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
740	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
741	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
742	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
743	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
744	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
745	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
746	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
747	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
748	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0
749	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	-	0/0
750	JODHPUR - BARMER SECTION OF PACKAGE - I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
751	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
752	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
753	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
754	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
755	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
756	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
757	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
758	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
759	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
760	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
761	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
762	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
763	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
764	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
765	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
766	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
767	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
768	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
769	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
770	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
771	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
772	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
773	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
774	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
775	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
776	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
777	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
778	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
779	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
780	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
781	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
782	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
783	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
784	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
785	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
786	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
787	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
788	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
789	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
790	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
791	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
792	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
793	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
794	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
795	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
796	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0
797	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASTHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
798	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
799	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
800	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
801	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
802	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
803	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
804	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
805	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
806	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
807	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-	0/0
808	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
809	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
810	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
811	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
812	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
813	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
814	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	-	-	0/0
815	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	-	-	0/0
816	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	-	-	0/0
817	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	-	-	0/0
818	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	-	-	0/0
819	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	-	-	0/0
820	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	-	-	0/0
821	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	-	-	0/0
822	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	-	-	0/0
823	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	-	-	0/0
824	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
825	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
826	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
827	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
828	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
829	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
830	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
831	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
832	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
833	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
834	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
835	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
836	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
837	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
838	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
839	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
840	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
841	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
842	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
843	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
844	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
845	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
846	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
National Highways Development Project						
847	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
848	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
849	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
850	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
851	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
852	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
853	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
854	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
855	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
856	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
857	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
858	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
859	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
860	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
861	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
862	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
863	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0
864	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
865	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
<u>Public Works Dept Of State</u>						
866	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
867	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
868	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
869	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
870	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
871	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
872	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
873	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
874	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
875	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
876	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
877	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
878	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
879	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
880	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
881	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
882	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
883	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
884	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
885	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
886	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
887	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
888	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
889	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
890	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
891	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
892	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
893	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
894	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
895	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-	0/0
896	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
897	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
898	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
899	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
900	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
901	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
902	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
903	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
904	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
905	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
906	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
907	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
908	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
909	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
910	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
911	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
912	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
913	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
914	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
915	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
916	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
917	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
918	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
919	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
920	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
921	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
922	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
923	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
924	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
925	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
926	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
927	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
928	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
929	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Kamarajar Port Limited</u>					
930	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
931	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	08/2019	0/0
	<u>Mumbai Port Trust</u>					
932	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
	<u>Port Trust</u>					
933	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	12/2017	0/0
934	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Bharat Sanchar Nigam Limited</u>					
935	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL, MAHARASHTRA	08/2017	159.30 -	04/2018 -	04/2018	0/0
936	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL, MAHARASHTRA	08/2017	167.68 -	04/2018 -	04/2018	0/0
937	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL, MAHARASHTRA	08/2017	212.70 -	05/2018 -	05/2018	0/0
938	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL, MAHARASHTRA	08/2017	215.30 -	05/2018 -	05/2018	0/0
939	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL, GUJARAT	09/2017	171.54 -	05/2018 -	05/2018	0/0
940	UP (EAST) ACCESS LOT1 - [N26000112]BSNL, UTTAR PRADESH	11/2017	169.45 -	08/2018 -	08/2018	0/0
	<u>Department Of Telecommunication</u>					
941	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 04/2020	04/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
942	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	06/2017 -	03/2018	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Bangalore Metro Rail Corporation Limited</u>					
943	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
944	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	12/2015 -	03/2018	0/0
945	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	03/2015 12/2017	03/2018	0/0
946	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 03/2018	04/2018	0/0
947	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]CPWD, KERALA	07/2015	154.00 -	11/2015 05/2018	05/2018	0/0
948	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD, DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
949	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
950	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 -	02/2020 -	02/2020	0/0
951	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD, DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
952	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	06/2017 -	06/2020	0/0
953	CONSTRUCTION OF CENTRAL EXCISE DEPARTMENT AT CR COLONY - [N28000109]CPWD, TAMIL NADU	11/2017	348.77 -	- -	-	0/0
	<u>Chennai Metro Rail Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
954	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	03/2018	0/0
	<u>Delhi Metro Rail Corporation Ltd</u>					
955	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	03/2018	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
956	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
957	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
958	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
959	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
960	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
961	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	Total		10,46,426.91 -			0/0
	Grand Total		10,46,426.91			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,881.40	14.08	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	2,321.00	72.66	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216	1/2016	247.52	247.52	88.97	02/2019 -	12/2018
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	664.00	240.15	12/2020 -	02/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226	2/2016	356.00	356.00	109.51	05/2019 -	12/2018
	Total		10,668.92 -	10,668.92	720.34		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209	1/2016	162.11 -	162.11	124.71	05/2018 -	03/2018
8	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210	1/2016	207.88 -	207.88	105.62	07/2018 -	03/2018
	Total		369.99 -	369.99	230.33		
	<u>RAILWAYS</u>						
	<u>East Coast Railway</u>						
9	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381	4/2015	1,172.92	1,172.92	122.87	03/2021 -	03/2020
	Total		1,172.92 -	1,172.92	122.87		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
10	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498	6/2016	667.00 -	667.00	184.20	07/2018 -	06/2018

Costing Rs. 150 Crore and above

(February 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	23.87	03/2020 -	05/2019
	Total		963.19 -	921.00	208.07		
	Grand Total		13,175.02	13,132.83	1,281.61		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	182.02	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	288.00	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	41.80	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	25.64	03/2019 -	03/2019
6	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	682.47	03/2026 -	03/2026
7	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	30.12	03/2019 -	03/2019
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	371.19	03/2021 -	03/2021
9	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
	<u>Neyveli Lignite Corporation</u>						
10	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	340.71	06/2015 09/2019	09/2019
11	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	5,170.78	12/2015 04/2018	04/2018
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	1,309.20	11/2021 -	11/2021
13	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	168.58	12/2019 -	12/2019
14	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	6.22	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
15	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	434.36	03/2018 -	03/2018
16	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	28.21	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
17	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	72.81	03/2019 -	03/2019
18	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						
19	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	135.60	03/2015 03/2020	03/2020
20	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	77.18	03/2023 03/2021	03/2021
21	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	29.37	03/2022 -	03/2022
22	MADANNAGAR OPENCASE PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
23	VIJAY WEST OPENCASE PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
24	AMADAND OPENCASE EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	111.56	03/2021 -	03/2021
25	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,634.97	03/2023 -	03/2023
26	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,669.22	03/2023 -	03/2023
27	DURGAPUR OPENCASE PROJECT - [N06000136]	2/2015	916.24 -	916.24	.99	03/2023 -	03/2023
28	AMGAON OPENCASE PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	44.19	03/2020 -	03/2020
29	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
30	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	35.61	03/2021 -	03/2021
31	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.47	03/2021 -	03/2021
32	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	50.54	03/2018 -	03/2018
33	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
34	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	51.12	03/2020 -	03/2020
35	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.18	03/2023 -	03/2023
36	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.79	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
37	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	17.31	03/2021 -	03/2021
38	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	86.78	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	.13	03/2022 -	03/2022
40	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	.04	03/2022 -	03/2022
41	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.30	03/2022 -	03/2022
42	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.26	03/2020 -	03/2020
43	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
44	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	231.76	03/2025 -	03/2025
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	73.88	03/2021 -	03/2021
46	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	94.00	03/2020 -	03/2020
47	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	88.13	03/2019 -	03/2019
48	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	371.19	03/2020 -	03/2020
49	GOKUL - [N06000120]	11/2014	267.67 -	267.67	206.04	03/2018 -	03/2018
50	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	237.08	03/2020 -	03/2020
51	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	126.84	03/2019 -	03/2019
52	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	39.89	03/2019 -	03/2019
53	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	139.76	03/2021 -	03/2021
54	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	46.91	03/2020 -	03/2020
	Total		75,174.95 -	73,796.21	16,147.73		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
55	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	172.99	50.97	05/2018 -	05/2018
56	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	296.05	44.22	08/2020 -	08/2020
	Total		453.64 -	469.04	95.19		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	-	11/2019 -	11/2019
58	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	-	11/2019 -	11/2019
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	-	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
60	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	97.94	11/2016 04/2019	04/2019
61	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	482.85	413.01	12/2017 04/2018	04/2018
	Total		1,355.20 -	1,366.85	510.95		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation</u>						
62	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.19	24.38	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
63	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	21.00	05/2018 08/2019	08/2019
64	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	149.00	08/2018 -	08/2018
65	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	77.50	09/2018 -	09/2018
66	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	21.79	03/2019 -	03/2019
67	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	274.19	29.68	03/2019 -	03/2019
	Total		1,822.51 -	1,822.51	323.35		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
68	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	44.60	04/2021 04/2021	04/2021
69	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	288.44	01/2020 01/2020	01/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
70	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
71	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	13.88	11/2020 11/2020	11/2020
	Total		6,912.00 -	6,912.00	346.92		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
72	HALDIA LPG IMPORT FACILITY - [N16000223	3/2015	694.00 -	694.00	253.60	10/2018 -	10/2018
73	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	4,588.29	1,145.97	08/2018 05/2019	05/2019
74	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264	5/2015	337.06 -	337.06	65.87	08/2018 -	08/2018
75	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262	5/2015	193.40 -	193.40	21.08	01/2019 -	01/2019
76	MMPL PIPELINE REROUTING PROJECT - [N16000261	4/2013	449.58 -	449.58	99.26	12/2019 -	12/2019
77	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	45.12	02/2020 -	02/2020
78	ENNORE TERMINAL - [N16000224	8/2014	393.00 -	393.00	259.17	04/2018 -	04/2018
	<u>Chennai Petroleum Corporation Limited</u>						
79	BS-VI PROJECTS - [N16000295	9/2017	1,858.00 -	1,858.00	144.26	12/2019 -	12/2019
80	RE-LIQUIFIED NATURAL GAS - [N16000301	8/2017	421.00 -	421.00	1.15	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
81	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072	3/2015	3,957.00 -	3,397.00	1,771.65	12/2018 -	12/2018
82	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	749.00	564.98	02/2020 -	02/2020
83	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231	7/2015	1,427.94 -	750.00	514.17	12/2018 -	12/2018
84	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232	7/2014	199.95 -	199.95	144.58	03/2018 -	03/2018
85	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289	7/2017	243.53 -	243.53	7.80	07/2022 -	07/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	287.49	39.40	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
87	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	6/2009	2,915.00 2,915.00	2,915.00	1,621.62	12/2012 02/2019	02/2019
88	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	5.73	12/2020 -	12/2020
89	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	11.32	12/2020 -	12/2020
90	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	42.30	12/2020 -	12/2020
91	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	60.27	12/2020 -	12/2020
	<u>Hindustan Petroleum Corporation Limited</u>						
92	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	130.15	09/2017 03/2018	03/2018
93	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB, HARYANA) - [N16000242]	11/2016	230.00 -	230.00	27.90	02/2019 -	02/2019
94	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
95	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	52.19	09/2019 -	09/2019
96	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - - [N16000296]	9/2017	2,677.00 -	2,677.00	5.87	03/2021 -	03/2021
97	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	412.08	06/2020 -	06/2020
	<u>Indian Oil Corporation Limited</u>						
98	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
99	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	4,190.00	2,505.63	09/2017 06/2018	06/2018
100	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	1,659.56	09/2017 12/2018	12/2018
101	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
102	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	-	06/2020 -	06/2020
103	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	26.19	07/2020 -	07/2020
104	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	28.99	12/2019 -	12/2019
105	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	23.16	02/2020 -	02/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	32.47	06/2020 -	06/2020
107	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	74.03	12/2018 -	12/2018
108	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	8.35	12/2020 -	12/2020
109	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	34.75	09/2019 -	09/2019
110	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	282.15	08/2021 -	08/2021
111	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY [N16000248]	7/2015	822.66 -	822.66	390.95	11/2018 -	11/2018
112	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	445.91	11/2019 -	11/2019
113	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	117.83	08/2019 -	08/2019
114	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	1,330.00	1,103.82	06/2018 -	06/2018
115	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	-	09/2019 -	09/2019
116	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	.84	10/2020 -	10/2020
117	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS & HSD, ADDITIONAL TANKS FOR MS,HSD AND BI - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
118	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
119	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	6.02	04/2021 -	04/2021
120	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	28.93	04/2020 -	04/2020
121	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	133.17	01/2019 -	01/2019
122	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD- AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
123	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
124	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
125	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021
126	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
127	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	134.25	07/2018 10/2020	10/2020
128	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	296.05	10/2019 -	10/2019
129	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	196.31	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
130	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	66.12	04/2019 -	04/2019
131	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	96.38	03/2019 -	03/2019
132	BSVI UPGRADEATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	80.45	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
133	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	2,067.29	03/2013 09/2018	09/2018
134	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	115.36	07/2016 06/2018	06/2018
135	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,316.24	04/2019 03/2019	03/2019
136	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	567.22	384.58	11/2019 12/2018	12/2018
137	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	779.10	03/2019 05/2020	05/2020
138	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	170.86	05/2021 -	05/2021
139	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	-	11/2019 11/2019	11/2019
140	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	-	11/2019 11/2019	11/2019
141	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	-	11/2019 11/2019	11/2019
142	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	140.80	05/2019 05/2019	05/2019
143	FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	-	09/2018 09/2018	09/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
144	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	216.56	03/2026 03/2026	03/2026
145	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	-	05/2020 05/2020	05/2020
146	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	253.97	06/2020 06/2020	06/2020
147	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	8.14	03/2023 03/2022	03/2022
148	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	1,314.87	04/2018 04/2018	04/2018
149	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	3,961.54	3,721.54	12/2017 03/2019	03/2019
150	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	161.79	09/2018 09/2018	09/2018
151	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	2,039.15	05/2014 05/2018	05/2018
152	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,729.04	03/2015 03/2018	03/2018
153	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	8.45	01/2014 11/2019	11/2019
154	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,504.61	1,237.43	05/2017 05/2018	05/2018
155	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	2,477.21	05/2019 10/2019	10/2019
156	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	5,578.73	05/2017 05/2018	05/2018
157	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	571.47	542.92	09/2011 06/2019	06/2019
158	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	5,725.50	4,290.94	04/2016 03/2018	03/2018
	<u>Oil India Limited</u>						
159	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	1.42	10/2020 -	10/2020
160	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	7.30	12/2019 -	12/2019
	Total		1,75,051.13 -	1,74,629.04	47,535.33		
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
161	50 MW SOLAR POWER PROJECT - [N18000251]	6/2017	287.48 -	287.48	110.15	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>National Thermal Power Corporation</u>						
162	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	8,722.00	09/2017 06/2019	06/2019
163	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	6,272.00	02/2019 10/2020	10/2020
164	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	306.00	09/2019 02/2022	02/2022
165	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	1,399.00	07/2020 10/2020	10/2020
166	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	4,433.00	09/2019 -	09/2019
167	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	9,341.00	06/2017 06/2019	06/2019
168	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	8,451.00	11/2016 03/2019	03/2019
169	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	16,934.65	15,364.00	01/2017 03/2018	03/2018
170	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	14,283.00	01/2011 04/2021	04/2021
171	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	7,029.00	08/2018 06/2019	06/2019
172	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	1/2008	4,375.35 -	8,150.00	6,984.00	09/2011 06/2018	06/2018
173	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,446.00	03/2013 12/2020	12/2020
	<u>North East Electric Power Corporation</u>						
174	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	6,146.13	12/2009 03/2018	03/2018
175	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,556.85	08/2013 03/2018	03/2018
	<u>Power Grid Corporation Of India Limited</u>						
176	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	3,707.22	04/2018 -	04/2018
177	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	71.53	05/2017 06/2019	06/2019
178	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 -	2,187.32	1,988.93	11/2008 09/2018	09/2018
179	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	29.17	02/2020 -	02/2020
180	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	70.63	02/2019 -	02/2019
181	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	8.59	07/2019 -	07/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
182	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	14.44	09/2018 -	09/2018
183	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	139.00	07/2020 -	07/2020
184	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	1,415.00	04/2019 -	04/2019
185	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]	2/2015	1,750.00 -	1,750.00	761.00	06/2018 -	06/2018
186	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.00	06/2019 -	06/2019
187	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	323.07	04/2020 -	04/2020
188	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	9.11	09/2019 -	09/2019
189	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	19.67	12/2019 -	12/2019
190	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	7.96	06/2019 -	06/2019
191	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	11.35	03/2019 -	03/2019
192	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	17.19	02/2019 -	02/2019
193	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	-	02/2020 -	02/2020
194	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	114.89	04/2019 -	04/2019
195	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	70.81	01/2019 -	01/2019
196	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	7.71	11/2019 -	11/2019
197	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION - [N18000237]	10/2016	167.75 -	167.75	48.78	04/2019 -	04/2019
198	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	1.76	06/2019 -	06/2019
199	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	18.59	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
200	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	42.66	02/2019 -	02/2019
201	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	75.73	02/2019 -	02/2019
202	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	193.70	03/2019 -	03/2019
203	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	48.37	07/2018 -	07/2018
204	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	98.07	12/2018 -	12/2018
205	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	290.24	01/2019 -	01/2019
206	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	60.44	11/2018 -	11/2018
207	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	183.83	04/2019 -	04/2019
208	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.30	363.47	06/2019 -	06/2019
209	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	90.51	06/2018 -	06/2018
210	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	455.95	12/2018 -	12/2018
211	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	992.21	11/2019 -	11/2019
212	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	910.61	05/2019 -	05/2019
213	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	192.91	11/2018 -	11/2018
214	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	191.54	05/2018 -	05/2018
215	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	182.24	04/2018 -	04/2018
216	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	866.47	07/2018 -	07/2018
217	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	833.39	04/2017 03/2018	03/2018
218	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	1,042.50	07/2018 -	07/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
219	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	96.34	10/2018 -	10/2018
220	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	62.63	03/2018 -	03/2018
	<u>Satluj Jal Vidyut Nigam Limited</u>						
221	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	85.72	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
222	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	39.79	09/2020 -	09/2020
	Total		1,81,243.88 -	2,04,317.64	1,10,104.85		
	<u>RAILWAYS</u>						
	<u>Container Corporation Of India</u>						
223	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	385.61	03/2018 -	03/2018
224	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	387.70	375.37	03/2018 -	03/2018
225	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	149.15	03/2018 -	03/2018
226	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	20.03	03/2019 -	03/2019
227	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	241.05	03/2019 -	03/2019
228	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	217.53	03/2019 -	03/2019
229	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	257.28	03/2019 -	03/2019
230	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	8/2016	234.50 -	234.50	.39	03/2019 -	03/2019
231	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]	12/2015	174.00 -	174.00	121.35	03/2019 -	03/2019
	<u>East Central Railways</u>						
232	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
233	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
234	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	119.12	03/2020 -	03/2020
	<u>East Coast Railway</u>						
235	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	71.55	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
236	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	53.02	03/2021 -	03/2021
237	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
	<u>North Central Railway</u>						
238	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
239	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	50.86	03/2022 -	03/2022
	<u>Rail India Technical And Economic Service</u>						
240	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
241	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	22.91	12/2024 -	12/2024
242	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	977.00	830.06	03/2019 -	03/2019
243	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	574.09	12/2026 -	12/2026
244	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,356.10	03/2020 -	03/2020
245	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	695.29	03/2020 -	03/2020
246	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.30	766.30	12/2020 -	12/2020
247	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	729.73	12/2020 -	12/2020
248	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	845.10	03/2019 -	03/2019
249	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	748.08	03/2020 -	03/2020
250	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.16	12/2025 -	12/2025
251	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	32.37	12/2025 -	12/2025
252	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	45.79	12/2024 -	12/2024
	<u>South Central Railway</u>						
253	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
254	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
	<u>South Eastern Railway</u>						
255	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	82.00	03/2020 -	03/2020
256	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	-	12/2021 -	12/2021
257	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	126.44	03/2021 -	03/2021
258	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	-	12/2021 -	12/2021
	<u>West Central Railway</u>						
259	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
260	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
261	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	-	03/2022 -	03/2022
	Total		44,682.64 -	58,420.30	9,085.89		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
262	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
263	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]	1/2015	326.63 327.00	327.00	-	04/2018 -	04/2018
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	56.41	03/2018 -	03/2018
265	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	6.65	05/2018 -	05/2018
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
266	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	5/2015	454.89 -	454.89	22.74	05/2018 -	05/2018
267	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
268	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
269	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
270	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
271	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]	3/2015	235.08 -	235.08	47.81	05/2018 -	05/2018
272	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
273	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
274	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
275	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	30.54	05/2018 -	05/2018
276	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
277	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
278	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
279	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
280	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
	<u>National Highways Authority Of India</u>						
281	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
282	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	-	02/2018 -	02/2018
283	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	-	03/2018 -	03/2018
284	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	673.79	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
285	BIKANER - PHALODI SECTION TO FOUR LANEING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
286	4 LANEING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
287	4 LANEING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	179.92	06/2018 -	06/2018
288	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
289	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
290	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
291	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
292	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	-	03/2020 -	03/2020
293	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
294	FOUR LANEING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
295	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
296	FOUR LANEING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
297	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
298	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020
299	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
300	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
301	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
302	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
303	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
304	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	3/2017	988.34 -	1,043.28	-	03/2020 -	03/2020
305	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	3/2017	1,030.44 -	1,065.51	-	03/2020 -	03/2020
306	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
307	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
308	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
309	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	23.48	03/2020 -	03/2020
310	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	3/2017	1,288.07 -	1,420.00	-	03/2020 -	03/2020
311	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	-	03/2020 -	03/2020
312	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	-	03/2020 -	03/2020
313	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	222.05	06/2018 -	06/2018
314	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	218.34	06/2018 -	06/2018
315	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	130.35	06/2018 -	06/2018
316	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
317	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
318	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
319	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	773.95	03/2018 -	03/2018
320	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
321	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]	2/2017	904.16 -	904.16	6.00	02/2020 -	02/2020
322	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	743.26	03/2018 -	03/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
323	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	567.30	03/2018 -	03/2018
324	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
325	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
	<u>National Highways Development Project</u>						
326	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
327	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.17	06/2018 -	06/2018
328	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
	<u>Public Works Dept Of State</u>						
329	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
330	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
	Total		51,710.60 -	52,412.71	4,039.80		
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
331	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	131.15	03/2018 -	03/2018
332	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
	<u>National Mineral Development Corporation (Nmhc)</u>						
333	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	13,298.64	05/2015 10/2018	10/2018
334	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	28.13	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
335	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	168.02	03/2018 -	03/2018
336	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	38.51	06/2019 -	06/2019
	Total		17,231.06 -	17,231.06	13,753.36		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
337	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	-	04/2018 -	04/2018
338	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 -	05/2018
339	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	05/2018 -	05/2018
340	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	-	08/2018 -	08/2018
341	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	212.70	-	05/2018 -	05/2018
342	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	167.68	-	04/2018 -	04/2018
	<u>Department Of Telecommunication</u>						
343	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	24,664.00	7,642.00	07/2015 04/2020	04/2020
	Total		14,429.97 -	25,759.97	7,642.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
344	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER - [N28000093]	7/2015	154.00 -	154.00	82.18	11/2015 05/2018	05/2018
345	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	1.21	03/2020 -	03/2020
346	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	12/2016	164.00 -	164.00	79.25	01/2018 05/2018	05/2018
347	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]	8/2016	294.00 -	294.00	67.24	04/2019 06/2019	06/2019
348	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
349	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUDEM AP - [N28000108]	1/2018	206.58 -	206.58	-	03/2019 -	03/2019
350	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	-	06/2019 -	06/2019
351	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	1.66	02/2020 -	02/2020
	<u>Chennai Metro Rail Ltd</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
352	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]	6/2016	3,770.00 -	3,770.00	-	03/2018 -	03/2018
	<u>Lucknow Metro Rail Corporation Limited</u>						
353	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>National Building Construcion Corporation Ltd</u>						
354	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,993.00	11/2019 -	11/2019
	Total		16,663.29 -	16,517.29	5,761.31		
	Grand Total		5,86,730.87	6,33,654.62	2,15,346.68		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	06/2018	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	10/2017	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	767.00	06/2017 -	02/2018	11.60
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
6	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2018	87.58
	<u>Singareni Colliers Company Limited</u>						
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2019	80.24
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2020	114.60
	Total		19,411.53 -	20,221.55			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
11	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	172.99	05/2018 -	05/2018	2.97
12	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	296.05	08/2020 -	08/2020	3.51
	Total		453.64 -	469.04			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
13	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	03/2018	13.31
	Total		168.90 -	191.38			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
16	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	11/2017	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
18	CAPACITY ENHANCEMENT/ REVAMP OF NHT- 2/PLATFORMER-2/CCR-2/PSA-2/RSU [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
19	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
20	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	04/2018	1.77
	<u>Oil India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
21	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	11/2018	24.47
22	TWENTY NOS. FEEDER GAS LINES - [N16000192]	03/2009	228.64 -	256.41	12/2016 -	05/2018	12.15
23	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2017	37.72
	Total		8,836.93 -	10,792.59			
	<u>POWER</u>						
	<u>Damodar Valley Corporation</u>						
24	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
25	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
	<u>National Hydro-Electric Power Corporation</u>						
26	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
27	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
28	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,882.01	01/2016 -	03/2018	61.50
	<u>National Thermal Power Corporation</u>						
29	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
30	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
31	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
32	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
33	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	02/2019	49.41
34	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	02/2019	5.91
35	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	03/2018	11.66
36	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
37	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
38	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
	<u>Power Grid Corporation Of India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
39	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	06/2018	30.37
40	SYSTEM STRENGTHENING XII OF SR - [N18000085]	02/2010	232.34 -	341.00	06/2012 -	03/2018	46.77
41	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	426.29	08/2014 -	03/2018	43.37
42	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49
43	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
44	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	03/2018	42.83
	<u>Satluj Jal Vidyut Nigam Limited</u>						
45	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
46	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	11/2020	52.10
47	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	12/2020	165.65
	Total		1,27,462.27 -	1,71,682.12			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
48	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	390.00
49	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	- -	03/2024	120.28
50	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	- -	03/2024	25.04
	<u>East Central Railways</u>						
51	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
52	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
53	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
54	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
55	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
57	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
58	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	<u>East Coast Railway</u>						
59	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
60	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
61	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
62	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
63	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
64	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
65	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
66	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
	<u>Eastern Railways</u>						
67	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
68	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
69	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
70	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
71	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
72	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
73	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
74	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
75	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
77	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
78	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
	<u>Metropolitan Rapid Transport Projects</u>						
79	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
80	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	732.89	06/2013 -	03/2017	47.84
81	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
82	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
83	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
84	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
85	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
86	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
	<u>North East Frontier Railway</u>						
87	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	03/2020	123.75
88	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
89	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
90	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,450.00	04/2008 12/2011	06/2018	263.33
91	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
92	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
93	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2020	290.00
94	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,135.00	- -	03/2020	611.67

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
95	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
96	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
97	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	03/2020	27.24
98	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
99	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
100	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
101	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	- -	07/2019	130.16
102	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	630.00	- -	03/2018	200.33
103	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	450.00	- -	03/2019	58.70
104	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
105	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	03/2020	94.45
106	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
107	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2020	171.38
108	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
109	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	535.00	- -	03/2019	71.41
110	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
111	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	- -	03/2021	.00
112	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	03/2020	10.01
<u>North Eastern Railway</u>							
113	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	- -	04/2018	88.85
114	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
115	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	- -	05/2019	212.37

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
116	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [N220100256]	04/1999	744.71 -	1,126.79	-	-	51.31
117	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10
118	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	308.00	-	-	.33
119	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	-	08/2018	10.26
120	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
121	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	227.00	-	08/2018	13.64
122	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	-	10/2018	61.80
123	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
	<u>North Western Railway</u>						
124	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	895.00	03/2014 -	06/2019	37.02
125	DAUSA-GANGAPUR CITY(NL),NWR - [N220100184]	02/1997	410.08 -	795.01	-	02/2019	93.87
126	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	-	03/2020	14.33
127	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	04/2008	829.74 -	1,143.70	03/2015 -	12/2019	37.84
128	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	-	03/2019	41.64
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,562.27	-	-	23.02
130	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	-	10/2018	24.47
131	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	420.08	-	-	-7.88
132	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	-	02/2019	14.35
133	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	-	10/2018	19.86
134	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	-	03/2019	44.16
	<u>Northern Railway</u>						
135	JIND-SONEPAT (NL),NR - [N220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
136	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	-	-	25.87

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
137	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	-	-	117.77
138	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	-	-	57.68
139	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	-	-	369.31
140	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
141	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,946.00	11/2002 -	12/2018	1,017.84
142	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
143	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
144	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.99	- 09/2009	03/2019	293.18
145	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.07	02/2015 -	12/2019	556.04
146	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	343.00	03/2009 03/2009	12/2017	65.70
147	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2019	48.26
148	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	1,030.00	03/2010 -	03/2018	49.88
149	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
150	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	4,500.00	- -	03/2019	329.85
151	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
152	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,141.70	12/2012 -	-	275.56
153	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2017	70.82
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	12/2020	7.78
155	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	350.00	- -	03/2018	84.11
156	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
157	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
158	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	- -	12/2020	22.24

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
159	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,810.00	-	03/2018	120.09
160	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
161	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	-	9.32
162	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
163	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2019	5.39
164	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
165	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	12/2026	277.53
166	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
167	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,183.30	12/2020 -	12/2020	.00
168	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	<u>Railway Electrification</u>						
169	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
170	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
171	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
172	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
173	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
174	GUDUR-DURGARA JAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
175	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
176	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	607.70	01/1999 -	-	94.00
177	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	-	488.33
178	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
179	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	-	284.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
180	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	-	711.70
	<u>South East Central Railway</u>						
181	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
182	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
	<u>South Eastern Railway</u>						
183	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
184	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
185	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
186	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
187	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	491.33	06/2004 -	-	153.17
188	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	-	40.49
189	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
190	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
191	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
193	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
194	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	-	41.36
195	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
196	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
197	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	<u>South Western Railway</u>						
198	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
199	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
200	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	-	57.65
201	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	-	-	47.93
202	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	-	-	2.29
203	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	-	-	14.14
204	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	-	-	840.53
<u>Southern Railway</u>							
205	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	-	-	141.40
206	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	-	-	491.45
207	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	-	-	300.71
208	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	-	-	412.75
209	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	-	-	210.34
210	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	-	-	404.39
211	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	-	-	411.93
212	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	-	-	147.28
213	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	-	-	348.88
214	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	-	-	78.78
215	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
216	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
217	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	-	-	295.05
218	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71
219	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	-	-	78.83
220	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	-	-	199.29

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
221	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	4,131.90	- -	-	359.10
	<u>West Central Railway</u>						
222	RAMGANJMUHI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	- -	03/2021	273.12
223	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
	<u>Western Railway</u>						
224	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	-	70.85
225	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
226	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
227	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	844.10	- -	-	91.89
	Total		1,07,849.00 -	2,73,569.85			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
228	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
229	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	10/2017	15.30
	<u>National Highways Authority Of India</u>						
230	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2018	28.93
231	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2017	92.75
232	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2018	80.68
233	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2018	68.99
234	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50
235	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	04/2018	42.25
236	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	-	2.29
237	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
238	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	09/2017	2.65
239	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83
240	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
241	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
242	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	03/2020	3.40
243	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	03/2020	5.56
244	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06
245	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
246	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
247	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
248	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
249	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	03/2020	4.02
250	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2020	10.24
251	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
252	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
253	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
Public Works Dept Of State							
254	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
255	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
256	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
257	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12
258	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	.01
259	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
	Total		22,179.94 -	28,654.53			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
260	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	-	18.20
261	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
	<u>Mumbai Port Trust</u>						
262	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
263	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2017	300.00
	Total		959.83 -	1,762.94			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
264	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
265	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Rastrya Ispat Nigam Limited</u>						
266	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,261.61 -	1,777.68			
	<u>TELECOMMUNICATIONS</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(February 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Department Of Telecommunication</u>						
267	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	04/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
268	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
269	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.60
	Total		1,715.39 -	2,090.99			
	Grand Total		3,09,467.11	5,46,798.83			

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2018)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,566.79	09/2010 09/2016	06/2018	93	21
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	11,285.00	12/2015 11/2016	11/2019	47	36
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	8,887.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	2,133.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	69,728.00	27,871.79				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.44	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	26.44				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	161.38	05/2014 -	04/2018	47	-
7	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	163.95	04/2014 -	04/2018	48	-
8	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
9	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	273.25	04/2015 -	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
10	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	347.96	03/2016 -	03/2018	24	-
11	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	98.15	03/2012 -	03/2019	84	-
12	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	154.01	03/2012 -	03/2019	84	-
13	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60	-
14	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.28	03/2011 -	03/2020	108	-
15	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	120.77	07/2012 -	03/2021	104	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Eastern Coal Fields Limited</u>								
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	336.18	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
17	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	331.07	03/2010 -	03/2018	96	-
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	299.61	03/2017 -	05/2018	14	-
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	478.12	03/2013 -	11/2018	68	-
20	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	201.18	03/2010 -	03/2019	108	-
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	209.07	03/2012 -	03/2019	84	-
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	222.60	03/2013 -	03/2019	72	-
	<u>Neyveli Lignite Corporation</u>								
23	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC, TAMIL NADU	05/2016	687.28 -	767.00	749.25	06/2017 12/2017	02/2018	8	2
	<u>Northern Coal Fields Limited</u>								
24	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 -	486.57	399.01	03/2012 -	03/2018	72	-
	<u>Singareni Colliers Company Limited</u>								
25	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	154.52	03/2015 -	03/2018	36	-
26	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	159.87	03/2012 -	03/2018	72	-
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	125.24	06/2015 -	03/2018	33	-
28	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	149.50	03/2016 -	03/2018	24	-
29	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	448.86	185.65	03/2012 -	03/2019	84	-
30	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
31	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	.37	03/2015 -	03/2020	60	-
32	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	349.28	1.31	03/2015 -	03/2020	60	-
33	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	114.71	07/2016 -	03/2020	44	-
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	437.51	-	03/2015 -	03/2021	72	-
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	48.57	03/2012 -	03/2023	132	-
	<u>South-Eastern Coal Fields Limited</u>								
36	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	153.81	03/2016 -	03/2018	24	-
37	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
39	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	200.64	03/2014 -	03/2020	72	-
	<u>Western Coal Fields Limited</u>								
40	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94 409.68	409.68	86.03	03/2023 02/2017	03/2023	0	73
	Total		12,924.33 -	13,807.08	6,290.58				
	<u>STEEL</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
41	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY- JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	253.92	193.97	06/2016 -	03/2018	21	-
42	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-
43	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
44	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
45	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Rastriya Ispat Nigam Limited</u>								
46	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	120.00	07/2018 -	09/2018	2	-
47	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	786.45	12/2017 -	10/2018	10	-
48	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	37.04	08/2018 -	10/2018	2	-
49	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	178.10	09/2018 -	01/2019	4	-
50	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	236.32	10/2016 -	03/2019	29	-
	<u>Steel Authority Of India Limited (Sail)</u>								
51	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	18,560.44	03/2013 -	02/2018	59	-
52	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	614.96	12/2017 -	11/2018	11	-
53	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	213.12	10/2017 -	12/2018	14	-
54	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,018.18	04/2018 -	02/2019	10	-
	Total		30,588.39 -	30,375.79	23,902.24				

Costing Rs. 150 Crore and above

(February 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
	<u>Chennai Petroleum Corporation Limited</u>								
55	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	202.35	11/2016 -	06/2018	19	-
	<u>Gas Authority Of India Limited</u>								
56	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	47.80	04/2018 -	07/2018	3	-
	<u>Hindustan Petroleum Corporation Limited</u>								
57	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	449.68	10/2014 03/2018	02/2019	52	11
	<u>Indian Oil Corporation Limited</u>								
58	FUEL QUALITY UPGRADATION (DHD/DHDS) PROJECT AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	470.76	07/2017 -	02/2018	7	-
59	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	315.63	10/2017 -	03/2019	17	-
	<u>Oil & Natural Gas Corporation Limited</u>								
60	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 181.02	181.02	168.93	01/2017 03/2018	05/2018	16	2
61	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,188.01	05/2013 03/2018	11/2018	66	8
62	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	390.52	97.34	03/2019 -	04/2019	1	-
	<u>Oil India Limited</u>								
63	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	256.41	147.21	12/2016 -	05/2018	17	-
64	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	146.36	03/2017 -	11/2018	20	-
65	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	1.03	01/2019 -	09/2019	8	-
	Total		4,798.05 -	5,700.03	3,235.10				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
66	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	893.51	04/2020 -	06/2023	38	-
	<u>National Hydro-Electric Power Corporation</u>								
67	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,882.01	5,233.88	01/2016 -	03/2018	26	-
68	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,652.65	09/2009 -	12/2020	135	-
	<u>National Thermal Power Corporation</u>								
69	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	6,974.42	05/2014 03/2017	02/2019	57	23

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
70	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	-	01/2018 -	02/2019	13	-
71	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,957.91	12/2016 -	02/2019	26	-
72	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	3,918.00	03/2019 03/2019	09/2019	6	6
73	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	3,004.00	-	11/2019 -	12/2019	1	-
	<u>Power Grid Corporation Of India Limited</u>								
74	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,630.98	08/2013 12/2017	03/2018	55	3
75	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	341.00	246.94	06/2012 -	03/2018	69	-
76	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,436.82	11/2012 12/2017	03/2018	64	3
77	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	426.29	375.94	08/2014 12/2017	03/2018	43	3
78	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	137.13	09/2014 09/2017	03/2018	42	6
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 882.13	882.13	734.04	11/2014 06/2017	03/2018	40	9
80	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	156.45	04/2016 12/2017	03/2018	23	3
81	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	143.08	03/2016 07/2017	03/2018	24	8
82	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,113.00	12/2015 -	03/2018	27	-
83	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,746.00	11/2017 -	03/2018	4	-
84	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,287.00	01/2018 -	03/2018	2	-
85	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	142.77	02/2016 08/2017	04/2018	26	8
86	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,610.29	12/2012 02/2018	06/2018	66	4
87	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	587.18	06/2015 12/2017	06/2018	36	6
88	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	2,125.29	12/2015 12/2017	06/2018	30	6
89	EASTERN REGION STRENGTHENING SCHEME- V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,183.35	04/2016 09/2017	06/2018	26	9

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	399.39	06/2016 02/2018	06/2018	24	4
91	EASTERN REGION STRENGTHENING SCHEME- XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	389.04	11/2016 11/2017	06/2018	19	7
92	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	234.00	02/2017 06/2017	06/2018	16	12
93	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	185.89	03/2018 -	06/2018	3	-
94	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,395.80	09/2014 06/2017	09/2018	48	15
95	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	541.66	09/2017 -	09/2018	12	-
96	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,354.03	04/2018 -	09/2018	5	-
97	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	168.46	03/2017 10/2017	09/2018	18	11
98	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,223.54	09/2017 -	09/2018	12	-
99	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	160.59	10/2017 10/2017	10/2018	12	12
100	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 5,135.01	5,135.01	3,683.22	01/2015 03/2018	11/2018	46	8
101	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	659.02	09/2010 12/2017	12/2018	99	12
102	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,507.26	10/2012 02/2018	12/2018	74	10
103	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	177.40	07/2017 -	12/2018	17	-
104	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	178.76	11/2017 -	12/2018	13	-
105	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	487.29	06/2014 03/2018	03/2019	57	12
106	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	1,894.73	03/2018 -	03/2019	12	-
107	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	263.03	01/2018 -	03/2019	14	-

Costing Rs. 150 Crore and above

(February 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
108	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	4,754.42	541.38	12/2018 -	12/2019	12	-
109	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	5,111.33	429.76	12/2018 -	12/2019	12	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
110	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	197.07	11/2017 -	03/2018	4	-
111	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	481.23	12/2016 -	12/2018	24	-
	<u>Thdc India Limited</u>								
112	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	158.67	02/2014 02/2018	03/2019	61	13
113	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,344.53	06/2013 -	11/2020	89	-
114	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,458.96	02/2016 09/2019	12/2020	58	15
	Total		1,25,701.73 -	1,48,563.80	82,801.34				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
115	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	191.38	110.00	05/2017 -	03/2018	10	-
116	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	147.30	05/2017 -	06/2018	13	-
117	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	39.00	02/2018 -	08/2018	6	-
118	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	217.60	05/2017 -	09/2018	16	-
119	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	505.58	257.00	03/2018 -	09/2018	6	-
	Total		1,325.52 -	1,348.00	770.90				
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
120	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	-
	<u>East Coast Railway</u>								
121	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	48.52	03/2021 -	03/2022	12	-
122	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	34.98	03/2021 -	03/2022	12	-
	<u>Eastern Railways</u>								

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
123	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	757.23	- 12/2009	03/2019	-	111
124	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
	<u>Metropolitan Rapid Transport Projects</u>								
125	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
126	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
127	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	801.59	03/2004 -	03/2020	192	-
	<u>North Central Railway</u>								
128	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
129	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
	<u>North East Frontier Railway</u>								
130	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 -	5,450.00	4,965.44	04/2008 12/2011	06/2018	122	78
131	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,040.00	2,842.53	12/2008 -	03/2019	123	-
132	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	9,658.00	7,211.12	03/2011 -	03/2020	108	-
133	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	2,550.24	03/2014 -	03/2020	72	-
134	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	4,600.00	1,928.11	04/2014 -	03/2020	71	-
135	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
136	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	3,000.00	428.38	03/2015 -	03/2020	60	-
	<u>North Western Railway</u>								
137	DAUSA-GANGAPUR CITY (NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 780.98	795.01	388.59	- 02/1997	02/2019	-	264
138	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	895.00	685.07	03/2014 -	06/2019	63	-
139	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	1,143.70	554.05	03/2015 -	12/2019	57	-
	<u>Northern Railway</u>								
140	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 19,565.00	27,946.00	16,131.46	11/2002 -	12/2018	193	-
	<u>Rail Vikas Nigam Ltd.</u>								
141	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	1,030.00	1,027.36	03/2010 -	03/2018	96	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
142	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.50	729.94	03/2016 -	12/2018	33	-
143	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.99	1,078.57	- 09/2009	03/2019	-	114
144	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.07	488.99	02/2015 -	12/2019	58	-
145	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	388.00	348.52	02/2006 -	12/2019	166	-
146	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,568.77	03/2008 06/2008	03/2020	144	141
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,567.98	03/2016 -	12/2020	57	-
	<u>South East Central Railway</u>								
148	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
	<u>South Western Railway</u>								
149	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	341.68	- 11/2015	03/2020	-	52
	<u>West Central Railway</u>								
150	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
151	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	81.96	03/2012 -	03/2019	84	-
152	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 816.86	385.60	387.69	03/2013 -	03/2020	84	-
	Total		42,271.83 -	1,14,376.72	54,572.53				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
153	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
154	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
155	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
157	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
158	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 -	02/2018	117	-
159	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	-	11/2016 -	02/2018	15	-
160	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2018	112	-
161	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 -	03/2018	117	-
162	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 -	03/2018	119	-
163	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	-	07/2009 -	03/2018	104	-
164	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	-	11/2011 -	03/2018	76	-
165	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	03/2018	50	-
166	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	-	07/2013 -	03/2018	56	-
167	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	03/2018	42	-
168	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,945.82	08/2013 -	03/2018	55	-
169	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	551.12	07/2014 -	03/2018	44	-
170	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	416.83	06/2014 -	03/2018	45	-
171	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	03/2018	49	-
172	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,375.60	09/2016 -	03/2018	18	-
173	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	283.32	09/2017 -	03/2018	6	-
174	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,104.55	06/2012 -	03/2018	69	-
175	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	309.56	-	04/2010 -	04/2018	96	-
176	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	-	03/2014 -	04/2018	49	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
177	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	-	10/2017 -	04/2018	6	-
178	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	-	02/2009 -	05/2018	111	-
179	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	-	02/2013 -	06/2018	64	-
180	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	261.09	86.28	05/2017 -	06/2018	13	-
181	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	186.50	11/2016 -	06/2018	19	-
182	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
183	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	340.37	06/2016 -	06/2018	24	-
184	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	149.66	07/2016 -	07/2018	24	-
185	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	769.28	11/2017 -	08/2018	9	-
186	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	09/2018	118	-
187	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	10/2018	114	-
188	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	-
189	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	-
190	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	-
191	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	-
192	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	12/2018	12	-
193	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,476.75	08/2016 -	02/2019	30	-
194	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	03/2019	44	-
195	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2019	36	-
196	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	-
197	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	-	03/2020 -	05/2020	2	-

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	-	03/2020 -	05/2020	2	-
199	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	-	03/2020 -	06/2020	3	-
	<u>Public Works Dept Of State</u>								
200	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
	Total		35,576.13 -	38,136.91	14,130.38				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
201	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	-	12/2017 -	08/2019	20	-
	<u>Mumbai Port Trust</u>								
202	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	411.12	12/2010 -	12/2018	96	-
	Total		966.39 -	927.36	411.12				
	<u>TELECOMMUNICATIONS</u>								
	<u>Mahanagar Telephone Nigam Limited</u>								
203	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	418.26	172.30	06/2017 -	03/2018	9	-
	Total		418.26 -	418.26	172.30				
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
204	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
205	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	25.91	10/2012 04/2017	03/2018	65	11
206	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	545.04	12/2015 -	03/2018	27	-
207	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	443.73	03/2015 12/2017	03/2018	36	3

Costing Rs. 150 Crore and above

(February 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	321.00	297.34	09/2016 03/2018	04/2018	19	1
209	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	296.50	03/2016 12/2017	04/2018	25	4
210	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	126.35	08/2016 -	06/2018	22	-
211	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	170.62	149.22	03/2012 03/2018	06/2018	75	3
212	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	316.80	05/2017 02/2018	06/2018	13	4
213	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	134.18	11/2014 -	10/2018	47	-
214	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
215	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	39.91	03/2016 -	12/2018	33	-
216	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	47.29	04/2018 -	05/2019	13	-
217	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
218	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	160.53	10/2019 -	03/2020	5	-
219	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	-	06/2017 -	06/2020	36	-
	<u>Delhi Metro Rail Corporation Ltd</u>								
220	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	34,270.32	03/2016 -	03/2018	24	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
221	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
222	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	2,604.63	03/2018 -	12/2019	21	-
	Total		84,227.01 -	84,946.10	41,901.21				
	Grand Total		4,06,232.25	5,08,769.38	2,56,085.93				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492	93
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3&4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	NEYVELI SOLAR POWER PROJECT 130 MW	NLC	05/2016	06/2017	02/2018	687.28	8
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2018	365.01	33
9	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
10	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
11	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
12	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
13	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	04/2018	269.82	48
14	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2018	302.96	96
15	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24
16	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
17	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
18	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
19	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
20	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2018	209.78	36
22	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	84
23	KISTARAM OCP	SCCL	11/2010	03/2015	03/2020	242.29	60
24	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
25	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
26	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2018	181.19	72
27	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
28	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
29	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	04/2018	289.45	47
30	MURAIIDH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
31	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
32	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.4	72
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
38	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
39	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
40	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
42	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	08/2019	363.99	15
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	6
46	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	03/2018	168.9	10
47	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	08/2018	152.95	6
48	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16
49	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	06/2018	204.44	13

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
51	NEW 250 TMTA LPG PLANT AT PANAGARH	HPCL	08/2014	09/2017	03/2018	190.45	6
52	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
53	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
54	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	05/2018	2899.93	12
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
56	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
57	SIX PIPELINE REPLACEMENT PROJECT	ONGC	03/2009	01/2017	05/2018	181.02	16
58	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74
59	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	09/2018	2465.15	66
60	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
61	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2019	736.65	93
62	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT	OIL	07/2011	03/2017	11/2018	352.56	20

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	AT MADHUBAN						
63	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
64	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	23
65	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
66	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
67	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
68	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	05/2018	228.64	17
69	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	06/2018	257.87	19
70	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
71	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	11/2018	861.79	66
72	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2018	2592.17	48
73	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52
74	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7
75	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
76	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	03/2018	723.63	40
78	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	03/2018	15166.19	14
79	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
80	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846	24
81	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	06/2018	514.2	36
82	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	06/2018	2514.88	30
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	09/2018	305.04	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
84	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
85	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
86	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
87	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
88	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20
89	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
90	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	10/2018	871.62	12
91	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	12/2018	203.28	17
92	EASTERN REGION STRENGTHENING SCHEME- III	PGCIL	07/2010	11/2012	03/2018	1272.8	64
93	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	09/2018	1071.24	12
94	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	03/2018	232.34	69
95	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	06/2018	522.29	19
96	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	03/2018	155.57	24
97	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
98	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2018	4375.35	81
99	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPSPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	12
100	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	06/2018	288.49	16
101	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	04/2018	196.58	26
102	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	06/2023	8112.12	38
103	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
104	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
105	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353	57
106	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
107	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	03/2018	1479.3	11
108	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	12/2018	307.18	13
109	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	89
110	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	48
111	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955	27
112	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	02/2019	12964.6	13
113	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	02/2019	9750.89	26
114	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	135
115	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	99
116	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2018	4824.12	74
117	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	11/2018	4404.57	46
118	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
119	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2018	11130.19	55
120	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2018	2144	66
121	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2018	1364.52	26
122	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	03/2018	374.63	23
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	06/2018	539.82	24
124	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657	58
125	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2019	487.49	57
126	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	55
127	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2018	297.33	43
128	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	03/2018	3642.04	26
129	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
130	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123
131	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	03/2018	198.63	42
132	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.9	99
133	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
134	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
135	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	06/2018	4874.58	27
136	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	57
137	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
139	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
140	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
141	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
142	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.2	96
143	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
144	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTPT	03/1996	03/2004	03/2020	495.44	192
145	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
146	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
147	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
149	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
150	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
151	MUMBAI URBAN TRANSPORT PROJECT PHASE-	MRTPT	04/2008	03/2014	03/2019	5300	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	II						
152	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
153	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
155	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	63
156	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
157	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
158	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
159	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	12
160	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
161	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
162	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	12

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
163	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00)	NHIDCL	03/2016	08/2016	08/2019	429.52	36
164	4-LANING OF BRAHMAPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55
165	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	02/2019	1655.01	30
166	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	05/2018	280	111
167	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	09/2018	167.64	118
168	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	112
169	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	10/2018	200	114
170	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	02/2018	160	117
171	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2018	196	104
172	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2018	217.61	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	07/2018	641.17	24
174	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA)	PWD	12/2011	08/2015	03/2018	191.08	31
175	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
176	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2018	671.3	64
177	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374	67
178	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2018	485	64
179	JORBAT - BARAPANI	NHAI	01/2011	01/2014	03/2018	536	50
180	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	03/2018	575	56
181	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	03/2018	702.16	44
182	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108	76
183	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	03/2018	1348.2	49
184	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
185	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2018	1266.6	18
186	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2018	1250	60
187	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571	62
188	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2018	2848	49
189	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	03/2018	1410	42
190	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	03/2018	208	119
191	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	03/2018	225	117
192	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2018	942.69	45
193	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	03/2018	709	6
194	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2018	1387.11	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	12/2018	563.92	12
196	FOUR LANING OF VARANASI BYPASS	NHAI	05/2015	05/2017	06/2018	261.09	13
197	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	06/2018	563.92	19
198	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2018	597	6
199	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
200	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
201	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
202	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
203	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
204	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
205	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
206	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	08/2019	600	20
208	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
209	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	10/2018	2858	10
210	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
211	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	02/2018	17265	59
212	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	HSCL	12/2007	06/2016	03/2018	253.92	21
213	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSCL	05/2015	03/2017	08/2018	189	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
214	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HACL	04/2014	09/2017	12/2018	151.33	15
215	IRRIGATION WORK OF BAGMATI	HACL	10/2005	03/2015	03/2021	956	72
216	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HACL	02/2014	12/2016	12/2018	787.29	24
217	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2018	15525	41
218	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2018	1154.18	11
219	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2018	1034.01	14
220	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
221	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	MTNL	06/2016	06/2017	03/2018	418.26	9
222	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	04/2020	13334	57

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
223	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
224	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER	CPWD	07/2015	11/2015	05/2018	154	30
225	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
226	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2018	165.23	65
227	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	04/2018	241.33	25
228	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2018	270.83	47
229	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	04/2018	332.72	19
230	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2018	350.02	36
231	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
232	NSG AT KOLKATA	CPWD	10/2014	04/2018	05/2019	162.88	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
233	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
234	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	06/2018	388	13
235	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	06/2018	156.57	22
236	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2018	171.86	33
237	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	06/2018	205	75
238	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	03/2018	884.3	27
239	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
240	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	03/2018	38585	24
241	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
8	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPR	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
14	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
15	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
19	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
20	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
21	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	5725.5	1601.15
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
25	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
27	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5882.01	2239.97
28	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	426.29	128.96
29	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
30	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
31	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
32	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3789.61	1298.03
35	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	232.34	341	108.66
36	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
37	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
38	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
41	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
42	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
43	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
44	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	723.63	882.13	158.5
45	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
46	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
48	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
49	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
50	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
51	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
52	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
53	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
54	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
55	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
56	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
57	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
58	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
59	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
60	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
61	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	4404.57	5135.01	730.44

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
62	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
63	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	N.A.	36.8	614	577.2
64	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
65	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	920	764.45
66	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
67	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
68	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
69	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
70	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
71	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	343	209.59
72	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.07	1018.84
73	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
74	HATHUA-BHATNI (N L) (NER)	NER	04/2005	N.A.	230.03	718.54	488.51
75	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	245.39	125.39
76	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	412.05	193.86
77	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	N.A.	470.92	2713.09	2242.17
78	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
79	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
80	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
81	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
82	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
83	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
84	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
85	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
86	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
87	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
88	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5450	3950
89	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84
90	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
91	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
92	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
93	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
94	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	607.7	294.46
95	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
96	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
97	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	1514.45	1750	235.55
98	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2026	4295.3	16216	11920.7
99	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
100	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	900	4131.9	3231.9
101	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
102	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
103	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	03/2021	701.61	810.02	108.41
104	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
105	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
106	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	3246.26	3548.67	302.41
107	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
108	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
109	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
110	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
111	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	N.A.	2750	3438.51	688.51
112	PUNE-NASIK (265 KM)	CR	02/2016	N.A.	2425	5341.68	2916.68
113	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
114	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1800	1198.57
115	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
116	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
117	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	535	222.88
118	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
119	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
120	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
121	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
122	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
123	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
124	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
125	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
126	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	283.55	450	166.45
127	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	630	420.23
128	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	580	328
129	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
130	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
131	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1810	987.61
132	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
133	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
134	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
135	ATTIPPATTU PUTTUR	SR	04/2008	N.A.	446.87	1105	658.13
136	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
137	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
138	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
139	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
140	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
141	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
142	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
143	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
144	DIGHA-JALESWAR INCLUDING MM FOR DIGHA- EGRA	SER	04/2010	N.A.	553.63	1009	455.37
145	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
146	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
147	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	N.A.	242.09	349	106.91
148	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
149	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2562.27	479.52
150	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	N.A.	1266.89	1548.66	281.77
151	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	858.96	538.3
152	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	844.1	404.22
153	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
154	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
155	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	348.55	102.47
156	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	477.31	182.31
157	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
158	NANGALDAM-TALWARA(NL),NR	NR	03/1981	07/2012	450	2100	1650
159	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	N.A.	410.08	795.01	384.93
160	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
161	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
162	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
163	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
164	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
165	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
166	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2135	1835
167	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	2815.62	2265.62
168	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.97	195.96
169	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
170	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1143.7	313.96
171	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
172	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	1389.62	2446.85	1057.23
173	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
174	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	227	2135	1908
175	RANCHI-LOHARDAGA(GC),SER	SER	04/1997	06/2004	194.07	491.33	297.26
176	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
177	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
178	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
179	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
180	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	350	159.9
181	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
182	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
183	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24
184	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
185	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	555	230.1
186	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	1141.7	837.7
187	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
188	JALANDHAR-PATHANKOT- JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
189	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27946	25446
190	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
191	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	732.89	237.15
192	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44
193	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
194	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3040	2307
195	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
196	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
197	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
198	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
199	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
200	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
201	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
202	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
203	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
204	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
205	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	4500	3453.12
206	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
207	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
208	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
209	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
210	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	2300	1844
211	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
212	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
213	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	1030	342.8
214	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
215	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
216	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	3168.29	2668.99
217	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
218	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	895	241.81
219	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	12/2006	1049.69	3404.92	2355.23
220	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
221	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
222	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
223	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
224	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.99	884.35
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
225	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
226	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
227	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
228	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
229	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
230	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
231	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
232	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
233	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
234	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
235	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
236	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
237	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
238	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
239	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
241	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2018)

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
242	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCCL	05/2005	02/2014	768.88	1113.34	344.46
243	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
245	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
246	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
247	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
248	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
249	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	06/2018	3492.00	6100.00	2608	93

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2020	162.76	349.28	186.52	60
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
5	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2018	259.40	486.57	227.17	72
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2019	249.03	448.86	199.83	84

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	723.40	413.59	52
8	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36
9	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
10	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	11/2018	861.79	1256.72	394.93	66
11	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076.00	4190.00	1114	9
12	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	714.25	107.19	17
13	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	03/2018	4124.35	5725.50	1601.15	23
14	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)-DRASS- KARGIL-KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	2333.71	545.3	12
16	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	1,1846.00	1,2739.82	893.82	24
17	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	06/2018	514.20	703.10	188.9	36
18	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	1,5095.67	6402.7	123
19	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	03/2018	3642.04	5882.01	2239.97	26
20	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2018	573.99	1337.76	763.77	55
21	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	03/2018	232.34	341.00	108.66	69
22	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	02/2019	5353.00	7998.00	2645	57
23	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	602.44	165.76	24
24	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	11/2020	2491.58	3789.61	1298.03	89
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2018	2496.90	6179.96	3683.06	99
26	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	2702.65	762.52	48
27	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	12/2020	1657.00	4401.90	2744.9	58
28	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2019	487.49	639.46	151.97	57
29	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	03/2018	297.33	426.29	128.96	43
30	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	738.48	260.79	99

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2018	4824.12	5071.94	247.82	74
32	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
33	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2018	4375.35	8150.00	3774.65	81
34	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	1,2532.44	1,3740.53	1208.09	10
35	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	1,4366.58	1,5164.05	797.47	20
36	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	03/2018	1272.80	1731.10	458.3	64
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
38	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	03/2018	1,5166.19	1,6934.65	1768.46	14
39	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	03/2018	723.63	882.13	158.5	40
40	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	03/2018	955.00	1364.00	409	27
41	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	02/2019	1,2964.60	1,3731.26	766.66	13
42	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	8398.75	4479.16	135
43	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	11/2018	4404.57	5135.01	730.44	46
44	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	1,1638.55	1,2865.92	1227.37	21
45	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2018	1,1130.19	1,3762.80	2632.61	55
46	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	06/2018	2144.00	2932.88	788.88	66
47	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2018	1364.52	1891.41	526.89	26

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
48	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
49	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR)	NWR	04/2008	03/2015	12/2019	829.74	1143.70	313.96	57
50	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261
51	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34
52	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	4259.48	307.5	57
53	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
54	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
55	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
56	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
57	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
58	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)	NWR	04/2008	03/2014	06/2019	653.19	895.00	241.81	63
59	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192
60	MANDARHILL - DUMKA - RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
61	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5450.00	3950	122
62	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
63	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3040.00	2307	123

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
65	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.07	1018.84	58
66	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.70	388.00	126.3	166
67	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	03/2018	687.20	1030.00	342.8	96
68	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
69	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	2,7946.00	25446	193

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
70	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2018	196.00	331.23	135.23	104
71	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	03/2018	1108.00	2288.00	1180	76
72	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2018	155.04	280.13	125.09	112

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
73	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
74	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343.00	488.40	145.4	29

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
75	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	04/2020	1,3334.00	2,4664.00	11330	57

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
76	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
77	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	04/2018	241.33	349.33	108	25
78	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	03/2018	350.02	479.87	129.85	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	12/2017	.00	47
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	07/2017	.00	50
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	10/2017	.00	53
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	08/2017	.00	87
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2017	.00	49
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	-	.00	0
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	03/2018	.00	50
11	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
12	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
13	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2017	.00	42
14	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	03/2018	.00	56
15	DEOLI KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51
16	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
17	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2017	.00	64

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
18	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	-	.00	0
19	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	06/2019	.00	0
20	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00	650.00	11/2013	08/2017	.00	45
21	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00	664.00	02/2014	-	.00	0
22	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	06/2018	.00	64
23	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16	702.16	07/2014	03/2018	.00	44
24	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	11/2017	.00	56
25	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	06/2019	.00	0
26	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	04/2018	.00	0
27	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36	830.36	07/2018	07/2018	.00	0
28	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	11/2017	.00	12
29	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
30	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	01/2018	.00	6
31	4-LANING OF BRAHMAPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	03/2018	.00	55
32	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00	1,046.00	09/2013	10/2017	.00	49
33	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	12/2017	.00	42
34	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	12/2017	.00	52
35	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	12/2017	.00	42
36	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	08/2017	.00	48
37	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,206.10	04/2013	09/2017	2.65	53
38	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	12/2018	.00	60

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
39	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,266.60	09/2016 -	03/2018	.00	18
40	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00 -	1,267.00	06/2013 -	09/2017	.00	51
41	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	03/2018	.00	49
42	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	- -	08/2018	.00	0
43	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00 -	1,393.00	- -	01/2018	.00	0
44	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	12/2017	.00	39
45	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	03/2018	.00	42
46	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	12/2017	.00	30
47	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00 -	1,535.00	05/2014 -	06/2017	.00	37
48	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00 -	1,573.00	09/2015 -	10/2017	.00	25
49	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79 -	1,583.79	- -	01/2019	.00	0
50	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00 -	1,585.00	05/2013 -	12/2017	.00	55
51	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	09/2017	51.83	22
52	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01 -	1,655.01	08/2016 -	02/2019	.00	30
53	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20 -	1,657.20	- -	01/2019	.00	0
54	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	1,665.00	- -	12/2017	.00	0
55	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70 -	1,673.70	10/2011 -	12/2017	.00	74
56	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75 -	1,693.75	08/2011 -	09/2017	.00	73
57	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55 -	1,724.55	03/2013 -	12/2017	.00	57
58	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76 -	1,813.76	07/2013 -	11/2017	.00	52
59	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34 -	1,871.34	01/2018 -	01/2018	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
60	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79 -	1,916.79	11/2016 -	02/2018	.00	15
61	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22 -	1,928.22	04/2015 -	12/2017	.00	32
62	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00 -	1,987.00	07/2015 -	03/2019	.00	44
63	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	07/2017	.00	19
64	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
65	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
66	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2018	106.50	76
67	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
68	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	12/2017	.00	40
69	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2018	.00	49
70	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	12/2017	114.56	63
	Total		81,844.48 -	85,331.12				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
71	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	-	18.20	0
72	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0
	<u>Mumbai Port Trust</u>							
73	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,162.94				
	Grand Total		82,654.31	86,494.06				
