

**436th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
February, 2022**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for February 2022 contains information on the status of the 1565 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1565 projects, 46 projects are added and 66 projects (27 projects of Railways, 25 projects of Road Transport and Highways, 5 Project of Power, 3 projects of Petroleum, 2 project each of Fertilizers & Urban development and 1 project each of Coal & Water Resources sector) are completed. 647 projects are delayed with respect to their original schedules and 217 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 217 projects, 29 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S.No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report
1	ROAD TRANSPORT AND HIGHWAYS	854	235	67
2	RAILWAYS	211	131	53
3	PETROLEUM	144	84	21
4	COAL	103	31	9
5	POWER	76	50	13
6	WATER RESOURCES	41	38	16
7	HEALTH AND FAMILY WELFARE	28	4	8
8	URBAN DEVELOPMENT	27	16	8
9	DEPARTMENT OF HIGHER EDUCATION	23	16	1
10	CIVIL AVIATION	19	17	11
11	STEEL	7	4	2
12	MINES	6	6	1
13	ATOMIC ENERGY	5	4	0
14	HOME AFFAIRS	5	5	2
15	TELECOMMUNICATIONS	3	3	2
16	FINANCE	2	0	0
17	FERTILISERS	2	1	2
18	DPIIT	2	1	0
19	HEAVY INDUSTRY	1	0	0
20	SHIPPING AND PORTS	1	0	0
21	SOCIAL JUSTICE	1	0	0
22	DEFENCE PRODUCTION	1	1	1
23	COMMERCE	1	0	0
24	DONER	1	0	0
25	RENEWABLE ENERGY	1	0	0
		1565	647	217

3. Total original cost of implementation of the 1565 projects was ₹21,86,542.05 crore and their anticipated completion cost is likely to be ₹26,59,914.61 crore, which reflects overall cost overruns of ₹4,73,352.56 crore (21.65% of original cost). The expenditure incurred on these projects till February 2022 is ₹13,26,569.75 crore, which is 49.87% of the anticipated cost of the projects. The information can be viewed graphically as:

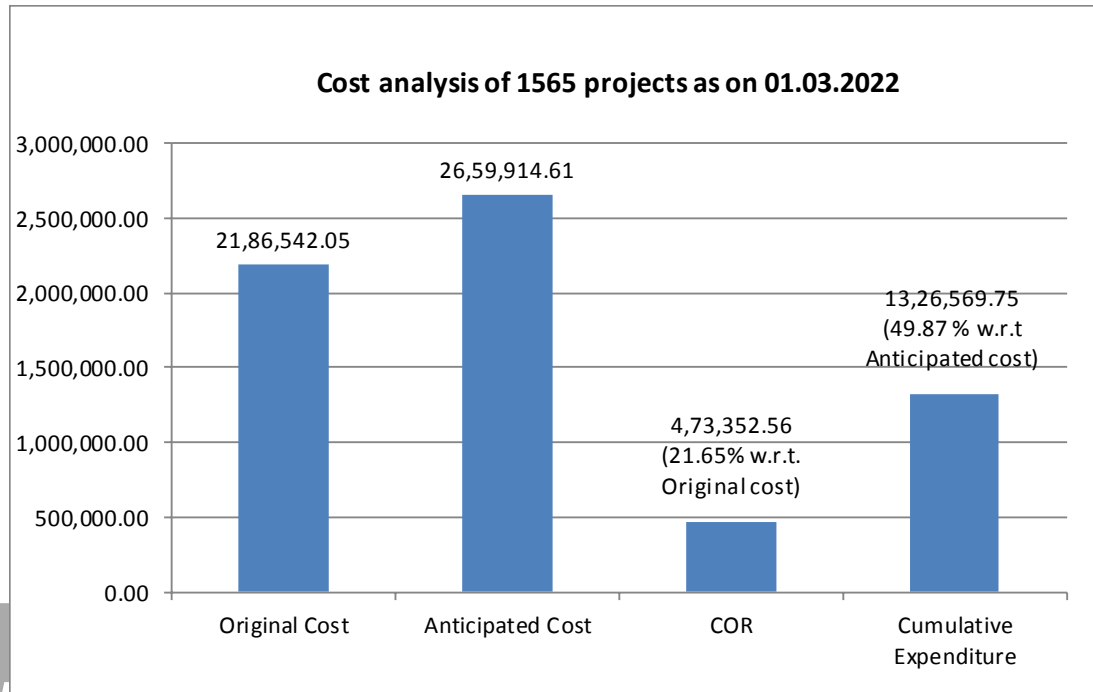


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute terms are at **Table A** and **Table B** respectively.


5. Out of the 1565 projects, 9 projects are ahead of schedule, 278 are on schedule, 647 are delayed, 421 projects reported cost overrun and 215 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 553 if delay is calculated on the basis of latest schedule of completion. Further, for 631 projects neither the year of commissioning nor the tentative gestation period has been reported.

Status of projects (as on 01.03.2022)


(All the figures corresponds to number of project)

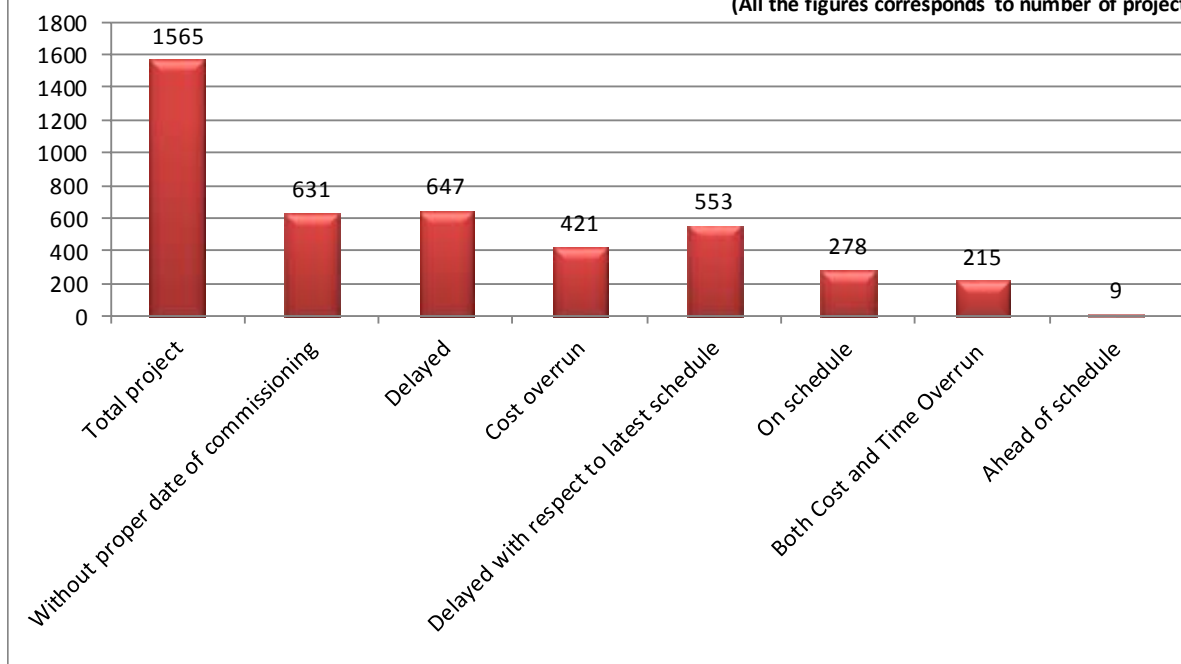

6. Out of 647 delayed projects, 84 (12.98%) projects have overall delay in the range of 1 to 12 months, 124 (19.17%) projects have delay in the range of 13 to 24 months, 327 (50.54%) projects have delay in the range of 25 to 60 months and 112 (17.31%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

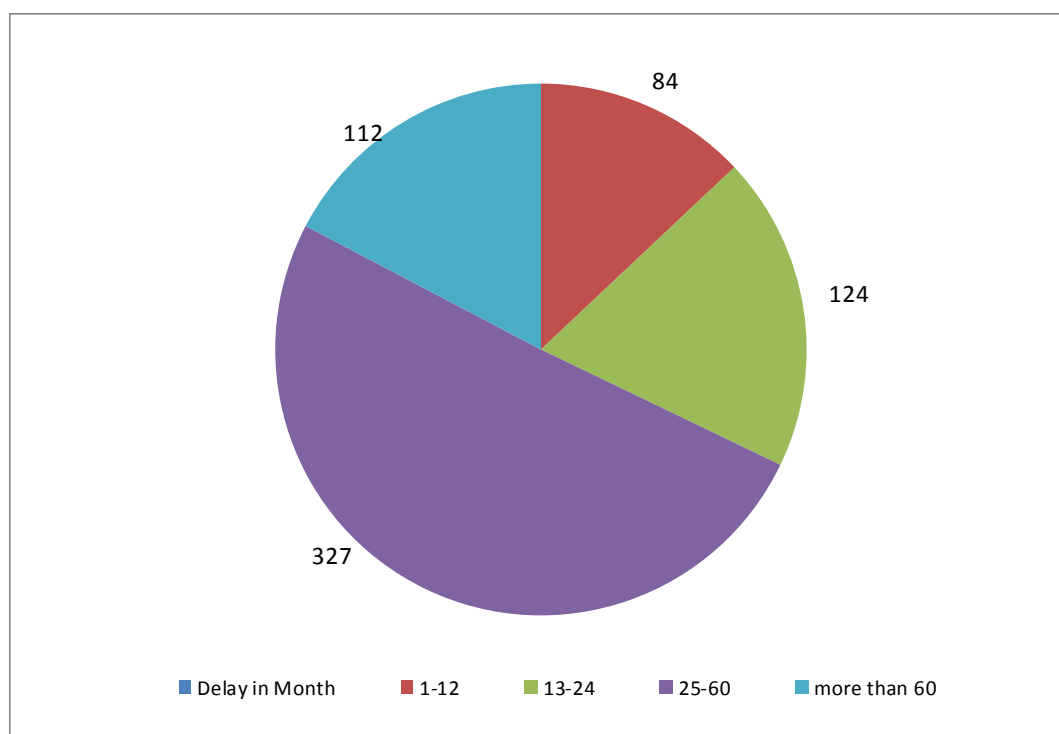

7. The status of online reporting of projects can be viewed month wise as:

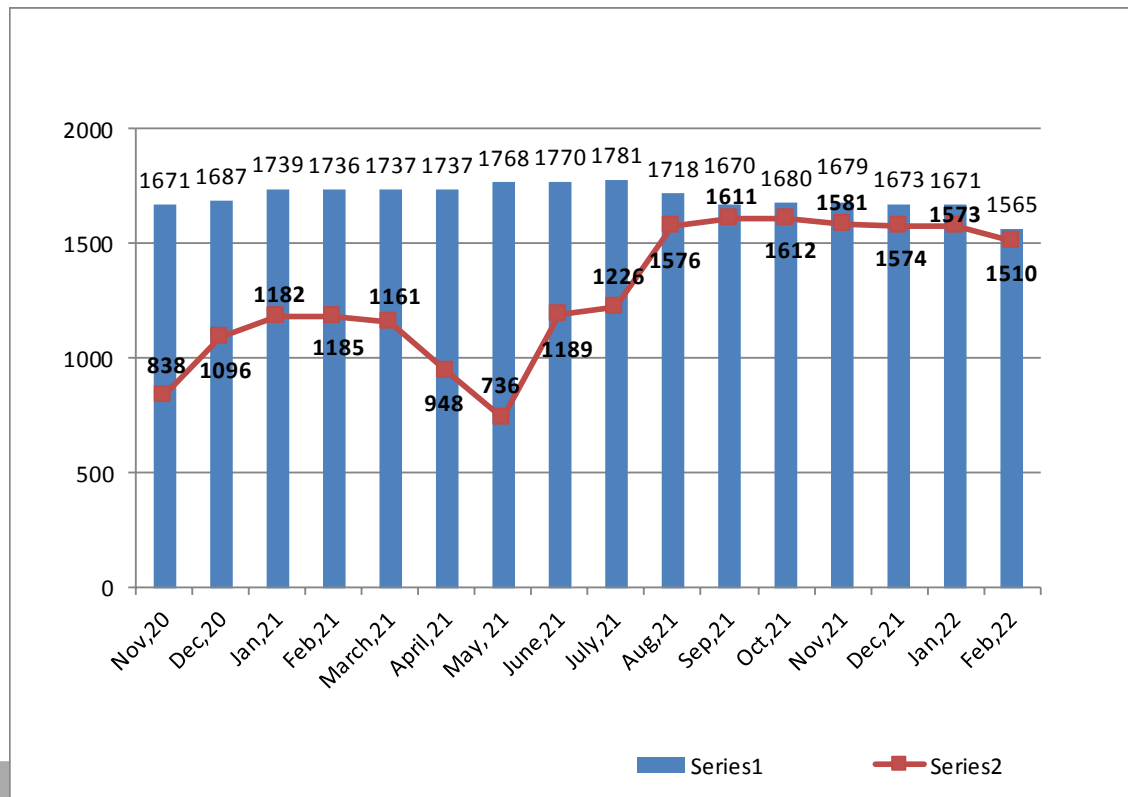

The average time overrun in these 647 delayed projects is 42.60 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-03-2022)**

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	19220.00	67.73
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1938.00	40.13
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
COAL					
8	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
9	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	808.97	68.70
10	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	37.56
11	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	35.10
12	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	08/2016	319.76	404.45	26.49
DEPARTMENT OF HIGHER EDUCATION					
13	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	210.60	13.23
14	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	580.00	5.59
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
DPIIT					
16	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	41.63
19	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	205.00	30.94
20	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
21	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
22	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	586.96	16.10
HEAVY INDUSTRY					
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3727.30	116.96
HOME AFFAIRS					
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04
25	NSG AT KOLKATA	10/2014	162.88	228.63	40.37
26	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	4.68
MINES					
27	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	355.00	581.00	63.66
28	UTKAL D AND E COAL BLOCK 6	05/2016	534.00	667.23	24.95

29	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	5540.00	6435.90	16.17
PETROLEUM					
30	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.34	132.23
31	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
32	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
33	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
34	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
36	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4825.60	191.23
37	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
38	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
39	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	126.58
RAILWAYS					
40	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
41	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI	04/2011	120.70	2111.88	1649.69
42	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	37012.26	1380.49
43	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
44	RAMGANJMUHDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
RENEWABLE ENERGY					
45	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	365.00	34.24
ROAD TRANSPORT AND HIGHWAYS					
46	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
47	MUZAFFARNAGAR-HARIDWAR	09/2011	754.00	2047.64	171.57
48	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
49	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	03/2018	478.74	1135.08	137.10
50	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	478.51	1082.40	126.20
STEEL					
51	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
URBAN DEVELOPMENT					
52	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
53	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	461.42	7.02
54	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
55	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	25.89
56	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
57	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12925.22	19.98
58	NAGPUR METRO RAIL	08/2014	8680.00	9759.79	12.44
WATER RESOURCES					
59	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
60	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	76.68
61	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	62.63
62	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	03/2017	665.78	942.18	41.52
63	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overrun.

Table - B**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)****(as on 01-03-2022)**

SN	PROJECT	DATE OF APPROVAL	COST ORIGINAL (Rs in crore)	COST ANTICIPATED (Rs in crore)	COR (Rs in crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	19220.00	7761.00
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
4	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	1383.00	1938.00	555.00
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	290.50
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
COAL					
8	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
9	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
10	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	808.97	329.44
11	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	91.27
12	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	08/2016	319.76	404.45	84.69
DEPARTMENT OF HIGHER EDUCATION					
13	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	580.00	30.69
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	210.60	24.60
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
DPIIT					
16	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
17	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
HEALTH AND FAMILY WELFARE					
18	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	172.39
19	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	586.96	81.38
21	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	205.00	48.44
22	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3727.30	2009.30
HOME AFFAIRS					
24	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79
25	NSG AT KOLKATA	10/2014	162.88	228.63	65.75
26	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	277.35	290.33	12.98
MINES					
27	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	5540.00	6435.90	895.90
28	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	355.00	581.00	226.00
29	UTKAL D AND E COAL BLOCK	05/2016	534.00	667.23	133.23
PETROLEUM					
30	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	01/2019	12366.00	18968.00	6602.00
31	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
32	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00

33	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
34	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
POWER					
35	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
36	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
37	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
38	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
39	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9129.32	4374.90
RAILWAYS					
40	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	51219.00	39630.00
41	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	37012.26	34512.26
42	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
43	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	14322.00	9867.83
44	RISHIKESH - KARNAPRAYAG NEW LINE	04/2011	16216.00	24659.00	8443.00
RENEWABLE ENERGY					
45	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	365.00	93.10
ROAD TRANSPORT AND HIGHWAYS					
46	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	07/2020	3426.00	5148.00	1722.00
47	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
48	MUZAFFARNAGAR-HARIDWAR	09/2011	754.00	2047.64	1293.64
49	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
50	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	03/2016	1443.00	2330.79	887.79
STEEL					
51	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
TELECOMMUNICATIONS					
52	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
53	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	461.42	30.26
URBAN DEVELOPMENT					
54	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
55	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	3780.00
56	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12925.22	2152.22
57	DELHI MRTS PHASE-III	09/2011	38585.00	40180.91	1595.91
58	NAGPUR METRO RAIL	08/2014	8680.00	9759.79	1079.79
WATER RESOURCES					
59	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
60	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	03/2017	665.78	942.18	276.40
61	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	173.13
62	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	159.16
63	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	47.50

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)

(as on 01-03-2022)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING	TOR (in month)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	12/2022	84
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2023	84
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	10/2022	49
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	01/2016	03/2020	03/2024	48
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	03/2021	03/2025	48
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	12/2022	34
9	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	06/2018	02/2022	12/2024	34
COAL					
10	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	04/2013	06/2015	09/2027	147
11	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2023	144
12	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
13	MURADIH UG TURN-KEY PROJECT	02/2011	04/2014	10/2025	138
14	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	03/2013	03/2024	132
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL, BANGLORE	12/2016	02/2020	06/2022	28
DEPARTMENT OF HIGHER EDUCATION					
16	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	06/2022	93
17	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	03/2022	72
18	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	03/2022	57
19	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	05/2019	03/2020	02/2023	35
20	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	03/2020	06/2020	03/2023	33
DPIIT					
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019	05/2022	29
FERTILISERS					
22	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	03/2022	23
HEALTH AND FAMILY WELFARE					
23	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	06/2022	49
24	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	04/2022	19
25	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	06/2021	05/2022	11
26	AIIMS BILASPUR	04/2018	09/2021	06/2022	9
HOME AFFAIRS					
27	NSG AT KOLKATA	10/2014	04/2018	12/2022	56

28	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	06/2022	32
29	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAUJI	05/2019	01/2022	12/2022	11
30	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	01/2020	10/2023	04/2024	6
31	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	06/2019	07/2022	12/2022	5
MINES					
32	UTKAL D AND E COAL BLOCK	05/2016	01/2020	11/2023	46
33	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	09/2017	06/2019	12/2022	42
34	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	12/2023	37
35	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	01/2024	33
36	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	12/2023	32
PETROLEUM					
37	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2025	146
38	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	05/2022	108
39	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
40	LPG TERMINAL AT KOCHI	10/2015	10/2017	12/2022	62
41	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	04/2016	04/2018	06/2022	50
POWER					
42	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2023	162
43	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	06/2025	144
45	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
46	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	03/2013	12/2024	141
RAILWAYS					
47	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2028	312
48	MUNEERABAD-MAHABOONAGAR(NL),SCR	04/1997	03/2000	03/2023	276
49	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	04/2023	245
50	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	06/2022	219
51	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	03/2009	03/2027	216
ROAD TRANSPORT AND HIGHWAYS					
52	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	06/2023	118
53	PUNE-SATARA(NH-4)	10/2010	03/2013	04/2022	109
54	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	05/2010	05/2013	02/2022	105
55	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
56	KANDLA - MUNDRA PORT	01/2011	07/2013	03/2022	104
STEEL					
57	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	06/2022	85
58	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	11/2022	61
59	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	05/2022	35
60	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	06/2023	06/2024	12
TELECOMMUNICATIONS					
61	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2022	80
62	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	03/2018	03/2022	48
63	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	06/2022	12
URBAN DEVELOPMENT					
64	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2021	03/2025	49
65	NAGPUR METRO RAIL	08/2014	03/2018	02/2022	47

66	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
67	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	03/2020	03/2023	36
68	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	07/2021	06/2024	35
WATER RESOURCES					
69	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	09/2020	03/2024	42
70	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	01/2019	04/2022	12/2024	32
71	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR	03/2019	04/2022	12/2024	32
72	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	04/2022	12/2024	32
73	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	03/2019	07/2021	03/2024	32

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

FLASH REPORT

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-03-2022)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL							
1	ANANTA OCP EXPANSION PH III	08/2008	228.08	228.08	0.00	03/2012	03/2012
2	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	93.05	09/2020	N.A.
3	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
4	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	113.42	09/2020	N.A.
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
COMMERCE							
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	30.00	10/2020	N.A.
DEPARTMENT OF HIGHER EDUCATION							
7	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	429.70	233.00	09/2014	06/2022
8	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	09/2019	588.72	588.72	142.46	09/2022	06/2023
9	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	03/2020	808.62	808.62	318.94	07/2022	10/2022
10	C/O ADDITIONAL INFRASTRUCTURE AT IISC, BANGALORE.SH- RCC MONOLITHIC FOR MEN HOSTEL(S 14), WOMEN HOST	08/2021	316.25	316.25	0.00	11/2021	N.A.
DPIIT							
11	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9574.07	09/2019	07/2021
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	3062.37	12/2019	05/2022
HEALTH AND FAMILY WELFARE							
13	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
14	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	586.50	586.50	11/2013	09/2021
15	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	635.00	557.97	06/2020	N.A.
16	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	760.00	604.15	04/2020	N.A.
17	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	12/2021
HOME AFFAIRS							
18	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAUJI	05/2019	199.31	199.31	75.31	01/2022	12/2022
PETROLEUM							
19	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	19.44	02/2017	08/2022
20	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
21	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	855.28	06/2019	02/2023
22	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	348.00	437.00	226.74	01/2021	08/2022
23	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	06/2016	224.75	198.00	189.00	08/2020	03/2022
POWER							
24	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	200.27	06/2006	N.A.
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	15300.08	09/2010	08/2023
26	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	5289.25	3776.81	10/2017	N.A.
27	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	2169.01	04/2020	07/2025

28	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9129.32	3182.67	12/2018	03/2024
RAILWAYS							
29	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2017.96	883.53	07/2012	11/2024
30	VIZIANAGARAM -SAMABALPUR 3RD LINE	01/1991	2335.67	3327.72	2139.84	12/2024	12/2026
31	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	1483.14	1469.46	N.A.	03/2024
32	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	2923.13	3791.66	1729.29	03/2009	12/2024
33	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	04/1994	320.66	1378.11	558.66	03/2019	03/2025
RENEWABLE ENERGY							
34	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	365.00	282.96	11/2019	N.A.
ROAD TRANSPORT AND HIGHWAYS							
35	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	404.10	345.06	N.A.	06/2022
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	675.00	780.77	424.27	N.A.	06/2022
37	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	255.23	0.00	11/2008	N.A.
38	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	340.14	0.00	04/2009	N.A.
39	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	0.00	11/2008	N.A.
STEEL							
40	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	89.30	12/2023	12/2023
41	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP	01/2022	970.18	970.18	0.00	05/2025	05/2025
TELECOMMUNICATIONS							
42	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	20545.00	07/2015	03/2022
43	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	461.42	70.25	06/2021	06/2022
URBAN DEVELOPMENT							
44	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6065.82	07/2017	09/2020
45	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	20484.28	03/2020	03/2023
46	NAGPUR METRO RAIL	08/2014	8680.00	9759.79	8462.32	03/2018	02/2022
47	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1128.00	1128.00	30.00	03/2022	06/2024
48	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	422.00	422.00	139.55	03/2021	06/2022
WATER RESOURCES							
49	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	225.99	12/2019	05/2022
50	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	299.08	03/2020	03/2022
51	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	261.87	04/2020	03/2022
52	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	380.87	01/2021	05/2022
53	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	211.79	211.79	261.19	12/2021	12/2022

N.A.: Not Available

Table-E

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates

14
(as on 01-03-2022)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	6268.20
	CIVIL AVIATION				
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	0.00	507.91
	COAL				
3	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	815.72
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	0.00	7429.39
	DEPARTMENT OF HIGHER EDUCATION				
5	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	199.00	206.20
	HEALTH AND FAMILY WELFARE				
6	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	586.50
7	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	249.24
8	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
	HEAVY INDUSTRY				
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	3526.63
	HOME AFFAIRS				
12	NSG AT KOLKATA	10/2014	162.88	0.00	173.62
	PETROLEUM				
13	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	09/2017	2677.00	0.00	2730.95
14	PIPELINE REPLACEMENT PROJECT (PRP-VI)	05/2019	763.92	0.00	829.58
	POWER				
15	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	0.00	4409.29
16	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	9014.00
17	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	11130.19	0.00	12394.95
18	NAITWAR MORI HEP	10/2017	648.33	0.00	820.12
	RAILWAYS				
19	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	883.53
20	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	04/1994	320.66	0.00	558.66
21	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	715.89
22	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	495.44	0.00	1868.04
23	AHMEDNAGAR-PARLI VAJNATH(NL) CR	02/1997	2271.50	0.00	2921.95
	RENEWABLE ENERGY				
24	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	271.90	0.00	282.96
	ROAD TRANSPORT AND HIGHWAYS				
25	TRICHY - KARUR	03/2007	516.00	0.00	886.96
26	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	1673.70	0.00	3326.93
27	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2848.49
28	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	0.00	3684.44
29	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	07/2010	1987.00	0.00	3116.66
	STEEL				
30	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	0.00	19611.48
	TELECOMMUNICATIONS				
31	NETWORK FOR SPECTRUM	03/2012	13334.00	0.00	20545.00
	URBAN DEVELOPMENT				
32	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	18051.27
33	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39728.58
34	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	6065.82
	WATER RESOURCES				
35	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	299.08
36	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	380.87
37	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	211.79	0.00	261.19

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-03-2022)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	09/2015	06/2019	12/2021	12/2021
	COAL				
2	ANANTA OCP EXPANSION PH III	08/2008	03/2012	N.A.	03/2012
3	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
4	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	03/2021	N.A.	N.A.
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
	COMMERCE				
7	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
	DEPARTMENT OF HIGHER EDUCATION				
8	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
9	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	11/2021	11/2021
10	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	07/2019	07/2021	07/2021
11	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	01/2018	07/2020	N.A.	12/2021
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	09/2020	N.A.	07/2021
	DONER				
13	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	N.A.	N.A.
	DPIIT				
14	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	N.A.	07/2021
	FERTILISERS				
15	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	N.A.	01/2022
	FINANCE				
16	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	N.A.	07/2021
17	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021	N.A.	11/2021
	HEALTH AND FAMILY WELFARE				
18	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
19	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	09/2021
20	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	06/2021
21	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
22	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	04/2020
	HEAVY INDUSTRY				
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	N.A.	N.A.
	PETROLEUM				
24	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
25	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND	08/2017	06/2020	12/2021	12/2021
26	SWRO II WITH LLPH FACILITIES	09/2019	07/2020	N.A.	01/2022
27	220 KV GRID SUPPLY	10/2020	03/2021	N.A.	12/2021
	POWER				
28	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.

29	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	04/2019	N.A.
30	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	07/2012	N.A.	N.A.
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	N.A.	03/2018
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
33	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	N.A.	N.A.	N.A.
34	JALANDHAR-PATHANKOT-JAMMU TAWI	03/2002	03/2016	N.A.	N.A.
35	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	04/2008	03/2014	N.A.	N.A.
36	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	03/2010	N.A.	N.A.	N.A.
37	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	04/2010	03/2016	N.A.	N.A.
RENEWABLE ENERGY					
38	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
39	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	N.A.	N.A.	12/2021
40	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
41	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	N.A.	N.A.
42	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	N.A.	N.A.
43	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	04/2009	N.A.	N.A.
URBAN DEVELOPMENT					
44	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
45	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	N.A.
46	KOCHI METRO RAIL PROJECT	07/2012	07/2017	N.A.	09/2020
47	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	06/2016	03/2018	02/2021	N.A.
48	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	05/2017	12/2020	09/2021	N.A.
WATER RESOURCES					
49	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	N.A.	N.A.
50	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	05/2017	05/2020	N.A.	N.A.

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	854	67
2	RAILWAYS	211	53
3	PETROLEUM	144	21
4	COAL	103	9
5	POWER	76	13
6	WATER RESOURCES	41	16
7	HEALTH AND FAMILY WELFARE	28	8
8	URBAN DEVELOPMENT	27	8
9	DEPARTMENT OF HIGHER EDUCATION	23	1
10	CIVIL AVIATION	19	11
11	STEEL	7	2
12	MINES	6	1
13	ATOMIC ENERGY	5	0
14	HOME AFFAIRS	5	2
15	TELECOMMUNICATIONS	3	2
16	FINANCE	2	0
17	FERTILISERS	2	2
18	DPIIT	2	0
19	HEAVY INDUSTRY	1	0
20	SHIPPING AND PORTS	1	0
21	SOCIAL JUSTICE	1	0
22	DEFENCE PRODUCTION	1	1
23	COMMERCE	1	0
24	DONER	1	0
25	RENEWABLE ENERGY	1	0
	Total	1565	217

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2021			
	<u>PETROLEUM</u>			
1	MMPL PIPELINE REROUTING PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000261]	449.58	12/2019	396.13
2	PUNE POL STORAGE DEPOT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000313]	282.64	08/2020	194.26
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000664]	639.79	03/2020	597.77
4	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000930]	378.24	01/2018	315.42
5	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001183]	251.55	02/2015	7.74
	June,2021			
	<u>PETROLEUM</u>			
6	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	<u>WATER RESOURCES</u>			
8	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI (Uttarakhand Pey Jal Nigam) - [N30000003]	273.37	08/2019	84.55
9	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR (Bihar Urban Infrastructure Development Corporation Ltd) - [N300000038]	184.93	04/2020	163.36
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000287]	485.44	12/2015	447.13

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000617]	198.00	10/2016	184.62
12	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001220]	491.52	09/2016	474.76
	August,2021			
	<u>PETROLEUM</u>			
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN (OIL INDIA LIMITED) - [N16000167]	352.56	03/2017	455.00
14	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
15	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000312]	255.00	11/2020	275.68
	<u>POWER</u>			
16	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
19	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
20	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
21	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
22	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
23	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000273]	587.44	09/2020	463.48
24	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000274]	349.00	11/2020	313.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
25	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000251]	297.00	04/2018	290.64
26	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000276]	156.26	-	141.35

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
27	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000294]	269.22	01/2015	33.24
28	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000295]	257.09	01/2015	14.18
29	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000297]	376.52	04/2014	171.16
30	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000298]	383.40	03/2015	244.68
31	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000311]	207.03	05/2012	308.09
32	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000317]	157.18	07/2015	148.24
33	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000318]	154.14	08/2015	142.06
34	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000333]	621.43	06/2018	387.22
35	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000371]	445.89	03/2017	464.05
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000376]	219.40	01/2018	0.10
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000379]	218.63	10/2017	29.27
38	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000385]	766.36	-	685.36
39	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000388]	497.05	05/2017	754.27
40	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000389]	847.02	-	795.00
41	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000397]	322.00	03/2018	56.41

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000402]	358.22	10/2016	339.86
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000414]	229.41	05/2018	6.65
44	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000417]	342.05	01/2017	258.91
45	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000467]	511.00	10/2013	2,323.04
46	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000470]	511.00	10/2013	492.00
47	FOUR LANING OF CHANDIGARH - KHARAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000503]	447.29	12/2017	346.39
48	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000523]	159.39	11/2017	210.29
49	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000524]	892.17	-	648.44
50	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000537]	278.39	08/2014	22.18
51	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
52	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000580]	206.80	07/2016	74.04
53	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000581]	288.24	11/2015	287.37
54	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000608]	248.97	05/2019	270.65
55	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000625]	1,004.67	05/2019	577.21
56	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000640]	326.63	04/2018	249.26
57	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000641]	239.91	10/2017	147.25
58	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000644]	342.05	01/2017	258.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
59	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000646]	157.30	06/2018	97.29
60	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000727]	960.24	-	738.74
61	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000871]	600.87	11/2017	682.36
62	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000873]	823.20	11/2017	807.99
63	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000878]	235.91	02/2018	176.23
64	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000879]	202.69	11/2019	148.21
65	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000884]	191.21	11/2019	127.13
66	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000895]	287.34	01/2019	194.85
67	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000905]	322.48	07/2020	291.93
68	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000906]	173.24	06/2020	56.66
69	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000908]	276.01	03/2019	187.39
70	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000911]	165.06	12/2016	92.59
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000936]	244.95	08/2018	136.22
72	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 ((MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000938]	297.12	07/2018	373.98
73	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000942]	208.50	11/2019	165.82
74	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000962]	178.23	09/2018	122.99
75	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000999]	230.34	10/2019	201.82

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
76	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001001]	199.98	08/2016	163.16
77	MAJALGAON TO KAIJ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001036]	413.99	07/2019	299.72
78	AKKALKOT TO DHUDHNI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001120]	211.42	02/2019	131.85
79	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001131]	212.99	06/2020	156.72
80	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001139]	218.94	03/2020	120.69
81	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001143]	176.94	10/2018	141.11
82	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001147]	239.63	02/2019	212.53
83	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001148]	599.34	01/2020	492.15
84	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001153]	197.37	02/2014	89.36
85	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001155]	175.20	01/2017	142.48
86	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001184]	269.69	09/2019	0.01
87	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001202]	388.83	12/2019	304.70
88	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001205]	209.10	10/2019	201.70
89	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001223]	179.89	03/2013	242.23
90	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001225]	169.26	01/2019	270.11
91	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001237]	162.72	09/2016	136.59
92	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001238]	307.70	01/2017	313.06
	URBAN DEVELOPMENT			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
93	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000079]	884.30	12/2015	874.29
94	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000123]	218.72	11/2020	175.63
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
95	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000102]	294.00	04/2019	289.13
	September,2021			
	<u>STEEL</u>			
96	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000121]	263.36	09/2020	253.46
	<u>POWER</u>			
97	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66
98	SYSTEM STRENGTHENING XIII OF SR GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000109]	487.49	06/2014	590.30
99	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
100	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
101	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000181]	871.62	10/2017	628.13
102	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000182]	203.28	07/2017	200.16
103	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
104	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000238]	283.72	11/2019	196.10
105	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000239]	408.46	01/2019	369.27
106	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000240]	608.24	04/2019	425.04
107	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000257]	3,654.00	04/2019	3,508.04

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
108	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT Central Sector Projects(Power Grid Corporation of India Limited) - [N18000261]	175.64	09/2018	115.43
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) Central Sector Projects(Power Grid Corporation of India Limited) - [N18000263]	445.89	02/2019	372.58
110	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) (Power Grid Corporation of India Limited) - [N18000267]	198.49	09/2019	132.15
111	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT (Power Grid Corporation of India Limited) - [N18000269]	193.14	06/2019	108.80
	RAILWAYS			
112	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
113	NANDYAL-YERRAGUNTLA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
114	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
115	ETAWAH-MAINPURI (NL),NCR (NORTH CENTRAL RAILWAY) - [220100318]	120.00	12/2008	345.51
116	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
117	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
118	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) (WESTERN RAILWAY) - [N22000125]	117.36	03/2011	809.40
119	BANGURGRAM-GURIYA PATCH DOUBLING (NORTH WESTERN RAILWAY) - [N22000137]	246.08	12/2019	366.92
120	THIYAT HAMIRA-SANU (NORTH WESTERN RAILWAY) - [N22000149]	236.93	10/2018	287.42
121	AJMER-BANGURGRAM (NORTH WESTERN RAILWAY) - [N22000155]	213.39	11/2019	361.83
122	ALWAR-BANDIKUI DOUBLING (NORTH WESTERN RAILWAY) - [N22000157]	242.09	02/2019	476.34
123	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING (SOUTH EASTERN RAILWAY) - [N22000165]	258.20	12/2018	318.44
124	HAJIPUR-RAMDAYALUNAGAR DOUBLING (EAST CENTRAL RAILWAYS) - [N22000182]	213.01	-	498.44
125	CUDDALORE-SALEM VIA VRIDDHACHALAM GC (SOUTHERN RAILWAY) - [N22000187]	198.68	-	273.57
126	AMBARI FALAKATA TO NEW MAYNAGURI (NORTH EAST FRONTIER RAILWAY) - [N22000210]	314.00	03/2019	831.65
127	PIRPAINTI-BHAGALPUR (EASTERN RAILWAYS) - [N22000222]	261.38	-	553.59
128	HANSDIHA-GODDA NL (EASTERN RAILWAYS) - [N22000236]	542.18	03/2020	545.97
129	HARIDWAR-LAKSAR (NORTHERN RAILWAY) - [N22000289]	219.83	-	204.53
130	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND (SOUTH EASTERN RAILWAY) - [N22000323]	148.77	12/2016	206.49

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
131	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM (SOUTHERN RAILWAY) - [N22000373]	187.26	04/2014	276.82
132	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO (WESTERN RAILWAY) - [N22000433]	243.60	-	423.00
133	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING (SOUTHERN RAILWAY) - [N22000444]	257.00	03/2018	153.84
134	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION (NORTH EASTERN RAILWAY) - [N22000461]	622.50	04/2017	521.88
135	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR (EAST CENTRAL RAILWAYS) - [N22000475]	180.82	-	546.29
136	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
137	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION (WESTERN RAILWAY) - [N22000487]	551.51	03/2019	773.12
138	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM (WESTERN RAILWAY) - [N22000494]	691.84	03/2020	812.08
ROAD TRANSPORT AND HIGHWAYS				
139	SONAPUR TO GUWAHTI (AS-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000044]	245.00	03/2008	240.36
140	NALBARI TO BIJNI (AS-6) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000047]	225.00	06/2008	390.72
141	NALBARI T BIJNI (AS-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000048]	208.00	04/2008	370.56
142	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000049]	160.00	05/2008	270.97
143	BRAHMPUTRA BRIDGE,NH NO-31 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000063]	217.61	04/2010	489.84
144	VADODARA-SURAT SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000361]	503.16	08/2016	389.50
145	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
146	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000518]	399.54	04/2019	259.67
147	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
148	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000542]	197.69	07/2018	151.11
149	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
150	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
151	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROMEXISTI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000837]	307.79	-	197.30

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
152	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000850]	551.58	-	305.46
153	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000978]	172.75	-	134.38
154	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001174]	235.31	11/2020	195.72
155	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG EPC(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24001257]	159.85	10/2022	2.80
	<u>URBAN DEVELOPMENT</u>			
156	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	<u>WATER RESOURCES</u>			
157	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS (Uttar Pradesh Jal Nigam) - [N30000007]	904.00	09/2021	148.55
158	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR (Uttar Pradesh Jal Nigam) - [N30000009]	370.40	08/2020	396.14
159	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA (Uttar Pradesh Jal Nigam) - [N30000011]	161.31	11/2019	91.38
160	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA (Bihar Urban Infrastructure Development Corporation Ltd) - [N30000041]	184.86	05/2021	168.85
	October,2021			
	<u>CIVIL AVIATION</u>			
161	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNAI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000040]	535.00	06/2010	0.01
	<u>COAL</u>			
162	SINGHORI OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000130]	205.49	03/2020	138.58
163	AMALGAMATED PAUNI-II III OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000131]	483.69	03/2021	253.70
164	AMALGAMATED GONDEGAON GHATROHAN OC (WESTERN COAL FIELDS LIMITED) - [N06000149]	198.68	03/2019	272.90
	<u>PETROLEUM</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
165	GAIL GAS LTD BENGALURU CGD PROJECT Central Sector Projects(GAS AUTHORITY OF INDIA LIMITED) - [N16000210]	749.00	02/2020	1,043.56
166	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50
167	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75
	<u>RAILWAYS</u>			
168	GHAZIPUR - AUNRIHAR (40 KM) (NORTH EASTERN RAILWAY) - [N22000321]	182.92	-	0.01
	<u>URBAN DEVELOPMENT</u>			
169	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000143]	532.00	11/2020	541.00
	November,2021			
	<u>COAL</u>			
170	KOLAR PIMPRI EXTENSION OC (WESTERN COAL FIELDS LIMITED) - [N06000160]	362.73	03/2020	336.00
	December,2021			
	<u>STEEL</u>			
171	COKE OVEN BATTERY-5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000117]	2,858.00	12/2017	2,018.72
	<u>PETROLEUM</u>			
172	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT (INDIAN OIL CORPORATION LIMITED) - [N16000236]	423.00	08/2019	447.89
173	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE (INDIAN OIL CORPORATION LIMITED) - [N16000267]	212.00	01/2021	177.58
174	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI (INDIAN OIL CORPORATION LIMITED) - [N16000276]	261.00	01/2021	195.22
175	PIPELINE NETWORK PROJECT GELEKI, ASSAM (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000278]	249.85	05/2020	229.85
176	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP (INDIAN OIL CORPORATION LIMITED) - [N16000302]	384.58	04/2021	302.10
177	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000365]	1,524.06	12/2021	1,037.45
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
178	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000553]	229.37	11/2018	152.85
	January,2022			
	<u>COAL</u>			
179	RFR OF MANUGURU OC PROJECT (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000102]	430.45	03/2016	213.44
	<u>STEEL</u>			
180	FORGED WHEEL PLANT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000116]	1,682.85	09/2018	1,767.98
	<u>PETROLEUM</u>			
181	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000297]	4,006.83	05/2021	3,526.55
182	BS VI PROJECT AT GUWAHATI REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000339]	557.00	02/2020	559.57
183	RESITEMENT OF RAICHUR DEPOT TO GULBARGA (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000347]	206.26	03/2021	163.25
	<u>HEAVY INDUSTRY</u>			
184	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA Central Sector Projects(BHARAT HEAVY ELECTRICALS LIMITED) - [N20000002]	1,554.00	09/2019	815.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
185	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000349]	1,387.11	11/2017	980.46
186	THIRUMAYAM - MANAMADURAI SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000359]	401.11	01/2017	273.89
187	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000623]	1,100.19	-	1,355.00
188	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000840]	1,158.35	-	496.04
	February,2022			
	<u>COAL</u>			
189	PATHERDIH NLW WASHERY (BHARAT COKING COAL LIMITED) - [N06000127]	269.82	04/2014	214.74
	<u>FERTILISERS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
190	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA (NATIONAL FERTILISER LIMITED) - [N08000015]	218.83	11/2019	200.49
191	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL (NATIONAL FERTILISER LIMITED) - [N08000016]	239.81	11/2019	205.94
	PETROLEUM			
192	AUGMENTATION OF CTMPL Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000286]	228.00	11/2021	164.20
193	RE-LIQUIFIED NATURAL GAS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000301]	421.00	08/2020	297.95
194	SEA WATER DESALINATION PLANT Central Sector Projects(MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000319]	581.00	03/2020	593.44
	POWER			
195	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000157]	374.63	04/2016	259.44
196	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000213]	808.63	01/2018	690.89
197	EASTERN REGION STRENGTHENING SCHEME-XV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000214]	454.11	04/2018	345.21
198	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000219]	14,733.37	11/2019	11,823.97
199	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000247]	5,070.13	04/2020	4,236.67
	RAILWAYS			
200	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR (NORTH EAST FRONTIER RAILWAY) - [220100266]	1,180.19	12/2008	3,983.32
201	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) (METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100268]	1,049.69	12/2006	3,837.57
202	KOSI BRIDGE (NL), ECR (EAST CENTRAL RAILWAYS) - [220100304]	499.41	03/2020	468.05
203	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR (EAST CENTRAL RAILWAYS) - [N22000002]	477.88	03/2012	723.12
204	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT (RAILWAY ELECTRIFICATION) - [N22000094]	171.10	03/2012	141.55
205	AHMEDABAD-BOTAD (GC) (RAIL VIKAS NIGAM LTD.) - [N22000140]	975.62	12/2021	1,755.44
206	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR (NORTH WESTERN RAILWAY) - [N22000152]	420.18	03/2020	387.54
207	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION (SOUTH EASTERN RAILWAY) - [N22000162]	149.90	03/2015	240.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
208	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF (SOUTHERN RAILWAY) - [N22000202]	931.98	-	1,005.24
209	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE (METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000214]	714.10	04/2016	65.20
210	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) (EASTERN RAILWAYS) - [N22000230]	157.94	11/2018	51.75
211	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL (EASTERN RAILWAYS) - [N22000244]	257.42	03/2014	109.66
212	3RD LINE BETWEEN BHUSAWAL-JALGAON (CENTRAL RAILWAYS) - [N22000247]	184.06	03/2019	325.52
213	SAMBALPUR - ANGUL RLY. ELECTRIFICATION (EAST COAST RAILWAY) - [N22000319]	155.81	03/2020	224.76
214	MATHURA-PLWAL 4TH LINE (80KM) (NORTH CENTRAL RAILWAY) - [N22000372]	668.70	03/2020	531.20
215	MUZAFFARPUR-SITAMARHI NEW LINE (EAST CENTRAL RAILWAYS) - [N22000374]	332.15	07/2014	560.09
216	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000390]	602.27	12/2021	1,135.28
217	MULTI MODAL LOGISTICS PARK AT KATHUWAS (CONTAINER CORPORATION OF INDIA) - [N22000421]	493.17	03/2018	464.53
218	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN (CONTAINER CORPORATION OF INDIA) - [N22000422]	305.00	03/2019	269.73
219	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM (CONTAINER CORPORATION OF INDIA) - [N22000424]	387.70	03/2018	434.63
220	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR (CONTAINER CORPORATION OF INDIA) - [N22000425]	207.00	03/2018	153.83
221	MULTI MODAL LOGISTICS PARK AT BARHI (CONTAINER CORPORATION OF INDIA) - [N22000426]	346.32	03/2019	320.28
222	MULTI MODAL LOGISTICS PARK AT TIHI (CONTAINER CORPORATION OF INDIA) - [N22000427]	174.00	03/2019	172.08
223	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 (WESTERN RAILWAY) - [N22000437]	153.83	-	109.05
224	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) (SOUTHERN RAILWAY) - [N22000441]	268.87	03/2005	922.01
225	GARHWA ROAD-RAMNA (EAST CENTRAL RAILWAYS) - [N22000465]	348.23	03/2021	407.08
226	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM) (SOUTH EASTERN RAILWAY) - [N22000507]	354.54	12/2018	303.25
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
227	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106277]	280.00	02/2009	612.58
228	GWALIOR-JHANSI, NH-75 PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000089]	604.00	12/2009	360.15
229	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000260]	255.75	09/2017	319.68

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
230	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000316]	258.97	08/2015	229.77
231	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000344]	425.19	09/2016	276.40
232	FOUR LANING OF GWALIOR-SHIVPURI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000494]	1,055.00	11/2015	1,393.40
233	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000496]	1,012.90	03/2016	226.10
234	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000509]	1,170.52	06/2012	2,051.36
235	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000517]	479.20	05/2018	712.89
236	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000520]	275.90	-	289.13
237	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000546]	273.20	02/2019	670.27
238	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000572]	364.56	-	353.42
239	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000586]	637.18	06/2019	550.35
240	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000591]	688.70	-	870.48
241	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000593]	331.46	10/2018	267.94
242	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000624]	1,244.10	-	1,665.00
243	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000729]	607.00	-	510.71
244	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000791]	261.76	-	213.27
245	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000794]	1,103.88	-	720.73
246	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000797]	716.76	-	687.07
247	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000838]	874.25	-	866.55
248	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001140]	215.16	09/2019	145.76

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
249	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001146]	249.50	05/2019	229.82
250	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001203]	218.90	03/2020	147.70
251	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001204]	208.88	10/2019	183.54
	<u>URBAN DEVELOPMENT</u>			
252	LUCKNOW METRO RAIL CORPORATION LTD (LUCKNOW METRO RAIL CORPORATION LIMITED) - [N28000094]	6,928.00	03/2019	6,928.00
253	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000106]	238.56	05/2020	208.57
	<u>WATER RESOURCES</u>			
254	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA (Uttar Pradesh Jal Nigam) - [N30000020]	279.91	12/2019	263.53

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2022			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000321]	829.00	01/2019	350.14
2	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000430]	223.30	06/2018	111.16
3	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000618]	434.06	-	306.05
4	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000676]	138.93	01/2017	124.76
5	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
6	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000681]	194.66	04/2017	117.61
7	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000689]	507.68	04/2017	129.13
8	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000766]	318.42	11/2017	66.63
	August,2022			
9	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
10	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000274]	333.21	12/2015	256.11
11	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000296]	278.87	05/2014	0.00
12	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000302]	333.21	12/2015	256.11

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000307]	156.63	02/2012	0.00
14	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000309]	305.49	03/2011	131.08
15	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
16	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000335]	159.12	11/2015	0.00
17	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000373]	305.49	03/2017	0.00
18	SATANA-BELA SECTION OF NH-75(4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000375]	320.48	08/2015	189.49
19	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000395]	257.80	-	12.38
20	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000396]	470.20	02/2011	569.40
21	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000398]	282.41	08/2016	327.21
22	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
23	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000407]	333.21	11/2015	256.11
24	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
25	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
26	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000519]	478.35	-	516.69
27	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000530]	154.62	-	0.00
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000575]	665.50	07/2016	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
29	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000577]	369.77	06/2016	0.00
30	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000927]	293.64	08/2020	28.24
31	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001144]	445.89	03/2017	469.64
32	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001145]	164.54	08/2015	141.33
33	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001154]	367.44	01/2017	61.95
34	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001167]	165.67	01/2016	87.63
35	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001170]	471.16	08/2014	201.64
36	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001230]	281.45	12/2020	112.70
	September,2022			
	<u>RAILWAYS</u>			
37	DANIAWAN-BIHARSARIF (NL), ECR (EAST CENTRAL RAILWAYS) - [220100311]	406.92	-	200.00
38	GOOTY-DHARMAVARAM-BANGLORE (RAIL INDIA TECHNICAL AND ECONOMIC SERVICE) - [N22000370]	636.38	-	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
39	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000253]	187.79	07/2016	82.95
40	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000275]	289.60	-	160.70
41	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02
42	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000650]	244.90	05/2019	251.87

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	<u>RURAL DEVELOPMENT</u>			
43	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V (HSCL FOR RURAL) - [N12000098]	149.73	12/2015	144.95
44	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI (HSCL FOR RURAL) - [N12000099]	202.61	12/2016	190.22
45	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII (HSCL FOR RURAL) - [N12000100]	175.49	12/2016	124.87
	October,2022			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
46	STUDY IN INDIA (EDCIL(India) Limited) - [N42000003]	150.00	04/2018	0.00
47	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION (Indian Institute of Technology, Kharagpur) - [N42000004]	418.00	03/2019	110.00
48	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES(CPWD OF HIGHER EDUCATION) - [N44000001]	127.26	10/2023	12.73
	<u>HOME AFFAIRS</u>			
49	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 (CPWD FOR MHA) - [N45000001]	166.98	05/2022	0.29
	November,2022			
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA(CPWD FOR MHA) - [N28000101]	114.26	12/2013	0.00
	<u>RURAL DEVELOPMENT</u>			
51	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT(CPWD FOR RURAL) - [N28000132]	361.60	07/2021	12.44
	February,2022			
	<u>COAL</u>			
52	MAGADH EXPANSION OC(51 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000015]	6,964.33	07/2012	815.07
53	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY (EASTERN COAL FIELDS LIMITED) - [N06000020]	1,210.12	03/2029	91.96
54	BHUBANESWARI EXPENSION OCP(40.0 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000034]	3,145.45	03/2017	715.56

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
55	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000035]	8,416.19	03/2013	1,204.92
56	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000044]	3,504.21	03/2010	595.58
57	BATURA OCP (2.0 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000049]	1,186.64	03/2023	261.21
58	ANANTA OC EXPANSION PH-III (15.0 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000067]	207.28	03/2012	271.27
59	JAGANNATHPOR OCP(3.00MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000075]	152.43	03/2015	201.95
60	RAMAGUNDAM OC-II EXTENSION (SINGARENI COLLIERS COMPANY LIMITED) - [N06000078]	418.97	03/2012	416.07
61	KISTARAM OCP (SINGARENI COLLIERS COMPANY LIMITED) - [N06000089]	242.29	03/2015	143.08
62	RCE OF INDARAM OCP(1.20 MTPA) (SINGARENI COLLIERS COMPANY LIMITED) - [N06000093]	162.76	03/2015	306.11
63	JALAGAM VENGALA RAO OCP-II (SINGARENI COLLIERS COMPANY LIMITED) - [N06000094]	447.06	03/2015	245.94
64	KALYANIKHANI OPENCAST PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000101]	417.33	07/2016	168.51
65	RECAST EPR AMRAPALI OC (CENTRAL COAL FIELDS LIMITED) - [N06000103]	4,983.58	03/2020	371.36
66	SONEPUR BAZARI (COMB) OCP (8.0 MTY) (EASTERN COAL FIELDS LIMITED) - [N06000109]	1,055.05	03/2018	711.21
67	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000118]	1,184.33	03/2020	436.49
68	BHANEAGAON OC (WESTERN COAL FIELDS LIMITED) - [N06000121]	187.94	03/2023	87.35
69	KAKATIYAKHANI OPENCAST-2 PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000129]	397.09	03/2019	127.15
70	ADASA UG TO OC (WESTERN COAL FIELDS LIMITED) - [N06000133]	288.90	03/2023	158.85
71	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000141]	313.34	03/2021	159.87
72	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000142]	851.60	03/2020	283.28
73	BHATADI EXPANSION OC MINE (WESTERN COAL FIELDS LIMITED) - [N06000150]	304.52	03/2019	162.29
74	RPR FOR JAMUNIA UG (0.90 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000153]	281.25	03/2022	23.52
75	RECAST PR FOR DHANKASA UG (1.00 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000155]	289.29	03/2022	37.55
76	SEMARIA OPENCAST PROJECT (NORTHERN COAL FIELDS LIMITED) - [N06000176]	396.58	03/2026	0.00
77	NORTH URIMARI EXPANSION OCP (CENTRAL COAL FIELDS LIMITED) - [N06000182]	1,553.06	03/2023	416.42
	RAILWAYS			
78	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES (EASTERN RAILWAYS) - [N22000249]	166.89	-	0.02

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
79	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) (SOUTHERN RAILWAY) - [N22000445]	1,567.00	03/2024	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
80	HARANGAJO TO MAIBANG, NH-54 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000062]	196.00	07/2009	655.17
81	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000133]	2,288.00	11/2011	3,450.00
82	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000568]	834.64	-	209.94
83	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000587]	763.23	06/2019	198.01
	<u>WATER RESOURCES</u>			
84	IRRIGATION WORK OF BAGMATI (HSCL FOR WATER) - [N12000108]	956.00	03/2015	712.37

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1671
No of Projects Completed/Dropped/Frozen in Current Month	150
No of Projects Fell Down in Current Month	2
No of Projects added in Current Month	46
No of Projects in Current Month	1565

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	647 (41.34%)	9 (.58%)	278 (17.76%)	117 (7.48%)	514 (32.84%)	1565
Latest Approved (Date)	553 (35.34%)	11 (.70%)	399 (25.50%)	84 (5.37%)	518 (33.10%)	1565

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1336	18,96,206.45	21,19,888.53	9,49,889.66	44.80	2,23,682.08	11.80
Project with Revision in Cost	229	5,31,147.48	5,40,026.08	3,76,680.09	69.80	8,878.60	1.70
Total	1,565	24,27,353.93	26,59,914.61	13,26,569.75	49.87	2,32,560.68	9.58
Original Cost of All Projects							
Original Cost	1,565	21,86,542.05	26,59,914.61	13,26,569.75	49.87	4,73,372.56	21.65

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	647	9,31,002.14	12,41,299.67	7,37,580.20	59.40	3,10,297.53	33.33
Latest Approved (RCE)	553	8,45,850.75	9,99,931.57	5,86,756.34	58.70	1,54,080.82	18.22

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	217	2,57,343.34	3,45,788.23	2,17,345.94	62.90	88,444.89	34.40
Total	217	2,57,343.34	3,45,788.23	2,17,345.94	62.86	88,444.89	34.37

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	3	27,271.00	43,139.00	58.19
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	4	3,288.50	4,358.06	32.52
3	COAL	103	1,53,083.23	1,57,457.70	2.86	9	28,175.10	33,298.68	18.18
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	2	642.64	642.64	0.00	0	0.00	0.00	0.00
6	MINES	6	7,333.99	8,585.67	17.07	3	6,429.00	7,684.13	19.52
7	STEEL	7	21,618.48	28,033.48	29.67	1	15,525.00	21,940.00	41.32
8	PETROLEUM	144	3,77,065.98	3,95,519.73	4.89	29	66,969.75	91,502.05	36.63
9	POWER	76	1,96,489.83	2,60,007.47	32.33	28	1,09,390.83	1,74,426.52	59.45
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
11	HEALTH AND FAMILY WELFARE	28	13,696.26	14,162.35	3.40	12	4,281.23	4,855.32	13.41
12	RAILWAYS	211	4,08,405.75	6,65,174.44	62.87	157	2,12,988.70	4,76,053.67	123.51
13	ROAD TRANSPORT AND HIGHWAYS	854	5,17,126.74	5,40,821.11	4.58	147	1,21,063.06	1,50,589.15	24.39
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,373.62	81.07	2	13,765.16	25,125.42	82.53
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	8	1,14,518.89	1,35,012.56	17.90
17	WATER RESOURCES	41	23,466.28	69,468.25	196.03	8	12,622.34	58,713.79	365.16
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
19	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	0	0.00	0.00	0.00
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
21	DEPARTMENT OF HIGHER EDUCATION	23	10,455.86	10,390.34	-0.63	3	1,231.49	1,289.59	4.72

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	3	1,659.44	2,518.96	51.80
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	1	271.90	365.00	34.24
Total		1565	21,86,542.05	26,59,914.61	21.65	421	7,58,521.48	12,53,589.50	65.27

^ - Cost Overrun = Anticipated Cost minus Original Cost

FLASH REPORT

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above		
(All Cost/ Expenditure in Rs. crore)										
						Projects with cost overrun^				
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)	
1	ANDHRA PRADESH	65	1,11,390.87	1,63,336.49	46.63	15	46,526.12	1,01,771.62	118.74	
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	5	8,861.14	22,797.48	157.27	
3	ASSAM	45	47,656.00	56,342.77	18.23	10	18,330.96	28,229.48	54.00	
4	BIHAR	85	1,17,311.78	1,53,928.66	31.21	36	58,055.82	95,717.43	64.87	
5	GOA	10	5,332.77	5,343.26	0.20	2	529.17	539.66	1.98	
6	GUJARAT	56	1,06,855.31	1,21,047.93	13.28	18	35,079.44	50,141.21	42.94	
7	HARYANA	35	60,694.21	62,645.55	3.22	16	13,933.38	16,405.73	17.74	
8	HIMACHAL PRADESH	19	21,990.88	33,028.18	50.19	5	9,650.78	20,714.91	114.64	
9	JAMMU AND KASHMIR	29	46,603.49	81,343.00	74.54	2	4,659.00	39,531.26	748.49	
10	KARNATAKA	55	84,883.48	93,093.46	9.67	20	20,685.46	29,239.17	41.35	
11	KERALA	21	29,984.85	35,049.87	16.89	10	13,303.17	18,368.21	38.07	
12	MADHYA PRADESH	75	66,341.06	74,667.19	12.55	17	16,027.73	25,379.33	58.35	
13	MAHARASHTRA	224	2,03,291.90	2,27,367.17	11.84	37	73,446.36	1,02,243.68	39.21	
14	MANIPUR	26	12,108.58	22,615.20	86.77	2	5,032.79	15,633.05	210.62	
15	MEGHALAYA	12	4,790.48	7,912.42	65.17	1	906.46	4,083.02	350.44	
16	MIZORAM	24	11,957.35	16,911.60	41.43	5	3,593.57	8,547.82	137.86	
17	NAGALAND	35	15,989.03	20,373.15	27.42	3	3,035.84	7,419.96	144.41	
18	ODISHA	77	1,09,972.84	1,19,431.95	8.60	20	23,358.60	32,817.71	40.50	
19	PUNJAB	24	17,419.37	18,661.82	7.13	5	4,354.68	5,707.30	31.06	
20	RAJASTHAN	49	59,049.82	64,466.52	9.17	5	15,137.56	20,647.37	36.40	
21	SIKKIM	18	7,278.84	14,598.73	100.56	2	1,727.48	9,047.37	423.73	
22	TAMIL NADU	58	1,96,061.35	2,16,066.26	10.20	17	40,906.07	62,417.19	52.59	
23	TRIPURA	19	5,084.45	5,225.78	2.78	2	767.30	944.91	23.15	
24	UTTAR PRADESH	103	1,39,667.42	1,48,121.08	6.05	37	47,762.08	58,272.74	22.01	
25	WEST BENGAL	62	62,517.29	74,251.74	18.77	24	26,954.70	39,015.68	44.75	
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	44.38	
27	DELHI	27	82,096.45	85,824.51	4.54	13	47,510.66	51,317.92	8.01	
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00	
29	CHHATISGARH	44	75,822.81	85,814.67	13.18	10	27,355.95	37,467.16	36.96	
30	JHARKHAND	38	68,059.63	74,961.76	10.14	11	23,038.04	31,145.84	35.19	
31	UTTARAKHAND	29	35,446.38	53,598.18	51.21	10	27,699.47	45,851.27	65.53	
32	TELANGANA	49	37,332.16	40,209.86	7.71	8	16,066.31	19,311.89	20.20	
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	38.72	
34	MULTI STATE	91	3,13,927.74	4,39,710.63	40.07	50	1,23,224.09	2,51,436.07	104.05	
Total		1565	21,86,542.05	26,59,914.61	21.65	421	7,58,521.48	12,53,589.50	65.27	

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	4	67,120.00	82,988.00	36 - 145
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	17	13,078.09	14,147.65	12 - 49
3	COAL	103	1,53,083.23	1,57,457.70	2.86	31	35,785.45	37,983.80	12 - 147
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	2	642.64	642.64	0.00	1	426.72	426.72	23 - 23
6	MINES	6	7,333.99	8,585.67	17.07	6	7,333.99	8,585.67	30 - 46
7	STEEL	7	21,618.48	28,033.48	29.67	4	19,728.88	26,143.88	12 - 85
8	PETROLEUM	144	3,77,065.98	3,95,519.73	4.89	84	1,53,700.65	1,66,140.61	2 - 146
9	POWER	76	1,96,489.83	2,60,007.47	32.33	50	1,43,700.78	1,98,152.89	6 - 162
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	28	13,696.26	14,162.35	3.40	4	2,169.99	2,289.99	9 - 49
12	RAILWAYS	211	4,08,405.75	6,65,174.44	62.87	131	1,79,906.18	3,21,051.16	2 - 312
13	ROAD TRANSPORT AND HIGHWAYS	854	5,17,126.74	5,40,821.11	4.58	235	1,26,749.96	1,30,435.31	1 - 118
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,373.62	81.07	3	14,013.36	25,373.62	12 - 80
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	16	1,29,952.06	1,43,394.54	3 - 49
17	WATER RESOURCES	41	23,466.28	69,468.25	196.03	38	22,222.12	67,947.69	5 - 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
19	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	1	246.31	200.00	28 - 28
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
21	DEPARTMENT OF HIGHER EDUCATION	23	10,455.86	10,390.34	-0.63	16	8,068.87	7,974.89	3 - 93
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	5	2,025.73	2,885.25	5 - 56
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	-
Total		1565	21,86,542.05	26,59,914.61	21.65	647	9,31,002.14	12,41,299.67	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	65	1,11,390.87	1,63,336.49	46.63	30	83,699.45	1,35,026.79	7 - 216
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	6	7,811.86	21,690.30	14 - 155
3	ASSAM	45	47,656.00	56,342.77	18.23	15	9,172.64	11,933.75	1 - 74
4	BIHAR	85	1,17,311.78	1,53,928.66	31.21	37	42,068.43	63,733.95	11 - 141
5	GOA	10	5,332.77	5,343.26	0.20	3	1,790.89	1,790.89	25 - 35
6	GUJARAT	56	1,06,855.31	1,21,047.93	13.28	22	47,845.26	61,821.09	3 - 139
7	HARYANA	35	60,694.21	62,645.55	3.22	12	8,550.51	8,881.12	5 - 43
8	HIMACHAL PRADESH	19	21,990.88	33,028.18	50.19	4	5,923.10	12,021.10	4 - 162
9	JAMMU AND KASHMIR	29	46,603.49	81,343.00	74.54	7	13,011.36	47,523.62	3 - 245
10	KARNATAKA	55	84,883.48	93,093.46	9.67	19	43,488.08	44,942.44	4 - 312
11	KERALA	21	29,984.85	35,049.87	16.89	6	4,805.39	6,005.46	13 - 62
12	MADHYA PRADESH	75	66,341.06	74,667.19	12.55	39	44,327.91	51,983.47	12 - 64
13	MAHARASHTRA	224	2,03,291.90	2,27,367.17	11.84	118	1,15,146.46	1,38,960.39	5 - 219
14	MANIPUR	26	12,108.58	22,615.20	86.77	1	4,454.17	14,322.00	153 - 153
15	MEGHALAYA	12	4,790.48	7,912.42	65.17	3	1,154.59	1,099.97	40 - 93
16	MIZORAM	24	11,957.35	16,911.60	41.43	10	6,763.47	10,897.00	15 - 117
17	NAGALAND	35	15,989.03	20,373.15	27.42	8	4,566.17	8,902.65	42 - 132
18	ODISHA	77	1,09,972.84	1,19,431.95	8.60	37	49,789.96	59,248.53	2 - 189
19	PUNJAB	24	17,419.37	18,661.82	7.13	9	4,753.34	4,712.90	3 - 108
20	RAJASTHAN	49	59,049.82	64,466.52	9.17	12	24,535.68	29,780.33	3 - 84
21	SIKKIM	18	7,278.84	14,598.73	100.56	3	2,032.47	9,292.99	13 - 96
22	TAMIL NADU	58	1,96,061.35	2,16,066.26	10.20	25	66,829.15	75,834.37	2 - 147
23	TRIPURA	19	5,084.45	5,225.78	2.78	2	817.39	956.49	9 - 30
24	UTTAR PRADESH	103	1,39,667.42	1,48,121.08	6.05	40	82,016.71	84,677.74	2 - 103
25	WEST BENGAL	62	62,517.29	74,251.74	18.77	37	31,391.24	37,865.22	5 - 141
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	5	1,715.32	2,005.82	44 - 53
27	DELHI	27	82,096.45	85,824.51	4.54	13	12,197.58	13,336.82	5 - 58
28	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
29	CHHATISGARH	44	75,822.81	85,814.67	13.18	25	35,909.07	45,299.99	3 - 144
30	JHARKHAND	38	68,059.63	74,961.76	10.14	19	41,173.00	43,068.90	3 - 144
31	UTTARAKHAND	29	35,446.38	53,598.18	51.21	14	28,329.39	45,519.50	3 - 144
32	TELANGANA	49	37,332.16	40,209.86	7.71	8	15,455.34	16,057.19	13 - 180
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	27 - 27
34	MULTI STATE	91	3,13,927.74	4,39,710.63	40.07	56	88,935.49	1,31,431.56	6 - 276
Total		1565	21,86,542.05	26,59,914.61	21.65	647	9,31,002.14	12,41,299.67	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of time overrun in projects with respect to latest schedule						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	4	79,640.00	82,988.00	36 - 145
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	1	1,383.00	1,938.00	27 - 27
3	COAL	103	1,53,190.70	1,57,457.70	2.79	30	35,536.85	37,731.09	12 - 147
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	2	642.64	642.64	0.00	0	0.00	0.00	-
6	MINES	6	8,585.67	8,585.67	0.00	1	255.37	255.37	30 - 30
7	STEEL	7	21,618.48	28,033.48	29.67	4	19,728.88	26,143.88	12 - 85
8	PETROLEUM	144	3,88,571.32	3,95,519.73	1.79	60	93,098.62	98,286.46	0 - 146
9	POWER	76	2,42,671.39	2,60,007.47	7.14	42	1,24,744.98	1,32,856.17	0 - 141
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	28	13,711.40	14,162.35	3.29	4	2,169.99	2,289.99	9 - 49
12	RAILWAYS	211	5,17,762.52	6,65,174.44	28.47	124	1,69,809.89	2,71,062.94	0 - 312
13	ROAD TRANSPORT AND HIGHWAYS	854	5,31,640.50	5,40,821.11	1.73	215	1,12,194.23	1,12,695.97	0 - 118
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,043.62	25,373.62	80.68	3	14,043.62	25,373.62	12 - 80
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	10	1,12,387.86	1,25,909.54	3 - 49
17	WATER RESOURCES	41	68,864.11	69,468.25	0.88	38	67,619.95	67,947.69	5 - 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	-
19	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	1	210.00	200.00	28 - 28
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
21	DEPARTMENT OF HIGHER EDUCATION	23	10,424.24	10,390.34	-0.33	12	6,595.07	6,555.89	3 - 57
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	3	1,659.44	2,518.96	5 - 56
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	-
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	-
Total		1565	24,27,353.93	26,59,914.61	9.58	553	8,45,850.75	9,99,931.57	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	4	3,288.50	4,358.06	32.52
3	COAL	103	1,53,190.70	1,57,457.70	2.79	6	26,832.50	31,849.53	18.70
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	2	642.64	642.64	0.00	0	0.00	0.00	0.00
6	MINES	6	8,585.67	8,585.67	0.00	0	0.00	0.00	0.00
7	STEEL	7	21,618.48	28,033.48	29.67	1	15,525.00	21,940.00	41.32
8	PETROLEUM	144	3,88,571.32	3,95,519.73	1.79	12	40,660.08	54,609.04	34.31
9	POWER	76	2,42,671.39	2,60,007.47	7.14	21	58,222.53	79,185.66	36.01
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
11	HEALTH AND FAMILY WELFARE	28	13,711.40	14,162.35	3.29	12	4,281.23	4,855.32	13.41
12	RAILWAYS	211	5,17,762.52	6,65,174.44	28.47	146	2,37,690.76	4,13,082.96	73.79
13	ROAD TRANSPORT AND HIGHWAYS	854	5,31,640.50	5,40,821.11	1.73	147	1,04,368.37	1,24,422.77	19.22
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,043.62	25,373.62	80.68	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	8	1,14,518.89	1,35,012.56	17.90
17	WATER RESOURCES	41	68,864.11	69,468.25	0.88	7	2,471.30	3,164.92	28.07
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0.00
19	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	0	0.00	0.00	0.00
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
21	DEPARTMENT OF HIGHER EDUCATION	23	10,424.24	10,390.34	-0.33	3	1,254.49	1,289.59	2.80
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	3	1,659.44	2,518.96	51.80
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	1	271.90	365.00	34.24
Total		1565	24,27,353.93	26,59,914.61	9.58	376	6,46,941.08	9,30,875.97	43.89

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs.						150	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	1	3,492.00	6,840.00	145- 145
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	1	1,383.00	1,938.00	27- 27
3	COAL	103	1,53,190.70	1,57,457.70	2.79	5	20,925.39	23,868.74	19- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	2	642.64	642.64	0.00	0	0.00	0.00	0- 0
6	MINES	6	8,585.67	8,585.67	0.00	0	0.00	0.00	0- 0
7	STEEL	7	21,618.48	28,033.48	29.67	1	15,525.00	21,940.00	85- 85
8	PETROLEUM	144	3,88,571.32	3,95,519.73	1.79	8	26,654.47	33,736.11	13- 66
9	POWER	76	2,42,671.39	2,60,007.47	7.14	15	33,977.12	45,715.36	6- 88
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	28	13,711.40	14,162.35	3.29	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	211	5,17,762.52	6,65,174.44	28.47	88	1,22,346.72	2,24,846.16	3- 312
13	ROAD TRANSPORT AND HIGHWAYS	854	5,31,640.50	5,40,821.11	1.73	43	24,657.08	27,536.32	14- 105
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,043.62	25,373.62	80.68	1	13,334.00	24,664.00	80- 80
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	4	42,786.33	56,308.01	34- 47
17	WATER RESOURCES	41	68,864.11	69,468.25	0.88	6	1,805.52	2,222.74	18- 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
19	DEFENCE PRODUCTION	1	210.00	200.00	-4.76	0	0.00	0.00	0- 0
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
21	DEPARTMENT OF HIGHER EDUCATION	23	10,424.24	10,390.34	-0.33	1	496.00	498.99	57- 57
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	3	1,659.44	2,518.96	5- 56
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	0- 0
Total		1565	24,27,353.93	26,59,914.61	9.58	179	3,15,166.07	4,79,282.39	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	3	27,271.00	43,139.00	84- 145
2	CIVIL AVIATION	19	14,128.17	15,161.45	7.31	4	3,288.50	4,358.06	27- 49
3	COAL	103	1,53,083.23	1,57,457.70	2.86	6	21,220.95	24,168.41	19- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	2	642.64	642.64	0.00	0	0.00	0.00	0- 0
6	MINES	6	7,333.99	8,585.67	17.07	3	6,429.00	7,684.13	33- 46
7	STEEL	7	21,618.48	28,033.48	29.67	1	15,525.00	21,940.00	85- 85
8	PETROLEUM	144	3,77,065.98	3,95,519.73	4.89	24	52,668.79	70,001.30	6- 146
9	POWER	76	1,96,489.83	2,60,007.47	32.33	24	88,091.06	1,44,061.22	6- 162
10	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	28	13,696.26	14,162.35	3.40	1	1,351.00	1,471.00	9- 9
12	RAILWAYS	211	4,08,405.75	6,65,174.44	62.87	96	1,32,322.50	2,74,928.00	3- 312
13	ROAD TRANSPORT AND HIGHWAYS	854	5,17,126.74	5,40,821.11	4.58	35	22,965.74	28,298.41	14- 105
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,373.62	81.07	2	13,765.16	25,125.42	12- 80
16	URBAN DEVELOPMENT	27	2,84,108.54	3,04,523.01	7.19	4	42,786.33	56,308.01	34- 47
17	WATER RESOURCES	41	23,466.28	69,468.25	196.03	7	11,956.56	57,771.61	18- 42
18	SOCIAL JUSTICE	1	170.99	170.99	0.00	0	0.00	0.00	0- 0
19	DEFENCE PRODUCTION	1	246.31	200.00	-18.80	0	0.00	0.00	0- 0
20	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
21	DEPARTMENT OF HIGHER EDUCATION	23	10,455.86	10,390.34	-0.63	1	496.18	498.99	57- 57
22	HOME AFFAIRS	5	2,025.73	2,885.25	42.43	3	1,659.44	2,518.96	5- 56
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
25	RENEWABLE ENERGY	1	271.90	365.00	34.24	0	0.00	0.00	0- 0
Total		1565	21,86,542.05	26,59,914.61	21.65	215	4,46,570.21	7,67,450.52	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	03/2015	459.49	03/2022	201.95
2	MAGADH EXPANSION OC(51 MTY)	08/2008	6,964.33	07/2012	7,254.37	03/2028	815.07
3	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY	11/2015	1,210.12	03/2029	1,210.12	03/2029	91.96
4	BATURA OCP (2.0 MTY)	08/2015	1,186.64	03/2023	1,248.93	03/2026	261.21
5	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	03/2012	489.62	03/2023	416.07
6	KISTARAM OCP	11/2010	242.29	03/2015	164.04	03/2022	143.08
7	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	313.34	03/2021	313.34	03/2024	159.87
8	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	08/2012	1,055.05	03/2018	1,055.05	03/2029	711.21
9	BHANEAGAON OC	02/2015	187.94	03/2023	409.68	03/2023	87.35
10	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	03/2015	349.28	03/2022	306.11
11	JALAGAM VENGALA RAO OCP-II	07/2011	447.06	03/2015	473.22	03/2023	245.94
12	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY)	12/2007	3,504.21	03/2010	3,504.21	03/2029	595.58
13	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	03/2012	207.28	03/2022	271.27
14	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3,145.45	03/2017	3,145.45	03/2031	715.56
15	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY)	12/2007	8,416.19	03/2013	8,416.19	03/2028	1,204.92
16	ADASA UG TO OC	08/2015	288.90	03/2023	333.43	03/2024	158.85
17	KAKATIYAKHANI OPENCAST-2 PROJECT	05/2015	397.09	03/2019	442.42	03/2022	127.15
18	PATHERDIH NLW WASHERY	10/2012	269.82	04/2014	269.82	04/2020	214.74
19	NORTH URIMARI EXPANSION OCP	03/2019	1,553.06	03/2023	778.80	03/2026	416.42
20	SEMARIA OPENCAST PROJECT	05/2019	396.58	03/2026	396.58	03/2026	0.00
21	RECAST PR FOR DHANKASA UG (1.00 MTY)	09/2016	289.29	03/2022	289.30	03/2025	37.55
22	RPR FOR JAMUNIA UG (0.90 MTY)	07/2016	281.25	03/2022	281.25	03/2026	23.52
23	BHATADI EXPANSION OC MINE	02/2016	304.52	03/2019	327.41	03/2022	162.29
24	RECAST EPR AMRAPALI OC	02/2012	4,983.58	03/2020	4,983.58	03/2028	371.36
25	KALYANIKHANI OPENCAST PROJECT	07/2012	417.33	07/2016	384.32	03/2022	168.51
26	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	1,184.33	03/2020	1,184.33	03/2027	436.49
27	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	851.60	03/2020	826.80	03/2026	283.28
	<u>FERTILISERS</u>						

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
28	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	218.83	11/2019	218.83	N.A.	200.49
29	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	239.81	11/2019	239.81	N.A.	205.94
	<u>PETROLEUM</u>						
30	AUGMENTATION OF CTMPL Central Sector Projects	12/2016	228.00	11/2021	228.00	12/2021	164.20
31	SEA WATER DESALINATION PLANT Central Sector Projects	11/2017	581.00	03/2020	637.00	12/2021	593.44
32	RE-LIQUIFIED NATURAL GAS	08/2017	421.00	08/2020	315.00	12/2021	297.95
	<u>POWER</u>						
33	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	04/2016	374.63	12/2021	259.44
34	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	05/2016	14,733.37	11/2019	14,733.37	10/2021	11,823.97
35	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	02/2017	5,070.13	04/2020	5,070.13	06/2021	4,236.67
36	EASTERN REGION STRENGTHENING SCHEME-XV	04/2016	454.11	04/2018	454.11	06/2021	345.21
37	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	03/2016	808.63	01/2018	808.63	06/2021	690.89
	<u>RAILWAYS</u>						
38	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	03/2019	614.00	N.A.	275.06
39	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1,049.69	12/2006	3,404.92	N.A.	3,837.57
40	DEOGHAR - SULTANGANJ (INL), ER	04/2000	607.09	02/2013	1,425.44	03/2024	638.87
41	HATHUA-BHATNI (N L) (NER)	04/2005	230.03	12/2022	230.03	12/2022	277.14
42	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	04/2010	157.94	11/2018	157.94	03/2021	51.75
43	3RD LINE BETWEEN BHUSAWAL-JALGAON	04/2011	184.06	03/2019	325.00	N.A.	325.52
44	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	04/2009	257.42	03/2014	257.42	03/2025	109.66
45	MAGRAHAT-DIAMOND HARBOUR WITH	04/2009	499.96	02/2012	680.68	03/2025	142.05

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL						
46	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	04/2003	337.96	N.A.	336.96	03/2025	40.65
47	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	04/2000	297.47	N.A.	298.22	03/2025	36.13
48	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	494.54	03/2005	494.59	03/2025	30.12
49	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	04/2011	299.60	03/2017	335.62	03/2026	1.12
50	TARAKESHWAR-MAGRA NEW BG LINE	04/2010	365.17	N.A.	527.54	03/2025	1.76
51	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	04/2007	450.55	N.A.	250.55	03/2025	20.11
52	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	04/2008	228.05	N.A.	228.05	03/2024	1.53
53	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	04/2008	678.62	N.A.	678.62	N.A.	3.20
54	MOTIHARI-SITAMARHI (NL)	04/2006	211.00	N.A.	1,006.00	N.A.	4.99
55	DARBANGHA-KUSHESHWARSTHAN (NL)	04/2005	205.00	N.A.	205.00	N.A.	5.21
56	GAYA-CHATRA (NL)	04/2008	415.67	N.A.	549.75	N.A.	15.58
57	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	04/2008	445.25	N.A.	445.25	N.A.	1.15
58	NAWADA-LAXMIPUR (NL)	04/2008	620.57	N.A.	620.57	N.A.	0.31
59	ARA-BHABHUA ROAD (NL)	04/2008	633.87	N.A.	633.87	N.A.	0.40
60	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	04/2010	149.90	03/2015	266.61	03/2019	240.53
61	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	04/2010	174.56	N.A.	174.56	03/2025	71.43
62	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	04/2005	595.51	03/2017	769.40	03/2025	97.40
63	HANSNABAD-HINGALGANJ NEW BG LINE	04/2010	172.03	N.A.	260.10	03/2025	11.77
64	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	04/2007	450.00	N.A.	1,261.34	03/2025	0.00
65	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	03/2006	545.70	03/2025	149.30
66	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	04/2012	714.10	04/2016	714.10	N.A.	65.20
67	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND	04/1999	819.23	N.A.	1,090.60	N.A.	1,089.12

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
	MM CHALSA NAXAL RAJABHATKHOWA JAINTI						
68	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	04/2007	931.98	N.A.	1,122.00	12/2022	1,005.24
69	ERODE-PALANI	04/2008	288.57	N.A.	603.23	03/2030	1.68
70	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	04/2010	221.42	N.A.	380.00	N.A.	38.20
71	CHENNAI-CUDDALORE VIA MAMALLAPURAM	04/2008	523.52	N.A.	1,205.00	03/2030	2.28
72	ATTIPPATTU PUTTUR	04/2008	151.84	02/2019	527.37	03/2030	2.59
73	MUZAFFARPUR-DARBANGHA (NL)	04/2008	281.30	N.A.	281.30	N.A.	0.59
74	KURSELA-BIHARIGANJ (NL)	04/2008	192.56	N.A.	192.56	N.A.	0.39
75	GARHWA ROAD-RAMNA	03/2015	348.23	03/2021	390.00	03/2022	407.08
76	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	02/2017	1,567.00	03/2024	1,567.00	03/2026	0.00
77	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	03/2005	991.83	N.A.	922.01
78	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	03/2012	153.83	N.A.	154.15	N.A.	109.05
79	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	346.32	03/2019	346.32	N.A.	320.28
80	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	05/2014	207.00	03/2018	207.00	N.A.	153.83
81	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	01/2013	387.70	03/2018	487.13	N.A.	434.63
82	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	305.00	03/2019	305.00	N.A.	269.73
83	MULTI MODAL LOGISTICS PARK AT KATHUWAS	01/2011	493.17	03/2018	493.17	N.A.	464.53
84	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	1,027.40	03/2003	2,373.00	03/2030	485.04
85	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	04/2016	602.27	12/2021	1,167.00	10/2021	1,135.28
86	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	07/2014	560.09	N.A.	560.09
87	MATHURA-PLWAL 4TH LINE (80KM)	04/2015	668.70	03/2020	680.00	N.A.	531.20
88	CHAKRADHARPUR TO GOILKERA 3RD LINE (34 KM)	11/2015	354.54	12/2018	354.54	06/2020	303.25
89	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN	02/1999	380.60	04/2010	1,090.60	N.A.	1,089.12
90	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	174.00	03/2019	174.00	N.A.	172.08
91	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	04/2010	651.00	03/2015	1,009.00	03/2025	7.96

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
92	BOWAICHANDI-ARAMBAGH	04/2010	267.37	N.A.	620.00	03/2025	41.78
93	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	04/2013	420.18	03/2020	480.00	09/2021	387.54
94	AJMER-KOTA (NASIRABAD-JAUNDRI)	04/2013	822.00	N.A.	821.64	N.A.	0.00
95	RATLAM-DUNGARPUR VIA BANSWARA (NL)	04/2011	2,082.75	N.A.	4,262.36	N.A.	191.39
96	AHMEDABAD-BOTAD (GC)	04/2012	975.62	12/2021	1,555.42	10/2021	1,755.44
97	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	03/2007	243.78	12/2021	895.00	12/2021	116.44
98	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	05/2015	873.71	N.A.	2,215.27	N.A.	4.60
99	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	03/2007	1,026.00	N.A.	182.57
100	MACHERLA-NALGONDA(NL)(SCR)	07/1998	458.25	N.A.	458.25	N.A.	3.69
101	KISHANGANJ JALALGARH, NL, NEFR	04/2008	333.76	N.A.	360.00	N.A.	6.74
102	KOSI BRIDGE (NL), ECR	04/2002	499.41	03/2020	516.02	12/2021	468.05
103	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	04/2000	1,180.19	12/2008	4,541.38	12/2021	3,983.32
104	QADIAN-BEAS	04/2011	205.22	N.A.	841.90	03/2024	1.73
105	UNCHAHAR-AMETHI	04/2012	1,229.00	N.A.	489.64	N.A.	105.51
106	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	04/2011	166.89	N.A.	166.89	03/2025	0.02
107	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	03/2012	155.81	03/2020	238.03	06/2022	224.76
108	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	477.88	03/2012	751.55	02/2022	723.12
109	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	02/2008	171.10	03/2012	275.08	N.A.	141.55
110	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	09/2006	227.40	N.A.	227.40	03/2030	65.02
111	KICHHA-KHATIMA (NL) - NER	04/2003	142.45	N.A.	228.40	N.A.	0.15
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
112	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	02/2009	612.58	N.A.	612.58
113	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	09/2014	425.19	09/2016	425.19	N.A.	276.40
114	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	06/2015	1,012.90	03/2016	950.74	N.A.	226.10
115	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	02/2018	1,103.88	N.A.	1,103.88	N.A.	720.73
116	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO	02/2018	261.76	N.A.	223.49	02/2022	213.27

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	FEROZPUR IN THE STATE OF PUNJAB						
117	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	03/2018	323.98	09/2018	323.98	11/2022	50.13
118	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	01/2018	607.00	N.A.	607.00	08/2021	510.71
119	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	03/2016	429.52	08/2016	429.52	N.A.	238.28
120	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	02/2017	167.28	04/2017	167.28	04/2022	68.50
121	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	09/2016	1,244.10	N.A.	1,244.10	N.A.	1,665.00
122	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	07/2016	331.46	10/2018	331.46	N.A.	267.94
123	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	07/2016	688.70	N.A.	688.70	N.A.	870.48
124	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D EPC	08/2020	232.29	04/2022	232.29	04/2022	4.98
125	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	07/2016	208.88	10/2019	208.88	03/2021	183.54
126	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	218.90	03/2020	218.90	03/2021	147.70
127	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	03/2016	249.50	05/2019	249.50	04/2021	229.82
128	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	215.16	09/2019	215.16	10/2019	145.76
129	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	01/2017	256.66	N.A.	256.66	05/2023	16.42
130	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	03/2018	874.25	N.A.	866.55	10/2021	866.55
131	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	02/2018	716.76	N.A.	716.76	07/2021	687.07
132	FOUR LANING OF MAHUVA TO	06/2016	763.23	06/2019	763.23	N.A.	198.01

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM PPP (BOT)						
133	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR PPP (BOT)	06/2016	637.18	06/2019	637.18	09/2019	550.35
134	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	05/2016	364.56	N.A.	375.12	04/2021	353.42
135	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	05/2016	834.64	N.A.	834.64	N.A.	209.94
136	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	02/2016	273.20	02/2019	273.20	N.A.	670.27
137	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	08/2015	275.90	N.A.	275.90	N.A.	289.13
138	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	479.20	05/2018	479.20	N.A.	712.89
139	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	04/2010	1,170.52	06/2012	1,170.52	03/2019	2,051.36
140	FOUR LANING OF GWALIOR-SHIVPURI PPP (BOT)	05/2013	1,055.00	11/2015	1,601.77	N.A.	1,393.40
141	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 EPC	01/2014	255.75	09/2017	348.43	N.A.	319.68
142	GWALIOR-JHANSI, NH-75 PPP (ANNUITY)	12/2003	604.00	12/2009	364.59	09/2020	360.15
143	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	07/2009	655.17	N.A.	655.17
144	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT EPC	03/2015	258.97	08/2015	268.92	N.A.	229.77
145	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH EPC	07/2015	197.16	10/2018	197.16	N.A.	91.25
146	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) PPP (BOT)	05/2009	2,288.00	11/2011	2,288.00	N.A.	3,450.00
	<u>URBAN DEVELOPMENT</u>						
147	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	6,928.00	03/2019	6,928.00	N.A.	6,928.00
148	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	238.56	05/2020	238.56	02/2022	208.57

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>WATER RESOURCES</u>						
149	IRRIGATION WORK OF BAGMATI	10/2005	956.00	03/2015	721.37	N.A.	712.37
150	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	12/2019	330.05	11/2021	263.53

FLASH REPORT

TABLE-14

List of projects added Rs. 150 Crore and above					(February 2022)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT	11/2015	489.62	3/2023	489.62	3/2023
2	RCE OF INDARAM OPENCAST PROJECT	8/2017	349.28	3/2021	349.28	3/2021
3	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II	3/2019	473.22	3/2021	473.22	3/2021
4	RCE OF KALYANIKHANI OPENCAST PROJECT	3/2016	384.32	3/2020	384.32	3/2020
5	EXPANSION PROJECT AMRAPALI OCP	8/2020	5,136.15	3/2028	5,136.15	3/2028
6	ADASA UG TO OC (1.50 MTY)	11/2018	333.43	3/2024	333.43	3/2024
7	BHANEAGAON OC (1MTY)	2/2017	409.68	3/2023	409.68	3/2023
8	EXPANSION PR OF JHANJRA UG (5.00 MTY)	4/2020	1,210.12	3/2029	1,210.12	3/2029
9	ANANTA OCP EXPANSION PH III	8/2008	228.08	3/2012	228.08	3/2012
10	BHATADI EXPASION OC (0.975 MTY)	2/2016	327.41	3/2019	327.41	9/2026
11	RAMPUR BATURA OC (4.0 MTY)	7/2019	1,248.93	3/2026	1,248.93	3/2026
12	JAGANNATHPUR OC RCE (3.0 MTY)	7/2016	459.49	3/2020	459.49	3/2022
13	MUNGOLI NIRGUDA EXTENSION (DEEP) OC	11/2020	826.80	3/2026	826.80	3/2026
14	BALARAM EXPANSION OCP	8/2020	3,504.21	3/2029	3,504.21	3/2029
15	RPR FOR JAMUNIA UG	8/2020	281.25	3/2026	281.25	3/2026
16	GOPALJI-KANIHA OCP	8/2020	8,416.19	3/2028	8,416.19	3/2028
17	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY)	9/2018	313.34	3/2024	313.34	3/2024
18	BHUBANESWARI EXPANSION OCP	8/2020	3,145.45	3/2031	3,145.45	3/2031
19	DHANKASA UG (RECAST) (1 MTY)	2/2020	289.30	3/2025	289.30	3/2025
20	DINESH (MAKARDHOKDA-III) OC (8.0 MTY)	2/2020	1,184.33	3/2027	1,184.33	3/2027
21	SONEPUR BAZARI EXPANSION OC	7/2021	5,365.88	3/2029	5,365.88	3/2029
22	UCE OF EPR OF NORTH URIMARI OCP	7/2021	778.80	3/2026	778.80	3/2026
23	REVISED PROJECT REPORT MAGADH EXPANSION OCP	8/2020	7,254.37	3/2028	7,254.37	3/2028
24	RCE OF KISTARAM OPENCAST PROJECT	3/2017	164.04	3/2021	164.04	3/2021
25	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	8/2017	442.42	3/2020	442.42	3/2020
	<u>POWER</u>					
26	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION EPC	5/2021	179.29	4/2023	179.29	4/2023
27	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2021	1,184.88	9/2022	1,184.88	9/2022
28	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II	10/2019	1,031.00	8/2021	1,031.00	8/2021

List of projects added Rs. 150 Crore and above					(February 2022)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	(2000 MW) IN GUJARAT					
29	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	353.85	12/2022	353.85	12/2022
30	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	713.82	12/2022	713.82	12/2022
31	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	1,006.00	12/2022	1,006.00	12/2022
32	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS	11/2018	496.11	6/2020	496.11	3/2022
33	SOUTHERN REGION SYSTEM STRENGTHENING - XXV	7/2019	154.72	7/2021	154.72	2/2022
34	NORTH EASTERN REGION STRENGTHENING SCHEME - III	9/2015	167.31	12/2017	167.31	3/2022
35	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII	9/2018	221.36	3/2021	221.36	2/2022
36	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	11/2018	241.38	11/2021	241.38	5/2022
37	NORTH EASTERN REGION STRENGTHENING SCHEME-XII	5/2021	576.42	3/2023	576.42	3/2023
38	EASTERN REGION STRENGTHENING SCHEME - XXIII	7/2020	239.89	6/2021	239.89	3/2022
39	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA PPP (BOT)	1/2020	562.86	1/2021	562.86	3/2022
40	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN	8/2019	2,578.47	12/2020	2,578.47	2/2022
41	WESTERN REGION SYSTEM STRENGTHENING - XX	7/2019	226.98	8/2021	226.98	2/2022
42	NORTHERN REGION SYSTEM STRENGTHENING - XL	2/2019	572.98	12/2020	572.98	12/2020
43	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	1,562.00	12/2022	1,562.00	12/2022
44	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	1,340.81	12/2022	1,340.81	12/2022
45	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	1/2019	267.33	3/2022	267.33	3/2022
	<u>STEEL</u>					
46	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP EPC	1/2022	970.18	5/2025	970.18	5/2025

TABLE-15

Milestones (Cumulative due & achieved) Rs. 150 Crore and above

Total 6007

Achieved up to month 2991

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II AAI	1,216.90	1,216.90	10/2022	12/2023	03/2024	3
2	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN AAI	456.86	456.86	09/2020	09/2022	12/2022	3
3	UPGRADATION OF JABALPUR AIRPORT AAI	412.24	412.24	06/2021	12/2022	03/2023	3
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR AAI	417.23	707.73	09/2018	06/2022	10/2022	4
5	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI AAI	951.28	951.28	10/2021	12/2022	04/2023	4
6	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT AAI	1,405.00	1,405.00	08/2022	03/2023	08/2023	5
7	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI AAI	2,467.00	2,467.00	02/2022	06/2024	12/2024	6
8	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT AAI	346.27	480.33	09/2021	06/2023	12/2023	6
9	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH AAI	645.63	645.63	08/2022	11/2022	10/2023	11
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT AAI	475.39	475.39	04/2021	08/2022	08/2023	12
11	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA AAI	458.00	458.00	03/2020	04/2022	03/2024	23

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
12	2.0 MTPA BHOJUDIH NLW WASHERY BCCL	304.13	341.22	03/2017	10/2022	12/2022	2
13	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	11/2022	06/2023	7
14	PATHERDIH 2.5 NLW COAL WASHERY BCCL	243.00	334.27	04/2018	10/2022	06/2023	8
15	CHURI BENTI UG (0.81 MTY) CCL	163.51	163.51	03/2011	03/2022	03/2023	12
16	RAJRAPPA RCE OCP (3.0 MTY) CCL	510.85	510.85	03/2016	03/2022	03/2023	12
17	KARMA OCP (1.0MTY) CCL	162.46	162.46	03/2014	03/2022	03/2023	12
18	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	03/2022	03/2023	12
19	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	03/2019	02/2023	04/2024	14
20	MURAIIDH UG TURN-KEY PROJECT BCCL	339.88	339.88	04/2014	04/2023	10/2025	30
	<u>FERTILISERS</u>						
21	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT NFL	215.92	215.92	11/2019	12/2021	01/2022	1
22	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY RCF	426.72	426.72	04/2020	01/2022	03/2022	2
	<u>MINES</u>						
23	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU NALCO	166.62	163.17	06/2019	12/2020	12/2022	24
	<u>STEEL</u>						
24	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	03/2022	06/2022	3
25	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 NMDC Central Sector Projects	2,907.00	2,907.00	06/2023	06/2023	06/2024	12
	<u>PETROLEUM</u>						
26	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	02/2022	03/2022	1
27	LPG BP PROJECT KHORDHA IOCL Central Sector Projects	161.59	161.59	12/2019	12/2022	01/2023	1

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
28	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY IOCL	189.00	189.00	01/2021	02/2022	03/2022	1
29	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT GAIL	286.42	327.01	08/2020	03/2022	04/2022	1
30	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	01/2024	02/2024	1
31	SITARGANJ LPG PROJECT IOCL Central Sector Projects	160.10	160.10	02/2020	08/2022	10/2022	2
32	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN OIL	224.75	198.00	08/2020	01/2022	03/2022	2
33	DOBHI-DURGAPUR PIPELINE PROJECT GAIL	2,433.00	2,433.00	12/2020	03/2022	06/2022	3
34	KHARAGPUR LPG BOTTLING PLANT IOCL	163.02	207.36	04/2020	07/2022	10/2022	3
35	PIPELINE REPLACEMENT PROJECT (PRP-VI) ONGC	763.92	829.58	12/2020	02/2022	05/2022	3
36	DHAMRA-ANGUL PIPELINE PROJECT GAIL	1,933.00	1,933.00	12/2020	03/2022	07/2022	4
37	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE IOCL	906.00	906.00	02/2020	03/2022	07/2022	4
38	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT IOCL	1,636.00	1,636.00	08/2020	04/2022	09/2022	5
39	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY IOCL	909.00	909.00	01/2021	03/2022	08/2022	5
40	COMPRESSED BIO GAS PLANT AT GORAKHPUR IOCL	164.69	164.69	07/2021	03/2022	08/2022	5
41	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	5,909.00	12/2012	08/2024	02/2025	6
42	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP IOCL	316.20	316.20	10/2021	03/2022	09/2022	6
43	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY IOCL	255.40	255.40	08/2020	03/2022	10/2022	7
44	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT GAIL	217.92	217.92	04/2021	03/2022	10/2022	7
45	HEERA REDEVELOPMENT - PHASE III ONGC	2,494.68	2,354.72	03/2022	03/2022	03/2023	12
46	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 ONGC	650.82	650.82	03/2019	09/2021	05/2023	20

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>POWER</u>						
47	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	02/2022	03/2022	1
48	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	2,426.00	12/2018	02/2022	03/2022	1
49	JETSAR SOLAR 160 MW NTPC EPC	702.28	702.28	03/2021	02/2022	03/2022	1
50	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII PGCIL	379.95	379.95	12/2019	02/2022	04/2022	2
51	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	02/2022	04/2022	2
52	RAMAGUNDAM FLOATING SOLAR 100 MW NTPC EPC	401.90	442.03	04/2021	03/2022	05/2022	2
53	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC	2,978.48	5,867.38	03/2013	09/2024	12/2024	3
54	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	679.00	11/2018	03/2022	06/2022	3
55	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,998.00	11/2020	10/2022	02/2023	4
56	ANTA SOLAR 90 MW NTPC EPC	382.22	382.22	03/2022	05/2022	10/2022	5
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCIL	2,491.58	3,860.35	06/2013	12/2024	06/2025	6
58	RAMMAM-III HEPP (3X40 MW) NTPC	1,381.84	1,803.00	09/2019	12/2024	07/2025	7
59	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES PGCIL	5,111.33	6,700.00	12/2018	03/2022	01/2024	22
	<u>HEALTH AND FAMILY WELFARE</u>						
60	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB HSCC	152.95	177.92	02/2018	03/2021	04/2021	1
61	GERIATRICS BLOCK- AIIMS DLEHI HSCC	156.56	205.00	N.A.	12/2021	01/2022	1
62	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI HSCC Central Sector Projects	268.84	284.67	N.A.	03/2021	05/2021	2
63	AIIMS - MOTHER AND CHILD BLOCK HSCC	204.44	250.00	05/2017	03/2021	06/2021	3
64	NEIGRIHMS SHILLONG MEGHALYA HSCC	363.99	363.99	05/2018	03/2022	06/2022	3

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
65	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR HSCC	505.58	586.96	03/2018	09/2019	04/2020	7
66	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR HSCC	168.90	191.20	05/2017	07/2019	01/2021	18
67	CNCI KOLKATA WEST BENGAL HSCC	244.00	248.00	09/2018	05/2019	12/2021	31
	RAILWAYS						
68	BHADRACHALAM ROAD-SATTUPALLI SCR	704.31	927.94	03/2020	02/2022	03/2022	1
69	KIUL - GAYA DOUBLING PROJECT ECR	1,200.20	1,200.20	03/2020	03/2023	05/2023	2
70	AGARTALA-AKHAURA NL NFR	569.63	708.73	03/2020	06/2022	09/2022	3
71	HOSPET-HUBLI-LONDA-VASCODAGAMA DL RVNL	2,127.00	3,300.00	03/2023	12/2022	03/2023	3
72	MARIKUPPAM - KUPPAM SWR	279.54	279.54	03/2016	12/2023	03/2024	3
73	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) RVNL	1,503.71	3,633.12	03/2020	03/2022	06/2022	3
74	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) RVNL	713.48	2,725.00	03/2020	12/2021	03/2022	3
75	RAIPUR - TITLAGARH - DOUBLING RVNL	1,402.02	1,300.00	03/2020	03/2022	06/2022	3
76	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,268.32	02/2019	12/2021	03/2022	3
77	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	12/2022	04/2023	4
78	KODERMA-RANCHI VIA BARKAKANA (NL),ECR ECR	1,033.07	3,650.00	N.A.	03/2022	07/2022	4
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. RVNL	2,913.51	4,834.54	03/2016	03/2025	07/2025	4
80	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD RVNL	632.68	950.00	03/2016	12/2021	04/2022	4
81	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	2,009.00	03/2020	12/2021	04/2022	4
82	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRTP	495.74	774.51	06/2013	07/2022	12/2022	5
83	DHASA-JETALSAR (GC) RVNL	644.38	923.28	03/2021	12/2021	05/2022	5

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
84	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING RVNL	760.00	1,536.00	03/2020	06/2022	12/2022	6
85	PURULIA TO KOTSHILA DOUBLING (39.1 KM) SER	338.00	393.83	06/2022	06/2023	12/2023	6
86	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	324.73	1,090.00	03/2012	11/2022	06/2023	7
87	PALANPUR-SAMAKHAYALI (DL) RVNL	1,548.66	2,538.01	12/2021	03/2022	12/2022	9
88	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	927.01	1,457.79	03/2019	06/2022	03/2023	9
89	BANASPANI- JAKHPURA - DOUBLING RVNL	942.95	1,552.26	03/2019	06/2022	03/2023	9
90	BINA - KOTA DOUBLING WITH RE RVNL	1,485.85	1,835.83	12/2020	12/2021	09/2022	9
91	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM ECR	744.04	1,215.54	03/2021	03/2024	12/2024	9
92	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS WR	537.31	537.31	03/2024	03/2024	12/2024	9
93	BANDEL-BOINCHI 3RD LINE ER	288.35	502.48	N.A.	03/2021	02/2022	11
94	MANIYACHI - NAGERCOIL (102 KM) DOUBLING RVNL	1,700.00	1,305.00	03/2022	06/2022	05/2023	11
95	KODERMA-TILAIYA (NL), ECR	459.91	1,625.87	N.A.	03/2023	03/2024	12
96	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	385.20	1,145.79	03/2019	03/2023	03/2024	12
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) RVNL	3,951.98	4,259.48	03/2016	03/2025	03/2026	12
98	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) ECR	372.14	1,470.50	N.A.	03/2023	03/2024	12
99	KIRANDUL - JAGDALPUR DOUBLING ECOR	1,160.00	1,160.83	03/2020	03/2023	03/2024	12
100	GUNTUR-GUNTAKAL SCR	3,631.00	3,887.48	03/2022	03/2024	03/2025	12
101	JAGDALPUR-KORAPUT DOUBLING ECOR	1,547.38	1,547.38	03/2022	03/2023	03/2024	12
102	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE ECOR	701.61	810.02	11/2018	03/2024	03/2025	12
103	KADUR CHIKMAGALUR SAKLIESHPUR NEW LINE (93 KM) SWR	644.78	817.23	03/2017	03/2025	03/2026	12
104	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) ECR	162.87	614.45	N.A.	12/2023	03/2025	15

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
105	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) WR	844.10	844.10	N.A.	03/2024	10/2025	19
106	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR ECR	528.65	2,066.78	N.A.	03/2023	12/2024	21
107	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) WR	320.66	1,378.11	03/2019	03/2023	03/2025	24
108	SHIMOGA-HARIHAR NL SWR	832.47	832.47	03/2016	03/2024	03/2026	24
109	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, ECR	329.39	1,483.14	N.A.	03/2022	03/2024	24
110	NIMACH BADI SADRI NEW LINE PROJECT WR	495.18	495.18	03/2022	03/2024	03/2026	24
111	ARARIA-SUPAUL (NL) ECR	1,605.17	1,605.17	N.A.	03/2023	12/2025	33
112	KOTLPALLI-NARASAPUR (NL) (SCR) SCR	1,045.20	2,120.16	03/2009	03/2024	03/2027	36
113	RATLAM-MHOW-KHANDWA-AKOLA (GC) WR	3,503.69	6,383.82	03/2022	03/2023	03/2026	36
114	HUBLI-ANKOLA(NL),SWR SWR	2,315.00	5,174.30	N.A.	12/2024	03/2028	39
115	CHIKBALLA-PUR-GOWRIBIDANUR NL SWR	327.25	367.77	N.A.	12/2023	03/2027	39
116	SAKRI-HASANPUR ROAD (NL) ECR	325.00	735.20	N.A.	03/2021	12/2024	45
117	BANGLORE - SATYAMANGALAM (NL)(SWR) SWR	1,382.78	1,383.00	03/2002	03/2024	03/2028	48
118	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL SWR	558.00	692.43	N.A.	12/2023	03/2028	51
119	SRINIVASA-PURA-MADANAPALLI NL SWR	296.00	466.65	N.A.	12/2023	03/2028	51
120	CHOTTAUDEPUR-DHAR(NL) WR	1,347.26	1,524.68	03/2022	03/2023	10/2027	55
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
121	PUNE-SATARA(NH-4) NHAI PPP (BOT)	1,724.55	1,724.55	03/2013	03/2022	04/2022	1
122	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	02/2022	03/2022	1
123	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM MoRTH EPC	268.08	390.73	05/2017	05/2022	06/2022	1
124	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	02/2022	03/2022	1

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
125	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) NHAI EPC	289.21	289.21	N.A.	01/2022	02/2022	1
126	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS MoRTH	162.56	162.56	03/2018	02/2022	03/2022	1
127	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS MoRTH	166.21	174.90	08/2018	02/2022	03/2022	1
128	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS MoRTH	184.62	184.62	02/2018	02/2022	03/2022	1
129	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. MoRTH	205.05	205.05	03/2017	02/2022	03/2022	1
130	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS MoRTH	217.22	226.88	08/2018	02/2022	03/2022	1
131	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS MoRTH	233.04	233.04	03/2018	02/2022	03/2022	1
132	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS MoRTH	279.44	279.44	03/2018	02/2022	03/2022	1
133	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM MoRTH	877.79	949.54	06/2019	02/2022	03/2022	1
134	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE NHIDCL	818.00	818.00	N.A.	03/2023	04/2023	1
135	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA MoRTH	536.65	536.65	12/2019	02/2022	03/2022	1
136	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION MoRTH	335.32	335.32	06/2017	03/2022	04/2022	1
137	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 NHIDCL EPC	636.42	636.42	12/2022	12/2022	01/2023	1
138	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL NHIDCL EPC	588.95	588.95	11/2018	02/2022	04/2022	2
139	FOUR LANING WITH PS TALEBANI -SMBALPUR NHAI	752.28	752.28	N.A.	03/2022	05/2022	2
140	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T NHAI	804.97	804.97	06/2018	03/2022	05/2022	2

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
141	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS MoRTH	809.16	809.16	07/2018	01/2022	03/2022	2
142	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	1,928.22	04/2015	12/2021	03/2022	3
143	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. NHIDCL EPC	289.99	289.99	12/2018	12/2021	03/2022	3
144	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM NHAI PPP (BOT)	822.90	822.90	04/2018	12/2021	03/2022	3
145	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI	479.00	479.00	N.A.	12/2022	03/2023	3
146	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 NHAI	1,737.00	2,421.37	N.A.	09/2021	12/2021	3
147	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 NHIDCL	245.79	245.79	N.A.	12/2021	03/2022	3
148	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV NHAI	894.00	929.32	04/2020	03/2022	06/2022	3
149	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 NHAI	953.09	953.09	N.A.	03/2022	06/2022	3
150	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O NHIDCL	234.27	234.27	10/2018	03/2022	06/2022	3
151	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 NHIDCL	290.05	290.05	11/2017	12/2021	03/2022	3
152	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION MoRTH	496.02	496.02	03/2015	03/2022	06/2022	3
153	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI NHAI EPC	989.66	989.66	01/2024	01/2024	04/2024	3
154	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI NHIDCL	403.36	403.36	06/2018	03/2022	07/2022	4
155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO NHIDCL	215.12	215.12	09/2018	11/2021	03/2022	4
156	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	01/2022	05/2022	4

List of projects reporting additional delayed Rs. 150 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
157	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND MoRTH	160.27	213.97	08/2019	11/2022	03/2023	4
158	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) NHAI	1,071.61	1,048.10	N.A.	12/2021	05/2022	5
159	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 MoRTH	205.95	205.95	01/2021	11/2021	04/2022	5
160	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN NHAI	754.54	756.27	03/2020	09/2022	03/2023	6
161	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 NHIDCL	274.31	274.31	05/2018	03/2022	09/2022	6
162	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA NHIDCL	417.24	417.24	05/2018	03/2022	09/2022	6
163	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM NHIDCL	306.28	306.28	05/2019	03/2022	09/2022	6
164	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 MoRTH	497.14	572.66	08/2016	06/2022	12/2022	6
165	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N MoRTH	236.78	263.26	08/2019	08/2022	03/2023	7
166	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM NHIDCL	391.00	391.00	10/2018	03/2022	12/2022	9
167	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 NHIDCL	188.78	188.78	N.A.	03/2022	12/2022	9
168	2-LANING FROM MANU-SIMLUNG (PKG I) NHIDCL EPC	247.76	247.76	01/2022	01/2022	10/2022	9
169	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG NHAI	614.48	614.48	N.A.	08/2021	06/2022	10
170	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	1,827.00	03/2021	07/2021	05/2022	10
171	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN MoRTH	160.00	160.00	09/2021	02/2022	12/2022	10
172	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL NHAI	870.00	1,418.78	03/2019	11/2020	10/2021	11

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
173	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. MoRTH	426.18	426.18	09/2020	01/2022	12/2022	11
174	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H MoRTH	271.17	291.20	11/2018	03/2022	03/2023	12
175	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. NHIDCL	200.44	200.44	N.A.	12/2021	12/2022	12
176	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 MoRTH	351.00	255.00	06/2021	06/2021	06/2022	12
177	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N NHIDCL EPC	402.94	402.94	04/2022	04/2022	05/2023	13
178	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (NHIDCL	262.97	262.97	10/2018	01/2022	03/2023	14
179	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN MoRTH	396.86	396.86	09/2019	10/2021	12/2022	14
180	NAGPUR RING ROAD PACKAGE-1 NHAI	546.00	546.00	07/2019	12/2021	03/2023	15
181	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	08/2021	12/2022	16
182	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST MoRTH	243.89	243.89	N.A.	09/2020	02/2022	17
183	NAGPUR RING ROAD PACKAGE-2 NHAI	591.66	591.66	07/2019	12/2021	08/2023	20
184	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 NHAI Central Sector Projects	950.64	1,168.00	08/2017	02/2022	10/2023	20
185	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO MoRTH	254.30	254.30	10/2020	06/2021	03/2023	21
186	SRINAGAR TO BANIHAL NHAI PPP (ANNUITY)	1,100.70	1,100.70	06/2014	10/2020	09/2022	23
187	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHAI PPP (BOT)	1,655.01	1,655.01	08/2016	12/2020	03/2023	27
	TELECOMMUNICATIONS						

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
188	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT CPWD FOR TELECO	248.20	248.20	03/2018	01/2022	03/2022	2
189	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART BSNL Central Sector Projects	431.16	461.42	06/2021	03/2022	06/2022	3
	<u>URBAN DEVELOPMENT</u>						
190	NAGPUR METRO RAIL NMRCL	8,680.00	9,759.79	03/2018	12/2021	02/2022	2
191	SURAT METRO RAIL PROJECT MEGA	12,020.32	12,020.32	03/2024	03/2024	06/2024	3
192	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI CPWD	299.97	299.97	09/2020	01/2023	05/2023	4
193	AGRA METRO RAIL PROJECT LMRCL Public Private (SPV)	8,379.62	8,379.62	03/2024	05/2025	12/2025	7
194	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I CPWD	1,180.00	1,100.80	07/2021	06/2023	06/2024	12
195	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I CPWD	1,128.00	1,128.00	03/2022	06/2023	06/2024	12
196	BHOPAL METRO RAIL MPMRCL	6,941.40	6,941.40	02/2023	02/2023	05/2025	27
197	INDORE METRO RAIL MPMRCL	7,500.80	7,500.80	02/2023	02/2023	07/2025	29
	<u>WATER RESOURCES</u>						
198	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR BUIDCO	225.77	398.90	03/2020	02/2022	03/2022	1
199	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI DJB	515.07	515.07	01/2021	12/2021	02/2022	2
200	SAIDPUR SEWER NETWORK PATNA BUIDCO	268.63	268.63	01/2021	03/2022	05/2022	2
201	SEWERAGE SCHEME AT PAHARI ZONE V PATNA BUIDCO	356.37	356.37	04/2021	04/2022	06/2022	2
202	MATHURA SEWERAGE SCHEME UP JalNigam	460.45	460.45	12/2020	12/2021	03/2022	3
203	SEWERAGE TREATMENT PLANT AT PAHARI PATNA BUIDCO	191.62	191.62	11/2020	12/2021	03/2022	3

List of projects reporting additional delayed Rs. 150 Crore and above (February 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
204	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH UPJalNigam	231.79	234.03	12/2021	12/2022	06/2023	6
205	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS KMDA	384.96	384.96	04/2022	04/2024	12/2024	8
206	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR KMDA	287.53	287.53	04/2022	04/2024	12/2024	8
207	I AND D AND STP WORKS AT BURDWAN WEST BENGAL KMDA	234.31	234.31	04/2022	04/2024	12/2024	8
208	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA KMDA	307.12	307.12	09/2022	04/2024	12/2024	8
209	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA UPJalNigam	767.59	767.59	09/2021	03/2022	12/2022	9
210	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS UPJalNigam	967.23	967.23	09/2021	12/2021	09/2022	9
211	SEWER NETWORK SPS AND STP BEGUSARAI BUIDCO	230.06	230.06	07/2021	04/2022	03/2023	11
212	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA BUIDCO	578.89	578.89	06/2022	12/2022	12/2023	12
213	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA BUIDCO	824.00	824.00	06/2022	12/2022	12/2023	12
	<u>DEFENCE PRODUCTION</u>						
214	RESIDENTIAL QUATERS FOR HAL,BANGLORE CPWD FOR DEFENC	246.31	200.00	02/2020	03/2022	06/2022	3
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
215	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR CPWD EDUCATION	790.79	790.79	03/2022	06/2022	09/2022	3
	<u>HOME AFFAIRS</u>						
216	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	2,000.00	10/2019	05/2022	06/2022	1
217	NSG AT KOLKATA CPWD FOR MHA Central Sector Projects	162.88	228.63	04/2018	08/2022	12/2022	4

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (February 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)

FLASH REPORT

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,292,61.00	1,32,609.00	73,812.20
CIVIL AVIATION	19	14,128.17	141,28.17	15,161.45	5,956.58
COAL	103	1,53,083.23	1,531,90.70	1,57,457.70	47,810.81
FINANCE	2	557.77	5,57.77	557.73	412.93
FERTILISERS	2	642.64	6,42.64	642.64	549.98
MINES	6	7,333.99	85,85.67	8,585.67	1,907.82
STEEL	7	21,618.48	216,18.48	28,033.48	21,179.62
PETROLEUM	144	3,77,065.98	3,885,71.32	3,95,519.73	1,27,100.07
POWER	76	1,96,489.83	2,426,71.39	2,60,007.47	1,65,748.86
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,727.30	3,526.63
HEALTH AND FAMILY WELFARE	28	13,696.26	137,11.40	14,162.35	9,693.60
RAILWAYS	211	4,08,405.75	5,177,62.52	6,65,174.44	3,25,319.01
ROAD TRANSPORT AND HIGHWAYS	854	5,17,126.74	5,316,40.50	5,40,821.11	3,25,990.17
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	2,013.22
TELECOMMUNICATIONS	3	14,013.36	140,43.62	25,373.62	20,789.12
URBAN DEVELOPMENT	27	2,84,108.54	2,841,08.54	3,04,523.01	1,53,113.49
WATER RESOURCES	41	23,466.28	688,64.11	69,468.25	22,562.69
SOCIAL JUSTICE	1	170.99	1,70.99	170.99	0.00
DEFENCE PRODUCTION	1	246.31	2,10.00	200.00	168.90
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	23	10,455.86	104,24.24	10,390.34	4,422.70
HOME AFFAIRS	5	2,025.73	20,25.73	2,885.25	1,392.62
DPIIT	2	17,352.09	173,52.09	18,990.30	12,636.44
DONER	1	151.33	1,51.33	151.33	149.33
RENEWABLE ENERGY	1	271.90	2,71.90	365.00	282.96
Grand total	1565	21,86,542.05	24,27,353.93	26,59,914.61	13,26,569.75

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	65	1,11,390.87	1,63,336.49	46.63	6	38,791.57	93,280.63	14 - 216
2	ARUNACHAL PRADESH	43	23,906.60	37,842.94	58.29	4	6,882.14	20,760.58	59 - 155
3	ASSAM	45	47,656.00	56,342.77	18.23	6	5,442.47	8,230.33	12 - 61
4	BIHAR	85	1,17,311.78	1,53,928.66	31.21	16	29,963.29	52,030.33	24 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	56	1,06,855.31	1,21,047.93	13.28	13	29,980.78	44,166.71	12 - 139
7	HARYANA	35	60,694.21	62,645.55	3.22	3	1,091.05	1,421.66	20 - 29
8	HIMACHAL PRADESH	19	21,990.88	33,028.18	50.19	2	5,270.59	11,368.59	9 - 162
9	JAMMU AND KASHMIR	29	46,603.49	81,343.00	74.54	1	2,500.00	37,012.26	245 - 245
10	KARNATAKA	55	84,883.48	93,093.46	9.67	6	4,948.80	6,746.89	7 - 312
11	KERALA	21	29,984.85	35,049.87	16.89	3	2,843.17	4,043.24	44 - 62
12	MADHYA PRADESH	75	66,341.06	74,667.19	12.55	12	13,847.91	22,116.83	15 - 55
13	MAHARASHTRA	224	2,03,291.90	2,27,367.17	11.84	19	53,717.51	77,713.59	9 - 219
14	MANIPUR	26	12,108.58	22,615.20	86.77	1	4,454.17	14,322.00	153 - 153
15	MEGHALAYA	12	4,790.48	7,912.42	65.17	0	0.00	0.00	-
16	MIZORAM	24	11,957.35	16,911.60	41.43	1	2,393.47	6,527.00	117 - 117
17	NAGALAND	35	15,989.03	20,373.15	27.42	1	2,326.52	6,663.00	132 - 132
18	ODISHA	77	1,09,972.84	1,19,431.95	8.60	18	22,995.14	32,453.71	6 - 189
19	PUNJAB	24	17,419.37	18,661.82	7.13	1	754.54	756.27	36 - 36
20	RAJASTHAN	49	59,049.82	64,466.52	9.17	3	13,624.08	18,868.73	26 - 84
21	SIKKIM	18	7,278.84	14,598.73	100.56	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	58	1,96,061.35	2,16,066.26	10.20	8	11,137.58	21,497.46	33 - 145
23	TRIPURA	19	5,084.45	5,225.78	2.78	1	569.63	708.73	30 - 30
24	UTTAR PRADESH	103	1,39,667.42	1,48,121.08	6.05	15	27,442.43	31,065.74	6 - 73
25	WEST BENGAL	62	62,517.29	74,251.74	18.77	15	16,760.75	23,240.00	18 - 141
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	1	417.23	707.73	49 - 49
27	DELHI	27	82,096.45	85,824.51	4.54	4	6,466.89	7,685.33	5 - 34
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	44	75,822.81	85,814.67	13.18	8	25,599.32	35,109.59	18 - 85
30	JHARKHAND	38	68,059.63	74,961.76	10.14	4	15,428.62	18,325.52	13 - 62
31	UTTARAKHAND	29	35,446.38	53,598.18	51.21	7	25,075.74	42,265.85	3 - 144
32	TELANGANA	49	37,332.16	40,209.86	7.71	4	12,794.04	13,763.77	13 - 180
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	27 - 27
34	MULTI STATE	91	3,13,927.74	4,39,710.63	40.07	30	61,365.03	1,05,518.12	12 - 276
Total		1565	21,86,542.05	26,59,914.61	21.65	215	4,46,570.21	7,67,450.52	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	153	13
2	RAILWAYS	133	34
3	PETROLEUM	61	7
4	POWER	40	7
5	COAL	31	3
6	URBAN DEVELOPMENT	22	7
7	ATOMIC ENERGY	5	0
8	CIVIL AVIATION	5	3
9	STEEL	3	2
10	HEALTH AND FAMILY WELFARE	3	0
11	DPIIT	2	0
12	MINES	1	0
13	HEAVY INDUSTRY	1	0
14	SHIPPING AND PORTS	1	0
15	TELECOMMUNICATIONS	1	0
16	WATER RESOURCES	1	0
17	HOME AFFAIRS	1	1
	Total	464	77

FLASH REPORT

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	June,2021			
	<u>PETROLEUM</u>			
1	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	August,2021			
	<u>PETROLEUM</u>			
3	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
	<u>POWER</u>			
4	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
6	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
7	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
8	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
9	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
10	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
	September,2021			
	<u>POWER</u>			
12	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000061]	4,824.12	10/2012	4,612.66

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	EASTERN REGION STRENGTHENING SCHEME-V (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000155]	1,364.52	04/2016	1,290.03
14	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000168]	5,151.37	03/2018	3,269.93
15	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000218]	3,519.59	05/2019	2,562.41
16	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI Central Sector Projects (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000257]	3,654.00	04/2019	3,508.04
	RAILWAYS			
17	GONDIA-JABALPUR(GC),(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100186]	511.86	04/2020	1,867.16
18	NANDYAL-YERRAGUNTALA(NL),SCR (SOUTH CENTRAL RAILWAY) - [220100192]	164.36	02/2009	1,148.67
19	HARIDASPUR-PARADEEP(NL) (RAIL VIKAS NIGAM LTD.) - [220100285]	1,185.64	12/2017	2,129.37
20	CHHINDWARA - NAGPUR (GC)(SECR) (SOUTH EAST CENTRAL RAILWAY) - [220100324]	383.79	-	1,448.56
21	BARDHAMAN-KATWA (GC) (EASTERN RAILWAYS) - [N22000091]	1,106.62	12/2010	1,003.78
22	CHAMPA-JHARSUGUDA 3RD LINE (SOUTH EAST CENTRAL RAILWAY) - [N22000483]	872.00	12/2019	1,156.06
	ROAD TRANSPORT AND HIGHWAYS			
23	FOUR LANING OF AURANGABAD - YEDISHI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000508]	1,871.34	01/2018	3,443.43
24	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000541]	1,081.57	06/2019	480.25
25	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000545]	1,134.97	11/2018	809.71
26	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 ((NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000621]	1,239.82	-	1,691.00
	URBAN DEVELOPMENT			
27	REDEVELOPMENT OF EAST KIDWAI NAGAR (NATIONAL BUILDING CONSTRUCTION CORPORATION LTD) - [N28000080]	4,264.00	11/2019	4,683.08
	October,2021			
	PETROLEUM			
28	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000227]	4,588.29	08/2018	5,376.50

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
29	BS-VI PROJECTS (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000295]	1,858.00	12/2019	1,528.75
	December,2021			
	<u>STEEL</u>			
30	COKE OVEN BATTERY-5 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000117]	2,858.00	12/2017	2,018.72
	<u>PETROLEUM</u>			
31	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000365]	1,524.06	12/2021	1,037.45
	January,2022			
	<u>STEEL</u>			
32	FORGED WHEEL PLANT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000116]	1,682.85	09/2018	1,767.98
	<u>PETROLEUM</u>			
33	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000297]	4,006.83	05/2021	3,526.55
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
34	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000349]	1,387.11	11/2017	980.46
35	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000623]	1,100.19	-	1,355.00
36	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000840]	1,158.35	-	496.04
	February,2022			
	<u>POWER</u>			
37	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000219]	14,733.37	11/2019	11,823.97
38	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000247]	5,070.13	04/2020	4,236.67
	<u>RAILWAYS</u>			

Month wise List of Completed Projects Costing Rs. 1000 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
39	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR (NORTH EAST FRONTIER RAILWAY) - [220100266]	1,180.19	12/2008	3,983.32
40	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) (METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100268]	1,049.69	12/2006	3,837.57
41	AHMEDABAD-BOTAD (GC) (RAIL VIKAS NIGAM LTD.) - [N22000140]	975.62	12/2021	1,755.44
42	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF (SOUTHERN RAILWAY) - [N22000202]	931.98	-	1,005.24
43	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) (NORTH EAST FRONTIER RAILWAY) - [N22000390]	602.27	12/2021	1,135.28
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
44	FOUR LANING OF GWALIOR-SHIVPURI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000494]	1,055.00	11/2015	1,393.40
45	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000509]	1,170.52	06/2012	2,051.36
46	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000624]	1,244.10	-	1,665.00
47	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000794]	1,103.88	-	720.73
	<u>URBAN DEVELOPMENT</u>			
48	LUCKNOW METRO RAIL CORPORATION LTD (LUCKNOW METRO RAIL CORPORATION LIMITED) - [N28000094]	6,928.00	03/2019	6,928.00

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2022			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
	August,2022			
2	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
3	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
4	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
5	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
6	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
	September,2022			
7	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000439]	1,885.74	05/2019	1,636.02
	February,2022			
	<u>COAL</u>			
8	MAGADH EXPANSION OC(51 MTY) (CENTRAL COAL FIELDS LIMITED) - [N06000015]	6,964.33	07/2012	815.07
9	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY (EASTERN COAL FIELDS LIMITED) - [N06000020]	1,210.12	03/2029	91.96
10	BHUBANESWARI EXPENSION OCP(40.0 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000034]	3,145.45	03/2017	715.56
11	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000035]	8,416.19	03/2013	1,204.92
12	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000044]	3,504.21	03/2010	595.58
13	BATURA OCP (2.0 MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000049]	1,186.64	03/2023	261.21
14	RECAST EPR AMRAPALI OC (CENTRAL COAL FIELDS LIMITED) - [N06000103]	4,983.58	03/2020	371.36
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) (EASTERN COAL FIELDS LIMITED) - [N06000109]	1,055.05	03/2018	711.21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
16	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) (WESTERN COAL FIELDS LIMITED) - [N06000118]	1,184.33	03/2020	436.49
	<u>RAILWAYS</u>			
17	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) (SOUTHERN RAILWAY) - [N22000445]	1,567.00	03/2024	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
18	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000133]	2,288.00	11/2011	3,450.00

FLASH REPORT

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	475
No of Projects Completed/Dropped/Frozen in Current Month	34
No of Projects Elevated in Current Month	8
No of Projects added in Current Month	15
No of Projects in Current Month	464

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	219 (47.20%)	6 (1.29%)	76 (16.38%)	41 (8.84%)	122 (26.29%)	464
Latest Approved (Date)	180 (38.79%)	6 (1.29%)	128 (27.59%)	25 (5.39%)	125 (26.94%)	464

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	385	14,98,942.30	17,13,847.98	7,55,072.38	44.10	2,14,905.68	14.30
Project with Revision in Cost	79	4,65,214.34	4,76,157.55	3,36,653.07	70.70	10,943.21	2.40
Total	464	19,64,156.64	21,90,005.53	10,91,725.45	49.85	2,25,848.89	11.50
Original Cost of All Projects							
Original Cost	464	17,29,105.56	21,90,005.53	10,91,725.45	49.85	4,60,899.97	26.66

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	219	7,54,302.21	10,58,507.99	6,40,782.90	60.50	3,04,205.78	40.33
Latest Approved (RCE)	180	6,91,560.89	8,41,697.07	5,04,032.17	59.90	1,50,136.18	21.71

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	77	1,99,013.64	2,82,802.77	1,82,979.22	64.70	83,789.13	42.10
Total	77	1,99,013.64	2,82,802.77	1,82,979.22	64.70	83,789.13	42.10

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	3	27,271.00	43,139.00	58.19
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	2	2,525.00	3,170.00	25.54
3	COAL	31	1,19,969.98	1,24,529.21	3.80	3	25,805.84	30,365.07	17.67
4	MINES	1	5,540.00	6,435.90	16.17	1	5,540.00	6,435.90	16.17
5	STEEL	3	19,466.01	25,881.01	32.95	1	15,525.00	21,940.00	41.32
6	PETROLEUM	61	3,43,306.92	3,60,852.13	5.11	15	61,689.32	85,050.89	37.87
7	POWER	40	1,81,268.77	2,44,130.41	34.68	20	1,05,541.13	1,69,920.82	61.00
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	8.88
10	RAILWAYS	133	3,68,711.79	6,19,585.95	68.04	103	1,91,092.72	4,43,235.85	131.95
11	ROAD TRANSPORT AND HIGHWAYS	153	2,30,528.43	2,50,828.70	8.81	65	84,530.98	1,06,917.01	26.48
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	7	1,14,321.56	1,34,795.56	17.91
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		464	17,29,105.56	21,90,005.53	26.66	227	6,78,967.89	11,51,371.57	69.58

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.						1000	Crore and above		
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	18	93,351.27	1,45,410.95	55.77	9	44,306.33	99,338.01	124.21
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	2	8,264.33	22,029.33	166.56
3	ASSAM	8	33,271.03	41,273.55	24.05	5	16,996.48	26,169.00	53.97
4	BIHAR	29	92,631.95	1,27,150.67	37.26	17	49,026.30	84,180.52	71.70
5	GUJARAT	24	88,350.27	1,01,898.74	15.34	10	31,232.80	45,440.32	45.49
6	HARYANA	13	51,014.43	51,953.20	1.84	8	9,730.19	10,668.96	9.65
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	5	9,650.78	20,714.91	114.64
8	JAMMU AND KASHMIR	14	40,458.66	75,198.17	85.86	2	4,659.00	39,531.26	748.49
9	KARNATAKA	20	70,306.27	78,049.02	11.01	12	17,587.60	25,330.35	44.02
10	KERALA	9	24,577.63	28,831.32	17.31	7	12,015.73	16,269.42	35.40
11	MADHYA PRADESH	18	38,074.61	45,700.16	20.03	8	12,194.36	20,336.96	66.77
12	MAHARASHTRA	44	1,28,464.70	1,55,791.16	21.27	22	65,999.78	93,533.59	41.72
13	MANIPUR	2	5,032.79	15,633.05	210.62	2	5,032.79	15,633.05	210.62
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	172.70
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	186.39
17	ODISHA	35	90,420.70	98,645.80	9.10	11	19,958.29	28,183.39	41.21
18	PUNJAB	7	8,647.82	9,958.16	15.15	2	2,557.95	3,868.29	51.23
19	RAJASTHAN	17	44,583.36	49,576.83	11.20	2	13,284.17	18,277.64	37.59
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	26	1,78,878.21	1,99,255.47	11.39	13	39,220.75	59,993.01	52.96
22	UTTAR PRADESH	43	1,11,549.03	1,19,671.42	7.28	19	40,496.65	49,614.18	22.51
23	WEST BENGAL	19	47,030.89	58,432.61	24.24	10	23,280.95	34,698.67	49.04
24	DELHI	8	75,922.38	78,624.88	3.56	3	44,577.21	47,358.91	6.24
25	CHHATISGARH	16	62,856.61	72,615.96	15.53	7	25,757.63	35,619.00	38.29
26	JHARKHAND	13	58,767.88	65,556.00	11.55	5	20,920.79	28,709.91	37.23
27	UTTARAKHAND	9	28,781.19	46,559.53	61.77	7	25,870.41	43,648.75	68.72
28	TELANGANA	6	19,991.02	22,312.66	11.61	4	14,138.06	16,827.58	19.02
29	MULTI STATE	48	2,96,199.06	4,18,226.20	41.20	31	1,15,242.63	2,39,523.54	107.84
Total		464	17,29,105.56	21,90,005.53	26.66	227	6,78,967.89	11,51,371.57	69.58

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	4	67,120.00	82,988.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	5	7,613.90	8,258.90	12 - 48
3	COAL	31	1,19,969.98	1,24,529.21	3.80	6	25,542.64	28,028.19	12 - 61
4	MINES	1	5,540.00	6,435.90	16.17	1	5,540.00	6,435.90	33 - 33
5	STEEL	3	19,466.01	25,881.01	32.95	3	19,466.01	25,881.01	12 - 85
6	PETROLEUM	61	3,43,306.92	3,60,852.13	5.11	34	1,34,557.43	1,46,372.12	2 - 146
7	POWER	40	1,81,268.77	2,44,130.41	34.68	26	1,34,558.34	1,88,354.45	6 - 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	133	3,68,711.79	6,19,585.95	68.04	95	1,61,187.25	2,98,804.77	3 - 312
11	ROAD TRANSPORT AND HIGHWAYS	153	2,30,528.43	2,50,828.70	8.81	28	39,247.63	42,459.21	14 - 109
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	12	1,28,640.76	1,42,063.57	3 - 49
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	32 - 32
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
Total		464	17,29,105.56	21,90,005.53	26.66	219	7,54,302.21	10,58,507.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,351.27	1,45,410.95	55.77	8	75,303.28	1,26,820.34	14 - 216
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,273.55	24.05	4	4,630.48	7,201.00	12 - 60
4	BIHAR	29	92,631.95	1,27,150.67	37.26	12	32,000.92	53,209.12	17 - 141
5	GUJARAT	24	88,350.27	1,01,898.74	15.34	9	40,395.92	54,149.83	3 - 84
6	HARYANA	13	51,014.43	51,953.20	1.84	3	5,172.94	5,172.94	7 - 25
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	14	40,458.66	75,198.17	85.86	3	11,712.82	46,225.08	63 - 245
9	KARNATAKA	20	70,306.27	78,049.02	11.01	7	36,238.01	37,579.29	27 - 312
10	KERALA	9	24,577.63	28,831.32	17.31	3	2,843.17	4,043.24	44 - 62
11	MADHYA PRADESH	18	38,074.61	45,700.16	20.03	14	32,826.03	40,451.58	12 - 55
12	MAHARASHTRA	44	1,28,464.70	1,55,791.16	21.27	23	77,833.77	1,00,956.18	5 - 219
13	MANIPUR	2	5,032.79	15,633.05	210.62	1	4,454.17	14,322.00	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	117 - 117
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	132 - 132
17	ODISHA	35	90,420.70	98,645.80	9.10	21	42,778.25	51,003.35	8 - 189
18	PUNJAB	7	8,647.82	9,958.16	15.15	1	1,069.59	1,069.59	38 - 38
19	RAJASTHAN	17	44,583.36	49,576.83	11.20	5	19,952.49	24,711.49	6 - 84
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	26	1,78,878.21	1,99,255.47	11.39	13	59,590.13	69,242.75	2 - 145
22	UTTAR PRADESH	43	1,11,549.03	1,19,671.42	7.28	18	73,237.66	75,836.89	5 - 103
23	WEST BENGAL	19	47,030.89	58,432.61	24.24	9	23,045.43	29,045.88	5 - 141
24	DELHI	8	75,922.38	78,624.88	3.56	5	9,694.73	10,801.32	27 - 58
25	CHHATISGARH	16	62,856.61	72,615.96	15.53	7	28,310.02	37,468.43	12 - 85
26	JHARKHAND	13	58,767.88	65,556.00	11.55	5	37,023.06	38,662.48	23 - 61
27	UTTARAKHAND	9	28,781.19	46,559.53	61.77	7	25,811.19	42,701.74	3 - 144
28	TELANGANA	6	19,991.02	22,312.66	11.61	3	13,183.42	13,427.82	27 - 180
29	MULTI STATE	48	2,96,199.06	4,18,226.20	41.20	32	79,579.34	1,21,254.63	7 - 276
Total		464	17,29,105.56	21,90,005.53	26.66	219	7,54,302.21	10,58,507.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	4	79,640.00	82,988.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	1	1,383.00	1,938.00	27 - 27
3	COAL	31	1,19,970.10	1,24,529.21	3.80	6	25,542.64	28,028.19	12 - 61
4	MINES	1	6,435.90	6,435.90	0.00	0	0.00	0.00	-
5	STEEL	3	19,466.01	25,881.01	32.95	3	19,466.01	25,881.01	12 - 85
6	PETROLEUM	61	3,54,068.25	3,60,852.13	1.92	23	78,793.88	84,055.76	2 - 146
7	POWER	40	2,27,346.21	2,44,130.41	7.38	19	1,16,132.22	1,23,736.73	0 - 141
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	133	4,76,928.59	6,19,585.95	29.91	88	1,51,123.00	2,48,708.05	3 - 312
11	ROAD TRANSPORT AND HIGHWAYS	153	2,41,710.09	2,50,828.70	3.77	23	31,363.50	32,106.89	0 - 109
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	8	1,11,890.56	1,25,392.57	3 - 49
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	32 - 32
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
Total		464	19,64,156.64	21,90,005.53	11.50	180	6,91,560.89	8,41,697.07	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	2	2,525.00	3,170.00	25.54
3	COAL	31	1,19,970.10	1,24,529.21	3.80	3	25,805.84	30,365.07	17.67
4	MINES	1	6,435.90	6,435.90	0.00	0	0.00	0.00	0.00
5	STEEL	3	19,466.01	25,881.01	32.95	1	15,525.00	21,940.00	41.32
6	PETROLEUM	61	3,54,068.25	3,60,852.13	1.92	5	37,761.00	51,283.24	35.81
7	POWER	40	2,27,346.21	2,44,130.41	7.38	13	54,268.71	74,679.96	37.61
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	8.88
10	RAILWAYS	133	4,76,928.59	6,19,585.95	29.91	95	2,16,523.79	3,82,134.12	76.49
11	ROAD TRANSPORT AND HIGHWAYS	153	2,41,710.09	2,50,828.70	3.77	47	63,721.75	77,876.58	22.21
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	7	1,14,321.56	1,34,795.56	17.91
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		464	19,64,156.64	21,90,005.53	11.50	180	5,68,918.95	8,33,937.13	46.58

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,29,261.00	1,32,609.00	2.59	1	3,492.00	6,840.00	145- 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	1	1,383.00	1,938.00	27- 27
3	COAL	31	1,19,970.10	1,24,529.21	3.80	2	19,898.73	22,384.28	19- 60
4	MINES	1	6,435.90	6,435.90	0.00	0	0.00	0.00	0- 0
5	STEEL	3	19,466.01	25,881.01	32.95	1	15,525.00	21,940.00	85- 85
6	PETROLEUM	61	3,54,068.25	3,60,852.13	1.92	4	25,395.00	32,315.24	13- 66
7	POWER	40	2,27,346.21	2,44,130.41	7.38	8	30,657.10	41,888.66	13- 88
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	133	4,76,928.59	6,19,585.95	29.91	67	1,11,709.29	2,10,414.30	3- 312
11	ROAD TRANSPORT AND HIGHWAYS	153	2,41,710.09	2,50,828.70	3.77	7	10,743.80	11,922.94	14- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80- 80
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	3	42,589.00	56,091.01	36- 47
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	32- 32
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
Total		464	19,64,156.64	21,90,005.53	11.50	98	2,82,070.13	4,39,047.43	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	5	1,16,741.00	1,32,609.00	13.59	3	27,271.00	43,139.00	84- 145
2	CIVIL AVIATION	5	7,613.90	8,258.90	8.47	2	2,525.00	3,170.00	27- 48
3	COAL	31	1,19,969.98	1,24,529.21	3.80	2	19,898.73	22,384.28	19- 60
4	MINES	1	5,540.00	6,435.90	16.17	1	5,540.00	6,435.90	33- 33
5	STEEL	3	19,466.01	25,881.01	32.95	1	15,525.00	21,940.00	85- 85
6	PETROLEUM	61	3,43,306.92	3,60,852.13	5.11	13	48,500.05	64,945.10	12- 146
7	POWER	40	1,81,268.77	2,44,130.41	34.68	16	84,241.36	1,39,555.52	13- 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	3	4,583.00	4,703.00	2.62	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	133	3,68,711.79	6,19,585.95	68.04	75	1,21,758.66	2,60,496.14	3- 312
11	ROAD TRANSPORT AND HIGHWAYS	153	2,30,528.43	2,50,828.70	8.81	9	11,135.64	14,715.10	14- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80- 80
14	URBAN DEVELOPMENT	22	2,82,232.24	3,02,627.04	7.23	3	42,589.00	56,091.01	36- 47
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	32- 32
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
Total		464	17,29,105.56	21,90,005.53	26.66	130	4,09,812.69	7,21,733.92	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

List of projects completed/dropped/Frozen during current month							
Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	MAGADH EXPANSION OC(51 MTY)	08/2008	6,964.33	07/2012	7,254.37	03/2028	815.07
2	EXPANSION PR OF JHANJRA UG(5.00 MTY) OLD (3.50) MTY	11/2015	1,210.12	03/2029	1,210.12	03/2029	91.96
3	BATURA OCP (2.0 MTY)	08/2015	1,186.64	03/2023	1,248.93	03/2026	261.21
4	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) OLD (40 MTY)	12/2007	8,416.19	03/2013	8,416.19	03/2028	1,204.92
5	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3,145.45	03/2017	3,145.45	03/2031	715.56
6	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	1,184.33	03/2020	1,184.33	03/2027	436.49
7	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	08/2012	1,055.05	03/2018	1,055.05	03/2029	711.21
8	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) OLD (8 MTY)	12/2007	3,504.21	03/2010	3,504.21	03/2029	595.58
9	RECAST EPR AMRAPALI OC	02/2012	4,983.58	03/2020	4,983.58	03/2028	371.36
	<u>POWER</u>						
10	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	05/2016	14,733.37	11/2019	14,733.37	10/2021	11,823.97
11	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	02/2017	5,070.13	04/2020	5,070.13	06/2021	4,236.67
	<u>RAILWAYS</u>						
12	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1,049.69	12/2006	3,404.92	N.A.	3,837.57
13	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	05/2015	873.71	N.A.	2,215.27	N.A.	4.60
14	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	03/2007	1,026.00	N.A.	182.57
15	AHMEDABAD-BOTAD (GC)	04/2012	975.62	12/2021	1,555.42	10/2021	1,755.44
16	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	04/2010	651.00	03/2015	1,009.00	03/2025	7.96
17	CHENNAI-CUDDALORE VIA MAMALLAPURAM	04/2008	523.52	N.A.	1,205.00	03/2030	2.28
18	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	04/1999	819.23	N.A.	1,090.60	N.A.	1,089.12

List of projects completed/dropped/Frozen during current month							
Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Project	DOA	Original		Now anticipated		Final Expenditure
			Cost	DOC	Cost	DOC	
19	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	04/2007	450.00	N.A.	1,261.34	03/2025	0.00
20	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	02/1999	380.60	04/2010	1,090.60	N.A.	1,089.12
21	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	02/2017	1,567.00	03/2024	1,567.00	03/2026	0.00
22	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	1,027.40	03/2003	2,373.00	03/2030	485.04
23	NEW MAYNAGURI-GUMANIHAT- DOUBLING OF REMAINING PORTION (51.65 KM)	04/2016	602.27	12/2021	1,167.00	10/2021	1,135.28
24	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	04/2007	931.98	N.A.	1,122.00	12/2022	1,005.24
25	MOTIHARI-SITAMARHI (NL)	04/2006	211.00	N.A.	1,006.00	N.A.	4.99
26	RATLAM-DUNGARPUR VIA BANSWARA (NL)	04/2011	2,082.75	N.A.	4,262.36	N.A.	191.39
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	04/2000	1,180.19	12/2008	4,541.38	12/2021	3,983.32
28	DEOGHAR - SULTANGANJ (INL), ER	04/2000	607.09	02/2013	1,425.44	03/2024	638.87
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
29	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) PPP (BOT)	05/2009	2,288.00	11/2011	2,288.00	N.A.	3,450.00
30	FOUR LANING OF GWALIOR-SHIVPURI PPP (BOT)	05/2013	1,055.00	11/2015	1,601.77	N.A.	1,393.40
31	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	04/2010	1,170.52	06/2012	1,170.52	03/2019	2,051.36
32	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	02/2018	1,103.88	N.A.	1,103.88	N.A.	720.73
33	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	09/2016	1,244.10	N.A.	1,244.10	N.A.	1,665.00
	<u>URBAN DEVELOPMENT</u>						
34	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	6,928.00	03/2019	6,928.00	N.A.	6,928.00

TABLE-32

List of projects added Rs. 1000 Crore and above					(February 2022)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	REVISED PROJECT REPORT MAGADH EXPANSION OCP	8/2020	7,254.37	3/2028	7,254.37	3/2028
2	EXPANSION PROJECT AMRAPALI OCP	8/2020	5,136.15	3/2028	5,136.15	3/2028
3	SONEPUR BAZARI EXPANSION OC	7/2021	5,365.88	3/2029	5,365.88	3/2029
4	BHUBANESWARI EXPANSION OCP	8/2020	3,145.45	3/2031	3,145.45	3/2031
5	GOPALJI-KANIHA OCP	8/2020	8,416.19	3/2028	8,416.19	3/2028
6	EXPANSION PR OF JHANJRA UG (5.00 MTY)	4/2020	1,210.12	3/2029	1,210.12	3/2029
7	DINESH (MAKARDHOKDA-III) OC (8.0 MTY)	2/2020	1,184.33	3/2027	1,184.33	3/2027
8	BALARAM EXPANSION OCP	8/2020	3,504.21	3/2029	3,504.21	3/2029
9	RAMPUR BATURA OC (4.0 MTY)	7/2019	1,248.93	3/2026	1,248.93	3/2026
	<u>POWER</u>					
10	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2021	1,184.88	9/2022	1,184.88	9/2022
11	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	10/2019	1,031.00	8/2021	1,031.00	8/2021
12	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	1,340.81	12/2022	1,340.81	12/2022
13	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	1,562.00	12/2022	1,562.00	12/2022
14	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	1,006.00	12/2022	1,006.00	12/2022
15	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN	8/2019	2,578.47	12/2020	2,578.47	2/2022

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2747	
Achieved up to month	1676	

FLASH REPORT

TABLE-34

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above							(February 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II AAI	1,216.90	1,216.90	10/2022	12/2023	03/2024	3
2	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT AAI	1,405.00	1,405.00	08/2022	03/2023	08/2023	5
3	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI AAI	2,467.00	2,467.00	02/2022	06/2024	12/2024	6
	<u>COAL</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	11/2022	06/2023	7
5	JAYANT EXPANSION OCP 10 TO 20 MTPA NCL Central Sector Projects	1,783.09	1,783.09	03/2021	03/2022	03/2023	12
6	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	03/2019	02/2023	04/2024	14
	<u>STEEL</u>						
7	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	21,940.00	05/2015	03/2022	06/2022	3
8	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 NMDC Central Sector Projects	2,907.00	2,907.00	06/2023	06/2023	06/2024	12
	<u>PETROLEUM</u>						
9	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	02/2022	03/2022	1
10	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	01/2024	02/2024	1
11	DOBHI-DURGAPUR PIPELINE PROJECT GAIL	2,433.00	2,433.00	12/2020	03/2022	06/2022	3
12	DHAMRA-ANGUL PIPELINE PROJECT GAIL	1,933.00	1,933.00	12/2020	03/2022	07/2022	4
13	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT IOCL	1,636.00	1,636.00	08/2020	04/2022	09/2022	5
14	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	5,909.00	12/2012	08/2024	02/2025	6
15	HEERA REDEVELOPMENT - PHASE III ONGC	2,494.68	2,354.72	03/2022	03/2022	03/2023	12

List of projects reporting additional delayed Rs. 1000 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>POWER</u>						
16	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	1,885.13	2,426.00	12/2018	02/2022	03/2022	1
17	EASTERN REGION STRENGTHENING SCHEME- XVIII PGCIL Central Sector Projects	3,500.00	3,994.00	07/2020	02/2022	04/2022	2
18	TAPOVAN-VISHNUGAD HEP (4X130MW) NTPC	2,978.48	5,867.38	03/2013	09/2024	12/2024	3
19	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,998.00	11/2020	10/2022	02/2023	4
20	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCIL	2,491.58	3,860.35	06/2013	12/2024	06/2025	6
21	RAMMAM-III HEPP (3X40 MW) NTPC	1,381.84	1,803.00	09/2019	12/2024	07/2025	7
22	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES PGCIL	5,111.33	6,700.00	12/2018	03/2022	01/2024	22
	<u>RAILWAYS</u>						
23	KIUL - GAYA DOUBLING PROJECT ECR	1,200.20	1,200.20	03/2020	03/2023	05/2023	2
24	HOSPET-HUBLI-LONDA-VASCODAGAMA DL RVNL	2,127.00	3,300.00	03/2023	12/2022	03/2023	3
25	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) RVNL	1,503.71	3,633.12	03/2020	03/2022	06/2022	3
26	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) RVNL	713.48	2,725.00	03/2020	12/2021	03/2022	3
27	RAIPUR - TITLAGARH - DOUBLING RVNL	1,402.02	1,300.00	03/2020	03/2022	06/2022	3
28	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT SECR	585.93	1,268.32	02/2019	12/2021	03/2022	3
29	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	37,012.26	11/2002	12/2022	04/2023	4
30	KODERMA-RANCHI VIA BARKAKANA (NL),ECR ECR	1,033.07	3,650.00	N.A.	03/2022	07/2022	4
31	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. RVNL	2,913.51	4,834.54	03/2016	03/2025	07/2025	4
32	SAMBALPUR - TITLAGARH - DOUBLING RVNL	948.04	2,009.00	03/2020	12/2021	04/2022	4
33	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING RVNL	760.00	1,536.00	03/2020	06/2022	12/2022	6

List of projects reporting additional delayed Rs. 1000 Crore and above							(February 2022)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	324.73	1,090.00	03/2012	11/2022	06/2023	7
35	PALANPUR-SAMAKHAYALI (DL) RVNL	1,548.66	2,538.01	12/2021	03/2022	12/2022	9
36	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	927.01	1,457.79	03/2019	06/2022	03/2023	9
37	BANASPANI- JAKHPURA - DOUBLING RVNL	942.95	1,552.26	03/2019	06/2022	03/2023	9
38	BINA - KOTA DOUBLING WITH RE RVNL	1,485.85	1,835.83	12/2020	12/2021	09/2022	9
39	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM ECR	744.04	1,215.54	03/2021	03/2024	12/2024	9
40	MANIYACHI - NAGERCOIL (102 KM) DOUBLING RVNL	1,700.00	1,305.00	03/2022	06/2022	05/2023	11
41	KODERMA-TILAIYA (NL), ECR	459.91	1,625.87	N.A.	03/2023	03/2024	12
42	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	385.20	1,145.79	03/2019	03/2023	03/2024	12
43	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) RVNL	3,951.98	4,259.48	03/2016	03/2025	03/2026	12
44	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) ECR	372.14	1,470.50	N.A.	03/2023	03/2024	12
45	KIRANDUL - JAGDALPUR DOUBLING ECR	1,160.00	1,160.83	03/2020	03/2023	03/2024	12
46	GUNTUR-GUNTAKAL SCR	3,631.00	3,887.48	03/2022	03/2024	03/2025	12
47	JAGDALPUR-KORAPUT DOUBLING ECR	1,547.38	1,547.38	03/2022	03/2023	03/2024	12
48	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	528.65	2,066.78	N.A.	03/2023	12/2024	21
49	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) WR	320.66	1,378.11	03/2019	03/2023	03/2025	24
50	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, ECR	329.39	1,483.14	N.A.	03/2022	03/2024	24
51	ARARIA-SUPAUL (NL) ECR	1,605.17	1,605.17	N.A.	03/2023	12/2025	33
52	KOTLPALLI-NARASAPUR (NL) (SCR) SCR	1,045.20	2,120.16	03/2009	03/2024	03/2027	36
53	RATLAM-MHOW-KHANDWA-AKOLA (GC) WR	3,503.69	6,383.82	03/2022	03/2023	03/2026	36
54	HUBLI-ANKOLA(NL),SWR	2,315.00	5,174.30	N.A.	12/2024	03/2028	39

List of projects reporting additional delayed Rs. 1000 Crore and above							(February 2022)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
55	BANGLORE - SATYAMANGALAM (NL)(SWR) SWR	1,382.78	1,383.00	03/2002	03/2024	03/2028	48
56	CHOTTAUDEPUR-DHAR(NL) WR	1,347.26	1,524.68	03/2022	03/2023	10/2027	55
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
57	PUNE-SATARA(NH-4) NHAI PPP (BOT)	1,724.55	1,724.55	03/2013	03/2022	04/2022	1
58	4-LANING OF FARAKA-RAIGANJ NHAI PPP (BOT)	1,078.84	1,078.84	08/2013	02/2022	03/2022	1
59	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	02/2022	03/2022	1
60	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	1,928.22	04/2015	12/2021	03/2022	3
61	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 NHAI	1,737.00	2,421.37	N.A.	09/2021	12/2021	3
62	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	01/2022	05/2022	4
63	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) NHAI	1,071.61	1,048.10	N.A.	12/2021	05/2022	5
64	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) NHAI	1,532.62	1,827.00	03/2021	07/2021	05/2022	10
65	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL NHAI	870.00	1,418.78	03/2019	11/2020	10/2021	11
66	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 MoRTH	1,069.59	1,069.59	10/2019	08/2021	12/2022	16
67	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 NHAI Central Sector Projects	950.64	1,168.00	08/2017	02/2022	10/2023	20
68	SRINAGAR TO BANIHAL NHAI PPP (ANNUITY)	1,100.70	1,100.70	06/2014	10/2020	09/2022	23
69	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHAI PPP (BOT)	1,655.01	1,655.01	08/2016	12/2020	03/2023	27
<u>URBAN DEVELOPMENT</u>							
70	NAGPUR METRO RAIL NMRCL	8,680.00	9,759.79	03/2018	12/2021	02/2022	2
71	SURAT METRO RAIL PROJECT MEGA	12,020.32	12,020.32	03/2024	03/2024	06/2024	3
72	AGRA METRO RAIL PROJECT LMRCL Public Private (SPV)	8,379.62	8,379.62	03/2024	05/2025	12/2025	7

List of projects reporting additional delayed Rs. 1000 Crore and above (February 2022)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
73	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I CPWD	1,180.00	1,100.80	07/2021	06/2023	06/2024	12
74	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I CPWD	1,128.00	1,128.00	03/2022	06/2023	06/2024	12
75	BHOPAL METRO RAIL MPMRCL	6,941.40	6,941.40	02/2023	02/2023	05/2025	27
76	INDORE METRO RAIL MPMRCL	7,500.80	7,500.80	02/2023	02/2023	07/2025	29
	<u>HOME AFFAIRS</u>						
77	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI CPWD FOR MHA	1,219.21	2,000.00	10/2019	05/2022	06/2022	1

FLASH REPORT

TABLE-35

<u>Sector wise analysis of projects</u> Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	5	1,16,741.00	1,292,61.00	1,32,609.00	73,812.20
CIVIL AVIATION	5	7,613.90	76,13.90	8,258.90	2,533.09
COAL	31	1,19,969.98	1,199,70.10	1,24,529.21	40,488.96
MINES	1	5,540.00	64,35.90	6,435.90	1,268.54
STEEL	3	19,466.01	194,66.01	25,881.01	20,820.09
PETROLEUM	61	3,43,306.92	3,540,68.25	3,60,852.13	1,10,566.79
POWER	40	1,81,268.77	2,273,46.21	2,44,130.41	1,59,697.33
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,727.30	3,526.63
HEALTH AND FAMILY WELFARE	3	4,583.00	45,83.00	4,703.00	1,761.43
RAILWAYS	133	3,68,711.79	4,769,28.59	6,19,585.95	3,01,527.15
ROAD TRANSPORT AND HIGHWAYS	153	2,30,528.43	2,417,10.09	2,50,828.70	1,68,960.92
SHIPPING AND PORTS	1	5,369.18	53,69.18	4,633.81	2,013.22
TELECOMMUNICATIONS	1	13,334.00	133,34.00	24,664.00	20,545.00
URBAN DEVELOPMENT	22	2,82,232.24	2,822,32.24	3,02,627.04	1,52,056.28
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	18,422.33
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	1,089.05
DPIIT	2	17,352.09	173,52.09	18,990.30	12,636.44
Grand total	464	17,29,105.56	19,64,156.64	21,90,005.53	10,91,725.45


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	93,351.27	1,45,410.95	55.77	6	38,791.57	93,280.63	14 - 216
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	41,273.55	24.05	4	4,630.48	7,201.00	12 - 60
4	BIHAR	29	92,631.95	1,27,150.67	37.26	8	26,350.34	47,558.54	36 - 141
5	GUJARAT	24	88,350.27	1,01,898.74	15.34	7	26,970.60	40,724.51	12 - 84
6	HARYANA	13	51,014.43	51,953.20	1.84	0	0.00	0.00	-
7	HIMACHAL PRADESH	10	18,720.95	29,785.08	59.10	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	14	40,458.66	75,198.17	85.86	1	2,500.00	37,012.26	245 - 245
9	KARNATAKA	20	70,306.27	78,049.02	11.01	3	3,526.02	4,867.30	33 - 312
10	KERALA	9	24,577.63	28,831.32	17.31	3	2,843.17	4,043.24	44 - 62
11	MADHYA PRADESH	18	38,074.61	45,700.16	20.03	8	12,194.36	20,336.96	15 - 55
12	MAHARASHTRA	44	1,28,464.70	1,55,791.16	21.27	13	50,441.00	73,703.37	9 - 219
13	MANIPUR	2	5,032.79	15,633.05	210.62	1	4,454.17	14,322.00	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	6,527.00	172.70	1	2,393.47	6,527.00	117 - 117
16	NAGALAND	2	6,600.52	10,937.00	65.70	1	2,326.52	6,663.00	132 - 132
17	ODISHA	35	90,420.70	98,645.80	9.10	11	19,958.29	28,183.39	24 - 189
18	PUNJAB	7	8,647.82	9,958.16	15.15	0	0.00	0.00	-
19	RAJASTHAN	17	44,583.36	49,576.83	11.20	1	12,320.00	17,079.00	84 - 84
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	26	1,78,878.21	1,99,255.47	11.39	6	10,455.67	20,503.29	33 - 145
22	UTTAR PRADESH	43	1,11,549.03	1,19,671.42	7.28	7	24,295.00	27,517.17	9 - 48
23	WEST BENGAL	19	47,030.89	58,432.61	24.24	6	14,396.39	20,396.84	60 - 141
24	DELHI	8	75,922.38	78,624.88	3.56	2	5,992.21	7,178.00	29 - 32
25	CHHATISGARH	16	62,856.61	72,615.96	15.53	5	24,001.00	33,261.43	18 - 85
26	JHARKHAND	13	58,767.88	65,556.00	11.55	1	14,366.58	17,007.00	55 - 55
27	UTTARAKHAND	9	28,781.19	46,559.53	61.77	6	24,427.41	41,317.96	3 - 144
28	TELANGANA	6	19,991.02	22,312.66	11.61	2	11,759.46	12,371.74	27 - 180
29	MULTI STATE	48	2,96,199.06	4,18,226.20	41.20	23	57,523.58	1,00,717.27	12 - 276
Total		464	17,29,105.56	21,90,005.53	26.66	130	4,09,812.69	7,21,733.92	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

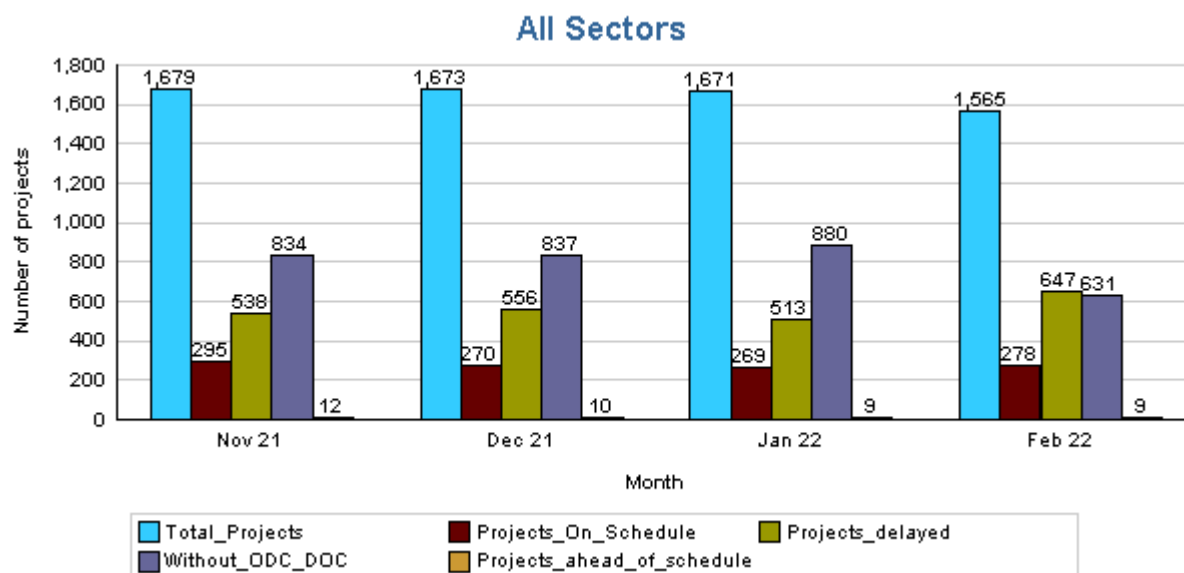

Break-up of 647 Delayed projects in February 2022

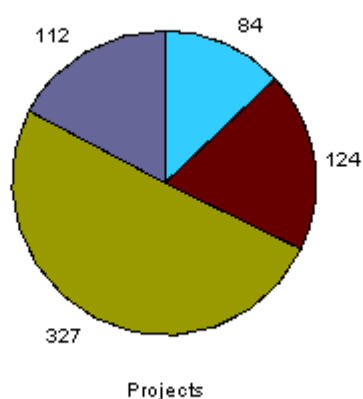


Delay in Months

Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of DPIIT Sector

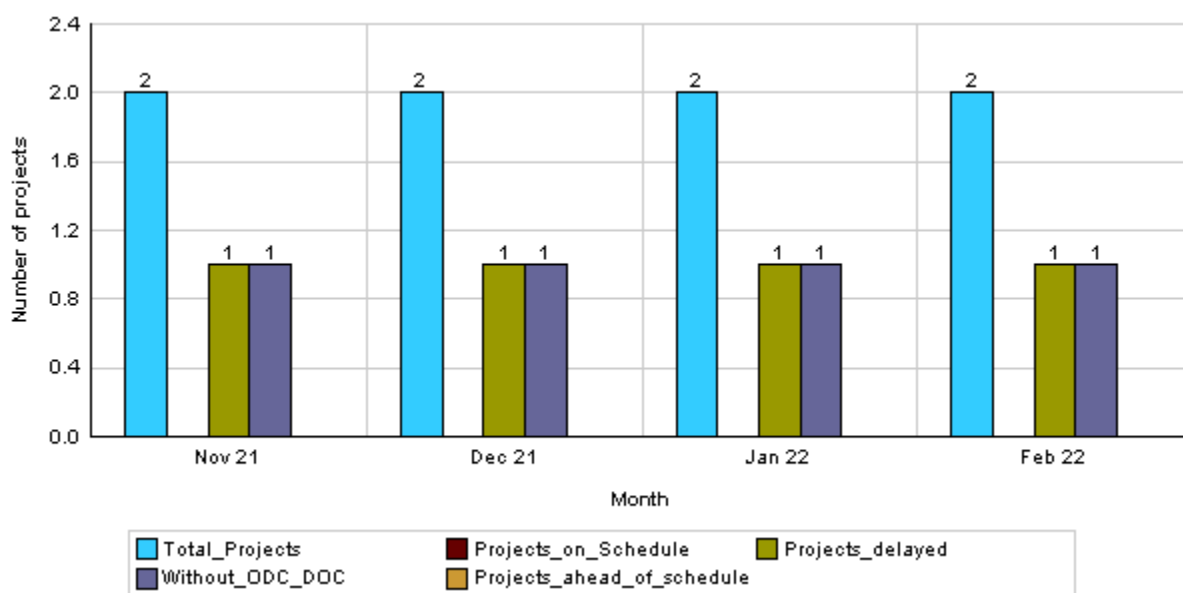


Break-up of 1 Delayed projects in February 2022




Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of HOME AFFAIRS Sector

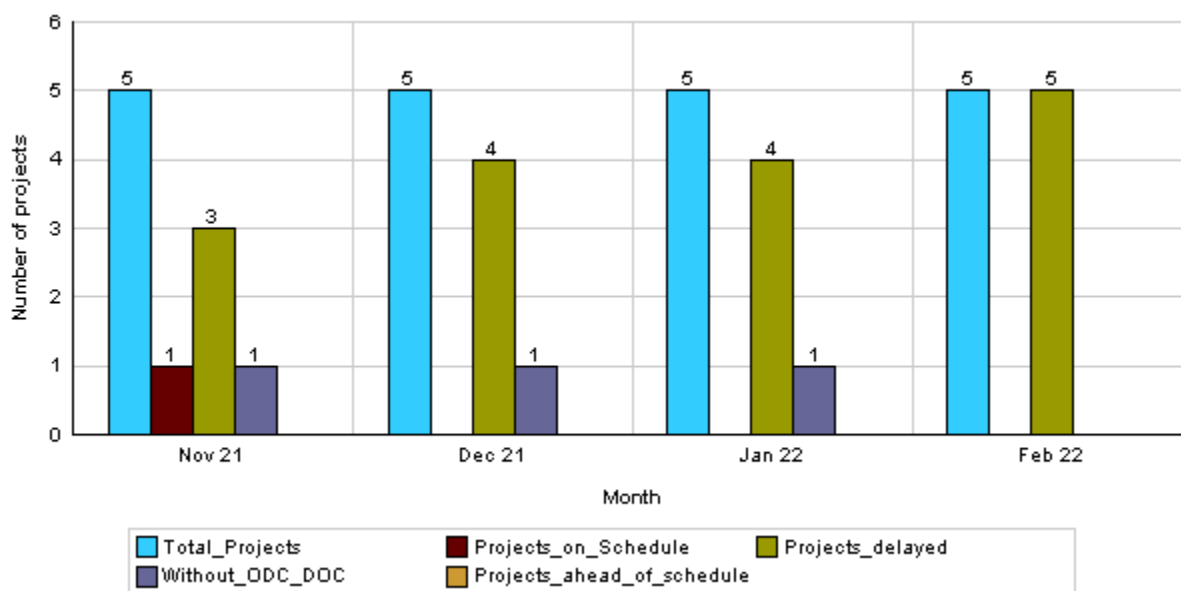


Break-up of 5 Delayed projects in February 2022

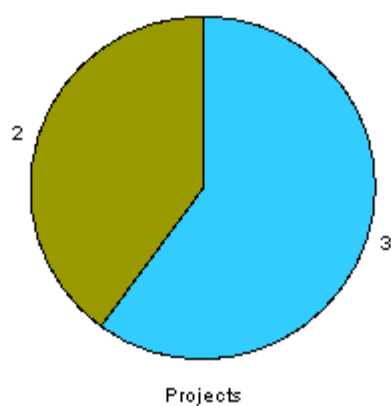


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

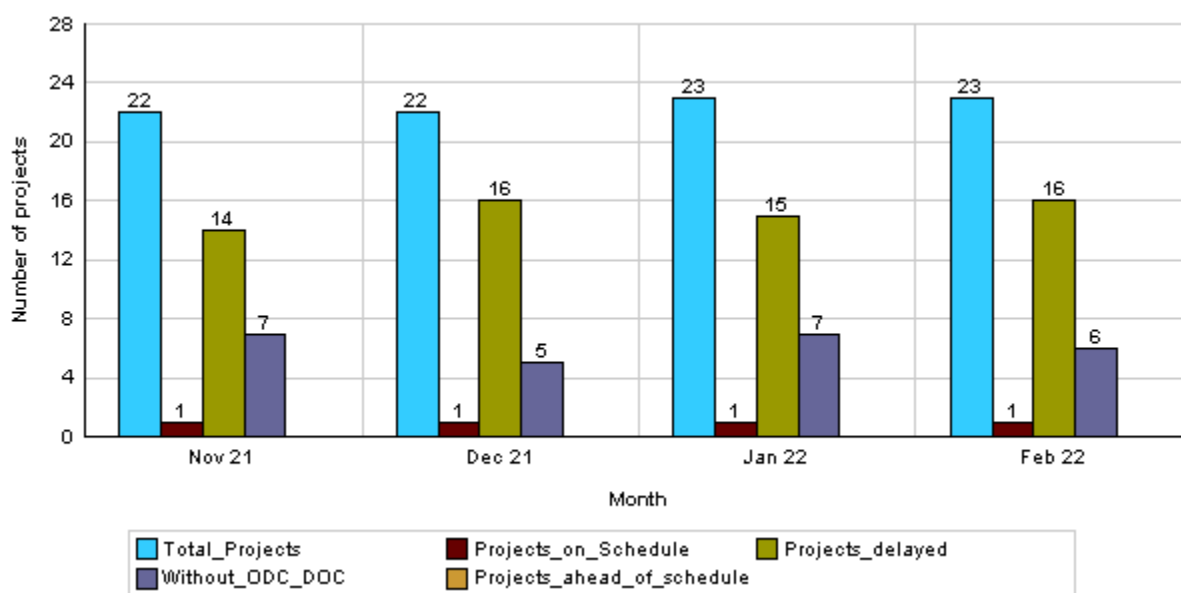


Break-up of 16 Delayed projects in February 2022

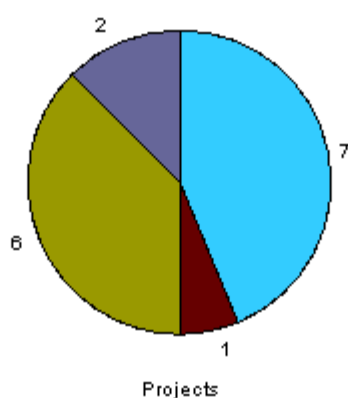


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

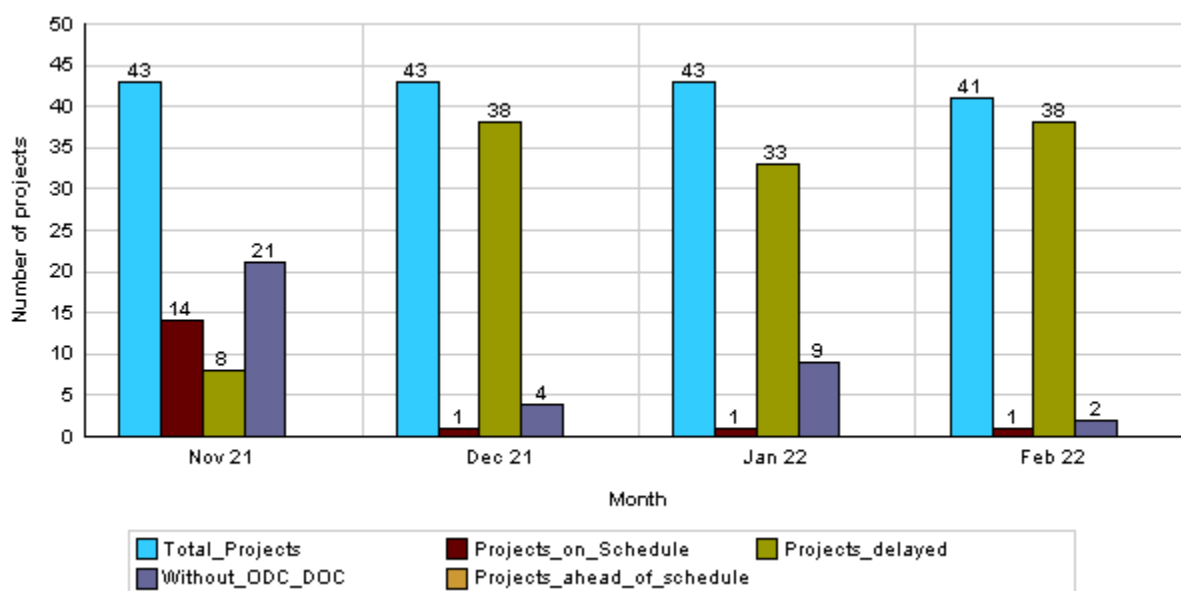


Break-up of 38 Delayed projects in February 2022

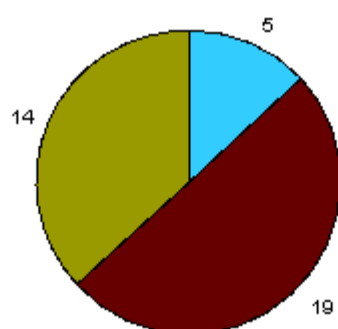


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of URBAN DEVELOPMENT Sector

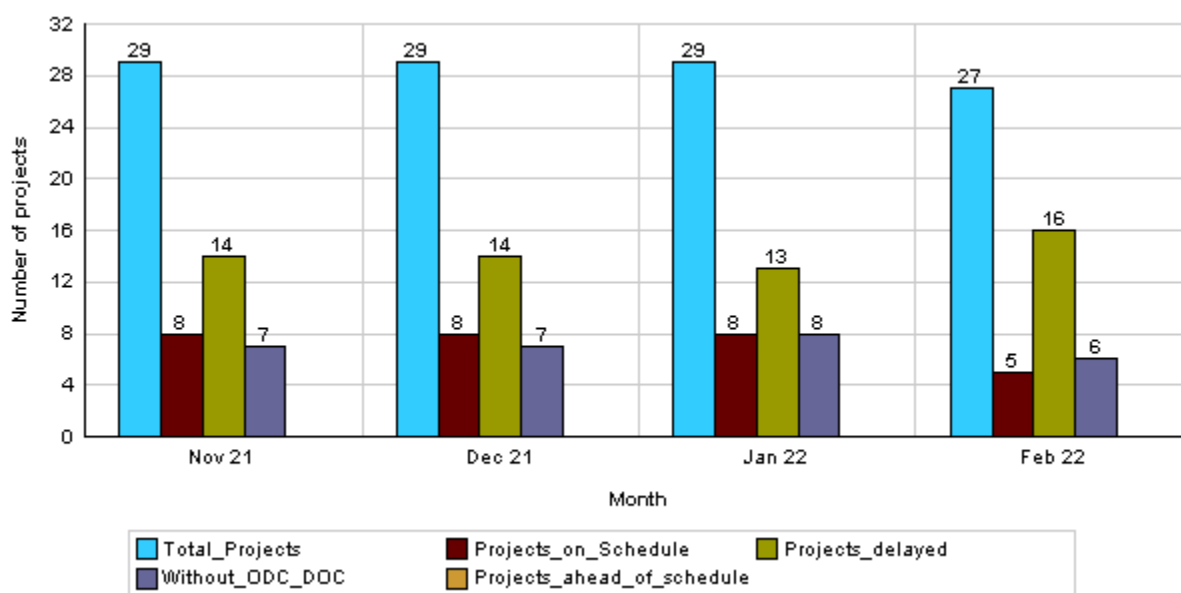


Break-up of 16 Delayed projects in February 2022

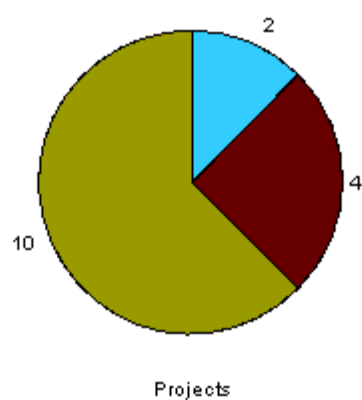


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

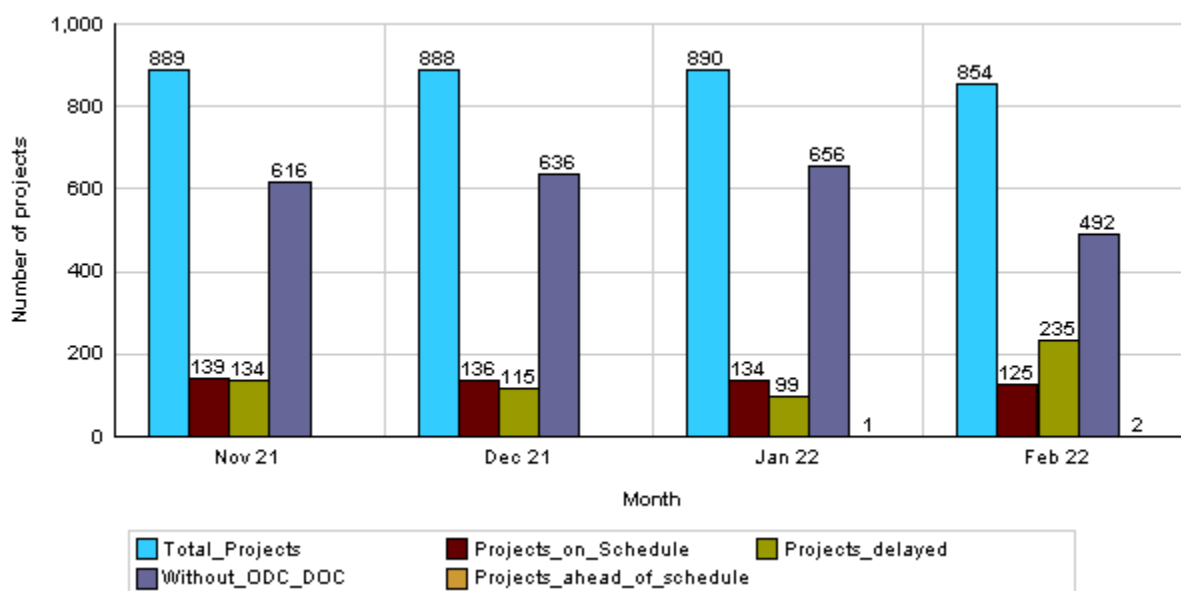


Break-up of 235 Delayed projects in February 2022

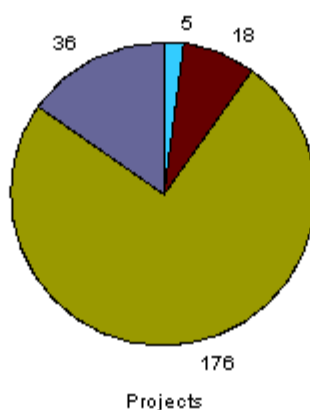


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

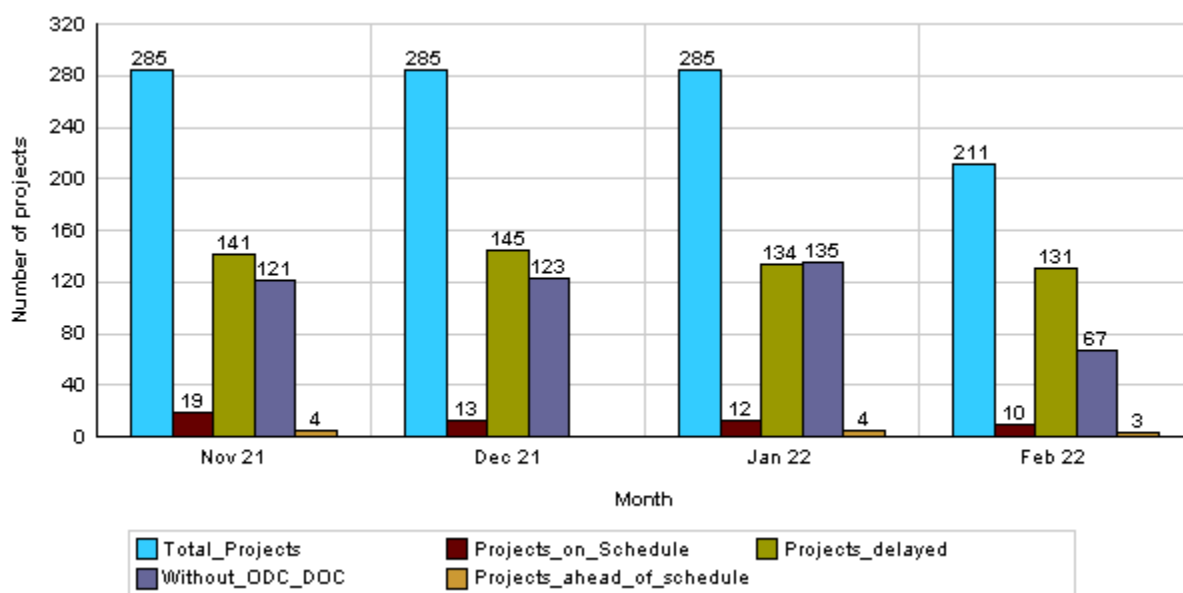


Break-up of 131 Delayed projects in February 2022

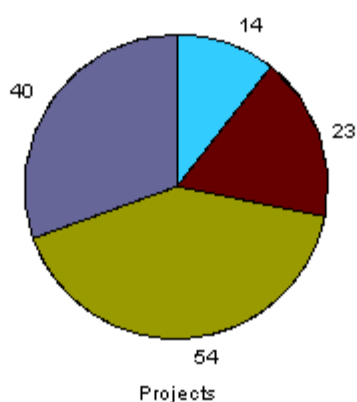


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

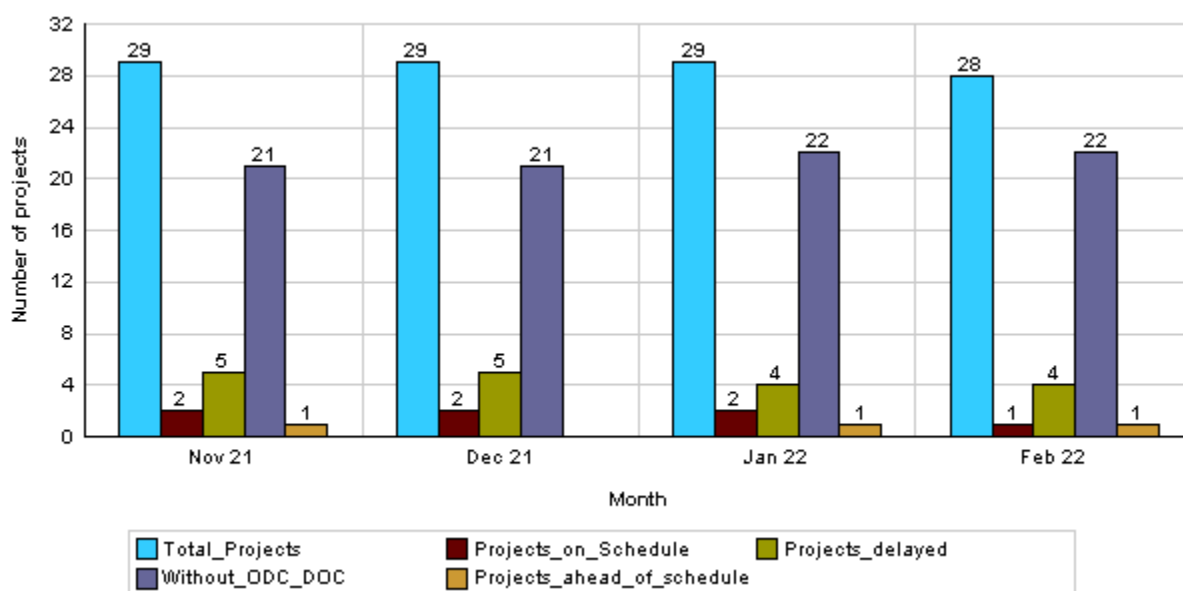


Break-up of 4 Delayed projects in February 2022

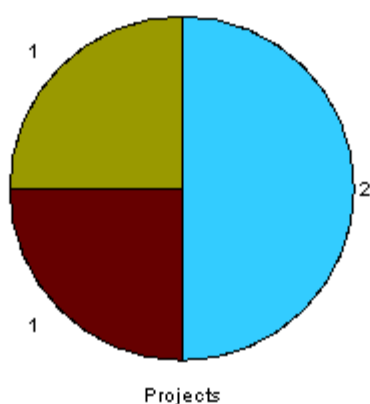


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

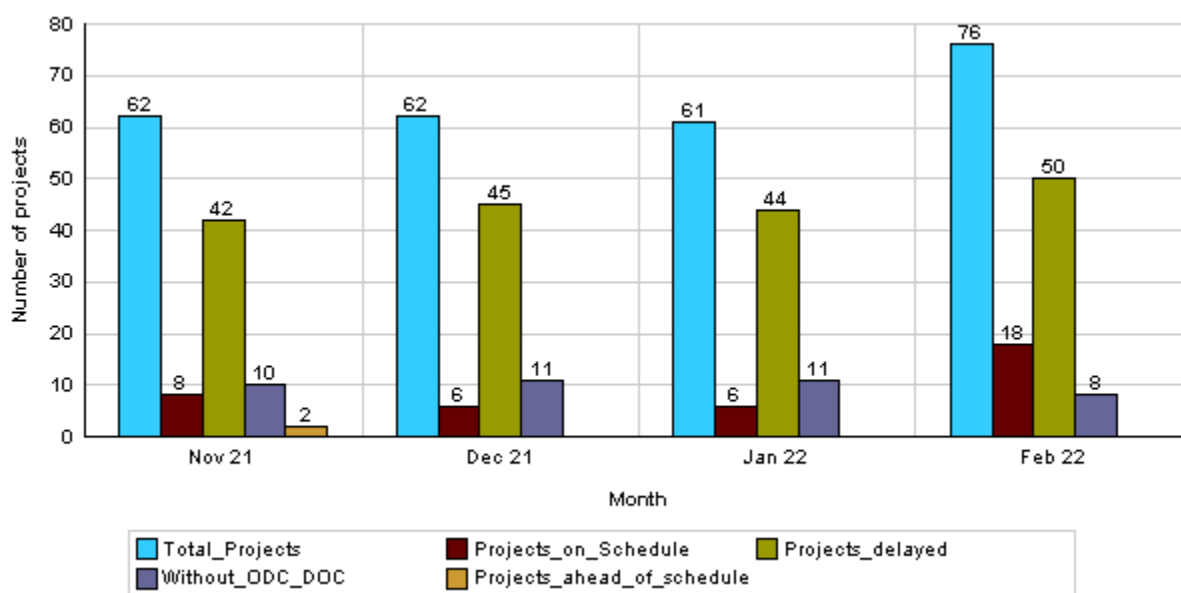


Break-up of 50 Delayed projects in February 2022

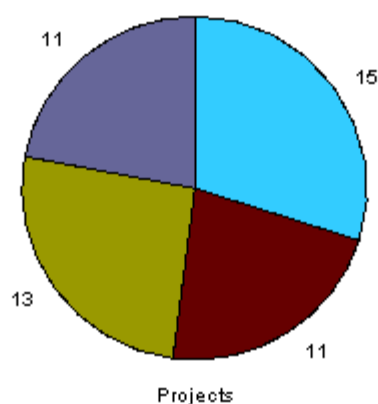


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

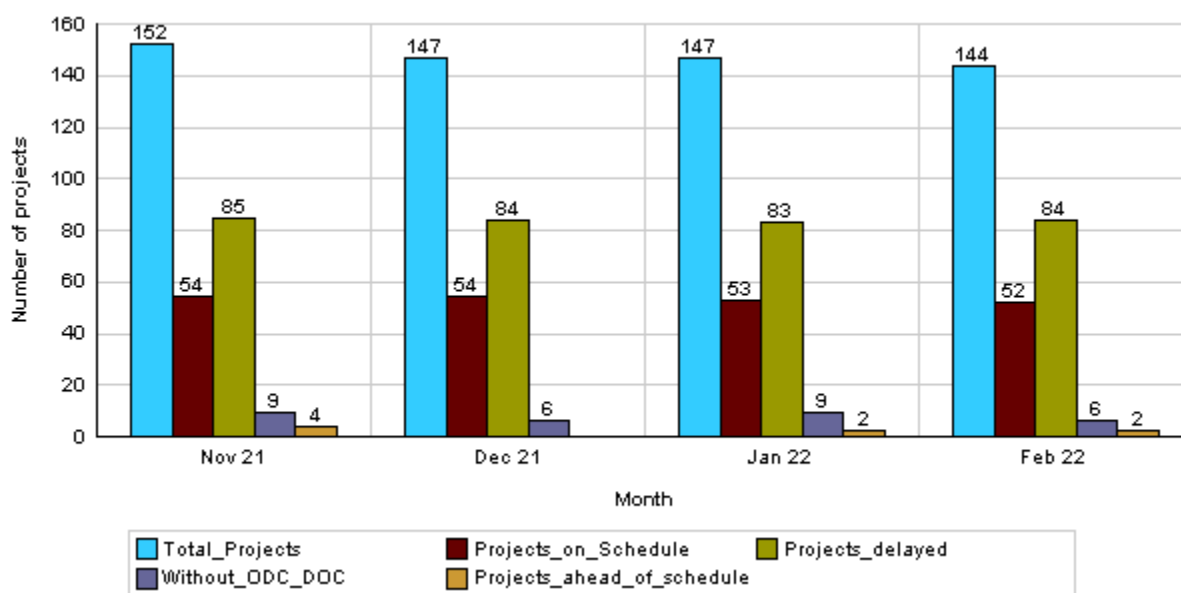


Break-up of 84 Delayed projects in February 2022

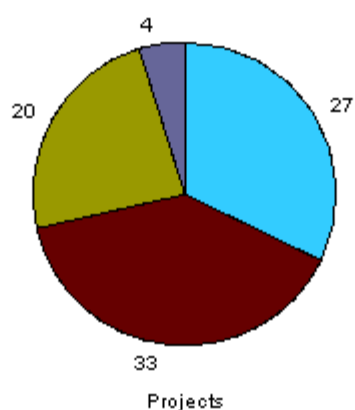


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of STEEL Sector

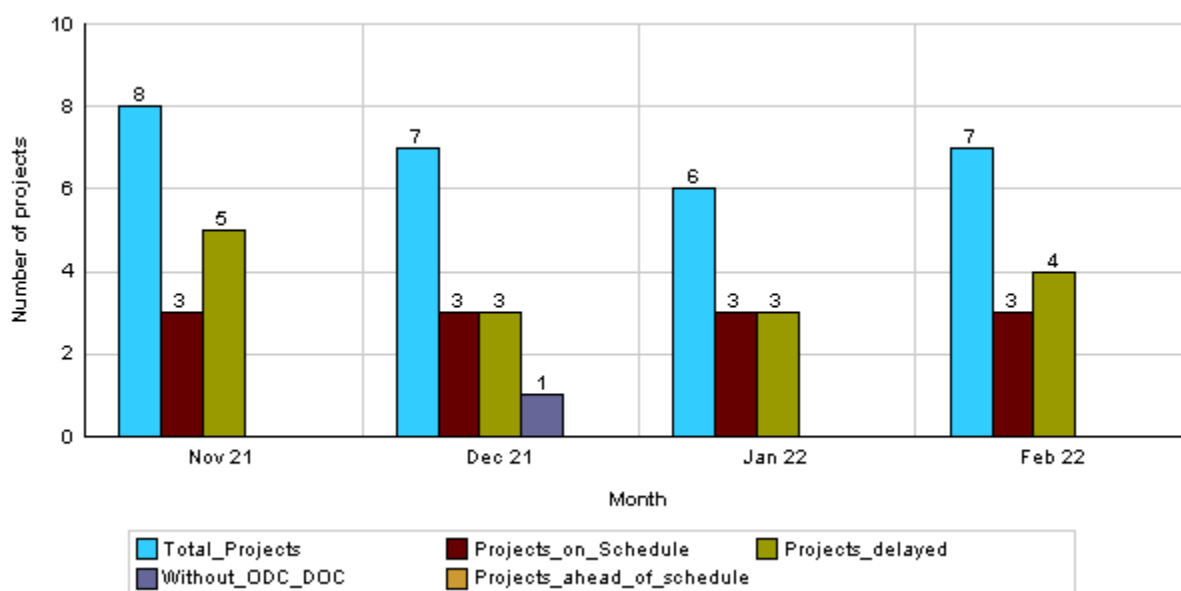


Break-up of 4 Delayed projects in February 2022

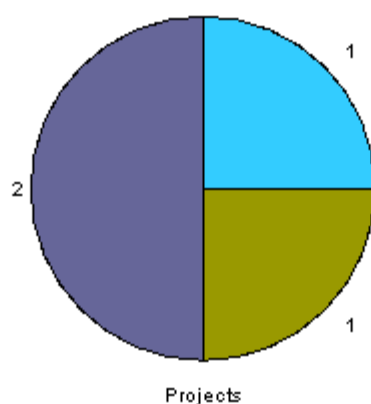

Delay in Months

1-12	13-24	25-60	MORE THAN 60
1	0	1	2

Graphical Presentation of MINES Sector

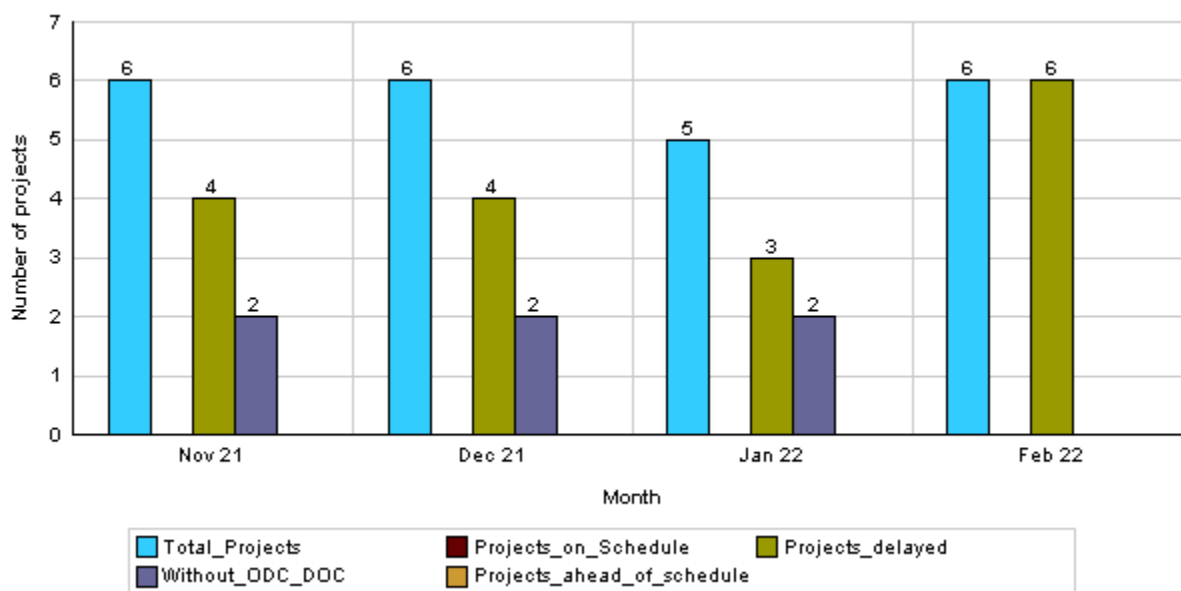


Break-up of 6 Delayed projects in February 2022




Delay in Months

Graphical Presentation of FERTILISERS Sector

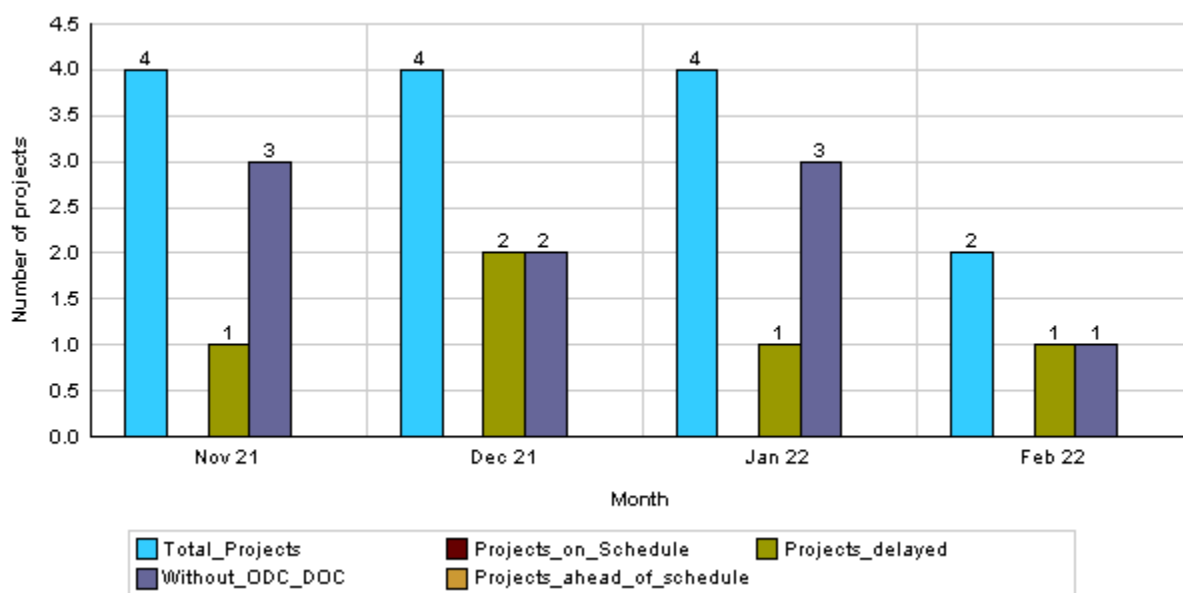


Break-up of 1 Delayed projects in February 2022

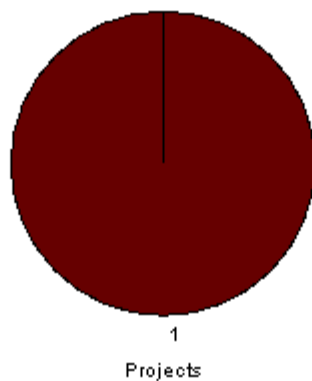


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	1	0	0

Graphical Presentation of COAL Sector

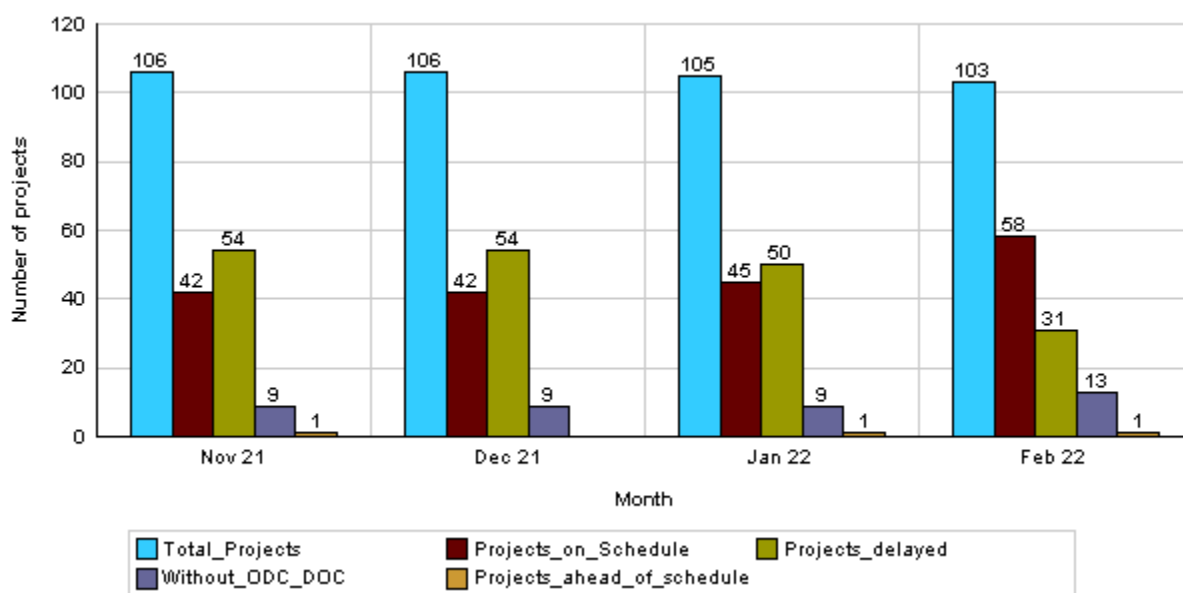


Break-up of 31 Delayed projects in February 2022

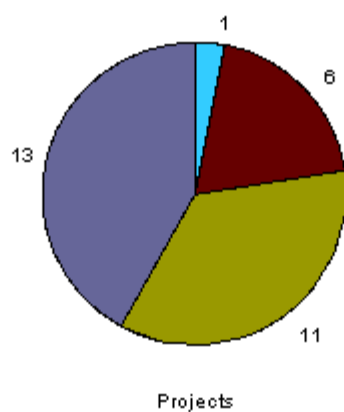


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of CIVIL AVIATION Sector

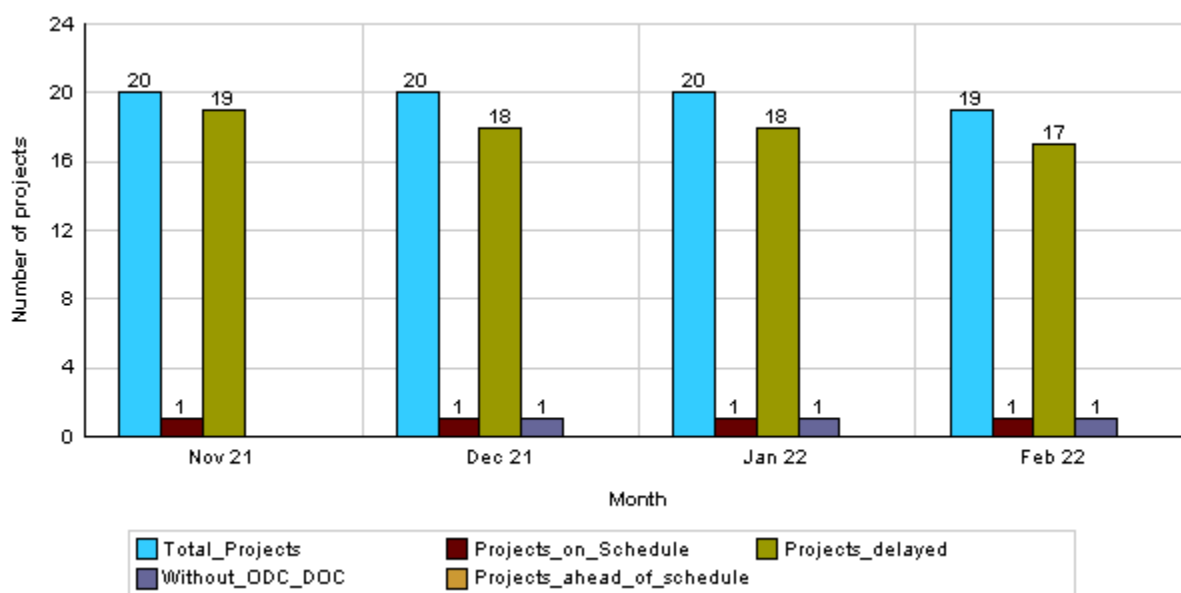


Break-up of 17 Delayed projects in February 2022

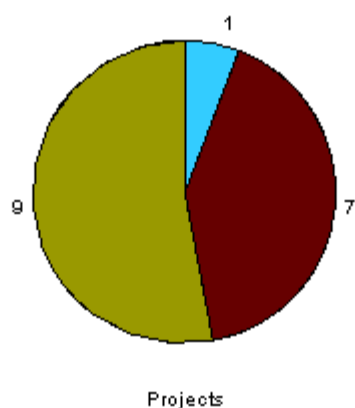


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

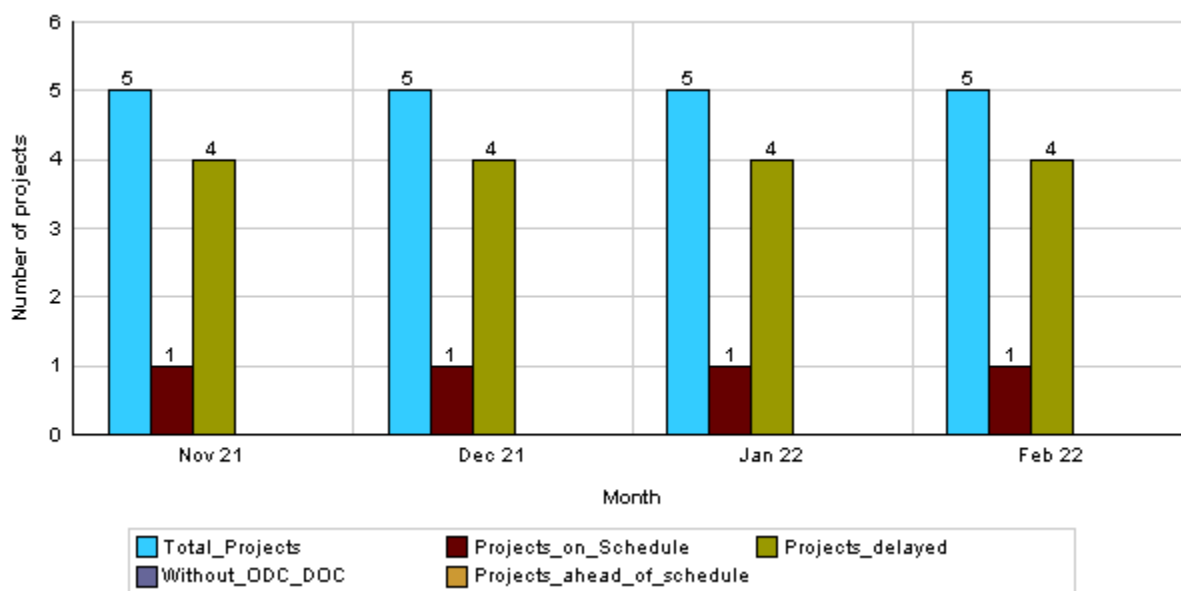

Break-up of 4 Delayed projects in February 2022

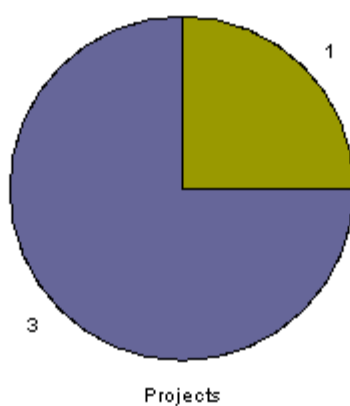

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	0	0
13-24	0	0	0	0
25-60	0	0	3	0
MORE THAN 60	0	0	0	0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 19,220.00	19,220.00	17,806.00	12/2015 -	12/2022	84(O) -	63/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 17,079.00	17,079.00	14,142.00	12/2016 -	12/2023	84(O) -	53/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	6,268.20	09/2010 -	10/2022	145(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	30,143.00	11/2020 -	11/2023	36(O) -	29/76
5	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]NPCIL,TAMIL NADU ,	06/2017	49,621.00 -	49,621.00	5,453.00	09/2027 -	09/2027	0(O) -	16/80
	Total		1,16,741.00 -	1,32,609.00	73,812.20				244/381
	CIVIL AVIATION								
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23 -	707.73	507.91	09/2018 10/2022	10/2022	49(O) 4	0/6
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10 -	177.10	115.40	02/2020 12/2022	12/2022	34(O) 0	1/4
8	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80 -	611.80	88.95	03/2023 03/2023	03/2023	0(O) 0	5/14
9	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH ,	02/2019	645.63 -	645.63	296.53	08/2022 10/2023	10/2023	14(O) 11	0/3
10	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00 -	1,232.00	391.13	03/2021 03/2025	03/2025	48(O) 0	0/1
11	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90 -	1,216.90	283.65	10/2022 03/2024	03/2024	17(O) 3	0/3
12	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00 -	1,405.00	439.69	08/2022 08/2023	08/2023	12(O) 5	1/15
13	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH ,	07/2018	346.27 -	480.33	145.28	09/2021 12/2023	12/2023	27(O) 6	2/4
14	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24 -	412.24	243.86	06/2021 03/2023	03/2023	21(O) 3	0/1
15	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39 -	475.39	202.52	04/2021 08/2023	08/2023	28(O) 12	3/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00 -	2,467.00	838.87	02/2022 12/2024	12/2024	34(O) 6	0/12
17	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	548.93	10/2021 04/2023	04/2023	18(O) 4	3/14
18	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	20.42	03/2022 03/2024	03/2024	24(O) 0	4/18
19	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	109.92	05/2022 12/2023	12/2023	19(O) 0	2/4
20	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI,TRIPURA ,	09/2015	438.28 -	402.00	398.21	06/2019 12/2021	12/2021	-	1/1
21	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 -	1,938.00	579.75	09/2021 -	12/2023	27(O) -	0/2
22	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	340.28	09/2020 12/2022	12/2022	27(O) 3	1/1
23	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	171.37	03/2020 03/2024	03/2024	48(O) 23	0/2
24	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	233.91	11/2021 04/2023	04/2023	17(O) 0	0/2
	Total		14,128.17 -	15,161.45	5,956.58				23/117
	<u>COAL</u>								
25	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,768.67	03/2023 -	03/2023	0(O) -	15/21
26	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	3,393.76	03/2023 -	03/2023	0(O) -	13/22
27	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	10.32	03/2023 -	03/2023	0(O) -	1/12
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	9.23	03/2014 -	03/2026	144(O) -	3/9
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	224.43	03/2014 -	03/2023	108(O) -	5/6
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	179.09	03/2022 -	03/2025	36(O) -	4/11
31	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	48.36	03/2018 -	03/2023	60(O) -	1/7
32	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	152.47	03/2020 -	03/2023	36(O) -	3/6
33	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	12.61	03/2023 -	03/2023	0(O) -	2/12
34	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	2/6
35	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	86.57	03/2026 -	03/2026	0(O) -	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
36	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	63.39	03/2026 -	03/2026	0(O) -	2/4
37	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	2.02	03/2026 -	03/2026	0(O) -	3/5
38	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	362.52	03/2029 -	03/2029	0(O) -	0/0
39	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	190.30	03/2024 -	03/2024	0(O) -	0/0
40	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
41	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	1,881.55	03/2029 -	03/2029	0(O) -	0/0
42	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL,CHHATISGARH ,	07/2016	459.49 -	459.49	.00	03/2020 -	03/2022	24(O) -	0/0
43	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	124.86	03/2011 -	03/2023	144(O) -	7/7
44	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	502.12	03/2016 -	03/2023	84(O) -	7/7
45	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	98.68	03/2014 -	03/2023	108(O) -	7/7
46	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	91.62	04/2014 -	10/2025	138(O) -	4/7
47	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	515.18	03/2019 -	04/2024	61(O) -	2/6
48	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2023	24(O) -	0/2
49	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	288.42	05/2014 -	03/2022	94(O) -	0/8
50	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	260.95	03/2022 -	03/2022	0(O) -	4/22
51	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	165.05	03/2024 -	03/2024	0(O) -	0/17
52	TETARIAKHAR EXPANSION OCP - [N06000186]CCL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	42.98	03/2023 -	03/2023	0(O) -	1/1
53	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	38.76	09/2028 -	09/2023	-60(O) -	5/11
54	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 -	334.27	32.60	04/2018 -	06/2023	62(O) -	0/0
55	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]CCL,JHARKHAND ,	08/2020	7,254.37 -	7,254.37	.00	03/2028 -	03/2028	0(O) -	0/0
56	EXPANSION PROJECT AMRAPALI OCP - [N06000217]CCL,JHARKHAND ,	08/2020	5,136.15 -	5,136.15	.00	03/2028 -	03/2028	0(O) -	0/0
57	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]CCL,JHARKHAND ,	07/2021	778.80 -	778.80	.00	03/2026 -	03/2026	0(O) -	0/0
58	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	3/10
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	86.60	03/2021 -	-	-	4/10
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	79.50	03/2021 -	03/2024	36(O) -	5/9
61	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	2.59	03/2022 -	03/2022	0(O) -	1/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	AMADAND OPENCASST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	137.22	03/2021 -	03/2025	48(O) -	4/6
63	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	954.78	03/2021 -	03/2023	24(O) -	4/9
64	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	584.00	03/2022 -	03/2023	12(O) -	5/9
65	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
66	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	2.65	03/2026 -	03/2026	0(O) -	2/7
67	BLOCK-B EXPANSION OPENCASST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	2.45	03/2023 -	03/2023	0(O) -	1/7
68	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
69	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH ,	03/2021	496.28 -	496.28	.00	03/2028 -	03/2028	0(O) -	0/0
70	DHANKASA UG (RECAST) (1 MTY) - [N06000224]WCL,MADHYA PRADESH ,	02/2020	289.30 -	289.30	.00	03/2025 -	03/2025	0(O) -	0/0
71	RPR FOR JAMUNIA UG - [N06000228]WCL,MADHYA PRADESH ,	08/2020	281.25 -	281.25	.00	03/2026 -	03/2026	0(O) -	0/0
72	RAMPUR BATURA OC (4.0 MTY) - [N06000233]SECL,MADHYA PRADESH ,	07/2019	1,248.93 -	1,248.93	.00	03/2026 -	03/2026	0(O) -	0/0
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 299.67	299.67	213.93	03/2019 -	03/2022	36(O) -	12/13
74	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 745.83	745.03	456.01	03/2025 -	03/2025	0(O) -	9/13
75	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	226.62	03/2021 -	09/2022	18(O) -	1/4
76	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	107.27	03/2021 09/2022	09/2022	18(O) 0	0/3
77	GHONSA EXPANSION DEEP OC - [N06000205]WCL,MAHARASHTRA ,	03/2021	241.72 -	241.72	57.00	03/2028 -	03/2028	0(O) -	0/7
78	SASTI EXPANSION OC - [N06000206]WCL,MAHARASHTRA ,	08/2020	371.59 -	371.59	52.55	03/2026 -	03/2026	0(O) -	1/7
79	DHUPTALA OC(SASTI UG TO OC) - [N06000209]WCL,MAHARASHTRA ,	02/2019	720.87 -	720.87	108.38	03/2028 -	03/2028	0(O) -	0/6
80	ADASA UG TO OC (1.50 MTY) - [N06000219]WCL,MAHARASHTRA ,	11/2018	333.43 -	333.43	.00	03/2024 -	03/2024	0(O) -	0/0
81	BHANEGAON OC (1MTY) - [N06000221]WCL,MAHARASHTRA ,	02/2017	409.68 -	409.68	.00	03/2023 -	03/2023	0(O) -	0/0
82	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]WCL,MAHARASHTRA ,	02/2020	1,184.33 -	1,184.33	.00	03/2027 -	03/2027	0(O) -	0/0
83	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]WCL,MAHARASHTRA ,	09/2018	313.34 -	313.34	.00	03/2024 -	03/2024	0(O) -	0/0
84	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]WCL,MAHARASHTRA ,	11/2020	826.80 -	826.80	.00	03/2026 -	03/2026	0(O) -	0/0
85	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL,MAHARASHTRA ,	02/2016	327.41 -	327.41	.00	03/2019 -	09/2026	90(O) -	0/0
86	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 404.45	404.45	252.90	03/2022 -	03/2022	0(O) -	0/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	298.48	03/2021 -	09/2023	30(O) -	5/6
88	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
89	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	808.97	815.72	03/2013 -	03/2024	132(O) -	6/9
90	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	254.83	03/2019 -	03/2024	60(O) -	3/9
91	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	2,718.35	03/2026 -	03/2026	0(O) -	9/15
92	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	710.64	03/2021 -	03/2026	60(O) -	9/10
93	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	841.95	03/2027 -	03/2027	0(O) -	3/12
94	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,341.19	03/2029 -	03/2029	0(O) -	1/9
95	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	920.53	01/2027 -	04/2020	-	19/22
96	NAINI COAL MINE - [N06000203]SCCL,ODISHA ,	03/2020	494.30 -	494.30	137.86	03/2024 -	03/2024	0(O) -	1/7
97	ANANTA OCP EXPANSION PH III - [N06000225]MCL,ODISHA ,	08/2008	228.08 -	228.08	.00	03/2012 -	03/2012	-	0/0
98	BHUBANESWARI EXPANSION OCP - [N06000227]MCL,ODISHA ,	08/2020	3,145.45 -	3,145.45	.00	03/2031 -	03/2031	0(O) -	0/0
99	GOPALJI-KANIHA OCP - [N06000229]MCL,ODISHA ,	08/2020	8,416.19 -	8,416.19	.00	03/2028 -	03/2028	0(O) -	0/0
100	BALARAM EXPANSION OCP - [N06000230]MCL,ODISHA ,	08/2020	3,504.21 -	3,504.21	.00	03/2029 -	03/2029	0(O) -	0/0
101	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
102	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
103	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	93.05	09/2020 -	-	-	0/0
104	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	113.42	09/2020 -	-	-	0/0
105	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	7,980.79	7,429.39	12/2015 -	02/2021	-	35/35
106	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 -	709.06	496.44	06/2015 -	09/2027	147(O) -	5/7
107	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	290.90	03/2022 -	03/2022	0(O) -	6/11
108	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	03/2018 -	03/2022	48(O) -	2/6
109	GODAVARIKHANI COAL MINE - [N06000202]SCCL,TELANGANA ,	07/2019	438.98 -	438.98	95.10	03/2023 -	03/2023	0(O) -	1/11
110	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA ,	10/2020	484.51 -	484.51	27.52	03/2023 -	03/2023	0(O) -	0/8
111	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]SCCL,TELANGANA ,	11/2015	489.62 -	489.62	.00	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	RCE OF INDARAM OPENCASE PROJECT - [N06000211]SCCL,TELANGANA ,	08/2017	349.28 -	349.28	.00	03/2021 -	03/2021	-	0/0
113	RCE-II OF JALAGAM VENGALRAO OPENCASE PROJECT-II - [N06000212]SCCL,TELANGANA ,	03/2019	473.22 -	473.22	.00	03/2021 -	03/2021	-	0/0
114	RCE OF KALYANIKHANI OPENCASE PROJECT - [N06000213]SCCL,TELANGANA ,	03/2016	384.32 -	384.32	.00	03/2020 -	03/2020	-	0/0
115	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL,TELANGANA ,	08/2017	442.42 -	442.42	.00	03/2020 -	03/2020	-	0/0
116	RCE OF KISTARAM OPENCASE PROJECT - [N06000215]SCCL,TELANGANA ,	03/2017	164.04 -	164.04	.00	03/2021 -	03/2021	-	0/0
117	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	13,185.30	11/2021 -	06/2023	19(O) -	20/48
118	KHADIA EXPANSION OCP - [N06000208]NCL,UTTAR PRADESH ,	06/2021	491.67 -	491.67	.00	03/2025 -	03/2025	0(O) -	0/5
119	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	625.60	08/2019 -	08/2024	60(O) -	1/19
120	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.75	03/2026 -	03/2026	0(O) -	4/22
121	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	26.86	03/2029 -	03/2029	0(O) -	2/22
122	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	4.48	03/2027 -	03/2027	0(O) -	2/27
123	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	1.49	03/2027 -	03/2027	0(O) -	0/22
124	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	9.64	03/2025 -	03/2025	0(O) -	0/0
125	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 -	341.22	91.55	03/2017 -	12/2022	69(O) -	0/0
126	SONEPUR BAZARI EXPANSION OC - [N06000220]ECL,WEST BENGAL ,	07/2021	5,365.88 5,366.00	5,365.88	.00	03/2029 -	03/2029	0(O) -	0/0
127	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]ECL,WEST BENGAL ,	04/2020	1,210.12 -	1,210.12	.00	03/2029 -	03/2029	0(O) -	0/0
	Total		1,53,083.23 -	1,57,457.70	47,810.81				279/714
	FINANCE								
128	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU ,	12/2015	209.00 -	208.96	208.93	10/2019 -	07/2021	-	1/6
129	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU ,	11/2017	348.77 -	348.77	204.00	11/2021 -	11/2021	-	3/8
	Total		557.77 -	557.73	412.93				4/14
	FERTILISERS								
130	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	186.27	11/2019 -	01/2022	-	1/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	363.71	04/2020 03/2022	03/2022	23(O) 2	14/14
	Total		642.64 -	642.64	549.98				15/16
	<u>MINES</u>								
132	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	6,435.90	1,268.54	04/2021 01/2024	01/2024	33(O) 0	4/4
133	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 667.23	667.23	395.98	01/2020 11/2023	11/2023	46(O) 0	3/3
134	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 581.00	581.00	96.18	11/2020 12/2023	12/2023	37(O) 0	3/3
135	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	10.96	04/2021 12/2023	12/2023	32(O) 0	2/2
136	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2022	12/2022	42(O) 24	1/1
137	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART DG GSI AT SECTOR-V SA - [N10000015]CPWD,WEST BENGAL , EPC	04/2019	255.37 -	255.37	1.16	04/2022 -	10/2024	30(O) -	0/1
	Total		7,333.99 -	8,585.67	1,907.82				13/14
	<u>STEEL</u>								
138	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	21,940.00	19,611.48	05/2015 01/2022	06/2022	85(O) 3	75/86
139	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	89.30	12/2023 -	12/2023	0(O) -	0/0
140	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	636.12	06/2023 -	06/2024	12(O) -	2/8
141	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	572.49	10/2017 12/2021	11/2022	61(O) 0	0/2
142	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	212.42	06/2019 02/2022	05/2022	35(O) 0	1/1
143	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	57.81	05/2023 -	05/2023	0(O) -	0/1
144	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125]SAIL,ODISHA , EPC	01/2022	970.18 -	970.18	.00	05/2025 -	05/2025	0(O) -	0/0
	Total		21,618.48 -	28,033.48	21,179.62				78/98
	<u>PETROLEUM</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
145	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	26,264.00	18,232.09	07/2020 -	07/2022	24(O) -	95/111
146	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	31,040.00	16,067.78	06/2020 05/2023	05/2023	35(O) 0	15/20
147	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	313.36	04/2021 09/2022	09/2022	17(O) 0	0/0
148	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	135.36	04/2022 -	02/2023	10(O) -	0/0
149	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	152.91	10/2021 03/2022	09/2022	11(O) 6	0/0
150	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	291.62	02/2021 -	03/2023	25(O) -	0/16
151	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	107.95	07/2020 -	01/2022	-	1/5
152	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	22.01	07/2022 -	02/2023	7(O) -	0/5
153	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022	0(O) -	0/0
154	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	224.20	03/2021 -	12/2021	-	0/0
155	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	130.17	08/2021 -	03/2022	7(O) -	0/0
156	CGD PROJECT AT SRIKAKULAM VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH ,	06/2019	2,880.00 -	2,880.00	117.00	08/2027 -	08/2027	0(O) -	0/0
157	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]HPCL,ANDHRA PRADESH , EPC	09/2021	160.00 -	160.00	.13	06/2024 -	06/2024	0(O) -	1/12
158	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	638.60	412.80	02/2020 -	06/2022	28(O) -	1/14
159	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 -	198.00	189.00	08/2020 03/2022	03/2022	19(O) 2	0/0
160	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 -	18,968.00	940.95	10/2024 -	10/2024	0(O) -	0/0
161	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	9,058.00	1,966.98	10/2024 -	10/2024	0(O) -	0/0
162	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]IOCL,ASSAM ,	05/2021	412.00 -	412.00	30.01	10/2023 -	10/2023	0(O) -	3/10
163	GAS ASSISTED GRAVITY DRAINAGE SCHEME KASOMARIGAON - [N16000433]ONGC,ASSAM , EPC	08/2021	218.38 -	218.38	33.82	02/2023 -	02/2023	0(O) -	3/5
164	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	174.10	03/2021 03/2022	02/2022	11(O) -1	25/26
165	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	112.94	10/2020 08/2022	08/2022	22(O) 0	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	200.37	10/2022 -	10/2023	12(O) -	10/10
167	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	185.52	01/2021 06/2021	03/2022	14(O) 1	7/8
168	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	423.89	03/2021 03/2022	03/2022	12(O) 0	0/0
169	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	2,561.63	04/2023 -	04/2023	0(O) -	2/2
170	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	126.54	08/2022 -	08/2022	0(O) -	0/0
171	CGD PROJECT AT AURANGABAD KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR ,	10/2018	176.00 -	176.00	90.56	08/2027 -	08/2027	0(O) -	0/0
172	CGD PROJECT AT ARARIA PURNIA KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR ,	06/2019	988.00 -	988.00	49.65	12/2029 -	12/2029	0(O) -	0/0
173	CGD PROJECT AT ARWAL JEHANABAD BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR ,	06/2019	439.00 -	439.00	133.31	02/2028 -	02/2028	0(O) -	0/0
174	CGD PROJECT AT KHAGARIA SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR ,	06/2019	163.00 -	163.00	28.39	12/2029 -	12/2029	0(O) -	0/0
175	CGD PROJECT AT LAKHISARAI MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR ,	06/2019	347.00 -	347.00	114.50	02/2028 -	02/2028	0(O) -	0/0
176	CGD PROJECT AT MUZAFFARPUR VAISHALI SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR ,	06/2019	2,996.00 -	2,996.00	329.06	02/2028 -	02/2028	0(O) -	0/0
177	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]HPCL,CHHATISGARH , EPC	03/2021	456.00 -	456.00	88.45	03/2024 -	03/2024	0(O) -	6/62
178	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	220.00	200.10	04/2018 -	06/2022	50(O) -	19/20
179	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	1,162.56	947.93	03/2026 -	03/2026	0(O) -	9/10
180	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	376.32	02/2020 10/2021	07/2022	29(O) 4	7/8
181	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	730.20	226.83	- 05/2023	05/2023	- 0	12/17
182	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	247.90	120.91	02/2021 -	10/2022	20(O) -	6/8
183	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	208.61	04/2022 -	04/2022	0(O) -	10/11
184	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	836.13	05/2023 -	05/2023	0(O) -	6/11
185	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	187.71	12/2022 -	12/2022	0(O) -	0/0
186	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	171.45	08/2022 -	08/2022	0(O) -	5/6
187	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	953.51	09/2024 -	08/2024	-1(O) -	3/6
188	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	66.18	08/2023 -	08/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
189	REDEVELOPMENT OF LINCH FIELD - [N16000428]ONGC,GUJARAT , EPC	04/2021	631.03 -	631.03	228.08	03/2025 -	03/2025	0(O) -	0/2
190	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]ONGC,GUJARAT , EPC	08/2021	885.63 -	885.63	206.93	02/2026 -	02/2026	0(O) -	0/2
191	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 340.76	340.76	172.39	02/2020 07/2022	07/2022	29(O) 0	6/7
192	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	1,012.58	08/2020 04/2022	09/2022	25(O) 5	6/7
193	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	551.04	01/2021 03/2022	08/2022	19(O) 5	3/6
194	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 753.89	753.89	495.80	02/2020 07/2022	07/2022	29(O) 0	4/5
195	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.00	327.01	233.20	08/2020 12/2021	04/2022	20(O) 1	14/16
196	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	139.82	06/2021 07/2022	07/2022	13(O) 0	3/5
197	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 3,219.94	2,281.94	703.22	12/2022 07/2023	07/2023	7(O) 0	4/6
198	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	473.01	12/2021 01/2023	01/2023	13(O) 0	3/7
199	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	45.60	07/2021 03/2022	08/2022	13(O) 5	4/9
200	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	215.09	09/2026 -	02/2027	5(O) -	43/52
201	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]IOCL,HARYANA ,	02/2021	34,627.00 -	34,627.00	538.73	09/2024 -	09/2024	0(O) -	0/0
202	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	784.66	03/2023 03/2022	03/2022	-12(O) 0	9/11
203	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	136.30	06/2020 -	03/2022	21(O) -	11/12
204	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	152.67	10/2022 -	10/2022	0(O) -	19/19
205	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	149.47	06/2022 -	09/2022	3(O) -	0/0
206	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	113.23	10/2022 -	08/2023	10(O) -	9/9
207	CGD PROJECT AT BOKARO HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND ,	10/2018	613.00 -	613.00	171.20	12/2029 -	12/2029	0(O) -	0/0
208	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,809.28	12/2019 04/2021	03/2022	27(O) 0	12/12
209	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	1,539.20	06/2022 -	06/2022	0(O) -	13/18
210	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	185.98	12/2022 -	12/2022	0(O) -	15/19

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
211	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	348.51	11/2021 03/2022	03/2022	4(O) 0	18/19
212	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 304.00	304.00	2.61	06/2023 01/2024	01/2024	7(O) 0	3/6
213	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 1,236.00	1,236.00	568.65	10/2017 03/2022	12/2022	62(O) 0	44/52
214	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,507.24	855.28	06/2019 -	02/2023	44(O) -	0/0
215	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023	0(O) -	0/0
216	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 319.61	319.61	237.99	06/2020 12/2021	12/2021	-	0/0
217	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH ,	10/2018	177.00 -	177.00	68.94	02/2027 -	02/2027	0(O) -	0/0
218	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 2,001.34	2,001.34	1,613.65	05/2013 05/2022	05/2022	108(O) 0	5/8
219	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,892.72	04/2018 05/2022	05/2022	49(O) 0	13/15
220	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,657.30	02/2022 -	07/2022	5(O) -	5/5
221	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 437.00	437.00	226.74	01/2021 -	08/2022	19(O) -	0/0
222	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	212.46	06/2020 -	03/2022	21(O) -	5/12
223	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,292.46	2,255.02	05/2021 12/2022	12/2022	19(O) 0	5/6
224	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,790.56	03/2022 05/2023	05/2023	14(O) 0	4/6
225	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	3,233.86	05/2021 05/2022	05/2022	12(O) 0	4/6
226	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,824.00	03/2022 -	03/2023	12(O) -	4/6
227	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	829.58	829.58	12/2020 05/2022	05/2022	17(O) 3	4/5
228	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	380.90	12/2021 -	06/2022	6(O) -	0/0
229	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	338.87	03/2023 -	03/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
230	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]GAIL,MAHARASHTRA ,	05/2019	8,797.00 -	8,797.00	210.01	04/2025 -	04/2025	0(O) -	12/20
231	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]ONGC,MAHARASHTRA , EPC	01/2022	3,183.58 -	3,183.58	.00	05/2024 -	05/2024	0(O) -	4/5
232	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	2,315.92	03/2021 12/2021	05/2022	14(O) 0	5/5
233	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	3,154.79	12/2020 03/2022	03/2022	15(O) 0	5/5
234	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	609.43	07/2018 05/2021	03/2022	44(O) 0	27/36
235	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	340.00	287.12	10/2020 -	03/2022	17(O) -	6/12
236	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	510.00	494.68	12/2019 -	03/2022	27(O) -	6/22
237	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,661.00	12/2020 -	03/2022	15(O) -	23/24
238	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,209.40	12/2020 12/2021	06/2022	18(O) 3	21/24
239	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,048.00	2,271.40	12/2020 12/2021	06/2022	18(O) 0	21/24
240	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,781.00	12/2012 02/2022	02/2025	146(O) 6	26/42
241	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022	13(O) -	20/26
242	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,060.00	2,727.90	12/2021 -	06/2023	18(O) -	17/20
243	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	466.13	11/2022 -	11/2022	0(O) -	14/20
244	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	555.30	07/2022 -	07/2022	0(O) -	11/14
245	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	365.30	11/2022 -	11/2022	0(O) -	9/12
246	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	2,002.80	05/2023 -	05/2023	0(O) -	17/29
247	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE ,	06/2019	169.00 -	169.00	43.28	12/2029 -	12/2029	0(O) -	0/0
248	CGD PROJECT AT SHEIKHPURA JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE ,	06/2019	303.00 -	303.00	140.07	02/2028 -	02/2028	0(O) -	0/0
249	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,620.10	12/2020 12/2021	07/2022	19(O) 4	20/24
250	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	71.65	12/2019 03/2022	01/2023	37(O) 1	18/26

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
251	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	167.21	07/2022 -	08/2023	13(O) -	10/10
252	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL, ODISHA ,	08/2017	315.00 -	315.00	232.78	12/2021 -	02/2022	2(O) -	3/3
253	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL, ODISHA ,	07/2017	182.20 -	182.20	101.14	07/2022 -	08/2023	13(O) -	9/9
254	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL, ODISHA ,	04/2018	5,654.00 -	5,654.00	3,652.22	10/2021 07/2022	07/2022	9(O) 0	9/10
255	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL, ODISHA ,	10/2018	1,297.50 -	1,297.50	914.85	10/2021 -	06/2022	8(O) -	1/1
256	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL, ODISHA ,	11/2018	462.30 543.00	543.00	176.32	09/2021 06/2022	06/2022	9(O) 0	4/5
257	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL, ODISHA ,	05/2019	3,361.00 -	3,361.00	2,141.68	08/2021 09/2022	09/2022	13(O) 0	7/11
258	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL, ODISHA ,	06/2019	371.00 427.10	427.10	41.54	09/2022 03/2023	03/2023	6(O) 0	4/8
259	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL, ODISHA ,	08/2019	1,607.00 -	1,607.00	338.29	08/2022	06/2023	10(O)	0/21
260	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL, ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	88.43	07/2022	07/2022	0(O)	2/4
261	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL, ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	763.89	01/2024 -	01/2024	0(O) -	2/12
262	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL, PUNJAB ,	05/2020	1,421.46 -	1,421.46	281.96	02/2023 -	02/2023	0(O) -	11/22
263	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN ,	03/2018	229.80 -	229.80	101.10	- 05/2022	03/2023	- 0	17/26
264	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]IOCL, RAJASTHAN ,	12/2021	9,028.00 -	9,028.00	.00	10/2024 -	10/2024	0(O) -	0/0
265	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
266	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU ,	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	66(O) -	0/0
267	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC, TAMIL NADU ,	11/2015	650.82 -	650.82	457.24	03/2019 09/2021	05/2023	50(O) 20	4/6
268	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	4,270.46	12/2018 02/2022	06/2022	42(O) 0	5/5
269	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL, TAMIL NADU ,	12/2017	466.43 -	466.43	304.44	10/2020 -	03/2022	17(O) -	0/0
270	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL, TAMIL NADU ,	10/2020	921.00 -	921.00	5.70	09/2023 -	02/2024	5(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
271	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	164.75	12/2023 -	02/2024	2(O) -	0/0
272	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU ,	10/2018	2,998.00 -	2,998.00	210.74	03/2030 -	03/2030	0(O) -	0/0
273	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU ,	10/2018	1,304.00 -	1,304.00	49.47	03/2030 -	03/2030	0(O) -	0/0
274	CBR 9 MMTPA PROJECT - [N16000434]CPCL,TAMIL NADU , Joint Venture	01/2021	31,580.00 -	31,580.00	571.14	06/2025 -	06/2025	0(O) -	0/0
275	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	139.54	04/2022 -	08/2023	16(O) -	0/0
276	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	345.15	265.22	04/2022 -	04/2022	0(O) -	44/53
277	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	188.36	08/2021 03/2023	03/2023	19(O) 0	0/0
278	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	154.50	08/2020 03/2022	10/2022	26(O) 7	3/3
279	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	546.09	08/2022 -	08/2022	0(O) -	3/3
280	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	621.42	03/2029 -	08/2029	5(O) -	32/64
281	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 -	217.92	106.90	04/2021 03/2022	10/2022	18(O) 7	12/14
282	60 KTA POLYPROPYLENE PROJECT - [N16000429]GAIL,UTTAR PRADESH ,	03/2019	910.56 -	910.56	141.31	04/2024 -	04/2024	0(O) -	10/17
283	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	106.27	02/2020 06/2021	10/2022	32(O) 2	19/26
284	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	983.90	12/2020 12/2021	06/2023	30(O) 0	13/24
285	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	207.36	135.65	04/2020 10/2021	10/2022	30(O) 3	19/26
286	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 3,696.00	3,696.00	2,441.32	09/2022 -	09/2022	0(O) -	3/3
287	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	174.36	03/2031 -	08/2031	5(O) -	24/50
288	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	177.06	01/2023 -	01/2023	0(O) -	4/6
	Total		3,77,065.98 -	3,95,519.73	1,27,100.07				1096/1607
	POWER								

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
289	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	15,300.08	09/2010 08/2023	08/2023	155(O) 0	0/0
290	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	19,738.00	10/2011 07/2023	07/2023	141(O) 0	34/48
291	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	10,566.00	9,014.00	07/2012 -	-	-	25/25
292	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 19,413.00	17,304.00	16,748.00	05/2018 -	03/2022	46(O) -	44/45
293	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	03/2019	10,439.09 -	10,439.09	4,677.91	01/2024 -	01/2024	0(O) -	16/27
294	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]PGCIL,BIHAR , EPC	05/2021	179.29 -	179.29	5.66	04/2023 -	04/2023	0(O) -	0/0
295	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	580.89	05/2017 -	03/2022	58(O) -	4/9
296	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT , EPC	08/2020	261.80 -	293.03	118.68	10/2021 -	10/2022	12(O) -	0/0
297	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT , EPC	01/2021	842.27 -	842.27	93.92	07/2022 -	07/2022	0(O) -	0/0
298	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI MESANKA AND RADHANPUR) - [N18000296]NTPC,GUJARAT , EPC	05/2021	674.92 -	674.92	76.91	09/2022 -	09/2022	0(O) -	0/0
299	Bagodara Solar Power Project - [N18000297]SJVN,GUJARAT ,	05/2021	296.20 -	296.20	.43	10/2022 -	10/2022	0(O) -	0/5
300	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL,GUJARAT ,	10/2019	1,031.00 -	1,031.00	654.77	08/2021 -	08/2021	-	0/0
301	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL,HARYANA ,	01/2019	267.33 -	267.33	31.72	03/2022 -	03/2022	0(O) -	0/0
302	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	9,558.69	09/2009 03/2023	03/2023	162(O) 0	5/5
303	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	622.39	01/2026 -	01/2026	0(O) -	0/10
304	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN,HIMACHAL PRADESH ,	10/2020	687.97 -	687.97	215.23	11/2025 -	11/2025	0(O) -	2/11
305	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	2,169.01	04/2020 07/2025	07/2025	63(O) 0	0/0
306	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR ,	03/2019	4,287.59 -	4,287.59	670.22	- 08/2024	07/2025	- 0	0/0
307	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 17,007.00	17,007.00	12,634.00	06/2019 10/2022	01/2024	55(O) 0	30/43
308	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	5,289.25	3,776.81	10/2017 04/2019	-	-	0/0
309	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND ,	11/2017	18,668.00 -	17,667.00	5,021.00	03/2023 -	02/2025	23(O) -	3/21
310	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	123.49	06/2021 01/2022	07/2022	13(O) 0	0/0
311	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	663.84	09/2020 -	08/2022	23(O) -	18/25

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
312	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 -	1,311.05	200.27	06/2006 -	-	-	0/0
313	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 -	13,199.00	12,394.95	08/2013 -	03/2018	-	23/26
314	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	546.36	480.89	11/2016 -	03/2022	64(O) -	10/12
315	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	90.97	03/2018 -	03/2022	48(O) -	0/0
316	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	205.65	02/2019 -	04/2022	38(O) -	0/0
317	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	159.02	06/2019 -	03/2022	33(O) -	0/0
318	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	251.70	12/2019 -	04/2022	28(O) -	0/0
319	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,129.32	3,182.67	12/2018 -	03/2024	63(O) -	0/0
320	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,700.00	3,522.04	12/2018 -	01/2024	61(O) -	0/0
321	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	04/2022	21(O) -	0/0
322	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	2,635.55	1,832.15	02/2020 -	04/2023	38(O) -	0/0
323	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	262.29	05/2020 -	02/2022	21(O) -	0/0
324	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE ,	02/2019	572.98 -	572.98	.00	12/2020 -	12/2020	-	0/0
325	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS - [N18000309]PGCIL,MULTI STATE ,	11/2018	496.11 -	496.11	.00	06/2020 -	03/2022	21(O) -	0/0
326	WESTERN REGION SYSTEM STRENGTHENING - XX - [N18000310]PGCIL,MULTI STATE ,	07/2019	226.98 -	226.98	.00	08/2021 -	02/2022	6(O) -	0/0
327	SOUTHERN REGION SYSTEM STRENGTHENING - XXV - [N18000311]PGCIL,MULTI STATE ,	07/2019	154.72 -	154.72	.00	07/2021 -	02/2022	7(O) -	0/0
328	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE ,	09/2015	167.31 -	167.31	.00	12/2017 -	03/2022	51(O) -	0/0
329	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE ,	07/2020	239.89 -	239.89	.00	06/2021 -	03/2022	9(O) -	0/0
330	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]PGCIL,MULTI STATE ,	05/2021	576.42 -	576.42	.00	03/2023 -	03/2023	0(O) -	0/0
331	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE ,	11/2018	241.38 -	241.38	.00	11/2021 -	05/2022	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
332	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII - [N18000318]PGCIL,MULTI STATE ,	09/2018	221.36 -	221.36	.00	03/2021 -	02/2022	11(O) -	0/0
333	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 2,311.80	2,426.00	2,027.32	12/2018 03/2022	03/2022	39(O) 1	9/10
334	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	1,114.48	09/2021 08/2022	03/2022	6(O) -5	0/0
335	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	910.29	09/2021 10/2022	10/2022	13(O) 0	0/0
336	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	609.51	03/2021 12/2021	03/2022	12(O) 1	0/0
337	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	1,362.64	09/2021 -	03/2022	6(O) -	0/0
338	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN , EPC	01/2021	382.22 -	382.22	8.24	03/2022 -	10/2022	7(O) -	0/0
339	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN , EPC	01/2021	1,221.73 -	1,221.73	140.11	07/2022 -	07/2022	0(O) -	0/0
340	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN , EPC	02/2021	599.99 -	599.99	71.06	07/2022 -	07/2022	0(O) -	0/0
341	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN ,	05/2021	1,184.88 -	1,184.88	12.83	09/2022 -	09/2022	0(O) -	0/0
342	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN ,	03/2021	353.85 -	353.85	22.91	12/2022 -	12/2022	0(O) -	0/0
343	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL,RAJASTHAN ,	03/2021	1,340.81 -	1,340.81	151.70	12/2022 -	12/2022	0(O) -	0/0
344	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN ,	06/2021	713.82 -	713.82	130.01	12/2022 -	12/2022	0(O) -	0/0
345	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN ,	06/2021	1,562.00 -	1,562.00	249.63	12/2022 -	12/2022	0(O) -	0/0
346	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN ,	06/2021	1,006.00 -	1,006.00	253.02	12/2022 -	12/2022	0(O) -	0/0
347	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN - [N18000312]PGCIL,RAJASTHAN ,	08/2019	2,578.47 -	2,578.47	.00	12/2020 -	02/2022	14(O) -	0/0
348	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG) FATEHGARH-II & BHADLA - [N18000314]PGCIL,RAJASTHAN , PPP (BOT)	01/2020	562.86 -	562.86	.00	01/2021 -	03/2022	14(O) -	0/0
349	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	219.66	169.82	07/2019 -	08/2022	37(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
350	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	948.04	09/2021 -	08/2022	11(O) -	0/0
351	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,998.00	9,223.00	11/2020 07/2022	02/2023	27(O) 4	30/35
352	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	442.03	293.40	04/2021 -	05/2022	13(O) -	0/0
353	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	3,654.43	09/2023 -	08/2024	11(O) -	3/13
354	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	524.83	400.95	09/2021 -	03/2022	6(O) -	0/0
355	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	852.90	596.05	09/2021 -	05/2022	8(O) -	0/0
356	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,803.19	612.20	09/2021 -	10/2022	13(O) -	0/0
357	PARASAN SOLAR POWER PROJECT - [N18000298]SJVN,UTTAR PRADESH ,	08/2021	313.58 -	313.58	298.99	12/2022 -	12/2022	0(O) -	0/5
358	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 -	4,825.60	4,409.29	02/2016 -	06/2023	88(O) -	24/34
359	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	5,247.00	03/2013 12/2021	12/2024	141(O) 3	8/15
360	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 3,860.35	3,860.35	2,416.30	06/2013 06/2025	06/2025	144(O) 6	10/25
361	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,527.00	149.93	08/2017 -	-	-	0/15
362	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022	6(O) -	14/32
363	RAMMAM-III HEP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,803.00	754.00	09/2019 12/2024	07/2025	70(O) 7	6/10
364	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 633.80	679.00	513.91	11/2018 06/2022	06/2022	43(O) 3	8/20
	Total		1,96,489.83 -	2,60,007.47	1,65,748.86				326/526
	<u>HEAVY INDUSTRY</u>								
365	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,727.30	3,526.63	09/2011 -	-	-	24/25
	Total		1,718.00 -	3,727.30	3,526.63				24/25
	<u>HEALTH AND FAMILY WELFARE</u>								
366	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	280.00	273.40	03/2019 -	02/2021	-	0/0
367	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	538.47	- -	03/2022	- -	0/0
368	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
369	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 890.14	860.00	446.44	05/2021 -	-	-	0/0
370	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	586.50	586.50	11/2013 -	09/2021	-	0/0
371	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	249.24	05/2017 -	06/2021	-	2/2
372	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
373	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	205.00	191.36	- -	01/2022	-	0/0
374	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	245.78	- -	05/2021	-	0/0
375	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	586.96	586.96	03/2018 -	04/2020	-	2/2
376	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	1,089.38	09/2021 -	06/2022	9(O) -	2/4
377	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
378	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	439.65	09/2023 -	09/2023	0(O) -	0/0
379	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	232.40	09/2025 -	05/2024	-16(O) -	0/0
380	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD FOR HEALTH,KERALA ,	09/2017	150.29 -	150.29	74.24	03/2020 -	12/2021	-	2/7
381	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	259.46	03/2019 -	01/2021	-	0/0
382	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	554.43	- -	12/2021	-	0/0
383	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	274.40	05/2018 -	06/2022	49(O) -	0/0
384	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19(O) -	0/33
385	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	177.21	02/2018 -	04/2021	-	1/1
386	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	635.00	557.97	06/2020 -	-	-	0/0
387	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA ,	10/2016	209.84 -	209.84	202.48	03/2020 -	05/2021	-	1/5
388	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	284.67	279.53	- -	05/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
389	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	760.00	604.15	04/2020 -	-	-	0/0
390	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC, WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	01/2021	-	3/3
391	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	12/2021	-	0/0
392	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	321.31	03/2019 -	12/2021	-	0/0
393	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL ,	04/2018	651.99 -	651.99	609.49	-	12/2021	-	0/0
	Total		13,696.26 -	14,162.35	9,693.60				18/62
	<u>RAILWAYS</u>								
394	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027	216(O) -	0/0
395	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022	27(O) -	0/0
396	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,495.93	03/2022 -	03/2025	36(O) -	0/0
397	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	3,683.68	12/2023 -	12/2023	0(O) -	0/0
398	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]JECOR, ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	835.30	03/2022 03/2026	03/2026	48(O) 0	0/0
399	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019 -	-	-	0/0
400	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR, ASSAM ,	09/2006	385.20 -	1,145.79	937.36	03/2019 -	03/2024	60(O) -	0/0
401	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM ,	04/2015	2,232.32 -	2,950.00	1,986.82	03/2022 -	03/2023	12(O) -	0/0
402	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM ,	04/2015	870.96 -	1,873.21	1,646.66	03/2021 -	03/2022	12(O) -	0/0
403	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]JECR, BIHAR ,	04/1997	324.73 967.29	1,090.00	1,093.59	03/2012 -	06/2023	135(O) -	0/0
404	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]JECR, BIHAR ,	04/1997	162.87 614.45	614.45	353.25	-	03/2025	-	0/0
405	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]JECR, BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,610.87	-	12/2024	-	0/0
406	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR, BIHAR ,	09/2006	532.87 -	2,145.00	1,108.94	03/2019 -	03/2024	60(O) -	0/0
407	BIHTA-AURANGABAD (NL) - [N22000170]JECR, BIHAR ,	04/2008	326.20 -	2,995.01	2.55	-	03/2024	-	0/0
408	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECR, BIHAR ,	04/1999	325.00 735.20	735.20	392.88	-	12/2024	-	0/0
409	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]JECR, BIHAR ,	04/2006	378.56 -	1,893.55	386.78	-	03/2023	-	0/0
410	ARARIA-SUPAUL (NL) - [N22000177]JECR, BIHAR ,	04/2008	1,605.17 1,605.17	1,605.17	159.03	-	12/2025	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
411	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	1,536.32	- -	03/2024	- -	0/0
412	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	57(O) -	0/0
413	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 519.33	519.33	320.25	- -	12/2024	- -	0/0
414	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	1,059.76	03/2020 -	05/2023	38(O) -	0/1
415	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	581.48	03/2020 -	03/2023	36(O) -	1/1
416	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 1,215.54	1,215.54	585.85	03/2021 -	12/2024	45(O) -	0/0
417	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 1,185.73	1,185.73	452.12	03/2021 -	03/2024	36(O) -	0/0
418	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 1,483.14	1,483.14	1,469.46	- -	03/2024	- -	0/0
419	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	1,036.36	03/2020 03/2023	03/2024	48(O) 12	1/1
420	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,367.10	03/2020 -	06/2022	27(O) -	0/0
421	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 2,135.34	2,135.34	833.36	03/2021 12/2023	12/2023	33(O) 0	0/1
422	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	1,078.79	03/2022 -	09/2023	18(O) -	0/1
423	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,800.17	09/2018 -	06/2022	45(O) -	0/1
424	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	371.86	03/2020 06/2022	06/2022	27(O) 0	1/2
425	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	118.38	- -	03/2024	- -	0/0
426	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	167.23	- -	09/2023	- -	0/0
427	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024	48(O) -	0/0
428	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	139(O) -	0/0
429	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	923.28	995.52	03/2021 -	05/2022	14(O) -	0/0
430	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	294.10	- -	10/2025	- -	0/0
431	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025	72(O) -	0/0
432	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
433	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022	21(O) -	0/0
434	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,016.39	1,056.11	808.35	03/2021 -	12/2022	21(O) -	0/0
435	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
436	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	528.49	123.75	-	-	-	0/0
437	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT ,	04/2017	692.25 -	742.88	2.26	03/2020 -	03/2024	48(O) -	0/0
438	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT ,	04/2018	537.31 -	537.31	.64	03/2024 -	12/2024	9(O) -	0/0
439	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	760.84	12/2011 -	-	-	0/0
440	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	2,006.69	12/2026 -	03/2025	-21(O) -	0/0
441	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	37,012.26	27,846.00	11/2002 04/2023	04/2023	245(O) 4	0/0
442	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,650.00	3,679.49	-	07/2022	-	0/0
443	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	981.50	-	03/2024	-	0/0
444	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	1,153.09	03/2021 -	12/2023	33(O) -	0/0
445	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND ,	04/2018	428.65 -	472.50	1.62	06/2022 -	12/2025	42(O) -	0/0
446	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND ,	04/2018	390.39 -	511.75	149.63	12/2021 -	01/2023	13(O) -	0/0
447	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	5,174.30	158.11	-	03/2028	-	0/0
448	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2028	312(O) -	0/0
449	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	2,000.97	83.08	-	03/2025	-	0/0
450	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	1,530.09	326.02	03/2016 -	12/2026	129(O) -	1/1
451	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.43	.00	-	03/2028	-	0/0
452	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2026	120(O) -	0/0
453	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	-	03/2025	-	0/0
454	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,300.00	2,564.14	03/2023 -	03/2023	0(O) -	0/1
455	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	401.14	12/2018 -	06/2025	78(O) -	0/0
456	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	367.77	.00	-	03/2027	-	0/0
457	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	37.12	03/2016 -	03/2024	96(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
458	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,954.21	1,238.40	03/2020 -	12/2022	33(O) -	1/5
459	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	758.36	674.14	03/2020 -	02/2022	23(O) -	2/2
460	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 -	817.23	495.18	03/2017 -	03/2026	108(O) -	0/0
461	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	264.51	- -	-	-	0/0
462	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	709.69	256.71	- -	03/2025	- -	0/0
463	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	448.10	268.74	- -	03/2025	- -	0/0
464	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	942.65	- -	03/2024	- -	0/0
465	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,339.00	.83	- -	03/2025	- -	0/0
466	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
467	RAMGANJMUUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,439.82	03/2021 -	03/2024	36(O) -	4/15
468	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,839.02	6,383.82	2,404.99	03/2022 -	03/2026	48(O) -	0/0
469	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 2,445.30	2,445.30	1,392.72	03/2020 -	10/2024	55(O) -	1/1
470	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022	21(O) -	0/0
471	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15(O) -	4/17
472	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,247.64	561.88	03/2022 -	12/2023	21(O) -	1/1
473	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022	37(O) -	0/1
474	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.94	795.59	12/2021 12/2023	12/2023	24(O) 0	0/0
475	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 -	603.69	358.78	06/2020 -	03/2023	33(O) -	0/0
476	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH ,	04/2017	495.18 -	495.18	.63	03/2022 -	03/2026	48(O) -	0/0
477	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022	219(O) -	0/0
478	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24(O) -	0/0
479	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	-	-	0/0
480	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023	0(O) -	0/0
481	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24(O) -	0/0
482	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
483	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
484	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
485	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.49	.00	03/2024 -	-	-	0/0
486	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12(O) -	0/0
487	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12(O) -	0/0
488	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,764.97	03/2024 -	03/2023	-12(O) -	0/0
489	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023	0(O) -	0/0
490	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24(O) -	0/0
491	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12(O) -	0/0
492	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022	24(O) -	0/0
493	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
494	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	3,176.60	1,576.19	03/2023 12/2023	12/2023	9(O) 0	0/1
495	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	311.36	.00	- -	-	-	0/0
496	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	393.62	152.98	- -	-	-	0/0
497	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	36(O) -	0/1
498	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	14,322.00	12,156.19	03/2011 -	12/2023	153(O) -	0/0
499	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 -	4,083.02	265.38	03/2021 -	-	-	0/0
500	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 -	6,527.00	4,766.68	03/2014 -	12/2023	117(O) -	0/0
501	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024	148(O) -	0/0
502	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023	276(O) -	0/0
503	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202(O) -	1/9
504	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	728.92	613.91	01/2019 -	02/2022	37(O) -	0/0
505	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,524.68	1,010.81	03/2022 -	10/2027	67(O) -	0/0
506	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	883.21	03/2022 -	03/2025	36(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
507	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	534.75	03/2022 -	12/2024	33(O) -	0/5
508	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	.00	- -	12/2027	- -	0/0
509	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	2,047.51	586.70	03/2019 -	12/2023	57(O) -	0/0
510	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	749.40	591.35	- -	03/2022	- -	0/0
511	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	76.57	03/2020 -	-	-	0/0
512	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	401.65	338.00	- -	03/2023	-	0/0
513	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	750.00	157.78	03/2020 -	-	-	0/0
514	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,111.88	314.32	03/2019 -	12/2027	105(O) -	0/0
515	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	472.06	03/2022 -	03/2025	36(O) -	0/0
516	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	529.13	- 09/2021	02/2022	- 11	0/0
517	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	622.26	03/2016 -	03/2024	96(O) -	0/0
518	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	204.40	03/2016 -	03/2025	108(O) -	0/0
519	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	508.16	03/2017 -	03/2025	96(O) -	0/0
520	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	333.93	- -	03/2022	-	0/0
521	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	803.75	03/2023 -	03/2024	12(O) -	0/0
522	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	689.83	- -	09/2023	-	0/0
523	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	03/2028	-	0/0
524	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,404.03	1,108.07	- -	12/2025	-	2/2
525	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	713.38	03/2020 -	03/2022	24(O) -	1/1
526	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	347.14	03/2014 -	03/2027	156(O) -	1/1
527	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	418.15	- -	03/2024	-	0/0
528	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	342.53	03/2020 -	10/2022	31(O) -	0/0
529	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,104.00	1,014.52	03/2020 -	02/2022	23(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
530	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 -	1,878.00	1,530.18	03/2019 -	02/2024	59(O) -	0/0
531	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 -	929.86	964.41	03/2019 -	12/2021	-	0/38
532	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 28,181.00	51,219.00	35,951.00	- 06/2022	-	-	0/0
533	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,676.08	03/2021 -	03/2024	36(O) -	0/0
534	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	21,986.54	12/2023 -	12/2023	0(O) -	0/2
535	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 72,785.00	51,101.00	47,476.00	03/2020 06/2022	-	-	0/0
536	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.13	480.97	03/2023 12/2025	12/2025	33(O) 0	0/0
537	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	839.00	839.36	03/2016 -	-	-	0/0
538	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE ,	03/2019	1,866.31 -	1,866.31	350.68	05/2023	12/2023	7(O) -	0/0
539	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,663.00	1,534.31	03/2015	03/2026	132(O) -	0/0
540	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
541	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,791.66	1,729.29	03/2009 -	12/2024	189(O) -	0/0
542	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022	88(O) -	0/0
543	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022	165(O) 0	1/1
544	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	947.41	06/2021 -	03/2025	45(O) -	0/0
545	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	1,243.24	02/2019 -	03/2022	37(O) -	0/0
546	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	324.59	10/2020 -	03/2024	41(O) -	0/0
547	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	758.80	03/2022 03/2023	03/2024	24(O) 12	0/0
548	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	564.03	03/2022 03/2026	03/2026	48(O) 0	0/0
549	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	209.78	11/2018 -	03/2025	76(O) -	0/0
550	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	734.63	12/2018 -	03/2024	63(O) -	0/0
551	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,312.97	1,155.00	03/2020 -	06/2022	27(O) -	0/0
552	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	2,139.84	12/2024 -	12/2026	24(O) -	0/0
553	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022	25(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
554	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023	48(O) -	0/0
555	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108(O) -	0/0
556	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	775.62	02/2019 -	06/2022	40(O) -	0/0
557	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	322.98	.00	-	-	-	0/0
558	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	435.41	08/2022 -	11/2022	3(O) -	0/0
559	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	8,600.00	2,504.91	12/2015 -	12/2023	96(O) -	0/0
560	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,549.09	715.89	03/2020 -	03/2025	60(O) -	0/0
561	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	774.51	539.14	06/2013 -	12/2022	114(O) -	1/4
562	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	3,081.20	1,726.52	02/2019 -	03/2025	73(O) -	0/0
563	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	3,444.00	241.49	-	12/2025	-	0/0
564	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	839.01	.63	-	03/2030	-	0/0
565	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	591.00	430.16	-	03/2022	-	0/0
566	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	1,137.46	03/2022 -	05/2023	14(O) -	0/0
567	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022	33(O) -	0/0
568	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,373.74	695.73	03/2010 -	03/2025	180(O) -	1/1
569	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	619.35	03/2016 -	04/2022	73(O) -	0/0
570	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	-	-	-	1/1
571	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	661.74	03/2021 12/2022	-	-	3/3
572	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	1,248.22	12/2024 -	12/2024	0(O) -	0/0
573	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	242.28	75.42	03/2022 -	-	-	0/0
574	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	708.73	549.81	03/2020 06/2022	09/2022	30(O) 3	2/3
575	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	-	-	-	0/0
576	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
577	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,824.00	1,518.04	03/2022 -	03/2022	0(O) -	0/0
578	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022	9(O) -	0/0
579	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023	48(O) -	0/0
580	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	1,129.41	03/2023 -	12/2024	21(O) -	0/0
581	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022	18(O) -	0/0
582	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,570.66	03/2020 -	03/2024	48(O) -	0/0
583	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	347.96	03/2019 -	03/2022	36(O) -	0/0
584	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	88.76	04/2016 -	12/2021	-	0/0
585	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
586	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	341.66	.00	04/2017 -	10/2022	66(O) -	0/0
587	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0
588	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
589	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	800.00	164.95	-	12/2023	-	0/0
590	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	345.95	01/2022 -	03/2022	2(O) -	0/0
591	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	493.91	12/2019 -	04/2021	-	0/0
592	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	89.74	03/2023 -	06/2025	27(O) -	0/0
593	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	1,080.53	03/2021 -	06/2023	27(O) -	1/6
594	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	2,601.90	12/2023 -	12/2023	0(O) -	0/0
595	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	24,659.00	6,259.16	12/2024 -	03/2025	3(O) -	0/0
596	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER, WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	912.17	03/2019 12/2009	03/2025	72(O) 0	0/0
597	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
598	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
599	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	3,139.94	03/2016 -	03/2026	120(O) -	0/0
600	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,834.54	1,586.17	03/2016 -	07/2025	112(O) -	0/0
601	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	-	0/0
602	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
603	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	311.86	- -	03/2022	-	0/0
604	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER, WEST BENGAL ,	04/2018	338.00 -	393.83	23.56	06/2022 -	12/2023	18(O) -	0/0
	Total		4,08,405.75 -	6,65,174.44	3,25,319.01				32/131
	SOCIAL JUSTICE								
605	CENTRE FOR DISABILITY SPORTS - [N38000001]CPWD, MADHYA PRADESH , EPC	02/2019	170.99 -	170.99	.00	03/2024 -	03/2024	0(O) -	1/5
	Total		170.99 -	170.99	.00				1/5
	DEPARTMENT OF HIGHER EDUCATION								
606	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD EDUCATION, ANDHRA PRADESH ,	02/2019	186.00 199.00	210.60	206.20	09/2020 -	07/2021	-	7/7
607	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION, ANDHRA PRADESH ,	02/2019	655.34 -	655.34	375.85	06/2020 -	11/2022	29(O) -	0/110
608	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRIC - [N42000007]CPWD EDUCATION, ANDHRA PRADESH ,	09/2019	588.72 -	588.72	142.46	09/2022 -	06/2023	9(O) -	0/0
609	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION, BIHAR ,	02/2016	496.18 496.00	498.99	318.32	06/2017 -	03/2022	57(O) -	2/6
610	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION, BIHAR ,	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26(O) -	3/7
611	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD EDUCATION, CHHATTISGARH ,	03/2020	808.62 -	808.62	318.94	07/2022 -	10/2022	3(O) -	0/0
612	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD EDUCATION, GOA ,	05/2019	303.90 -	303.90	61.00	03/2020 -	02/2023	35(O) -	3/8

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Mile tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
613	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH ,	11/2012	270.83 -	244.00	243.03	11/2014 11/2021	11/2021	-	8/8
614	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022	4(O) 0	0/2
615	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR ,	03/2019	424.93 -	424.93	86.21	07/2022 10/2022	10/2022	3(O) 0	0/14
616	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD EDUCATION,JAMMU AND KASHMIR ,	01/2018	676.00 676.00	676.00	42.51	04/2023 04/2023	04/2023	0(O) 0	0/1
617	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION,JHARKHAND ,	09/2012	171.86 171.86	171.86	144.27	03/2016 03/2022	03/2022	72(O) 0	4/6
618	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	361.47	03/2022 -	10/2022	7(O) -	0/12
619	C/O ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE.SH- RCC MONOLITHIC FOR MEN HOSTEL(S.14) WOMEN HOST - [N42000010]CPWD,KARNATAKA ,	08/2021	316.25 -	316.25	.00	11/2021 -	-	-	0/0
620	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	7/8
621	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	234.20	03/2021 -	02/2023	23(O) -	2/11
622	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA ,	01/2018	223.37 -	223.37	117.64	07/2020 -	12/2021	-	4/14
623	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA ,	09/2013	484.32 429.70	429.70	233.00	09/2014 06/2022	06/2022	93(O) 0	0/0
624	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA ,	01/2019	790.79 -	790.79	294.36	03/2022 -	09/2022	6(O) -	1/5
625	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB ,	01/2018	430.00 -	387.83	241.27	05/2020 -	08/2022	27(O) -	3/5
626	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB ,	10/2019	348.24 -	348.24	35.43	05/2022 -	10/2022	5(O) -	1/8
627	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN ,	12/2016	549.31 559.49	580.00	559.49	07/2019 07/2021	07/2021	-	6/6
628	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL , EPC	03/2020	193.83 -	193.83	77.27	06/2020 -	03/2023	33(O) -	0/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		10,455.86 -	10,390.34	4,422.70				51/252
	<u>HOME AFFAIRS</u>								
629	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI ,	10/2013	1,219.21 -	2,000.00	1,089.05	10/2019 -	06/2022	32(O) -	1/7
630	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI , EPC	06/2019	277.35 -	290.33	46.80	07/2022 -	12/2022	5(O) -	2/6
631	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD FOR MHA,HARYANA , EPC	01/2020	166.98 166.98	166.98	7.84	10/2023 04/2024	04/2024	6(O) 0	0/1
632	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD FOR MHA,UTTAR PRADESH ,	05/2019	199.31 -	199.31	75.31	01/2022 12/2022	12/2022	11(O) 0	0/0
633	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	228.63	173.62	04/2018 -	12/2022	56(O) -	6/7
	Total		2,025.73 -	2,885.25	1,392.62				9/21
	<u>DPIIT</u>								
634	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI ,	11/2017	4,773.00 -	5,178.00	3,062.37	12/2019 -	05/2022	29(O) -	0/0
635	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 -	07/2021	-	0/0
	Total		17,352.09 -	18,990.30	12,636.44				0/0
	<u>DONER</u>								
636	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL FOR DONER,MEGHALAYA ,	04/2014	151.33 -	151.33	149.33	09/2017 -	-	-	12/15
	Total		151.33 -	151.33	149.33				12/15
	<u>RENEWABLE ENERGY</u>								
637	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI ,	10/2017	271.90 -	365.00	282.96	11/2019 -	-	-	0/0
	Total		271.90 -	365.00	282.96				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
638	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	63.74	10/2018 -	03/2023	53(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
639	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	135.48	12/2017 -	03/2022	51(O) -	2/4
640	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	202.59	04/2017 -	10/2021	-	3/4
641	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	77.75	10/2018 -	12/2022	50(O) -	1/4
642	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	75.22	10/2018 -	06/2022	44(O) -	2/4
643	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	148.90	11/2019 -	10/2021	-	0/0
644	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	214.90	11/2019 -	06/2021	-	0/0
645	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	260.07	07/2019 -	-	-	0/4
646	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
647	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,287.35	05/2014 -	-	-	0/0
648	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
649	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	243.29	10/2015 06/2021	-	-	4/4
650	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	.00	02/2017 -	-	-	0/0
651	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	970.99	03/2020 -	-	-	0/0
652	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	1,247.69	- -	-	-	0/0
653	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
654	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,389.19	- -	10/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
655	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022	14(O) -	4/4
656	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,666.08	- -	09/2021	-	0/0
657	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	661.98	- -	02/2021	-	0/0
658	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
659	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	464.83	- -	-	-	0/0
660	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	353.43	334.89	12/2015 01/2021	-	-	3/3
661	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 309.37	309.37	270.19	02/2017 02/2022	02/2022	60(O) 0	3/4
662	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 290.15	290.15	164.56	05/2017 04/2022	04/2022	59(O) 0	3/4
663	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 319.28	319.28	222.37	08/2017 05/2022	05/2022	57(O) 0	3/4
664	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 373.05	373.05	329.89	11/2017 -	05/2022	54(O) -	3/4
665	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 202.83	202.83	148.81	08/2018 07/2022	-	-	3/4
666	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 234.73	234.73	221.79	08/2018 08/2022	-	-	3/4
667	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 504.00	504.19	479.00	11/2018 02/2022	-	-	3/4
668	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	609.49	05/2016 10/2022	10/2022	77(O) 0	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
669	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 386.99	386.99	350.05	08/2018 02/2022	-	-	3/4
670	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	328.03	01/2017 06/2022	06/2022	65(O) 0	3/4
671	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 316.06	316.06	214.31	05/2016 06/2022	06/2022	73(O) 0	3/4
672	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	257.45	08/2016 05/2022	07/2021	-	3/4
673	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	365.54	09/2016 05/2022	05/2022	68(O) 0	3/4
674	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	335.69	08/2017 -	06/2022	58(O) -	3/4
675	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 263.45	263.45	122.71	09/2017 05/2022	11/2022	62(O) 0	1/4
676	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 686.13	686.13	438.61	01/2018 10/2022	-	-	2/4
677	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 570.98	570.98	346.85	01/2020 08/2021	-	-	0/0
678	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 655.64	668.45	546.69	02/2019 04/2021	-	-	0/0
679	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 1,240.13	1,321.60	405.54	02/2021 04/2021	-	-	0/0
680	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	111.79	02/2021 -	-	-	0/0
681	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH , EPC	03/2020	207.79 -	207.79	117.71	03/2021 -	04/2022	13(O) -	2/4
682	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH , EPC	06/2020	221.40 -	221.40	28.78	05/2021 -	12/2022	19(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
683	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH , EPC	08/2020	222.61 -	222.61	11.71	03/2021 -	03/2023	24(O) -	0/4
684	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	390.07	06/2018 -	03/2021	-	3/3
685	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	217.41	- -	03/2022	- -	3/4
686	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	197.27	04/2017 -	03/2022	59(O) -	3/4
687	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	158.08	04/2017 -	03/2022	59(O) -	2/4
688	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	159.83	04/2017 -	03/2022	59(O) -	2/4
689	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	61.40	04/2017 -	02/2021	-	1/4
690	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	159.32	04/2017 -	03/2022	59(O) -	3/4
691	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0
692	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	128.67	- -	12/2022	- -	3/4
693	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	520.71	- -	03/2022	- -	2/4
694	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	360.28	- -	03/2022	- -	0/0
695	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	129.11	- -	12/2022	- -	3/4
696	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	101.99	- -	04/2022	- -	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
697	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	87.87	- 04/2022	04/2022	- 0	3/4
698	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	145.76	- -	10/2021	-	4/4
699	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,251.08	- -	12/2021	-	0/0
700	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	229.09	- -	02/2022	-	0/0
701	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	30.42	04/2022 -	04/2022	0(O) -	0/4
702	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	31.06	05/2022 -	05/2022	0(O) -	0/4
703	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	108.53	03/2027 -	02/2023	-49(O) -	0/0
704	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	212.53	03/2027 -	-	-	0/0
705	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	79.40	03/2027 -	-	-	0/0
706	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	183.06	03/2027 -	-	-	0/0
707	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	127.93	03/2027 -	-	-	0/0
708	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	252.02	03/2027 -	-	-	0/0
709	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	168.44	03/2027 -	-	-	0/0
710	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	73.42	03/2027 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
711	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	71.20	03/2027 -	-	-	0/0
712	TADADEGE - HENKAR - [N24001315]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	550.45 -	550.45	13.03	03/2023 -	03/2023	0(O) -	0/4
713	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	445.96 -	445.96	.00	04/2023 -	04/2023	0(O) -	0/4
714	DOGINALA - GAU - [N24001320]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	242.30 -	242.30	9.31	09/2022 -	09/2022	0(O) -	0/4
715	DEMBUEN - BRUNI - [N24001321]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	606.63 -	606.63	.00	03/2023 -	03/2023	0(O) -	0/4
716	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH,ARUNACHAL PRADESH , EPC	02/2021	588.09 -	588.09	108.20	03/2024 -	03/2024	0(O) -	0/0
717	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]MoRTH,ARUNACHAL PRADESH , EPC	01/2020	358.26 -	358.26	49.89	02/2024 -	02/2024	0(O) -	0/0
718	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	437.60 -	437.60	7.78	03/2027 -	-	-	0/0
719	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	496.47 -	496.47	8.93	03/2027 -	-	-	0/0
720	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH , EPC	03/2021	182.55 -	182.55	7.59	03/2027 -	09/2021	-	0/0
721	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390]NHIDCL,ARUNACHAL PRADESH ,	08/2020	228.71 -	228.71	48.24	04/2022 -	04/2022	0(O) -	2/4
722	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	294.04 -	294.04	91.30	04/2022 -	04/2022	0(O) -	2/4
723	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	199.03 -	199.03	59.12	04/2022 -	04/2022	0(O) -	2/4
724	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	184.88 -	184.88	48.06	04/2022 -	04/2022	0(O) -	2/4
725	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	.00	04/2009 -	-	-	0/0
726	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	.00	11/2008 -	-	-	0/0
727	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	.00	11/2008 -	-	-	0/0
728	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	389.26	05/2018 -	03/2022	46(O) -	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
729	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	113.03	06/2018 -	12/2021	-	1/4
730	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	182.43	06/2018 -	12/2021	-	2/4
731	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	169.08	11/2018 -	11/2021	-	4/4
732	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	528.66	11/2018 -	04/2022	41(O) -	3/4
733	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	390.73	368.28	05/2017 06/2022	06/2022	61(O) 1	0/0
734	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	207.71	- -	12/2021	-	3/4
735	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	110.95	12/2018 -	03/2022	39(O) -	2/4
736	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	229.26	01/2016 -	03/2022	74(O) -	3/4
737	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	141.40	01/2016 -	03/2022	74(O) -	2/4
738	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74(O) -	2/3
739	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	302.72	- -	04/2023	- -	2/4
740	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	135.75	09/2021 12/2022	12/2022	15(O) 10	0/0
741	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	155.61	- -	12/2021	-	2/4
742	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	64.22	12/2020 12/2022	-	-	0/0
743	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	45.79	12/2022 -	12/2022	0(O) -	1/4
744	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	27.45	04/2022 -	04/2022	0(O) -	1/4
745	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	71.71	03/2022 -	03/2022	0(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
746	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	50.81	03/2022 -	03/2022	0(O) -	2/4
747	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]NHIDCL,ASSAM , EPC	11/2020	4,997.04 -	4,997.04	624.88	09/2028 -	09/2028	0(O) -	1/4
748	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]NHIDCL,ASSAM , EPC	12/2020	804.00 -	804.00	93.33	08/2023 -	08/2023	0(O) -	1/4
749	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM , EPC	03/2020	261.13 -	261.13	31.46	06/2022 -	06/2022	0(O) -	1/4
750	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM , EPC	03/2020	217.50 -	217.50	34.17	06/2022 -	06/2022	0(O) -	0/4
751	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]NHIDCL,ASSAM , EPC	09/2019	761.54 -	761.54	155.57	05/2023 -	05/2023	0(O) -	2/4
752	DABOKA KATHKATI PACKAGE-2 - [N24001364]NHIDCL,ASSAM , EPC	03/2021	335.88 -	335.88	33.72	01/2024 -	01/2024	0(O) -	1/4
753	DABOKA KATHKATI PACKAGE-4 - [N24001365]NHIDCL,ASSAM , EPC	02/2021	260.07 -	260.07	78.09	12/2023 -	12/2023	0(O) -	2/4
754	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM , EPC	03/2021	288.85 -	288.85	.00	01/2023 -	01/2023	0(O) -	0/4
755	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM , EPC	03/2021	636.42 -	636.42	55.56	12/2022 -	01/2023	1(O) -	0/4
756	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]NHIDCL,ASSAM , EPC	03/2021	286.72 -	286.72	.00	01/2024 -	01/2024	0(O) -	0/4
757	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM , EPC	02/2021	925.47 -	925.47	.06	07/2025 -	07/2025	0(O) -	0/0
758	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	1,199.64	02/2013 -	-	-	3/4
759	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.92	03/2014 -	-	-	0/0
760	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
761	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	506.88	07/2013 -	-	-	2/3
762	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	591.00	578.00	11/2013 -	-	-	0/0
763	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 780.77	780.77	424.27	- 06/2022	06/2022	- 0	0/0
764	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
765	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 567.00	639.58	501.61	04/2019 07/2022	07/2022	39(O) 0	0/0
766	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	846.15	- -	10/2021	-	3/4
767	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	217.73	04/2018 -	-	-	0/0
768	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	550.29	- -	-	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
769	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	296.90	- -	-	-	0/0
770	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,034.54	- -	-	-	3/4
771	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	651.41	04/2018 -	-	-	4/4
772	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 404.10	404.10	345.06	- 06/2022	06/2022	- 0	0/0
773	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 698.82	698.82	709.80	07/2016 06/2022	06/2022	71(O) 0	0/0
774	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 225.06	225.06	168.79	05/2016 06/2022	06/2022	73(O) 0	0/0
775	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 587.41	587.41	537.14	05/2016 03/2022	03/2022	70(O) 0	0/0
776	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 2,138.16	2,138.16	1,241.55	10/2016 03/2022	03/2022	65(O) 0	0/0
777	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	.00	05/2017 -	-	-	0/0
778	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,605.30	12/2016 05/2022	05/2022	65(O) 0	0/0
779	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 736.01	830.31	105.50	03/2020 12/2018	03/2023	36(O) 0	0/0
780	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	-	0/0
781	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 1,161.00	1,168.00	354.24	08/2017 08/2018	10/2023	74(O) 20	0/0
782	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	1,962.50	363.79	- -	-	-	0/0
783	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 644.50	726.99	156.13	- 12/2019	06/2023	- 0	0/0
784	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
785	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	80.68	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
786	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	81.56	- -	-	-	0/0
787	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	97.01	- 03/2022	03/2022	- 0	0/0
788	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	370.19	- -	-	-	0/0
789	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	44.00	12/2020 -	-	-	0/0
790	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
791	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	60.06	11/2020 -	-	-	0/0
792	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR , EPC	10/2019	1,101.99 -	1,101.99	270.71	02/2020 -	-	-	0/4
793	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	252.61	- -	02/2022	-	0/0
794	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
795	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
796	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	1,096.52	518.73	04/2018 -	-	-	0/0
797	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	402.95	- -	03/2021	-	0/0
798	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 -	572.66	288.50	08/2016 -	12/2022	76(O) -	0/0
799	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	290.07	06/2017 -	04/2022	58(O) -	0/0
800	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 544.00	544.00	402.15	09/2016 -	03/2022	66(O) -	0/0
801	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 -	731.50	486.06	10/2016 -	06/2022	68(O) -	0/0
802	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 -	435.61	128.55	07/2016 -	12/2022	77(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
803	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	298.70	01/2018 -	03/2022	50(O) -	0/0
804	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	251.53	03/2015 -	06/2022	87(O) -	0/0
805	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	120.07	05/2019 -	03/2022	34(O) -	0/0
806	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	338.42	11/2017 -	02/2022	51(O) -	0/0
807	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 354.43	298.33	325.55	- 12/2021	03/2022	- 0	0/4
808	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	118.37	- -	12/2021	-	2/4
809	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	244.36	- 02/2019	01/2020	-	3/4
810	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	560.12	- 09/2022	12/2022	- 0	0/0
811	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	400.90	- -	03/2022	-	0/0
812	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	410.10	- -	03/2022	-	0/0
813	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	329.59	05/2020 -	06/2022	25(O) -	1/4
814	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	225.16	12/2019 -	03/2022	27(O) -	1/4
815	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-	-	2/3
816	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 1,066.87	953.88	93.63	07/2013 03/2020	03/2022	104(O) 0	0/0
817	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	439.98	12/2015 -	-	-	3/3
818	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	772.39	- -	-	-	2/2
819	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE- IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	528.22	- -	-	-	2/2
820	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	427.78	- -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
821	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
822	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	311.41	- -	-	-	0/0
823	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	199.86	- -	-	-	0/3
824	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,361.00	461.82	- -	-	-	2/4
825	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	-	3/3
826	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
827	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 -	1,361.00	461.82	- -	-	-	2/4
828	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	2,021.55	- -	-	-	0/0
829	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	564.11	- -	07/2021	-	0/0
830	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
831	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 913.49	913.49	645.24	11/2018 06/2021	07/2022	44(O) 0	3/4
832	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	319.03	11/2018 -	07/2021	-	4/4
833	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 394.44	394.44	188.34	05/2019 -	05/2022	36(O) -	2/4
834	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	455.49	03/2018 -	12/2022	57(O) -	2/4
835	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 255.00	255.00	195.11	06/2021 -	06/2022	12(O) -	3/4
836	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
837	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	991.59 -	507.70	.00	06/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
838	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	.00	07/2018 -	-	-	0/0
839	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 2,408.72	2,408.72	1,577.44	04/2019 -	09/2021	-	0/0
840	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	739.08	- -	12/2020	-	0/0
841	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	214.83	- -	-	-	0/0
842	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	925.96	341.09	- -	02/2018	-	0/0
843	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	922.64	387.49	- -	02/2018	-	0/0
844	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	170.71	- -	-	-	0/0
845	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	191.96	- -	-	-	0/0
846	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MORTH,HARYANA ,	01/2017	247.25 -	247.25	186.63	03/2019 -	10/2022	43(O) -	0/1
847	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 1,118.07	1,118.07	957.15	- 05/2022	05/2022	- 0	3/4
848	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 1,206.48	1,206.48	1,006.03	- 07/2022	07/2022	- 0	3/4
849	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 1,238.29	1,238.29	1,111.87	- 06/2022	06/2022	- 0	3/4
850	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 1,044.32	1,044.32	899.01	- 03/2022	03/2022	- 0	0/4
851	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 1,407.35	1,407.35	1,162.45	- 04/2022	04/2022	- 0	0/4
852	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 986.10	986.10	837.89	- 05/2022	05/2022	- 0	3/4
853	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 1,072.08	1,072.08	956.46	- 05/2022	05/2022	- 0	3/4
854	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 1,173.65	1,173.65	1,070.65	- 05/2022	05/2022	- 0	3/4
855	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
856	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	1,457.82	1,347.64	03/2018 03/2021	-	-	0/0
857	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	-	-	0/0
858	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	905.56	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
859	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,344.55	- -	-	-	0/0
860	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	1,079.89	06/2020 -	09/2021	-	0/0
861	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	1,135.08	802.65	- 11/2022	-	-	0/0
862	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH , EPC	08/2020	272.98 -	272.98	14.07	04/2021 -	-	-	0/0
863	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH , EPC	08/2020	242.80 -	242.80	22.78	03/2021 -	-	-	0/0
864	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH , EPC	08/2020	349.20 -	349.20	110.47	04/2021 -	-	-	0/0
865	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH , EPC	02/2021	345.89 -	345.89	27.32	09/2021 -	-	-	0/0
866	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020	-	0/0
867	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	-	0/0
868	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,654.58	07/2013 -	-	-	0/0
869	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,933.43	06/2014 -	09/2022	99(O) -	0/0
870	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	1,158.40	06/2019 -	-	-	0/0
871	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,763.58	12/2018 -	-	-	0/0
872	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,339.00	1,058.70	- -	01/2021	-	2/3
873	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	246.27	08/2018 -	05/2022	45(O) -	2/4
874	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	120.10	11/2018 -	08/2022	45(O) -	1/4
875	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	92.24	07/2019 -	12/2022	41(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
876	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023	0(O) -	2/4
877	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	439.59	09/2026 -	09/2026	0(O) -	0/6
878	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	29.96	04/2022 -	04/2022	0(O) -	1/4
879	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	25.14	04/2022 -	04/2022	0(O) -	1/4
880	KHELLANI-KHANABAL PKG-1 - [N24001323]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	486.45 -	486.45	78.46	09/2022 -	09/2022	0(O) -	1/4
881	KHELLANI-KHANABAL PKG-6 - [N24001324]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	285.28 -	285.28	36.42	09/2022 -	09/2022	0(O) -	1/4
882	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	398.51 -	398.51	11.84	12/2022 -	12/2022	0(O) -	0/4
883	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	260.40 -	260.40	.00	12/2022 -	12/2022	0(O) -	0/4
884	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	512.43 -	512.43	16.50	02/2023 -	02/2023	0(O) -	0/0
885	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	859.67 -	859.67	9.03	08/2023 -	08/2023	0(O) -	0/0
886	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR , EPC	07/2021	497.09 -	497.09	10.16	02/2023 -	02/2023	0(O) -	0/0
887	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	431.28 -	431.28	40.41	03/2023 -	03/2023	0(O) -	0/0
888	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	486.00	406.73	-	-	-	0/0
889	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	355.24	322.26	08/2018 -	-	-	0/0
890	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	123.65	-	-	-	0/0
891	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	950.49	537.17	-	-	-	0/0
892	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- 02/2023	02/2023	- 0	0/0
893	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	109.08	09/2021 -	09/2021	-	0/4
894	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 1,046.56	946.00	818.53	06/2018 07/2022	07/2022	49(O) 0	3/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
895	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	122.21	11/2015 -	-	-	0/0
896	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	541.35	09/2017 -	09/2019	-	0/0
897	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 2,639.00	1,655.01	1,867.51	08/2016 03/2023	03/2023	79(O) 27	0/0
898	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,311.10	08/2018 -	-	-	0/0
899	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	435.62	03/2019 -	03/2022	36(O) -	0/0
900	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 1,418.78	1,418.78	36.30	03/2019 10/2021	10/2021	-	0/0
901	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	1,232.91	04/2020 -	12/2020	-	0/0
902	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	348.00	03/2019 -	06/2023	51(O) -	0/0
903	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	1,108.00	1,482.29	08/2019 -	-	-	0/0
904	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	-	0/0
905	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-	-	0/0
906	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	171.98	- -	-	-	0/0
907	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,442.06	- -	11/2021	-	0/0
908	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,547.20	- -	-	-	0/0
909	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	264.34	187.00	09/2017 -	-	-	0/0
910	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	172.75	02/2017 -	-	-	0/0
911	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	79.74	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
912	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	122.86	07/2018 -	-	-	0/0
913	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	111.52	10/2018 -	-	-	0/0
914	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	318.28	234.82	01/2019 -	-	-	0/0
915	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	386.41	351.36	10/2018 -	-	-	0/0
916	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	239.82	02/2017 -	-	-	0/0
917	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	303.49	03/2017 -	-	-	0/0
918	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	228.23	03/2017 -	-	-	0/0
919	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	127.96	01/2016 -	-	-	0/0
920	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	86.09	05/2018 -	-	-	0/0
921	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	226.46	08/2017 -	-	-	0/0
922	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 187.61	157.32	.95	05/2019 -	-	-	0/0
923	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA , EPC	01/2017	264.34 -	264.34	187.00	09/2017 -	-	-	0/0
924	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA , EPC	03/2019	423.15 -	423.15	159.07	12/2019 12/2022	12/2022	36(O) 0	0/0
925	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	.00	08/2012 -	-	-	0/0
926	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	902.51	- 01/2020	01/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
927	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	600.78	06/2018 12/2021	05/2022	47(O) 2	0/0
928	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,300.00	971.90	09/2017 12/2021	05/2022	56(O) 0	0/0
929	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
930	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA , EPC	02/2017	294.28 -	294.26	184.57	08/2017 -	-	-	0/0
931	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA , EPC	02/2017	380.76 -	380.76	263.70	09/2017 -	-	-	0/0
932	KARGIL-ZANSKR PACKAGE-5 - [N24001330]NHIDCL,LADAKH , EPC	08/2020	169.79 -	169.79	48.49	12/2023 -	12/2023	0(O) -	1/4
933	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH , EPC	03/2021	384.23 -	384.23	10.11	01/2023 -	01/2023	0(O) -	0/4
934	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH , EPC	03/2021	404.89 -	404.89	1.98	01/2023 -	01/2023	0(O) -	0/4
935	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH , EPC	08/2020	381.01 -	381.01	8.23	01/2023 -	01/2023	0(O) -	0/4
936	KARGIL-ZANSKR PACKAGE-6 - [N24001346]NHIDCL,LADAKH , EPC	01/2021	239.81 -	239.81	36.62	05/2024 -	05/2024	0(O) -	1/4
937	KARGIL-ZANSKR PACKAGE-7 - [N24001347]NHIDCL,LADAKH , EPC	01/2021	308.86 -	308.86	38.81	06/2024 -	06/2024	0(O) -	1/4
938	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL,LADAKH , EPC	03/2021	398.37 -	398.37	9.04	01/2023 -	01/2023	0(O) -	0/4
939	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
940	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
941	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	306.63	- -	03/2022	- -	0/0
942	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	392.42	04/2015 -	-	-	0/0
943	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	686.13	669.94	- -	-	-	0/0
944	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	691.38	669.35	- -	-	-	0/0
945	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	464.44	01/2020 -	03/2022	26(O) -	0/0
946	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	927.73	780.19	02/2020 -	01/2022	-	0/0
947	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	867.83	- -	-	-	0/0
948	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	742.47	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
949	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	414.81	08/2017 -	12/2022	64(O) -	0/0
950	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	193.99	01/2019 -	-	-	4/4
951	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	485.68	10/2017 -	-	-	4/4
952	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	215.49	09/2017 -	-	-	4/4
953	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	727.78	09/2017 -	12/2021	-	4/4
954	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	352.62	- -	03/2022	- -	4/4
955	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	452.13	- -	-	-	0/0
956	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	137.52	03/2018 -	03/2022	48(O) -	0/0
957	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	174.90	154.26	08/2018 -	03/2022	43(O) -	0/0
958	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	67.54	03/2018 -	04/2022	49(O) -	0/0
959	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	132.76	02/2018 -	03/2022	49(O) -	0/0
960	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	136.22	03/2017 -	03/2022	60(O) -	0/0
961	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	82.99	03/2018 -	06/2022	51(O) -	0/0
962	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	182.97	08/2018 -	03/2022	43(O) -	0/0
963	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	178.31	03/2018 -	03/2022	48(O) -	0/0
964	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	219.86	07/2018 -	02/2022	43(O) -	0/0
965	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	187.73	02/2018 -	03/2022	49(O) -	0/0
966	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	231.61	03/2018 -	03/2022	48(O) -	0/0
967	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	238.66	09/2019 -	12/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
968	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	635.00	07/2018 -	03/2022	44(O) -	0/0
969	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	949.54	807.22	06/2019 -	03/2022	33(O) -	0/0
970	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	324.22	06/2019 -	-	-	0/4
971	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022	48(O) -	0/0
972	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	157.77	03/2021 -	03/2022	12(O) -	0/0
973	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	557.00	- -	06/2022	- -	2/3
974	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	470.00	- -	11/2022	- -	2/4
975	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	897.00	- -	05/2022	- -	3/4
976	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	671.00	- -	10/2022	- -	2/4
977	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	845.00	12/2019 -	06/2022	30(O) -	2/3
978	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	635.00	03/2020 -	08/2022	29(O) -	2/3
979	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	673.00	05/2020 -	08/2022	27(O) -	2/3
980	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	737.00	03/2020 -	08/2022	29(O) -	2/3
981	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	716.00 -	716.00	59.57	07/2021 -	-	-	0/0
982	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,701.66	03/2013 -	04/2022	109(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
983	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
984	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	106.56	- -	06/2019	-	0/4
985	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	303.72	- -	-	-	3/4
986	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	112.51	- -	09/2022	-	0/0
987	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 414.00	414.00	410.01	05/2018 11/2020	11/2020	-	1/1
988	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022	46(O) -	0/0
989	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022	49(O) -	0/1
990	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	244.16	03/2019 06/2022	06/2022	39(O) 0	0/0
991	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	489.00	05/2018 -	06/2021	-	0/1
992	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0
993	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	868.72	11/2016 -	-	-	0/0
994	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	309.98	07/2019 -	03/2023	44(O) -	0/0
995	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	319.05	07/2019 08/2023	08/2023	49(O) 20	0/0
996	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA ,	03/2016	1,142.62 1,907.03	1,142.62	978.04	- -	07/2021	-	0/0
997	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	334.55	- -	03/2023	-	0/0
998	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	1,203.21	- 12/2021	05/2022	- 5	3/4
999	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	529.08	- 01/2022	04/2022	- 0	2/4
1000	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	206.24	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1001	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	171.45	03/2019 -	-	-	0/0
1002	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	359.60	340.48	- -	05/2017	-	3/4
1003	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	.00	02/2020 03/2022	03/2022	25(O) 0	0/0
1004	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 -	-	-	0/0
1005	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 07/2022	07/2024	52(O) 0	0/0
1006	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	.00	03/2020 01/2022	01/2022	-	0/3
1007	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	.00	03/2020 01/2022	01/2022	-	3/3
1008	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	-	0/0
1009	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	03/2022	24(O) -	0/0
1010	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	.00	03/2020 01/2022	-	-	0/3
1011	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	448.18	495.92	- -	09/2021	-	0/0
1012	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	595.00	- -	-	-	2/3
1013	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	252.05	- 02/2022	02/2022	- 0	0/0
1014	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	237.47	- 02/2022	02/2022	- 1	0/0
1015	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 1,182.87	1,182.87	69.25	- -	07/2021	-	0/0
1016	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	748.98	- -	-	-	0/0
1017	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	195.79	07/2019 -	09/2022	38(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1018	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	109.24	06/2019 -	09/2022	39(O) -	0/4
1019	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	220.54	06/2019 -	11/2020	-	0/4
1020	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	160.15	05/2019 -	09/2019	-	0/0
1021	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	314.20	05/2019 -	11/2020	-	0/4
1022	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	03/2020	-	0/4
1023	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	401.46	06/2019 -	01/2020	-	0/4
1024	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	243.68	06/2019 -	03/2022	33(O) -	0/0
1025	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	11/2019	-	0/0
1026	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	234.67	06/2019 -	12/2020	-	0/0
1027	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	12/2019	-	0/0
1028	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	154.69	06/2019 -	09/2020	-	3/4
1029	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	274.75	06/2019 -	12/2019	-	0/0
1030	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	265.78	06/2019 -	01/2020	-	0/4
1031	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	289.79	06/2019 -	02/2020	-	3/4
1032	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	73.08	09/2019 -	12/2022	39(O) -	1/4
1033	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	261.86	06/2019 -	12/2020	-	0/4
1034	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	354.16	07/2019 -	03/2022	32(O) -	2/4
1035	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	269.58	07/2019 -	02/2022	31(O) -	3/4
1036	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	91.77	05/2019 -	09/2022	40(O) -	1/4
1037	SHAHUPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	59.88	12/2019 -	06/2022	30(O) -	1/4
1038	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	121.71	12/2019 -	03/2022	27(O) -	0/4
1039	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	243.81	08/2019 -	06/2022	34(O) -	2/4
1040	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	321.34	08/2019 -	06/2022	34(O) -	2/4
1041	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	159.32	08/2019 -	03/2022	31(O) -	2/4
1042	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	283.86	05/2019 -	06/2022	37(O) -	0/4
1043	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	308.66	07/2019 -	03/2022	32(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1044	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	269.24	07/2019 -	06/2022	35(O) -	2/4
1045	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	263.13	12/2019 -	06/2021	-	0/4
1046	KAJJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	304.78	07/2019 -	06/2022	35(O) -	2/4
1047	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	12/2022	31(O) -	0/4
1048	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	132.98	-	09/2022	-	0/4
1049	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	326.81	11/2019 -	03/2022	28(O) -	2/4
1050	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	130.63	07/2019 -	02/2022	31(O) -	2/4
1051	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	271.38	12/2019 -	03/2022	27(O) -	0/4
1052	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	200.00	05/2020 -	09/2022	28(O) -	0/4
1053	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	467.78	06/2019 -	08/2020	-	0/4
1054	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	204.36	11/2019 -	01/2021	-	0/4
1055	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	210.81	07/2019 -	03/2022	32(O) -	0/4
1056	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	204.49	11/2019 -	12/2020	-	0/0
1057	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	151.60	07/2019 -	03/2022	32(O) -	0/0
1058	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	245.82	12/2019 -	03/2022	27(O) -	0/4
1059	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	135.51	12/2019 -	06/2022	30(O) -	0/4
1060	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	143.39	12/2019 -	12/2020	-	0/4
1061	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	166.31	12/2019 -	03/2022	27(O) -	0/4
1062	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	218.73	06/2019 -	12/2022	42(O) -	0/4
1063	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.92	11/2019 -	07/2019	-	0/4
1064	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	223.81	07/2019 -	07/2021	-	0/4
1065	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	302.13	07/2019 -	03/2022	32(O) -	0/0
1066	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	196.83	06/2019 -	09/2022	39(O) -	0/4
1067	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	136.94	12/2019 -	06/2022	30(O) -	0/4
1068	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	03/2022	27(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1069	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	138.05	12/2019 -	03/2022	27(O) -	0/4
1070	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	107.85	12/2019 -	06/2022	30(O) -	0/4
1071	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	224.98	12/2019 -	03/2022	27(O) -	0/4
1072	WADIGODRI TO DHANGRIIMPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	116.21	02/2020 -	01/2021	-	0/4
1073	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	137.57	02/2020 -	06/2021	-	0/4
1074	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	177.80	12/2019 -	03/2022	27(O) -	0/4
1075	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	203.39	12/2019 -	12/2020	-	0/4
1076	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	09/2021	-	0/4
1077	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	133.93	12/2019 -	09/2020	-	1/4
1078	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	456.93	09/2019 -	06/2022	33(O) -	1/4
1079	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	137.99	12/2019 -	09/2020	-	2/4
1080	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	181.37	08/2020 -	03/2022	19(O) -	0/4
1081	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	137.37	12/2019 -	09/2020	-	0/4
1082	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	176.39	08/2020 -	09/2022	25(O) -	0/0
1083	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	03/2020	-	0/0
1084	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	169.80	08/2020 -	06/2022	22(O) -	0/4
1085	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	146.73	12/2019 -	12/2019	-	0/0
1086	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	199.34	12/2019 -	12/2020	-	2/4
1087	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	93.73	12/2019 -	04/2022	28(O) -	0/0
1088	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	219.56	06/2020 -	06/2022	24(O) -	1/4
1089	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	174.63	12/2019 -	04/2022	28(O) -	0/0
1090	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	149.16	12/2019 -	06/2022	30(O) -	1/4
1091	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	68.00	12/2019 -	03/2022	27(O) -	0/0
1092	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	251.00	12/2019 -	12/2020	-	2/4
1093	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	159.96	05/2020 -	02/2022	21(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1094	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	260.48	06/2019 -	11/2020	-	0/4
1095	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	159.96	07/2019 -	11/2020	-	0/4
1096	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	156.87	11/2019 -	02/2022	27(O) -	0/4
1097	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	11/2020	-	0/0
1098	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	196.00	12/2019 -	10/2020	-	0/4
1099	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	257.83	07/2019 -	03/2022	32(O) -	0/4
1100	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	557.20	12/2019 -	03/2022	27(O) -	0/0
1101	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	284.02	07/2019 -	09/2022	38(O) -	0/4
1102	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	192.24	12/2019	06/2022	30(O)	0/0
1103	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	170.33	03/2019	12/2021	-	0/0
1104	SATARA MURVAD PILLOV/ PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	199.61	- -	06/2022	- -	0/0
1105	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	189.64	03/2019 -	03/2022	36(O) -	0/0
1106	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	61.42	05/2020 -	12/2022	31(O) -	0/4
1107	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	160.37	12/2019 -	07/2021	-	1/4
1108	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	233.89	07/2019 -	09/2022	38(O) -	0/4
1109	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	470.17	08/2019 -	08/2021	-	0/4
1110	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	03/2022	32(O) -	0/4
1111	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	170.80	07/2019 -	03/2022	32(O) -	0/4
1112	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	174.16	07/2019 -	03/2021	-	0/4
1113	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	191.12	06/2019 -	06/2022	36(O) -	2/4
1114	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	201.73	03/2019 -	06/2022	39(O) -	0/4
1115	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	105.37	03/2018 -	06/2022	51(O) -	0/4
1116	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	12/2022	31(O) -	0/4
1117	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	145.87	12/2019 -	03/2021	-	0/4
1118	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	169.24	12/2019 -	07/2021	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1119	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	167.95	04/2020 -	03/2021	-	1/4
1120	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	74.00	04/2019 -	06/2022	38(O) -	0/4
1121	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	175.24	09/2019 -	06/2022	33(O) -	2/4
1122	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	144.69	09/2018 -	03/2022	42(O) -	0/4
1123	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	791.90	12/2019 -	06/2022	30(O) -	1/4
1124	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	1,054.53	11/2019 -	06/2022	31(O) -	1/4
1125	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	343.45	06/2019 -	03/2022	33(O) -	2/4
1126	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	64.74	07/2019 -	06/2022	35(O) -	1/4
1127	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	190.75	06/2019 -	06/2022	36(O) -	0/4
1128	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.40	07/2019 -	11/2019	-	0/4
1129	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	210.10	11/2018 -	04/2021	-	0/4
1130	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	155.96	06/2019 -	12/2022	42(O) -	0/4
1131	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	186.62	06/2019 -	09/2022	39(O) -	0/4
1132	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	330.00	06/2019 -	06/2022	36(O) -	0/4
1133	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	232.56	06/2019 -	06/2022	36(O) -	0/4
1134	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	336.68	06/2019 -	06/2022	36(O) -	0/4
1135	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.64	06/2019 -	06/2019	-	0/0
1136	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	169.64	07/2019 -	11/2020	-	0/4
1137	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	350.07	06/2021 -	09/2022	15(O) -	1/4
1138	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 2,226.11	983.14	726.13	12/2019 -	09/2022	33(O) -	1/4
1139	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	12/2022	37(O) -	1/4
1140	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	840.10	02/2019 -	11/2021	-	0/0
1141	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 1,428.09	904.70	969.90	03/2020 -	10/2020	-	2/4
1142	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 2,617.44	1,338.13	1,346.39	03/2020 -	03/2020	-	3/5
1143	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	85.47	06/2019 -	06/2022	36(O) -	1/4
1144	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	246.86	12/2019 -	03/2022	27(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1145	WARDHA TO ARVI - [N24001150]MORTH, MAHARASHTRA ,	02/2018	313.58 -	313.58	202.69	04/2020 -	03/2022	23(O) -	0/4
1146	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI, MAHARASHTRA , EPC	02/2019	731.89 -	732.34	401.61	11/2019 -	-	-	0/0
1147	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI, MAHARASHTRA , EPC	02/2019	362.46 -	362.46	243.39	11/2019 -	-	-	0/0
1148	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI, MAHARASHTRA , EPC	02/2019	594.75 -	606.75	245.90	11/2019 -	-	-	0/0
1149	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL, MANIPUR ,	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	-	4/4
1150	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL, MANIPUR , EPC	03/2019	471.00 -	471.00	167.94	07/2022 -	07/2022	0(O) -	2/4
1151	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL, MANIPUR , EPC	03/2020	292.24 -	292.24	59.71	06/2022 -	06/2022	0(O) -	2/4
1152	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL, MANIPUR , EPC	06/2020	365.53 -	365.53	91.93	08/2022 -	08/2022	0(O) -	2/4
1153	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL, MANIPUR , EPC	03/2020	167.95 -	167.95	42.83	06/2022 -	06/2022	0(O) -	2/4
1154	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL, MANIPUR , EPC	07/2020	177.76 -	177.76	36.05	08/2022 -	08/2022	0(O) -	2/4
1155	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL, MANIPUR , EPC	08/2020	379.39 -	379.39	12.26	04/2022 -	04/2022	0(O) -	0/4
1156	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL, MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4
1157	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL, MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1158	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL, MANIPUR , EPC	03/2020	167.95 -	167.95	50.50	06/2022 -	06/2022	0(O) -	2/4
1159	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL, MANIPUR , EPC	02/2021	226.32 -	226.32	6.70	12/2022 -	12/2022	0(O) -	0/4
1160	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL, MANIPUR , EPC	02/2021	188.36 -	188.36	16.08	12/2022 -	12/2022	0(O) -	1/4
1161	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL, MANIPUR , EPC	02/2021	232.26 -	232.26	6.41	12/2022 -	12/2022	0(O) -	0/4
1162	IMPHAL - MOREH PACKAGE- 3 - [N24001352]NHIDCL, MANIPUR , EPC	03/2021	259.31 -	259.31	46.59	12/2022 -	12/2022	0(O) -	1/4
1163	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL, MANIPUR , EPC	03/2021	195.14 -	195.14	.00	12/2022 -	12/2022	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1164	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL,MANIPUR , EPC	03/2021	234.08 -	234.08	15.09	12/2022 -	12/2022	0(O) -	1/4
1165	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR , EPC	07/2021	204.58 -	204.58	10.48	03/2023 -	03/2023	0(O) -	0/0
1166	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL,MANIPUR , EPC	03/2021	277.99 -	277.99	5.57	01/2023 -	01/2023	0(O) -	0/0
1167	SENAPATI- IMPHAL PKG-5B - [N24001400]NHIDCL,MANIPUR , EPC	03/2021	211.70 -	211.70	.00	01/2023 -	01/2023	0(O) -	0/4
1168	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR , EPC	07/2021	467.00 -	467.00	.00	03/2023 -	03/2023	0(O) -	0/0
1169	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR , EPC	07/2021	185.80 -	185.80	6.20	03/2023 -	03/2023	0(O) -	0/0
1170	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR , EPC	07/2021	483.87 -	483.87	22.78	03/2023 -	03/2023	0(O) -	0/0
1171	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR , EPC	07/2021	198.77 -	198.77	6.59	03/2023 -	03/2023	0(O) -	0/0
1172	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL,MANIPUR , EPC	07/2021	673.27 -	673.27	11.12	10/2023 -	10/2023	0(O) -	0/0
1173	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	211.57	-	09/2021	-	2/4
1174	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	135.84	05/2019 -	09/2022	40(O) -	2/4
1175	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]NHIDCL,MEGHALAYA , EPC	11/2020	351.12 -	351.12	171.47	12/2023 -	12/2023	0(O) -	0/4
1176	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]NHIDCL,MEGHALAYA , EPC	11/2020	525.68 -	525.68	301.78	12/2023 -	12/2023	0(O) -	1/4
1177	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]NHIDCL,MEGHALAYA , EPC	11/2020	445.51 -	445.51	174.37	12/2023 -	12/2023	0(O) -	1/4
1178	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]NHIDCL,MEGHALAYA , EPC	11/2020	284.21 -	284.21	44.52	12/2023 -	12/2023	0(O) -	0/4
1179	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA , EPC	10/2020	157.86 -	157.86	68.77	04/2022 -	04/2022	0(O) -	2/4
1180	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA , EPC	03/2021	260.21 -	260.21	66.51	12/2022 -	12/2022	0(O) -	1/4
1181	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 1,109.88	992.67	978.43	03/2011 12/2022	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1182	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 374.59	327.92	329.03	10/2010 12/2022	-	-	0/0
1183	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 434.65	377.99	384.74	10/2010 12/2022	-	-	0/0
1184	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	140.92	09/2019 -	04/2023	43(O) -	1/4
1185	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	124.67	09/2019 -	07/2023	46(O) -	1/4
1186	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	133.41	09/2019 -	06/2023	45(O) -	1/4
1187	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	137.39	09/2019 -	04/2023	43(O) -	1/4
1188	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	163.81	09/2019 -	04/2023	43(O) -	1/4
1189	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	164.47	09/2019 -	06/2023	45(O) -	1/4
1190	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	75.58	09/2019 -	04/2024	55(O) -	0/4
1191	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	120.31	09/2019 -	09/2023	48(O) -	1/4
1192	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	308.85	09/2014 03/2022	-	-	0/0
1193	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM ,	01/2017	205.95 -	205.95	123.24	01/2021 -	04/2022	15(O) -	0/0
1194	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	32.96	10/2022 -	10/2022	0(O) -	1/4
1195	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	39.88	07/2022 -	07/2022	0(O) -	1/4
1196	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	70.76	07/2022 -	07/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1197	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	72.45	07/2022 -	07/2022	0(O) -	0/4
1198	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	120.63	07/2022 -	07/2022	0(O) -	2/4
1199	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM , EPC	03/2021	374.39 -	374.39	43.39	12/2022 -	12/2022	0(O) -	0/4
1200	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM , EPC	03/2021	233.25 -	233.25	16.96	12/2022 -	12/2022	0(O) -	0/4
1201	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM , EPC	03/2021	674.71 -	674.71	60.00	06/2023 -	06/2023	0(O) -	0/4
1202	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM , EPC	03/2021	698.44 -	698.44	.00	12/2022 -	12/2022	0(O) -	0/4
1203	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM , EPC	03/2021	740.58 -	740.58	.00	01/2023 -	01/2023	0(O) -	0/4
1204	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1205	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 03/2022	03/2022	91(O) 0	0/0
1206	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105(O) -	0/0
1207	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 2,047.64	2,047.64	1,364.18	03/2013 06/2021	-	-	0/0
1208	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	1,890.04	04/2015 03/2022	03/2022	83(O) 3	3/4
1209	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	11/2021	-	0/0
1210	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	11/2018	-	0/0
1211	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	356.14	08/2016 -	05/2021	-	3/4
1212	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	312.71	08/2016 -	05/2021	-	3/4
1213	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	341.40	09/2018 -	03/2022	42(O) -	3/4
1214	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	156.49	09/2018 -	11/2022	50(O) -	2/4
1215	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	186.85	09/2018 -	07/2022	46(O) -	2/4
1216	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	134.40	09/2018 -	05/2022	44(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1217	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	100.70	09/2018 -	09/2022	48(O) -	2/4
1218	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	120.99	09/2018 -	12/2021	-	0/4
1219	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	125.87	09/2018 -	12/2021	-	0/4
1220	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	134.89	09/2018 -	11/2021	-	3/4
1221	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	157.06	09/2018 -	11/2021	-	3/4
1222	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	183.30	09/2018 -	11/2021	-	2/4
1223	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	127.24	09/2018 -	03/2022	42(O) -	1/4
1224	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	82.09	09/2018 -	12/2021	-	1/4
1225	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	87.49	09/2018 -	10/2022	49(O) -	0/4
1226	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	142.40	12/2020 12/2021	-	-	0/0
1227	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	132.43	12/2020 12/2021	-	-	0/0
1228	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 -	369.96	322.13	09/2019 -	11/2020	-	0/0
1229	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	115.36	11/2020 04/2022	-	-	0/0
1230	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	110.76	12/2022 -	07/2022	-5(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1231	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 -	277.44	33.95	10/2022 -	10/2022	0(O) -	0/4
1232	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	7.02	04/2022 -	04/2022	0(O) -	0/4
1233	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	9.39	04/2022 -	04/2022	0(O) -	0/4
1234	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	55.18	04/2022 -	04/2022	0(O) -	1/4
1235	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	64.91	06/2022 -	06/2022	0(O) -	1/4
1236	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	79.81	06/2022 -	06/2022	0(O) -	1/4
1237	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	41.90	06/2022 -	06/2022	0(O) -	1/4
1238	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	72.60	12/2021 -	12/2021	-	1/4
1239	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	101.27	06/2022 -	06/2022	0(O) -	2/4
1240	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	53.72	12/2021 -	12/2021	-	1/4
1241	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]NHIDCL,NAGALAND , EPC	03/2020	206.53 -	206.53	88.93	06/2022 -	06/2022	0(O) -	2/4
1242	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND , EPC	07/2021	258.52 -	258.52	31.67	03/2023 -	03/2023	0(O) -	0/0
1243	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND , EPC	02/2021	207.33 -	207.33	.00	03/2023 -	03/2023	0(O) -	0/0
1244	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	14.80	09/2014 -	-	-	0/0
1245	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,874.47	06/2014 -	-	-	0/0
1246	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	720.08	-	02/2022	-	0/0
1247	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	289.28	-	05/2022	-	0/1
1248	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	182.41	08/2015 -	-	-	0/0
1249	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	856.33	-	04/2022	-	0/0
1250	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	653.06	08/2019 -	06/2022	34(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1251	REHABILITATION AND UPGRADE TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	1,148.65	- -	03/2022	- -	0/0
1252	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	-	0/0
1253	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	107.06	06/2016 -	-	-	0/0
1254	REHABILITATION AND UPGRADE BY 4-LANE OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	1,100.45	03/2020 -	03/2022	24(O) -	0/0
1255	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	258.64	07/2017 -	06/2022	59(O) -	0/0
1256	REHABILITATION AND UPGRADE OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	290.00	- -	06/2022	- -	0/0
1257	REHABILITATION AND UPGRADE OF FOUR LANE OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	294.69	- -	03/2022	- -	0/0
1258	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	514.05	- -	06/2022	- -	0/0
1259	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	415.26	- -	02/2022	- -	0/0
1260	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	200.00	- -	03/2023	- -	0/1
1261	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	359.38	- -	06/2022	- -	0/0
1262	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	432.74	- -	03/2022	- -	0/1
1263	REHABILITATION AND UPGRADE OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	254.00	- -	06/2022	- -	0/0
1264	REHABILITATION SIX LANE UPGRADE CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	525.19	- -	-	-	0/0
1265	REHABILITATION AND UPGRADE OF SIX LANE OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	221.63	- -	03/2023	- -	0/0
1266	REHABILITATION AND UP-GRADATION TO 4-LANE OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	158.96	- -	06/2022	- -	0/0
1267	SIX LANE OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	450.59	- -	06/2022	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1268	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	226.26	02/2017 -	-	-	0/0
1269	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	220.15	02/2017 -	-	-	0/0
1270	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	149.61	08/2018 -	-	-	0/0
1271	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	133.36	04/2018 -	-	-	0/0
1272	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	132.67	08/2018 -	-	-	0/0
1273	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	135.38	08/2018 -	-	-	0/0
1274	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	851.32	-	-	-	0/1
1275	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 479.00	479.00	456.80	- 03/2023	03/2023	- 3	3/4
1276	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	-	0/0
1277	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	2,280.00	1,367.00	-	-	-	0/0
1278	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 756.27	756.27	466.03	03/2020 03/2023	03/2023	36(O) 6	2/4
1279	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	-	-	-	0/0
1280	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	-	-	-	0/0
1281	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	214.90	08/2020 -	12/2022	28(O) -	0/1
1282	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	729.55	10/2019 -	12/2022	38(O) -	0/1
1283	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 192.48	170.57	75.41	11/2020 -	12/2022	25(O) -	0/1
1284	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	261.09	08/2020 -	10/2022	26(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1285	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414]NHAI,PUNJAB , EPC	12/2020	733.00 -	733.00	.00	01/2024 04/2024	01/2024	0(O) 0	0/0
1286	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB , EPC	12/2020	881.00 -	881.00	.00	04/2024 -	04/2024	0(O) -	0/0
1287	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB , EPC	12/2020	989.66 -	989.66	.00	01/2024 -	04/2024	3(O) -	0/0
1288	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB , EPC	12/2020	1,234.40 -	1,234.40	.00	04/2024 -	04/2024	0(O) -	0/0
1289	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB , EPC	12/2020	1,094.46 -	1,094.46	.00	04/2024 -	04/2024	0(O) -	0/0
1290	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB , EPC	02/2021	1,269.96 -	1,269.96	.00	04/2024 -	04/2024	0(O) -	0/0
1291	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420]NHAI,PUNJAB , EPC	02/2021	853.66 -	853.66	.00	04/2024 -	04/2024	0(O) -	0/0
1292	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	.00	10/2017 09/2021	09/2021	-	3/4
1293	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1294	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	03/2022	47(O) -	0/0
1295	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1296	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	690.17	06/2019 -	-	-	0/0
1297	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	1,518.41	- -	03/2022	- -	0/0
1298	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	06/2022	26(O) -	0/0
1299	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 1,140.64	1,198.64	1,014.01	10/2017 -	-	-	0/0
1300	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1301	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 649.00	649.00	373.86	- 10/2021	12/2022	- 0	0/0
1302	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	134.77	04/2018 -	-	-	3/4
1303	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	122.04	04/2018 -	07/2020	-	4/4
1304	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	328.71	06/2018 -	-	-	3/4
1305	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	248.67	05/2018 -	-	-	4/4
1306	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	164.94	- -	-	-	4/4
1307	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	245.15	08/2022 -	-	-	3/4
1308	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	70.90	08/2020 -	-	-	2/4
1309	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	63.07	11/2020 -	-	-	1/4
1310	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN , EPC	07/2020	319.09 -	319.09	12.93	09/2021 -	-	-	0/4
1311	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN , EPC	08/2020	216.72 -	216.72	63.57	12/2020 -	-	-	0/4
1312	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN , EPC	12/2020	379.23 -	379.23	25.84	10/2021 -	-	-	0/0
1313	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN , EPC	12/2020	339.65 -	339.65	28.60	10/2021 -	-	-	0/0
1314	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN , EPC	02/2021	240.99 -	240.99	.00	11/2021 -	11/2021	-	0/0
1315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	295.14	10/2017 -	-	-	3/4
1316	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	81.82	- -	04/2023	- -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1317	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	154.83	11/2017 -	03/2022	52(O) -	2/4
1318	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	63.83	06/2018 -	-	-	1/4
1319	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	79.70	04/2022 -	05/2023	13(O) -	1/4
1320	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	48.15	04/2023 -	04/2023	0(O) -	1/4
1321	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	59.98	06/2022 -	06/2022	0(O) -	1/4
1322	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	32.50	04/2023 -	04/2023	0(O) -	1/4
1323	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	96.67	04/2023 -	04/2023	0(O) -	1/4
1324	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM , EPC	09/2020	183.31 -	183.31	76.84	05/2022 -	05/2022	0(O) -	0/4
1325	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM , EPC	09/2020	262.84 -	262.84	120.72	05/2023 -	05/2023	0(O) -	0/4
1326	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM , EPC	08/2020	292.80 -	292.80	42.83	05/2022 -	05/2022	0(O) -	0/4
1327	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM 27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM , EPC	08/2020	230.45 -	230.45	2.58	04/2023 -	04/2023	0(O) -	1/4
1328	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM , EPC	10/2020	493.42 -	493.42	.00	11/2023 -	11/2023	0(O) -	0/4
1329	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM , EPC	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023	0(O) -	0/4
1330	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]NHIDCL,SIKKIM , EPC	01/2021	332.20 -	332.20	.00	09/2023 -	09/2023	0(O) -	0/4
1331	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]NHIDCL,SIKKIM , EPC	12/2020	410.60 -	410.60	.00	02/2024 -	02/2024	0(O) -	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1332	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-	-	0/0
1333	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	8.12	06/2013 -	09/2021	-	0/0
1334	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	84.29	05/2013 -	02/2022	105(O) -	0/0
1335	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	271.64	08/2013 -	-	-	0/0
1336	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	106.65	04/2014 -	09/2022	101(O) -	0/0
1337	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	42.83	12/2017 -	05/2023	65(O) -	0/0
1338	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1339	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	434.89	08/2018 -	01/2022	-	0/0
1340	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	403.81	07/2018 -	12/2021	-	0/0
1341	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	252.08	03/2020 -	12/2021	-	0/0
1342	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	403.81	07/2016 -	12/2021	-	0/0
1343	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59(O) -	0/0
1344	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	178.41	09/2017 -	-	-	0/0
1345	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	841.80	09/2017 -	07/2022	58(O) -	0/0
1346	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	254.10	-	12/2021	-	0/0
1347	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	346.17	-	05/2022	-	0/0
1348	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	255.05	-	12/2022	-	0/0
1349	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	411.17	-	03/2022	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1350	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- 08/2023	-	-	0/0
1351	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	383.75	- -	12/2022	-	0/0
1352	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	12/2021	-	0/0
1353	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU ,	03/2019	297.55 -	297.55	250.73	11/2019 -	-	-	3/4
1354	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 -	240.38	143.36	06/2019 -	-	-	3/4
1355	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	5,148.00	.00	12/2021 -	12/2021	-	0/0
1356	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU , EPC	08/2020	302.62 -	302.62	87.40	02/2021 -	-	-	1/4
1357	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1358	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	.00	03/2016 -	-	-	1/4
1359	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA , EPC	10/2014	295.47 -	295.47	207.71	02/2017 -	-	-	0/1
1360	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0
1361	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	1,020.25	11/2018 07/2019	03/2022	40(O) 1	0/0
1362	FOUR LANING OF KHAMMAM-DEVARAPALLE SECTION (GREENFIELD) - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1363	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	476.66	- -	-	-	0/0
1364	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	686.55	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1365	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	373.21	- -	-	-	0/0
1366	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 1,140.50	828.29	287.90	- 03/2021	-	-	0/0
1367	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA ,	10/2016	298.32 -	298.32	135.18	02/2019 -	-	-	0/0
1368	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA ,	10/2016	248.83 -	248.83	126.24	03/2019 -	-	-	0/0
1369	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA ,	01/2017	244.54 -	244.54	166.41	05/2019 -	-	-	0/0
1370	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA ,	01/2017	196.52 -	196.52	116.85	10/2019 -	-	-	0/0
1371	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA ,	01/2017	283.00 -	283.00	245.68	12/2019 -	-	-	0/0
1372	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA ,	01/2017	359.27 -	359.27	306.88	05/2019 -	-	-	0/0
1373	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA ,	01/2017	300.00 -	300.00	208.95	05/2019 -	-	-	0/0
1374	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA ,	01/2018	283.15 -	283.15	162.89	05/2020 -	-	-	0/0
1375	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA ,	01/2018	230.03 -	230.03	220.35	12/2019 -	-	-	0/0
1376	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA ,	02/2018	206.13 -	206.13	184.68	06/2020 -	-	-	0/0
1377	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA ,	02/2018	294.13 -	294.13	160.81	11/2019 -	-	-	0/0
1378	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA ,	02/2018	220.28 -	220.28	170.34	11/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1379	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA ,	02/2018	426.52 -	426.52	395.25	04/2020 -	-	-	0/0
1380	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	239.94	09/2020 -	-	-	0/0
1381	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	218.04	07/2020 -	-	-	0/0
1382	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	410.21	10/2019 -	-	-	0/0
1383	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	165.04	07/2019 -	-	-	0/0
1384	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	147.53	-	-	-	0/0
1385	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	358.78	03/2018 -	-	-	4/4
1386	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	142.81	08/2020 -	11/2021	-	0/0
1387	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA , EPC	03/2020	247.76 -	247.76	36.82	01/2022 -	10/2022	9(O) -	1/4
1388	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA , EPC	06/2020	347.36 -	347.36	116.18	01/2022 -	01/2022	-	2/4
1389	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA , EPC	06/2020	277.50 -	277.50	114.77	01/2022 -	01/2022	-	1/4
1390	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA , EPC	03/2020	154.51 -	154.51	47.29	07/2022 -	07/2022	0(O) -	1/4
1391	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	22.21	07/2022 -	07/2022	0(O) -	1/4
1392	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	236.18	86.74	12/2022 -	12/2022	0(O) -	0/0
1393	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]NHIDCL,TRIPURA , EPC	11/2020	332.14 -	332.14	10.93	07/2022 -	07/2022	0(O) -	1/4
1394	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA , EPC	11/2020	159.13 -	159.13	12.02	06/2022 -	06/2022	0(O) -	1/4
1395	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]NHIDCL,TRIPURA , EPC	11/2020	280.91 -	280.91	99.97	07/2022 -	07/2022	0(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1396	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL, TRIPURA , EPC	11/2020	206.78 -	206.78	87.79	07/2022 -	07/2022	0(O) -	1/4
1397	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL, TRIPURA , EPC	06/2020	201.99 -	201.99	18.87	01/2022 -	01/2022	-	1/4
1398	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL, TRIPURA , EPC	09/2020	173.17 -	173.17	13.63	04/2022 -	04/2022	0(O) -	1/4
1399	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL, TRIPURA , EPC	06/2020	257.96 -	257.96	122.81	01/2022 -	01/2022	-	4/4
1400	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL, TRIPURA , EPC	03/2020	165.54 -	165.54	14.10	07/2022 -	07/2022	0(O) -	1/4
1401	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL, TRIPURA , EPC	03/2021	354.79 -	354.79	14.79	12/2022 -	12/2022	0(O) -	0/4
1402	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	03/2022	103(O) -	0/0
1403	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	469.31	459.07	01/2014 -	-	-	0/0
1404	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	01/2016	-	0/0
1405	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]NHAI, UTTAR PRADESH , EPC	01/2014	282.41 -	319.96	193.60	03/2016 -	04/2022	73(O) -	0/0
1406	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1407	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH ,	04/2014	351.34 -	417.68	433.68	01/2016 -	-	-	0/0
1408	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH ,	09/2015	368.73 503.36	368.73	487.13	09/2016 -	-	-	0/0
1409	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH ,	04/2014	495.78 -	627.93	633.24	01/2016 -	-	-	0/0
1410	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1411	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1412	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1413	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1414	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1415	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]NHAI, UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	141.33	08/2015 -	01/2021	-	0/0
1416	MEERUT-BULANDSHAHR - [N24000539]NHAI, UTTAR PRADESH ,	01/2016	683.24 -	987.94	.00	-	-	-	0/2
1417	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH ,	03/2016	676.73 -	676.73	985.40	04/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1418	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	- -	-	-	0/0
1419	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1420	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1421	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 1,376.86	1,376.86	887.23	04/2019 06/2022	06/2022	38(O) 0	0/0
1422	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 2,501.85	2,501.85	946.08	- 02/2022	-	-	0/0
1423	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 1,330.02	1,330.02	920.72	- 07/2022	07/2022	- 0	0/0
1424	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 2,421.37	2,421.37	2,192.68	- 12/2021	12/2021	-	0/0
1425	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1426	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1427	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1428	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	1,357.48	03/2020 -	03/2022	24(O) -	3/4
1429	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,307.68	03/2020 -	01/2022	-	3/4
1430	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	772.56	03/2020 -	-	-	0/0
1431	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	-	0/0
1432	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	1,084.94	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1433	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1434	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1435	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1436	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	75.10	- -	-	-	0/0
1437	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	1,065.70	930.46	- -	-	-	0/0
1438	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,176.70	- -	-	-	0/0
1439	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1440	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,315.69	- -	-	-	0/0
1441	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,525.15	- -	-	-	0/0
1442	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	222.94	- -	-	-	0/0
1443	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	332.69	- -	-	-	0/0
1444	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1445	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	137.90	- -	03/2022	-	0/0
1446	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	200.10	01/2020 -	03/2021	-	0/0
1447	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 2,262.00	2,262.00	1,720.10	01/2019 -	01/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1448	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	190.01	04/2020 -	03/2022	23(O) -	0/0
1449	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.69	02/2020 -	01/2021	-	0/0
1450	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19(O) -	0/0
1451	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	237.81	09/2020 -	12/2021	-	0/0
1452	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	197.64	- -	01/2022	-	0/0
1453	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	319.96	126.00	- -	03/2022	-	0/0
1454	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 -	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1455	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH , EPC	07/2018	1,948.25 -	1,948.25	313.56	02/2024 -	02/2024	0(O) -	0/0
1456	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 1,082.40	1,082.40	1,023.73	10/2013 03/2022	03/2022	101(O) 0	0/0
1457	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 793.63	793.63	291.10	- 09/2022	09/2022	- 0	0/0
1458	4-LANNING OF CHUTMALPUR-GANESHUPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 2,330.79	2,330.79	1,246.85	- 02/2022	02/2022	- 0	0/0
1459	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 1,023.23	1,023.23	980.59	07/2018 02/2022	05/2022	46(O) 0	0/4
1460	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	136.62	05/2018 -	09/2022	52(O) -	3/4
1461	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	224.23	06/2018 -	07/2022	49(O) -	3/4
1462	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	276.32	05/2018 -	09/2022	52(O) -	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1463	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	214.90	12/2019 -	07/2021	-	0/0
1464	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	185.44	12/2019 -	07/2021	-	0/0
1465	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	234.12	12/2019 -	08/2021	-	0/0
1466	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	207.83	06/2019 -	12/2021	-	0/0
1467	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	171.22	11/2019 -	07/2021	-	0/0
1468	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	259.90	11/2019 -	05/2021	-	0/0
1469	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	186.16	11/2019 -	10/2020	-	0/0
1470	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	287.56	02/2020 -	09/2021	-	0/0
1471	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	183.73	- -	10/2021	-	0/0
1472	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	109.23	05/2020 -	12/2021	-	0/0
1473	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	116.25	- -	-	-	0/0
1474	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	299.26	07/2018 -	07/2022	48(O) -	2/5
1475	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND ,	08/2016	234.88 -	234.88	174.51	12/2017 -	12/2020	-	0/0
1476	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	03/2022	103(O) -	3/4
1477	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,913.66	08/2013 -	06/2023	118(O) -	3/4
1478	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	1,396.18	09/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1479	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 416.00	363.93	277.34	- -	-	-	0/0
1480	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 1,414.01	1,414.01	990.95	06/2018 -	-	-	0/0
1481	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,516.44	- -	-	-	0/0
1482	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	708.78	08/2018 -	-	-	0/0
1483	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,952.20	97.16	- -	-	-	0/0
1484	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL ,	03/2016	271.17 291.20	291.20	120.51	11/2018 03/2022	03/2023	52(O) 12	0/0
1485	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAL-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 -	396.86	277.42	09/2019 01/2022	12/2022	39(O) 14	0/0
1486	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 -	426.18	258.00	09/2020 01/2022	12/2022	27(O) 11	0/0
1487	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 -	218.70	122.50	11/2020 -	06/2021	-	0/0
1488	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 -	254.30	118.68	10/2020 12/2021	03/2023	29(O) 21	0/0
1489	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 -	213.97	27.41	08/2019 11/2022	03/2023	43(O) 4	0/0
1490	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 -	263.26	78.56	08/2019 08/2022	03/2023	43(O) 7	0/0
1491	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.22	398.52	331.86	08/2017 -	02/2020	-	0/0
	Total		5,17,126.74 -	5,40,821.11	3,25,990.17				550/1560
	SHIPPING AND PORTS								
1492	JAL MARG VIKAS PROJECT - [N25000072]JWAI, MULTI STATE ,	01/2018	5,369.18 -	4,633.81	2,013.22	03/2023 -	03/2023	0(O) -	2/7
	Total		5,369.18 -	4,633.81	2,013.22				2/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
1493	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI ,	10/2014	248.20 -	248.20	173.87	03/2018 -	03/2022	48(O) -	3/5
1494	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	80(O) -	0/0
1495	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE , Central Sector Projects	03/2020	431.16 461.42	461.42	70.25	06/2021 11/2021	06/2022	12(O) 3	0/0
	Total		14,013.36 -	25,373.62	20,789.12				3/5
	<u>URBAN DEVELOPMENT</u>								
1496	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR ,	02/2019	13,365.77 -	13,925.50	307.63	06/2024 -	06/2024	0(O) -	0/0
1497	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH ,	05/2019	299.97 -	299.97	27.44	09/2020 -	05/2023	32(O) -	1/6
1498	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI ,	09/2011	38,585.00 -	40,180.91	39,728.58	03/2016 08/2021	-	-	1/1
1499	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	217.00	187.17	04/2019 -	02/2022	34(O) -	1/2
1500	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	1,034.98	- -	03/2023	- -	0/9
1501	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	139.55	03/2021 06/2022	06/2022	15(O) -12	0/0
1502	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	204.84	08/2020 04/2022	04/2022	20(O) -2	2/5
1503	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 -	1,100.80	35.90	07/2021 06/2024	06/2024	35(O) 12	0/6
1504	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 -	1,128.00	30.00	03/2022 06/2024	06/2024	27(O) 12	0/0
1505	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	2,949.03	03/2025 -	03/2025	0(O) -	0/1
1506	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	498.21	12/2020 09/2021	-	-	1/1
1507	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,925.22	10,015.98	12/2018 -	08/2022	44(O) -	0/1
1508	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	431.21	03/2024 -	03/2024	0(O) -	0/1
1509	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	439.23	03/2024 -	06/2024	3(O) -	0/1
1510	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	20,025.67	02/2021 -	03/2025	49(O) -	162/249

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1511	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151]BMRCL,KARNATAKA , EPC	06/2021	14,788.10 -	14,788.10	2,290.84	06/2026 -	06/2026	0(O) -	0/76
1512	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	6,218.14	6,065.82	07/2017 -	09/2020	-	0/0
1513	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	409.75	02/2023 05/2025	05/2025	27(O) 27	0/0
1514	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	264.77	02/2023 07/2025	07/2025	29(O) 29	0/0
1515	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	9,759.79	8,462.32	03/2018 -	02/2022	47(O) -	0/0
1516	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	20,484.28	03/2020 -	03/2023	36(O) -	0/0
1517	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	7,764.11	11/2021 -	12/2022	13(O) -	0/0
1518	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	6,762.86	06/2025 -	06/2025	0(O) -	0/8
1519	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	18,380.00	18,051.27	12/2015 -	-	-	24/24
1520	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	3,346.80	03/2018 02/2021	-	-	10/21
1521	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	2,561.78	03/2024 -	11/2024	8(O) -	0/0
1522	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	593.47	03/2024 -	12/2025	21(O) -	0/0
	Total		2,84,108.54 -	3,04,523.01	1,53,113.49				202/412
	<u>WATER RESOURCES</u>								
1523	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	18,422.33	03/2020 11/2021	04/2022	25(O) 0	0/19
1524	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	98.80	07/2021 -	03/2023	20(O) -	0/0
1525	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	413.29	.07	09/2020 -	03/2024	42(O) -	0/0
1526	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	66.51	12/2020 -	07/2022	19(O) -	0/0
1527	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	44.87	08/2021 -	04/2023	20(O) -	0/0
1528	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	38.57	10/2021 -	12/2023	26(O) -	0/0
1529	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	398.90	299.08	03/2020 -	03/2022	24(O) -	0/0
1530	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	380.87	01/2021 -	05/2022	16(O) -	0/0
1531	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	154.13	04/2021 -	06/2022	14(O) -	0/0
1532	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	74.10	11/2020 -	03/2022	16(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1533	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	263.52	05/2021 -	05/2022	12(O) -	0/0
1534	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	42.75	06/2022 -	12/2023	18(O) -	0/0
1535	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	101.12	06/2022 -	12/2023	18(O) -	0/0
1536	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	942.18	261.19	12/2022 -	12/2022	0(O) -	0/0
1537	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	261.19	12/2021 -	12/2022	12(O) -	0/0
1538	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	176.36	02/2022 -	12/2022	10(O) -	0/0
1539	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	363.66	01/2021 -	02/2022	13(O) -	0/0
1540	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1541	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	193.05	12/2019 -	-	-	0/0
1542	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	152.31	09/2021 -	12/2022	15(O) -	0/0
1543	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 -	261.12	.00	03/2022 -	04/2024	25(O) -	0/0
1544	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	109.63	09/2021 -	09/2022	12(O) -	0/0
1545	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	03/2024	31(O) -	0/0
1546	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	248.16	12/2020 -	03/2022	15(O) -	0/0
1547	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	18(O) -	0/0
1548	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	95.91	10/2021 -	03/2022	5(O) -	0/0
1549	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	04/2024	22(O) -	0/0
1550	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 -	213.91	.00	07/2021 -	03/2024	32(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1551	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	87.59	11/2019 -	03/2022	28(O) -	0/0
1552	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	12/2024	32(O) -	0/0
1553	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	12/2024	32(O) -	0/0
1554	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	12/2024	32(O) -	0/0
1555	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 -	224.69	.00	02/2022 -	03/2024	25(O) -	0/0
1556	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	03/2024	21(O) -	0/0
1557	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	12/2024	27(O) -	0/0
1558	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 -	154.73	.00	02/2022 -	03/2024	25(O) -	0/0
1559	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	38.00	12/2021 -	09/2023	21(O) -	0/0
1560	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	225.99	12/2019 -	05/2022	29(O) -	0/0
1561	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	261.87	04/2020 -	03/2022	23(O) -	0/0
1562	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	38.00	12/2021 -	09/2023	21(O) -	0/0
1563	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	34.69	12/2021 -	09/2023	21(O) -	0/0
	Total		23,466.28 -	69,468.25	22,562.69				0/19
	<u>DEFENCE PRODUCTION</u>								
1564	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA ,	12/2016	246.31 210.00	200.00	168.90	02/2020 03/2022	06/2022	28(O) 3	9/10
	Total		246.31 -	200.00	168.90				9/10
	<u>COMMERCE</u>								
1565	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI ,	06/2018	302.64 -	302.64	30.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	30.00				0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(February 2022)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Grand Total		21,86,542.05	26,59,914.61	13,26,569.75				2991/6007

FLASH REPORT


Summary of projects in the Flash Report for the month of February, 2022

Project Implementation - Current Status:

Number of Projects in Previous Month	1671
Number of Projects completed/dropped/frozen in Current Month	150
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	46
Number of Projects in Current Month	1565

Brief Analysis

Project Status with respect to Original Schedule: Out of 1565 projects, 9 projects are ahead of schedule, 278 projects are on schedule 647 projects are delayed. 514 projects do not have fixed dates of commissioning. 117 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

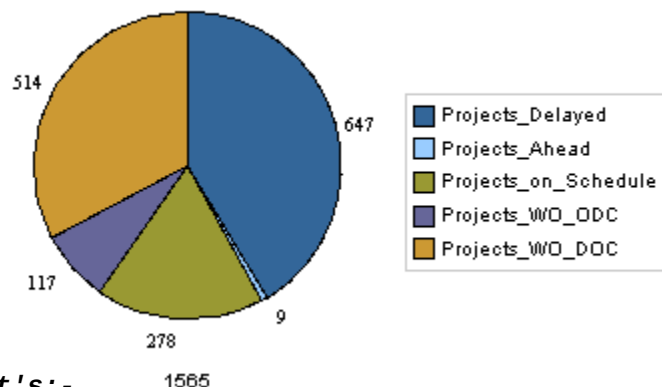


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1565 projects when sanctioned, was of the order of Rs. 2186542.05 crore but this was subsequently revised to Rs. 2659914.61 crore implying a cost overrun of 21.6%. The expenditure incurred on these projects till February, 2022 is Rs. 1326569.75 crore, which is 49.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

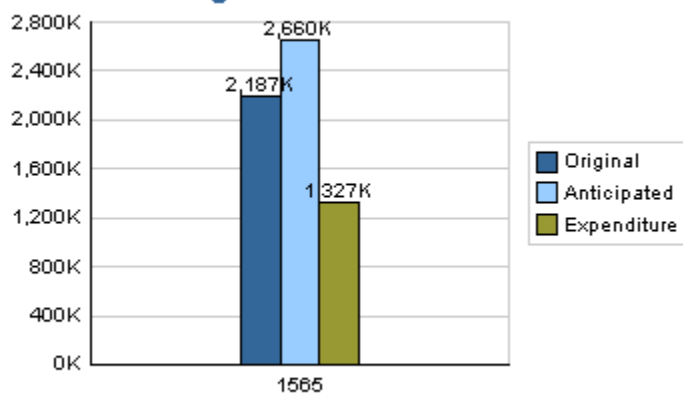

Sector wise current status of projects on the Flash Report

DPIIT

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

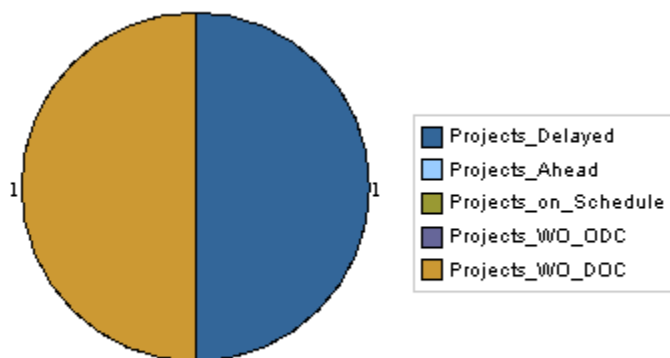


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 17352.09 crore but this was subsequently anticipated to Rs. 18990.3 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till February, 2022 is Rs. 12636.44 crore, which is 66.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

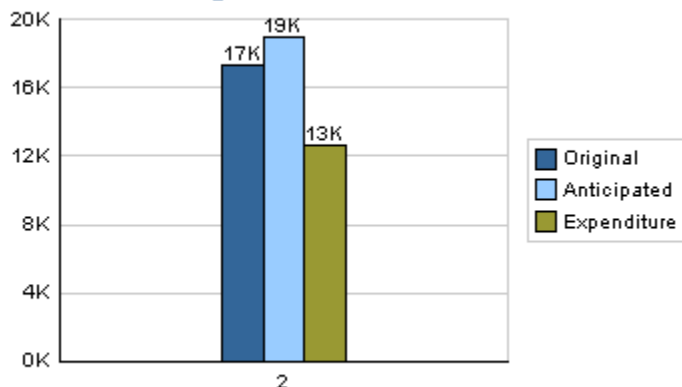

Sector wise current status of projects on the Flash Report


HOME AFFAIRS

Current Status:

Number of Projects	5
Number of Projects Delayed	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are delayed.

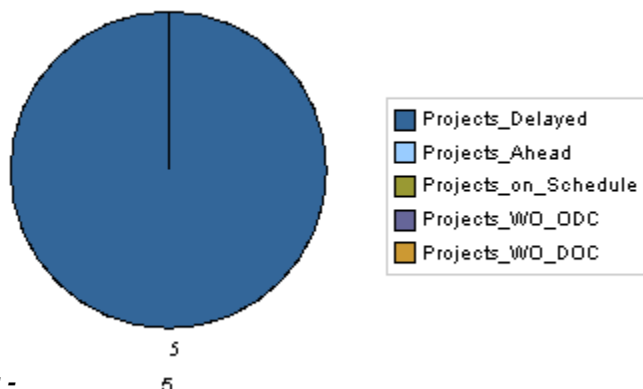


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 2025.73 crore but this was subsequently anticipated to Rs. 2885.25 crore implying a cost overrun of 42.4%. The expenditure incurred on these projects till February, 2022 is Rs. 1392.62 crore, which is 48.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

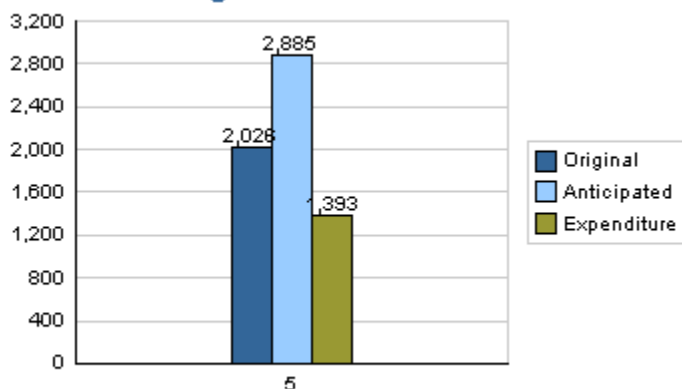

Sector wise current status of projects on the Flash Report

DEPARTMENT OF HIGHER EDUCATION


Current Status:

Number of Projects	23
Number of Projects On Schedule	1
Number of Projects Delayed	16

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 1 project is on schedule 16 projects are delayed. 6 projects do not have fixed dates of commissioning.

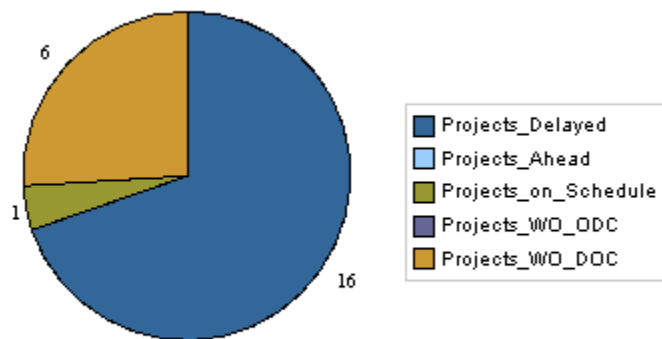


Total No Of Project's:-

23

Investment Scenario

Total original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 10455.86 crore but this was subsequently anticipated to Rs. 10390.34 cr The expenditure incurred on these projects till February, 2022 is Rs. 4422.7 crore, which is 42.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

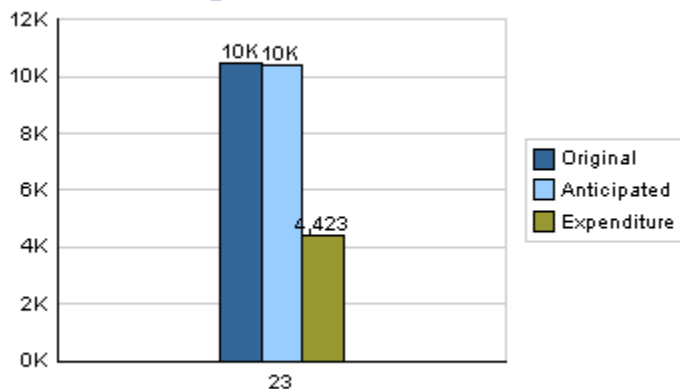

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	38

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 41 projects, 1 project is on schedule 38 projects are delayed. 2 projects do not have fixed dates of commissioning.

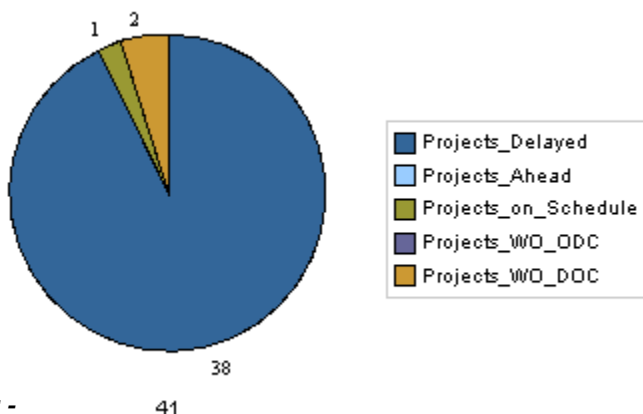


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 23466.28 crore but this was subsequently anticipated to Rs. 69468.25 crore implying a cost overrun of 196%. The expenditure incurred on these projects till February, 2022 is Rs. 22562.69 crore, which is 32.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

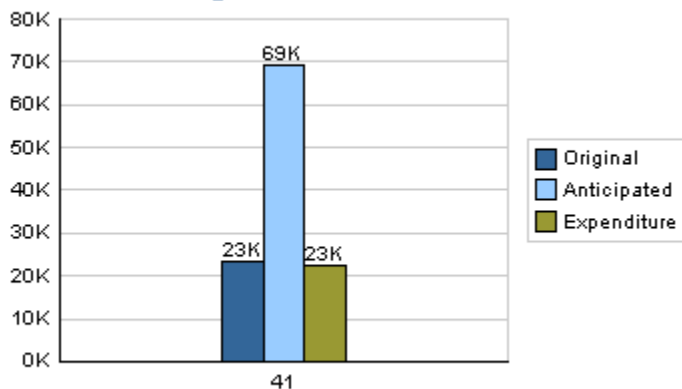

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	27
Number of Projects On Schedule	5
Number of Projects Delayed	16

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 27 projects, 5 projects are on schedule 16 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

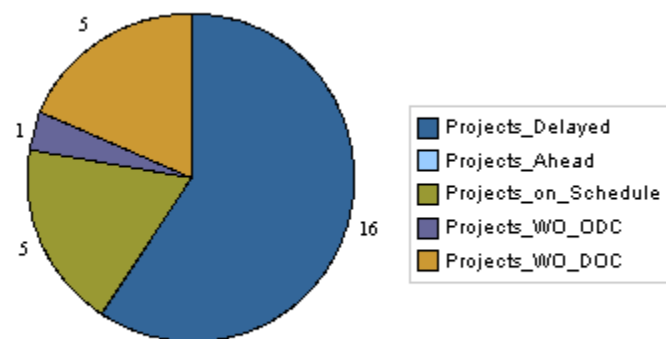


Total No Of Project's:-

27

Investment Scenario

Total original cost of implementation of 27 projects when sanctioned, was of the order of Rs. 284108.54 crore but this was subsequently anticipated to Rs. 304523.01 crore implying a cost overrun of 7.2%. The expenditure incurred on these projects till February, 2022 is Rs. 153113.49 crore, which is 50.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

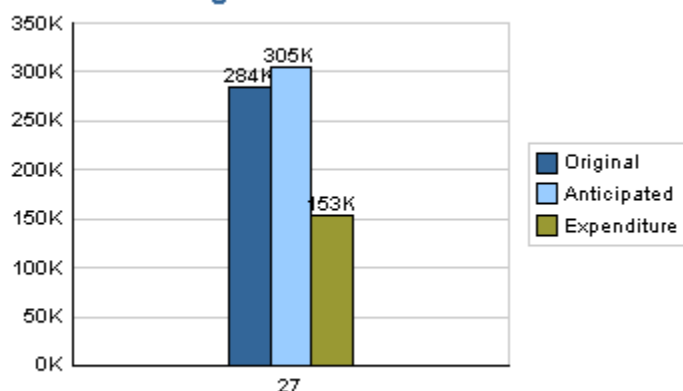

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	854
Number of Projects On Schedule	125
Number of Projects Delayed	235
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	73
Number of Projects Without Date Of Commissioning	419

Brief Analysis

Project Status with respect to Original Schedule: Out of 854 projects, 2 projects are ahead of schedule, 125 projects are on schedule 235 projects are delayed. 419 projects do not have fixed dates of commissioning. 73 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

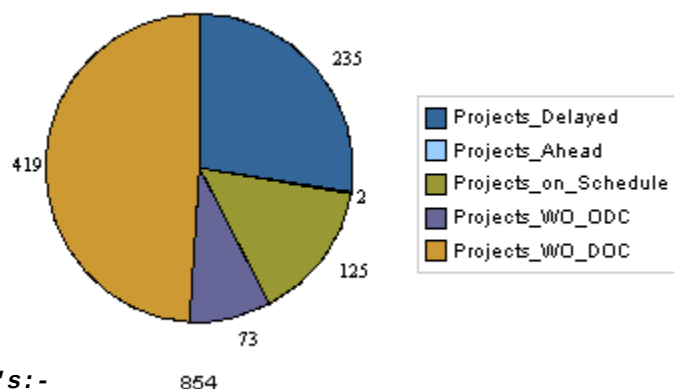


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 854 projects when sanctioned, was of the order of Rs. 517126.74 crore but this was subsequently anticipated to Rs. 540821.11 crore implying a cost overrun of 4.6%. The expenditure incurred on these projects till February, 2022 is Rs. 325990.17 crore, which is 60.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

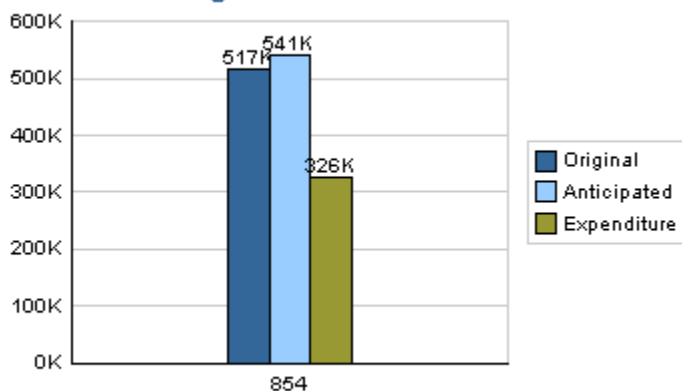

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	211
Number of Projects On Schedule	10
Number of Projects Delayed	131
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	39
Number of Projects Without Date Of Commissioning	28

Brief Analysis

Project Status with respect to Original Schedule: Out of 211 projects, 3 projects are ahead of schedule, 10 projects are on schedule 131 projects are delayed. 28 projects do not have fixed dates of commissioning. 39 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

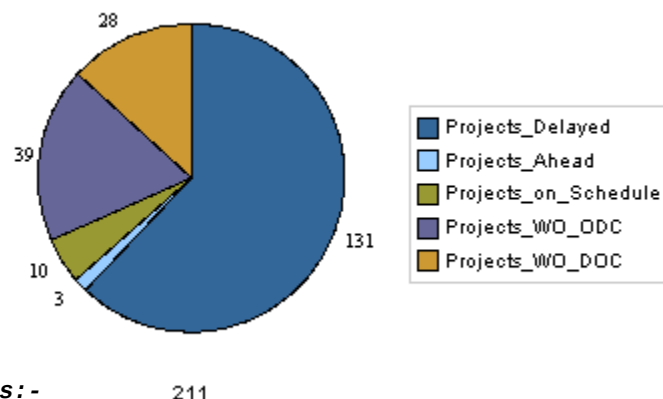


Total No Of Project's:-

211

Investment Scenario

Total original cost of implementation of 211 projects when sanctioned, was of the order of Rs. 408405.75 crore but this was subsequently anticipated to Rs. 665174.44 crore implying a cost overrun of 62.9%. The expenditure incurred on these projects till February, 2022 is Rs. 325319.01 crore, which is 48.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

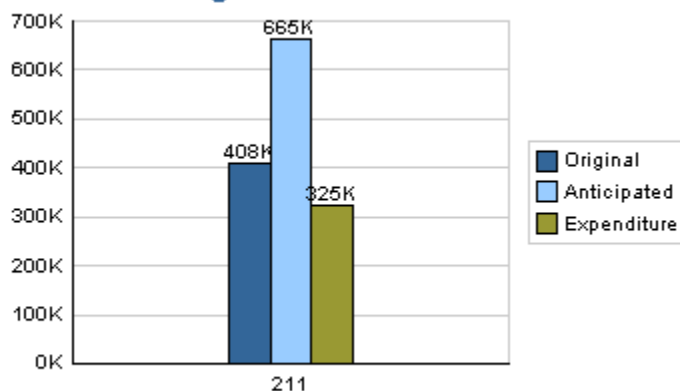

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	28
Number of Projects On Schedule	1
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	21

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 1 project is ahead of schedule, 1 project is on schedule 4 projects are delayed. 21 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

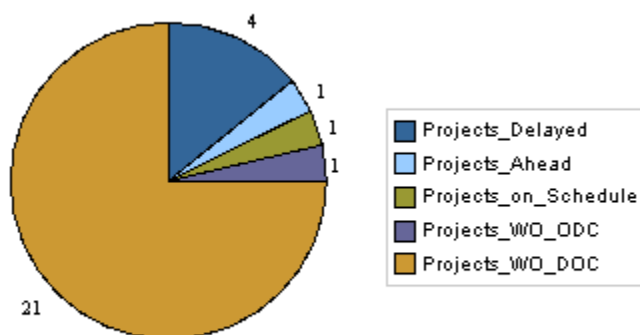


Total No Of Project's:-

28

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 13696.26 crore but this was subsequently anticipated to Rs. 14162.35 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till February, 2022 is Rs. 9693.6 crore, which is 68.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

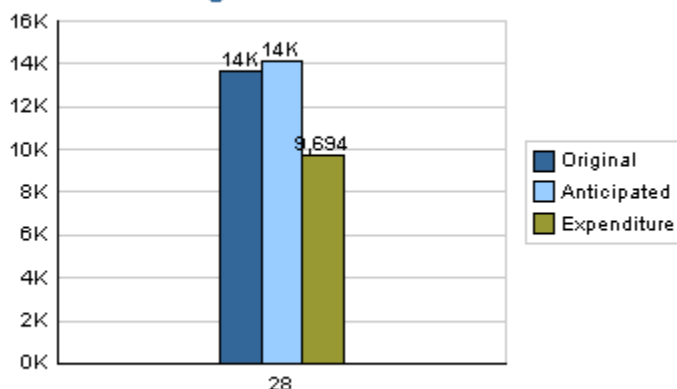

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	76
Number of Projects On Schedule	18
Number of Projects Delayed	50

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 76 projects, 18 projects are on schedule 50 projects are delayed. 7 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

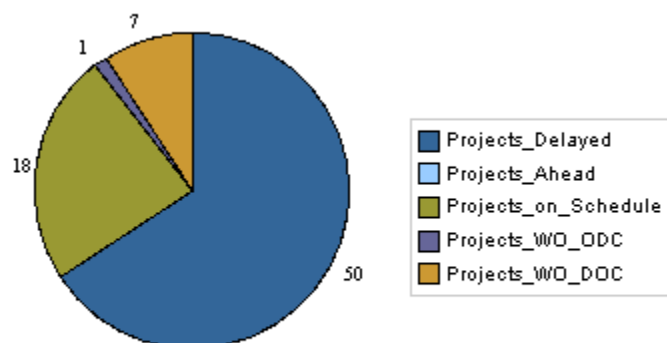


Total No Of Project's:-

76

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 196489.83 crore but this was subsequently anticipated to Rs. 260007.47 crore implying a cost overrun of 32.3%. The expenditure incurred on these projects till February, 2022 is Rs. 165748.86 crore, which is 63.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

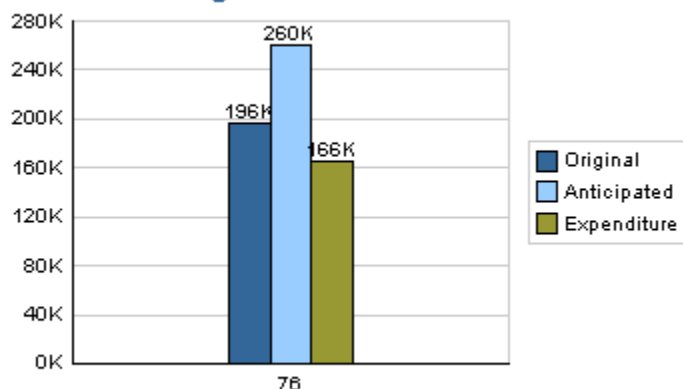

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	144
Number of Projects On Schedule	52
Number of Projects Delayed	84
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 144 projects, 2 projects are ahead of schedule, 52 projects are on schedule 84 projects are delayed. 4 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

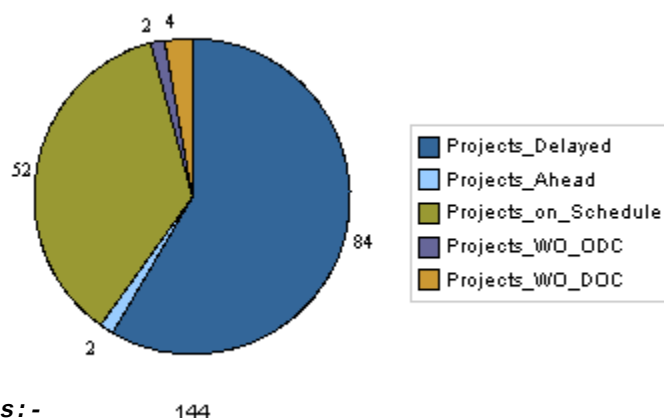


Total No Of Project's:-

144

Investment Scenario

Total original cost of implementation of 144 projects when sanctioned, was of the order of Rs. 377065.98 crore but this was subsequently anticipated to Rs. 395519.73 crore implying a cost overrun of 4.9%. The expenditure incurred on these projects till February, 2022 is Rs. 127100.07 crore, which is 32.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

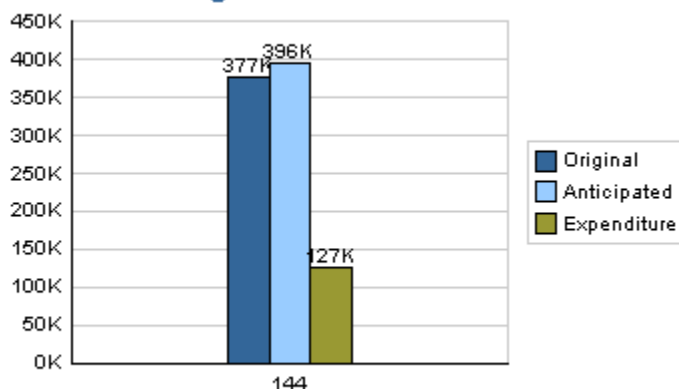

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	7
Number of Projects On Schedule	3
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 3 projects are on schedule 4 projects are delayed.

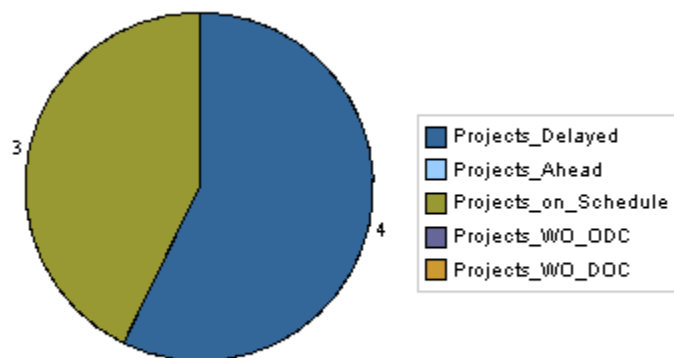


Total No Of Project's:-

7

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 21618.48 crore but this was subsequently anticipated to Rs. 28033.48 crore implying a cost overrun of 29.7%. The expenditure incurred on these projects till February, 2022 is Rs. 21179.62 crore, which is 75.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

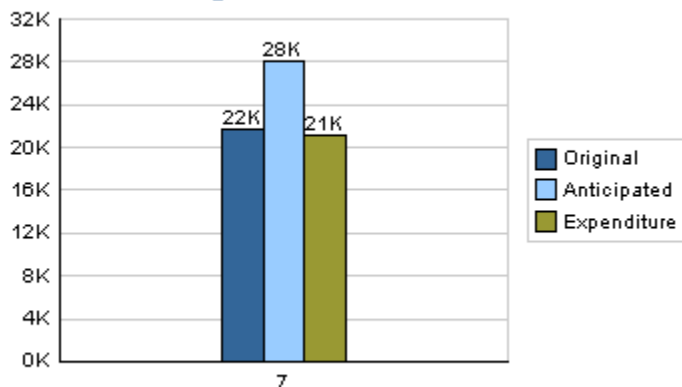

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects 6

Number of Projects Delayed 6

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 6 projects are delayed.

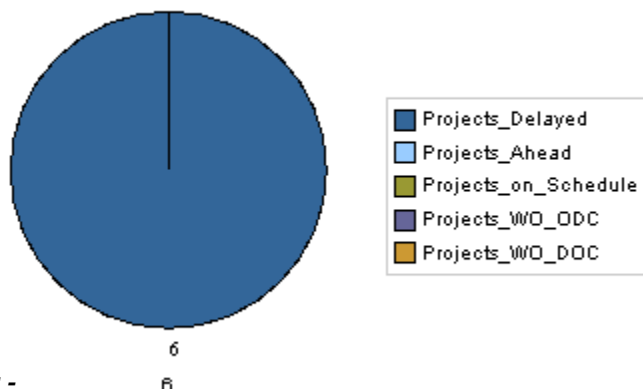


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 7333.99 crore but this was subsequently anticipated to Rs. 8585.67 crore implying a cost overrun of 17.1%. The expenditure incurred on these projects till February, 2022 is Rs. 1907.82 crore, which is 22.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

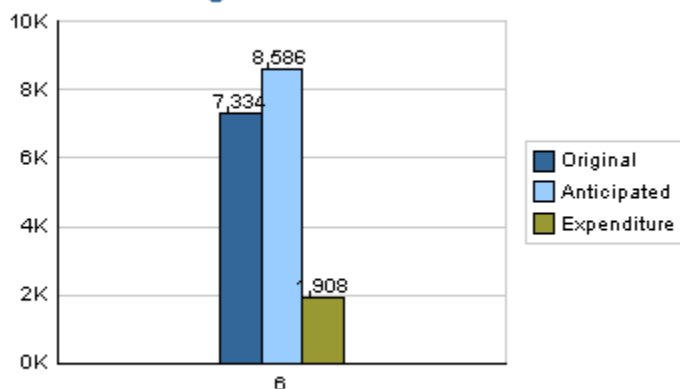

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

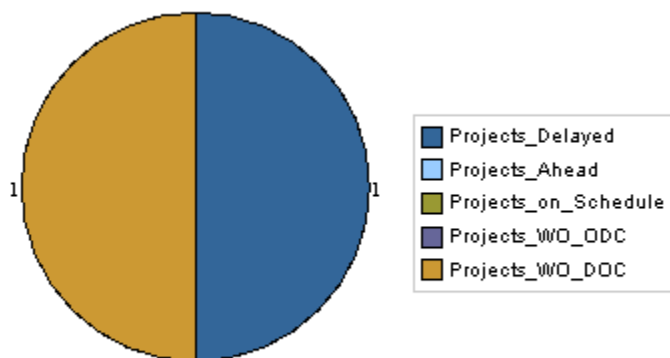


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 642.64 crore but this was subsequently anticipated to Rs. 642.64 crore. The expenditure incurred on these projects till February, 2022 is Rs. 549.98 crore, which is 85.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

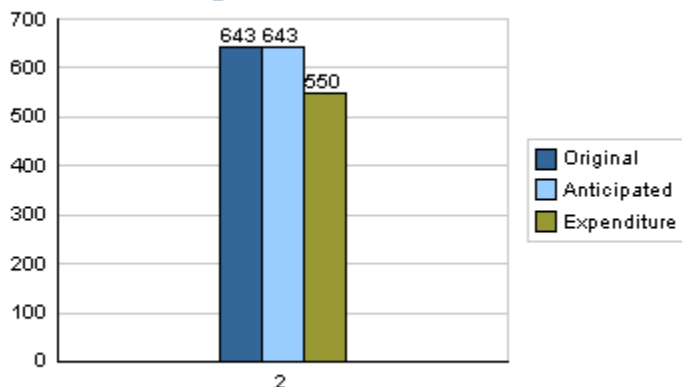

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	103
Number of Projects On Schedule	58
Number of Projects Delayed	31
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	13

Brief Analysis

Project Status with respect to Original Schedule: Out of 103 projects, 1 project is ahead of schedule, 58 projects are on schedule 31 projects are delayed. 13 projects do not have fixed dates of commissioning.

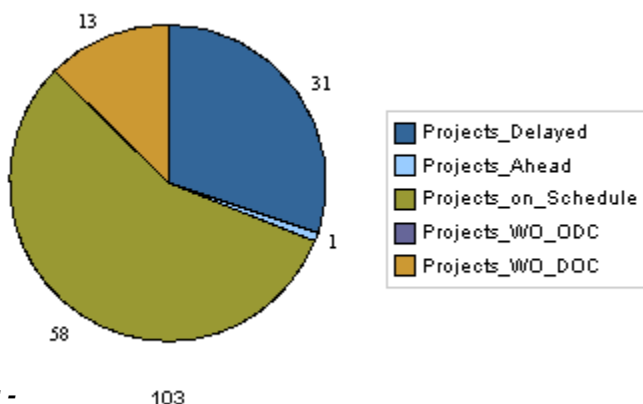


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 103 projects when sanctioned, was of the order of Rs. 153083.23 crore but this was subsequently anticipated to Rs. 157457.7 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till February, 2022 is Rs. 47810.81 crore, which is 30.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

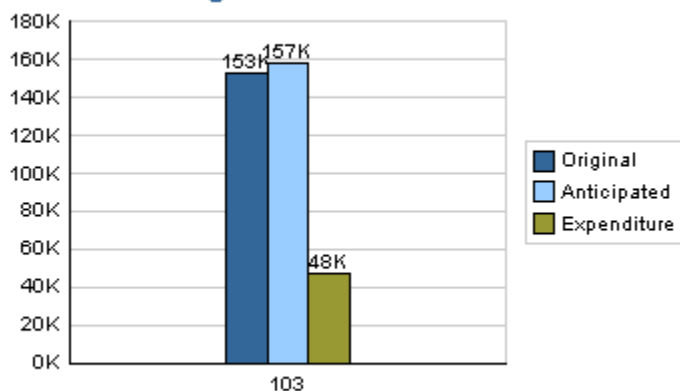

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	17

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 19 projects, 1 project is on schedule 17 projects are delayed. 1 project does not have fixed dates of commissioning.

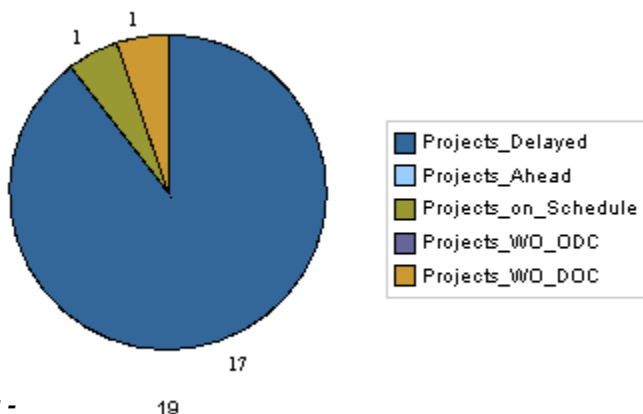


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 14128.17 crore but this was subsequently anticipated to Rs. 15161.45 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till February, 2022 is Rs. 5956.58 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

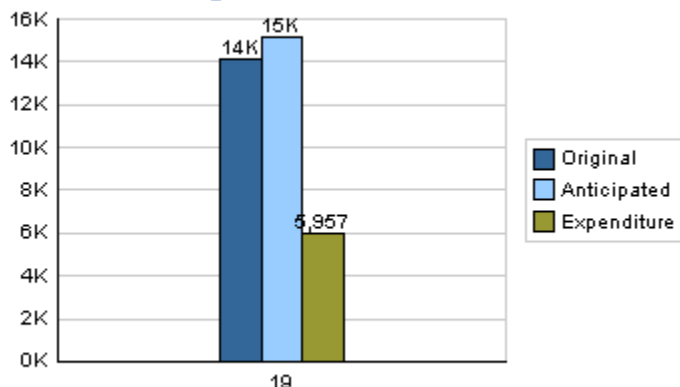

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 1 project is on schedule 4 projects are delayed.

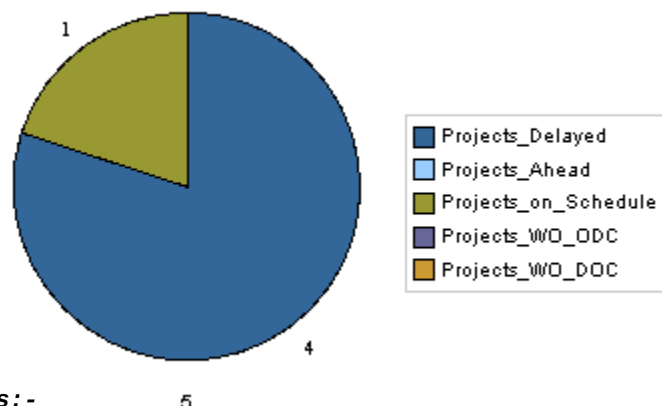


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 116741 crore but this was subsequently anticipated to Rs. 132609 crore implying a cost overrun of 13.6%. The expenditure incurred on these projects till February, 2022 is Rs. 73812.2 crore, which is 55.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

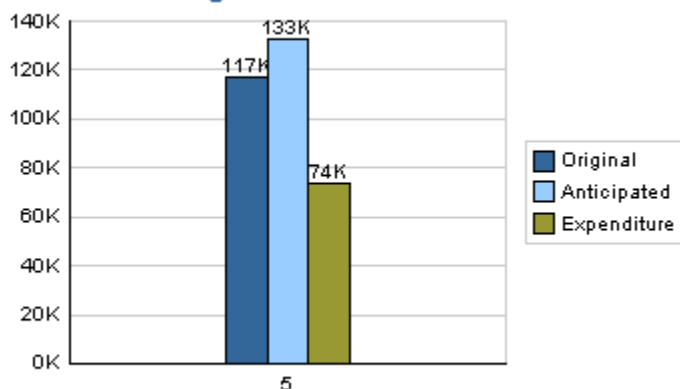

ANNEXURE

FLASH REPORT

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (FEBRUARY 2022)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	3,159.99	1,686.56
2	ANDHRA PRADESH	65	1,11,390.87	1,63,336.49	86,140.61
3	ARUNACHAL PRADESH	43	23,906.6	37,842.94	21,684.01
4	ASSAM	45	47,656	56,342.77	13,962.12
5	BIHAR	85	1,17,311.78	1,53,928.66	83,640.44
6	CHHATISGARH	44	75,822.81	85,814.67	44,274.93
7	DELHI	27	82,096.45	85,824.51	52,749.07
8	GOA	10	5,332.77	5,343.26	2,920.93
9	GUJARAT	56	1,06,855.31	1,21,047.93	56,308.38
10	HARYANA	35	60,694.21	62,645.55	18,434.86
11	HIMACHAL PRADESH	19	21,990.88	33,028.18	21,462.52
12	JAMMU AND KASHMIR	29	46,603.49	81,343	50,964.39
13	JHARKHAND	38	68,059.63	74,961.76	33,499.83
14	KARNATAKA	55	84,883.48	93,093.46	52,126.57
15	KERALA	21	29,984.85	35,049.87	13,136.59
16	LADAKH	8	2,633.23	2,767.29	298.56
17	MADHYA PRADESH	75	66,341.06	74,667.19	34,515.13
18	MAHARASHTRA	224	2,03,291.9	2,27,367.17	1,21,386.57
19	MANIPUR	26	12,108.58	22,615.2	13,404.22
20	MEGHALAYA	12	4,790.48	7,912.42	2,096.94
21	MIZORAM	24	11,957.35	16,911.6	8,408.56
22	MULTI STATE	91	3,13,927.74	4,39,710.63	2,36,772.21
23	NAGALAND	35	15,989.03	20,373.15	5,605.36
24	ODISHA	77	1,09,972.84	1,19,431.95	50,445.94
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	24	17,419.37	18,661.82	6,972.2
27	RAJASTHAN	49	59,049.82	64,466.52	32,414.83
28	SIKKIM	18	7,278.84	14,598.73	3,662.7
29	TAMIL NADU	58	1,96,061.35	2,16,066.26	94,822.68
30	TELANGANA	49	37,332.16	40,209.86	22,217.94
31	TRIPURA	19	5,084.45	5,225.78	2,268.53
32	UTTAR PRADESH	103	1,39,667.42	1,48,121.08	77,459.61
33	UTTARAKHAND	29	35,446.38	53,598.18	26,645.49
34	WEST BENGAL	62	62,517.29	74,251.74	34,164.06
TOTAL		1,565	21,86,542.05	26,59,914.61	13,26,569.75

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	6,840.00	6,268.20	09/2010 -	10/2022
	Total		3,492.00 -	6,840.00	6,268.20		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	507.91	09/2018 10/2022	10/2022
	Total		417.23 -	707.73	507.91		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
3	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	808.97	815.72	03/2013 -	03/2024
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	7,980.79	7,429.39	12/2015 -	02/2021
	Total		6,386.64 -	8,789.76	8,245.11		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
5	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	2/2019	186.00 199.00	210.60	206.20	09/2020 -	07/2021
	Total		186.00 -	210.60	206.20		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
6	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	586.50	586.50	11/2013 -	09/2021
7	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	06/2021
8	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
9	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	586.96	586.96	03/2018 -	04/2020
10	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	177.21	02/2018 -	04/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
11	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021	3/2018	268.84 -	284.67	279.53	-	05/2021
12	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	205.00	191.36	-	01/2022
13	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	8/2017	272.19 -	280.00	273.40	03/2019 -	02/2021
14	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	169.51	05/2017 -	01/2021
	Total		2,437.22 -	2,887.25	2,813.47		
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
15	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	4/2011	1,718.00 -	3,727.30	3,526.63	09/2011 -	-
	Total		1,718.00 -	3,727.30	3,526.63		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
16	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	228.63	173.62	04/2018 -	12/2022
	Total		162.88 -	228.63	173.62		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
17	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	9/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022
	<u>Oil & Natural Gas Corporation Limited</u>						
18	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	5/2019	763.92 -	829.58	829.58	12/2020 05/2022	05/2022
	Total		3,440.92 -	3,901.58	3,560.53		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
19	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190	1/2007	5,353.00 -	10,566.00	9,014.00	07/2012 -	-
	<u>Power Grid Corporation Of India Limited</u>						
20	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	2/2009	11,130.19 -	13,199.00	12,394.95	08/2013 -	03/2018
	<u>Satluj Jal Vidyut Nigam Limited</u>						
21	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Thdc India Limited</u>						
22	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	7/2006	1,657.00 -	4,825.60	4,409.29	02/2016 -	06/2023
	Total		18,788.52 -	29,538.49	26,638.36		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
23	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	2/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
24	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346	10/2006	11,589.00 30,357.00	51,219.00	35,951.00	- 06/2022	-
	<u>East Central Railways</u>						
25	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	3/1999	1,033.07 -	3,650.00	3,679.49	- -	07/2022
26	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	4/2004	372.14 -	1,470.50	1,536.32	- -	03/2024
27	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	4/2006	378.56 -	1,893.55	386.78	- -	03/2023
28	HAJIPUR - BACHAWARA - [N22000334	5/2015	678.54 -	929.86	964.41	03/2019 -	12/2021
29	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	4/1997	324.73 -	1,090.00	1,093.59	03/2012 -	06/2023
	<u>East Coast Railway</u>						
30	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	4/2005	810.78 -	1,928.07	947.41	06/2021 -	03/2025
31	SAMBALPUR-TALCHER DOUBLING - [N22000315	3/2011	1,111.99 -	1,539.28	1,243.24	02/2019 -	03/2022
	<u>Eastern Railways</u>						
32	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI- SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	4/2010	365.17 -	439.30	508.16	03/2017 -	03/2025
33	MONIGRAM- NIMTITA - [N22000301	4/2012	250.93 -	310.70	418.15	- -	03/2024
34	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	4/2012	255.64 -	272.20	311.86	- -	03/2022
35	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	4/2011	175.80 -	495.10	333.93	- -	03/2022
36	BANDEL-BOINCHI 3RD LINE - [N22000221	4/2011	288.35 -	502.48	529.13	- 09/2021	02/2022
	<u>Metropolitan Rapid Transport Projects</u>						
37	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	3/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022
38	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	4/2006	495.74 -	774.51	539.14	06/2013 -	12/2022

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-
	<u>North East Frontier Railway</u>						
40	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	6,527.00	4,766.68	03/2014 -	12/2023
41	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	9/2006	532.87 -	2,145.00	1,108.94	03/2019 -	03/2024
42	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	8,600.00	2,504.91	12/2015 -	12/2023
43	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	1,873.21	1,646.66	03/2021 -	03/2022
44	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	4/2010	241.52 -	401.65	338.00	- -	03/2023
45	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	9/2006	385.20 -	1,145.79	937.36	03/2019 -	03/2024
46	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	4/2003	4,454.17 -	14,322.00	12,156.19	03/2011 -	12/2023
	<u>North Eastern Railway</u>						
47	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	728.92	613.91	01/2019 -	02/2022
48	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,518.04	03/2022 -	03/2022
	<u>North Western Railway</u>						
49	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	775.62	02/2019 -	06/2022
	<u>Northern Railway</u>						
50	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	760.84	12/2011 -	-
51	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	689.83	- -	09/2023
52	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	839.00	839.36	03/2016 -	-
53	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	480.97	03/2023 12/2025	12/2025
54	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024
	<u>Rail India Technical And Economic Service</u>						
55	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	661.74	03/2021 12/2022	-
	<u>Rail Vikas Nigam Ltd.</u>						
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022
58	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	923.28	995.52	03/2021 -	05/2022
59	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,300.00	2,564.14	03/2023 -	03/2023

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
60	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	3/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022
61	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022
62	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022
63	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022
64	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023
65	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022
66	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022
67	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023
68	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	1,248.22	12/2024 -	12/2024
69	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022
70	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,683.68	12/2023 -	12/2023
71	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022
<u>South Central Railway</u>							
72	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027
73	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023
74	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	927.94	713.38	03/2020 -	03/2022
<u>South East Central Railway</u>							
75	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022
<u>South Eastern Railway</u>							
76	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.97	1,155.00	03/2020 -	06/2022
<u>South Western Railway</u>							
77	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,156.94 -	1,954.21	1,238.40	03/2020 -	12/2022
78	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	1,104.00	1,014.52	03/2020 -	02/2022
79	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	758.36	674.14	03/2020 -	02/2022
<u>Southern Railway</u>							
80	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	9/2007	724.69 -	3,081.20	1,726.52	02/2019 -	03/2025

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
81	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	4/2011	120.70 -	2,111.88	314.32	03/2019 -	12/2027
82	ERNAKULAM-KUMBALAM - [N22000204]	4/2010	189.24 -	448.10	268.74	- -	03/2025
83	MADURAI-BODINAYAKKANUR - [N22000201]	4/2008	164.41 -	591.00	430.16	- -	03/2022
84	KUMBALAM-TURAVUR - [N22000191]	4/2011	252.96 -	709.69	256.71	- -	03/2025
85	KURUPPANTHARA-CHINGAVANAM - [N22000190]	4/2007	270.14 -	749.40	591.35	- -	03/2022
86	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	9/1995	303.98 -	1,549.09	715.89	03/2020 -	03/2025
	<u>West Central Railway</u>						
87	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,439.82	03/2021 -	03/2024
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025
	<u>Western Railway</u>						
89	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024
90	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022
91	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025
	Total		72,247.37 -	1,98,748.18	1,42,058.70		
	<u>RENEWABLE ENERGY</u>						
	<u>Cpwd For Renewable Energy</u>						
92	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI [N28000118]	10/2017	271.90 -	365.00	282.96	11/2019 -	-
	Total		271.90 -	365.00	282.96		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
93	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM [N24000392]	11/2010	268.08 -	390.73	368.28	05/2017 06/2022	06/2022
94	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	557.20	12/2019 -	03/2022
95	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]	1/2017	166.67 -	264.34	187.00	09/2017 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
96	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	322.24	308.85	09/2014 03/2022	-
97	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	3/2018	325.86 -	386.41	351.36	10/2018 -	-
98	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022
99	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	353.43	334.89	12/2015 01/2021	-
100	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]	11/2013	683.83 -	698.82	709.80	07/2016 06/2022	06/2022
National Highways And Infrastructure Development Corporation Ltd.							
101	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	169.08	11/2018 -	11/2021
National Highways Authority Of India							
102	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
103	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 03/2022	03/2022
104	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,701.66	03/2013 -	04/2022
105	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]	6/2016	649.00 -	649.00	690.17	06/2019 -	-
106	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
107	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	985.40	04/2019 -	-
108	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	886.96	07/2008 -	-
109	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	8/2015	516.13 -	649.27	651.41	04/2018 -	-
110	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	8/2015	854.80 -	1,038.56	1,034.54	- -	-
111	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	2,360.65	4,516.44	- -	-
112	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	8/2015	814.04 -	825.17	846.15	- -	10/2021
113	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	1,457.82	1,347.64	03/2018 03/2021	-
114	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
115	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
116	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	6/2015	845.24 -	941.00	902.51	- 01/2020	01/2020
117	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
118	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	844.08	04/2018 -	03/2022
119	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022
120	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	03/2022
121	PATNA-MUZZAFFARPUR - [N24000165]	8/2010	671.30 -	671.30	1,199.64	02/2013 -	-
122	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]	7/2010	1,813.76 -	1,813.76	2,654.58	07/2013 -	-
123	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-
124	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	3,116.66	07/2015 -	09/2020
125	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
126	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
127	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-
128	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-
129	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	3/2017	1,184.71 -	1,310.00	1,307.68	03/2020 -	01/2022
130	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- [N24000636]	12/2016	1,031.95 -	1,031.95	1,518.41	- -	03/2022
131	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]	10/2016	447.75 -	447.75	1,344.55	- -	-
132	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]	10/2016	1,008.96 -	1,008.96	1,148.65	- -	03/2022
133	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	359.60	340.48	- -	05/2017
134	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]	11/2016	1,071.61 -	1,048.10	1,203.21	- 12/2021	05/2022
135	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	1,108.00	1,482.29	08/2019 -	-
136	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	8/2016	1,169.61 -	2,280.00	1,367.00	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
137	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022
138	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	671.00	- -	10/2022
139	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	3/2018	642.13 -	807.00	748.98	- -	-
140	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	3/2018	478.74 -	1,135.08	802.65	- 11/2022	-
141	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848	3/2018	181.78 -	181.78	191.96	- -	-
142	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810	3/2018	565.09 -	565.09	661.98	- -	02/2021
143	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809	3/2018	1,550.98 -	1,550.98	1,666.08	- -	09/2021
144	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	3/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022
145	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	3/2018	1,120.57 -	1,332.00	1,525.15	- -	-
146	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	3/2018	925.40 -	1,197.00	1,176.70	- -	-
147	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792	3/2018	809.07 -	1,065.70	930.46	- -	-
148	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,547.20	- -	-
149	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,442.06	- -	11/2021
150	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	495.92	- -	09/2021
151	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	3/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-
152	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	912.41	03/2020 -	-
153	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
154	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020
155	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	627.93	633.24	01/2016 -	-
156	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	417.68	433.68	01/2016 -	-
157	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	01/2016
158	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	469.31	459.07	01/2014 -	-
159	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205	12/2011	1,047.00 -	1,047.00	1,874.47	06/2014 -	-
160	4-LANING OF BRAHAMPORE-FARAKA - [N24000203	2/2011	998.79 -	998.79	1,913.66	08/2013 -	06/2023
161	4-LANING OF FARAKA-RAIGANJ - [N24000202	2/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	03/2022
162	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	2,933.43	06/2014 -	09/2022
163	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	591.00	578.00	11/2013 -	-
164	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	-
165	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	768.92	03/2014 -	-
166	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,287.35	05/2014 -	-
167	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022
168	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
169	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-
170	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
171	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
	Total		77,152.50 -	87,243.22	1,12,698.09		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
172	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	21,940.00	19,611.48	05/2015 01/2022	06/2022
	Total		15,525.00 -	21,940.00	19,611.48		
	<u>TELECOMMUNICATIONS</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Department Of Telecommunication</u>						
173	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022
	Total		13,334.00 -	24,664.00	20,545.00		
	<u>URBAN DEVELOPMENT</u>						
	<u>Chennai Metro Rail Ltd</u>						
174	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	2/2009	14,600.00 -	18,380.00	18,051.27	12/2015 -	-
	<u>Delhi Metro Rail Corporation</u>						
175	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	40,180.91	39,728.58	03/2016 08/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>						
176	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	6,218.14	6,065.82	07/2017 -	09/2020
	Total		58,366.79 -	64,779.05	63,845.67		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
177	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	299.08	03/2020 -	03/2022
178	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	380.87	01/2021 -	05/2022
	<u>Delhi Jal Board</u>						
179	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015	5/2016	211.79 -	211.79	261.19	12/2021 -	12/2022
	Total		706.19 -	879.32	941.14		
	Grand Total		2,74,633.16	4,55,450.11	4,11,923.07		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
1	PACHWARA SOUTH COAL BLOCK - [N06000193]	7/2013	1,795.01	1,795.01	38.76	09/2028	09/2023
	Total		1,795.01	1,795.01	38.76		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	232.40	09/2025	05/2024
	Total		1,828.00	1,828.00	232.40		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
3	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50	206.50	174.10	03/2021 03/2022	02/2022
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00	18,936.00	953.51	09/2024	08/2024
	Total		19,142.50	19,142.50	1,127.61		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
5	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71	1,522.71	1,114.48	09/2021 08/2022	03/2022
	Total		1,522.71	1,522.71	1,114.48		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
6	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,764.97	03/2024	03/2023
	<u>Rail Vikas Nigam Ltd.</u>						
7	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	2,006.69	12/2026	03/2025
8	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	.19	12/2025	03/2025
	Total		7,318.24	11,104.67	3,771.85		

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
9	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180	3/2019	237.51	237.51	110.76	12/2022 -	07/2022
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289	3/2019	403.68	403.68	108.53	03/2027 -	02/2023
	<u>National Highways Authority Of India</u>						
11	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00	733.00	-	01/2024 04/2024	01/2024
	Total		1,374.19 -	1,374.19	219.29		
	Grand Total		32,980.65	36,767.08	6,504.39		

FLASH REPORT

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	5,453.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	5,453.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	88.95	03/2023 03/2023	03/2023
	Total		611.80 -	611.80	88.95		
	<u>COAL</u>						
	<u>Central Coal Fields Limited</u>						
3	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	-	03/2028 -	03/2028
4	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	42.98	03/2023 -	03/2023
5	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]	7/2021	778.80 -	778.80	-	03/2026 -	03/2026
6	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	-	03/2028 -	03/2028
	<u>Eastern Coal Fields Limited</u>						
7	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	4.48	03/2027 -	03/2027
8	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	-	03/2029 -	03/2029
9	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	260.95	03/2022 -	03/2022
10	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	9.64	03/2025 -	03/2025
11	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	-	03/2029 -	03/2029
12	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	26.86	03/2029 -	03/2029
13	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	165.05	03/2024 -	03/2024
14	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
15	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	1.49	03/2027 -	03/2027
	<u>Mahanadi Coal Fields Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
16	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	-	03/2029 -	03/2029
17	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	-	03/2031 -	03/2031
18	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	841.95	03/2027 -	03/2027
19	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	-	03/2028 -	03/2028
20	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,718.35	03/2026 -	03/2026
21	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,341.19	03/2029 -	03/2029
	<u>Northern Coal Fields Limited</u>						
22	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	2.45	03/2023 -	03/2023
23	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
24	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
25	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
	<u>Singareni Colliers Company Limited</u>						
26	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	27.52	03/2023 -	03/2023
27	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	95.10	03/2023 -	03/2023
28	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	137.86	03/2024 -	03/2024
29	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]	11/2015	489.62 -	489.62	-	03/2023 -	03/2023
30	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	290.90	03/2022 -	03/2022
	<u>South-Eastern Coal Fields Limited</u>						
31	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,393.76	03/2023 -	03/2023
32	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
33	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	63.39	03/2026 -	03/2026
34	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
35	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [O60100093]	6/2010	11,816.40 -	11,816.40	4,768.67	03/2023 -	03/2023
36	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	12.61	03/2023 -	03/2023
37	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	2.02	03/2026 -	03/2026
38	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	2.59	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,881.55	03/2029 -	03/2029
40	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	10.32	03/2023 -	03/2023
41	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	-	03/2026 -	03/2026
42	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
43	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	362.52	03/2029 -	03/2029
44	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	190.30	03/2024 -	03/2024
45	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
46	VIJAY WEST OPENCAST PROJECT - [N06000158] <u>Western Coal Fields Limited</u>	5/2017	976.95 -	976.95	86.57	03/2026 -	03/2026
47	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
48	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	-	03/2027 -	03/2027
49	ADASA UG TO OC (1.50 MTY) - [N06000219]	11/2018	333.43 -	333.43	-	03/2024 -	03/2024
50	RPR FOR JAMUNIA UG - [N06000228]	8/2020	281.25 -	281.25	-	03/2026 -	03/2026
51	DHANKASA UG (RECAST) (1 MTY) - [N06000224]	2/2020	289.30 -	289.30	-	03/2025 -	03/2025
52	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	108.38	03/2028 -	03/2028
53	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	252.90	03/2022 -	03/2022
54	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
55	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]	11/2020	826.80 -	826.80	-	03/2026 -	03/2026
56	BHANEGAON OC (1MTY) - [N06000221]	2/2017	409.68 -	409.68	-	03/2023 -	03/2023
57	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
58	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	2.65	03/2026 -	03/2026
59	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	456.01	03/2025 -	03/2025
60	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]	9/2018	313.34 -	313.34	-	03/2024 -	03/2024
	Total		99,450.45 -	99,552.89	17,735.32		
	DEPARTMENT OF HIGHER EDUCATION						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Cpwd Of Higher Education</u>						
61	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	42.51	04/2023 04/2023	04/2023
	Total		676.00 -	676.00	42.51		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
62	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	439.65	09/2023 -	09/2023
	Total		1,404.00 -	1,404.00	439.65		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
63	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	338.87	03/2023 -	03/2023
64	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
	<u>Chennai Petroleum Corporation Limited</u>						
65	CBR 9 MMTA PROJECT - [N16000434]	1/2021	31,580.00 -	31,580.00	571.14	06/2025 -	06/2025
	<u>Gas Authority Of India Limited</u>						
66	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	152.67	10/2022 -	10/2022
67	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	265.22	04/2022 -	04/2022
68	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	2,002.80	05/2023 -	05/2023
69	60 KTA POLYPROPYLENE PROJECT - [N16000429]	3/2019	910.56 -	910.56	141.31	04/2024 -	04/2024
70	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	555.30	07/2022 -	07/2022
71	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430]	5/2019	8,797.00 -	8,797.00	210.01	04/2025 -	04/2025
72	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	365.30	11/2022 -	11/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
73	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,539.20	06/2022 -	06/2022
74	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022
75	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	466.13	11/2022 -	11/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
76	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	0.13	06/2024 -	06/2024
77	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	88.45	03/2024 -	03/2024
78	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	185.98	12/2022 -	12/2022
79	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,421.46	281.96	02/2023 -	02/2023
	<u>Indian Oil Corporation Limited</u>						
80	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	546.09	08/2022 -	08/2022
81	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	210.74	03/2030 -	03/2030
82	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	140.07	02/2028 -	02/2028
83	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	90.56	08/2027 -	08/2027
84	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	177.06	01/2023 -	01/2023
85	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]	12/2021	9,028.00 -	9,028.00	-	10/2024 -	10/2024
86	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	114.50	02/2028 -	02/2028
87	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	49.65	12/2029 -	12/2029
88	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	187.71	12/2022 -	12/2022
89	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	30.01	10/2023 -	10/2023
90	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	126.54	08/2022 -	08/2022
91	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	329.06	02/2028 -	02/2028
92	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	28.39	12/2029 -	12/2029
93	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	49.47	03/2030 -	03/2030
94	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	171.20	12/2029 -	12/2029
95	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	2,441.32	09/2022 -	09/2022
96	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	763.89	01/2024 -	01/2024
97	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	208.61	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
98	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	88.43	07/2022 -	07/2022
99	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	117.00	08/2027 -	08/2027
100	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]	2/2021	34,627.00 -	34,627.00	538.73	09/2024 -	09/2024
101	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	66.18	08/2023 -	08/2023
102	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	836.13	05/2023 -	05/2023
103	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	43.28	12/2029 -	12/2029
104	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	2,561.63	04/2023 -	04/2023
105	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	68.94	02/2027 -	02/2027
106	CGD PROJECT AT ARVAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	133.31	02/2028 -	02/2028
	<u>Numaligarh Refinery Limited</u>						
107	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINERY - [N16000379]	1/2019	12,366.00 -	18,968.00	940.95	10/2024 -	10/2024
108	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	1,966.98	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
109	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	947.93	03/2026 -	03/2026
110	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431]	8/2021	885.63 -	885.63	206.93	02/2026 -	02/2026
111	PIPELINE REPLACEMENT PROJECT - VII - [N16000436]	1/2022	3,183.58 -	3,183.58	-	05/2024 -	05/2024
112	REDEVELOPMENT OF LINCH FIELD - [N16000428]	4/2021	631.03 -	631.03	228.08	03/2025 -	03/2025
113	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON - [N16000433]	8/2021	218.38 -	218.38	33.82	02/2023 -	02/2023
114	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]	2/2020	444.87 -	444.87	171.45	08/2022 -	08/2022
	Total		2,01,341.40 -	2,06,815.06	22,235.29		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
115	CHHATTARGARH 150 MW - [N18000294]	2/2021	599.99 -	599.99	71.06	07/2022 -	07/2022
116	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]	5/2021	674.92 -	674.92	76.91	09/2022 -	09/2022
117	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]	1/2021	842.27 -	842.27	93.92	07/2022 -	07/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
118	BHENSARA 320 MW - [N18000293]	1/2021	1,221.73 -	1,221.73	140.11	07/2022 -	07/2022
	<u>Power Grid Corporation Of India Limited</u>						
119	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]	6/2021	1,006.00 -	1,006.00	253.02	12/2022 -	12/2022
120	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]	3/2021	1,340.81 -	1,340.81	151.70	12/2022 -	12/2022
121	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]	5/2021	179.29 -	179.29	5.66	04/2023 -	04/2023
122	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]	1/2019	267.33 -	267.33	31.72	03/2022 -	03/2022
123	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]	5/2021	1,184.88 -	1,184.88	12.83	09/2022 -	09/2022
124	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]	6/2021	1,562.00 -	1,562.00	249.63	12/2022 -	12/2022
125	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]	3/2021	353.85 -	353.85	22.91	12/2022 -	12/2022
126	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]	6/2021	713.82 -	713.82	130.01	12/2022 -	12/2022
127	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]	5/2021	576.42 -	576.42	-	03/2023 -	03/2023
	<u>Satluj Jal Vidyut Nigam Limited</u>						
128	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	4,677.91	01/2024 -	01/2024
129	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	622.39	01/2026 -	01/2026
130	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	298.99	12/2022 -	12/2022
131	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	215.23	11/2025 -	11/2025
132	Bagodara Solar Power Project - [N18000297]	5/2021	296.20 -	296.20	0.43	10/2022 -	10/2022
	Total		24,070.71 -	24,070.71	7,054.43		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
133	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
134	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023
135	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
136	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
	<u>North Eastern Railway</u>						
137	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,518.04	03/2022 -	03/2022
	<u>National High Speed Rail Corporation Limited</u>						
138	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	21,986.54	12/2023 -	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
139	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,300.00	2,564.14	03/2023 -	03/2023
140	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	2,601.90	12/2023 -	12/2023
141	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,683.68	12/2023 -	12/2023
142	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	1,248.22	12/2024 -	12/2024
	Total		1,36,557.67 -	1,42,036.87	35,688.92		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
143	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]	7/2018	1,948.25 -	1,948.25	313.56	02/2024 -	02/2024
144	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	108.20	03/2024 -	03/2024
145	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	49.89	02/2024 -	02/2024
146	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	236.18	86.74	12/2022 -	12/2022
147	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]	2/2021	925.47 -	925.47	0.06	07/2025 -	07/2025
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
148	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
149	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]	11/2020	332.14 -	332.14	10.93	07/2022 -	07/2022
150	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
151	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
152	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	174.37	12/2023 -	12/2023
153	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	72.45	07/2022 -	07/2022
154	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
155	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	36.62	05/2024 -	05/2024
156	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
157	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
158	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	46.59	12/2022 -	12/2022
159	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	11.84	12/2022 -	12/2022
160	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	48.49	12/2023 -	12/2023
161	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	36.05	08/2022 -	08/2022
162	IMPHAL – MOREH (PACKAGE 4) - [N24001399]	3/2021	277.99 -	277.99	5.57	01/2023 -	01/2023
163	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
164	KHELLANI-KHANABAL PKG-4 - [N24001395]	7/2021	859.67 -	859.67	9.03	08/2023 -	08/2023
165	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	33.72	01/2024 -	01/2024
166	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]	8/2020	292.80 -	292.80	42.83	05/2022 -	05/2022
167	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]	3/2020	165.54 -	165.54	14.10	07/2022 -	07/2022
168	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	96.67	04/2023 -	04/2023
169	MARIAM - PEREN (PKG 2A) - [N24001398]	7/2021	204.58 -	204.58	10.48	03/2023 -	03/2023
170	KHELLANI-KHANABAL PKG-5 - [N24001396]	7/2021	497.09 -	497.09	10.16	02/2023 -	02/2023
171	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]	9/2019	761.54 -	761.54	155.57	05/2023 -	05/2023
172	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) - [N24001393]	8/2020	184.88 -	184.88	48.06	04/2022 -	04/2022
173	SENAPATI- IMPHAL PKG-5B - [N24001400]	3/2021	211.70 -	211.70	-	01/2023 -	01/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
174	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
175	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	301.78	12/2023 -	12/2023
176	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	91.93	08/2022 -	08/2022
177	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	39.88	07/2022 -	07/2022
178	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	22.21	07/2022 -	07/2022
179	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	29.96	04/2022 -	04/2022
180	TAMENGLONG - MAHUR PKG-1 - [N24001402]	7/2021	185.80 -	185.80	6.20	03/2023 -	03/2023
181	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	32.50	04/2023 -	04/2023
182	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	8.23	01/2023 -	01/2023
183	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	55.18	04/2022 -	04/2022
184	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]	3/2020	242.97 -	242.97	59.98	06/2022 -	06/2022
185	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	99.97	07/2022 -	07/2022
186	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
187	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	6.59	03/2023 -	03/2023
188	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]	3/2019	471.00 -	471.00	167.94	07/2022 -	07/2022
189	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]	9/2020	277.44 -	277.44	33.95	10/2022 -	10/2022
190	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	45.79	12/2022 -	12/2022
191	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	64.91	06/2022 -	06/2022
192	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	624.88	09/2028 -	09/2028
193	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95 -	278.95	101.27	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
194	KHELLANI-KHANABAL PKG-2 - [N24001394]	7/2021	512.43 -	512.43	16.50	02/2023 -	02/2023
195	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	47.29	07/2022 -	07/2022
196	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
197	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	78.46	09/2022 -	09/2022
198	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
199	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	60.00	06/2023 -	06/2023
200	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	79.81	06/2022 -	06/2022
201	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) [N24001279]	3/2020	216.49 -	216.49	70.76	07/2022 -	07/2022
202	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) - [N24001392]	8/2020	199.03 -	199.03	59.12	04/2022 -	04/2022
203	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]	3/2020	216.49 -	216.49	50.81	03/2022 -	03/2022
204	IMPHAL - KHONGSANG PKG-3 - [N24001401]	7/2021	467.00 -	467.00	-	03/2023 -	03/2023
205	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	6.41	12/2022 -	12/2022
206	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) [N24001283]	3/2020	281.78 -	281.78	120.63	07/2022 -	07/2022
207	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	16.96	12/2022 -	12/2022
208	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	10.11	01/2023 -	01/2023
209	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	59.71	06/2022 -	06/2022
210	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
211	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391]	8/2020	294.04 -	294.04	91.30	04/2022 -	04/2022
212	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	66.51	12/2022 -	12/2022
213	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	31.06	05/2022 -	05/2022
214	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
215	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	13.63	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
216	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248	8/2020	208.84 -	208.84	27.45	04/2022 -	04/2022
217	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
218	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355	3/2021	374.39 -	374.39	43.39	12/2022 -	12/2022
219	KARGIL-ZANSKR PACKAGE-8 - [N24001348	3/2021	398.37 -	398.37	9.04	01/2023 -	01/2023
220	PEREN-DIMAPUR SECTION PKG-2 - [N24001406	7/2021	258.52 -	258.52	31.67	03/2023 -	03/2023
221	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244	8/2020	301.06 -	301.06	30.42	04/2022 -	04/2022
222	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
223	TLABUNG - LUNGLEI PKG-A - [N24001358	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
224	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	32.96	10/2022 -	10/2022
225	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	25.14	04/2022 -	04/2022
226	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311	11/2020	206.78 -	206.78	87.79	07/2022 -	07/2022
227	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328	12/2020	804.00 -	804.00	93.33	08/2023 -	08/2023
228	DABOKA KATHKATI PACKAGE-4 - [N24001365	2/2021	260.07 -	260.07	78.09	12/2023 -	12/2023
229	GOHA-KHELLANI PKG-3 - [N24001397	2/2021	431.28 -	431.28	40.41	03/2023 -	03/2023
230	PEREN-DIMAPUR PKG-5 - [N24001407	2/2021	207.33 -	207.33	-	03/2023 -	03/2023
231	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	42.83	06/2022 -	06/2022
232	KHELLANI-KHANABAL PKG-6 - [N24001324	2/2021	285.28 -	285.28	36.42	09/2022 -	09/2022
233	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325	9/2020	262.84 -	262.84	120.72	05/2023 -	05/2023
234	TAMENGLONG - MAHUR PKG-3 - [N24001354	3/2021	234.08 -	234.08	15.09	12/2022 -	12/2022
235	DOGINALA - GAU - [N24001320	12/2020	242.30 -	242.30	9.31	09/2022 -	09/2022
236	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312	3/2020	167.95 -	167.95	50.50	06/2022 -	06/2022
237	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331	3/2020	261.13 -	261.13	31.46	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
238	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	439.59	09/2026 -	09/2026
239	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
240	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	14.79	12/2022 -	12/2022
241	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]	9/2020	183.31 -	183.31	76.84	05/2022 -	05/2022
242	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	41.90	06/2022 -	06/2022
243	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
244	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	48.15	04/2023 -	04/2023
245	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
246	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	16.08	12/2022 -	12/2022
247	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]	10/2020	157.86 -	157.86	68.77	04/2022 -	04/2022
248	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	6.70	12/2022 -	12/2022
249	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	12.26	04/2022 -	04/2022
250	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	171.47	12/2023 -	12/2023
251	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389]	3/2020	206.53 -	206.53	88.93	06/2022 -	06/2022
252	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	9.39	04/2022 -	04/2022
253	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	71.71	03/2022 -	03/2022
254	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	11.12	10/2023 -	10/2023
255	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	38.81	06/2024 -	06/2024
256	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	44.52	12/2023 -	12/2023
257	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	22.78	03/2023 -	03/2023
258	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]	11/2020	159.13 -	159.13	12.02	06/2022 -	06/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
259	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	7.02	04/2022 -	04/2022
260	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) - [N24001390	8/2020	228.71 -	228.71	48.24	04/2022 -	04/2022
	<u>National Highways Authority Of India</u>						
261	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
262	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
263	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
264	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
265	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
266	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
267	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00 -	733.00	-	01/2024 04/2024	01/2024
	Total		61,140.78 -	61,179.29	7,083.27		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
268	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	2,013.22	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	2,013.22		
	<u>SOCIAL JUSTICE</u>						
	<u>Central Public Works Department</u>						
269	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	-	03/2024 -	03/2024
	Total		170.99 -	170.99	.00		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
270	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	89.30	12/2023 -	12/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
271	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	57.81	05/2023 -	05/2023
272	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125	1/2022	970.18 -	970.18	-	05/2025 -	05/2025
	Total		1,889.60 -	1,889.60	147.11		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
273	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	431.21	03/2024 -	03/2024
	<u>Bangalore Metro Rail Corporation Limited</u>						
274	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151	6/2021	14,788.10 -	14,788.10	2,290.84	06/2026 -	06/2026
	<u>Delhi Metro Rail Corporation</u>						
275	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135	7/2019	24,948.65 -	24,948.65	2,949.03	03/2025 -	03/2025
	<u>National Capital Region Transport Corp</u>						
276	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	6,762.86	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
277	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,925.50	307.63	06/2024 -	06/2024
	Total		88,760.69 -	89,320.42	12,741.57		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
278	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014	3/2017	665.78 -	942.18	261.19	12/2022 -	12/2022
	Total		665.78 -	942.18	261.19		
	Grand Total		6,71,730.05	6,82,924.62	1,10,984.43		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	6,268.20	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	19,220.00	17,806.00	12/2015 -	12/2022	67.73
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	14,142.00	12/2016 -	12/2023	38.63
	Total		27,271.00 -	43,139.00	38,216.20			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	707.73	507.91	09/2018 -	10/2022	69.63
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 -	1,938.00	579.75	09/2021 -	12/2023	40.13
6	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	145.28	09/2021 -	12/2023	38.72
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	391.13	03/2021 -	03/2025	7.88
	Total		3,288.50 -	4,358.06	1,624.07			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	32.60	04/2018 -	06/2023	37.56
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	91.55	03/2017 -	12/2022	12.20
	<u>Eastern Coal Fields Limited</u>							
10	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	625.60	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>							
11	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	808.97	815.72	03/2013 -	03/2024	68.70
	<u>Neyveli Lignite Corporation</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,429.39	12/2015 -	02/2021	35.10
13	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	13,185.30	11/2021 -	06/2023	.00
	<u>Western Coal Fields Limited</u>							
14	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	213.93	03/2019 -	03/2022	1.39
15	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	08/2015	727.28 -	745.03	456.01	03/2025 -	03/2025	2.44
16	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	252.90	03/2022 -	03/2022	26.49
	Total		28,175.10 -	33,298.68	23,103.00			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
17	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	318.32	06/2017 -	-	.57
18	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	580.00	559.49	07/2019 -	07/2021	5.59
19	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	210.60	206.20	09/2020 -	-	13.23
	Total		1,231.49 -	1,289.59	1,084.01			
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
20	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	9,574.07	09/2019 -	-	9.80
	<u>Iicc For Dpiit</u>							
21	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	3,062.37	12/2019 -	05/2022	8.49
	Total		17,352.09 -	18,990.30	12,636.44			
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
22	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	586.50	11/2013 -	09/2021	41.63
23	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	06/2021	22.29

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
24	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
25	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	01/2021	13.20
26	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	586.96	586.96	03/2018 -	04/2020	16.10
27	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	177.21	02/2018 -	04/2021	16.33
28	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	12/2021	1.64
29	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	280.00	273.40	03/2019 -	02/2021	2.87
30	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	205.00	191.36	- -	01/2022	30.94
31	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]	03/2018	268.84 -	284.67	279.53	- -	05/2021	5.89
32	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	245.78	- -	05/2021	.02
	<u>Nbcc For Health</u>							
33	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	1,089.38	09/2021 -	06/2022	8.88
	Total		4,281.23 -	4,855.32	4,373.55			
	<u>HEAVY INDUSTRY</u>							
	<u>Natrip Implementation Socity</u>							
34	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	3,526.63	09/2011 -	-	116.96
	Total		1,718.00 -	3,727.30	3,526.63			
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
35	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	1,089.05	10/2019 -	06/2022	64.04
36	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	228.63	173.62	04/2018 -	12/2022	40.37
37	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI [N45000002]	06/2019	277.35 -	290.33	46.80	07/2022 -	12/2022	4.68
	Total		1,659.44 -	2,518.96	1,309.47			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
	<u>National Aluminum Company Limited (Nalco)</u>							
38	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	6,435.90	1,268.54	04/2021 -	01/2024	16.17
39	UTKAL D AND E COAL BLOCK - [N10000011]	05/2016	534.00 -	667.23	395.98	01/2020 -	11/2023	24.95
40	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	581.00	96.18	11/2020 -	12/2023	63.66
	Total		6,429.00 -	7,684.13	1,760.70			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
41	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11
42	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	855.28	06/2019 -	02/2023	35.54
	<u>Gas Authority Of India Limited</u>							
43	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,781.00	12/2012 -	02/2025	102.71
44	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	265.22	04/2022 -	04/2022	20.06
45	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	120.91	02/2021 -	10/2022	9.91
46	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	233.20	08/2020 -	04/2022	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
47	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	18,232.09	07/2020 -	07/2022	25.50
48	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>							
49	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	568.65	10/2017 -	12/2022	103.60
50	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,315.92	03/2021 -	05/2022	66.09
51	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,154.79	12/2020 -	03/2022	43.82

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
52	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00	6,025.00	4,270.46	12/2018	06/2022	33.98
53	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00	437.00	226.74	01/2021	08/2022	25.57
54	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02	207.36	135.65	04/2020	10/2022	27.20
55	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00	319.61	237.99	06/2020	12/2021	35.43
56	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63	340.76	172.39	02/2020	07/2022	64.91
57	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	03/2018	588.20	730.20	226.83	-	05/2023	24.14
58	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00	753.89	495.80	02/2020	07/2022	26.07
59	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30	543.00	176.32	09/2021	06/2022	17.46
60	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00	427.10	41.54	09/2022	03/2023	15.12
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
61	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00	304.00	2.61	06/2023	01/2024	52.00
	<u>Numaligarh Refinery Limited</u>							
62	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]	01/2019	12,366.00	18,968.00	940.95	10/2024	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>							
63	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	2,001.34	1,613.65	05/2013	05/2022	132.23
64	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69	3,375.90	2,892.72	04/2018	05/2022	5.80
65	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27	1,137.79	784.66	03/2023	03/2022	38.20
66	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80	3,976.67	1,790.56	03/2022	05/2023	23.16
67	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71	3,740.05	3,233.86	05/2021	05/2022	2.17
68	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	05/2019	763.92	829.58	829.58	12/2020	05/2022	8.60

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Oil India Limited</u>							
69	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	412.80	02/2020 -	06/2022	17.41
	Total		66,969.75 -	91,502.05	50,762.56			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
70	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62 -	1,311.05	200.27	06/2006 -	-	126.58
71	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	9,558.69	09/2009 -	03/2023	152.52
72	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	15,300.08	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
73	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	5,247.00	03/2013 -	12/2024	96.99
74	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	17,007.00	12,634.00	06/2019 -	01/2024	18.38
75	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,803.00	754.00	09/2019 -	07/2025	30.48
76	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	9,014.00	07/2012 -	-	97.38
77	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,748.00	05/2018 -	03/2022	33.47
78	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	19,738.00	10/2011 -	07/2023	145.16
79	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	9,223.00	11/2020 -	02/2023	3.76
80	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	5,289.25	3,776.81	10/2017 -	-	24.81
81	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,426.00	2,027.32	12/2018 -	03/2022	28.69
82	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	679.00	513.91	11/2018 -	06/2022	28.19
83	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 -	524.83	400.95	09/2021 -	03/2022	4.70
84	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 -	852.90	596.05	09/2021 -	05/2022	6.85
85	NOKHRA - [N18000282]	03/2020	1,722.14 -	1,803.19	612.20	09/2021 -	10/2022	4.71
86	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	118.68	10/2021 -	10/2022	11.93
87	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 -	442.03	293.40	04/2021 -	05/2022	9.99

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Power Grid Corporation Of India Limited</u>							
88	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,199.00	12,394.95	08/2013 -	03/2018	18.59
89	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.89	11/2016 -	03/2022	4.61
90	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	3,182.67	12/2018 -	03/2024	92.02
91	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,522.04	12/2018 -	01/2024	31.08
92	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	04/2022	14.11
93	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	169.82	07/2019 -	08/2022	17.99
94	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	1,832.15	02/2020 -	04/2023	36.46
	<u>Satluj Jal Vidyut Nigam Limited</u>							
95	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022	46.20
	<u>Thdc India Limited</u>							
96	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,416.30	06/2013 -	06/2025	54.94
97	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,409.29	02/2016 -	06/2023	191.23
	Total		1,09,390.83 -	1,74,426.52	139,084.02			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
98	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023	8.75
99	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	75.00
100	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	111.08
101	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
102	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	-	03/2024 -	-	25.04
103	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	.89
104	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023	10.94

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Container Corporation Of India</u>							
105	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
106	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	51,219.00	35,951.00	- -	-	341.96
107	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	47,476.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
108	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,650.00	3,679.49	- -	07/2022	253.32
109	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,610.87	- -	12/2024	290.95
110	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,090.00	1,093.59	03/2012 -	06/2023	235.66
111	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	614.45	353.25	- -	03/2025	277.26
112	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	320.25	- -	12/2024	36.67
113	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	964.41	03/2019 -	-	37.04
114	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	1,625.87	981.50	- -	03/2024	253.52
115	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	2.55	- -	-	818.15
116	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	735.20	392.88	- -	12/2024	126.22
117	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,893.55	386.78	- -	-	400.20
118	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,470.50	1,536.32	- -	03/2024	295.15
119	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	49.45
120	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	585.85	03/2021 -	12/2024	63.37
121	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	452.12	03/2021 -	03/2024	62.06
122	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	1,469.46	- -	03/2024	350.27
	<u>East Coast Railway</u>							
123	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	947.41	06/2021 -	03/2025	137.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
124	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,729.29	03/2009 -	12/2024	29.71
125	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	1,243.24	02/2019 -	03/2022	38.43
126	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	1,036.36	03/2020 -	03/2024	.07
127	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	209.78	11/2018 -	03/2025	15.45
	<u>Eastern Railways</u>							
128	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	912.17	03/2019 12/2009	03/2025	36.22
129	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	508.16	03/2017 -	03/2025	20.30
130	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	333.93	- -	03/2022	181.63
131	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	310.70	418.15	- -	03/2024	23.82
132	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	311.86	- -	03/2022	6.48
133	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	472.06	03/2022 -	03/2025	133.39
134	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	502.48	529.13	- -	02/2022	74.26
135	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	622.26	03/2016 -	03/2024	7.75
	<u>Indian Railway Construction Company Limited</u>							
136	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	1,078.79	03/2022 -	09/2023	117.23
137	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	2,800.17	09/2018 -	06/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>							
138	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022	501.57
139	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	774.51	539.14	06/2013 -	12/2022	56.23
140	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	75.91
	<u>North Central Railway</u>							
141	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	534.75	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
142	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.00	4,766.68	03/2014 -	12/2023	172.70
143	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.00	12,156.19	03/2011 -	12/2023	221.54
144	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,145.79	937.36	03/2019 -	03/2024	197.45
145	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	1,108.94	03/2019 -	03/2024	302.54
146	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	1,534.31	03/2015 -	03/2026	186.39
147	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	2,504.91	12/2015 -	12/2023	542.04
148	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	2,047.51	586.70	03/2019 -	12/2023	13.88
149	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	708.73	549.81	03/2020 -	09/2022	24.42
150	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	265.38	03/2021 -	-	350.44
151	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	76.57	03/2020 -	-	94.45
152	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	401.65	338.00	- -	03/2023	66.30
153	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	157.78	03/2020 -	-	80.79
154	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,986.82	03/2022 -	03/2023	32.15
155	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,646.66	03/2021 -	03/2022	115.07
<u>North Eastern Railway</u>								
156	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	-	358.99
157	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	728.92	613.91	01/2019 -	-	147.09
158	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	-	.16
159	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,824.00	1,518.04	03/2022 -	03/2022	40.80
160	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	88.76	04/2016 -	-	.16
161	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	127.77
162	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	-	01/2018 -	-	.15
163	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	164.95	- -	12/2023	32.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>North Western Railway</u>							
164	DAUSA-GANGAPUR CITY(NL),NWR - [N22000184	02/1997	410.08 -	860.41	775.62	02/2019 -	06/2022	109.82
165	PHULERA - DIGANA DOUBLING - [N22000326	05/2015	600.00 -	701.81	342.53	03/2020 -	10/2022	16.97
	<u>Northern Railway</u>							
166	GRADE SEPERATOR AT DAYABASTI - [N22000269	04/1999	156.65 -	359.00	118.38	-	03/2024	129.17
167	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	893.45	760.84	12/2011 -	-	211.31
168	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274	04/2007	336.91 -	791.39	689.83	-	09/2023	134.90
169	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281	04/2012	295.68 -	419.00	167.23	-	09/2023	41.71
170	NANGALDAM-TALWARA(NL),NR - [N220100188	03/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024	348.44
171	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [N220100133	03/1995	2,500.00 -	37,012.26	27,846.00	11/2002 -	04/2023	1,380.49
172	CHANDIGARH-BADDI - [N22000467	04/2007	328.14 -	1,540.13	480.97	03/2023 -	12/2025	369.35
173	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492	03/2002	625.00 -	839.00	839.36	03/2016 -	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>							
174	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325	04/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022	102.92
175	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327	04/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022	224.56
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,834.54	1,586.17	03/2016 -	07/2025	65.94
177	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	2,006.69	12/2026 -	03/2025	127.62
178	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	3,300.00	2,564.14	03/2023 -	03/2023	55.15
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	3,139.94	03/2016 -	03/2026	7.78
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
181	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022	141.61
182	DHASA-JETALSAR (GC) - [N22000141	04/2012	644.38 -	923.28	995.52	03/2021 -	05/2022	43.28
183	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022	63.88

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
184	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	619.35	03/2016 -	04/2022	50.15
185	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	3,683.68	12/2023 -	12/2023	9.32
186	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022	58.97
187	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	1,248.22	12/2024 -	12/2024	9.83
188	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023	57.26
189	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	6,259.16	12/2024 -	03/2025	52.07
190	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022	281.93
191	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	2,139.84	12/2024 -	12/2026	42.47
192	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022	111.91
193	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023	64.62
194	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022	86.23
195	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022	23.55
196	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022	102.11
South Central Railway								
197	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027	102.85
198	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	695.73	03/2010 -	03/2025	18.38
199	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	-	-	161.86
200	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	803.75	03/2023 -	03/2024	5.16
201	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	713.38	03/2020 -	03/2022	31.75
202	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	347.14	03/2014 -	03/2027	42.44
203	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023	98.57
204	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,495.93	03/2022 -	03/2025	7.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
205	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	75.42	03/2022 -	-	102.36
	<u>South East Central Railway</u>							
206	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,176.60	1,576.19	03/2023 -	12/2023	66.44
207	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022	116.46
208	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60
209	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	2,135.34	833.36	03/2021 -	12/2023	8.23
210	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	795.59	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
211	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.97	1,155.00	03/2020 -	06/2022	35.38
212	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508	04/2018	428.65 -	472.50	1.62	06/2022 -	12/2025	10.23
213	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509	04/2018	390.39 -	511.75	149.63	12/2021 -	01/2023	31.09
214	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510	04/2018	338.00 -	393.83	23.56	06/2022 -	12/2023	16.52
	<u>South Western Railway</u>							
215	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 -	2,000.97	83.08	- -	03/2025	11.10
216	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,530.09	326.02	03/2016 -	12/2026	55.13
217	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.43	-	- -	03/2028	24.09
218	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	-	- -	03/2028	57.65
219	RAYADURGA-TUMKUR NL - [N22000279	04/2007	2,062.30 -	2,404.03	1,108.07	- -	12/2025	16.57
220	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	-	- -	03/2027	12.38
221	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	2,315.00 -	5,174.30	158.11	- -	03/2028	123.51
222	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2028	.02
223	HUBLI- CHIKJAJUR - [N22000325	03/2015	1,156.94 -	1,954.21	1,238.40	03/2020 -	12/2022	68.91
224	YELAHANKA-PENUKONDA - [N22000328	05/2015	860.43 -	1,104.00	1,014.52	03/2020 -	02/2022	28.31

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
225	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	758.36	674.14	03/2020 -	02/2022	31.20
226	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,530.18	03/2019 -	02/2024	16.31
227	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	817.23	495.18	03/2017 -	03/2026	26.75
	<u>Southern Railway</u>							
228	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	3,081.20	1,726.52	02/2019 -	03/2025	325.17
229	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,444.00	241.49	- -	12/2025	490.91
230	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,549.09	715.89	03/2020 -	03/2025	409.60
231	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	264.51	- -	-	79.80
232	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	0.63	- -	03/2030	.00
233	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	591.35	- -	03/2022	177.41
234	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	256.71	- -	03/2025	180.55
235	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	591.00	430.16	- -	03/2022	259.47
236	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	268.74	- -	03/2025	136.79
237	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	2,111.88	314.32	03/2019 -	12/2027	1,649.69
238	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	0.83	- -	03/2025	33.90
	<u>West Central Railway</u>							
239	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	1,439.82	03/2021 -	03/2024	585.35
240	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	3,230.57
241	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 -	2,445.30	1,392.72	03/2020 -	10/2024	38.63
242	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	16.02
243	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	561.88	03/2022 -	12/2023	114.32
	<u>Western Railway</u>							
244	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,383.82	2,404.99	03/2022 -	03/2026	82.20

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
245	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	1.06
246	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024	167.96
247	CHOTTADEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	1,010.81	03/2022 -	10/2027	13.17
248	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025	329.77
249	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022	33.41
250	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,056.11	808.35	03/2021 -	12/2022	5.36
251	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM [N22000434]	03/2010	265.88 -	311.36	-	-	-	17.11
252	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	152.98	-	-	81.07
253	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	123.75	-	-	112.88
254	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25 -	742.88	2.26	03/2020 -	03/2024	7.31
	Total		2,12,988.70 -	4,76,053.67	276,311.94			
	<u>RENEWABLE ENERGY</u>							
	<u>Cpwd For Renewable Energy</u>							
255	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI [N28000118]	10/2017	271.90 -	365.00	282.96	11/2019 -	-	34.24
	Total		271.90 -	365.00	282.96			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
256	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	978.43	03/2011 -	-	58.98
257	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	329.03	10/2010 -	-	69.30
258	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B [N24000331]	01/2014	282.41 -	319.96	193.60	03/2016 -	04/2022	13.30

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
259	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	244.36	- -	01/2020	3.72
260	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382	01/1991	675.00 -	780.77	424.27	- -	06/2022	15.67
261	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	368.28	05/2017 -	06/2022	45.75
262	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	851.32	- -	-	1.75
263	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	384.74	10/2010 -	-	93.80
264	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	404.10	345.06	- -	06/2022	26.41
265	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000574	11/2013	683.83 -	698.82	709.80	07/2016 -	06/2022	2.19
266	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576	02/2016	178.85 -	225.06	168.79	05/2016 -	06/2022	25.84
267	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000578	02/2016	553.30 -	587.41	537.14	05/2016 -	03/2022	6.16
268	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	01/2014	1,408.85 -	2,138.16	1,241.55	10/2016 -	03/2022	51.77
269	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	.26
270	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	107.06	06/2016 -	-	.02
271	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	116.25	- -	-	.06
272	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	148.90	11/2019 -	-	.08
273	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	174.90	154.26	08/2018 -	03/2022	5.23
274	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2023	7.39
275	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 -	213.97	27.41	08/2019 -	03/2023	33.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
276	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	78.56	08/2019 -	03/2023	11.18
277	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	331.86	08/2017 -	-	42.48
278	UPGRADATION OF PORSABHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	182.97	08/2018 -	03/2022	4.45
279	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	807.22	06/2019 -	03/2022	8.17
280	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922	12/2017	867.97 -	913.49	645.24	11/2018 -	07/2022	5.24
281	FOUR LANEING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	334.89	12/2015 -	-	6.07
282	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970	01/2017	576.48 -	686.13	438.61	01/2018 -	-	19.02
283	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	169.64	07/2019 -	11/2020	.31
284	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022	9.23
285	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156	01/2017	166.67 -	264.34	187.00	09/2017 -	-	58.60
286	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	234.82	01/2019 -	-	7.06
287	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 -	386.41	351.36	10/2018 -	-	18.58
288	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	369.96	322.13	09/2019 -	11/2020	10.03
289	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	308.85	09/2014 -	-	72.36
290	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	1,251.08	- -	12/2021	2.93
291	FOUR LANEING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	12.16
292	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	126.00	- -	03/2022	13.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
293	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	288.50	08/2016 -	12/2022	15.19
294	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	402.15	09/2016 -	03/2022	14.24
295	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	486.06	10/2016 -	06/2022	17.04
296	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	86.74	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
297	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	158.08	04/2017 -	03/2022	29.48
298	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	159.83	04/2017 -	03/2022	29.48
299	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	356.14	08/2016 -	-	3.73
300	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	159.32	04/2017 -	03/2022	27.16
301	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	295.14	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>							
302	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	-	04/2009 -	-	70.23
303	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	-	11/2008 -	-	159.95
304	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	-	11/2008 -	-	64.62
305	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15
306	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
307	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	16.67
308	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66
309	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	578.00	11/2013 -	-	15.53
310	MUZAFFARNAGAR-HARIDWAR - [N24000201]	09/2011	754.00 -	2,047.64	1,364.18	03/2013 -	-	171.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
311	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	-	61.08
312	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]	11/2011	478.51 -	1,082.40	1,023.73	10/2013 -	03/2022	126.20
313	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	-	18.88
314	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	-	26.66
315	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022	40.22
316	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	277.34	-	-	.77
317	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022	20.90
318	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	07/2015	2,128.72 -	2,408.72	1,577.44	04/2019 -	-	13.15
319	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	902.51	-	01/2020	11.33
320	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,414.01	990.95	06/2018 -	-	30.56
321	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	09/2015	934.46 -	1,457.82	1,347.64	03/2018 -	-	56.01
322	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	846.15	-	-	1.37
323	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	550.29	-	-	6.11
324	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	296.90	-	-	1.33
325	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	1,096.52	518.73	04/2018 -	-	50.90
326	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,516.44	-	-	41.78
327	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,034.54	-	-	21.50
328	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	651.41	04/2018 -	-	25.80
329	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	-	-	-	44.60
330	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
331	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]	03/2016	870.00 -	1,418.78	36.30	03/2019 -	10/2021	63.08

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
332	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	03/2016	899.00 -	1,376.86	887.23	04/2019 -	06/2022	53.15
333	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]	03/2016	720.00 -	793.63	291.10	- -	09/2022	10.23
334	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]	03/2016	1,443.00 -	2,330.79	1,246.85	- -	02/2022	61.52
335	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]	03/2016	1,668.00 -	2,501.85	946.08	- -	-	49.99
336	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]	03/2016	1,737.00 -	2,421.37	2,192.68	- -	12/2021	39.40
337	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 -	486.00	406.73	- -	-	6.11
338	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	14.40
339	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,367.00	- -	-	94.94
340	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	355.24	322.26	08/2018 -	-	9.74
341	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,482.29	08/2019 -	-	16.55
342	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	359.60	340.48	- -	-	23.69
343	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	1,023.23	980.59	07/2018 -	05/2022	68.89
344	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11 -	1,361.00	461.82	- -	-	8.78
345	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	1,307.68	03/2020 -	-	10.58
346	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	07/2024	31.88
347	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	-	03/2020 -	01/2022	3.40
348	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	-	03/2020 -	01/2022	5.56
349	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	1.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
350	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	-	03/2020 -	-	5.70
351	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	466.03	03/2020 -	03/2023	.23
352	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	830.31	105.50	03/2020 -	03/2023	23.39
353	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	970.99	03/2020 -	-	13.97
354	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	1,100.45	03/2020 -	03/2022	10.24
355	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	18.50
356	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	41.54
357	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	1,319.54	03/2020 -	-	44.39
358	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	04/2017	894.00 -	929.32	810.00	04/2020 -	06/2022	3.95
359	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	1.78
360	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]	08/2017	950.64 -	1,168.00	354.24	08/2017 -	10/2023	22.86
361	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]	10/2017	964.17 -	1,198.64	1,014.01	10/2017 -	-	24.32
362	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,300.00	971.90	09/2017 -	05/2022	15.65
363	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 -	448.18	495.92	-	-	10.68
364	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]	01/2018	573.70 -	726.99	156.13	-	06/2023	26.72
365	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	123.65	-	-	.99
366	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
367	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 -	1,296.93	346.17	- -	05/2022	11.20
368	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	3,442.06	- -	-	20.28
369	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	2,547.20	- -	-	12.50
370	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	1,952.20	97.16	- -	-	54.69
371	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	03/2018	809.07 -	1,065.70	930.46	- -	-	31.72
372	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 -	1,197.00	1,176.70	- -	-	29.35
373	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 -	1,332.00	1,525.15	- -	-	18.87
374	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 -	1,361.00	461.82	- -	-	29.35
375	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022	19.21
376	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	80.68	- -	-	8.26
377	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]	03/2018	1,029.96 -	1,261.05	402.95	- -	-	22.44
378	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92 -	1,071.00	383.75	- -	12/2022	5.32
379	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 -	2,169.00	-	- -	-	4.99
380	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
381	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]	03/2018	634.70 -	925.96	341.09	- -	-	45.89
382	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]	03/2018	795.50 -	922.64	387.49	- -	-	15.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
383	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851	03/2018	1,162.92 -	1,182.87	69.25	-	-	1.72
384	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 -	1,135.08	802.65	-	-	137.10
385	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	748.98	-	-	25.68
386	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185	11/2017	2,159.00 -	2,262.00	1,720.10	01/2019	01/2019	4.77
387	ISMAILABAD-NARNAUL PKG-5 - [N24001186	01/2019	1,051.91 -	1,118.07	957.15	-	05/2022	6.29
388	ISMAILABAD-NARNAUL PKG-6 - [N24001187	01/2019	1,120.06 -	1,206.48	1,006.03	-	07/2022	7.72
389	ISMAILABAD-NARNAUL PKG-7 - [N24001188	01/2019	1,137.42 -	1,238.29	1,111.87	-	06/2022	8.87
390	ISMAILABAD-NARNAUL PKG-8 - [N24001189	01/2019	1,033.19 -	1,044.32	899.01	-	03/2022	1.08
391	ISMAILABAD-NARNAUL PKG-2 - [N24001190	01/2019	1,243.45 -	1,407.35	1,162.45	-	04/2022	13.18
392	ISMAILABAD-NARNAUL PKG-3 - [N24001191	01/2019	889.36 -	986.10	837.89	-	05/2022	10.88
393	ISMAILABAD-NARNAUL PKG-4 - [N24001192	01/2019	1,018.79 -	1,072.08	956.46	-	05/2022	5.23
394	ISMAILABAD-NARNAUL PKG-1 - [N24001193	01/2019	996.65 -	1,173.65	1,070.65	-	05/2022	17.76
395	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	557.00	-	06/2022	.00
396	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	470.00	-	11/2022	27.86
397	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	671.00	-	10/2022	305.58
398	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299	09/2018	617.41 -	668.45	546.69	02/2019	-	8.27
399	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,321.60	405.54	02/2021	-	7.72
400	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	07/2020	3,426.00 -	5,148.00	-	12/2021	-	50.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
401	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	401.61	11/2019 -	-	.06
402	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	245.90	11/2019 -	-	2.02
	Total		1,21,063.06 -	1,50,589.15	99,789.35			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmhc)</u>							
403	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	19,611.48	05/2015 -	06/2022	41.32
	Total		15,525.00 -	21,940.00	19,611.48			
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
404	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114	03/2020	431.16 431.00	461.42	70.25	06/2021 -	06/2022	7.02
	<u>Department Of Telecommunication</u>							
405	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	84.97
	Total		13,765.16 -	25,125.42	20,615.25			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
406	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,925.22	10,015.98	12/2018 -	08/2022	19.98
	<u>Central Public Works Department</u>							
407	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	06/2015	197.33 -	217.00	187.17	04/2019 -	02/2022	9.97
	<u>Chennai Metro Rail Ltd</u>							
408	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	18,380.00	18,051.27	12/2015 -	-	25.89
	<u>Delhi Metro Rail Corporation</u>							
409	DELHI MRTS PHASE-III - [N28000056	09/2011	38,585.00 -	40,180.91	39,728.58	03/2016 -	-	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>							
410	KOCHI METRO RAIL PROJECT - [N28000081	07/2012	5,181.79 -	6,218.14	6,065.82	07/2017 -	-	20.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(February 2022)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Mumbai Metro Rail Corporation Ltd</u>							
411	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	20,484.28	03/2020 -	03/2023	44.39
	<u>Nagpur Metro Rail Corporation Ltd</u>							
412	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00 -	9,759.79	8,462.32	03/2018 -	02/2022	12.44
	<u>Patna Metro Rail Corporation</u>							
413	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	307.63	06/2024 -	06/2024	4.19
	Total		1,14,518.89 -	1,35,012.56	103,303.05			
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
414	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	0.07	09/2020 -	03/2024	62.63
415	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	398.90	299.08	03/2020 -	03/2022	76.68
	<u>Delhi Jal Board</u>							
416	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	03/2017	665.78 -	942.18	261.19	12/2022 -	12/2022	41.52
	<u>Kolkata Metropolitan Development Authority</u>							
417	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	13.23
	<u>Polavaram Project Authority</u>							
418	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	18,422.33	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
419	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	22.24
420	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	.97
421	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	1.31
	Total		12,622.34 -	58,713.79	19,011.04			
	Grand Total		7,58,521.48	12,53,589.50	816,405.72			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	6,268.20	09/2010 -	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	17,806.00	12/2015 -	12/2022	84	67.73	
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	30,143.00	11/2020 -	11/2023	36	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	14,142.00	12/2016 -	12/2023	84	38.63	
	Total		67,120.00 -	82,988.00	68,359.20					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 -	707.73	507.91	09/2018 10/2022	10/2022	49	69.63	Nil
6	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI, UTTARAKHAND	07/2018	456.86 -	456.86	340.28	09/2020 12/2022	12/2022	27	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10 -	177.10	115.40	02/2020 12/2022	12/2022	34	0	1. A portion of the site measuring 3.40 acres is fouling in the Runway extension and Basic Strip due to which the work will be delayed further 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men, materials & Machinery for the work.
8	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24 -	412.24	243.86	06/2021 03/2023	03/2023	21	0	Diversion of Road Crossing the runway is pending with state Govt. (Amount Deposited by AAI)
9	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28 -	951.28	548.93	10/2021 04/2023	04/2023	18	0	Nil
10	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI,WEST BENGAL	01/2019	389.71 -	389.71	233.91	11/2021 04/2023	04/2023	17	0	2
11	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39 -	475.39	202.52	04/2021 08/2023	08/2023	28	0	Nil
12	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00 -	1,405.00	439.69	08/2022 08/2023	08/2023	12	0	1) Resolving land swapping of Doshaliguna village. 2) Removal of structures of Lomakotadi village coming inside operational area. 3) Relocation of Juna Hirasar village 4) Relocation of wind mills, Lowering of Pylon mast & Cell phone mast. 5) Construction of Flyover and service road yet to be taken up by State Govt.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
13	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]AAI,ARUNACHAL PRADESH	02/2019	645.63 -	645.63	296.53	08/2022 10/2023	10/2023	14	0	Shifting of 132 KV Power Grid line, Acquisition of 5 acres of Assam land, Construction of boundary wall, Construction of four lane approach road to Airport.
14	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,938.00	579.75	09/2021 -	12/2023	27	40.13	
15	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	346.27 -	480.33	145.28	09/2021 12/2023	12/2023	27	38.72	Nil
16	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]AAI,TELANGANA	05/2020	353.61 -	353.61	109.92	05/2022 12/2023	12/2023	19	0	Nil
17	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	458.00	171.37	03/2020 03/2024	03/2024	48	0	Nil
18	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	283.65	10/2022 03/2024	03/2024	17	0	AUGUMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTIONG NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
19	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	20.42	03/2022 03/2024	03/2024	24	0	Nil
20	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	838.87	02/2022 12/2024	12/2024	34	0	Nil
21	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	391.13	03/2021 03/2025	03/2025	48	7.88	Transportation strike from 1st week of November 2020, to end of the month at CEMENT Plant in Govt, of Assam & Meghalaya.
	Total		13,078.09 -	14,147.65	5,469.42					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
22	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	288.42	05/2014 -	03/2022	94	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
23	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13	341.22	91.55	03/2017	12/2022	69	12.2	
24	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL, JHARKHAND	02/2014	555.52	555.52	5.87	03/2021	03/2023	24	0	
25	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00	334.27	32.60	04/2018	06/2023	62	37.56	
26	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	515.18	03/2019	04/2024	61	0	
27	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88	339.88	91.62	04/2014	10/2025	138	0	
Central Coal Fields Limited										
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51	163.51	124.86	03/2011	03/2023	144	0	
29	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85	510.85	502.12	03/2016	03/2023	84	0	
30	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	98.68	03/2014	03/2023	108	0	
Eastern Coal Fields Limited										
31	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	625.60	08/2019	08/2024	60	93.35	i). Approval of Deptt. of IC& E, Govt. of WB regarding utilization of further 100.32 acres vested land which was identified and finalized by ADDA for this rehabilitation project. ii). To expedite shifting of families at the Bijaynagar site where construction of 160 flats has already been completed with infrastructural development. iii). Approval of revised R&R package by cabinet of Govt. of WB before sending to Ministry of Coal, GOI for competent approval. iv). Publication of final figure of Demographic survey report for non-ECL houses by ADDA. v). Finalization and publication of valuation report for Legal Title Holder households by ADDA.
Mahanadi Coal Fields Limited										

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
32	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	808.97	815.72	03/2013	03/2024	132	68.7	
33	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15	479.15	254.83	03/2019	03/2024	60	0	
34	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38	1,375.38	710.64	03/2021	03/2026	60	0	
	<u>Neyveli Lignite Corporation</u>									
35	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00	17,237.80	13,185.30	11/2021	06/2023	19	0	1. Acquisition of Balance 5.4572 ha of pocket land in main plant area. 2. Acquisition of Balance 14.5940 ha of Railway siding land.
36	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17	709.06	496.44	06/2015	09/2027	147	-51.37	
	<u>Northern Coal Fields Limited</u>									
37	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09	1,783.09	954.78	03/2021	03/2023	24	0	
38	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17	1,255.17	584.00	03/2022	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
39	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	03/2018	03/2022	48	0	
	<u>South-Eastern Coal Fields Limited</u>									
40	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATISGARH	07/2016	459.49	459.49	-	03/2020	03/2022	24	0	
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	224.43	03/2014	03/2023	108	0	
42	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97	335.97	48.36	03/2018	03/2023	60	0	
43	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10	316.10	152.47	03/2020	03/2023	36	0	
44	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04	371.04	79.50	03/2021	03/2024	36	0	
45	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH	12/2013	610.63	610.63	179.09	03/2022	03/2025	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
46	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL, MADHYA PRADESH	03/2016	869.44	869.44	137.22	03/2021	03/2025	48	0	
47	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	9.23	03/2014	03/2026	144	0	
	<u>Western Coal Fields Limited</u>									
48	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56	299.67	213.93	03/2019	03/2022	36	1.39	
49	UKNI DEEP OC - [N06000179]WCL, MAHARASHTRA	11/2018	318.14	318.14	226.62	03/2021	09/2022	18	0	
50	BELLORA-NAIGAON DEEP OC - [N06000180]WCL, MAHARASHTRA	11/2018	252.71	252.71	107.27	03/2021	09/2022	18	0	
51	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL, MULTI STATE	02/2017	328.00	328.00	298.48	03/2021	09/2023	30	0	
52	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL, MAHARASHTRA	02/2016	327.41	327.41	-	03/2019	09/2026	90	0	
	Total		35,785.45	37,983.80	21,208.56					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
53	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF, MAHARASHTRA	04/2018	426.72	426.72	363.71	04/2020	03/2022	23	0	
	Total		426.72	426.72	363.71					
	<u>MINES</u>									
	<u>Central Public Works Department</u>									
54	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD, WEST BENGAL	04/2019	255.37	255.37	1.16	04/2022	10/2024	30	0	
	<u>National Aluminum Company Limited (Nalco)</u>									
55	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO, TAMIL NADU	09/2017	166.62	163.17	135.00	06/2019	12/2022	42	-2.07	Extension of NFR (Noted For Record) is pending with TANGEDCO.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
56	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 667.23	667.23	395.98	01/2020 11/2023	11/2023	46	24.95	
57	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 581.00	581.00	96.18	11/2020 12/2023	12/2023	37	63.66	
58	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	10.96	04/2021 12/2023	12/2023	32	0	
59	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	6,435.90	1,268.54	04/2021 01/2024	01/2024	33	16.17	1. For Refinery, issuance of NOC by Department of Water Resource, Govt of Odisha for laying of pipeline from the water drawl point and transfer of lease by IDCO for construction of pump house. 2. For pottangi mines, forest diversion proposal is pending with DFO Koraput for stage-I FC.
	Total		7,333.99 -	8,585.67	1,907.82					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
60	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	21,940.00	19,611.48	05/2015 01/2022	06/2022	85	41.32	
61	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH	11/2015	2,907.00 -	2,907.00	636.12	06/2023 -	06/2024	12	0	
	<u>Steel Authority Of India Limited (Sail)</u>									
62	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	212.42	06/2019 02/2022	05/2022	35	0	
63	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	572.49	10/2017 12/2021	11/2022	61	0	
	Total		19,728.88 -	26,143.88	21,032.51					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
64	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	640.00	380.90	12/2021 -	06/2022	6	0	
65	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	66	117.11	Delay due to RoU issues in Tamil Nadu (TN) portion due to local resistance and lack of support / clarity from TN Govt. including delay in release of GO on land and crop compensation which was released in Feb 2020. Detailed Engineering Survey and other ROU activities could not be done due to local protests. TIDCO has been nominated as Nodal Agency for resolving ROU issues in Oct 2021. Pipeline route is being discussed with TIDCO officials.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
66	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55	248.55	149.47	06/2022	09/2022	3	0	Activities on 18 acres of land out of 70 acres were on hold due to Status Quo order by Hon'ble court of Ranchi- Jharkhand (Land of 10 acres since 24.09.2019 and land of 8 acres since 04.07.2020). High Court has given verdict for 10 acres of land on 03.09.2021 directing State Government to determine appropriate compensation of land and to hand over possession of same to BPCL on payment of proportionate compensation to petitioners. BPCL has deposited the said compensation amount, however State Government is yet to disburse the compensation to petitioners. Hence clearance for construction activity is not given to BPCL. Second petition with respect to 8 acres of land yet to be taken up for hearing.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
67	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	1,507.24	855.28	06/2019 -	02/2023	44	35.54	Kerala State: Delays in release of Kerala GO on compensation, RoU acquisition, permission from Chalakudy Municipality etc. Major Project activities started only after Kerala GO on compensation to landowners which was released in Jan 2019. Tamil Nadu State: Project work was stalled since Dec'2014 after denial of permissions from SH authorities to lay pipeline along roads. Local resistance and lack of support / clarity from Tamil Nadu Govt. including delay in release of GO on land and crop compensation resulted in delays. GO was released in Feb 2020. Competent Authority was appointed in May 2021. TIDCO has been nominated as Nodal Agency for resolving ROU issues in Oct 2021. ROU acquisition activities has been started in section up to Coimbatore (42 KM).
68	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	291.62	02/2021 -	03/2023	25	0	
69	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL,ODISHA	08/2019	1,607.00 -	1,607.00	338.29	08/2022 -	06/2023	10	0	
	<u>Gas Authority Of India Limited</u>									
70	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,661.00	12/2020 -	03/2022	15	-30.59	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
71	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.00	327.01	233.20	08/2020 12/2021	04/2022	20	14.17	Stiff resistance from Farmers (From Ch 113 to 133.9 in patches ~ 9 Km) is being faced demanding higher compensation in Hissar district
72	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	220.00	200.10	04/2018 -	06/2022	50	-32.88	
73	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,209.40	12/2020 12/2021	06/2022	18	0	1) Delay in RoU acquisition in West Bengal. 2) Delay in forest Permission in Jharkhand (76 Km)
74	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 -	3,048.00	2,271.40	12/2020 12/2021	06/2022	18	-11.32	1) Delay in receipt of Forest permission in Odisha(65 Km). Working permission received in June/July/21. 2) Other RoU related issues/encumbrance/resistance such as resistance in Sundergarh & Angul district, Chakbandi land etc.
75	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,620.10	12/2020 12/2021	07/2022	19	0	1) Delay in grant of Forest permission in Odisha.(13 Km) 2) Unprecedented flood leading to inundation of RoU. 3) RoU related issues/encumbrance/resistance.
76	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	247.90	120.91	02/2021 -	10/2022	20	9.91	Nil
77	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 -	217.92	106.90	04/2021 03/2022	10/2022	18	0	
78	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	983.90	12/2020 12/2021	06/2023	30	0	Non – availability of RoU in West Bengal.
79	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	3,060.00	2,727.90	12/2021 -	06/2023	18	-7.5	Delay in RoU acquisition in West Bengal (189 Km).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
80	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL, ODISHA	07/2017	243.53 -	243.53	167.21	07/2022 -	08/2023	13	0	
81	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL, ODISHA	07/2017	182.20 -	182.20	101.14	07/2022 -	08/2023	13	0	NIL
82	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]GAIL, JHARKHAND	10/2017	221.45 -	221.45	113.23	10/2022 -	08/2023	10	0	NIL
83	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL, BIHAR	10/2017	359.25 -	359.25	200.37	10/2022 -	10/2023	12	0	NIL
84	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,781.00	12/2012 02/2022	02/2025	146	102.71	Non - availability of hindrance free RoU in Tamil Nadu.
	<u>Hindustan Petroleum Corporation Limited</u>									
85	180 TMTPA NEW LPG PLANT AT PATALGANGA (DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL, MAHARASHTRA	06/2017	249.26 -	249.26	212.46	06/2020 -	03/2022	21	0	
86	120 TMTPA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL, JHARKHAND	06/2017	161.50 -	161.50	136.30	06/2020 -	03/2022	21	0	
87	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL, KARNATAKA	06/2018	380.00 -	380.00	348.51	11/2021 03/2022	03/2022	4	0	
88	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	210.94	130.17	08/2021 -	03/2022	7	0	
89	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH	07/2016	20,928.00 -	26,264.00	18,232.09	07/2020 -	07/2022	24	25.5	
90	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL, MULTI STATE	09/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022	13	14.76	Delay in lands acquisition for Dharmapuri terminal construction Delay in RoU permissions from NHAI in TN Villager's resistance to pipeline laying in ROU Delay in obtaining Wildlife / Forest clearances

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
91	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	215.09	09/2026 -	02/2027	5	0	
92	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	621.42	03/2029 -	08/2029	5	0	
93	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	5,830.20	174.36	03/2031 -	08/2031	5	0	
	<u>Indian Oil Corporation Limited</u>									
94	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	315.00	232.78	12/2021 -	02/2022	2	0	
95	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	174.10	03/2021 03/2022	02/2022	11	0	
96	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	3,154.79	12/2020 03/2022	03/2022	15	43.82	1. Stiff resistance in opening of RoU in 1.1 Km RoU in Dinkia in Jagat Singhpur district in Odisha
97	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	609.43	07/2018 05/2021	03/2022	44	0	
98	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	304.44	10/2020 -	03/2022	17	0	
99	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	185.52	01/2021 06/2021	03/2022	14	0	
100	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	423.89	03/2021 03/2022	03/2022	12	0	Dispute over a section of boundary wall leading to non availability of sectional work front. Issue resolved on 20th Jan 2022

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
101	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,315.92	03/2021 12/2021	05/2022	14	66.09	1. Delay in permanent land acquisition for SV locations in Bihar due to non-availability of updated land records and exorbitant compensation being demanded by landowners. As on date, permanent land acquisition is pending for 6 SV locations 2. Stiff resistance in opening of RoU in Bihar and West Bengal due to demand of exorbitant compensation and diversion of route. As on date, work is hampered in 0.9 km in Begusarai districts of Bihar 3. Intermittent disturbance of construction activities in various stretches in Bihar and West Bengal. As on date, intermittent disturbance is observed in 1.0 km RoU in Patna district of Bihar
102	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	4,270.46	12/2018 02/2022	06/2022	42	33.98	1. Delay in finalization of Market value of land for payment of enhanced compensation. Till date, Market value for 195 villages out of total 665 villages received. 2. Resistance against laying of pipeline in 1.0 Km RoU stretch in Madurai District and 1.59 Km in Thiruvallur district in Tamil Nadu. 3. Delay in Permission to lay pipeline (2.7 km) along the service lane of proposed North Port Access Road (NPAR) of TNRDC in Vannivakkam, Anupampattu villages of Ponneri Taluk, Thiruvallur district.
103	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	914.85	10/2021 -	06/2022	8	0	
104	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 543.00	543.00	176.32	09/2021 06/2022	06/2022	9	17.46	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
105	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	1,945.00	1,657.30	02/2022 -	07/2022	5	0	1. Stiff resistance in opening of RoU in Maharashtra due to demand of exorbitant compensation and diversion of route. As on date, work is hampered in 26.01 Km of RoU in different stretches in Nandurbar (1.9 Km), Dhule (1.40 Km), Ahmednagar (15.08 Km), Beed (0.52 Km), Osmanabad (2.71) and Solapur (4.4 Km) districts 2. Delay in permanent land acquisition for construction of SV land in Gujarat and Maharashtra. All land acquisition was completed by Oct 2021 only.
106	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	172.39	02/2020 07/2022	07/2022	29	64.91	
107	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	376.32	02/2020 10/2021	07/2022	29	0	
108	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	5,654.00	3,652.22	10/2021 07/2022	07/2022	9	0	
109	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 753.89	753.89	495.80	02/2020 07/2022	07/2022	29	26.07	
110	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	139.82	06/2021 07/2022	07/2022	13	0	
111	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	226.74	01/2021 -	08/2022	19	25.57	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
112	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL, BIHAR	12/2017	199.36 -	199.36	112.94	10/2020 08/2022	08/2022	22	0	
113	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL, HARYANA	01/2019	909.00 -	909.00	551.04	01/2021 03/2022	08/2022	19	0	
114	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL, HARYANA	09/2019	164.69 -	164.69	45.60	07/2021 03/2022	08/2022	13	0	
115	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL, HARYANA	08/2018	1,636.00 -	1,636.00	1,012.58	08/2020 04/2022	09/2022	25	0	
116	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	466.00	313.36	04/2021 09/2022	09/2022	17	0	
117	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL, ANDHRA PRADESH	10/2018	316.20 -	316.20	152.91	10/2021 03/2022	09/2022	11	0	
118	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL, ODISHA	05/2019	3,361.00 -	3,361.00	2,141.68	08/2021 09/2022	09/2022	13	0	
119	SITARGANJ LPG PROJECT - [N16000282]IOCL, UTTARAKHAND	02/2017	160.10 -	160.10	106.27	02/2020 06/2021	10/2022	32	0	
120	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	207.36	135.65	04/2020 10/2021	10/2022	30	27.2	
121	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL, UTTAR PRADESH	08/2017	255.40 -	255.40	154.50	08/2020 03/2022	10/2022	26	0	
122	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 1,236.00	1,236.00	568.65	10/2017 03/2022	12/2022	62	103.6	
123	LPG BP PROJECT KHORDHA - [N16000283]IOCL, ODISHA	12/2016	161.59 -	161.59	71.65	12/2019 03/2022	01/2023	37	0	
124	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL, HARYANA	08/2019	1,255.00 -	1,255.00	473.01	12/2021 01/2023	01/2023	13	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
125	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	135.36	04/2022 -	02/2023	10	0	
126	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	22.01	07/2022 -	02/2023	7	0	
127	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	188.36	08/2021 03/2023	03/2023	19	0	
128	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.10	427.10	41.54	09/2022 03/2023	03/2023	6	15.12	
129	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 3,219.94	2,281.94	703.22	12/2022 07/2023	07/2023	7	0	
130	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	139.54	04/2022 -	08/2023	16	0	
131	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.70	09/2023 -	02/2024	5	0	
132	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	164.75	12/2023 -	02/2024	2	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
133	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,809.28	12/2019 04/2021	03/2022	27	0	
134	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 304.00	304.00	2.61	06/2023 01/2024	01/2024	7	52	
	<u>Oil & Natural Gas Corporation Limited</u>									
135	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 2,001.34	2,001.34	1,613.65	05/2013 05/2022	05/2022	108	132.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
136	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,892.72	04/2018 05/2022	05/2022	49	5.8	
137	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	05/2019	3,660.71 3,740.05	3,740.05	3,233.86	05/2021 05/2022	05/2022	12	2.17	
138	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	829.58	829.58	12/2020 05/2022	05/2022	17	8.6	
139	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,292.46	2,255.02	05/2021 12/2022	12/2022	19	0	
140	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	06/2019	2,494.68 -	2,354.72	1,824.00	03/2022 -	03/2023	12	-5.61	
141	Field Development Plan of Madanam NLP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	457.24	03/2019 09/2021	05/2023	50	0	Facilities: Grant of CTE is awaited from TNPCB, Govt of Tamil Nadu. Drilling: * Public hearing for grant of Environmental Clearance (EC) and site access issues have delayed drilling of balance wells.
142	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	31,040.00	16,067.78	06/2020 05/2023	05/2023	35	-8.74	
143	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,790.56	03/2022 05/2023	05/2023	14	23.16	
<u>Oil India Limited</u>										
144	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	340.00	287.12	10/2020 -	03/2022	17	-16.26	
145	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	494.68	12/2019 -	03/2022	27	-10.79	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
146	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 -	198.00	189.00	08/2020 03/2022	03/2022	19	-11.9	
147	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL, ASSAM	01/2018	543.91 -	638.60	412.80	02/2020 -	06/2022	28	17.41	
	Total		1,53,700.65 -	1,66,140.61	1,02,217.42					
	POWER									
	Chenab Valley Power Projects [P] Limited									
148	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,169.01	04/2020 07/2025	07/2025	63	0	
	National Hydro-Electric Power Corporation									
149	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	9,558.69	09/2009 03/2023	03/2023	162	152.52	
150	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	15,300.08	09/2010 08/2023	08/2023	155	218.08	PPA is yet to be signed with Delhi DISCOMS for Power of 113 MW.
	National Thermal Power Corporation									
151	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 19,413.00	17,304.00	16,748.00	05/2018 -	03/2022	46	33.47	
152	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC, ODISHA	05/2016	1,885.13 2,311.80	2,426.00	2,027.32	12/2018 03/2022	03/2022	39	28.69	None
153	DEVKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	524.83	400.95	09/2021 -	03/2022	6	4.7	
154	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC, RAJASTHAN	01/2020	1,522.71 -	1,522.71	1,114.48	09/2021 08/2022	03/2022	6	0	
155	JETSAR SOLAR 160 MW - [N18000287]NTPC, RAJASTHAN	12/2019	702.28 -	702.28	609.51	03/2021 12/2021	03/2022	12	0	
156	FATEHGARH SOLAR 296MW - [N18000289]NTPC, RAJASTHAN	03/2020	1,749.31 -	1,749.31	1,362.64	09/2021 -	03/2022	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
157	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	852.90	596.05	09/2021 -	05/2022	8	6.85	
158	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	442.03	293.40	04/2021 -	05/2022	13	9.99	
159	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	679.00	513.91	11/2018 06/2022	06/2022	43	28.19	None
160	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	403.62	123.49	06/2021 01/2022	07/2022	13	0	Approval of metering scheme from KSEB required for commissioning of the project.
161	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	1,316.22	948.04	09/2021 -	08/2022	11	0	
162	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,803.19	612.20	09/2021 -	10/2022	13	4.71	
163	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	293.03	118.68	10/2021 -	10/2022	12	11.93	
164	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	910.29	09/2021 10/2022	10/2022	13	0	
165	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	382.22	8.24	03/2022 -	10/2022	7	0	
166	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	9,223.00	11/2020 07/2022	02/2023	27	3.76	
167	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 21,312.11	21,312.11	19,738.00	10/2011 07/2023	07/2023	141	145.16	Bakhtiyarpur ROR line: Acquisition of 12.241 Acres supplementary land is under process. Land award has been done. Payment to landowner is in progress. However, few Raiyats are unwilling to accept the compensation as the award has been issued based on reduced circle rate. State Govt support required to Railways for acquisition / possession of said Land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
168	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 17,007.00	17,007.00	12,634.00	06/2019 10/2022	01/2024	55	18.38	1. Maintaining Law & order and resolution of following issue: Agitation by villagers for compensation on already awarded land. Villagers again stopped the entry of man and material inside the plant from 03.10.21 to 06.10.21 and 15.11.21 to 13.12.21. 2. Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. Forest clearance in ATS lines. Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD
169	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,247.00	03/2013 12/2021	12/2024	141	96.99	
170	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,667.00	5,021.00	03/2023 -	02/2025	23	-5.36	Readiness of Start-up power and ATS matching with commissioning schedule of the project Expedient Award of construction of power evacuation and start-up power line is required. Transfer & possession of balance land.
171	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,803.00	754.00	09/2019 12/2024	07/2025	70	30.48	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSERC. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (11 Nos + 01 School).
	<u>Power Grid Corporation Of India Limited</u>									
172	WESTERN REGION SYSTEM STRENGTHENING - XX - [N18000310]PGCIL,MULTI STATE	07/2019	226.98 -	226.98	-	08/2021 -	02/2022	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
173	SOUTHERN REGION SYSTEM STRENGTHENING - XXV - [N18000311]PGCIL,MULTI STATE	07/2019	154.72 -	154.72	-	07/2021 -	02/2022	7	0	
174	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN - [N18000312]PGCIL,RAJASTHAN	08/2019	2,578.47 -	2,578.47	-	12/2020 -	02/2022	14	0	
175	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII - [N18000318]PGCIL,MULTI STATE	09/2018	221.36 -	221.36	-	03/2021 -	02/2022	11	0	
176	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	262.29	05/2020 -	02/2022	21	0	
177	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	480.89	11/2016 -	03/2022	64	4.61	
178	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.97	03/2018 -	03/2022	48	0	
179	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	580.89	05/2017 -	03/2022	58	0	
180	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	159.02	06/2019 -	03/2022	33	0	
181	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS - [N18000309]PGCIL,MULTI STATE	11/2018	496.11 -	496.11	-	06/2020 -	03/2022	21	0	
182	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	167.31	-	12/2017 -	03/2022	51	0	
183	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA - [N18000314]PGCIL,RAJASTHAN	01/2020	562.86 -	562.86	-	01/2021 -	03/2022	14	0	
184	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE	07/2020	239.89 -	239.89	-	06/2021 -	03/2022	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
185	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	205.65	02/2019 -	04/2022	38	0	
186	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	251.70	12/2019 -	04/2022	28	0	
187	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	04/2022	21	14.11	
188	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	241.38	-	11/2021 -	05/2022	6	0	
189	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	219.66	169.82	07/2019 -	08/2022	37	17.99	
190	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,832.15	02/2020 -	04/2023	38	36.46	
191	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	3,522.04	12/2018 -	01/2024	61	31.08	
192	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	3,182.67	12/2018 -	03/2024	63	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
193	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022	6	46.2	1. Stay imposed by Hon'ble High Court of Uttarakhand on all construction activities within 200 m of the river. 2. Agitation by locals in project area. 3. Delay due to Covid-19 pandemic. 4. Geological challenges. 5. Change in Design and scope of work.
	<u>Thdc India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
194	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21	1,587.16	663.84	09/2020	08/2022	23	-24.57	(i) Tree Felling Activities in 139 Ha priority Forest land needs to be expedited by DFO, Singrauli. (ii) Private/ Tenancy Land (337.35 Ha): Disposal of pending cases & payment of Compensation to balance PAFs and handing over of balance 116.35 Ha land is pending with Dist Admin, Singrauli. (iii) Tree Felling activities needs to be expedited in 0.87 Ha Forest land for CEC & RS by DFO, Singrauli.
195	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00	4,825.60	4,409.29	02/2016	06/2023	88	191.23	• Non-availability of encumbrance/ hindrance free Asena Quarry. • Interference at Chopra Dumping yard. Additional dumping yard provided at nearby Koti Colony. • Local community interference (third party intervention) and blockages at project site. Issue resolved.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
196	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	3,654.43	09/2023	08/2024	11	0	• M - ake-up Water related issues pending with Irrigation & Water Resources Dept, GoUP. • La - w & Order Issues in taking possession of small patches of land acquired for Railway Siding & land within boundary of already acquired 1201 Acre land. • Si - gning of Lease deed by UPSIDC is getting delayed due to Court case filed by PAFs. • He - lp of District Administration required for demolition of old Nagla houses for final shifting.
197	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,416.30	06/2013 06/2025	06/2025	144	54.94	• All - Law & order issues have been resolved in Aug'21 with the support of GoUK/ District Administration, Chamoli.
	Total		1,43,700.78	1,98,152.89	1,31,833.48					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Cpwd For Health</u>									
198	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00	195.00	16.41	09/2020	04/2022	19	0	
199	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00	260.00	25.38	06/2021	05/2022	11	0	
	<u>Hospital Services Consultancy Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
200	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	274.40	05/2018 -	06/2022	49	0	
	<u>Nbcc For Health</u>									
201	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	1,089.38	09/2021 -	06/2022	9	8.88	
	Total		2,169.99 -	2,289.99	1,405.57					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
202	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24	111.08	
203	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24	75	
204	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12	.89	
205	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24	0	
206	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12	0	
207	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24	0	
208	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12	0	
	<u>East Central Railways</u>									
209	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	347.96	03/2019 -	03/2022	36	0	
210	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	581.48	03/2020 -	03/2023	36	0	
211	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	1,059.76	03/2020 -	05/2023	38	0	
212	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	1,090.00	1,093.59	03/2012 -	06/2023	135	235.66	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
213	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,570.66	03/2020 -	03/2024	48	0	
214	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	452.12	03/2021 -	03/2024	36	62.06	
215	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	57	49.45	
216	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	585.85	03/2021 -	12/2024	45	63.37	
	<u>East Coast Railway</u>									
217	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,243.24	02/2019 -	03/2022	37	38.43	Delay in land acquisition due to non-posting of SPL.LAO. Law and order situation in village Badmal of Sambalpur District delayed construction of Major Br no.11FOR ONE YEAR. Law and Order situation in village Kaniabeda not allowing construction of ROB(Br No 382),villagers of Laxmanpur not allowing construction activities over a length of 1.65km . Forest diversion proposal pending for stage 1 clearance.
218	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	324.59	10/2020 -	03/2024	41	0	
219	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGAR H	12/2012	1,160.00 -	1,160.83	1,036.36	03/2020 03/2023	03/2024	48	.07	
220	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	758.80	03/2022 03/2023	03/2024	24	0	
221	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	734.63	12/2018 -	03/2024	63	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
222	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13	3,791.66	1,729.29	03/2009	12/2024	189	29.71	Complete handover of private land by state govt as per MOU has not been made till date. 406.35acres of balance private land yet to be handed over by State Govt. of Odisha. Pending Stage-I forest clearance & working permission between Km.112-180 needs to be sanctioned for early taking up the construction works in forest land.
223	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78	1,928.07	947.41	06/2021	03/2025	45	137.8	Acquisition of balance 575.620 Ac. of Private land & 185.94 Ac. of Govt. land Balance 12924 nos. of trees to be cut out of 30734 nos. Shifting/modification of EHT/HT/LT power line crossings bet. Km. 43.50-43.98, 44.60-44.72, 45.695-45.800, 46.240, 46.550, 47.50, 48.24-48.38, 51.10, 51.54-52.00, 52.220 by TP Central Odisha Distribution Ltd.(TPCODL).
224	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61	810.02	209.78	11/2018	03/2025	76	15.45	Delay in land acquisition due to non -posting of revenue officials (Amin, RI)in SP.LAO office. The 11(1) notification is issued on 26.02.21 but 19(1) notification is delayed and 11(1) notification may become time barred.
225	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71	2,499.71	835.30	03/2022	03/2026	48	0	
226	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74	2,361.74	564.03	03/2022	03/2026	48	0	
	<u>Eastern Railways</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
227	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	995.10	622.26	03/2016	03/2024	96	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of un authorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- V/Compliance in BdMtg, dated 09.10.2020
228	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91	1,619.48	912.17	03/2019	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30KM between Kamarpukur and Jairambati in Hooghly district is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
229	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	472.06	03/2022 -	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
230	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	204.40	03/2016 -	03/2025	108	-3.95	For Ranaghat to Duttaphulia (8.17 Km) New Line section work will start after acquisition and handing over of land by State Government.
231	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	508.16	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 Km) New line - Work could not be started due to non-availability of land.
	<u>Indian Railway Construction Company Limited</u>									
232	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,800.17	09/2018 -	06/2022	45	0	1-Agitation by Land losers.
233	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	1,078.79	03/2022 -	09/2023	18	117.23	
	<u>Metropolitan Rapid Transport Projects</u>									
234	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022	219	501.57	
235	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	774.51	539.14	06/2013 -	12/2022	114	56.23	
	<u>North Central Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
236	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	1,080.53	03/2021 -	06/2023	27	0	
237	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	534.75	03/2022 -	12/2024	33	32.02	
238	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	89.74	03/2023 -	06/2025	27	0	
	<u>North East Frontier Railway</u>									
239	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,646.66	03/2021 -	03/2022	12	115.07	
240	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	708.73	549.81	03/2020 06/2022	09/2022	30	24.42	
241	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,986.82	03/2022 -	03/2023	12	32.15	
242	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	14,322.00	12,156.19	03/2011 -	12/2023	153	221.54	
243	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	6,527.00	4,766.68	03/2014 -	12/2023	117	172.7	
244	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	8,600.00	2,504.91	12/2015 -	12/2023	96	542.04	
245	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,047.51	586.70	03/2019 -	12/2023	57	13.88	
246	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,145.79	937.36	03/2019 -	03/2024	60	197.45	
247	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	1,108.94	03/2019 -	03/2024	60	302.54	
248	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,663.00	1,534.31	03/2015 -	03/2026	132	186.39	
	<u>North Eastern Railway</u>									
249	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	728.92	613.91	01/2019 -	02/2022	37	147.09	
250	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	345.95	01/2022 -	03/2022	2	-38.88	
251	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
252	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	127.77	
253	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-32.79	
	<u>North Western Railway</u>									
254	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	775.62	02/2019 -	06/2022	40	109.82	
255	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	342.53	03/2020 -	10/2022	31	16.97	
256	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	435.41	08/2022 -	11/2022	3	0	
	<u>Northern Railway</u>									
257	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	37,012.26	27,846.00	11/2002 04/2023	04/2023	245	1380.49	1. Law & Order issues (close liaison is maintained with State Govt) 2. Due to ban on mining of minor aggregates in UT of J&K wef Nov' 2019, the works of tunnel and bridges were adversely affected till July 2021 resulting in accumulation of arrears of around 35 Kms.Now, Private E-Auctions for open mining blocks have been finalised by the J&K UT government and the issue stands resolved.
258	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024	148	348.44	
259	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	0	
260	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	1,540.13	480.97	03/2023 12/2025	12/2025	33	369.35	
	<u>Rail India Technical And Economic Service</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
261	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	393.98	371.86	03/2020 06/2022	06/2022	27	0	
	<u>Rail Vikas Nigam Ltd.</u>									
262	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL, MAHARASHTRA	03/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022	24	281.93	
263	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	950.00	619.35	03/2016 -	04/2022	73	50.15	
264	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL, ODISHA	03/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022	25	111.91	
265	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	644.38 -	923.28	995.52	03/2021 -	05/2022	14	43.28	
266	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022	88	102.92	
267	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022	27	141.61	
268	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL, CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,367.10	03/2020 -	06/2022	27	-7.28	
269	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022	18	86.23	
270	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL, MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022	21	23.55	
271	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022	165	224.56	
272	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022	12	63.88	
273	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022	9	58.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
274	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022	33	102.11	
275	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023	48	57.26	
276	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023	48	64.62	
277	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,137.46	03/2022 -	05/2023	14	-23.24	
278	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,129.41	03/2023 -	12/2024	21	0	
279	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	24,659.00	6,259.16	12/2024 -	03/2025	3	52.07	
280	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,834.54	1,586.17	03/2016 -	07/2025	112	65.94	
281	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	18.95	
282	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,139.94	03/2016 -	03/2026	120	7.78	
283	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	2,139.84	12/2024 -	12/2026	24	42.47	
	<u>South Central Railway</u>									
284	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 -	927.94	713.38	03/2020 -	03/2022	24	31.75	
285	MUNEERABAD- MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023	276	98.57	
286	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	803.75	03/2023 -	03/2024	12	5.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
287	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,676.08	03/2021 -	03/2024	36	0	
288	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,373.74	695.73	03/2010 -	03/2025	180	18.38	
289	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,495.93	03/2022 -	03/2025	36	7.06	
290	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027	216	102.85	
291	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	347.14	03/2014 -	03/2027	156	42.44	
South East Central Railway										
292	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022	37	116.46	
293	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 -	3,176.60	1,576.19	03/2023 12/2023	12/2023	9	66.44	
294	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 2,135.34	2,135.34	833.36	03/2021 12/2023	12/2023	33	8.23	
295	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	795.59	12/2021 12/2023	12/2023	24	.07	
296	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	36	378.6	
South Eastern Railway										
297	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.97	1,155.00	03/2020 -	06/2022	27	35.38	
298	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	511.75	149.63	12/2021 -	01/2023	13	31.09	
299	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,153.09	03/2021 -	12/2023	33	0	
300	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	350.68	05/2023 -	12/2023	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
301	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER, WEST BENGAL	04/2018	338.00 -	393.83	23.56	06/2022 -	12/2023	18	16.52	
302	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER, JHARKHAND	04/2018	428.65 -	472.50	1.62	06/2022 -	12/2025	42	10.23	
	<u>South Western Railway</u>									
303	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	1,104.00	1,014.52	03/2020 -	02/2022	23	28.31	
304	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	578.00 -	758.36	674.14	03/2020 -	02/2022	23	31.2	
305	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,156.94 -	1,954.21	1,238.40	03/2020 -	12/2022	33	68.91	
306	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,614.59 -	1,878.00	1,530.18	03/2019 -	02/2024	59	16.31	
307	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	279.54 -	279.54	37.12	03/2016 -	03/2024	96	0	
308	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	2,841.84 -	2,841.84	401.14	12/2018 -	06/2025	78	0	Out of 1611.16 Ha of land, 1144.09 Ha of land has been handed over by GOK. For balance 467.07 Ha, land acquisition by GOK is in progress as land to be given free by GOK.
309	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2026	120	0	
310	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 -	817.23	495.18	03/2017 -	03/2026	108	26.75	Chikmagalur - Belur section (25 Km): Out of 126.2 Ha of land, 63.47 Ha of land has been handed over by GOK. For balance 62.73 Ha, land acquisition by GOK is in progress as land to be given free by GOK.
311	BAGALKOT-KUDACHI NL - [N22000258]SWR, KARNATAKA	04/2010	986.30 -	1,530.09	326.02	03/2016 -	12/2026	129	55.13	Out of 1011.77 Ha of land, 544.56 Ha of land has been handed over by GOK. For balance 461.27 Ha, land acquisition by GOK is in progress as land to be given free by GOK.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
312	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2028	312	.02	Project kept under abeyance by Railway Board. GOK is yet to initiate land acquisition proceedings even though requisition to acquire 697.35 Ha of land has been submitted by Railways during the year 2013 itself as Land to be given free by GOK.
	<u>Southern Railway</u>									
313	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]SR,TAMIL NADU	09/1995	303.98 -	1,549.09	715.89	03/2020 -	03/2025	60	409.6	
314	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,726.52	02/2019 -	03/2025	73	325.17	
315	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,111.88	314.32	03/2019 -	12/2027	105	1649.69	
	<u>West Central Railway</u>									
316	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15	16.02	
317	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	561.88	03/2022 -	12/2023	21	114.32	
318	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,439.82	03/2021 -	03/2024	36	585.35	
319	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,392.72	03/2020 -	10/2024	55	38.63	
320	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	3230.57	
	<u>Western Railway</u>									
321	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022	21	33.41	
322	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,016.39	1,056.11	808.35	03/2021 -	12/2022	21	5.36	
323	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 -	603.69	358.78	06/2020 -	03/2023	33	-13.76	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
324	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	139	1.06	
325	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024	48	167.96	
326	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 -	742.88	2.26	03/2020 -	03/2024	48	7.31	
327	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 -	537.31	.64	03/2024 -	12/2024	9	0	
328	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	883.21	03/2022 -	03/2025	36	0	
329	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025	72	329.77	
330	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	6,383.82	2,404.99	03/2022 -	03/2026	48	82.2	
331	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.63	03/2022 -	03/2026	48	0	
332	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,524.68	1,010.81	03/2022 -	10/2027	67	13.17	
	Total		1,79,906.18 -	3,21,051.16	1,72,553.12					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
333	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 -	02/2022	43	0	
334	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	309.37	270.19	02/2017 02/2022	02/2022	60	-16.99	LA

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
335	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	355.17	269.58	07/2019 -	02/2022	31	0	
336	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	211.34	130.63	07/2019 -	02/2022	31	0	
337	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	244.93	159.96	05/2020 -	02/2022	21	0	
338	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	222.13	156.87	11/2019 -	02/2022	27	0	
339	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	338.42	11/2017 -	02/2022	51	0	
340	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	464.44	01/2020 -	03/2022	26	0	
341	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 587.41	587.41	537.14	05/2016 03/2022	03/2022	70	6.16	
342	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	2,138.16	1,241.55	10/2016 03/2022	03/2022	65	51.77	
343	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 -	03/2022	48	0	
344	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	174.90	154.26	08/2018 -	03/2022	43	5.23	
345	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	132.76	02/2018 -	03/2022	49	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
346	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	136.22	03/2017 -	03/2022	60	0	
347	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 -	03/2022	43	4.45	
348	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	178.31	03/2018 -	03/2022	48	0	
349	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	187.73	02/2018 -	03/2022	49	0	
350	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	231.61	03/2018 -	03/2022	48	0	
351	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 -	03/2022	44	0	
352	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	949.54	807.22	06/2019 -	03/2022	33	8.17	
353	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	852.67	225.16	12/2019 -	03/2022	27	0	
354	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	243.68	06/2019 -	03/2022	33	0	
355	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	457.52	354.16	07/2019 -	03/2022	32	0	
356	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	170.00	121.71	12/2019 -	03/2022	27	0	
357	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	228.54	159.32	08/2019 -	03/2022	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
358	MANHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	486.19	308.66	07/2019 -	03/2022	32	0	
359	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	461.96	326.81	11/2019 -	03/2022	28	0	
360	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	415.25	271.38	12/2019 -	03/2022	27	0	
361	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	210.81	210.81	07/2019 -	03/2022	32	0	
362	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	232.77	151.60	07/2019 -	03/2022	32	0	
363	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	344.85	245.82	12/2019 -	03/2022	27	0	
364	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	257.38	166.31	12/2019 -	03/2022	27	0	
365	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	422.02	302.13	07/2019 -	03/2022	32	0	
366	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	181.08	97.86	12/2019 -	03/2022	27	0	
367	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	227.19	138.05	12/2019 -	03/2022	27	0	
368	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	336.21	224.98	12/2019 -	03/2022	27	0	
369	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	238.19	177.80	12/2019 -	03/2022	27	0	
370	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	299.92	181.37	08/2020 -	03/2022	19	0	
371	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	223.46	68.00	12/2019 -	03/2022	27	0	
372	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	509.18	257.83	07/2019 -	03/2022	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
373	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	557.20	12/2019 -	03/2022	27	0	
374	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	189.64	03/2019 -	03/2022	36	0	
375	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	307.63	190.69	07/2019 -	03/2022	32	0	
376	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	218.38	170.80	07/2019 -	03/2022	32	0	
377	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	144.69	09/2018 -	03/2022	42	0	
378	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	484.15	343.45	06/2019 -	03/2022	33	0	
379	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	355.99	246.86	12/2019 -	03/2022	27	0	
380	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	313.58	202.69	04/2020 -	03/2022	23	0	
381	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022	48	9.23	
382	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	157.77	03/2021 -	03/2022	12	0	
383	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	190.01	04/2020 -	03/2022	23	-8.28	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
384	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19	12.16	
385	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	544.00	402.15	09/2016 -	03/2022	66	14.24	
386	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	298.70	01/2018 -	03/2022	50	0	
387	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	120.07	05/2019 -	03/2022	34	0	
388	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE - I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	319.96	193.60	03/2016 -	04/2022	73	13.3	
389	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	67.54	03/2018 -	04/2022	49	0	
390	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 290.15	290.15	164.56	05/2017 04/2022	04/2022	59	0	Due to LA issues
391	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	228.31	93.73	12/2019 -	04/2022	28	0	
392	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	256.15	174.63	12/2019 -	04/2022	28	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
393	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	205.95	123.24	01/2021 -	04/2022	15	0	
394	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	290.07	06/2017 -	04/2022	58	0	
395	REHABILITATION AND UPGRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	117.71	03/2021 -	04/2022	13	0	
396	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	1,742.01	1,605.30	12/2016 05/2022	05/2022	65	0	
397	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 394.44	394.44	188.34	05/2019 -	05/2022	36	-1.58	Delayed due to Land Acquisition, Forest clearance & COVID-19
398	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 319.28	319.28	222.37	08/2017 05/2022	05/2022	57	0	Due to L.A issues
399	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	373.05	329.89	11/2017 -	05/2022	54	-13.13	LA issue
400	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	365.54	09/2016 05/2022	05/2022	68	0	Delay in LA
401	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	390.73	368.28	05/2017 06/2022	06/2022	61	45.75	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
402	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 698.82	698.82	709.80	07/2016 06/2022	06/2022	71	2.19	
403	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	225.06	168.79	05/2016 06/2022	06/2022	73	25.84	
404	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	82.99	03/2018 -	06/2022	51	0	
405	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	328.03	01/2017 06/2022	06/2022	65	0	Delay in LA
406	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	316.06	214.31	05/2016 06/2022	06/2022	73	-18.14	LA issue
407	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	335.69	08/2017 -	06/2022	58	0	LA issues , Soil Embankment issue
408	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	634.32	329.59	05/2020 -	06/2022	25	0	
409	SHAHAPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	150.79	59.88	12/2019 -	06/2022	30	0	
410	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	422.38	243.81	08/2019 -	06/2022	34	0	
411	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	595.77	321.34	08/2019 -	06/2022	34	0	
412	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	283.86	05/2019 -	06/2022	37	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
413	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	420.57	269.24	07/2019 -	06/2022	35	0	
414	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	554.78	304.78	07/2019 -	06/2022	35	0	
415	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	304.58	135.51	12/2019 -	06/2022	30	0	
416	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	276.95	136.94	12/2019 -	06/2022	30	0	
417	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	189.46	107.85	12/2019 -	06/2022	30	0	
418	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	456.93	456.93	09/2019 -	06/2022	33	0	
419	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	344.25	169.80	08/2020 -	06/2022	22	0	
420	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	426.06	219.56	06/2020 -	06/2022	24	0	
421	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	294.87	149.16	12/2019 -	06/2022	30	0	
422	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	309.94	192.24	12/2019 -	06/2022	30	0	
423	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	191.12	06/2019 -	06/2022	36	0	
424	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	467.70	201.73	03/2019 -	06/2022	39	0	
425	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	105.37	03/2018 -	06/2022	51	0	
426	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	74.00	04/2019 -	06/2022	38	0	
427	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	406.54	175.24	09/2019 -	06/2022	33	0	
428	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	1,202.52	791.90	12/2019 -	06/2022	30	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
429	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	1,054.53	11/2019 -	06/2022	31	0	
430	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	162.34	64.74	07/2019 -	06/2022	35	0	
431	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	362.96	190.75	06/2019 -	06/2022	36	0	
432	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	456.32	330.00	06/2019 -	06/2022	36	0	
433	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	337.46	232.56	06/2019 -	06/2022	36	0	
434	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	456.45	336.68	06/2019 -	06/2022	36	0	
435	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	205.72	85.47	06/2019 -	06/2022	36	0	
436	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 255.00	255.00	195.11	06/2021 -	06/2022	12	-27.35	Delay due to Land Acquisition, Utility Shifting, Forest Clearance & COVID-19
437	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	731.50	486.06	10/2016 -	06/2022	68	17.04	
438	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	251.53	03/2015 -	06/2022	87	0	
439	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 913.49	913.49	645.24	11/2018 06/2021	07/2022	44	5.24	Delay in obtaining utility shifting estimate from the concern department,obtaining forest clearance and tree cutting operation,obtaining approval for GAD and finalization of COS
440	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	545.64	195.79	07/2019 -	09/2022	38	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
441	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	313.95	109.24	06/2019 -	09/2022	39	0	
442	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	376.19	91.77	05/2019 -	09/2022	40	0	
443	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	420.63	200.00	05/2020 -	09/2022	28	0	
444	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	196.83	06/2019 -	09/2022	39	0	
445	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	301.38	176.39	08/2020 -	09/2022	25	0	
446	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	653.46	284.02	07/2019 -	09/2022	38	0	
447	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	488.60	233.89	07/2019 -	09/2022	38	0	
448	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	381.77	186.62	06/2019 -	09/2022	39	0	
449	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	743.21	350.07	06/2021 -	09/2022	15	0	
450	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 2,226.11	983.14	726.13	12/2019 -	09/2022	33	0	
451	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	186.63	03/2019 -	10/2022	43	0	"On account of delay in getting approval of GAD and other various approvals from Railway authorities. At present there is no issue."
452	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	609.49	05/2016 10/2022	10/2022	77	0	Due to LA issues

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
453	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	293.64	261.09	08/2020 -	10/2022	26	0	
454	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 263.45	263.45	122.71	09/2017 05/2022	11/2022	62	0	LA issues
455	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	414.81	08/2017 -	12/2022	64	0	
456	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	396.86	277.42	09/2019 01/2022	12/2022	39	0	
457	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	426.18	258.00	09/2020 01/2022	12/2022	27	0	
458	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	293.10	214.90	08/2020 -	12/2022	28	0	Due to LA
459	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	729.55	10/2019 -	12/2022	38	0	Due to clearance of land (LA) COS and EOT.
460	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	75.41	11/2020 -	12/2022	25	0	Due to pending approval of GAD from railway department.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
461	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	962.43	455.49	03/2018 -	12/2022	57	0	Delay in Approval of GAD & Construction drawing, Delay in Approvals of Mix Design, Proof Consultant, Construction Material and steel etc from Authority
462	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	363.82	73.08	09/2019 -	12/2022	39	0	
463	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	237.40	9.66	05/2020 -	12/2022	31	0	
464	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	218.73	06/2019 -	12/2022	42	0	
465	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	404.33	61.42	05/2020 -	12/2022	31	0	
466	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	381.08	9.66	05/2020 -	12/2022	31	0	
467	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	341.80	155.96	06/2019 -	12/2022	42	0	
468	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	12/2022	37	0	
469	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	160.00	135.75	09/2021 12/2022	12/2022	15	0	
470	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	572.66	288.50	08/2016 -	12/2022	76	15.19	
471	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	435.61	128.55	07/2016 -	12/2022	77	-3.83	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
472	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	28.78	05/2021 -	12/2022	19	0	
473	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	423.15	159.07	12/2019 12/2022	12/2022	36	0	
474	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 03/2022	03/2023	52	7.39	
475	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	254.30	118.68	10/2020 12/2021	03/2023	29	0	
476	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 -	213.97	27.41	08/2019 11/2022	03/2023	43	33.51	
477	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 -	263.26	78.56	08/2019 08/2022	03/2023	43	11.18	
478	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	11.71	03/2021 -	03/2023	24	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
479	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	389.26	05/2018 -	03/2022	46	0	
480	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	110.95	12/2018 -	03/2022	39	0	
481	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	229.26	01/2016 -	03/2022	74	0	
482	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	141.40	01/2016 -	03/2022	74	0	
483	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	284.09	197.27	04/2017 -	03/2022	59	0	
484	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	158.08	04/2017 -	03/2022	59	29.48	
485	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	159.83	04/2017 -	03/2022	59	29.48	
486	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	252.05	159.32	04/2017 -	03/2022	59	27.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
487	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 -	03/2022	51	0	
488	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	341.40	09/2018 -	03/2022	42	0	
489	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	127.24	09/2018 -	03/2022	42	0	
490	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	03/2022	52	0	
491	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	0	
492	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	528.66	11/2018 -	04/2022	41	0	
493	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	134.40	09/2018 -	05/2022	44	0	
494	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	404.17	246.27	08/2018 -	05/2022	45	0	
495	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 -	06/2022	44	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
496	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36	403.36	224.23	06/2018	07/2022	49	0	
497	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57	339.57	186.85	09/2018	07/2022	46	0	
498	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78	1,383.78	299.26	07/2018	07/2022	48	0	
499	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00	216.00	120.10	11/2018	08/2022	45	0	
500	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31	274.31	136.62	05/2018	09/2022	52	0	
501	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24	417.24	276.32	05/2018	09/2022	52	0	
502	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68	285.68	100.70	09/2018	09/2022	48	0	
503	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28	306.28	135.84	05/2019	09/2022	40	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
504	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	87.49	09/2018 -	10/2022	49	0	
505	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA	03/2020	247.76 -	247.76	36.82	01/2022 -	10/2022	9	0	
506	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	156.49	09/2018 -	11/2022	50	0	
507	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	12/2022	50	0	
508	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	253.44	92.24	07/2019 -	12/2022	41	0	
509	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	636.42	55.56	12/2022 -	01/2023	1	0	
510	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	63.74	10/2018 -	03/2023	53	0	
511	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	140.92	09/2019 -	04/2023	43	0	
512	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	137.39	09/2019 -	04/2023	43	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
513	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82	537.82	163.81	09/2019	04/2023	43	0	
514	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM	03/2019	402.94	402.94	79.70	04/2022	05/2023	13	0	
515	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96	642.96	133.41	09/2019	06/2023	45	0	
516	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53	518.53	164.47	09/2019	06/2023	45	0	
517	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07	640.07	124.67	09/2019	07/2023	46	0	
518	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11	428.11	120.31	09/2019	09/2023	48	0	
519	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29	404.29	75.58	09/2019	04/2024	55	0	
	<u>National Highways Authority Of India</u>									
520	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00	166.90	84.29	05/2013	02/2022	105	-55.37	
521	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76	2,498.76	2,531.46	08/2014 03/2022	03/2022	91	0	Nil
522	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00	1,141.00	1,715.00	08/2013	03/2022	103	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
523	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 1,066.87	953.88	93.63	07/2013 03/2020	03/2022	104	0	
524	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	03/2022	103	0	
525	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 1,082.40	1,082.40	1,023.73	10/2013 03/2022	03/2022	101	126.2	
526	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	1,890.04	04/2015 03/2022	03/2022	83	0	
527	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (-) [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022	46	40.22	
528	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	03/2022	47	0	
529	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	1,056.08	1,020.25	11/2018 07/2019	03/2022	40	-25.83	
530	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI, KARNATAKA	03/2016	701.40 -	701.40	435.62	03/2019 -	03/2022	36	0	
531	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	904.16	-	02/2020 03/2022	03/2022	25	0	NA
532	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI, UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	1,357.48	03/2020 -	03/2022	24	0	
533	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	254.00	254.85	03/2020 -	03/2022	24	-14.24	Nil
534	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI, ODISHA	03/2017	1,288.07 -	1,420.00	1,100.45	03/2020 -	03/2022	24	10.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
535	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,701.66	03/2013 -	04/2022	109	0	
536	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	600.78	06/2018 12/2021	05/2022	47	0	Borrow area permission
537	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 1,023.23	1,023.23	980.59	07/2018 02/2022	05/2022	46	68.89	
538	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,300.00	971.90	09/2017 12/2021	05/2022	56	15.65	
539	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022	14	19.21	
540	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022	49	20.9	
541	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	244.16	03/2019 06/2022	06/2022	39	0	
542	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 1,376.86	1,376.86	887.23	04/2019 06/2022	06/2022	38	53.15	
543	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	653.06	08/2019 -	06/2022	34	0	
544	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	06/2022	26	3.95	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
545	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI, ODISHA	07/2017	476.56	476.56	258.64	07/2017	06/2022	59	0	
546	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI, MADHYA PRADESH	02/2019	990.97	990.97	845.00	12/2019	06/2022	30	0	
547	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 1,046.56	946.00	818.53	06/2018 07/2022	07/2022	49	0	Change in demand time to time by local as well as public representative for flyover like Kundapur, Pumpwell etc
548	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 567.00	639.58	501.61	04/2019 07/2022	07/2022	39	-38.57	
549	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI, TAMIL NADU	08/2017	1,176.37	1,176.37	742.16	08/2017	07/2022	59	0	
550	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI, TAMIL NADU	09/2017	1,227.87	1,227.87	841.80	09/2017	07/2022	58	0	
551	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI, MADHYA PRADESH	02/2019	847.00	847.00	635.00	03/2020	08/2022	29	0	
552	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI, MADHYA PRADESH	03/2019	1,047.00	1,047.00	673.00	05/2020	08/2022	27	0	
553	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI, MADHYA PRADESH	02/2019	996.27	996.27	737.00	03/2020	08/2022	29	0	
554	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70	1,100.70	2,933.43	06/2014	09/2022	99	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
555	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	106.65	04/2014 -	09/2022	101	0	
556	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	18.66	
557	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 2,639.00	1,655.01	1,867.51	08/2016 03/2023	03/2023	79	0	"a) Due to non-availability of work front on account of non-disbursement of land compensation to the land owners, since the land owners are not coming forward to accept the LA compensation as many of the land owners are out of country. However, the action has been taken to issue the 3E notification. The same is under implementation by the district administration. b) Frequent transfer of SLAO delays in disbursement of compensation. 1. Due to non-availability of work front on account of non-disbursement of land compensation to the land owners, since the land owners are not coming forward to accept the LA compensation as many of the land owners are out of country. However, the action has been taken to issue the 3E notification. The same is under implementation by the district administration 2. Frequent transfer of SLAO delays in disbursement of compensation.
558	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	03/2023	44	0	Nil

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
559	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 756.27	756.27	466.03	03/2020 03/2023	03/2023	36	.23	
560	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 736.01	830.31	105.50	03/2020 12/2018	03/2023	36	23.39	Procedural delay in Land Acquisition. Now, disbursement to land owner is under progress and possession of land received.
561	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	42.83	12/2017 -	05/2023	65	0	
562	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,913.66	08/2013 -	06/2023	118	0	
563	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 -	06/2023	51	-25.48	
564	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 08/2023	08/2023	49	0	Nil
565	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	1,168.00	354.24	08/2017 08/2018	10/2023	74	22.86	Delay in providing the vacant access and Right of way to the site and adverse law and order situation in an around the project area.
566	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	989.66	-	01/2024 -	04/2024	3	0	
567	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	982.00	-	03/2020 07/2022	07/2024	52	31.88	Nil
	Total		1,26,749.96 -	1,30,435.31	88,926.36					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
568	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 461.42	461.42	70.25	06/2021 11/2021	06/2022	12	7.02	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Cpwd For Telecom</u>									
569	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	173.87	03/2018 -	03/2022	48	0	
	<u>Department Of Telecommunication</u>									
570	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	80	84.97	
	Total		14,013.36 -	25,373.62	20,789.12					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
571	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,925.22	10,015.98	12/2018 -	08/2022	44	19.98	NIL
572	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	12,020.32	439.23	03/2024 -	06/2024	3	0	NIL
	<u>Bangalore Metro Rail Corporation Limited</u>									
573	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	20,025.67	02/2021 -	03/2025	49	0	
	<u>Central Public Works Department</u>									
574	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	217.00	187.17	04/2019 -	02/2022	34	9.97	Reasons were mentioned during period of occurrence, available in previous months report.
575	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	392.00	204.84	08/2020 04/2022	04/2022	20	0	
576	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	422.00	139.55	03/2021 06/2022	06/2022	15	0	
577	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	299.97	27.44	09/2020 -	05/2023	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
578	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 -	1,100.80	35.90	07/2021 06/2024	06/2024	35	-6.71	
579	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	1,128.00	30.00	03/2022 06/2024	06/2024	27	0	
	<u>Lucknow Metro Rail Corporation Limited</u>									
580	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	2,561.78	03/2024 -	11/2024	8	0	NO
581	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	593.47	03/2024 -	12/2025	21	0	NO
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
582	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	7,764.11	11/2021 -	12/2022	13	0	land acquisition and R & R.
	<u>Mumbai Metro Rail Corporation Ltd</u>									
583	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	20,484.28	03/2020 -	03/2023	36	44.39	
	<u>Madhya Pradesh Metro Rail Co Limited</u>									
584	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	6,941.40	409.75	02/2023 05/2025	05/2025	27	0	na
585	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	7,500.80	264.77	02/2023 07/2025	07/2025	29	0	na
	<u>Nagpur Metro Rail Corporation Ltd</u>									
586	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	9,759.79	8,462.32	03/2018 -	02/2022	47	12.44	NIL
	Total		1,29,952.06 -	1,43,394.54	71,646.26					
	<u>WATER RESOURCES</u>									
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(February 2022)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
587	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77 -	398.90	299.08	03/2020 -	03/2022	24	76.68	
588	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62 -	191.62	74.10	11/2020 -	03/2022	16	0	
589	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63 -	268.63	380.87	01/2021 -	05/2022	16	0	
590	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42 -	277.42	263.52	05/2021 -	05/2022	12	0	
591	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37 -	356.37	154.13	04/2021 -	06/2022	14	0	
592	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15 -	236.15	66.51	12/2020 -	07/2022	19	0	
593	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06 -	230.06	98.80	07/2021 -	03/2023	20	0	
594	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19 -	305.19	44.87	08/2021 -	04/2023	20	0	
595	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02 -	294.02	38.57	10/2021 -	12/2023	26	0	
596	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89 -	578.89	42.75	06/2022 -	12/2023	18	0	
597	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00 -	824.00	101.12	06/2022 -	12/2023	18	0	
598	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13 -	413.29	.07	09/2020 -	03/2024	42	62.63	
	<u>Delhi Jal Board</u>									
599	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB, DELHI	12/2018	515.07 -	515.07	363.66	01/2021 -	02/2022	13	0	
600	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79 -	211.79	261.19	12/2021 -	12/2022	12	0	
601	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11 -	239.11	176.36	02/2022 -	12/2022	10	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Kolkata Metropolitan Development Authority</u>									
602	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32	272.32	261.87	04/2020	03/2022	23	0	
603	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76	274.76	225.99	12/2019	05/2022	29	0	
604	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22	185.22	38.00	12/2021	09/2023	21	0	
605	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10	172.10	38.00	12/2021	09/2023	21	0	
606	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93	164.93	34.69	12/2021	09/2023	21	0	
607	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43	224.69	-	02/2022	03/2024	25	13.23	
608	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16	165.16	-	06/2022	03/2024	21	0	
609	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00	154.73	-	02/2022	03/2024	25	-3.29	
610	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96	384.96	-	04/2022	12/2024	32	0	
611	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL	03/2019	287.53	287.53	-	04/2022	12/2024	32	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
612	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	234.31	-	04/2022 -	12/2024	32	0	
613	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	307.12	-	09/2022 -	12/2024	27	0	
	<u>Polavaram Project Authority</u>									
614	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,422.33	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									
615	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	460.45	248.16	12/2020 -	03/2022	15	0	
616	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	206.05	95.91	10/2021 -	03/2022	5	0	
617	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	967.23	109.63	09/2021 -	09/2022	12	0	
618	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	767.59	152.31	09/2021 -	12/2022	15	0	
619	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	18	.97	
620	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	271.39	-	08/2021 -	03/2024	31	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
621	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12	213.91	-	07/2021	03/2024	32	-28.25	
622	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UP JalNigam, UTTAR PRADESH	10/2017	213.62	261.12	-	03/2022	04/2024	25	22.24	
623	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UP JalNigam, UTTAR PRADESH	02/2019	681.78	690.71	-	06/2022	04/2024	22	1.31	
<u>Uttarakhand Pey Jal Nigam</u>										
624	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UK JalNigam, UTTARAKHAND	03/2017	158.00	158.00	87.59	11/2019	03/2022	28	0	
	Total		22,222.12	67,947.69	22,108.45					
	<u>DEFENCE PRODUCTION</u>									
	<u>Cpwd For Defence</u>									
625	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENCE, KARNATAKA	12/2016	246.31	200.00	168.90	02/2020	06/2022	28	-18.8	
	Total		246.31	200.00	168.90					
	<u>DEPARTMENT OF HIGHER EDUCATION</u>									
	<u>Cpwd Of Higher Education</u>									
626	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD EDUCATION, JHARKHAND	09/2012	171.86	171.86	144.27	03/2016	03/2022	72	0	
627	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION, PUNJAB	01/2018	430.00	387.83	241.27	05/2020	08/2022	27	-9.81	Nil
628	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION, ODISHA	01/2019	790.79	790.79	294.36	03/2022	09/2022	6	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
629	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD EDUCATION,JAMMU AND KASHMIR	03/2019	424.93 -	424.93	86.21	07/2022 10/2022	10/2022	3	0	
630	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	318.94	07/2022 -	10/2022	3	0	
631	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	35.43	05/2022 -	10/2022	5	0	
632	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA	07/2019	851.00 851.00	851.00	361.47	03/2022 -	10/2022	7	0	
633	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD EDUCATION,HIMACHAL PRADESH	09/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022	4	0	1. Due to non-resolution of certain encumbrances at the site allotted by the Government of Himachal Pradesh at site. The construction has been effected and delayed at certain locations. Likely to be resolved shortly.
634	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34 -	655.34	375.85	06/2020 -	11/2022	29	0	
635	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26	0	
636	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	234.20	03/2021 -	02/2023	23	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
637	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 -	303.90	61.00	03/2020 -	02/2023	35	0	
638	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	193.83	77.27	06/2020 -	03/2023	33	0	
639	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	142.46	09/2022 -	06/2023	9	0	
640	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	498.99	318.32	06/2017 -	03/2022	57	.57	
	<u>Rites Of Higher Education</u>									
641	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N420000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	429.70	233.00	09/2014 06/2022	06/2022	93	-11.28	Due to Law and Order and subsequent delay
	Total		8,068.87 -	7,974.89	3,135.31					
	<u>HOME AFFAIRS</u>									
	<u>Cpwd For Mha</u>									
642	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	2,000.00	1,089.05	10/2019 -	06/2022	32	64.04	Mandatory Approvals/NOC from Local Bodies, Fire Deptt, SDMC, Delhi Monument Authority & CEC
643	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL	10/2014	162.88 -	228.63	173.62	04/2018 -	12/2022	56	40.37	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (February 2022)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
644	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 -	290.33	46.80	07/2022 -	12/2022	5	4.68	
645	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	199.31	75.31	01/2022 12/2022	12/2022	11	0	
646	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD FOR MHA,HARYANA	01/2020	166.98 166.98	166.98	7.84	10/2023 04/2024	04/2024	6	0	
Total			2,025.73 -	2,885.25	1,392.62					
DPIIT										
IICC For Dpiit										
647	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,178.00	3,062.37	12/2019 -	05/2022	29	8.49	
Total			4,773.00 -	5,178.00	3,062.37					
Grand Total										
			9,31,002.14	12,41,299.67	7,37,580.20					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(February 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	6,268.20	09/2010	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00	17,079.00	14,142.00	12/2016	12/2023	38.63	84
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00	19,220.00	17,806.00	12/2015	12/2022	67.73	84
	Total		27,271.00	43,139.00	38,216.20				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	145.28	09/2021	12/2023	38.72	27
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23	707.73	507.91	09/2018	10/2022	69.63	49
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	391.13	03/2021	03/2025	7.88	48
7	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00	1,938.00	579.75	09/2021	12/2023	40.13	27
	Total		3,288.50	4,358.06	1,624.07				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
8	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00	334.27	32.60	04/2018	06/2023	37.56	62
9	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13	341.22	91.55	03/2017	12/2022	12.20	69
	<u>Eastern Coal Fields Limited</u>								
10	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	625.60	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>								
11	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53	808.97	815.72	03/2013	03/2024	68.70	132
	<u>Neyveli Lignite Corporation</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00	17,237.80	13,185.30	11/2021	06/2023	.00	19
	<u>Western Coal Fields Limited</u>								
13	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56	299.67	213.93	03/2019	03/2022	1.39	36
	Total		21,220.95	24,168.41	14,964.70				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
14	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	318.32	06/2017	-	.57	57
	Total		496.18	498.99	318.32				
	<u>DPIIT</u>								
	<u>licc For Dpiit</u>								
15	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00	5,178.00	3,062.37	12/2019	05/2022	8.49	29
	Total		4,773.00	5,178.00	3,062.37				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Nbcc For Health</u>								
16	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00	1,471.00	1,089.38	09/2021	06/2022	8.88	9
	Total		1,351.00	1,471.00	1,089.38				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
17	NSG AT KOLKATA - [N28000104]	10/2014	162.88	228.63	173.62	04/2018	12/2022	40.37	56
18	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]	06/2019	277.35	290.33	46.80	07/2022	12/2022	4.68	5
19	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21	2,000.00	1,089.05	10/2019	06/2022	64.04	32
	Total		1,659.44	2,518.96	1,309.47				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>MINES</u>								
	<u>National Aluminum Company Limited (Nalco)</u>								
20	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	581.00	96.18	11/2020 -	12/2023	63.66	37
21	UTKAL D AND E COAL BLOCK - [N10000011	05/2016	534.00 -	667.23	395.98	01/2020 -	11/2023	24.95	46
22	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	6,435.90	1,268.54	04/2021 -	01/2024	16.17	33
	Total		6,429.00 -	7,684.13	1,760.70				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
23	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11	66
24	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	855.28	06/2019 -	02/2023	35.54	44
	<u>Gas Authority Of India Limited</u>								
25	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	120.91	02/2021 -	10/2022	9.91	20
26	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	233.20	08/2020 -	04/2022	14.17	20
27	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,781.00	12/2012 -	02/2025	102.71	146
	<u>Hindustan Petroleum Corporation Limited</u>								
28	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022	14.76	13
29	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 -	26,264.00	18,232.09	07/2020 -	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
30	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02 -	207.36	135.65	04/2020 -	10/2022	27.20	30
31	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	04/2018	206.63 -	340.76	172.39	02/2020 -	07/2022	64.91	29
32	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	06/2019	371.00 -	427.10	41.54	09/2022 -	03/2023	15.12	6
33	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	05/2016	348.00 -	437.00	226.74	01/2021 -	08/2022	25.57	19

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
34	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	543.00	176.32	09/2021 -	06/2022	17.46	9
35	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	753.89	495.80	02/2020 -	07/2022	26.07	29
36	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	568.65	10/2017 -	12/2022	103.60	62
37	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,315.92	03/2021 -	05/2022	66.09	14
38	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	3,154.79	12/2020 -	03/2022	43.82	15
39	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	4,270.46	12/2018 -	06/2022	33.98	42
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
40	DEVANGONTHI MARKETING TERMINAL - [N16000401]	06/2020	200.00 -	304.00	2.61	06/2023 -	01/2024	52.00	7
	<u>Oil & Natural Gas Corporation Limited</u>								
41	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	05/2019	763.92 -	829.58	829.58	12/2020 -	05/2022	8.60	17
42	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	1,613.65	05/2013 -	05/2022	132.23	108
43	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,375.90	2,892.72	04/2018 -	05/2022	5.80	49
44	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	3,233.86	05/2021 -	05/2022	2.17	12
45	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,790.56	03/2022 -	05/2023	23.16	14
	<u>Oil India Limited</u>								
46	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	412.80	02/2020 -	06/2022	17.41	28
	Total		52,668.79 -	70,001.30	48,306.91				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
47	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	9,558.69	09/2009 -	03/2023	152.52	162
48	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	15,300.08	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
49	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 -	293.03	118.68	10/2021 -	10/2022	11.93	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
50	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284	06/2019	401.90 -	442.03	293.40	04/2021 -	05/2022	9.99	13
51	DEVIKOT SOLAR 90MW - [N18000280	03/2020	501.29 -	524.83	400.95	09/2021 -	03/2022	4.70	6
52	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277	12/2016	529.68 -	679.00	513.91	11/2018 -	06/2022	28.19	43
53	DEVIKOT SOLAR 150MW - [N18000281	01/2020	798.24 -	852.90	596.05	09/2021 -	05/2022	6.85	8
54	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,803.00	754.00	09/2019 -	07/2025	30.48	70
55	NOKHRA - [N18000282	03/2020	1,722.14 -	1,803.19	612.20	09/2021 -	10/2022	4.71	13
56	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276	05/2016	1,885.13 -	2,426.00	2,027.32	12/2018 -	03/2022	28.69	39
57	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	5,867.38	5,247.00	03/2013 -	12/2024	96.99	141
58	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212	01/2016	10,598.98 -	10,998.00	9,223.00	11/2020 -	02/2023	3.76	27
59	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 -	17,007.00	12,634.00	06/2019 -	01/2024	18.38	55
60	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192	01/2013	12,964.60 -	17,304.00	16,748.00	05/2018 -	03/2022	33.47	46
61	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	21,312.11	19,738.00	10/2011 -	07/2023	145.16	141
<u>Power Grid Corporation Of India Limited</u>									
62	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262	05/2017	186.17 -	219.66	169.82	07/2019 -	08/2022	17.99	37
63	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	546.36	480.89	11/2016 -	03/2022	4.61	64
64	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264	08/2017	1,931.39 -	2,635.55	1,832.15	02/2020 -	04/2023	36.46	38
65	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	04/2022	14.11	21
66	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250	12/2014	5,111.33 -	6,700.00	3,522.04	12/2018 -	01/2024	31.08	61
67	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249	12/2014	4,754.42 -	9,129.32	3,182.67	12/2018 -	03/2024	92.02	63
<u>Satluj Jal Vidyut Nigam Limited</u>									
68	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022	46.20	6
<u>Thdc India Limited</u>									

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
69	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58	3,860.35	2,416.30	06/2013	06/2025	54.94	144
70	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	4,825.60	4,409.29	02/2016	06/2023	191.23	88
	Total		88,091.06	1,44,061.22	113,697.99				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
71	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19	1,283.49	524.21	03/2022	03/2023	.89	12
72	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89	1,387.52	358.30	03/2021	03/2023	75.00	24
73	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	2,271.50	4,794.60	2,921.95	03/2021	03/2023	111.08	24
	<u>East Central Railways</u>								
74	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00	819.01	540.73	03/2020	12/2024	49.45	57
75	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73	1,090.00	1,093.59	03/2012	06/2023	235.66	135
76	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64	1,185.73	452.12	03/2021	03/2024	62.06	36
77	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04	1,215.54	585.85	03/2021	12/2024	63.37	45
	<u>East Coast Railway</u>								
78	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61	810.02	209.78	11/2018	03/2025	15.45	76
79	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00	1,160.83	1,036.36	03/2020	03/2024	.07	48
80	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99	1,539.28	1,243.24	02/2019	03/2022	38.43	37
81	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78	1,928.07	947.41	06/2021	03/2025	137.80	45
82	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13	3,791.66	1,729.29	03/2009	12/2024	29.71	189
	<u>Eastern Railways</u>								
83	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17	439.30	508.16	03/2017	03/2025	20.30	96
84	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52	995.10	622.26	03/2016	03/2024	7.75	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
85	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91	1,619.48	912.17	03/2019 12/2009	03/2025	36.22	72
86	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98	2,137.81	472.06	03/2022	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
87	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00	3,055.15	2,800.17	09/2018	06/2022	.00	45
88	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00	4,970.11	1,078.79	03/2022	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>								
89	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74	774.51	539.14	06/2013	12/2022	56.23	114
90	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44	2,980.41	1,868.04	03/2004	06/2022	501.57	219
	<u>North Central Railway</u>								
91	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96	3,845.60	534.75	03/2022	12/2024	32.02	33
	<u>North East Frontier Railway</u>								
92	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63	708.73	549.81	03/2020	09/2022	24.42	30
93	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20	1,145.79	937.36	03/2019	03/2024	197.45	60
94	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96	1,873.21	1,646.66	03/2021	03/2022	115.07	12
95	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00	2,047.51	586.70	03/2019	12/2023	13.88	57
96	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87	2,145.00	1,108.94	03/2019	03/2024	302.54	60
97	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32	2,950.00	1,986.82	03/2022	03/2023	32.15	12
98	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47	6,527.00	4,766.68	03/2014	12/2023	172.70	117
99	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52	6,663.00	1,534.31	03/2015	03/2026	186.39	132
100	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48	8,600.00	2,504.91	12/2015	12/2023	542.04	96
101	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17	14,322.00	12,156.19	03/2011	12/2023	221.54	153
	<u>North Eastern Railway</u>								
102	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00	341.66	-	04/2017	10/2022	127.77	66

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
103	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	728.92	613.91	01/2019 -	-	147.09	37
	<u>North Western Railway</u>								
104	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	342.53	03/2020 -	10/2022	16.97	31
105	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	775.62	02/2019 -	06/2022	109.82	40
	<u>Northern Railway</u>								
106	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	480.97	03/2023 -	12/2025	369.35	33
107	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024	348.44	148
108	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	37,012.26	27,846.00	11/2002 -	04/2023	1,380.49	245
	<u>Rail Vikas Nigam Ltd.</u>								
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022	224.56	165
110	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	923.28	995.52	03/2021 -	05/2022	43.28	14
111	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	619.35	03/2016 -	04/2022	50.15	73
112	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023	57.26	48
113	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022	58.97	9
114	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING [N22000451]	02/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022	102.11	33
115	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023	64.62	48
116	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022	23.55	21
117	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022	111.91	25
118	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022	86.23	18
119	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022	102.92	88
120	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022	63.88	12
121	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022	281.93	24
122	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95	141

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
123	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	2,139.84	12/2024 -	12/2026	42.47	24
124	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022	141.61	27
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	3,139.94	03/2016 -	03/2026	7.78	120
126	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,834.54	1,586.17	03/2016 -	07/2025	65.94	112
127	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	24,659.00	6,259.16	12/2024 -	03/2025	52.07	3
<u>South Central Railway</u>									
128	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	713.38	03/2020 -	03/2022	31.75	24
129	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 -	1,373.74	695.73	03/2010 -	03/2025	18.38	180
130	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 -	1,952.68	803.75	03/2023 -	03/2024	5.16	12
131	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027	102.85	216
132	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	347.14	03/2014 -	03/2027	42.44	156
133	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023	98.57	276
134	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,495.93	03/2022 -	03/2025	7.06	36
<u>South East Central Railway</u>									
135	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60	36
136	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022	116.46	37
137	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	795.59	12/2021 -	12/2023	.07	24
138	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	833.36	03/2021 -	12/2023	8.23	33
139	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	1,576.19	03/2023 -	12/2023	66.44	9
<u>South Eastern Railway</u>									
140	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 -	393.83	23.56	06/2022 -	12/2023	16.52	18
141	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 -	472.50	1.62	06/2022 -	12/2025	10.23	42

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
142	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39	511.75	149.63	12/2021	01/2023	31.09	13
143	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,312.97	1,155.00	03/2020	06/2022	35.38	27
	<u>South Western Railway</u>								
144	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00	758.36	674.14	03/2020	02/2022	31.20	23
145	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	817.23	495.18	03/2017	03/2026	26.75	108
146	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43	1,104.00	1,014.52	03/2020	02/2022	28.31	23
147	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78	1,383.00	7.35	03/2002	03/2028	.02	312
148	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30	1,530.09	326.02	03/2016	12/2026	55.13	129
149	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59	1,878.00	1,530.18	03/2019	02/2024	16.31	59
150	HUBLI- CHIKAJAJUR - [N22000325]	03/2015	1,156.94	1,954.21	1,238.40	03/2020	12/2022	68.91	33
	<u>Southern Railway</u>								
151	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98	1,549.09	715.89	03/2020	03/2025	409.60	60
152	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70	2,111.88	314.32	03/2019	12/2027	1,649.69	105
153	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]	09/2007	724.69	3,081.20	1,726.52	02/2019	03/2025	325.17	73
	<u>West Central Railway</u>								
154	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13	1,247.64	561.88	03/2022	12/2023	114.32	21
155	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93	2,445.30	1,392.72	03/2020	10/2024	38.63	55
156	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23	2,875.12	1,035.16	03/2022	06/2023	16.02	15
157	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60	2,909.99	1,439.82	03/2021	03/2024	585.35	36
158	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66	8,248.50	2,908.60	05/2008	03/2025	3,230.57	202
	<u>Western Railway</u>								
159	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	126.35	03/2012	10/2023	1.06	139
160	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25	742.88	2.26	03/2020	03/2024	7.31	48
161	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39	1,056.11	808.35	03/2021	12/2022	5.36	21

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
162	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025	329.77	72
163	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022	33.41	21
164	CHOTTAUDEPUR-DHAR(NL) - [N22000138	04/2007	1,347.26 -	1,524.68	1,010.81	03/2022 -	10/2027	13.17	67
165	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024	167.96	48
166	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,383.82	2,404.99	03/2022 -	03/2026	82.20	48
	Total		1,32,322.50 -	2,74,928.00	153,156.25				
ROAD TRANSPORT AND HIGHWAYS									
<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
167	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	174.90	154.26	08/2018 -	03/2022	5.23	43
168	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885	03/2016	160.27 -	213.97	27.41	08/2019 -	03/2023	33.51	43
169	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576	02/2016	178.85 -	225.06	168.79	05/2016 -	06/2022	25.84	73
170	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	182.97	08/2018 -	03/2022	4.45	43
171	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 -	263.26	78.56	08/2019 -	03/2023	11.18	43
172	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	120.51	11/2018 -	03/2023	7.39	52
173	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41 -	319.96	193.60	03/2016 -	04/2022	13.30	73
174	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	12.16	19
175	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	368.28	05/2017 -	06/2022	45.75	61
176	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022	9.23	48
177	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	402.15	09/2016 -	03/2022	14.24	66

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
178	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	288.50	08/2016 -	12/2022	15.19	76
179	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578	02/2016	553.30 -	587.41	537.14	05/2016 -	03/2022	6.16	70
180	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574	11/2013	683.83 -	698.82	709.80	07/2016 -	06/2022	2.19	71
181	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	486.06	10/2016 -	06/2022	17.04	68
182	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922	12/2017	867.97 -	913.49	645.24	11/2018 -	07/2022	5.24	44
183	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	807.22	06/2019 -	03/2022	8.17	33
184	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579	01/2014	1,408.85 -	2,138.16	1,241.55	10/2016 -	03/2022	51.77	65
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
185	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	159.32	04/2017 -	03/2022	27.16	59
186	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	158.08	04/2017 -	03/2022	29.48	59
187	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	159.83	04/2017 -	03/2022	29.48	59
	<u>National Highways Authority Of India</u>								
188	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022	20.90	49
189	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022	40.22	46
190	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	466.03	03/2020 -	03/2023	.23	36
191	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	830.31	105.50	03/2020 -	03/2023	23.39	36
192	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	06/2022	3.95	26

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
193	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	07/2024	31.88	52
194	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	1,023.23	980.59	07/2018 -	05/2022	68.89	46
195	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]	11/2011	478.51 -	1,082.40	1,023.73	10/2013 -	03/2022	126.20	101
196	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]	08/2017	950.64 -	1,168.00	354.24	08/2017 -	10/2023	22.86	74
197	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 -	1,300.00	971.90	09/2017 -	05/2022	15.65	56
198	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	03/2016	899.00 -	1,376.86	887.23	04/2019 -	06/2022	53.15	38
199	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	1,100.45	03/2020 -	03/2022	10.24	24
200	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022	19.21	14
201	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66	105
	Total		22,965.74 -	28,298.41	20,727.35				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
202	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	19,611.48	05/2015 -	06/2022	41.32	85
	Total		15,525.00 -	21,940.00	19,611.48				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
203	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]	03/2020	431.16 431.00	461.42	70.25	06/2021 -	06/2022	7.02	12
	<u>Department Of Telecommunication</u>								
204	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	84.97	80
	Total		13,765.16 -	25,125.42	20,615.25				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
205	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00	12,925.22	10,015.98	12/2018	08/2022	19.98	44
	<u>Central Public Works Department</u>								
206	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33	217.00	187.17	04/2019	02/2022	9.97	34
	<u>Mumbai Metro Rail Corporation Ltd</u>								
207	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00	33,406.00	20,484.28	03/2020	03/2023	44.39	36
	<u>Nagpur Metro Rail Corporation Ltd</u>								
208	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00	9,759.79	8,462.32	03/2018	02/2022	12.44	47
	<u>Total</u>		42,786.33	56,308.01	39,149.75				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
209	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77	398.90	299.08	03/2020	03/2022	76.68	24
210	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13	413.29	0.07	09/2020	03/2024	62.63	42
	<u>Kolkata Metropolitan Development Authority</u>								
211	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43	224.69	-	02/2022	03/2024	13.23	25
	<u>Polavaram Project Authority</u>								
212	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04	55,548.87	18,422.33	03/2020	04/2022	447.22	25
	<u>Uttar Pradesh Jal Nigam</u>								
213	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79	234.03	28.37	12/2021	06/2023	.97	18
214	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62	261.12	-	03/2022	04/2024	22.24	25
215	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78	690.71	-	06/2022	04/2024	1.31	22
	<u>Total</u>		11,956.56	57,771.61	18,749.85				
	<u>Grand Total</u>		4,46,570.21	7,67,450.52	496,360.04				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 12/2021	12/2021
	Total		438.28 -		
	<u>COAL</u>				
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	03/2012
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	01/2027 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
7	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
	<u>Singareni Colliers Company Limited</u>				
9	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL, TELANGANA	03/2016	384.32 -	03/2020 -	03/2020
10	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL, TELANGANA	08/2017	442.42 -	03/2020 -	03/2020
11	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL, TELANGANA	08/2017	349.28 -	03/2021 -	03/2021
12	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212]SCCL, TELANGANA	03/2019	473.22 -	03/2021 -	03/2021
13	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL, TELANGANA	03/2017	164.04 -	03/2021 -	03/2021
	<u>South-Eastern Coal Fields Limited</u>				
14	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL, MADHYA PRADESH	12/2014	357.80 -	03/2021 -	-
	Total		16,052.32 -		
	<u>FINANCE</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Cpwd For Finance</u>				
15	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
16	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	11/2021
	Total		557.77 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
17	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	11/2019 -	01/2022
	Total		215.92 -		
	<u>PETROLEUM</u>				
	<u>Hindustan Petroleum Corporation Limited</u>				
18	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	07/2020 -	01/2022
19	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	12/2021
	<u>Indian Oil Corporation Limited</u>				
20	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 319.61	06/2020 12/2021	12/2021
21	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		1,446.66 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
24	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	07/2012 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 04/2019	-
	<u>Power Grid Corporation Of India Limited</u>				
26	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL,GUJARAT	10/2019	1,031.00 -	08/2021 -	08/2021
27	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE	02/2019	572.98 -	12/2020 -	12/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	08/2013 -	03/2018
	Total		24,430.75 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
29	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
30	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
31	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	03/2020 -	12/2021
	<u>Hll Infra Tech Services Limited</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
33	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
35	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
36	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
37	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	04/2020
38	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	01/2021
39	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
40	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021
41	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	04/2021
42	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	05/2021
43	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2021
44	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	12/2021
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	12/2021
48	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	- -	12/2021
49	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	12/2021
50	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	- -	01/2022
	Total		7,693.25 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
51	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
52	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
53	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
54	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 72,785.00	03/2020 06/2022	-
	<u>East Central Railways</u>				
55	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 -	03/2019 -	12/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
56	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
57	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
58	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
	<u>North East Frontier Railway</u>				
59	DIMPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
60	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	-
61	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
62	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
64	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021
65	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
66	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
67	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
68	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
	<u>Northern Railway</u>				
69	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
70	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
71	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 12/2022	-
	<u>South Central Railway</u>				
72	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
73	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-
	<u>Southern Railway</u>				
74	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
75	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
76	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
77	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
78	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
	Total		48,642.45 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
79	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
80	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
81	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	01/2022
82	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.22	08/2017 -	02/2020
83	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
84	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	05/2021
85	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	06/2021
86	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 -	11/2020 -	06/2021
87	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
88	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	07/2021
89	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	07/2021
90	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	07/2021
91	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	08/2021
92	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	09/2021
93	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
94	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	03/2027 -	09/2021
95	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	10/2020
96	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	10/2021
97	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	10/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
98	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021
99	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2020
100	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2021
101	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	12/2021
102	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	12/2021
103	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021
104	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	-	06/2019
105	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019
106	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	07/2019
107	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019
108	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019
109	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	11/2019
110	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019
111	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019
112	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019
113	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- 02/2019	01/2020
114	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	01/2020
115	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	01/2020
116	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	02/2020
117	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	03/2020
118	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020
119	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	03/2020

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
120	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	08/2020
121	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	09/2020
122	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	09/2020
123	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	09/2020
124	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	09/2020
125	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	10/2020
126	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 1,428.09	03/2020 -	10/2020
127	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	11/2020
128	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	11/2020
129	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	11/2020
130	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	11/2020
131	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020
132	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	11/2020
133	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020
134	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020
135	NAGAJ TO VAIJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	12/2020
136	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020
137	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	12/2020
138	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	12/2020
139	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	12/2020
140	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	12/2020
141	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	01/2021
142	WADIGODRI TO DHANGRI PIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	01/2021
143	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	03/2021
144	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	03/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
145	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	03/2021
146	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	04/2021
147	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	06/2021
148	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	06/2021
149	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021
150	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	07/2021
151	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	07/2021
152	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	07/2021
153	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	07/2021
154	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2021
155	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	09/2021
156	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021
157	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
158	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	12/2021
159	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021
160	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	12/2021
161	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	01/2022
162	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
163	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
164	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
165	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
166	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
167	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
168	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
169	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
170	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
171	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
172	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
173	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
174	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
175	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
176	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
177	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
178	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
179	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
180	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
181	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
182	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
183	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
184	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 01/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
185	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 07/2022	-
186	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 234.73	08/2018 08/2022	-
187	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 02/2022	-
188	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
189	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
190	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
191	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
192	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 386.99	08/2018 02/2022	-
193	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 686.13	01/2018 10/2022	-
194	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
195	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
196	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
197	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
198	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
199	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
200	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
201	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
202	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
203	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
204	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
205	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
206	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
207	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
208	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
209	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
210	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
211	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
212	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
213	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
214	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
215	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
216	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
217	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
218	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
219	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
220	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
222	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
223	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
224	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
225	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
226	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
227	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 187.61	05/2019 -	-
228	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-
229	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-
230	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-
231	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 03/2022	-
232	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
233	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
234	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
235	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
236	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	-
237	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-
238	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
239	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
240	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	03/2027 -	-
241	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	03/2027 -	-
242	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	03/2027 -	-
243	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	03/2027 -	-
244	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	03/2027 -	-
245	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	03/2027 -	-
246	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	03/2027 -	-
247	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	03/2027 -	-
248	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
249	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
250	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	03/2027 -	-
251	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	03/2027 -	-
252	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
253	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
254	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
255	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-
256	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
258	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
259	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-
260	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
261	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
262	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 05/2022	07/2021
<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
263	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA	06/2020	347.36 -	01/2022 -	01/2022
264	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA	06/2020	277.50 -	01/2022 -	01/2022
265	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA	06/2020	201.99 -	01/2022 -	01/2022
266	STRENGTHENING OF CHURAIBARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL,TRIPURA	06/2020	257.96 -	01/2022 -	01/2022
267	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
268	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021
269	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
270	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
271	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	09/2021
272	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	10/2021
273	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	10/2018 -	10/2021
274	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	10/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39 -	11/2018 -	11/2021
276	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL, NAGALAND	03/2018	237.72 -	09/2018 -	11/2021
277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL, NAGALAND	03/2018	251.97 -	09/2018 -	11/2021
278	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL, NAGALAND	03/2018	282.98 -	09/2018 -	11/2021
279	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	06/2018 -	12/2021
280	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	06/2018 -	12/2021
281	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	12/2021
282	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	09/2018 -	12/2021
283	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	09/2018 -	12/2021
284	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	09/2018 -	12/2021
285	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL, NAGALAND	03/2020	330.78 -	12/2021 -	12/2021
286	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL, NAGALAND	04/2020	330.80 -	12/2021 -	12/2021
287	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL, ASSAM	03/2017	1,049.51 -	- -	12/2021
288	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA	10/2014	369.00 -	03/2018 -	-
289	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL, SIKKIM	04/2017	388.00 -	10/2017 -	-
290	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL, SIKKIM	03/2018	264.84 -	06/2018 -	-
	<u>National Highways Authority Of India</u>				
291	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	01/2021
292	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
293	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	01/2022
294	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	02/2018
295	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	02/2018
296	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
297	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
298	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2017
299	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021
300	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
301	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	06/2021
302	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021
303	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	- -	07/2021
304	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
305	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
306	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
307	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	04/2019 -	09/2021
308	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
309	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	09/2021
310	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
311	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	10/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
312	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021
313	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 332) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018
314	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021
315	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021
316	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
317	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020
318	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021
319	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021
320	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021
321	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	12/2021
322	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	12/2021
323	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021
324	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	12/2021
325	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021
326	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016
327	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019
328	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
329	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 414.00	05/2018 11/2020	11/2020
330	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 09/2021	09/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
331	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 1,418.78	03/2019 10/2021	10/2021
332	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 2,421.37	- 12/2021	12/2021
333	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 01/2022	01/2022
334	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 01/2022	01/2022
335	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
336	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
337	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
338	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
339	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
340	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
341	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
342	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
343	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
344	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
345	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
346	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
347	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
348	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
349	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
350	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
351	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
352	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
353	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
354	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
355	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
356	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 2,047.64	03/2013 06/2021	-
357	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
358	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
359	2-LANING WITH PS RAIBARELI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
360	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
361	WIDENING OF KHEDE-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
362	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
363	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-
364	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
365	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
366	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 503.36	09/2016 -	-
367	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
368	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 416.00	- -	-
369	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	991.59 -	06/2018 -	-
370	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
371	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
372	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
373	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
374	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 1,414.01	06/2018 -	-
375	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
376	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
377	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
378	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
379	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
380	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
381	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
382	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
383	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
384	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
385	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
386	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
387	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
388	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
389	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	-
390	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
391	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
392	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
393	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
394	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	-
395	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
396	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
397	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
398	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
399	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
400	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
401	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
402	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
403	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
404	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
405	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
406	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
407	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
408	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
409	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
410	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
411	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
412	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
413	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
414	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
415	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
416	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
417	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
418	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
419	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
420	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	-
421	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
422	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
423	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
424	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
425	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
426	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
427	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
428	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-
429	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
430	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
431	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 01/2022	-
432	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
433	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
434	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
435	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
436	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
437	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	-
438	JUNAGADH BYPASS - [N24000701]NHAI, GUJARAT	10/2017	232.49 -	10/2017 -	-
439	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
440	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	-
441	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
442	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
443	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
444	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
445	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
446	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
447	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
448	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
449	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
450	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
451	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
452	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
453	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
454	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
455	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
456	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
457	FOUR LANING OF KHAMMAM-DEVARAPALLE SECTION (GREENFIELD) - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
458	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
459	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
460	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
461	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
462	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
463	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
464	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
465	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
466	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
467	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-
468	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
469	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
470	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
471	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
472	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
473	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
474	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
475	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
476	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
477	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
478	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	- 03/2021	-
479	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
480	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
481	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(February 2022)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
482	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
483	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
484	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
485	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
486	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	-
487	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	-
488	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,240.13	02/2021 04/2021	-
489	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
490	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
491	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
492	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
493	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
494	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
495	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 -	11/2019 -	-
496	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 -	11/2019 -	-
497	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 -	11/2019 -	-
	Total		2,76,209.28 -		
	URBAN DEVELOPMENT				
	Chennai Metro Rail Ltd				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
498	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
499	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	-
	<u>Delhi Metro Rail Corporation</u>				
500	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
501	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
502	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	07/2017 -	09/2020
	Total		62,701.79 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
503	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Delhi Jal Board</u>				
504	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFGARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	Total		578.38 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
505	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Central Public Works Department</u>				
506	C/O ADDITIONAL INFRASTRUCTURE AT IISC, BANGALORE.SH-RCC MONOLITHIC FOR MEN HOSTEL(S 14), WOMEN HOST - [N42000010]CPWD,KARNATAKA	08/2021	316.25 -	11/2021 -	-
	<u>Cpwd Of Higher Education</u>				
507	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	07/2021
508	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	07/2020 -	12/2021
509	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31 559.49	07/2019 07/2021	07/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
510	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 11/2021	11/2021
511	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	-
	Total		1,710.99 -		
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
512	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 -	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
513	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
514	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		4,55,700.80		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (February 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
1	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	101.10	- 05/2022	03/2023	10(R3)	17/26
2	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	730.20	226.83	- 05/2023	05/2023	0(R3)	13/17
	Total		818.00 -	960.00	327.93				30/43
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
3	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	670.22	- 08/2024	07/2025	11(R3)	0/0
	Total		4,287.59 -	4,287.59	670.22				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
4	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	538.47	- -	03/2022	-	0/0
	Total		601.02 -	601.02	538.47				0/0
	<u>RAILWAYS</u>								
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>								
5	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 28,181.00	51,219.00	35,951.00	- 06/2022	-	-	0/0
	<u>East Central Railways</u>								
6	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,650.00	3,679.49	- -	07/2022	-	0/0
7	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	981.50	- -	03/2024	-	0/0
8	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	1,536.32	- -	03/2024	-	0/0
9	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,483.14	1,469.46	- -	03/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
10	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [N20100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,610.87	- -	12/2024	-	0/0
11	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	392.88	- -	12/2024	-	0/0
12	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	320.25	- -	12/2024	-	0/0
13	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [N20100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	353.25	- -	03/2025	-	0/0
14	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	159.03	- -	12/2025	-	0/0
15	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.55	- -	03/2024	-	0/0
16	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,893.55	386.78	- -	03/2023	-	0/0
<u>Eastern Railways</u>									
17	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	502.48	529.13	- 09/2021	02/2022	5(R3)	0/0
18	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	333.93	- -	03/2022	-	0/0
19	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	311.86	- -	03/2022	-	0/0
20	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	418.15	- -	03/2024	-	0/0
<u>Metropolitan Rapid Transport Projects</u>									
21	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
<u>North Central Railway</u>									
22	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	-	- -	12/2027	-	0/0
<u>North East Frontier Railway</u>									
23	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	401.65	338.00	- -	03/2023	-	0/0
<u>North Eastern Railway</u>									
24	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	800.00	164.95	- -	12/2023	-	0/0
<u>Northern Railway</u>									
25	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	689.83	- -	09/2023	-	0/0
26	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	167.23	- -	09/2023	-	0/0
27	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	118.38	- -	03/2024	-	0/0
<u>South Western Railway</u>									

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
28	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	2,000.97	83.08	-	03/2025	-	0/0
29	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	-	03/2025	-	0/0
30	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,404.03	1,108.07	-	12/2025	-	2/2
31	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	-	03/2027	-	0/0
32	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	5,174.30	158.11	-	03/2028	-	0/0
33	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	-	03/2028	-	0/0
34	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	-	03/2028	-	0/0
Southern Railway									
35	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	749.40	591.35	-	03/2022	-	0/0
36	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	591.00	430.16	-	03/2022	-	0/0
37	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	1,431.90	942.65	-	03/2024	-	0/0
38	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	709.69	256.71	-	03/2025	-	0/0
39	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	448.10	268.74	-	03/2025	-	0/0
40	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	1,339.00	.83	-	03/2025	-	0/0
41	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	3,444.00	241.49	-	12/2025	-	0/0
42	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.01	.63	-	03/2030	-	0/0
Western Railway									
43	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	844.10	294.10	-	10/2025	-	0/0
	Total		35,981.21 -	98,379.74	54,291.15				2/2
ROAD TRANSPORT AND HIGHWAYS									
Ministry Of Road Transport And Highways (State Pwds)									
44	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	252.61	-	02/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
45	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	243.89	229.09	- -	02/2022	-	0/0
46	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 354.43	298.33	325.55	- 12/2021	03/2022	3(R3)	0/4
47	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	306.63	- -	03/2022	-	0/0
48	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	773.98	400.90	- -	03/2022	-	0/0
49	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	819.95	410.10	- -	03/2022	-	0/0
50	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	137.90	- -	03/2022	-	0/0
51	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	153.24	97.01	- 03/2022	03/2022	0(R3)	0/0
52	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	319.96	126.00	- -	03/2022	-	0/0
53	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	780.77	424.27	- 06/2022	06/2022	0(R3)	0/0
54	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 404.10	404.10	345.06	- 06/2022	06/2022	0(R3)	0/0
55	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	388.44	199.61	- -	06/2022	-	0/0
56	REHABILITATION AND UPGRADING OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	225.81	112.51	- -	09/2022	-	0/0
57	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	356.66	132.98	- -	09/2022	-	0/4
58	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	936.40	560.12	- 09/2022	12/2022	3(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
59	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	1,101.58	334.55	- -	03/2023	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
60	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	217.41	- -	03/2022	-	3/4
61	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	520.71	- -	03/2022	-	2/4
62	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	568.92	360.28	- -	03/2022	-	0/0
63	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	101.99	- -	04/2022	-	3/4
64	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	87.87	- 04/2022	04/2022	0(R3)	3/4
65	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	128.67	- -	12/2022	-	3/4
66	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	188.78	129.11	- -	12/2022	-	3/4
67	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	375.80	81.82	- -	04/2023	-	2/4
68	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	302.72	- -	04/2023	-	2/4
	<u>National Highways Authority Of India</u>								
69	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	720.08	- -	02/2022	-	0/0
70	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 2,330.79	2,330.79	1,246.85	- 02/2022	02/2022	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
71	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	415.26	- -	02/2022	-	0/0
72	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	252.05	- 02/2022	02/2022	0(R3)	0/0
73	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	237.47	- 02/2022	02/2022	0(R3)	0/0
74	REHABILITATION AND UPGRADE TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	1,148.65	- -	03/2022	-	0/0
75	6-LANING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	1,518.41	- -	03/2022	-	0/0
76	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH-69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	352.62	- -	03/2022	-	4/4
77	REHABILITATION AND UPGRADE OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	294.69	- -	03/2022	-	0/0
78	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	432.74	- -	03/2022	-	0/1
79	FOUR LANING OF MADURAI- CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	411.17	- -	03/2022	-	0/0
80	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 1,044.32	1,044.32	899.01	- 03/2022	03/2022	0(R3)	0/4
81	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	856.33	- -	04/2022	-	0/0
82	4-LANING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	529.08	- 01/2022	04/2022	3(R3)	2/4
83	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 1,407.35	1,407.35	1,162.45	- 04/2022	04/2022	0(R3)	0/4
84	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	289.28	- -	05/2022	-	0/1
85	4-LANING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	1,203.21	- 12/2021	05/2022	5(R3)	3/4

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
86	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	05/2022	-	0/0
87	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 1,118.07	1,118.07	957.15	- 05/2022	05/2022	0(R3)	3/4
88	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 986.10	986.10	837.89	- 05/2022	05/2022	0(R3)	0/4
89	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 1,072.08	1,072.08	956.46	- 05/2022	05/2022	0(R3)	3/4
90	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 1,173.65	1,173.65	1,070.65	- 05/2022	05/2022	0(R3)	3/4
91	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	897.00	- -	05/2022	-	3/4
92	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	290.00	- -	06/2022	-	0/0
93	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	514.05	- -	06/2022	-	0/0
94	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	359.38	- -	06/2022	-	0/0
95	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	254.00	- -	06/2022	-	0/0
96	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	158.96	- -	06/2022	-	0/0
97	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	314.43	85.61	- -	06/2022	-	0/0
98	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	806.11	450.59	- -	06/2022	-	0/0
99	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 1,238.29	1,238.29	1,111.87	- 06/2022	06/2022	0(R3)	3/4
100	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	557.00	- -	06/2022	-	1/3

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
101	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 1,330.02	1,330.02	920.72	- 07/2022	07/2022	0(R3)	0/0
102	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 1,206.48	1,206.48	1,006.03	- 07/2022	07/2022	0(R3)	3/4
103	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 793.63	793.63	291.10	- 09/2022	09/2022	0(R3)	0/0
104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96 -	884.00	671.00	- -	10/2022	-	2/4
105	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98 -	840.00	470.00	- -	11/2022	-	2/4
106	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	649.00	373.86	- 10/2021	12/2022	14(R3)	0/0
107	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	255.05	- -	12/2022	-	0/0
108	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	1,071.00	383.75	- -	12/2022	-	0/0
109	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	1,005.08	-	- 02/2023	02/2023	0(R3)	0/0
110	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 479.00	479.00	456.80	- 03/2023	03/2023	0(R3)	3/4
111	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	633.68	200.00	- -	03/2023	-	0/1
112	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	999.00	221.63	- -	03/2023	-	0/0
113	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 644.50	726.99	156.13	- 12/2019	06/2023	42(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (February 2022)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
114	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	482.04	-	- 08/2023	-	-	0/0
115	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	1,135.08	802.65	- 11/2022	-	-	0/0
116	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 2,501.85	2,501.85	946.08	- 02/2022	-	-	0/0
	Total		52,385.53 -	56,618.72	34,296.40				56/106
	URBAN DEVELOPMENT								
	National Building Construcion Corporation Ltd								
117	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	2,694.00	1,034.98	- -	03/2023	-	0/9
	Total		2,694.00 -	2,694.00	1,034.98				0/9
	Grand Total		96,767.35	1,63,541.07	91,159.15				88/160

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>COAL</u>					
	<u>Bharat Coking Coal Limited</u>					
1	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 -	03/2017 -	12/2022	0/0
2	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 -	04/2018 -	06/2023	0/0
	<u>Central Coal Fields Limited</u>					
3	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]CCL, JHARKHAND	07/2021	778.80 -	03/2026 -	03/2026	0/0
4	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]CCL, JHARKHAND	08/2020	7,254.37 -	03/2028 -	03/2028	0/0
5	EXPANSION PROJECT AMRAPALI OCP - [N06000217]CCL, JHARKHAND	08/2020	5,136.15 -	03/2028 -	03/2028	0/0
	<u>Eastern Coal Fields Limited</u>					
6	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
7	SONEPUR BAZARI EXPANSION OC - [N06000220]ECL, WEST BENGAL	07/2021	5,365.88 5,366.00	03/2029 -	03/2029	0/0
8	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]ECL, WEST BENGAL	04/2020	1,210.12 -	03/2029 -	03/2029	0/0
	<u>Mahanadi Coal Fields Limited</u>					
9	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	03/2012	0/0
10	GOPALJI-KANIHA OCP - [N06000229]MCL, ODISHA	08/2020	8,416.19 -	03/2028 -	03/2028	0/0
11	BALARAM EXPANSION OCP - [N06000230]MCL, ODISHA	08/2020	3,504.21 -	03/2029 -	03/2029	0/0
12	BHUBANESWARI EXPANSION OCP - [N06000227]MCL, ODISHA	08/2020	3,145.45 -	03/2031 -	03/2031	0/0
	<u>Neyveli Lignite Corporation</u>					
13	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
15	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
16	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
	<u>Singareni Colliers Company Limited</u>					
17	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL, TELANGANA	03/2016	384.32 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
18	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL,TELANGANA	08/2017	442.42 -	03/2020 -	03/2020	0/0
19	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL,TELANGANA	08/2017	349.28 -	03/2021 -	03/2021	0/0
20	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212]SCCL,TELANGANA	03/2019	473.22 -	03/2021 -	03/2021	0/0
21	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL,TELANGANA	03/2017	164.04 -	03/2021 -	03/2021	0/0
22	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]SCCL,TELANGANA	11/2015	489.62 -	03/2023 -	03/2023	0/0
	<u>South-Eastern Coal Fields Limited</u>					
23	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL,CHHATISGARH	07/2016	459.49 -	03/2020 -	03/2022	0/0
24	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
25	RAMPUR BATURA OC (4.0 MTY) - [N06000233]SECL,MADHYA PRADESH	07/2019	1,248.93 -	03/2026 -	03/2026	0/0
26	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]SECL,MADHYA PRADESH	03/2021	496.28 -	03/2028 -	03/2028	0/0
27	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
28	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
29	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>Western Coal Fields Limited</u>					
30	BHANEGAON OC (1MTY) - [N06000221]WCL,MAHARASHTRA	02/2017	409.68 -	03/2023 -	03/2023	0/0
31	ADASA UG TO OC (1.50 MTY) - [N06000219]WCL,MAHARASHTRA	11/2018	333.43 -	03/2024 -	03/2024	0/0
32	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]WCL,MAHARASHTRA	09/2018	313.34 -	03/2024 -	03/2024	0/0
33	DHANKASA UG (RECAST) (1 MTY) - [N06000224]WCL,MADHYA PRADESH	02/2020	289.30 -	03/2025 -	03/2025	0/0
34	RPR FOR JAMUNIA UG - [N06000228]WCL,MADHYA PRADESH	08/2020	281.25 -	03/2026 -	03/2026	0/0
35	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]WCL,MAHARASHTRA	11/2020	826.80 -	03/2026 -	03/2026	0/0
36	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL,MAHARASHTRA	02/2016	327.41 -	03/2019 -	09/2026	0/0
37	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]WCL,MAHARASHTRA	02/2020	1,184.33 -	03/2027 -	03/2027	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (SAIL)</u>					
38	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
39	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125]SAIL,ODISHA	01/2022	970.18 -	05/2025 -	05/2025	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
40	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA	07/2020	640.00 -	12/2021 -	06/2022	0/0
41	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	08/2022	0/0
42	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND	11/2018	248.55 -	06/2022 -	09/2022	0/0
43	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	02/2023	0/0
44	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
45	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
46	CBR 9 MMTPA PROJECT - [N16000434]CPCL,TAMIL NADU	01/2021	31,580.00 -	06/2025 -	06/2025	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
47	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	12/2021	0/0
48	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	03/2022	0/0
49	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
	<u>Indian Oil Corporation Limited</u>					
50	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 319.61	06/2020 12/2021	12/2021	0/0
51	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	03/2022	0/0
52	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	03/2021 03/2022	03/2022	0/0
53	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	01/2021 -	08/2022	0/0
54	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
55	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 09/2022	09/2022	0/0
56	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 03/2022	09/2022	0/0
57	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00 -	12/2022 -	12/2022	0/0
58	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
59	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 03/2023	03/2023	0/0
60	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
61	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
62	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 -	02/2024	0/0
63	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	02/2024	0/0
64	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]IOCL,HARYANA	02/2021	34,627.00 -	09/2024 -	09/2024	0/0
65	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]IOCL,RAJASTHAN	12/2021	9,028.00 -	10/2024 -	10/2024	0/0
66	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	02/2027 -	02/2027	0/0
67	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	08/2027 -	08/2027	0/0
68	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 -	08/2027	0/0
69	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	02/2028 -	02/2028	0/0
70	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	02/2028 -	02/2028	0/0
71	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 -	02/2028	0/0
72	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE	06/2019	303.00 -	02/2028 -	02/2028	0/0
73	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	12/2029 -	12/2029	0/0
74	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	12/2029 -	12/2029	0/0
75	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	12/2029 -	12/2029	0/0
76	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	12/2029 -	12/2029	0/0
77	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
78	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
79	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
<u>Numaligarh Refinery Limited</u>						
80	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
81	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Oil India Limited</u>					
82	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL, ASSAM	06/2016	224.75 -	08/2020 03/2022	03/2022	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
83	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL, JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 07/2025	07/2025	0/0
84	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL, JAMMU AND KASHMIR	03/2019	4,287.59 -	- 08/2024	07/2025	0/0
	<u>National Hydro-Electric Power Corporation</u>					
85	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
86	LOKTAK D/S HEP (NHPC) - [180100078]NHPC, MANIPUR	12/1999	578.62 -	06/2006	-	0/0
	<u>National Thermal Power Corporation</u>					
87	DEVIKOT SOLAR 90MW - [N18000280]NTPC, UTTAR PRADESH	03/2020	501.29 -	09/2021	03/2022	0/0
88	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC, RAJASTHAN	01/2020	1,522.71 -	09/2021 08/2022	03/2022	0/0
89	JETSAR SOLAR 160 MW - [N18000287]NTPC, RAJASTHAN	12/2019	702.28 -	03/2021 12/2021	03/2022	0/0
90	FATEHGARH SOLAR 296MW - [N18000289]NTPC, RAJASTHAN	03/2020	1,749.31 -	09/2021	03/2022	0/0
91	DEVIKOT SOLAR 150MW - [N18000281]NTPC, UTTAR PRADESH	01/2020	798.24 -	09/2021	05/2022	0/0
92	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC, TELANGANA	06/2019	401.90 -	04/2021	05/2022	0/0
93	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC, KERALA	09/2019	403.62 -	06/2021 01/2022	07/2022	0/0
94	BHENSARA 320 MW - [N18000293]NTPC, RAJASTHAN	01/2021	1,221.73 -	07/2022	07/2022	0/0
95	CHHATTARGARH 150 MW - [N18000294]NTPC, RAJASTHAN	02/2021	599.99 -	07/2022	07/2022	0/0
96	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC, GUJARAT	01/2021	842.27 -	07/2022	07/2022	0/0
97	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC, TAMIL NADU	03/2020	1,316.22 -	09/2021	08/2022	0/0
98	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) - [N18000296]NTPC, GUJARAT	05/2021	674.92 -	09/2022	09/2022	0/0
99	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	09/2021	10/2022	0/0
100	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT	08/2020	261.80 -	10/2021	10/2022	0/0
101	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC, RAJASTHAN	03/2020	1,782.00 -	09/2021 10/2022	10/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
102	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	03/2022 -	10/2022	0/0
103	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 04/2019	-	0/0
	<u>Power Grid Corporation Of India Limited</u>					
104	WESTERN REGION SYSTEM STRENGTHENING - XX - [N18000310]PGCIL,MULTI STATE	07/2019	226.98 -	08/2021 -	02/2022	0/0
105	SOUTHERN REGION SYSTEM STRENGTHENING - XXV - [N18000311]PGCIL,MULTI STATE	07/2019	154.72 -	07/2021 -	02/2022	0/0
106	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN - [N18000312]PGCIL,RAJASTHAN	08/2019	2,578.47 -	12/2020 -	02/2022	0/0
107	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII - [N18000318]PGCIL,MULTI STATE	09/2018	221.36 -	03/2021 -	02/2022	0/0
108	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL,GUJARAT	10/2019	1,031.00 -	08/2021 -	08/2021	0/0
109	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE	02/2019	572.98 -	12/2020 -	12/2020	0/0
110	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 -	02/2022	0/0
111	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2022	0/0
112	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 -	03/2022	0/0
113	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302]PGCIL,HARYANA	01/2019	267.33 -	03/2022 -	03/2022	0/0
114	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS - [N18000309]PGCIL,MULTI STATE	11/2018	496.11 -	06/2020 -	03/2022	0/0
115	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	12/2017 -	03/2022	0/0
116	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA - [N18000314]PGCIL,RAJASTHAN	01/2020	562.86 -	01/2021 -	03/2022	0/0
117	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE	07/2020	239.89 -	06/2021 -	03/2022	0/0
118	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 -	04/2022	0/0
119	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	12/2019 -	04/2022	0/0
120	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	04/2022	0/0
121	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	11/2021 -	05/2022	0/0
122	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	07/2019 -	08/2022	0/0
123	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300]PGCIL,RAJASTHAN	05/2021	1,184.88 -	09/2022 -	09/2022	0/0
124	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303]PGCIL,RAJASTHAN	03/2021	353.85 -	12/2022 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
125	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304]PGCIL,RAJASTHAN	03/2021	1,340.81 -	12/2022 -	12/2022	0/0
126	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305]PGCIL,RAJASTHAN	06/2021	713.82 -	12/2022 -	12/2022	0/0
127	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306]PGCIL,RAJASTHAN	06/2021	1,562.00 -	12/2022 -	12/2022	0/0
128	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307]PGCIL,RAJASTHAN	06/2021	1,006.00 -	12/2022 -	12/2022	0/0
129	NORTH EASTERN REGION STRENGTHENING SCHEME-XII - [N18000316]PGCIL,MULTI STATE	05/2021	576.42 -	03/2023 -	03/2023	0/0
130	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 -	04/2023	0/0
131	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION - [N18000299]PGCIL,BIHAR	05/2021	179.29 -	04/2023 -	04/2023	0/0
132	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	12/2018 -	01/2024	0/0
133	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	12/2018 -	03/2024	0/0
HEALTH AND FAMILY WELFARE						
Cpwd For Health						
134	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
135	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
136	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD FOR HEALTH,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
HII Infra Tech Services Limited						
137	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-	0/0
138	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-	0/0
139	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-	0/0
Hospital Services Consultancy Corporation Ltd						
140	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
141	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
142	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021	0/0
143	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	-	05/2021	0/0
144	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	-	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
145	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	11/2013	09/2021	0/0
146	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00	09/2018	12/2021	0/0
147	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15	03/2019	12/2021	0/0
148	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	-	12/2021	0/0
149	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	-	12/2021	0/0
150	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC, DELHI	12/2017	156.56	-	01/2022	0/0
151	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	-	03/2022	0/0
152	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99	05/2018	06/2022	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
153	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50	03/2021	03/2023	0/0
154	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	3,168.29	03/2023	03/2023	0/0
155	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89	03/2021	03/2023	0/0
156	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19	03/2022	03/2023	0/0
157	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR, MAHARASHTRA	02/2015	3,627.47 3,627.00	03/2024	03/2023	0/0
158	DAUND - MANMAD (236 KM) - [N22000360]CR, MAHARASHTRA	02/2016	1,876.00	03/2023	03/2023	0/0
159	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02	03/2022	03/2024	0/0
160	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR, MAHARASHTRA	02/2016	9,968.00	03/2024	03/2024	0/0
161	PUNE-NASIK (265 KM) - [N22000354]CR, MAHARASHTRA	02/2016	2,425.00	03/2024	03/2024	0/0
162	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91	03/2023	03/2024	0/0
163	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16	03/2022	03/2024	0/0
164	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95	03/2023	03/2024	0/0
165	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00	03/2024	-	0/0
	<u>Container Corporation Of India</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
166	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-	0/0
167	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
168	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 28,181.00	- 06/2022	-	0/0
169	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 72,785.00	03/2020 06/2022	-	0/0
	<u>East Central Railways</u>					
170	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2019 -	03/2022	0/0
171	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 3,020.95	- -	07/2022	0/0
172	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 967.29	03/2012 -	06/2023	0/0
173	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 1,625.87	- -	03/2024	0/0
174	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 1,470.50	- -	03/2024	0/0
175	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2024	0/0
176	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]ECR, BIHAR	04/2016	731.64 1,185.73	03/2021 -	03/2024	0/0
177	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 1,483.14	- -	03/2024	0/0
178	HAJIPUR-SUGAU LI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 2,066.78	- -	12/2024	0/0
179	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 735.20	- -	12/2024	0/0
180	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	03/2020 -	12/2024	0/0
181	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00 519.33	- -	12/2024	0/0
182	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR, BIHAR	04/2016	744.04 1,215.54	03/2021 -	12/2024	0/0
183	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 614.45	- -	03/2025	0/0
184	ARARIA-SUPAU LI (NL) - [N22000177]ECR, BIHAR	04/2008	1,605.17 1,605.17	- -	12/2025	0/0
185	BIHTA-AURANGABAD (NL) - [N22000170]ECR, BIHAR	04/2008	326.20 -	- -	03/2024	0/0
186	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	- -	03/2023	0/0
	<u>East Coast Railway</u>					
187	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	1,111.99 -	02/2019 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
188	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2024	0/0
189	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2024	0/0
190	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2024	0/0
191	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	12/2024	0/0
192	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2025	0/0
193	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2025	0/0
194	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2026	03/2026	0/0
195	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2022 03/2026	03/2026	0/0
Eastern Railways						
196	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- 09/2021	02/2022	0/0
197	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
198	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
199	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2024	0/0
200	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
201	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
202	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
203	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
204	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
Kolkata Metro Rail Corporation Limited						
205	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
Metropolitan Rapid Transport Projects						
206	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 -	06/2022	0/0
207	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
208	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
209	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>North Central Railway</u>					
210	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	06/2025	0/0
211	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	12/2027	0/0
	<u>North East Frontier Railway</u>					
212	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2022	0/0
213	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	03/2023	0/0
214	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
215	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
216	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	03/2014 -	12/2023	0/0
217	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	12/2023	0/0
218	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	03/2019 -	12/2023	0/0
219	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	03/2024	0/0
220	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	03/2019 -	03/2024	0/0
221	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
222	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
223	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 -	03/2021 -	-	0/0
224	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
225	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
	<u>North Eastern Railway</u>					
226	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0
227	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
228	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
229	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	03/2022	0/0
230	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	03/2022	0/0
231	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
232	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
233	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	12/2023	0/0
234	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	03/2025	0/0
235	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
236	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
237	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
	<u>North Western Railway</u>					
238	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	02/2019 -	06/2022	0/0
239	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	10/2022	0/0
240	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	11/2022	0/0
241	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
	<u>Northern Railway</u>					
242	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 04/2023	04/2023	0/0
243	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	09/2023	0/0
244	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	09/2023	0/0
245	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	03/2024	0/0
246	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	11/2024	0/0
247	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	08/2016 -	08/2025	0/0
248	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 12/2025	12/2025	0/0
249	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-	0/0
250	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
251	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2022	0/0
252	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	04/2022	0/0
253	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
254	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38	03/2021	05/2022	0/0
255	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70	02/2015	06/2022	0/0
256	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	03/2020	06/2022	0/0
257	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02	03/2020	06/2022	0/0
258	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25	12/2020	06/2022	0/0
259	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85	12/2020	09/2022	0/0
260	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66	12/2021	12/2022	0/0
261	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60	03/2022	12/2022	0/0
262	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00	03/2020	12/2022	0/0
263	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01	03/2019	03/2023	0/0
264	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95	03/2019	03/2023	0/0
265	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00	03/2022	05/2023	0/0
266	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26	12/2023	12/2023	0/0
267	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76	12/2023	12/2023	0/0
268	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94	12/2024	12/2024	0/0
269	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92	03/2023	12/2024	0/0
270	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99	12/2026	03/2025	0/0
271	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00	12/2024	03/2025	0/0
272	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78	12/2025	03/2025	0/0
273	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51	03/2016	07/2025	0/0
274	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42	03/2014	12/2025	0/0
275	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98	03/2016	03/2026	0/0
276	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67	12/2024	12/2026	0/0
	<u>South Central Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
277	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2023	0/0
278	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
279	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
280	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2025	0/0
281	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2027	0/0
282	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-	0/0
	<u>South East Central Railway</u>					
283	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 12/2023	12/2023	0/0
	<u>South Eastern Railway</u>					
284	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	06/2022	0/0
285	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	12/2021 -	01/2023	0/0
286	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2023	0/0
287	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	05/2023 -	12/2023	0/0
288	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	06/2022 -	12/2023	0/0
289	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	06/2022 -	12/2025	0/0
	<u>South Western Railway</u>					
290	YELAHANKA-PENUGONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	02/2022	0/0
291	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	03/2019 -	02/2024	0/0
292	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	03/2024	0/0
293	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	03/2025	0/0
294	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	03/2025	0/0
295	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
296	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2026	0/0
297	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	03/2017 -	03/2026	0/0
298	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	03/2027	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
299	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	-	03/2028	0/0
300	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78	03/2002	03/2028	0/0
301	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	-	03/2028	0/0
302	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	-	03/2028	0/0
	<u>Southern Railway</u>					
303	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14	-	03/2022	0/0
304	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41	-	03/2022	0/0
305	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90	-	03/2024	0/0
306	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98	03/2020	03/2025	0/0
307	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69	02/2019	03/2025	0/0
308	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96	-	03/2025	0/0
309	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	-	03/2025	0/0
310	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00	-	03/2025	0/0
311	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	-	12/2025	0/0
312	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70	03/2019	12/2027	0/0
313	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	-	03/2030	0/0
314	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00	-	-	0/0
315	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00	03/2016	-	0/0
	<u>Western Railway</u>					
316	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15	03/2021	12/2022	0/0
317	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,016.39	03/2021	12/2022	0/0
318	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00	06/2020	03/2023	0/0
319	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24	03/2012	10/2023	0/0
320	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74	03/2020	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
321	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25	03/2020	03/2024	0/0
322	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31	03/2024	12/2024	0/0
323	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04	03/2022	03/2025	0/0
324	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66	03/2019	03/2025	0/0
325	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10	-	10/2025	0/0
326	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	03/2022	03/2026	0/0
327	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18	03/2022	03/2026	0/0
328	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26	03/2022	10/2027	0/0
329	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88	-	-	0/0
330	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38	-	-	0/0
331	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26	-	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
332	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54	08/2015	01/2021	0/0
333	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18	02/2020	01/2021	0/0
334	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59	-	01/2022	0/0
335	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.22	08/2017	02/2020	0/0
336	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRth,UTTAR PRADESH	03/2016	240.30 240.00	01/2020	03/2021	0/0
337	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51	11/2019	05/2021	0/0
338	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34	11/2019	06/2021	0/0
339	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70	11/2020	06/2021	0/0
340	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34	12/2019	07/2021	0/0
341	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34	12/2019	07/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
342	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	07/2021	0/0
343	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	08/2021	0/0
344	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	09/2021	0/0
345	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	03/2027 -	09/2021	0/0
346	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	10/2020	0/0
347	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	-	10/2021	0/0
348	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	10/2021	0/0
349	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021	0/0
350	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2020	0/0
351	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2021	0/0
352	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	12/2021	0/0
353	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	12/2021	0/0
354	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021	0/0
355	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019	0/0
356	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019	0/0
357	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019	0/0
358	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019	0/0
359	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019	0/0
360	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019	0/0
361	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020	0/0
362	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020	0/0
363	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
364	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020	0/0
365	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020	0/0
366	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021	0/0
367	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021	0/0
368	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021	0/0
369	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021	0/0
370	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	12/2021	0/0
371	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	01/2022	0/0
372	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- -	02/2022	0/0
373	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	02/2022	0/0
374	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	02/2022	0/0
375	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 -	02/2022	0/0
376	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- -	03/2022	0/0
377	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	01/2020 -	03/2022	0/0
378	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	03/2022	0/0
379	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	03/2022	0/0
380	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2-LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 587.41	05/2016 03/2022	03/2022	0/0
381	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 03/2022	03/2022	0/0
382	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	03/2022	0/0
383	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	03/2022	0/0
384	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	03/2022	0/0
385	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	03/2022	0/0
386	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
387	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	03/2022	0/0
388	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	03/2022	0/0
389	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	03/2022	0/0
390	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	03/2022	0/0
391	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	03/2022	0/0
392	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	03/2022	0/0
393	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- 03/2022	03/2022	0/0
394	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	03/2022	0/0
395	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	03/2022	0/0
396	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	03/2022	0/0
397	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	03/2022	0/0
398	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 -	03/2022	0/0
399	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	03/2022	0/0
400	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	03/2022	0/0
401	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	03/2018 -	03/2022	0/0
402	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 -	03/2022	0/0
403	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	03/2022	0/0
404	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	03/2022	0/0
405	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	03/2022	0/0
406	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	09/2016 -	03/2022	0/0
407	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 -	03/2022	0/0
408	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 -	03/2022	0/0
409	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	04/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
410	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	04/2022	0/0
411	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	04/2022	0/0
412	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	04/2022	0/0
413	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	01/2021 -	04/2022	0/0
414	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 -	04/2022	0/0
415	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 05/2022	05/2022	0/0
416	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- 06/2022	06/2022	0/0
417	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 06/2022	06/2022	0/0
418	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 404.10	- 06/2022	06/2022	0/0
419	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 698.82	07/2016 06/2022	06/2022	0/0
420	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 225.06	05/2016 06/2022	06/2022	0/0
421	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 -	06/2022	0/0
422	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	06/2022	0/0
423	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	06/2022	0/0
424	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	10/2016 -	06/2022	0/0
425	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 -	06/2022	0/0
426	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	07/2022	0/0
427	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	09/2022	0/0
428	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	09/2022	0/0
429	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	10/2022	0/0
430	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- 09/2022	12/2022	0/0
431	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
432	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	09/2019 01/2022	12/2022	0/0
433	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	09/2020 01/2022	12/2022	0/0
434	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM	09/2018	160.00 -	09/2021 12/2022	12/2022	0/0
435	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	08/2016 -	12/2022	0/0
436	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	07/2016 -	12/2022	0/0
437	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
438	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 12/2022	12/2022	0/0
439	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	03/2027 -	02/2023	0/0
440	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	03/2023	0/0
441	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 03/2022	03/2023	0/0
442	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	10/2020 12/2021	03/2023	0/0
443	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 -	08/2019 11/2022	03/2023	0/0
444	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 -	08/2019 08/2022	03/2023	0/0
445	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373]MoRTH,ARUNACHAL PRADESH	01/2020	358.26 -	02/2024 -	02/2024	0/0
446	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]MoRTH,UTTAR PRADESH	07/2018	1,948.25 -	02/2024 -	02/2024	0/0
447	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH,ARUNACHAL PRADESH	02/2021	588.09 -	03/2024 -	03/2024	0/0
448	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]MoRTH,ASSAM	02/2021	925.47 -	07/2025 -	07/2025	0/0
449	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
450	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-	0/0
451	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-	0/0
452	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
453	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
454	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-	0/0
455	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
456	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
457	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
458	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
459	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
460	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
461	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
462	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
463	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
464	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
465	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING REHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
466	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0
467	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
468	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
469	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
471	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
473	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
474	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
475	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
476	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
477	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
478	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
479	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
480	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
481	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
482	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
483	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-	0/0
484	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
485	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
486	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
487	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
488	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
489	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0
490	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
491	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
492	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
493	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
494	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
495	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
496	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
497	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 187.61	05/2019 -	-	0/0
498	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-	0/0
499	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-	0/0
500	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-	0/0
501	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 03/2022	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
502	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH, BIHAR	02/2019	2,926.42 -	- -	-	0/0
503	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH, ASSAM	03/2020	166.94 -	12/2020 12/2022	-	0/0
504	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH, ARUNACHAL PRADESH	03/2019	342.55 -	03/2027 -	-	0/0
505	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH, ARUNACHAL PRADESH	03/2019	421.48 -	03/2027 -	-	0/0
506	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH, ARUNACHAL PRADESH	03/2019	543.05 -	03/2027 -	-	0/0
507	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH, ARUNACHAL PRADESH	03/2019	486.70 -	03/2027 -	-	0/0
508	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH, ARUNACHAL PRADESH	03/2019	560.39 -	03/2027 -	-	0/0
509	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH, ARUNACHAL PRADESH	03/2019	347.78 -	03/2027 -	-	0/0
510	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH, ARUNACHAL PRADESH	03/2019	394.27 -	03/2027 -	-	0/0
511	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH, ARUNACHAL PRADESH	03/2019	450.65 -	03/2027 -	-	0/0
512	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH, KERALA	02/2017	294.28 -	08/2017 -	-	0/0
513	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH, KERALA	02/2017	380.76 -	09/2017 -	-	0/0
514	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH, ARUNACHAL PRADESH	06/2020	437.60 -	03/2027 -	-	0/0
515	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH, ARUNACHAL PRADESH	06/2020	496.47 -	03/2027 -	-	0/0
516	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH, HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-	0/0
517	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH, HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-	0/0
518	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH, HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-	0/0
519	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH, KARNATAKA	01/2017	264.34 -	09/2017 -	-	0/0
520	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH, RAJASTHAN	12/2020	379.23 -	10/2021 -	-	0/0
521	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH, RAJASTHAN	12/2020	339.65 -	10/2021 -	-	0/0
522	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH, HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
523	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL, ARUNACHAL PRADESH	09/2016	568.92 -	- -	03/2022	0/0
524	IMPHAL – MOREH (PACKAGE 4) - [N24001399]NHIDCL, MANIPUR	03/2021	277.99 -	01/2023 -	01/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
525	KHELLANI-KHANABAL PKG-2 - [N24001394]NHIDCL,JAMMU AND KASHMIR	07/2021	512.43 -	02/2023 -	02/2023	0/0
526	KHELLANI-KHANABAL PKG-5 - [N24001396]NHIDCL,JAMMU AND KASHMIR	07/2021	497.09 -	02/2023 -	02/2023	0/0
527	GOHA-KHELLANI PKG-3 - [N24001397]NHIDCL,JAMMU AND KASHMIR	02/2021	431.28 -	03/2023 -	03/2023	0/0
528	MARIAM - PEREN (PKG 2A) - [N24001398]NHIDCL,MANIPUR	07/2021	204.58 -	03/2023 -	03/2023	0/0
529	IMPHAL - KHONGSANG PKG-3 - [N24001401]NHIDCL,MANIPUR	07/2021	467.00 -	03/2023 -	03/2023	0/0
530	TAMENGLONG - MAHUR PKG-1 - [N24001402]NHIDCL,MANIPUR	07/2021	185.80 -	03/2023 -	03/2023	0/0
531	TAMENGLONG - MAHUR PKG-2 - [N24001403]NHIDCL,MANIPUR	07/2021	483.87 -	03/2023 -	03/2023	0/0
532	TAMENGLONG - MAHUR PKG-4 - [N24001404]NHIDCL,MANIPUR	07/2021	198.77 -	03/2023 -	03/2023	0/0
533	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]NHIDCL,NAGALAND	07/2021	258.52 -	03/2023 -	03/2023	0/0
534	PEREN-DIMAPUR PKG-5 - [N24001407]NHIDCL,NAGALAND	02/2021	207.33 -	03/2023 -	03/2023	0/0
535	KHELLANI-KHANABAL PKG-4 - [N24001395]NHIDCL,JAMMU AND KASHMIR	07/2021	859.67 -	08/2023 -	08/2023	0/0
536	CHURACHANPUR TUIVAI PKG-3 - [N24001405]NHIDCL,MANIPUR	07/2021	673.27 -	10/2023 -	10/2023	0/0
	<u>National Highways Authority Of India</u>					
537	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022	0/0
538	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	02/2018	0/0
539	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	02/2018	0/0
540	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021	0/0
541	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	02/2022	0/0
542	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021	0/0
543	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
544	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020	0/0
545	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021	0/0
546	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	- -	07/2021	0/0
547	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
548	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020	0/0
549	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021	0/0
550	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	04/2019 -	09/2021	0/0
551	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
552	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	09/2021	0/0
553	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
554	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
555	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018	0/0
556	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
557	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021	0/0
558	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020	0/0
559	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020	0/0
560	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021	0/0
561	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021	0/0
562	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021	0/0
563	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	12/2021	0/0
564	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
565	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	12/2021	0/0
566	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0
567	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016	0/0
568	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019	0/0
569	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020	0/0
570	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 1,418.78	03/2019 10/2021	10/2021	0/0
571	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 2,421.37	- 12/2021	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
572	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	02/2022	0/0
573	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 2,330.79	- 02/2022	02/2022	0/0
574	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	02/2022	0/0
575	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- 02/2022	02/2022	0/0
576	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- 02/2022	02/2022	0/0
577	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 03/2022	03/2022	0/0
578	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	03/2022	0/0
579	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 1,066.87	07/2013 03/2020	03/2022	0/0
580	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 1,082.40	10/2013 03/2022	03/2022	0/0
581	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	03/2022	0/0
582	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2022	0/0
583	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 07/2019	03/2022	0/0
584	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2022	0/0
585	REHABILITATION AND UPGADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	03/2022	0/0
586	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022	0/0
587	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 03/2022	03/2022	0/0
588	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	03/2022	0/0
589	REHABILITATION AND UPGADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2022	0/0
590	REHABILITATION AND UPGADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	03/2022	0/0
591	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	03/2022	0/0
592	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	04/2022	0/0
593	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	04/2022	0/0
594	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 12/2021	05/2022	0/0
595	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 1,023.23	07/2018 02/2022	05/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
596	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 12/2021	05/2022	0/0
597	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	05/2022	0/0
598	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 06/2022	06/2022	0/0
599	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 1,376.86	04/2019 06/2022	06/2022	0/0
600	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	06/2022	0/0
601	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	06/2022	0/0
602	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	06/2022	0/0
603	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	06/2022	0/0
604	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	06/2022	0/0
605	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	06/2022	0/0
606	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	06/2022	0/0
607	REHABILITATION AND UP-GRADATION TO 4-LANNING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	06/2022	0/0
608	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	06/2022	0/0
609	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	06/2022	0/0
610	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 567.00	04/2019 07/2022	07/2022	0/0
611	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 1,330.02	- 07/2022	07/2022	0/0
612	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0
613	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
614	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	09/2022	0/0
615	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	09/2022	0/0
616	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 793.63	- 09/2022	09/2022	0/0
617	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
618	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	- 10/2021	12/2022	0/0
619	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
620	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	12/2022	0/0
621	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- 02/2023	02/2023	0/0
622	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 2,639.00	08/2016 03/2023	03/2023	0/0
623	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	03/2023	0/0
624	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 736.01	03/2020 12/2018	03/2023	0/0
625	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	03/2023	0/0
626	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 -	03/2023 -	03/2023	0/0
627	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	05/2023	0/0
628	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	06/2023	0/0
629	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 644.50	- 12/2019	06/2023	0/0
630	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 08/2023	08/2023	0/0
631	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	08/2017 08/2018	10/2023	0/0
632	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRA ROAD (SH-1 - [N24001414]NHAI,PUNJAB	12/2020	733.00 -	01/2024 04/2024	01/2024	0/0
633	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415]NHAI,PUNJAB	12/2020	881.00 -	04/2024 -	04/2024	0/0
634	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	01/2024 -	04/2024	0/0
635	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417]NHAI,PUNJAB	12/2020	1,234.40 -	04/2024 -	04/2024	0/0
636	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418]NHAI,PUNJAB	12/2020	1,094.46 -	04/2024 -	04/2024	0/0
637	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- - [N24001419]NHAI,PUNJAB	02/2021	1,269.96 -	04/2024 -	04/2024	0/0
638	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420]NHAI,PUNJAB	02/2021	853.66 -	04/2024 -	04/2024	0/0
639	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 07/2022	07/2024	0/0
640	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
641	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
642	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
643	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
644	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
645	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
646	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
647	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
648	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
649	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
650	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
651	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
652	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
653	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
654	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
655	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 2,047.64	03/2013 06/2021	-	0/0
656	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
657	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
658	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
659	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
660	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
661	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
662	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
663	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 503.36	09/2016 -	-	0/0
664	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
665	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 416.00	- -	-	0/0
666	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	991.59 -	06/2018 -	-	0/0
667	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
668	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
669	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
670	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
671	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 1,414.01	06/2018 -	-	0/0
672	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
673	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
674	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-	0/0
675	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
676	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
677	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-	0/0
678	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
679	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
680	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
681	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
682	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
683	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
684	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
685	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
686	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	-	0/0
687	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
688	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
689	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
690	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	-	0/0
691	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
692	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00	07/2008	-	0/0
693	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73	04/2019	-	0/0
694	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50	-	-	0/0
695	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74	-	-	0/0
696	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49	04/2019	-	0/0
697	SIX-LANNING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60	-	-	0/0
698	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00	06/2019	-	0/0
699	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84	05/2017	-	0/0
700	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97	-	-	0/0
701	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03	-	-	0/0
702	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00	04/2019	-	0/0
703	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34	09/2019	-	0/0
704	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61	-	-	0/0
705	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18	-	-	0/0
706	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72	08/2018	-	0/0
707	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71	-	-	0/0
708	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03	08/2018	-	0/0
709	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69	08/2019	-	0/0
710	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25	03/2019	-	0/0
711	4-LANNING OF KODEBAD-DHMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17	03/2019	-	0/0
712	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00	02/2017	-	0/0
713	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75	-	-	0/0
714	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55	-	-	0/0
715	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR- 77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68	-	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
716	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
717	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
718	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
719	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
720	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
721	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
722	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
723	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
724	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	-	0/0
725	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
726	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
727	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
728	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
729	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
730	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
731	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
732	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
733	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
734	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
735	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
736	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
737	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
738	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
739	FOUR LANING OF KHAMMAM-DEVARAPALLE SECTION (GREENFIELD) - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
740	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
741	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
742	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
743	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
744	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
745	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
746	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
747	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
748	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
749	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
750	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
751	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
752	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
753	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
754	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
755	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
756	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
757	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
758	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
759	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	- 03/2021	-	0/0
760	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- 08/2023	-	0/0
761	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
762	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
763	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
764	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-	0/0
765	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-	0/0
766	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
767	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- 11/2022	-	0/0
768	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
769	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	-	0/0
770	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	-	0/0
771	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,240.13	02/2021 04/2021	-	0/0
772	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
773	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
774	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0
775	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
776	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-	0/0
777	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 -	11/2019 -	-	0/0
778	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 -	11/2019 -	-	0/0
779	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 -	11/2019 -	-	0/0
780	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 2,501.85	- 02/2022	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
781	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 461.42	06/2021 11/2021	06/2022	0/0
	<u>Department Of Telecommunication</u>					
782	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	03/2022	0/0
	<u>URBAN DEVELOPMENT</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Central Public Works Department</u>					
783	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	03/2021 06/2022	06/2022	0/0
784	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 -	03/2022 06/2024	06/2024	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
785	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	09/2020	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
786	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	11/2024	0/0
787	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	12/2025	0/0
	<u>Maharastra Metro Rail Corporation Ltd.</u>					
788	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	12/2022	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
789	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	03/2020 -	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
790	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 05/2025	05/2025	0/0
791	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 07/2025	07/2025	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
792	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	02/2022	0/0
	<u>Patna Metro Rail Corporation</u>					
793	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 -	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
794	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPP,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
795	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2022	0/0
796	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 -	03/2022	0/0
797	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	05/2022	0/0
798	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
799	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37	04/2021	06/2022	0/0
800	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15	12/2020	07/2022	0/0
801	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06	07/2021	03/2023	0/0
802	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19	08/2021	04/2023	0/0
803	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02	10/2021	12/2023	0/0
804	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89	06/2022	12/2023	0/0
805	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00	06/2022	12/2023	0/0
806	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13	09/2020	03/2024	0/0
Delhi Jal Board						
807	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07	01/2021	02/2022	0/0
808	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78	12/2022	12/2022	0/0
809	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79	12/2021	12/2022	0/0
810	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11	02/2022	12/2022	0/0
811	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81	05/2020	-	0/0
Kolkata Metropolitan Development Authority						
812	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32	04/2020	03/2022	0/0
813	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76	12/2019	05/2022	0/0
814	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22	12/2021	09/2023	0/0
815	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10	12/2021	09/2023	0/0
816	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93	12/2021	09/2023	0/0
817	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43	02/2022	03/2024	0/0
818	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16	06/2022	03/2024	0/0
819	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00	02/2022	03/2024	0/0
820	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96	04/2022	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)

			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
821	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	12/2024	0/0
822	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	12/2024	0/0
823	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	12/2024	0/0
	<u>Uttar Pradesh Jal Nigam</u>					
824	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam, UTTAR PRADESH	12/2017	460.45 -	12/2020 -	03/2022	0/0
825	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam, UTTAR PRADESH	01/2019	206.05 -	10/2021 -	03/2022	0/0
826	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam, UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2022	0/0
827	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam, UTTAR PRADESH	05/2017	767.59 -	09/2021 -	12/2022	0/0
828	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam, UTTAR PRADESH	01/2019	231.79 -	12/2021 -	06/2023	0/0
829	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam, UTTAR PRADESH	03/2019	271.39 -	08/2021 -	03/2024	0/0
830	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam, UTTAR PRADESH	03/2019	298.12 -	07/2021 -	03/2024	0/0
831	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam, UTTAR PRADESH	10/2017	213.62 -	03/2022 -	04/2024	0/0
832	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam, UTTAR PRADESH	02/2019	681.78 -	06/2022 -	04/2024	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
833	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam, UTTARAKHAND	03/2017	158.00 -	11/2019 -	03/2022	0/0
	<u>COMMERCE</u>					
	<u>Nbcc For Commerce</u>					
834	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER, DELHI	06/2018	302.64 -	10/2020 -	-	0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
	<u>Central Public Works Department</u>					
835	C/O ADDITIONAL INFRASTRUCTURE AT IISC, BANGALORE.SH- RCC MONOLITHIC FOR MEN HOSTEL(S 14), WOMEN HOST - [N42000010]CPWD, KARNATAKA	08/2021	316.25 -	11/2021 -	-	0/0
	<u>Cpwd Of Higher Education</u>					
836	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION, CHHATTISGARH	03/2020	808.62 -	07/2022 -	10/2022	0/0
837	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION, ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	06/2023	0/0
	<u>Rites Of Higher Education</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (February 2022)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
838	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES OF HIGHER,MEGHALAYA	09/2013	484.32 429.70	09/2014 06/2022	06/2022	0/0
	<u>HOME AFFAIRS</u>					
	<u>Cpwd For Mha</u>					
839	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003]CPWD FOR MHA,UTTAR PRADESH	05/2019	199.31 -	01/2022 12/2022	12/2022	0/0
	<u>DPIIT</u>					
	<u>Dmic For Dpiit</u>					
840	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 -	07/2021	0/0
	<u>Iicc For Dpiit</u>					
841	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	12/2019 -	05/2022	0/0
	<u>RENEWABLE ENERGY</u>					
	<u>Cpwd For Renewable Energy</u>					
842	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-	0/0
	Total		10,01,262.25 -			0/0
	Grand Total		10,01,262.25			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
1	PACHWARA SOUTH COAL BLOCK - [N06000193	7/2013	1,795.01	1,795.01	38.76	09/2028	09/2023
	Total		1,795.01	1,795.01	38.76		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
2	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150	3/2019	1,828.00	1,828.00	232.40	09/2025	05/2024
	Total		1,828.00	1,828.00	232.40		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
3	LPG BP PROJECT MOTIHARI - [N16000317	5/2018	206.50	206.50	174.10	03/2021 03/2022	02/2022
4	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409	9/2020	18,936.00	18,936.00	953.51	09/2024	08/2024
	Total		19,142.50	19,142.50	1,127.61		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
5	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285	1/2020	1,522.71	1,522.71	1,114.48	09/2021 08/2022	03/2022
	Total		1,522.71	1,522.71	1,114.48		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
6	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47	3,627.47	1,764.97	03/2024	03/2023
	<u>Rail Vikas Nigam Ltd.</u>						
7	BHANUPALI-BILASPUR BERI NL - [N22000273	4/2008	2,966.99	6,753.42	2,006.69	12/2026	03/2025
8	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78	723.78	0.19	12/2025	03/2025
	Total		7,318.24	11,104.67	3,771.85		

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
9	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH - [N24001180	3/2019	237.51	237.51	110.76	12/2022 -	07/2022
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289	3/2019	403.68	403.68	108.53	03/2027 -	02/2023
	<u>National Highways Authority Of India</u>						
11	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 - [N24001414	12/2020	733.00	733.00	-	01/2024 04/2024	01/2024
	Total		1,374.19 -	1,374.19	219.29		
	Grand Total		32,980.65	36,767.08	6,504.39		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 - [N02000029]	6/2017	49,621.00 -	49,621.00	5,453.00	09/2027 -	09/2027
	Total		49,621.00 -	49,621.00	5,453.00		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	507.91	09/2018 10/2022	10/2022
3	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]	6/2018	2,467.00 -	2,467.00	838.87	02/2022 12/2024	12/2024
4	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]	8/2018	951.28 -	951.28	548.93	10/2021 04/2023	04/2023
5	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	171.37	03/2020 03/2024	03/2024
6	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	233.91	11/2021 04/2023	04/2023
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]	3/2017	475.39 -	475.39	202.52	04/2021 08/2023	08/2023
8	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	7/2018	346.27 -	480.33	145.28	09/2021 12/2023	12/2023
9	CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]	5/2018	1,216.90 -	1,216.90	283.65	10/2022 03/2024	03/2024
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]	7/2018	456.86 -	456.86	340.28	09/2020 12/2022	12/2022
11	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH - [N04000092]	2/2019	645.63 -	645.63	296.53	08/2022 10/2023	10/2023
12	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	88.95	03/2023 03/2023	03/2023
13	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]	6/2019	380.87 -	380.87	20.42	03/2022 03/2024	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]	8/2017	177.10 -	177.10	115.40	02/2020 12/2022	12/2022
15	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]	1/2018	1,405.00 -	1,405.00	439.69	08/2022 08/2023	08/2023
16	UPGRADATION OF JABALPUR AIRPORT - [N04000087]	6/2016	412.24 -	412.24	243.86	06/2021 03/2023	03/2023
17	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	109.92	05/2022 12/2023	12/2023
18	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00 -	1,232.00	391.13	03/2021 03/2025	03/2025
	Total		12,306.89 -	12,821.45	4,978.62		
	COAL						
	Central Coal Fields Limited						
19	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	42.98	03/2023 -	03/2023
20	UCE OF EPR OF NORTH URIMARI OCP - [N06000218]	7/2021	778.80 -	778.80	-	03/2026 -	03/2026
21	REVISED PROJECT REPORT MAGADH EXPANSION OCP - [N06000216]	8/2020	7,254.37 -	7,254.37	-	03/2028 -	03/2028
22	EXPANSION PROJECT AMRAPALI OCP - [N06000217]	8/2020	5,136.15 -	5,136.15	-	03/2028 -	03/2028
	Eastern Coal Fields Limited						
23	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	260.95	03/2022 -	03/2022
24	EXPANSION PR OF JHANJRA UG (5.00 MTY) - [N06000223]	4/2020	1,210.12 -	1,210.12	-	03/2029 -	03/2029
25	SONEPUR BAZARI EXPANSION OC - [N06000220]	7/2021	5,365.88 5,366.00	5,365.88	-	03/2029 -	03/2029
26	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.75	03/2026 -	03/2026
27	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	165.05	03/2024 -	03/2024
28	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	9.64	03/2025 -	03/2025
29	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	1.49	03/2027 -	03/2027
30	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	4.48	03/2027 -	03/2027
31	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	26.86	03/2029 -	03/2029
	Mahanadi Coal Fields Limited						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
32	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,718.35	03/2026 -	03/2026
33	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	841.95	03/2027 -	03/2027
34	BALARAM EXPANSION OCP - [N06000230]	8/2020	3,504.21 -	3,504.21	-	03/2029 -	03/2029
35	GOPALJI-KANIHA OCP - [N06000229]	8/2020	8,416.19 -	8,416.19	-	03/2028 -	03/2028
36	BHUBANESWARI EXPANSION OCP - [N06000227]	8/2020	3,145.45 -	3,145.45	-	03/2031 -	03/2031
37	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,341.19	03/2029 -	03/2029
<u>Northern Coal Fields Limited</u>							
38	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	2.45	03/2023 -	03/2023
39	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
40	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
41	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
<u>Singareni Colliers Company Limited</u>							
42	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	290.90	03/2022 -	03/2022
43	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	95.10	03/2023 -	03/2023
44	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT - [N06000210]	11/2015	489.62 -	489.62	-	03/2023 -	03/2023
45	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	27.52	03/2023 -	03/2023
46	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	137.86	03/2024 -	03/2024
<u>South-Eastern Coal Fields Limited</u>							
47	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	10.32	03/2023 -	03/2023
48	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
49	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	2.59	03/2022 -	03/2022
50	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	3,393.76	03/2023 -	03/2023
51	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	4,768.67	03/2023 -	03/2023
52	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	12.61	03/2023 -	03/2023
53	RAMPUR BATURA OC (4.0 MTY) - [N06000233]	7/2019	1,248.93 -	1,248.93	-	03/2026 -	03/2026

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
54	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
55	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,881.55	03/2029 -	03/2029
56	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
57	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	190.30	03/2024 -	03/2024
58	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	362.52	03/2029 -	03/2029
59	JHIRIA WEST OPENCASST PROJECT - [N06000166]	11/2018	389.97 -	389.97	2.02	03/2026 -	03/2026
60	MAHAMAYA OPENCASST PROJECT - [N06000164]	5/2018	410.26 -	410.26	63.39	03/2026 -	03/2026
61	VIJAY WEST OPENCASST PROJECT - [N06000158]	5/2017	976.95 -	976.95	86.57	03/2026 -	03/2026
62	MADANNAGAR OPENCASST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
	Western Coal Fields Limited						
63	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	456.01	03/2025 -	03/2025
64	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
65	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	2.65	03/2026 -	03/2026
66	BELLORA-NAIGAON DEEP OC - [N06000180]	11/2018	252.71 -	252.71	107.27	03/2021 09/2022	09/2022
67	MUNGOLI NIRGUDA EXTENSION (DEEP) OC - [N06000231]	11/2020	826.80 -	826.80	-	03/2026 -	03/2026
68	RPR FOR JAMUNIA UG - [N06000228]	8/2020	281.25 -	281.25	-	03/2026 -	03/2026
69	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) - [N06000226]	9/2018	313.34 -	313.34	-	03/2024 -	03/2024
70	DHANKASA UG (RECAST) (1 MTY) - [N06000224]	2/2020	289.30 -	289.30	-	03/2025 -	03/2025
71	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) - [N06000222]	2/2020	1,184.33 -	1,184.33	-	03/2027 -	03/2027
72	BHANEGAON OC (1MTY) - [N06000221]	2/2017	409.68 -	409.68	-	03/2023 -	03/2023
73	ADASA UG TO OC (1.50 MTY) - [N06000219]	11/2018	333.43 -	333.43	-	03/2024 -	03/2024
74	DHUPTALA OC(SASTI UG TO OC) - [N06000209]	2/2019	720.87 -	720.87	108.38	03/2028 -	03/2028
75	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
76	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
77	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154	8/2016	319.76 -	404.45	252.90	03/2022 -	03/2022
	Total		99,703.16 -	99,805.60	17,842.59		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
78	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067	9/2012	171.86 -	171.86	144.27	03/2016 03/2022	03/2022
79	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008	9/2018	392.51 -	392.51	85.88	06/2022 10/2022	10/2022
80	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130	3/2019	424.93 -	424.93	86.21	07/2022 10/2022	10/2022
81	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131	1/2018	676.00 -	676.00	42.51	04/2023 04/2023	04/2023
	<u>Rites Of Higher Education</u>						
82	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001	9/2013	484.32 -	429.70	233.00	09/2014 06/2022	06/2022
	Total		2,149.62 -	2,095.00	591.87		
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
83	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	363.71	04/2020 03/2022	03/2022
	Total		426.72 -	426.72	363.71		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Cpwd For Health</u>						
84	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029	3/2019	1,404.00 -	1,404.00	439.65	09/2023 -	09/2023
	Total		1,404.00 -	1,404.00	439.65		
	<u>HOME AFFAIRS</u>						
	<u>Cpwd For Mha</u>						
85	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147	1/2020	166.98 167.00	166.98	7.84	10/2023 04/2024	04/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
86	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003	5/2019	199.31 -	199.31	75.31	01/2022 12/2022	12/2022
	Total		366.29 -	366.29	83.15		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
87	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	6,435.90	1,268.54	04/2021 01/2024	01/2024
88	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	667.23	395.98	01/2020 11/2023	11/2023
89	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	581.00	96.18	11/2020 12/2023	12/2023
90	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	163.17	135.00	06/2019 12/2022	12/2022
91	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	10.96	04/2021 12/2023	12/2023
	Total		7,078.62 -	8,330.30	1,906.66		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
92	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	425.30	03/2023 -	03/2023
93	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410	8/2020	697.00 -	697.00	338.87	03/2023 -	03/2023
	<u>Chennai Petroleum Corporation Limited</u>						
94	CBR 9 MMTPA PROJECT - [N16000434	1/2021	31,580.00 -	31,580.00	571.14	06/2025 -	06/2025
	<u>Gas Authority Of India Limited</u>						
95	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	345.15	265.22	04/2022 -	04/2022
96	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND - [N16000430	5/2019	8,797.00 -	8,797.00	210.01	04/2025 -	04/2025
97	60 KTA POLYPROPYLENE PROJECT - [N16000429	3/2019	910.56 -	910.56	141.31	04/2024 -	04/2024
98	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398	6/2020	7,844.25 -	7,844.25	2,002.80	05/2023 -	05/2023
99	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329	10/2017	226.45 -	226.45	152.67	10/2022 -	10/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
100	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	365.30	11/2022 -	11/2022
101	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	555.30	07/2022 -	07/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
102	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,539.20	06/2022 -	06/2022
103	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY - [N16000432]	9/2021	160.00 -	160.00	.13	06/2024 -	06/2024
104	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	88.45	03/2024 -	03/2024
105	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	30.88	11/2022 -	11/2022
106	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB [N16000402]	5/2020	1,421.46 -	1,421.46	281.96	02/2023 -	02/2023
107	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	466.13	11/2022 -	11/2022
108	SETTING UP OF PHASE II FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	348.51	11/2021 03/2022	03/2022
109	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	185.98	12/2022 -	12/2022
	<u>Indian Oil Corporation Limited</u>						
110	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	3,154.79	12/2020 03/2022	03/2022
111	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	188.36	08/2021 03/2023	03/2023
112	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	340.76	172.39	02/2020 07/2022	07/2022
113	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	2,441.32	09/2022 -	09/2022
114	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	226.83	- 05/2023	05/2023
115	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	836.13	05/2023 -	05/2023
116	LAB REVAMP AT GUJARAT REFINERY - [N16000377]	10/2019	403.00 -	403.00	208.61	04/2022 -	04/2022
117	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	473.01	12/2021 01/2023	01/2023
118	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	703.22	12/2022 07/2023	07/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	427.10	41.54	09/2022 03/2023	03/2023
120	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	139.82	06/2021 07/2022	07/2022
121	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	2,141.68	08/2021 09/2022	09/2022
122	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	543.00	176.32	09/2021 06/2022	06/2022
123	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	753.89	495.80	02/2020 07/2022	07/2022
124	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS [N16000420]	6/2019	2,880.00 -	2,880.00	117.00	08/2027 -	08/2027
125	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	49.47	03/2030 -	03/2030
126	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	210.74	03/2030 -	03/2030
127	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	68.94	02/2027 -	02/2027
128	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS [N16000416]	10/2018	613.00 -	613.00	171.20	12/2029 -	12/2029
129	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS [N16000415]	10/2018	176.00 -	176.00	90.56	08/2027 -	08/2027
130	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN - [N16000414]	5/2021	412.00 -	412.00	30.01	10/2023 -	10/2023
131	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	538.73	09/2024 -	09/2024
132	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM [N16000411]	10/2020	1,614.00 -	1,614.00	66.18	08/2023 -	08/2023
133	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE - [N16000435]	12/2021	9,028.00 -	9,028.00	-	10/2024 -	10/2024
134	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS [N16000427]	6/2019	303.00 -	303.00	140.07	02/2028 -	02/2028
135	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	43.28	12/2029 -	12/2029
136	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS [N16000425]	6/2019	2,996.00 -	2,996.00	329.06	02/2028 -	02/2028
137	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS [N16000424]	6/2019	347.00 -	347.00	114.50	02/2028 -	02/2028

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	28.39	12/2029 -	12/2029
139	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]	6/2019	439.00 -	439.00	133.31	02/2028 -	02/2028
140	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	49.65	12/2029 -	12/2029
141	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	187.71	12/2022 -	12/2022
142	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	126.54	08/2022 -	08/2022
143	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	763.89	01/2024 -	01/2024
144	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	88.43	07/2022 -	07/2022
145	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]	6/2020	1,019.00 -	1,019.00	177.06	01/2023 -	01/2023
146	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	2,561.63	04/2023 -	04/2023
147	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	423.89	03/2021 03/2022	03/2022
148	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	313.36	04/2021 09/2022	09/2022
149	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	3,652.22	10/2021 07/2022	07/2022
150	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	546.09	08/2022 -	08/2022
151	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	112.94	10/2020 08/2022	08/2022
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
152	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	304.00	2.61	06/2023 01/2024	01/2024
	<u>Numaligarh Refinery Limited</u>						
153	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]	1/2019	12,366.00 -	18,968.00	940.95	10/2024 -	10/2024
154	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	9,058.00	1,966.98	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
155	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	2,001.34	1,613.65	05/2013 05/2022	05/2022
156	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	5/2019	3,660.71 -	3,740.05	3,233.86	05/2021 05/2022	05/2022
157	PIPELINE REPLACEMENT PROJECT - VII - [N16000436	1/2022	3,183.58 -	3,183.58	-	05/2024 -	05/2024
158	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON [N16000433	8/2021	218.38 -	218.38	33.82	02/2023 -	02/2023
159	REDEVELOPMENT OF SOBHASAN COMPLEX - [N16000431	8/2021	885.63 -	885.63	206.93	02/2026 -	02/2026
160	REDEVELOPMENT OF LINCH FIELD - [N16000428	4/2021	631.03 -	631.03	228.08	03/2025 -	03/2025
161	REDEVELOPMENT OF NANDASAN FIELD - [N16000404	2/2020	444.87 -	444.87	171.45	08/2022 -	08/2022
162	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	5/2019	763.92 -	829.58	829.58	12/2020 05/2022	05/2022
163	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	4/2019	3,228.80 -	3,976.67	1,790.56	03/2022 05/2023	05/2023
164	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	823.27 -	1,137.79	784.66	03/2023 03/2022	03/2022
165	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	1,162.56	947.93	03/2026 -	03/2026
166	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247	3/2016	34,012.00 -	31,040.00	16,067.78	06/2020 05/2023	05/2023
167	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357	2/2019	2,292.46 -	2,292.46	2,255.02	05/2021 12/2022	12/2022
168	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213	12/2015	3,190.69 -	3,375.90	2,892.72	04/2018 05/2022	05/2022
<u>Oil India Limited</u>							
169	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN [N16000356	6/2016	224.75 -	198.00	189.00	08/2020 03/2022	03/2022
	Total		2,69,863.62 -	2,76,560.50	64,659.41		
<u>POWER</u>							
<u>Chenab Velley Power Projects [P] Limited</u>							
170	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172	10/2014	8,112.12 -	8,112.12	2,169.01	04/2020 07/2025	07/2025
<u>National Hydro-Electric Power Corporation</u>							
171	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	9/2002	3,919.59 -	9,897.59	9,558.69	09/2009 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
172	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221 <u>National Thermal Power Corporation</u>	9/2003	6,285.33 -	19,992.43	15,300.08	09/2010 08/2023	08/2023
173	BARH STPP(3X660MW) NTPC - [N180100242	2/2005	8,692.97 -	21,312.11	19,738.00	10/2011 07/2023	07/2023
174	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276	5/2016	1,885.13 -	2,426.00	2,027.32	12/2018 03/2022	03/2022
175	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277	12/2016	529.68 -	679.00	513.91	11/2018 06/2022	06/2022
176	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286	3/2020	1,782.00 -	1,782.00	910.29	09/2021 10/2022	10/2022
177	BHENSARA 320 MW - [N18000293	1/2021	1,221.73 -	1,221.73	140.11	07/2022 -	07/2022
178	GUJARAT 200 MW (GUVNL TENDER) - [N18000295	1/2021	842.27 -	842.27	93.92	07/2022 -	07/2022
179	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) [N18000296	5/2021	674.92 -	674.92	76.91	09/2022 -	09/2022
180	CHHATTARGARH 150 MW - [N18000294 <u>Power Grid Corporation Of India Limited</u>	2/2021	599.99 -	599.99	71.06	07/2022 -	07/2022
181	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC- INDIAN PORTION - [N18000299	5/2021	179.29 -	179.29	5.66	04/2023 -	04/2023
182	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000304	3/2021	1,340.81 -	1,340.81	151.70	12/2022 -	12/2022
183	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000306	6/2021	1,562.00 -	1,562.00	249.63	12/2022 -	12/2022
184	NORTH EASTERN REGION STRENGTHENING SCHEME- XII - [N18000316	5/2021	576.42 -	576.42	-	03/2023 -	03/2023
185	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000307	6/2021	1,006.00 -	1,006.00	253.02	12/2022 -	12/2022
186	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000305	6/2021	713.82 -	713.82	130.01	12/2022 -	12/2022
187	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000303	3/2021	353.85 -	353.85	22.91	12/2022 -	12/2022
188	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA - [N18000302	1/2019	267.33 -	267.33	31.72	03/2022 -	03/2022
189	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA - [N18000300	5/2021	1,184.88 -	1,184.88	12.83	09/2022 -	09/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
190	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	4,677.91	01/2024 -	01/2024
191	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	622.39	01/2026 -	01/2026
192	Bagodara Solar Power Project - [N18000297]	5/2021	296.20 -	296.20	.43	10/2022 -	10/2022
193	PARASAN SOLAR POWER PROJECT - [N18000298]	8/2021	313.58 -	313.58	298.99	12/2022 -	12/2022
194	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	215.23	11/2025 -	11/2025
	<u>Thdc India Limited</u>						
195	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,860.35	2,416.30	06/2013 06/2025	06/2025
	Total		57,769.11 -	92,132.31	59,688.03		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
196	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,445.48	1,418.98	03/2023 -	03/2023
197	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
198	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
199	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	667.42	03/2023 -	03/2023
	<u>East Coast Railway</u>						
200	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	835.30	03/2022 03/2026	03/2026
201	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	564.03	03/2022 03/2026	03/2026
	<u>North Eastern Railway</u>						
202	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,824.00	1,518.04	03/2022 -	03/2022
	<u>Northern Railway</u>						
203	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	37,012.26	27,846.00	11/2002 04/2023	04/2023
204	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	480.97	03/2023 12/2025	12/2025
	<u>National High Speed Rail Corporation Limited</u>						
205	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	21,986.54	12/2023 -	12/2023
	<u>Rail India Technical And Economic Service</u>						
206	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]	2/2016	393.98 -	393.98	371.86	03/2020 06/2022	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>Rail Vikas Nigam Ltd.</u>						
207	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	3,300.00	2,564.14	03/2023 -	03/2023
208	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	2,601.90	12/2023 -	12/2023
209	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	1,248.22	12/2024 -	12/2024
210	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	3,683.68	12/2023 -	12/2023
	<u>South East Central Railway</u>						
211	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,176.60	1,576.19	03/2023 12/2023	12/2023
212	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	2,135.34	833.36	03/2021 12/2023	12/2023
213	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.94	795.59	12/2021 12/2023	12/2023
	Total		1,49,892.75 -	1,92,527.57	68,992.22		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]	1/1991	675.00 -	780.77	424.27	- 06/2022	06/2022
215	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	368.28	05/2017 06/2022	06/2022
216	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000574]	11/2013	683.83 -	698.82	709.80	07/2016 06/2022	06/2022
217	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	1/1991	319.68 -	404.10	345.06	- 06/2022	06/2022
218	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000576]	2/2016	178.85 -	225.06	168.79	05/2016 06/2022	06/2022
219	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]	3/2018	153.24 -	153.24	97.01	- 03/2022	03/2022
220	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216) - [N24000967]	3/2016	444.84 -	444.84	365.54	09/2016 05/2022	05/2022
221	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21) - [N24000965]	1/2016	386.09 -	316.06	214.31	05/2016 06/2022	06/2022
222	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD) - [N24000964]	8/2016	350.61 -	350.61	328.03	01/2017 06/2022	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
223	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]	3/2016	995.09 995.00	995.09	609.49	05/2016 10/2022	10/2022
224	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]	1/2017	319.28 -	319.28	222.37	08/2017 05/2022	05/2022
225	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]	11/2016	290.15 -	290.15	164.56	05/2017 04/2022	04/2022
226	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]	9/2016	372.68 -	309.37	270.19	02/2017 02/2022	02/2022
227	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]	8/2016	1,742.01 -	1,742.01	1,605.30	12/2016 05/2022	05/2022
228	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD - [N24001421]	7/2018	1,948.25 -	1,948.25	313.56	02/2024 -	02/2024
229	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN - [N24001408]	2/2021	925.47 -	925.47	.06	07/2025 -	07/2025
230	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]	3/2019	423.15 -	423.15	159.07	12/2019 12/2022	12/2022
231	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	49.89	02/2024 -	02/2024
232	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	108.20	03/2024 -	03/2024
233	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	236.18	86.74	12/2022 -	12/2022
234	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	135.75	09/2021 12/2022	12/2022
235	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]	1/2014	1,408.85 -	2,138.16	1,241.55	10/2016 03/2022	03/2022
236	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P - [N24000578]	2/2016	553.30 -	587.41	537.14	05/2016 03/2022	03/2022
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
237	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]	2/2017	176.12 -	176.12	87.87	- 04/2022	04/2022
238	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	30.42	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
239	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246	3/2020	220.20 -	220.20	45.79	12/2022 -	12/2022
240	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	71.71	03/2022 -	03/2022
241	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253	12/2019	2,680.42 -	2,680.42	878.00	12/2023 -	12/2023
242	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	42.83	06/2022 -	06/2022
243	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	91.93	08/2022 -	08/2022
244	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	59.71	06/2022 -	06/2022
245	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	50.81	03/2022 -	03/2022
246	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	167.94	07/2022 -	07/2022
247	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267	3/2020	178.43 -	178.43	22.21	07/2022 -	07/2022
248	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	25.14	04/2022 -	04/2022
249	REHABILITATION AND UPGRADE OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265	3/2020	154.51 -	154.51	47.29	07/2022 -	07/2022
250	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264	7/2020	228.39 -	228.39	29.96	04/2022 -	04/2022
251	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	101.27	06/2022 -	06/2022
252	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284	3/2020	361.53 -	361.53	41.90	06/2022 -	06/2022
253	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283	3/2020	281.78 -	281.78	120.63	07/2022 -	07/2022
254	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282	3/2020	355.79 -	355.79	79.81	06/2022 -	06/2022
255	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281	3/2020	292.24 -	292.24	72.45	07/2022 -	07/2022
256	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280	3/2020	320.97 -	320.97	64.91	06/2022 -	06/2022
257	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279	3/2020	216.49 -	216.49	70.76	07/2022 -	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
258	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	39.88	07/2022 -	07/2022
259	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	32.96	10/2022 -	10/2022
260	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
261	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
262	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]	8/2020	379.39 -	379.39	12.26	04/2022 -	04/2022
263	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]	7/2020	177.76 -	177.76	36.05	08/2022 -	08/2022
264	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	624.88	09/2028 -	09/2028
265	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]	9/2020	262.84 -	262.84	120.72	05/2023 -	05/2023
266	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	36.42	09/2022 -	09/2022
267	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	78.46	09/2022 -	09/2022
268	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]	9/2020	183.31 -	183.31	76.84	05/2022 -	05/2022
269	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
270	DOGINALA - GAU - [N24001320]	12/2020	242.30 -	242.30	9.31	09/2022 -	09/2022
271	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	13.63	04/2022 -	04/2022
272	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
273	PEREN-DIMAPUR PKG-5 - [N24001407]	2/2021	207.33 -	207.33	-	03/2023 -	03/2023
274	PEREN-DIMAPUR SECTION PKG-2 - [N24001406]	7/2021	258.52 -	258.52	31.67	03/2023 -	03/2023
275	CHURACHANPUR TUIVAI PKG-3 - [N24001405]	7/2021	673.27 -	673.27	11.12	10/2023 -	10/2023
276	TAMENGLONG - MAHUR PKG-4 - [N24001404]	7/2021	198.77 -	198.77	6.59	03/2023 -	03/2023
277	TAMENGLONG - MAHUR PKG-2 - [N24001403]	7/2021	483.87 -	483.87	22.78	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
278	TAMENGLONG - MAHUR PKG-1 - [N24001402	7/2021	185.80 -	185.80	6.20	03/2023 -	03/2023
279	IMPHAL - KHONGSANG PKG-3 - [N24001401	7/2021	467.00 -	467.00	-	03/2023 -	03/2023
280	SENAPATI- IMPHAL PKG-5B - [N24001400	3/2021	211.70 -	211.70	-	01/2023 -	01/2023
281	IMPHAL – MOREH (PACKAGE 4) - [N24001399	3/2021	277.99 -	277.99	5.57	01/2023 -	01/2023
282	MARIAM - PEREN (PKG 2A) - [N24001398	7/2021	204.58 -	204.58	10.48	03/2023 -	03/2023
283	GOHA-KHELLANI PKG-3 - [N24001397	2/2021	431.28 -	431.28	40.41	03/2023 -	03/2023
284	KHELLANI-KHANABAL PKG-5 - [N24001396	7/2021	497.09 -	497.09	10.16	02/2023 -	02/2023
285	KHELLANI-KHANABAL PKG-4 - [N24001395	7/2021	859.67 -	859.67	9.03	08/2023 -	08/2023
286	KHELLANI-KHANABAL PKG-2 - [N24001394	7/2021	512.43 -	512.43	16.50	02/2023 -	02/2023
287	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) [N24001393	8/2020	184.88 -	184.88	48.06	04/2022 -	04/2022
288	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) [N24001392	8/2020	199.03 -	199.03	59.12	04/2022 -	04/2022
289	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) - [N24001391	8/2020	294.04 -	294.04	91.30	04/2022 -	04/2022
290	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) [N24001390	8/2020	228.71 -	228.71	48.24	04/2022 -	04/2022
291	CHANGTONGYA TO LONGLENG ROAD PKG-2 - [N24001389	3/2020	206.53 -	206.53	88.93	06/2022 -	06/2022
292	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
293	DABOKA KATHKATI PACKAGE-5 - [N24001366	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
294	DABOKA KATHKATI PACKAGE-4 - [N24001365	2/2021	260.07 -	260.07	78.09	12/2023 -	12/2023
295	DABOKA KATHKATI PACKAGE-2 - [N24001364	3/2021	335.88 -	335.88	33.72	01/2024 -	01/2024
296	MANU-SIMLUNG (PKG 4) - [N24001363	3/2021	354.79 -	354.79	14.79	12/2022 -	12/2022
297	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
298	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
299	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360	3/2021	260.21 -	260.21	66.51	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
300	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
301	TLABUNG - LUNGLEI PKG-A - [N24001358]	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
302	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	60.00	06/2023 -	06/2023
303	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	16.96	12/2022 -	12/2022
304	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	43.39	12/2022 -	12/2022
305	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	15.09	12/2022 -	12/2022
306	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
307	IMPHAL - MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	46.59	12/2022 -	12/2022
308	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	6.41	12/2022 -	12/2022
309	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	16.08	12/2022 -	12/2022
310	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	6.70	12/2022 -	12/2022
311	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	9.04	01/2023 -	01/2023
312	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	38.81	06/2024 -	06/2024
313	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	36.62	05/2024 -	05/2024
314	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	8.23	01/2023 -	01/2023
315	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	1.98	01/2023 -	01/2023
316	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	10.11	01/2023 -	01/2023
317	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
318	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	11.84	12/2022 -	12/2022
319	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) [N24001339]	10/2020	157.86 -	157.86	68.77	04/2022 -	04/2022
320	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
321	CONSTRUCTION AND UPGRADEATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
322	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336	8/2020	230.45 -	230.45	2.58	04/2023 -	04/2023
323	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335	11/2020	284.21 -	284.21	44.52	12/2023 -	12/2023
324	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334	11/2020	445.51 -	445.51	174.37	12/2023 -	12/2023
325	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333	9/2019	761.54 -	761.54	155.57	05/2023 -	05/2023
326	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
327	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331	3/2020	261.13 -	261.13	31.46	06/2022 -	06/2022
328	KARGIL-ZANSKR PACKAGE-5 - [N24001330	8/2020	169.79 -	169.79	48.49	12/2023 -	12/2023
329	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329	3/2020	165.54 -	165.54	14.10	07/2022 -	07/2022
330	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328	12/2020	804.00 -	804.00	93.33	08/2023 -	08/2023
331	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327	8/2020	292.80 -	292.80	42.83	05/2022 -	05/2022
332	TADADEGE - HENKAR - [N24001315	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
333	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314	11/2020	525.68 -	525.68	301.78	12/2023 -	12/2023
334	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313	11/2020	351.12 -	351.12	171.47	12/2023 -	12/2023
335	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312	3/2020	167.95 -	167.95	50.50	06/2022 -	06/2022
336	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311	11/2020	206.78 -	206.78	87.79	07/2022 -	07/2022
337	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310	11/2020	280.91 -	280.91	99.97	07/2022 -	07/2022
338	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309	11/2020	159.13 -	159.13	12.02	06/2022 -	06/2022
339	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308	11/2020	332.14 -	332.14	10.93	07/2022 -	07/2022
340	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262	7/2020	345.38 -	345.38	96.67	04/2023 -	04/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
341	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	32.50	04/2023 -	04/2023
342	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	55.18	04/2022 -	04/2022
343	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	9.39	04/2022 -	04/2022
344	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258]	8/2020	202.36 -	202.36	7.02	04/2022 -	04/2022
345	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]	9/2020	277.44 -	277.44	33.95	10/2022 -	10/2022
346	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	439.59	09/2026 -	09/2026
347	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]	3/2020	242.97 -	242.97	59.98	06/2022 -	06/2022
348	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	48.15	04/2023 -	04/2023
349	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	27.45	04/2022 -	04/2022
350	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	31.06	05/2022 -	05/2022
National Highways Authority Of India							
351	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 03/2022	03/2022
352	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	244.16	03/2019 06/2022	06/2022
353	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	639.58	501.61	04/2019 07/2022	07/2022
354	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]	3/2016	720.00 -	793.63	291.10	- 09/2022	09/2022
355	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]	3/2016	1,443.00 -	2,330.79	1,246.85	- 02/2022	02/2022
356	ISMAILABAD-NARNAUL PKG-1 - [N24001193]	1/2019	996.65 -	1,173.65	1,070.65	- 05/2022	05/2022
357	ISMAILABAD-NARNAUL PKG-4 - [N24001192]	1/2019	1,018.79 -	1,072.08	956.46	- 05/2022	05/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
358	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854	3/2018	1,005.08 -	1,005.08	-	- 02/2023	02/2023
359	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849	3/2018	289.21 -	289.21	237.47	- 02/2022	02/2022
360	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847	3/2018	291.53 -	291.53	252.05	- 02/2022	02/2022
361	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	466.03	03/2020 03/2023	03/2023
362	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651	2/2017	904.16 -	904.16	-	02/2020 03/2022	03/2022
363	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564	3/2016	1,408.00 -	1,330.02	920.72	- 07/2022	07/2022
364	NAGPUR RING ROAD PACKAGE-2 - [N24000560	3/2016	591.66 -	591.66	319.05	07/2019 08/2023	08/2023
365	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	1,376.86	887.23	04/2019 06/2022	06/2022
366	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR - [N24001420	2/2021	853.66 -	853.66	-	04/2024 -	04/2024
367	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- [N24001419	2/2021	1,269.96 -	1,269.96	-	04/2024 -	04/2024
368	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO - [N24001418	12/2020	1,094.46 -	1,094.46	-	04/2024 -	04/2024
369	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO - [N24001417	12/2020	1,234.40 -	1,234.40	-	04/2024 -	04/2024
370	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO - [N24001415	12/2020	881.00 -	881.00	-	04/2024 -	04/2024
371	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
372	ISMAILABAD-NARNAUL PKG-3 - [N24001191	1/2019	889.36 -	986.10	837.89	- 05/2022	05/2022
373	ISMAILABAD-NARNAUL PKG-2 - [N24001190	1/2019	1,243.45 -	1,407.35	1,162.45	- 04/2022	04/2022
374	ISMAILABAD-NARNAUL PKG-8 - [N24001189	1/2019	1,033.19 -	1,044.32	899.01	- 03/2022	03/2022
375	ISMAILABAD-NARNAUL PKG-7 - [N24001188	1/2019	1,137.42 -	1,238.29	1,111.87	- 06/2022	06/2022
376	ISMAILABAD-NARNAUL PKG-6 - [N24001187	1/2019	1,120.06 -	1,206.48	1,006.03	- 07/2022	07/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
377	ISMAILABAD-NARNAUL PKG-5 - [N24001186	1/2019	1,051.91 -	1,118.07	957.15	- 05/2022	05/2022
378	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483	9/2014	479.00 -	479.00	456.80	- 03/2023	03/2023
379	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 03/2023	03/2023
380	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER [N24000138	9/2010	946.00 -	946.00	818.53	06/2018 07/2022	07/2022
381	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212	11/2011	478.51 -	1,082.40	1,023.73	10/2013 03/2022	03/2022
382	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	1,890.04	04/2015 03/2022	03/2022
	Total		96,781.74 -	1,00,145.28	37,093.50		
	SHIPPING AND PORTS						
	<u>Inland Waterways Authority Of India</u>						
383	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	2,013.22	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	2,013.22		
	SOCIAL JUSTICE						
	<u>Central Public Works Department</u>						
384	CENTRE FOR DISABILITY SPORTS - [N38000001	2/2019	170.99 -	170.99	-	03/2024 -	03/2024
	Total		170.99 -	170.99	.00		
	STEEL						
	<u>Steel Authority Of India Limited (Sail)</u>						
385	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	57.81	05/2023 -	05/2023
386	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP - [N12000125	1/2022	970.18 -	970.18	-	05/2025 -	05/2025
387	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	89.30	12/2023 -	12/2023
	Total		1,889.60 -	1,889.60	147.11		
	URBAN DEVELOPMENT						
	<u>Ahmedabad Metro Rail</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
388	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137 <u>Bangalore Metro Rail Corporation Limited</u>	3/2019	5,384.17 -	5,384.17	431.21	03/2024 -	03/2024
389	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B - [N28000151 <u>Central Public Works Department</u>	6/2021	14,788.10 -	14,788.10	2,290.84	06/2026 -	06/2026
390	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	139.55	03/2021 06/2022	06/2022
391	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129	10/2016	1,128.00 -	1,128.00	30.00	03/2022 06/2024	06/2024
392	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128	10/2016	1,180.00 -	1,100.80	35.90	07/2021 06/2024	06/2024
393	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114 <u>Delhi Metro Rail Corporation</u>	10/2016	392.00 -	392.00	204.84	08/2020 04/2022	04/2022
394	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS [N28000135 <u>Madhya Pradesh Metro Rail Co Limited</u>	7/2019	24,948.65 -	24,948.65	2,949.03	03/2025 -	03/2025
395	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	409.75	02/2023 05/2025	05/2025
396	INDORE METRO RAIL - [N28000125 <u>National Capital Region Transport Corp</u>	11/2018	7,500.80 -	7,500.80	264.77	02/2023 07/2025	07/2025
397	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134 <u>Patna Metro Rail Corporation</u>	3/2019	30,274.00 -	30,274.00	6,762.86	06/2025 -	06/2025
398	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,925.50	307.63	06/2024 -	06/2024
	Total		1,06,324.89 -	1,06,805.42	13,826.38		
	<u>WATER RESOURCES</u>						
	<u>Delhi Jal Board</u>						
399	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014	3/2017	665.78 -	942.18	261.19	12/2022 -	12/2022
	Total		665.78 -	942.18	261.19		
	Grand Total		8,61,783.96	9,50,678.02	2,78,340.31		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 - 3,492.00	6,840.00	09/2010 -	10/2022	95.88
	Total		3,492.00 .00 3,492.00	6,840.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 - 417.23	707.73	09/2018 -	10/2022	69.63
3	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00 - 1,383.00	1,938.00	09/2021 -	12/2023	40.13
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	12/2023	38.72
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2025	7.88
	Total		3,288.50 .00 3,288.50	4,358.06			
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 - 243.00	334.27	04/2018 -	06/2023	37.56
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 - 304.13	341.22	03/2017 -	12/2022	12.20
	<u>Eastern Coal Fields Limited</u>						
8	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>						
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	808.97	03/2013 -	03/2024	68.70

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Neyveli Lignite Corporation</u>						
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 - 5,907.11	7,980.79	12/2015 -	02/2021	35.10
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	06/2023	.00
	Total		26,832.50 .00 26,832.50	31,849.53			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Cpwd Of Higher Education</u>						
12	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	-	.60
13	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 559.49	580.00	07/2019 -	07/2021	5.59
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	210.60	09/2020 -	-	5.83
	Total		1,231.49 695.00 1,254.49	1,289.59			
	<u>DPIIT</u>						
	<u>Dmic For Dpiit</u>						
15	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	-	9.80
	<u>licc For Dpiit</u>						
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	05/2022	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
17	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 - 414.11	586.50	11/2013 -	09/2021	41.63

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
18	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 - 204.44	250.00	05/2017 -	06/2021	22.29
19	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
20	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 - 168.90	191.20	05/2017 -	01/2021	13.20
21	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 - 505.58	586.96	03/2018 -	04/2020	16.10
22	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 - 152.95	177.92	02/2018 -	04/2021	16.33
23	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 - 244.00	248.00	09/2018 -	12/2021	1.64
24	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 - 272.19	280.00	03/2019 -	02/2021	2.87
25	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 - 156.56	205.00	- -	01/2022	30.94
26	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]	03/2018	268.84 - 268.84	284.67	- -	05/2021	5.89
27	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 - 249.01	249.07	- -	05/2021	.02
	<u>Nbcc For Health</u>						
28	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	06/2022	8.88
	Total		4,281.23 .00 4,281.23	4,855.32			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
29	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 - 1,718.00	3,727.30	09/2011 -	-	116.96
	Total		1,718.00 .00 1,718.00	3,727.30			
	<u>HOME AFFAIRS</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Cpwd For Mha</u>						
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	06/2022	64.04
31	NSG AT KOLKATA - [N28000104	10/2014	162.88 - 162.88	228.63	04/2018 -	12/2022	40.37
32	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002	06/2019	277.35 - 277.35	290.33	07/2022 -	12/2022	4.68
	Total		1,659.44 .00 1,659.44	2,518.96			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
33	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 - 678.00	1,472.00	02/2017 -	08/2022	117.11
34	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 - 1,112.00	1,507.24	06/2019 -	02/2023	35.54
	<u>Gas Authority Of India Limited</u>						
35	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	04/2017	287.49 - 287.49	345.15	04/2022 -	04/2022	20.06
36	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 - 225.54	247.90	02/2021 -	10/2022	9.91
37	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 - 327.00	327.01	08/2020 -	04/2022	14.17
	<u>Hindustan Petroleum Corporation Limited</u>						
38	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00 - 20,928.00	26,264.00	07/2020 -	07/2022	25.50
39	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>						
40	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02 - 163.02	207.36	04/2020 -	10/2022	27.20
41	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT - [N16000336	03/2018	588.20 - 588.20	730.20	- -	05/2023	24.14
	<u>Numaligarh Refinery Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
42	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY [N16000379]	01/2019	12,366.00 - 12,366.00	18,968.00	10/2024 -	10/2024	53.39
	<u>Oil & Natural Gas Corporation Limited</u>						
43	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	05/2019	763.92 - 763.92	829.58	12/2020 -	05/2022	8.60
	<u>Oil India Limited</u>						
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 - 543.91	638.60	02/2020 -	06/2022	17.41
	Total		40,619.50 - 40,660.08	54,609.04			
	POWER						
	<u>National Hydro-Electric Power Corporation</u>						
45	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62 - 578.62	1,311.05	06/2006 -	-	126.58
	<u>National Thermal Power Corporation</u>						
46	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 - 1,381.84	1,803.00	09/2019 -	07/2025	30.48
47	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 - 5,353.00	10,566.00	07/2012 -	-	97.38
48	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 - 10,598.98	10,998.00	11/2020 -	02/2023	3.76
49	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00 4,238.00	5,289.25	10/2017 -	-	24.81
50	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 - 2,311.80	2,426.00	12/2018 -	03/2022	28.69
51	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 - 633.80	679.00	11/2018 -	06/2022	28.19
52	DEVIKOT SOLAR 90MW - [N18000280]	03/2020	501.29 - 501.29	524.83	09/2021 -	03/2022	4.70
53	DEVIKOT SOLAR 150MW - [N18000281]	01/2020	798.24 - 798.24	852.90	09/2021 -	05/2022	6.85
54	NOKHRA - [N18000282]	03/2020	1,722.14 - 1,722.14	1,803.19	09/2021 -	10/2022	4.71

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	KAWAS SOLAR 56 MW - [N18000283]	08/2020	261.80 - 261.80	293.03	10/2021 -	10/2022	11.93
56	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	06/2019	401.90 - 401.90	442.03	04/2021 -	05/2022	9.99
	<u>Power Grid Corporation Of India Limited</u>						
57	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 - 11,130.19	13,199.00	08/2013 -	03/2018	18.59
58	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 - 522.29	546.36	11/2016 -	03/2022	4.61
59	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 - 4,754.42	9,129.32	12/2018 -	03/2024	92.02
60	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 - 5,111.33	6,700.00	12/2018 -	01/2024	31.08
61	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	04/2022	14.11
62	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 - 186.17	219.66	07/2019 -	08/2022	17.99
63	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 - 1,931.39	2,635.55	02/2020 -	04/2023	36.46
	<u>Satluj Jal Vidyut Nigam Limited</u>						
64	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	947.89	12/2021 -	06/2022	46.20
	<u>Thdc India Limited</u>						
65	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 - 1,657.00	4,825.60	02/2016 -	06/2023	191.23
	Total		57,691.70 7,738.00 58,222.53	79,185.66			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
66	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 - 3,168.29	3,445.48	03/2023 -	03/2023	8.75
67	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	1,387.52	03/2021 -	03/2023	75.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
68	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [N220100181]	02/1997	2,271.50 - 2,271.50	4,794.60	03/2021 -	03/2023	111.08
69	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
70	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.49	03/2024 -	-	25.04
71	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
72	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
73	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
74	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
75	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00 28,181.00	51,219.00	- - -	-	68.72
	<u>East Central Railways</u>						
76	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [N220100222]	03/1999	1,033.07 - 3,020.95	3,650.00	- -	07/2022	253.32
77	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [N220100240]	04/1997	324.73 - 967.29	1,090.00	03/2012 -	06/2023	235.66
78	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	-	37.04
79	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	-	818.15
80	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,893.55	- -	-	400.20
81	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	04/2009	548.00 - 548.00	819.01	03/2020 -	12/2024	49.45
	<u>East Coast Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
82	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 - 810.78	1,928.07	06/2021 -	03/2025	137.80
83	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 - 2,923.13	3,791.66	03/2009 -	12/2024	29.71
84	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	03/2022	38.43
85	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 - 1,160.00	1,160.83	03/2020 -	03/2024	.07
86	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380 Eastern Railways	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2025	15.45
87	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
88	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
89	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
90	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
91	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
92	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
93	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 - 288.35	502.48	- -	02/2022	74.26
94	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2024	7.75
	<u>Indian Railway Construction Company Limited</u>						
95	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	09/2023	117.23
96	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	06/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
97	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [N220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	06/2022	501.57
98	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	774.51	06/2013 -	12/2022	56.23
99	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	-	75.91
	<u>North Central Railway</u>						
100	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
	<u>North East Frontier Railway</u>						
101	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 2,393.47	6,527.00	03/2014 -	12/2023	172.70
102	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N220100288]	04/2003	4,454.17 - 4,454.17	14,322.00	03/2011 -	12/2023	221.54
103	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,145.79	03/2019 -	03/2024	197.45
104	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 - 532.87	2,145.00	03/2019 -	03/2024	302.54
105	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 - 2,326.52	6,663.00	03/2015 -	03/2026	186.39
106	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 1,339.48	8,600.00	12/2015 -	12/2023	542.04
107	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 - 1,798.00	2,047.51	03/2019 -	12/2023	13.88
108	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	708.73	03/2020 -	09/2022	24.42
109	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 906.46	4,083.02	03/2021 -	-	350.44
110	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
111	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	401.65	- -	03/2023	66.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
112	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	750.00	03/2020 -	-	80.79
113	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
114	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	03/2022	115.07
	<u>North Eastern Railway</u>						
115	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
116	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	728.92	01/2019 -	-	147.09
117	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
118	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 - 1,295.42	1,824.00	03/2022 -	03/2022	40.80
119	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	-	.16
120	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 - 150.00	341.66	04/2017 -	10/2022	127.77
121	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,345.00	01/2018 -	-	.15
122	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	800.00	- -	12/2023	32.78
	<u>North Western Railway</u>						
123	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	06/2022	109.82
124	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
	<u>Northern Railway</u>						
125	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
126	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	-	211.31

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
127	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	09/2023	134.90
128	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
129	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,017.96	07/2012 -	11/2024	348.44
130	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 - 27,949.00	37,012.26	11/2002 -	04/2023	1,380.49
131	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.13	03/2023 -	12/2025	369.35
132	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	839.00	03/2016 -	-	34.24
	<u>Rail Vikas Nigam Ltd.</u>						
133	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
134	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	433.00	03/2009 03/2009	12/2022	109.18
135	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 - 2,913.51	4,834.54	03/2016 -	07/2025	65.94
136	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 - 2,966.99	6,753.42	12/2026 -	03/2025	127.62
137	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 - 2,127.00	3,300.00	03/2023 -	03/2023	55.15
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 - 3,951.98	4,259.48	03/2016 -	03/2026	7.78
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 - 2,298.42	2,733.86	03/2014 -	12/2025	18.95
140	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 - 1,503.71	3,633.12	03/2020 -	06/2022	141.61
141	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 - 644.38	923.28	03/2021 -	05/2022	43.28
142	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 - 1,548.66	2,538.01	12/2021 -	12/2022	63.88

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
143	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 - 632.68	950.00	03/2016 -	04/2022	50.15
144	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 - 3,246.26	3,548.68	12/2023 -	12/2023	9.32
145	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 - 943.60	1,500.00	03/2022 -	12/2022	58.97
146	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 - 773.94	850.00	12/2024 -	12/2024	9.83
147	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 - 927.01	1,457.79	03/2019 -	03/2023	57.26
148	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 - 16,216.00	24,659.00	12/2024 -	03/2025	52.07
149	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 - 713.48	2,725.00	03/2020 -	03/2022	281.93
150	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
151	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	04/2022	111.91
152	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,552.26	03/2019 -	03/2023	64.62
153	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	2,203.53	12/2020 -	06/2022	86.23
154	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	09/2022	23.55
155	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	12/2022	102.11
	<u>South Central Railway</u>						
156	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2027	102.85
157	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	1,160.48 - 1,160.48	1,373.74	03/2010 -	03/2025	18.38
158	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
159	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
160	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	03/2022	31.75
161	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
162	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
163	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2025	7.06
164	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00 185.00	242.28	03/2022 -	-	30.96
<u>South East Central Railway</u>							
165	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 - 1,908.51	3,176.60	03/2023 -	12/2023	66.44
166	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 - 585.93	1,268.32	02/2019 -	03/2022	116.46
167	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 - 229.00	1,096.00	12/2021 -	12/2024	378.60
168	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
<u>South Eastern Railway</u>							
169	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 - 969.83	1,312.97	03/2020 -	06/2022	35.38
170	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]	04/2018	428.65 - 428.65	472.50	06/2022 -	12/2025	10.23
171	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]	04/2018	390.39 - 390.39	511.75	12/2021 -	01/2023	31.09
172	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]	04/2018	338.00 - 338.00	393.83	06/2022 -	12/2023	16.52
<u>South Western Railway</u>							
173	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 - 1,801.01	2,000.97	- -	03/2025	11.10

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
174	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 - 986.30	1,530.09	03/2016 -	12/2026	55.13
175	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 - 558.00	692.43	- -	03/2028	24.09
176	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	466.65	- -	03/2028	57.65
177	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,404.03	- -	12/2025	16.57
178	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 - 327.25	367.77	- -	03/2027	12.38
179	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 2,315.00	5,174.30	- -	03/2028	123.51
180	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 - 1,382.78	1,383.00	03/2002 -	03/2028	.02
181	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,954.21	03/2020 -	12/2022	68.91
182	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,104.00	03/2020 -	02/2022	28.31
183	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	758.36	03/2020 -	02/2022	31.20
184	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,614.59	1,878.00	03/2019 -	02/2024	16.31
185	KADUR CHIKMAGALUR SAKLLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 - 644.78	817.23	03/2017 -	03/2026	26.75
<u>Southern Railway</u>							
186	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	3,081.20	02/2019 -	03/2025	325.17
187	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,444.00	- -	12/2025	490.91
188	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,549.09	03/2020 -	03/2025	409.60
189	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
190	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	839.01	- -	03/2030	.00
191	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	749.40	- -	03/2022	177.41
192	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	709.69	- -	03/2025	180.55
193	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	591.00	- -	03/2022	259.47
194	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	448.10	- -	03/2025	136.79
195	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,111.88	03/2019 -	12/2027	1,649.69
196	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,339.00	- -	03/2025	33.90
<u>West Central Railway</u>							
197	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2024	585.35
198	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
199	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 - 2,478.23	2,875.12	03/2022 -	06/2023	16.02
200	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 - 582.13	1,247.64	03/2022 -	12/2023	114.32
<u>Western Railway</u>							
201	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 5,839.02	6,383.82	03/2022 -	03/2026	82.20
202	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 - 318.24	321.62	03/2012 -	10/2023	1.06
203	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 829.74	2,223.37	03/2020 -	03/2024	167.96
204	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 - 1,347.26	1,524.68	03/2022 -	10/2027	13.17

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
205	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 - 320.66	1,378.11	03/2019 -	03/2025	329.77
206	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 - 1,037.15	1,383.69	03/2021 -	12/2022	33.41
207	SURENDRA NAGAR RAJKOT - [N22000392	04/2015	1,002.39 - 1,016.39	1,056.11	03/2021 -	12/2022	5.36
208	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM [N22000434	03/2010	265.88 - 265.88	311.36	- -	-	17.11
209	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435	03/2012	217.38 - 217.38	393.62	- -	-	81.07
210	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436	03/2012	248.26 - 248.26	528.49	- -	-	112.88
211	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504	04/2017	692.25 - 692.25	742.88	03/2020 -	03/2024	7.31
	Total		1,92,253.60 34,377.00 2,37,690.76	4,13,082.96			
	<u>RENEWABLE ENERGY</u>						
	<u>Cpwd For Renewable Energy</u>						
212	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 - 271.90	365.00	11/2019 -	-	34.24
	Total		271.90 .00 271.90	365.00			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
213	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41 - 282.41	319.96	03/2016 -	04/2022	13.30
214	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 - 280.16	290.59	- -	01/2020	3.72
215	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 - 268.08	390.73	05/2017 -	06/2022	45.75
216	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 - 889.24	904.82	- -	-	1.75

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
217	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 - 460.73	461.00	- -	-	.06
218	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 - 237.80	238.00	11/2019 -	-	.08
219	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 - 166.21	174.90	08/2018 -	03/2022	5.23
220	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27 - 160.27	213.97	08/2019 -	03/2023	33.51
221	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78 - 236.78	263.26	08/2019 -	03/2023	11.18
222	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22 398.22	398.52	08/2017 -	-	.08
223	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 - 217.22	226.88	08/2018 -	03/2022	4.45
224	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 - 877.79	949.54	06/2019 -	03/2022	8.17
225	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 - 333.21	353.43	12/2015 -	-	6.07
226	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00 504.00	504.19	11/2018 -	-	.04
227	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00 995.00	995.09	05/2016 -	10/2022	.01
228	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00 203.00	203.21	05/2019 -	09/2019	.10
229	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00 373.00	373.10	05/2019 -	11/2020	.03
230	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00 322.00	322.48	05/2019 -	03/2020	.15
231	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00 548.00	548.03	06/2019 -	01/2020	.01
232	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00 391.00	391.06	06/2019 -	03/2022	.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
233	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	12/2020	.05
234	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	03/2022	40.76
235	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	03/2022	.15
236	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	03/2022	.00
237	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	09/2022	.05
238	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	03/2022	.08
239	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	06/2022	.24
240	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	03/2022	.06
241	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	01/2021	.12
242	DHANGIIMPRI TO JALNA AND AMBAD CHOWK MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	06/2021	.06
243	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	03/2022	.08
244	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	12/2020	.14
245	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	09/2021	.01
246	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	09/2022	.13
247	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	06/2022	.07
248	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	12/2020	.11

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
249	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	06/2022	.01
250	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	12/2020	.03
251	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	02/2022	.06
252	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	11/2020	.47
253	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	10/2020	.08
254	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00 356.00	536.65	12/2019 -	03/2022	50.74
255	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	12/2021	.02
256	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	03/2022	.16
257	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	12/2022	.08
258	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	12/2022	26.19
259	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	06/2022	2.47
260	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	11/2020	.31
261	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	09/2022	.03
262	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	12/2022	.00
263	REHABILITATION AND UPGRADATION OF KALUPUR- LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2- LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	-	.13
264	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 - 392.33	428.55	03/2018 -	03/2022	9.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
265	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156	01/2017	166.67 - 166.67	264.34	09/2017 -	-	58.60
266	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 - 297.30	318.28	01/2019 -	-	7.06
267	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 - 325.86	386.41	10/2018 -	-	18.58
268	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 - 336.25	369.96	09/2019 -	11/2020	10.03
269	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 - 186.96	322.24	09/2014 -	-	72.36
270	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 - 1,979.00	2,036.90	- - -	12/2021	2.93
271	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208	03/2018	288.30 - 288.30	323.36	08/2020 -	03/2022	12.16
272	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 - 281.45	319.96	- - -	03/2022	13.68
273	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 - 497.14	572.66	08/2016 -	12/2022	15.19
274	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 - 624.98	731.50	10/2016 -	06/2022	17.04
275	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 - 197.67	236.18	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
276	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 - 195.23	252.79	04/2017 -	03/2022	29.48
277	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 - 203.36	263.31	04/2017 -	03/2022	29.48
278	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 - 373.07	387.00	08/2016 -	-	3.73
279	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 - 198.22	252.05	04/2017 -	03/2022	27.16

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
280	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
281	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
282	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
283	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
284	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
285	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
286	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
287	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
288	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 511.54	591.00	11/2013 -	-	15.53
289	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 - 291.36	469.31	01/2014 -	-	61.08
290	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 - 351.34	417.68	01/2016 -	-	18.88
291	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 - 495.78	627.93	01/2016 -	-	26.66
292	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	744.73	05/2018 -	03/2022	40.22
293	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]	10/2015	593.26 - 593.26	717.24	05/2018 -	06/2022	20.90
294	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- - -	01/2020	11.33
295	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	09/2015	934.46 - 934.46	1,457.82	03/2018 -	-	56.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
296	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 - 567.00	639.58	04/2019 -	07/2022	-38.57
297	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	-	1.37
298	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
299	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
300	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 - 726.67	1,096.52	04/2018 -	-	50.90
301	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
302	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
303	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
304	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
305	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
306	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 - 458.03	486.00	- -	-	6.11
307	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	1,588.29	09/2019 -	-	14.40
308	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 - 1,169.61	2,280.00	- -	-	94.94
309	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 - 323.72	355.24	08/2018 -	-	9.74
310	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 - 950.69	1,108.00	08/2019 -	-	16.55
311	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 - 290.73	359.60	- -	-	23.69

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
312	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 - 1,251.11	1,361.00	- -	-	8.78
313	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
314	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	07/2024	31.88
315	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	01/2022	3.40
316	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 - 988.34	1,043.28	03/2020 -	01/2022	5.56
317	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
318	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
319	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 736.01	830.31	03/2020 -	03/2023	23.39
320	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
321	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	03/2022	10.24
322	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
323	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
324	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
325	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	06/2022	3.95
326	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	-	1.78
327	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696	08/2017	950.64 - 1,161.00	1,168.00	08/2017 -	10/2023	22.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
328	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]	10/2017	964.17 - 1,140.64	1,198.64	10/2017 -	-	24.32
329	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]	09/2017	1,124.11 - 1,124.11	1,300.00	09/2017 -	05/2022	15.65
330	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]	12/2017	404.94 - 404.94	448.18	- -	-	10.68
331	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]	01/2018	573.70 - 644.50	726.99	- -	06/2023	26.72
332	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 - 273.46	276.17	- -	-	.99
333	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
334	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]	02/2018	1,166.26 - 1,166.26	1,296.93	- -	05/2022	11.20
335	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 - 1,995.34	2,400.00	- -	-	20.28
336	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
337	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 - 1,261.98	1,952.20	- -	-	54.69
338	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	03/2018	809.07 - 809.07	1,065.70	- -	-	31.72
339	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
340	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
341	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]	02/2018	1,052.21 - 1,052.21	1,361.00	- -	-	29.35
342	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62 - 1,532.62	1,827.00	03/2021 -	05/2022	19.21
343	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 - 496.20	537.17	- -	-	8.26

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
344	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	-	22.44
345	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	12/2022	5.32
346	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
347	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
348	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	925.96	- -	-	45.89
349	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 795.50	922.64	- -	-	15.98
350	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	03/2018	478.74 - 478.74	1,135.08	- -	-	137.10
351	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
352	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	06/2022	.00
353	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
354	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	10/2022	305.58
355	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299	09/2018	617.41 - 655.64	668.45	02/2019 -	-	8.27
356	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 - 1,240.13	1,321.60	02/2021 -	-	7.72
357	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	07/2020	3,426.00 - 3,426.00	5,148.00	12/2021 -	-	50.26
358	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 - 731.89	732.34	11/2019 -	-	.06
359	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 - 594.75	606.75	11/2019 -	-	2.02

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		1,04,557.17 15,149.22 1,04,368.37	1,24,422.77			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
360	NMHC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 - 15,525.00	21,940.00	05/2015 -	06/2022	41.32
	Total		15,525.00 .00 15,525.00	21,940.00			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
361	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 - 13,334.00	24,664.00	07/2015 -	03/2022	84.97
	Total		13,334.00 .00 13,334.00	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
362	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 - 10,773.00	12,925.22	12/2018 -	08/2022	19.98
	<u>Central Public Works Department</u>						
363	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 - 197.33	217.00	04/2019 -	02/2022	9.97
	<u>Chennai Metro Rail Ltd</u>						
364	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 - 14,600.00	18,380.00	12/2015 -	-	25.89
	<u>Delhi Metro Rail Corporation</u>						
365	DELHI MRTS PHASE-III - [N28000056]	09/2011	38,585.00 - 38,585.00	40,180.91	03/2016 -	-	4.14
	<u>Kochi Metro Rail Corporation Ltd</u>						
366	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 - 5,181.79	6,218.14	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
367	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 - 23,136.00	33,406.00	03/2020 -	03/2023	44.39
	<u>Nagpur Metro Rail Corporation Ltd</u>						
368	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00 - 8,680.00	9,759.79	03/2018 -	02/2022	12.44
	<u>Patna Metro Rail Corporation</u>						
369	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 - 13,365.77	13,925.50	06/2024 -	06/2024	4.19
	Total		1,14,518.89 .00 1,14,518.89	1,35,012.56			
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
370	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 - 254.13	413.29	09/2020 -	03/2024	62.63
371	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 - 225.77	398.90	03/2020 -	03/2022	76.68
	<u>Delhi Jal Board</u>						
372	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	03/2017	665.78 - 665.78	942.18	12/2022 -	12/2022	41.52
	<u>Kolkata Metropolitan Development Authority</u>						
373	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 - 198.43	224.69	02/2022 -	03/2024	13.23
	<u>Uttar Pradesh Jal Nigam</u>						
374	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 - 213.62	261.12	03/2022 -	04/2024	22.24
375	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 - 231.79	234.03	12/2021 -	06/2023	.97
376	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 - 681.78	690.71	06/2022 -	04/2024	1.31
	Total		2,471.30 .00 2,471.30	3,164.92			

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(February 2022)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Grand Total		6,01,098.31 57,959.22 6,46,941.08	9,30,875.97			

FLASH REPORT

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	12320	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	12/2022	11459	84
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	AAI	02/2019	08/2022	10/2023	645.63	14
6	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	03/2024	380.87	24
7	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	AAI	01/2018	08/2022	08/2023	1405	12
8	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	12/2022	177.1	34
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	12/2022	456.86	27
10	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	AAI	05/2020	05/2022	12/2023	353.61	19
11	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	03/2023	412.24	21
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2025	1142	48
13	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	04/2023	389.71	17
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	10/2022	417.23	49
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	12/2024	2467	34
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	AAI	08/2018	10/2021	04/2023	951.28	18
17	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383	27
18	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2023	346.27	27
19	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	AAI	03/2017	04/2021	08/2023	475.39	28
20	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	03/2024	458	48
21	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	03/2024	1216.9	17

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
22	BHATADI EXPASION OC (0.975 MTY)	WCL	02/2016	03/2019	09/2026	327.41	90
23	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2023	321.5	108
24	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	132
25	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2025	339.88	138
26	MOONIDIH XV SEAM UG	BCCL	08/2011	03/2019	04/2024	1230.27	61
27	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2025	869.44	48
28	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	06/2023	17237	19
29	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
30	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
31	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	12/2022	304.13	69
32	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2023	1783.09	24
33	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2023	163.51	144
34	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2023	162.46	108
35	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
36	CHHAL OC SEAM -III (6.00 MTY)	SECL	12/2013	03/2022	03/2025	610.63	36
37	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2027	1458.17	147
38	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2023	555.52	24
39	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
40	GARJANBAHAL OCP	MCL	11/2014	03/2021	03/2026	1375.38	60
41	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
42	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	03/2022	289.45	94
44	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	03/2022	295.56	36
45	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
46	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2023	510.85	84
47	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	06/2023	243	62
48	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18
49	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
50	SRP OC-II EXPANSION PROJECT	SCCL	11/2016	03/2018	03/2022	272.73	48
51	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18
52	JAGANNATHPUR OC RCE (3.0 MTY)	SECL	07/2016	03/2020	03/2022	459.49	24

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD FOR DEFEN	12/2016	02/2020	06/2022	246.31	28

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
54	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD EDUCATION	09/2018	09/2020	11/2022	375	26
55	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD EDUCATION	07/2019	03/2021	02/2023	753.63	23
56	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD EDUCATION	07/2019	03/2022	10/2022	851	7
57	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH 6 PLUS 8 STOREYED	CPWD EDUCATION	03/2020	06/2020	03/2023	193.83	33
58	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD EDUCATION	09/2012	03/2016	03/2022	171.86	72
59	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD EDUCATION	02/2016	06/2017	03/2022	496.18	57
60	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD EDUCATION	01/2018	05/2020	08/2022	430	27
61	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	CPWD EDUCATION	01/2019	03/2022	09/2022	790.79	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
62	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	MITES OF HIGHE	09/2013	09/2014	06/2022	484.32	93
63	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	CPWD EDUCATION	05/2019	03/2020	02/2023	303.9	35
64	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	CPWD EDUCATION	02/2019	06/2020	11/2022	655.34	29
65	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT	CPWD EDUCATION	09/2019	09/2022	06/2023	588.72	9

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
66	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773	29

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
67	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	03/2022	426.72	23

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
68	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD FOR HEALTH	03/2018	09/2020	04/2022	195	19
69	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	06/2022	363.99	49
70	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351	9
71	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD FOR HEALTH	12/2018	06/2021	05/2022	260	11

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
72	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDLAULI	CPWD FOR MHA	05/2019	01/2022	12/2022	199.31	11
73	NSG AT KOLKATA	CPWD FOR MHA	10/2014	04/2018	12/2022	162.88	56
74	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MHA	10/2013	10/2019	06/2022	1219.21	32
75	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	CPWD FOR MHA	01/2020	10/2023	04/2024	166.98	6

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
76	25.5 MW WIND POWER PROJECT AT	NALCO	09/2017	06/2019	12/2022	166.62	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KAYATHAR IN TAMILNADU						
77	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	12/2023	355	37
78	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	12/2023	483	32
79	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	CPWD	04/2019	04/2022	10/2024	255.37	30
80	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	5540	33
81	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534	46

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFI	06/2020	06/2023	01/2024	200	7
83	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	BPCL	07/2020	12/2021	06/2022	640	6
84	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	10/2022	217.92	18
85	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	08/2022	164.69	13
86	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	IOCL	07/2018	01/2021	03/2022	189	14
87	ETHYLENE GLYCOL PROJECT AT PARADIP	IOCL	04/2018	10/2021	07/2022	5654	9
88	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	09/2022	1636	25
89	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	08/2022	909	19
90	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	07/2022	598	29
91	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	04/2022	286.42	20
92	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	03/2022	224.75	19
93	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2022	2292.46	19
94	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
95	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	ONGC	05/2019	05/2021	05/2022	3660.71	12
96	HEERA REDEVELOPMENT - PHASE III	ONGC	06/2019	03/2022	03/2023	2494.68	12
97	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
98	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	09/2022	3361	13
99	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
100	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
101	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
102	PIPELINE REPLACEMENT PROJECT (PRP-VI)	ONGC	05/2019	12/2020	05/2022	763.92	17
103	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	BPCL	08/2019	08/2022	06/2023	1607	10
104	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
105	PX-PTA REVAMP AT PANIPAT REFINERY	IOCL	08/2019	12/2021	01/2023	1255	13
106	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	06/2022	543.91	28
107	BARAUNI-GUWAHATI PIPELINE	GAIL	06/2018	12/2021	06/2023	3308	18
108	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	09/2022	466	17
109	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
110	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	03/2022	522	12
111	PARADIP SOMNATHPUR HALDIA PIPELINE	IOCL	10/2018	10/2021	06/2022	1297.5	8
112	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	10/2022	225.54	20
113	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	IOCL	10/2018	10/2021	09/2022	316.2	11
114	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
115	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	49
116	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2022	160.1	32
117	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	01/2023	161.59	37
118	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2025	2915	146
119	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	GAIL	07/2017	07/2022	08/2023	243.53	13
120	SULPHUR FORMING UNIT IN SRU	HPCL	10/2020	08/2021	03/2022	210.94	7

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
121	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	12/2022	607.06	62
122	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	05/2022	1823	14
123	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
124	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	03/2022	690	44
125	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	108
126	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	06/2022	327.78	50
127	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
128	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
129	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2023	650.82	50
130	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	05/2023	34012	35
131	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	06/2022	4497	42
132	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	03/2022	1810	27
133	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	03/2022	406	17
134	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	03/2022	571.66	27
135	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	08/2022	348	19
136	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2020	03/2022	2881.4	15
137	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	07/2022	1933	19
138	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2022	2433	18
139	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2022	3437	18
140	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	06/2023	1740	30
141	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677	13
142	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2022	163.02	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
143	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	03/2023	318.8	19
144	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	03/2022	466.43	17
145	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	03/2022	249.26	21
146	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	03/2022	161.5	21
147	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	02/2022	206.5	11
148	CATALYST MANUFACTURING UNIT OF 1500 MTA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	29
149	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	10/2022	255.4	26
150	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
151	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	07/2022	906	29
152	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	GAIL	10/2017	10/2022	10/2023	359.25	12
153	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	GAIL	07/2017	07/2022	08/2023	182.2	13
154	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2023	1112	44
155	LPG BP PROJECT CHITTOOR	IOCL	07/2019	07/2022	02/2023	167	7
156	CITY GAS DISTRIBUTION, JAMSHEDPUR	GAIL	10/2017	10/2022	08/2023	221.45	10

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
157	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII	PGCIL	09/2018	03/2021	02/2022	221.36	11
158	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	PGCIL	11/2018	11/2021	05/2022	241.38	6
159	EASTERN REGION STRENGTHENING SCHEME - XXIII	PGCIL	07/2020	06/2021	03/2022	239.89	9
160	NORTH EASTERN REGION STRENGTHENING SCHEME - III	PGCIL	09/2015	12/2017	03/2022	167.31	51
161	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN	PGCIL	08/2019	12/2020	02/2022	2578.47	14
162	SOUTHERN REGION SYSTEM STRENGTHENING - XXV	PGCIL	07/2019	07/2021	02/2022	154.72	7
163	KAYAMKULAM SOLAR 70 MW	NTPC	09/2019	06/2021	07/2022	403.62	13
164	FATEHGARH SOLAR 296MW	NTPC	03/2020	09/2021	03/2022	1749.31	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
165	ETTAYAPURAM SOLAR 230MW	NTPC	03/2020	09/2021	08/2022	1316.22	11
166	ANTA SOLAR 90 MW	NTPC	01/2021	03/2022	10/2022	382.22	7
167	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA	PGCIL	01/2020	01/2021	03/2022	562.86	14
168	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2022	12964.6	46
169	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	162
170	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	03/2022	197.4	48
172	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
173	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	04/2022	3500	21
174	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	08/2022	186.17	37
175	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	04/2023	1931.39	38
176	DEVIKOT SOLAR 90MW	NTPC	03/2020	09/2021	03/2022	501.29	6
177	DEVIKOT SOLAR 150MW	NTPC	01/2020	09/2021	05/2022	798.24	8
178	NOKHRA	NTPC	03/2020	09/2021	10/2022	1722.14	13
179	KAWAS SOLAR 56 MW	NTPC	08/2020	10/2021	10/2022	261.8	12
180	RAMAGUNDAM FLOATING SOLAR 100 MW	NTPC	06/2019	04/2021	05/2022	401.9	13
181	SAMBHU KI BHURJ SOLAR 250 MW	NTPC	01/2020	09/2021	03/2022	1522.71	6
182	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	10/2022	1782	13
183	JETSAR SOLAR 160 MW	NTPC	12/2019	03/2021	03/2022	702.28	12
184	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	03/2022	1394.52	58
185	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2025	2491.58	144
186	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657	88

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
187	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
188	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	02/2023	10598.98	27
189	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	04/2022	322.3	38
190	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	03/2022	235.53	33
191	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	04/2022	379.95	28
192	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	03/2022	522.29	64
193	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	141
194	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
195	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	01/2024	14366.58	55
196	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	07/2025	1381.84	70
197	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
198	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	61
199	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	6
200	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	02/2022	358.83	21
201	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
202	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	02/2025	18668	23
203	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2022	1885.13	39
204	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	06/2022	529.68	43
205	WESTERN REGION SYSTEM STRENGTHENING - XX	PGCIL	07/2019	08/2021	02/2022	226.98	6
206	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS	PGCIL	11/2018	06/2020	03/2022	496.11	21

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
207	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	SER	04/2018	06/2022	12/2023	338	18
208	MEHSANA PALANPUR DOUBLING PROJECT	WR	04/2018	03/2024	12/2024	537.31	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	65.10 KMS						
209	NIMACH BADI SADRI NEW LINE PROJECT	WR	04/2017	03/2022	03/2026	495.18	48
210	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
211	ANAND GODHRA DOUBLING PROJECT 79 KMS	WR	04/2017	03/2020	03/2024	692.25	48
212	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	01/2023	390.39	13
213	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33
214	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2022	943.6	9
215	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2023	927.01	48
216	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
217	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2022	713.48	24
218	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
219	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	04/2022	948.04	25
220	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	06/2022	1402.02	27
221	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2023	942.95	48
222	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
223	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	55
224	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
225	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
226	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
227	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
228	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2025	3631	36
229	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	1547.38	24
230	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2026	2499.71	48
231	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.2	216

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
232	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
233	RAMGANJMUHDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.6	36
234	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
235	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	165
236	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
237	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
238	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	117
239	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	180
240	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	112
241	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	48
242	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
243	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
244	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
245	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
246	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.3	129
247	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
248	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2026	832.47	120
249	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	03/2022	704.31	24
250	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
251	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
252	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	03/2024	279.54	96
253	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
254	BELAPUR-SEAWOOD-URAN ELECTRIFIED	MRTTP	03/1996	03/2004	06/2022	495.44	219

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DOUBLE LINE(MTP)						
255	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
256	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	06/2023	324.73	135
257	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2024	2923.13	189
258	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
259	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2022	495.74	114
260	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2024	385.2	60
261	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
262	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
263	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
264	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	40
265	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450	148
266	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	04/2023	2500	245
267	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2026	3951.98	120
268	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
269	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
270	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2028	1382.78	312
271	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
272	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	10/2023	318.24	139
273	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
274	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	06/2022	1503.71	27
275	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	37
276	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
277	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2024	1160	48
278	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	12/2022	1156.94	33
279	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31
280	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	02/2022	860.43	23
281	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	02/2022	578	23
282	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	02/2024	1614.59	59
283	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
284	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	10/2027	1347.26	67
285	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2025	1640.04	36
286	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	05/2022	644.38	14
287	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2025	320.66	72
288	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	12/2022	1548.66	12
289	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	21
290	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
291	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	12/2024	548	57
292	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798	57
293	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2022	569.63	30
294	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	04/2022	632.68	73
295	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
296	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
297	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2024	923.52	96
298	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	05/2023	1200.2	38
299	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
300	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	76
301	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
302	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
303	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	12
304	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
305	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
306	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	06/2022	969.83	27
307	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	06/2022	1183.25	18
308	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	09/2022	1485.85	21
309	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	15
310	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	12/2023	582.13	21
311	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
312	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
313	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
314	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
315	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
316	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	108
317	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288	18
318	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	06/2022	3055	45
319	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
320	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	NCR	03/2018	03/2023	06/2025	4329.53	27
321	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	06/2023	2001	27
322	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	BITES	02/2016	03/2020	06/2022	393.98	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
323	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	03/2022	585.93	37
324	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	RVNL	02/2015	03/2022	05/2023	1700	14
325	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	12/2022	760	33
326	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
327	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
328	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
329	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	33
330	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	45
331	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
332	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
333	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM)	SER	04/2018	06/2022	12/2025	428.65	42
334	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	SER	03/2019	05/2023	12/2023	1866.31	7

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
335	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	NHAI	02/2019	03/2020	08/2022	996.27	29
336	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	06/2022	990.97	30
337	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	03/2022	188.8	34
338	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	03/2022	423.79	50
339	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	06/2022	624.98	68
340	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MoRTH	11/2015	06/2017	04/2022	335.32	58
341	VADPALE TO BHOGAN KHURD	MoRTH	01/2017	11/2019	06/2022	1598.47	31
342	GADCHIROLI TO MUL	MoRTH	12/2016	06/2019	03/2022	484.15	33
343	MUL TO CHANDRAPUR	MoRTH	12/2016	07/2019	06/2022	162.34	35
344	SAKOLI TO BHANDARA	MoRTH	01/2017	06/2019	06/2022	362.96	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
345	PAITHAN TO SHIRUR	MORTH	03/2017	06/2019	12/2022	341.8	42
346	SHIRUR TO KHARDA	MoRTH	02/2017	06/2019	09/2022	381.77	39
347	AURANGABAD TO SILLOD	MoRTH	02/2017	06/2019	06/2022	456.32	36
348	SILLOD TO FARDAPUR	MoRTH	02/2017	06/2019	06/2022	337.46	36
349	FARDAPUR TO JALGAON	MoRTH	02/2017	06/2019	06/2022	456.45	36
350	KOLDE TO KHETIYA	MoRTH	01/2017	07/2019	03/2022	509.18	32
351	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600	MoRTH	03/2016	12/2019	03/2022	536.65	27
352	MASANIAKALA TO RENGAPALI ODISHA	MoRTH	01/2017	07/2019	09/2022	653.46	38
353	SATARA TO MHASWAD	MoRTH	12/2017	12/2019	06/2022	309.94	30
354	ARNI TO NAIGAINBANDI	MoRTH	01/2018	03/2019	03/2022	264.41	36
355	TALEGAON TO GONAPUR	MoRTH	07/2018	05/2020	12/2022	404.33	31
356	SELDOH TO PANVAR	MoRTH	01/2017	07/2019	09/2022	488.6	38
357	MHASWAD TO TEMBHURNI	MoRTH	01/2017	07/2019	03/2022	307.63	32
358	KURUDWADI TO PANDHARPUR	MoRTH	07/2017	07/2019	03/2022	218.38	32
359	PANDHARPUR TO SANGOLA	NHAI	08/2017	08/2017	10/2023	950.64	74
360	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	07/2022	1176.37	59
361	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	07/2017	07/2017	06/2022	476.56	59
362	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	09/2017	09/2017	05/2022	1124.11	56
363	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	07/2022	1227.87	58
364	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	05/2015	05/2018	03/2022	454.89	46
365	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM 453.000)	NHIDCL	10/2014	11/2018	04/2022	588.95	41
366	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	MoRTH	01/2014	03/2016	04/2022	282.41	73
367	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	MoRTH	11/2010	05/2017	06/2022	268.08	61
367	2 LANING FROM KANUBARI TO START OF	MoRTH	11/2010	05/2017	06/2022	268.08	61

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM						
368	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	03/2022	289.99	39
369	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	03/2022	628.45	26
370	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	12/2022	511.83	64
371	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	03/2022	294.17	74
372	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	03/2022	252	74
373	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	MoRTH	12/2017	11/2018	07/2022	867.97	44
374	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	MoRTH	10/2018	05/2019	05/2022	400.76	36
375	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	MoRTH	08/2017	03/2018	12/2022	962.43	57
376	2-LANING FROM MANU-SIMLUNG (PKG I)	NHIDCL	03/2020	01/2022	10/2022	247.76	9
377	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	NHIDCL	03/2019	04/2022	05/2023	402.94	13
378	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	MoRTH	03/2020	03/2021	04/2022	207.79	13
379	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	MoRTH	06/2020	05/2021	12/2022	221.4	19
380	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MoRTH	08/2020	03/2021	03/2023	222.61	24
381	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	MoRTH	03/2019	12/2019	12/2022	423.15	36
382	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2022	2498.76	91
383	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	02/2022	374	105
384	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	09/2022	1100.7	99
385	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	09/2022	624	101
386	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	04/2022	1724.55	109
387	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	03/2022	1141	103
388	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	03/2022	953.88	104
389	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
390	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	03/2022	1078.84	103
391	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2023	998.79	118
392	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	03/2022	1928.22	83
393	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	03/2022	822.9	47
394	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	03/2023	1655.01	79
395	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	07/2022	946	49
396	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	03/2022	478.51	101
397	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	05/2023	563.92	65
398	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	46
399	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2022	593.26	49
400	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB , SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	06/2022	649.5	39
401	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	NHAI	12/2015	04/2019	07/2022	1041.1	39
402	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	03/2022	1423.96	40
403	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
404	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	06/2022	899	38
405	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	03/2023	546	44
406	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	08/2023	591.66	49
407	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	05/2022	804.97	47
408	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	11/2013	07/2016	06/2022	683.83	71
409	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	02/2016	05/2016	06/2022	178.85	73
410	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	MORTH	02/2016	05/2016	03/2022	553.3	70
411	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	03/2022	1408.85	65
412	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	06/2023	1167.42	51

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
413	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	MoRTH	08/2016	12/2016	05/2022	1742.01	65
414	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	NHAI	09/2016	08/2019	06/2022	2510.04	34
415	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	05/2022	605.84	46
416	FOUR LANNING OF TULJAPUR-AUSA SECTION	NHAI	02/2017	02/2020	03/2022	904.16	25
417	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	03/2022	1373.28	24
418	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	52
419	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	NHAI	03/2017	03/2020	03/2022	296.19	24
420	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	03/2023	754.54	36
421	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2023	672.89	36
422	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2022	1288.07	24
423	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2022	284.09	59
424	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	03/2022	195.23	59
425	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	NHIDCL	02/2017	04/2017	03/2022	203.36	59
426	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	03/2022	198.22	59
427	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	06/2022	894	26
428	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MoRTH	03/2016	11/2018	03/2023	271.17	52
429	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MoRTH	02/2018	03/2018	04/2022	169.63	49
430	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MoRTH	01/2017	09/2019	12/2022	396.86	39
431	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MoRTH	02/2018	09/2020	12/2022	426.18	27
432	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2022	184.62	49
433	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	MoRTH	03/2018	10/2020	03/2023	254.3	29
434	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MoRTH	03/2016	08/2019	03/2023	160.27	43
435	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF	MoRTH	06/2016	08/2019	03/2023	236.78	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	EXISTING LEVEL CROSSING GATE N						
436	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MoRTH	01/2017	03/2017	03/2022	205.05	60
437	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2022	214.69	51
438	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2022	217.22	43
439	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2022	233.04	48
440	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	02/2022	249.05	43
441	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2022	254.17	49
442	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	03/2022	279.44	48
443	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	03/2022	809.16	44
444	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MoRTH	03/2016	06/2019	03/2022	877.79	33
445	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	05/2019	09/2022	306.28	40
446	CONSTN. OF 4 LANE IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	MoRTH	01/2017	03/2019	10/2022	247.25	43
447	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	MoRTH	03/2018	08/2020	12/2022	293.1	28
448	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MoRTH	10/2017	10/2019	12/2022	1069.59	38
449	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	MoRTH	03/2018	11/2020	12/2022	170.57	25
450	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	MoRTH	09/2016	02/2017	02/2022	372.68	60
451	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MoRTH	11/2016	05/2017	04/2022	290.15	59
452	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MoRTH	01/2017	08/2017	05/2022	319.28	57
453	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	MoRTH	02/2017	11/2017	05/2022	429.43	54
454	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MoRTH	03/2016	05/2016	10/2022	995.09	77
455	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	MoRTH	03/2018	08/2020	10/2022	293.64	26
456	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	MoRTH	08/2016	01/2017	06/2022	350.61	65
457	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	MoRTH	01/2016	05/2016	06/2022	386.09	73
458	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM	MoRTH	03/2016	09/2016	05/2022	444.84	68

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM34/230 TO KM84/550 OF NH214(NH216						
459	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MoRTH	11/2016	08/2017	06/2022	376.25	58
460	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	11/2022	263.45	62
461	SARSAM TO KOTHARI	MoRTH	02/2016	07/2019	09/2022	545.64	38
462	AKOLA TO AKOT	MoRTH	01/2017	06/2019	09/2022	313.95	39
463	PATRADEVI TO KARASWADA 4L	MoRTH	03/2017	05/2020	06/2022	634.32	25
464	KARASWADA TO BAMBOLIM	MoRTH	03/2017	12/2019	03/2022	852.67	27
465	DIGRAS DARWAH KARANJA	MoRTH	01/2017	06/2019	03/2022	391.06	33
466	WADI TO ASOLA	MoRTH	01/2017	09/2019	12/2022	363.82	39
467	MANGAON TO DIGHI PORT	MoRTH	01/2017	07/2019	03/2022	457.52	32
468	INDAPUR TO AGARDANDA	MoRTH	01/2017	07/2019	02/2022	355.17	31
469	WAKAN PALI KHOPOLI	MoRTH	01/2017	05/2019	09/2022	376.19	40
470	SHAHPUR PATGAON SECTION I	MoRTH	01/2018	12/2019	06/2022	150.79	30
471	PATGAON KHOPOLI SECTION I	MoRTH	01/2018	12/2019	03/2022	170	27
472	AHMADPUR TO PIMPLA	MoRTH	01/2017	08/2019	06/2022	422.38	34
473	PIMPLA TO MANJARUMBHA	MoRTH	01/2017	08/2019	06/2022	595.77	34
474	MANJUSUMBA TO CHUMBALI	MoRTH	01/2017	08/2019	03/2022	228.54	31
475	DEORI TO AMGAON	MoRTH	01/2017	05/2019	06/2022	409.62	37
476	MANTHA TALUKAS BORDER TO PARTUR	MoRTH	01/2017	07/2019	03/2022	486.19	32
477	PARTUR TO MAJALGAON	MoRTH	01/2017	07/2019	06/2022	420.57	35
478	KAIJ TO KUSALAM	MoRTH	01/2017	07/2019	06/2022	554.78	35
479	JAHIRABAD TO LATUR	MoRTH	01/2017	11/2019	03/2022	461.96	28
480	MAHAD TO RAIGAD FORT	MoRTH	07/2018	05/2020	12/2022	237.4	31

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
481	SHIROD SHAHPURER TO NANDED	MoRTH	01/2017	07/2019	02/2022	211.34	31
482	SALAIKHURD TO TIRORA	MoRTH	01/2018	12/2019	03/2022	415.25	27
483	NILAJPHATA TO BHANDARA	MoRTH	01/2018	05/2020	09/2022	420.63	28
484	RALEGAON TO RAMTIRTH	MoRTH	01/2017	07/2019	03/2022	210.81	32
485	MEHKAR TO AJISPUR	MoRTH	01/2017	07/2019	03/2022	232.77	32
486	KARAD TO VITA	MoRTH	01/2018	12/2019	03/2022	344.85	27
487	VITA TO NAGAJ	MoRTH	03/2018	12/2019	06/2022	304.58	30
488	SANGOLA TO JATH	MoRTH	01/2018	12/2019	03/2022	257.38	27
489	KARAD TO TAGAON	MoRTH	01/2017	06/2019	12/2022	537.81	42
490	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	MoRTH	02/2017	07/2019	03/2022	422.02	32
491	KARAD PATAN CHIPLUN GUHAGAR	MoRTH	02/2017	06/2019	09/2022	407.19	39
492	KARWANDI TO RAJURI	MoRTH	03/2018	12/2019	06/2022	276.95	30
493	SHIVUR TO YEOLA	MoRTH	03/2018	12/2019	03/2022	181.08	27
494	PALPHATA TO PHULAMBARI	MoRTH	03/2018	12/2019	03/2022	227.19	27
495	CHIKALI TO DHAD	MoRTH	03/2018	12/2019	06/2022	189.46	30
496	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	MoRTH	03/2018	12/2019	03/2022	336.21	27
497	PARBHANI TO GANGKHED	MoRTH	03/2018	12/2019	03/2022	238.19	27
498	NANDED TO JALKOT	MoRTH	12/2017	09/2019	06/2022	456.93	33
499	JALKOT TO TOGRI	MoRTH	07/2018	08/2020	03/2022	299.92	19
500	KOTHARI TO DHANORA	MoRTH	09/2018	08/2020	09/2022	301.38	25
501	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	09/2022	274.31	52
502	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	07/2022	403.36	49
503	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	09/2022	417.24	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
504	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	03/2023	262.97	53
505	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2017	03/2022	409.85	51
506	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	12/2022	391	50
507	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) 0	NHIDCL	03/2018	10/2018	06/2022	234.27	44
508	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2018	03/2022	387	42
509	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
510	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
511	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
512	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
513	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	03/2022	215.12	42
514	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
515	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	NHIDCL	11/2017	11/2017	03/2022	290.05	52
516	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	05/2022	1532.62	14
517	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	03/2022	829	74
518	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2018	07/2022	1383.78	48
519	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
520	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
521	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
522	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
523	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
524	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
525	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
526	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND	NHIDCL	04/2017	09/2019	09/2023	428.11	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GEOMETRIC IMPROVEMENTS FRO						
527	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	NHIDCL	03/2018	08/2018	05/2022	404.17	45
528	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	NHIDCL	03/2018	11/2018	08/2022	216	45
529	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	NHIDCL	03/2018	07/2019	12/2022	253.44	41
530	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	03/2022	162.56	48
531	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MoRTH	03/2018	08/2018	03/2022	166.21	43
532	OSMANNAGAR TO KUNDRAL	MoRTH	09/2017	08/2020	06/2022	344.25	22
533	PUNE TO MALE VILLAGE	MoRTH	03/2018	12/2019	04/2022	228.31	28
534	ARDHAPUR TO HIMAYATNAGAR	MoRTH	12/2017	06/2020	06/2022	426.06	24
535	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	MoRTH	03/2018	12/2019	04/2022	256.15	28
536	HIMAYATNAGAR TO PHULSAWANGI	MoRTH	03/2018	12/2019	06/2022	294.87	30
537	PUNE RAIGARH DISTRICT BORDER TO MANGAON	MoRTH	03/2018	12/2019	03/2022	223.46	27
538	PAHUR TO BODHWAD	MoRTH	01/2017	05/2020	02/2022	244.93	21
539	MANGRUPHIR TO MAHAN	MoRTH	03/2018	11/2019	02/2022	222.13	27
540	MALEWADA TO CHIMUR	MoRTH	10/2016	06/2019	06/2022	322.55	36
541	CHIMUR TO WARORA	MoRTH	11/2016	03/2019	06/2022	467.7	39
542	PEN TO KHOPOLI	MoRTH	03/2018	03/2018	06/2022	301.39	51
543	PANCHARAL TO MANDANGHAR	MoRTH	07/2018	05/2020	12/2022	381.08	31
544	KOLHA TO NASRATPUR	MoRTH	04/2016	04/2019	06/2022	281.78	38
545	NASRATPUR TO BARASGAON	MoRTH	07/2016	09/2019	06/2022	406.54	33
546	BARASGAON TO RAHATEE	MoRTH	07/2016	09/2018	03/2022	289.11	42
547	INDAPUR TO VADPALE	MoRTH	01/2017	12/2019	06/2022	1202.52	30
548	BHOGAN KHURD TO KASHEDI	MoRTH	09/2017	06/2021	09/2022	743.21	15
549	PARSHURAM GHAT TO ARAWALI	MoRTH	04/2016	12/2019	09/2022	983.14	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
550	KANTE TO WAKED	MoRTH	03/2016	11/2019	12/2022	1230.02	37
551	PARLI PIMPLA DAHIGUDA	MoRTH	02/2017	06/2019	06/2022	205.72	36
552	RISOD TO HINGOLI	MoRTH	02/2018	12/2019	03/2022	355.99	27
553	WARDHA TO ARVI	MoRTH	02/2018	04/2020	03/2022	313.58	23
554	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	03/2022	392.33	48
555	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	MoRTH	09/2018	09/2021	12/2022	160	15
556	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	MoRTH	01/2017	01/2021	04/2022	205.95	15
557	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	MoRTH	03/2018	06/2021	06/2022	351	12
558	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MoRTH	01/2019	03/2021	03/2022	264.5	12
559	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MoRTH	03/2018	04/2020	03/2022	263.89	23
560	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONALI - GORAKHPUR ROAD (J	MoRTH	03/2018	08/2020	03/2022	288.3	19
561	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MoRTH	01/2016	08/2016	12/2022	497.14	76
562	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MoRTH	01/2016	09/2016	03/2022	476.2	66
563	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	12/2022	452.94	77
564	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	06/2022	496.02	87
565	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	02/2022	379.16	51
566	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	08/2022	847	29
567	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	NHAI	03/2019	05/2020	08/2022	1047	27

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
568	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	05/2022	262.87	35
569	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	NMDC	11/2015	06/2023	06/2024	2907	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
570	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	06/2022	15525	85
571	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	11/2022	1034.01	61

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
572	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD FOR TELECOM	10/2014	03/2018	03/2022	248.2	48
573	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	BSNL	03/2020	06/2021	06/2022	431.16	12
574	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	13334	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
575	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	CPWD	05/2019	09/2020	05/2023	299.97	32
576	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	04/2022	392	20
577	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	11/2024	11076.48	8
578	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	12/2025	8379.62	21
579	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2021	03/2025	26405.14	49
580	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	02/2022	197.33	34
581	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	02/2022	8680	47
582	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	23136	36
583	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	CPWD	10/2016	03/2021	06/2022	422	15
584	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2022	11420	13
585	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44
586	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2024	1180	35
587	INDORE METRO RAIL	MPMRCL	11/2018	02/2023	07/2025	7500.8	29
588	BHOPAL METRO RAIL	MPMRCL	11/2018	02/2023	05/2025	6941.4	27
589	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2024	1128	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
590	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	BUIDCO	08/2017	06/2022	12/2023	824	18
591	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
592	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	BUIDCO	08/2017	06/2022	12/2023	578.89	18
593	INTERCEPTION AND DIVERSION WITH STP AT BALLY	KMDA	10/2017	12/2021	09/2023	164.93	21
594	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	KMDA	01/2018	12/2021	09/2023	172.1	21
595	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	KMDA	12/2014	04/2020	03/2022	272.32	23
596	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	KMDA	02/2014	12/2019	05/2022	274.76	29
597	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	KMDA	08/2017	12/2021	09/2023	185.22	21
598	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	BUIDCO	03/2017	05/2021	05/2022	277.42	12
599	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	03/2024	160	25
600	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	BUIDCO	05/2017	11/2020	03/2022	191.62	16
601	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	BUIDCO	05/2017	04/2021	06/2022	356.37	14
602	SAIDPUR SEWER NETWORK PATNA	BUIDCO	04/2015	01/2021	05/2022	268.63	16
603	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	03/2022	225.77	24
604	SEWER NETWORKS, SPS AND STP, MUNGER	BUIDCO	03/2018	10/2021	12/2023	294.02	26
605	SEWER NETWORKS SPS AND STP HAJIPUR	BUIDCO	03/2018	08/2021	04/2023	305.19	20
606	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	KMDA	08/2017	09/2022	12/2024	307.12	27
607	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	KMDA	03/2018	06/2022	03/2024	165.16	21
608	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	KMDA	05/2018	02/2022	03/2024	198.43	25
609	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	KMDA	12/2018	04/2022	12/2024	234.31	32
610	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER	KMDA	03/2019	04/2022	12/2024	287.53	32

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	DAMODAR AT DURGAPURL						
611	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	KMDA	01/2019	04/2022	12/2024	384.96	32
612	I AND D AND STP AT CHAPPRA	BUIDCO	11/2018	12/2020	07/2022	236.15	19
613	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	42
614	SEWER NETWORK SPS AND STP BEGUSARAI	BUIDCO	03/2018	07/2021	03/2023	230.06	20
615	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	03/2024	298.12	32
616	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	UPJalNigam	02/2019	06/2022	04/2024	681.78	22
617	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	UPJalNigam	01/2019	12/2021	06/2023	231.79	18
618	MATHURA SEWERAGE SCHEME	UPJalNigam	12/2017	12/2020	03/2022	460.45	15
619	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	DJB	12/2018	01/2021	02/2022	515.07	13
620	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
621	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12
622	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	UPJalNigam	03/2019	08/2021	03/2024	271.39	31
623	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	UPJalNigam	03/2018	09/2021	09/2022	967.23	12
624	FARRUKHABAD I AND D AND STP WORKS HAM	UPJalNigam	10/2017	03/2022	04/2024	213.62	25
625	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	UPJalNigam	05/2017	09/2021	12/2022	767.59	15
626	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	UKJalNigam	03/2017	11/2019	03/2022	158	28

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(FEBRUARY 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	19220	7761
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	1383	1938	555

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	479.53	808.97	329.44
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC FOR DPIIT	09/2011	09/2019	12579.09	13812.3	1233.21
11	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	4773	5178	405

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
12	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	414.11	586.5	172.39
13	AIIMS BILASPUR	WBCC FOR HEALTH	04/2018	09/2021	1351	1471	120

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	NATIONAL AUTOMOTIVE TESTING AND INFRASTRUCTURE PROJECT (NATRIP) RD	NATIS	04/2011	09/2011	1718	3727.3	2009.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD FOR MH	10/2013	10/2019	1219.21	2000	780.79

MINES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	5540	6435.9	895.9
17	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	534	667.23	133.23
18	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	355	581	226

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
20	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
21	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
22	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395
23	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
24	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
25	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
26	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
27	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
28	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
29	DEVANGONTHI MARKETING TERMINAL	MANGALORE RE	06/2020	06/2023	200	304	104
30	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY	NRL	01/2019	10/2024	12366	18968	6602
31	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
32	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	598	753.89	155.89
33	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
34	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001.34	1139.55

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
35	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
36	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
37	LOKTAK D/S HEP(NHPC)	NHPC	12/1999	06/2006	578.62	1311.05	732.43
38	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
40	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13199	2068.81
41	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	1381.84	1803	421.16
42	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	679	149.32
43	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	1885.13	2426	540.87
44	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
45	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
46	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	5289.25	1051.29
47	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10998	399.02
48	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
49	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6
50	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
51	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
52	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213
53	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
54	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	1931.39	2635.55	704.16
55	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	3500	3994	494

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
56	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	17007	2640.42
57	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
58	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3650	2616.93
59	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
60	RAMGANJMUHDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
61	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	433	299.59
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	3081.2	2356.51
63	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	6527	4133.53
64	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1530.09	543.79
65	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	2000.97	199.96
66	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
67	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	1387.52	594.63
68	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
69	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6383.82	2880.13
70	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4834.54	1921.03
71	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	1160.48	1373.74	213.26
72	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
73	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1090	765.27
75	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
76	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
77	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4794.6	2523.1

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
78	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3300	1173
79	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
80	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
81	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
82	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3633.12	2129.41
83	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	2223.37	1393.63
84	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1549.09	1245.11
85	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
86	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
87	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
88	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
89	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	37012.26	34512.26
90	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2017.96	1567.96
91	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	2538.01	989.35
92	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
93	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	923.28	278.9
94	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1524.68	177.42
95	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTD	03/2013	03/2016	4874.58	8574.97	3700.39
96	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	728.92	433.92
97	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
98	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
99	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
100	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	750	335.16
101	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	401.65	160.13
102	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
103	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
104	ERNAKULAM-KUMBALAM	SR	04/2010	N.A.	189.24	448.1	258.86
105	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	591	426.59
106	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	708.73	139.1
107	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	709.69	456.73
108	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	749.4	479.26
109	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
110	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
111	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	760	1536	776
112	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
113	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	WR	03/2012	N.A.	248.26	528.49	280.23
114	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	WR	03/2012	N.A.	217.38	393.62	176.24
115	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	242.28	122.55
116	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3176.6	1268.09
117	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
118	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	2478.23	2875.12	396.89
119	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
120	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	2203.53	1020.28
121	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1552.26	609.31
122	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
123	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
124	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
125	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	24659	8443
126	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1457.79	530.78
127	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	943.6	1500	556.4
128	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1339	339
129	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.97	343.14
130	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25
131	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
132	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
133	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
134	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
135	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
136	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.49	688.49
137	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
138	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2445.3	681.37
139	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	1824	528.58
140	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	51219	39630
141	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13
142	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
143	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2111.88	1991.18
144	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
145	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2047.51	249.51

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
146	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
147	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
148	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1893.55	1514.99
149	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
150	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
151	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
152	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1383.69	346.54
153	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
154	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1878	263.41
155	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	758.36	180.36
156	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
157	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1104	243.57
158	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
159	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1954.21	797.27
160	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
161	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
162	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
163	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6663	4336.48
164	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
165	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1145.79	760.59
166	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	774.51	278.77
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	14322	9867.83
168	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
169	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2404.03	341.73
170	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
171	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
172	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
173	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
174	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
175	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
176	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
177	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	390.39	511.75	121.36
178	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	839	214
179	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11
180	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	817.23	172.45
181	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
182	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
183	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
184	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
185	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
186	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	800	197.5
187	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
188	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3444	2861.17
189	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
190	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83
191	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
192	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
193	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
194	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
195	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
196	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	1408.85	2138.16	729.31
197	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	NHAI	03/2016	N.A.	1737	2421.37	684.37
198	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	NHAI	03/2016	N.A.	1668	2501.85	833.85
199	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	NHAI	03/2016	N.A.	1443	2330.79	887.79
200	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	899	1376.86	477.86
201	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	870	1418.78	548.78
202	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
203	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
204	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
205	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
206	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	MORTH	01/1991	N.A.	675	780.77	105.77
207	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
208	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	478.51	1082.4	603.89
209	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
210	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	754	2047.64	1293.64
211	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45
212	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
213	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	672.89	830.31	157.42
214	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
215	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
216	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	1251.11	1361	109.89
217	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	1023.23	417.39
218	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
219	4 LANING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
220	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	1588.29	199.95
221	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
222	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	322.24	135.28
223	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MORTH	01/2017	01/2018	576.48	686.13	109.65
224	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
225	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
226	FOUR LANING OF SOLAN-KAITHLIGHT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	NHAI	03/2018	N.A.	478.74	1135.08	656.34
227	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	NHAI	03/2018	N.A.	795.5	922.64	127.14
228	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	925.96	291.26
229	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
230	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
231	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	NHAI	07/2020	12/2021	3426	5148	1722
232	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	624.98	731.5	106.52
233	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
234	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
235	ISMAILABAD-NARNAUL PKG-1	NHAI	01/2019	N.A.	996.65	1173.65	177
236	ISMAILABAD-NARNAUL PKG-2	NHAI	01/2019	N.A.	1243.45	1407.35	163.9
237	ISMAILABAD-NARNAUL PKG-7	NHAI	01/2019	N.A.	1137.42	1238.29	100.87

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
238	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	NHAI	11/2017	01/2019	2159	2262	103
239	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
240	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	NHAI	03/2018	N.A.	809.07	1065.7	256.63
241	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
242	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
243	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
244	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
245	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
246	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	NHAI	01/2018	N.A.	573.7	726.99	153.29
247	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
248	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	1827	294.38
249	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	NHAI	02/2018	N.A.	1052.21	1361	308.79
250	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1300	175.89
251	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	964.17	1198.64	234.47
252	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	950.64	1168	217.36
253	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	NHAI	03/2017	03/2020	993.16	1434	440.84
254	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
255	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
256	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
257	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
258	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
259	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
260	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	726.67	1096.52	369.85

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
261	FOUR LANING OF PARWANOO -SOLAN	NHAI	09/2015	03/2018	934.46	1457.82	523.36
262	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1414.01	331.01
263	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	2128.72	2408.72	280
264	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	593.26	717.24	123.98
265	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	744.73	213.6
266	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	624.41	992.67	368.26
267	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
268	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
269	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
270	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
271	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35
272	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
273	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	8680	9759.79	1079.79
274	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73
275	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12925.22	2152.22
276	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	38585	40180.91	1595.91
277	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	33406	10270

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(FEBRUARY 2022)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
278	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
279	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD - 10MG/L	DJB	03/2017	12/2022	665.78	942.18	276.4
280	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
281	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13

FLASH REPORT

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2023	1,2320.00	1,7079.00	4759	84
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	12/2022	1,1459.00	1,9220.00	7761	84
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2023	346.27	480.33	134.06	27
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	10/2022	417.23	707.73	290.5	49
6	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383.00	1938.00	555	27

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
8	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	808.97	329.44	132

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
9	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC FOR DPIIT	11/2017	12/2019	05/2022	4773.00	5178.00	405	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
10	AIIMS BILASPUR	NBCC FOR HEALTH	04/2018	09/2021	06/2022	1351.00	1471.00	120	9

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
11	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT	CPWD FOR MHA	10/2013	10/2019	06/2022	1219.21	2000.00	780.79	32

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

533

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	NEW DELHI								

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	UTKAL D AND E COAL BLOCK	NALCO	05/2016	01/2020	11/2023	534.00	667.23	133.23	46
13	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	NALCO	12/2015	11/2020	12/2023	355.00	581.00	226	37
14	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	01/2024	5540.00	6435.90	895.9	33

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	DEVANGONTHI MARKETING TERMINAL	MANGALORE REFIN	06/2020	06/2023	01/2024	200.00	304.00	104	7
16	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24
17	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	3375.90	185.21	49
18	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2025	2915.00	5909.00	2994	146
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	12/2022	607.06	1236.00	628.94	62
20	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	05/2022	1823.00	3027.90	1204.9	14
21	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
22	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2022	861.79	2001.34	1139.55	108
23	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66
24	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677.00	3072.00	395	13
25	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	06/2022	4497.00	6025.00	1528	42

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

534

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
26	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2023	1112.00	1507.24	395.24	44
27	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
28	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	07/2022	598.00	753.89	155.89	29
29	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	340.76	134.13	29

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
30	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	06/2022	529.68	679.00	149.32	43
31	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	03/2022	1885.13	2426.00	540.87	39
32	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	04/2022	3500.00	3994.00	494	21
33	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	04/2023	1931.39	2635.55	704.16	38
34	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	03/2022	1,2964.60	1,7304.00	4339.4	46
35	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	9897.59	5978	162
36	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
37	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	01/2024	1,4366.58	1,7007.00	2640.42	55
38	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	07/2025	1381.84	1803.00	421.16	70
39	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2025	2491.58	3860.35	1368.77	144
40	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657.00	4825.60	3168.6	88
41	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

535

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
42	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	02/2023	1,0598.98	1,0998.00	399.02	27
43	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63
44	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	01/2024	5111.33	6700.00	1588.67	61
45	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	947.89	299.56	6
46	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2024	2978.48	5867.38	2888.9	141

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	SER	04/2018	12/2021	01/2023	390.39	511.75	121.36	13
48	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2026	644.78	817.23	172.45	108
49	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
50	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288.00	4970.11	2682.11	18
51	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
52	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	12/2024	744.04	1215.54	471.5	45
53	CHANDIGARH-BADDI	NR	04/2007	03/2023	12/2025	328.14	1540.13	1211.99	33
54	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	RVNL	02/2015	03/2020	12/2022	760.00	1536.00	776	33
55	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	04/2022	632.68	950.00	317.32	73
56	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2111.88	1991.18	105
57	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

536

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE
(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
58	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2024	1763.93	2445.30	681.37	55
59	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2025	3631.00	3887.48	256.48	36
60	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2025	701.61	810.02	108.41	76
61	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
62	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	1873.21	1002.25	12
63	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	06/2022	969.83	1312.97	343.14	27
64	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	06/2022	1503.71	3633.12	2129.41	27
65	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2022	1111.99	1539.28	427.29	37
66	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	12/2022	1156.94	1954.21	797.27	33
67	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
68	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	02/2022	860.43	1104.00	243.57	23
69	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	02/2022	578.00	758.36	180.36	23
70	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	02/2024	1614.59	1878.00	263.41	59
71	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	728.92	433.92	37
72	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	10/2027	1347.26	1524.68	177.42	67
73	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
74	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	06/2023	324.73	1090.00	765.27	135
75	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	12/2024	2923.13	3791.66	868.53	189

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

537

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,4322.00	9867.83	153
77	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	12/2022	495.74	774.51	278.77	114
78	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2024	385.20	1145.79	760.59	60
79	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60
80	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6663.00	4336.48	132
81	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	8600.00	7260.52	96
82	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2027	1045.20	2120.16	1074.96	216
83	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
84	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2024	424.60	2909.99	2485.39	36
85	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
86	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2022	133.41	433.00	299.59	165
87	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
88	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	3081.20	2356.51	73
89	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2023	2393.47	6527.00	4133.53	117
90	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2025	1160.48	1373.74	213.26	180
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	07/2025	2913.51	4834.54	1921.03	112
92	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2026	3503.69	6383.82	2880.13	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

538

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
93	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	1387.52	594.63	24
94	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.30	1530.09	543.79	129
95	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	03/2022	704.31	927.94	223.63	24
96	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
97	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4794.60	2523.1	24
98	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	06/2022	495.44	2980.41	2484.97	219
99	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	860.41	450.33	40
100	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	11/2024	450.00	2017.96	1567.96	148
101	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	04/2023	2500.00	3,7012.26	34512.3	245
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2026	3951.98	4259.48	307.5	120
103	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
104	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
105	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1549.09	1245.11	60
106	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	2223.37	1393.63	48
107	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	05/2022	644.38	923.28	278.9	14
108	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2025	320.66	1378.11	1057.45	72
109	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	12/2022	1548.66	2538.01	989.35	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

539

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
110	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	1383.69	346.54	21
111	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
112	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	12/2024	548.00	819.01	271.01	57
113	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798.00	2047.51	249.51	57
114	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	09/2022	569.63	708.73	139.1	30
115	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2022	943.60	1500.00	556.4	9
116	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2023	927.01	1457.79	530.78	48
117	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	03/2022	713.48	2725.00	2011.52	24
118	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
119	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	04/2022	948.04	2009.00	1060.96	25
120	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2023	942.95	1552.26	609.31	48
121	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	06/2022	1183.25	2203.53	1020.28	18
122	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	09/2022	1485.85	1835.83	349.98	21
123	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	06/2023	2478.23	2875.12	396.89	15
124	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	12/2023	582.13	1247.64	665.51	21
125	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3176.60	1268.09	9
126	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	03/2022	585.93	1268.32	682.39	37

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

540

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
127	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150.00	341.66	191.66	66
128	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
129	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	06/2022	624.98	731.50	106.52	68
130	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2022	1288.07	1420.00	131.93	24
131	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	03/2022	478.51	1082.40	603.89	101
132	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	744.73	213.6	46
133	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	06/2022	593.26	717.24	123.98	49
134	FOUR LANNING OF RAMPUR-KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	NHAI	03/2016	04/2019	06/2022	899.00	1376.86	477.86	38
135	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	MORTH	01/2014	10/2016	03/2022	1408.85	2138.16	729.31	65
136	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	07/2024	744.64	982.00	237.36	52
137	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	05/2022	605.84	1023.23	417.39	46
138	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	NHAI	03/2017	03/2020	03/2023	672.89	830.31	157.42	36
139	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	10/2023	950.64	1168.00	217.36	74
140	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	05/2022	1124.11	1300.00	175.89	56
141	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	06/2022	268.08	390.73	122.65	61
142	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

541

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(FEBRUARY 2022)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
143	FOUR LANE OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	05/2022	1532.62	1827.00	294.38	14

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
144	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	06/2022	1,5525.00	2,1940.00	6415	85

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
145	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	1,3334.00	2,4664.00	11330	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
146	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2925.22	2152.22	44
147	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	2,3136.00	3,3406.00	10270	36
148	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	02/2022	8680.00	9759.79	1079.79	47

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
149	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	03/2022	225.77	398.90	173.13	24
150	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	03/2024	254.13	413.29	159.16	42
151	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>POWER</u>							
	<u>Power Grid Corporation Of India Limited</u>							
1	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA - PPP (BOT) - [N18000314]	01/2020	562.86	562.86	01/2021	03/2022	.00	14
	Total		562.86	562.86				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
2	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS (ANNUITY) - [N24000176]	05/2010	374.00	166.90	05/2013	-	-55.37	105
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36	469.31	01/2014	-	61.08	0
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00	475.00	05/2013	-	46.15	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00	485.00	08/2013	-	.00	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	-	.00	0
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	-	.00	46
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	-	15.53	0
13	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	-	.00	0
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	09/2022	.00	101

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
15	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0
16	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - PPP BOT (Hybrid Annuity) - [N24001340]	11/2019	716.00	716.00	07/2021	-	.00	0
17	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	03/2022	.00	47
18	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
19	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	03/2022	.00	104
20	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
21	4-LANING OF BRAHAMPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2023	.00	118
22	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	0
23	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	03/2022	.00	103
24	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	09/2022	.00	99
25	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	03/2022	.00	103
26	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
27	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
28	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,321.60	02/2021	-	7.72	0
29	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
30	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0
31	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
32	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
33	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(February 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
35	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
36	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	01/2016	.00	4
37	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10	1,601.10	02/2021	-	.00	0
38	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	03/2023	.00	79
39	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
40	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
41	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	04/2022	.00	109
42	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
43	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
44	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	03/2022	.00	83
45	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	-	.00	62
46	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	2,047.64	03/2013	-	171.57	0
47	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
48	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,262.00	01/2019	01/2019	4.77	0
49	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	2,360.65	-	-	41.78	0
50	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,408.72	04/2019	-	13.15	29
51	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	03/2022	.00	91
52	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,519.00	06/2015	-	16.67	0
53	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	3,379.45	03/2014	12/2022	18.66	105
	Total		64,315.48	68,151.65				

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (February 2022)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Grand Total		64,878.34	68,714.51				

FLASH REPORT

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(February 2022)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u> HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH Total	03/2018	601.02 - 601.02 -	601.02	538.47 538.47	- - -	03/2022	-	0/0 0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
2	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	3,650.00	3,679.49	- -	07/2022	-	0/0
3	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	1,625.87	981.50	- -	03/2024	-	0/0
4	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	1,470.50	1,536.32	- -	03/2024	-	0/0
5	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 1,483.14	1,483.14	1,469.46	- -	03/2024	-	0/0
6	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	2,066.78	1,610.87	- -	12/2024	-	0/0
7	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	735.20	392.88	- -	12/2024	-	0/0
8	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 519.33	519.33	320.25	- -	12/2024	-	0/0
9	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	614.45	353.25	- -	03/2025	-	0/0
10	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 1,605.17	1,605.17	159.03	- -	12/2025	-	0/0
11	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20 -	2,995.01	2.55	- -	03/2024	-	0/0
12	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56 -	1,893.55	386.78	- -	03/2023	-	0/0
	<u>Eastern Railways</u>								
13	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	495.10	333.93	- -	03/2022	-	0/0
14	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20	311.86	- -	03/2022	-	0/0
15	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	310.70	418.15	- -	03/2024	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								

Costing Rs. 150 Crore and above (February 2022)									
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL <u>North Central Railway</u>	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
17	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE <u>North East Frontier Railway</u>	04/2010	2,030.50	2,030.50	-	-	12/2027	-	0/0
18	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE <u>North Eastern Railway</u>	04/2010	241.52	401.65	338.00	-	03/2023	-	0/0
19	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER, UTTAR PRADESH <u>Northern Railway</u>	04/2016	602.50	800.00	164.95	-	12/2023	-	0/0
20	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR, MULTI STATE	04/2007	336.91	791.39	689.83	-	09/2023	-	0/0
21	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR, DELHI	04/2012	295.68	419.00	167.23	-	09/2023	-	0/0
22	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR, DELHI <u>South Western Railway</u>	04/1999	156.65	359.00	118.38	-	03/2024	-	0/0
23	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01	2,000.97	83.08	-	03/2025	-	0/0
24	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85	348.85	.36	-	03/2025	-	0/0
25	RAYADURGA-TUMKUR NL - [N22000279]SWR, MULTI STATE	04/2007	2,062.30	2,404.03	1,108.07	-	12/2025	-	2/2
26	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25	367.77	-	-	03/2027	-	0/0
27	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00	5,174.30	158.11	-	03/2028	-	0/0
28	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00	692.43	-	-	03/2028	-	0/0
29	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE <u>Southern Railway</u>	04/2013	296.00	466.65	-	-	03/2028	-	0/0
30	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR, MULTI STATE	04/2007	270.14	749.40	591.35	-	03/2022	-	0/0
31	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41	591.00	430.16	-	03/2022	-	0/0
32	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR, KERALA	02/2015	1,431.90	1,431.90	942.65	-	03/2024	-	0/0
33	KUMBALAM-TURAVUR - [N22000191]SR, KERALA	04/2011	252.96	709.69	256.71	-	03/2025	-	0/0
34	ERNAKULAM-KUMBALAM - [N22000204]SR, KERALA	04/2010	189.24	448.10	268.74	-	03/2025	-	0/0
35	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR, KERALA	02/2015	1,000.00	1,339.00	.83	-	03/2025	-	0/0

Costing Rs. 150 Crore and above						(February 2022)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	3,444.00	241.49	-	12/2025	-	0/0
37	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	839.01	.63	-	03/2030	-	0/0
	<u>Western Railway</u>								
38	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10	844.10	294.10	-	10/2025	-	0/0
	Total		24,103.86	46,658.26	17,811.02				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
	<u>(State Pwds)</u>								
39	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05	291.05	252.61	-	02/2022	-	0/0
40	4 LANEING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89	243.89	229.09	-	02/2022	-	0/0
41	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51	390.51	306.63	-	03/2022	-	0/0
42	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98	773.98	400.90	-	03/2022	-	0/0
43	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95	819.95	410.10	-	03/2022	-	0/0
44	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	137.90	-	03/2022	-	0/0
45	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45	319.96	126.00	-	03/2022	-	0/0
46	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44	388.44	199.61	-	06/2022	-	0/0
47	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81	225.81	112.51	-	09/2022	-	0/0
48	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66	356.66	132.98	-	09/2022	-	0/4

Costing Rs. 150 Crore and above						(February 2022)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
49	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA <u>National Highways And Infrastructure Development Corporation Ltd.</u>	03/2016	1,101.58 -	1,101.58	334.55	- -	03/2023	-	0/0
50	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	217.41	- -	03/2022	-	3/4
51	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	520.71	- -	03/2022	-	2/4
52	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	568.92	360.28	- -	03/2022	-	0/0
53	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	101.99	- -	04/2022	-	3/4
54	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	128.67	- -	12/2022	-	3/4
55	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	188.78	129.11	- -	12/2022	-	3/4
56	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	375.80	81.82	- -	04/2023	-	2/4
57	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM <u>National Highways Authority Of India</u>	10/2017	818.00 -	818.00	302.72	- -	04/2023	-	2/4
58	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	720.08	- -	02/2022	-	0/0
59	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	415.26	- -	02/2022	-	0/0
60	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	1,148.65	- -	03/2022	-	0/0

Costing Rs.		150	Crore and above			(February 2022)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	1,518.41	- -	03/2022	-	0/0
62	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	352.62	- -	03/2022	-	4/4
63	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	417.51	294.69	- -	03/2022	-	0/0
64	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	432.74	- -	03/2022	-	0/1
65	FOUR LANING OF MADURAI-CHETTICULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	411.17	- -	03/2022	-	0/0
66	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	856.33	- -	04/2022	-	0/0
67	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	752.28	289.28	- -	05/2022	-	0/1
68	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	05/2022	-	0/0
69	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97 -	1,094.97	897.00	- -	05/2022	-	3/4
70	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	290.00	- -	06/2022	-	0/0
71	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	953.09	514.05	- -	06/2022	-	0/0
72	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	359.38	- -	06/2022	-	0/0
73	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	254.00	- -	06/2022	-	0/0
74	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	503.88	158.96	- -	06/2022	-	0/0

Costing Rs. 150 Crore and above						(February 2022)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	85.61	-	06/2022	-	0/0
76	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11	806.11	450.59	-	06/2022	-	0/0
77	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88	743.89	557.00	-	06/2022	-	1/3
78	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96	884.00	671.00	-	10/2022	-	2/4
79	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98	840.00	470.00	-	11/2022	-	2/4
80	FOUR LANINIG OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35	505.35	255.05	-	12/2022	-	0/0
81	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92	1,071.00	383.75	-	12/2022	-	0/0
82	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68	633.68	200.00	-	03/2023	-	0/1
83	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00	999.00	221.63	-	03/2023	-	0/0
	Total		29,467.77	30,540.10	17,039.01				30/54
	URBAN DEVELOPMENT								
	National Building Construcion Corporation Ltd								
84	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00	2,694.00	1,034.98	-	03/2023	-	0/9
	Total		2,694.00	2,694.00	1,034.98				0/9
	Grand Total		56,866.65	80,493.38	36,423.48				32/65

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above					(February 2022)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
	<u>Airport Authority Of India Limited</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT - [N04000084]AAI, TRIPURA	09/2015	438.28 -	06/2019 12/2021	12/2021
	Total		438.28 -		
	<u>COAL</u>				
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OCP EXPANSION PH III - [N06000225]MCL, ODISHA	08/2008	228.08 -	03/2012 -	03/2012
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC, ODISHA	07/2017	2,401.07 -	01/2027 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT (1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-
7	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
	<u>Singareni Colliers Company Limited</u>				
9	RCE OF KALYANIKHANI OPENCAST PROJECT - [N06000213]SCCL, TELANGANA	03/2016	384.32 -	03/2020 -	03/2020
10	RCE OF KAKATHIYAKHANI OC - 2 PROJECT - [N06000214]SCCL, TELANGANA	08/2017	442.42 -	03/2020 -	03/2020
11	RCE OF INDARAM OPENCAST PROJECT - [N06000211]SCCL, TELANGANA	08/2017	349.28 -	03/2021 -	03/2021
12	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II - [N06000212]SCCL, TELANGANA	03/2019	473.22 -	03/2021 -	03/2021
13	RCE OF KISTARAM OPENCAST PROJECT - [N06000215]SCCL, TELANGANA	03/2017	164.04 -	03/2021 -	03/2021
	<u>South-Eastern Coal Fields Limited</u>				
14	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL, MADHYA PRADESH	12/2014	357.80 -	03/2021 -	-
	Total		16,052.32 -		
	<u>FINANCE</u>				

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Cpwd For Finance</u>				
15	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD FOR FINANC,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
16	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD FOR FINANC,TAMIL NADU	11/2017	348.77 -	11/2021 -	11/2021
	Total		557.77 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
17	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	11/2019 -	01/2022
	Total		215.92 -		
	<u>PETROLEUM</u>				
	<u>Hindustan Petroleum Corporation Limited</u>				
18	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26 -	07/2020 -	01/2022
19	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	12/2021
	<u>Indian Oil Corporation Limited</u>				
20	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 319.61	06/2020 12/2021	12/2021
21	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	Total		1,446.66 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 -	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
24	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	07/2012 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 04/2019	-
	<u>Power Grid Corporation Of India Limited</u>				
26	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT - [N18000301]PGCIL,GUJARAT	10/2019	1,031.00 -	08/2021 -	08/2021
27	NORTHERN REGION SYSTEM STRENGTHENING - XL - [N18000308]PGCIL,MULTI STATE	02/2019	572.98 -	12/2020 -	12/2020

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
28	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	08/2013 -	03/2018
	Total		24,430.75 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
29	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Cpwd For Health</u>				
30	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD FOR HEALTH,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
31	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD FOR HEALTH,KERALA	09/2017	150.29 -	03/2020 -	12/2021
	<u>Hll Infra Tech Services Limited</u>				
32	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	-
33	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	-
34	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 890.14	05/2021 -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
35	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
36	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
37	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	04/2020
38	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	01/2021
39	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
40	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	02/2021
41	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	04/2021
42	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	05/2021
43	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	05/2021
44	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	12/2021
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	12/2021
48	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	- -	12/2021
49	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	12/2021
50	GERIATRICS BLOCK- AIIMS DELHI - [N21000019]HSCC, DELHI	12/2017	156.56 -	- -	01/2022
	Total		7,693.25 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
51	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR, MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
52	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
53	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
54	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 28,181.00	- 06/2022	-
55	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 72,785.00	03/2020 06/2022	-
	<u>East Central Railways</u>				
56	HAJIPUR - BACHAWARA - [N22000334]ECR, MULTI STATE	05/2015	678.54 -	03/2019 -	12/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
57	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
58	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
59	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
	<u>North East Frontier Railway</u>				
60	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
61	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 -	03/2021 -	-
62	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
64	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
65	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021
66	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
67	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
68	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
69	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
	<u>Northern Railway</u>				
70	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
71	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
72	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 12/2022	-
	<u>South Central Railway</u>				
73	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
74	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	-
	<u>Southern Railway</u>				
75	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
76	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
	<u>Western Railway</u>				
77	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
78	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
79	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
	Total		60,231.45 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
80	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	01/2021
81	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	01/2021
82	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	- -	01/2022
83	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.22	08/2017 -	02/2020
84	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	03/2021
85	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 -	05/2021
86	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 -	06/2021
87	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 -	11/2020 -	06/2021
88	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
89	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 -	07/2021
90	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 -	07/2021
91	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 -	07/2021
92	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	12/2019 -	08/2021
93	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	02/2020 -	09/2021
94	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND	12/2016	196.00 -	09/2021 -	09/2021
95	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	03/2027 -	09/2021
96	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 -	10/2020
97	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- -	10/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
98	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 -	11/2019 -	10/2021
99	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL- DUNGARPUR-HIRATA - VARDA-SAGWARA) SECTION OF NH-927A. PKG- - [N24001413]MoRTH,RAJASTHAN	02/2021	240.99 -	11/2021 -	11/2021
100	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 -	12/2020
101	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 -	12/2021
102	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 -	12/2021
103	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	12/2021
104	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	09/2020 -	12/2021
105	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	06/2019
106	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	06/2019
107	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	07/2019
108	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	09/2019
109	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	11/2019
110	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	11/2019
111	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	12/2019
112	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	12/2019
113	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	12/2019
114	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- 02/2019	01/2020
115	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	01/2020
116	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	01/2020
117	AMD I TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	02/2020
118	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	03/2020
119	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	03/2020

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
120	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 2,617.44	03/2020 -	03/2020
121	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	08/2020
122	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	09/2020
123	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	09/2020
124	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	09/2020
125	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	09/2020
126	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	10/2020
127	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 1,428.09	03/2020 -	10/2020
128	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	11/2020
129	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	11/2020
130	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	11/2020
131	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	11/2020
132	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	11/2020
133	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	11/2020
134	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 -	09/2019 -	11/2020
135	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	12/2020
136	NAGAJ TO VAIJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	12/2020
137	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	12/2020
138	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	12/2020
139	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	12/2020
140	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	12/2020
141	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	12/2020
142	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	01/2021
143	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	01/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
144	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	03/2021
145	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	03/2021
146	BAMNI TO NAVEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	03/2021
147	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	04/2021
148	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	06/2021
149	DHANGIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	06/2021
150	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 1,907.03	- -	07/2021
151	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	07/2021
152	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	07/2021
153	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	07/2021
154	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	07/2021
155	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	08/2021
156	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	09/2021
157	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	11/2021
158	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	11/2021
159	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	12/2021
160	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	12/2021
161	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- -	12/2021
162	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	02/2020 -	01/2022
163	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
164	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]MoRTH,TELANGANA	10/2014	295.47 -	02/2017 -	-
165	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
166	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
167	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
168	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
169	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 1,109.88	03/2011 12/2022	-
170	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 374.59	10/2010 12/2022	-
171	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
172	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
173	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
174	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 434.65	10/2010 12/2022	-
175	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
176	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
177	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
178	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
179	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
180	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
181	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
182	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
183	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
184	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
185	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH.0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 01/2021	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
186	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	08/2018 07/2022	-
187	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 234.73	08/2018 08/2022	-
188	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 504.00	11/2018 02/2022	-
189	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
190	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
191	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
192	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
193	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 386.99	08/2018 02/2022	-
194	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH	01/2017	576.48 686.13	01/2018 10/2022	-
195	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
196	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
197	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
198	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
199	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
200	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
201	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
202	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
203	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
204	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
205	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
206	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
207	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
208	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
209	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
210	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
211	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
212	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
213	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
214	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
215	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
216	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
217	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
218	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHAARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
219	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
220	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
222	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
223	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
224	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
225	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
226	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
227	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
228	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 187.61	05/2019 -	-
229	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	12/2020 12/2021	-
230	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	12/2020 12/2021	-
231	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	11/2020 04/2022	-
232	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 03/2022	-
233	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
234	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
235	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]MoRTH,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
236	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 -	06/2019 -	-
237	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN	03/2020	370.36 -	08/2022 -	-
238	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	08/2020 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
239	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	11/2020 -	-
240	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	-
241	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	03/2027 -	-
242	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	03/2027 -	-
243	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	03/2027 -	-
244	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	03/2027 -	-
245	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	03/2027 -	-
246	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	03/2027 -	-
247	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	03/2027 -	-
248	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	03/2027 -	-
249	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
250	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
251	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH	06/2020	437.60 -	03/2027 -	-
252	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH	06/2020	496.47 -	03/2027 -	-
253	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	-
254	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	-
255	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	-
256	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	-
258	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I. - [N24001409]MoRTH,RAJASTHAN	07/2020	319.09 -	09/2021 -	-
259	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II - [N24001410]MoRTH,RAJASTHAN	08/2020	216.72 -	12/2020 -	-
260	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I. - [N24001411]MoRTH,RAJASTHAN	12/2020	379.23 -	10/2021 -	-
261	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II. - [N24001412]MoRTH,RAJASTHAN	12/2020	339.65 -	10/2021 -	-
262	REHABILITATION AND UPGRADE TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K - [N24001422]MoRTH,HIMACHAL PRADESH	02/2021	345.89 -	09/2021 -	-
263	REHABILITATION UPGRADE OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 05/2022	07/2021
National Highways And Infrastructure Development Corporation Ltd.					
264	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA	06/2020	347.36 -	01/2022 -	01/2022
265	REHABILITATION AND UPGRADE OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA	06/2020	277.50 -	01/2022 -	01/2022
266	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA	06/2020	201.99 -	01/2022 -	01/2022
267	STRENGTHENING OF CHURAIBARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL,TRIPURA	06/2020	257.96 -	01/2022 -	01/2022
268	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
269	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	03/2021
270	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
271	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
272	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	09/2021
273	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	10/2021
274	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	10/2018 -	10/2021
275	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	- -	10/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
276	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM	03/2015	168.39 -	11/2018 -	11/2021
277	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL, NAGALAND	03/2018	237.72 -	09/2018 -	11/2021
278	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL, NAGALAND	03/2018	251.97 -	09/2018 -	11/2021
279	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL, NAGALAND	03/2018	282.98 -	09/2018 -	11/2021
280	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM	06/2015	437.39 -	06/2018 -	12/2021
281	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	06/2018 -	12/2021
282	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	-	12/2021
283	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	09/2018 -	12/2021
284	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	09/2018 -	12/2021
285	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	09/2018 -	12/2021
286	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL, NAGALAND	03/2020	330.78 -	12/2021 -	12/2021
287	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL, NAGALAND	04/2020	330.80 -	12/2021 -	12/2021
288	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL, ASSAM	03/2017	1,049.51 -	-	12/2021
289	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL, TRIPURA	10/2014	369.00 -	03/2018 -	-
290	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL, SIKKIM	04/2017	388.00 -	10/2017 -	-
291	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL, SIKKIM	03/2018	264.84 -	06/2018 -	-
	<u>National Highways Authority Of India</u>				
292	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 -	-	01/2021
293	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022
294	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	01/2022

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
295	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	02/2018
296	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	02/2018
297	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
298	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
299	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	05/2017
300	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021
301	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
302	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	06/2021
303	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021
304	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 1,182.87	- -	07/2021
305	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2019
306	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
307	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	09/2021
308	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 2,408.72	04/2019 -	09/2021
309	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021
310	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	09/2021
311	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021
312	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	10/2021
313	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
314	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	11/2018
315	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021
316	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	11/2021
317	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
318	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	12/2020
319	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021
320	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021
321	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021
322	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	12/2021
323	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	12/2021
324	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021
325	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	12/2021
326	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021
327	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	01/2016
328	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 2,262.00	01/2019 -	01/2019
329	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
330	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 414.00	05/2018 11/2020	11/2020
331	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 09/2021	09/2021
332	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 1,418.78	03/2019 10/2021	10/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
333	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 2,421.37	- 12/2021	12/2021
334	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 01/2022	01/2022
335	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 01/2022	01/2022
336	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
337	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
338	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
339	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
340	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
341	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
342	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
343	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
344	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
345	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
346	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
347	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
348	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
349	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
350	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
351	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
352	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-
353	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
354	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
355	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
356	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
357	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 2,047.64	03/2013 06/2021	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
358	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
359	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
360	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
361	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
362	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
363	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
364	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
365	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
366	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
367	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 503.36	09/2016 -	-
368	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
369	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 416.00	- -	-
370	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	991.59 -	06/2018 -	-
371	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
372	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
373	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
374	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
375	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 1,414.01	06/2018 -	-
376	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-
377	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-
378	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
379	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
380	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
381	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 03/2021	-
382	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
383	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
384	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
385	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
386	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
387	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
388	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
389	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
390	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	-
391	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
392	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
393	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
394	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
395	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	-
396	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
397	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
398	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
399	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
400	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
401	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
402	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
403	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
404	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
405	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-

Costing Rs. 150 Crore and above

(February 2022)

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
406	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
407	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
408	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
409	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
410	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-
411	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-
412	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-
413	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI, UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
414	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	-
415	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	- -	-
416	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
417	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
418	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI, JHARKHAND	08/2016	323.72 -	08/2018 -	-
419	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21 (PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
420	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL	09/2016	767.03 -	08/2018 -	-
421	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209 (EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	08/2019 -	-
422	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
423	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
424	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
425	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
426	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
427	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
428	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
429	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
430	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
431	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
432	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 01/2022	-
433	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
434	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
435	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
436	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
437	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
438	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	-
439	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
440	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
441	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 1,140.64	10/2017 -	-
442	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
443	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
444	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGOUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
445	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
446	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
447	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
448	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
449	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
450	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
451	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
452	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
453	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
454	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
455	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
456	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
457	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
458	FOUR LANING OF KHAMMAM-DEVARAPALLE SECTION (GREENFIELD) - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
459	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
460	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
461	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
462	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
463	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
464	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
465	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
466	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
467	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
468	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	-
469	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
470	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
471	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
472	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
473	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
474	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
475	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
476	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
477	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
478	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
479	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 1,140.50	- 03/2021	-
480	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- 08/2023	-
481	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
482	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
483	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
484	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
485	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
486	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
487	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- 11/2022	-
488	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
489	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 570.98	01/2020 08/2021	-
490	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 655.64	02/2019 04/2021	-
491	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 1,240.13	02/2021 04/2021	-
492	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
493	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
494	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
495	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
496	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	-
497	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
498	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 -	11/2019 -	-
499	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 -	11/2019 -	-
500	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 -	11/2019 -	-
501	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 2,501.85	- 02/2022	-
	Total		2,78,989.57 -		
	URBAN DEVELOPMENT				
	Chennai Metro Rail Ltd				

Costing Rs. 150 Crore and above					(February 2022)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
502	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
503	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 02/2021	-
	<u>Delhi Metro Rail Corporation</u>				
504	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 08/2021	-
505	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	12/2020 09/2021	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
506	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	09/2020
	Total		62,701.79 -		
	<u>WATER RESOURCES</u>				
	<u>Brahmaputra Board</u>				
507	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	-
	<u>Delhi Jal Board</u>				
508	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	Total		578.38 -		
	<u>COMMERCE</u>				
	<u>Nbcc For Commerce</u>				
509	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC FOR COMMER,DELHI	06/2018	302.64 -	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Central Public Works Department</u>				
510	C/O ADDITIONAL INFRASTRUCTURE AT IISC, BANGALORE.SH- RCC MONOLITHIC FOR MEN HOSTEL(S 14), WOMEN HOST - [N42000010]CPWD,KARNATAKA	08/2021	316.25 -	11/2021 -	-
	<u>Cpwd Of Higher Education</u>				
511	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD EDUCATION,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	07/2021
512	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD EDUCATION,MAHARASHTRA	01/2018	223.37 -	07/2020 -	12/2021
513	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD EDUCATION,RAJASTHAN	12/2016	549.31 559.49	07/2019 07/2021	07/2021

Costing Rs. 150 Crore and above					(February 2022)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
514	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD EDUCATION,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 11/2021	11/2021
515	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD EDUCATION,KERALA	01/2010	165.23 -	10/2012 -	-
	Total		1,710.99 -		
	<u>DPIIT</u>				
	<u>Dmic For Dpiit</u>				
516	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC FOR DPIIT,MULTI STATE	09/2011	12,579.09 -	09/2019 -	07/2021
	Total		12,579.09 -		
	<u>DONER</u>				
	<u>Hscl For Doner</u>				
517	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL FOR DONER,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
	Total		151.33 -		
	<u>RENEWABLE ENERGY</u>				
	<u>Cpwd For Renewable Energy</u>				
518	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD R ENERGY,DELHI	10/2017	271.90 -	11/2019 -	-
	Total		271.90 -		
	Grand Total		4,70,070.09		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(February 2022)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	6,840.00	6,268.20	09/2010 -	10/2022	145	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 19,220.00	19,220.00	17,806.00	12/2015 -	12/2022	84	-
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	30,143.00	11/2020 -	11/2023	36	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 17,079.00	17,079.00	14,142.00	12/2016 -	12/2023	84	-
	Total		67,120.00 -	82,988.00	68,359.20				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 -	1,938.00	579.75	09/2021 -	12/2023	27	-
	Total		1,383.00 -	1,938.00	579.75				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	288.42	05/2014 -	03/2022	94	-
7	2.0 MTPA BHOJDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13 -	341.22	91.55	03/2017 -	12/2022	69	-
8	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2023	24	-
9	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 -	334.27	32.60	04/2018 -	06/2023	62	-
10	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	515.18	03/2019 -	04/2024	61	-
11	MURAIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	91.62	04/2014 -	10/2025	138	-
	<u>Central Coal Fields Limited</u>								
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	124.86	03/2011 -	03/2023	144	-
13	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	502.12	03/2016 -	03/2023	84	-
14	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	98.68	03/2014 -	03/2023	108	-
	<u>Eastern Coal Fields Limited</u>								
15	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73 -	5,146.48	625.60	08/2019 -	08/2024	60	-
	<u>Mahanadi Coal Fields Limited</u>								

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	808.97	815.72	03/2013 -	03/2024	132	-
17	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	254.83	03/2019 -	03/2024	60	-
18	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	710.64	03/2021 -	03/2026	60	-
	<u>Neyveli Lignite Corporation</u>								
19	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	13,185.30	11/2021 -	06/2023	19	-
20	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	709.06	496.44	06/2015 -	09/2027	147	-
	<u>Northern Coal Fields Limited</u>								
21	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	954.78	03/2021 -	03/2023	24	-
22	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	584.00	03/2022 -	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
23	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73 -	272.73	153.75	03/2018 -	03/2022	48	-
	<u>South-Eastern Coal Fields Limited</u>								
24	JAGANNATHPUR OC RCE (3.0 MTY) - [N06000232]SECL, CHHATISGARH	07/2016	459.49 -	459.49	-	03/2020 -	03/2022	24	-
25	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	224.43	03/2014 -	03/2023	108	-
26	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	335.97	48.36	03/2018 -	03/2023	60	-
27	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL, CHHATISGARH	07/2015	316.10 -	316.10	152.47	03/2020 -	03/2023	36	-
28	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04 -	371.04	79.50	03/2021 -	03/2024	36	-
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL, CHHATISGARH	12/2013	610.63 -	610.63	179.09	03/2022 -	03/2025	36	-
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL, MADHYA PRADESH	03/2016	869.44 -	869.44	137.22	03/2021 -	03/2025	48	-
31	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	9.23	03/2014 -	03/2026	144	-
	<u>Western Coal Fields Limited</u>								
32	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 299.67	299.67	213.93	03/2019 -	03/2022	36	-
33	UKNI DEEP OC - [N06000179]WCL, MAHARASHTRA	11/2018	318.14 -	318.14	226.62	03/2021 -	09/2022	18	-
34	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL, MULTI STATE	02/2017	328.00 -	328.00	298.48	03/2021 -	09/2023	30	-
35	BHATADI EXPASION OC (0.975 MTY) - [N06000234]WCL, MAHARASHTRA	02/2016	327.41 -	327.41	-	03/2019 -	09/2026	90	-
	Total		35,532.74 -	37,731.09	21,101.29				
	<u>MINES</u>								
	<u>Central Public Works Department</u>								

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
36	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA - [N10000015]CPWD, WEST BENGAL	04/2019	255.37 -	255.37	1.16	04/2022 -	10/2024	30	-
	Total		255.37 -	255.37	1.16				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
37	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	21,940.00	19,611.48	05/2015 01/2022	06/2022	85	5
38	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC, CHHATISGARH	11/2015	2,907.00 -	2,907.00	636.12	06/2023 -	06/2024	12	-
	<u>Steel Authority Of India Limited (Sail)</u>								
39	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	212.42	06/2019 02/2022	05/2022	35	3
40	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	572.49	10/2017 12/2021	11/2022	61	11
	Total		19,728.88 -	26,143.88	21,032.51				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
41	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	640.00	380.90	12/2021 -	06/2022	6	-
42	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	66	-
43	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	248.55	149.47	06/2022 -	09/2022	3	-
44	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 -	1,507.24	855.28	06/2019 -	02/2023	44	-
45	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	291.62	02/2021 -	03/2023	25	-
46	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha - [N16000374]BPCL, ODISHA	08/2019	1,607.00 -	1,607.00	338.29	08/2022 -	06/2023	10	-
	<u>Gas Authority Of India Limited</u>								
47	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL, MULTI STATE	07/2015	2,881.40 -	2,000.00	1,661.00	12/2020 -	03/2022	15	-
48	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL, HARYANA	08/2018	286.42 327.00	327.01	233.20	08/2020 12/2021	04/2022	20	4
49	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	220.00	200.10	04/2018 -	06/2022	50	-
50	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL, MULTI STATE	03/2017	2,433.00 -	2,433.00	2,209.40	12/2020 12/2021	06/2022	18	6
51	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL, MULTI STATE	03/2017	3,437.00 -	3,048.00	2,271.40	12/2020 12/2021	06/2022	18	6

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,620.10	12/2020 12/2021	07/2022	19	7
53	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	247.90	120.91	02/2021 -	10/2022	20	-
54	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 -	217.92	106.90	04/2021 03/2022	10/2022	18	7
55	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	983.90	12/2020 12/2021	06/2023	30	18
56	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	3,060.00	2,727.90	12/2021 -	06/2023	18	-
57	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 -	243.53	167.21	07/2022 -	08/2023	13	-
58	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20 -	182.20	101.14	07/2022 -	08/2023	13	-
59	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]GAIL,JHARKHAND	10/2017	221.45 -	221.45	113.23	10/2022 -	08/2023	10	-
60	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	359.25	200.37	10/2022 -	10/2023	12	-
61	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,781.00	12/2012 02/2022	02/2025	146	36
<u>Hindustan Petroleum Corporation Limited</u>									
62	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	212.46	06/2020 -	03/2022	21	-
63	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	136.30	06/2020 -	03/2022	21	-
64	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH	10/2020	210.94 -	210.94	130.17	08/2021 -	03/2022	7	-
65	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH	07/2016	20,928.00 -	26,264.00	18,232.09	07/2020 -	07/2022	24	-
66	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE	09/2017	2,677.00 -	3,072.00	2,730.95	06/2021 -	07/2022	13	-
67	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA	09/2018	520.00 -	520.00	215.09	09/2026 -	02/2027	5	-
68	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	621.42	03/2029 -	08/2029	5	-
69	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL,WEST BENGAL	03/2019	5,830.20 -	5,830.20	174.36	03/2031 -	08/2031	5	-
<u>Indian Oil Corporation Limited</u>									
70	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	315.00	232.78	12/2021 -	02/2022	2	-
71	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	609.43	07/2018 05/2021	03/2022	44	10

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
72	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	304.44	10/2020 -	03/2022	17	-
73	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	185.52	01/2021 06/2021	03/2022	14	9
74	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,315.92	03/2021 12/2021	05/2022	14	5
75	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	4,270.46	12/2018 02/2022	06/2022	42	4
76	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	914.85	10/2021 -	06/2022	8	-
77	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	1,945.00	1,657.30	02/2022 -	07/2022	5	-
78	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	376.32	02/2020 10/2021	07/2022	29	9
79	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	226.74	01/2021 -	08/2022	19	-
80	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	551.04	01/2021 03/2022	08/2022	19	5
81	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	45.60	07/2021 03/2022	08/2022	13	5
82	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	1,012.58	08/2020 04/2022	09/2022	25	5
83	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	152.91	10/2021 03/2022	09/2022	11	6
84	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	106.27	02/2020 06/2021	10/2022	32	16
85	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	207.36	135.65	04/2020 10/2021	10/2022	30	12
86	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	154.50	08/2020 03/2022	10/2022	26	7
87	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 1,236.00	1,236.00	568.65	10/2017 03/2022	12/2022	62	9
88	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	71.65	12/2019 03/2022	01/2023	37	10
89	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	135.36	04/2022 -	02/2023	10	-
90	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	167.00	22.01	07/2022 -	02/2023	7	-
91	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	101.10	- 05/2022	03/2023	-	10

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
92	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	139.54	04/2022 -	08/2023	16	-
93	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.70	09/2023 -	02/2024	5	-
94	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	1,398.00	164.75	12/2023 -	02/2024	2	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
95	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,809.28	12/2019 04/2021	03/2022	27	11
	<u>Oil & Natural Gas Corporation Limited</u>								
96	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA	06/2019	2,494.68 -	2,354.72	1,824.00	03/2022 -	03/2023	12	-
97	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	650.82	457.24	03/2019 09/2021	05/2023	50	20
	<u>Oil India Limited</u>								
98	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	340.00	287.12	10/2020 -	03/2022	17	-
99	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	510.00	494.68	12/2019 -	03/2022	27	-
100	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	638.60	412.80	02/2020 -	06/2022	28	-
	Total		86,613.20 -	98,286.46	60,731.79				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
101	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	4,287.59	670.22	- 08/2024	07/2025	-	11
	<u>National Thermal Power Corporation</u>								
102	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 19,413.00	17,304.00	16,748.00	05/2018 -	03/2022	46	-
103	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	524.83	400.95	09/2021 -	03/2022	6	-
104	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	702.28	609.51	03/2021 12/2021	03/2022	12	3
105	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	1,749.31	1,362.64	09/2021 -	03/2022	6	-
106	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	852.90	596.05	09/2021 -	05/2022	8	-
107	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	442.03	293.40	04/2021 -	05/2022	13	-
108	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	403.62	123.49	06/2021 01/2022	07/2022	13	6
109	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	1,316.22	948.04	09/2021 -	08/2022	11	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,803.19	612.20	09/2021 -	10/2022	13	-
111	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	293.03	118.68	10/2021 -	10/2022	12	-
112	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	382.22	8.24	03/2022 -	10/2022	7	-
113	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,998.00	9,223.00	11/2020 07/2022	02/2023	27	7
114	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 17,007.00	17,007.00	12,634.00	06/2019 10/2022	01/2024	55	15
115	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	5,867.38	5,247.00	03/2013 12/2021	12/2024	141	36
116	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,667.00	5,021.00	03/2023 -	02/2025	23	-
117	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,803.00	754.00	09/2019 12/2024	07/2025	70	7
	<u>Power Grid Corporation Of India Limited</u>								
118	WESTERN REGION SYSTEM STRENGTHENING - XX - [N18000310]PGCIL,MULTI STATE	07/2019	226.98 -	226.98	-	08/2021 -	02/2022	6	-
119	SOUTHERN REGION SYSTEM STRENGTHENING - XXV - [N18000311]PGCIL,MULTI STATE	07/2019	154.72 -	154.72	-	07/2021 -	02/2022	7	-
120	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN - [N18000312]PGCIL,RAJASTHAN	08/2019	2,578.47 -	2,578.47	-	12/2020 -	02/2022	14	-
121	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII - [N18000318]PGCIL,MULTI STATE	09/2018	221.36 -	221.36	-	03/2021 -	02/2022	11	-
122	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	262.29	05/2020 -	02/2022	21	-
123	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	546.36	480.89	11/2016 -	03/2022	64	-
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.97	03/2018 -	03/2022	48	-
125	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	580.89	05/2017 -	03/2022	58	-
126	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	159.02	06/2019 -	03/2022	33	-
127	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS - [N18000309]PGCIL,MULTI STATE	11/2018	496.11 -	496.11	-	06/2020 -	03/2022	21	-
128	NORTH EASTERN REGION STRENGTHENING SCHEME - III - [N18000313]PGCIL,MULTI STATE	09/2015	167.31 -	167.31	-	12/2017 -	03/2022	51	-
129	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA - [N18000314]PGCIL,RAJASTHAN	01/2020	562.86 -	562.86	-	01/2021 -	03/2022	14	-
130	EASTERN REGION STRENGTHENING SCHEME - XXIII - [N18000315]PGCIL,MULTI STATE	07/2020	239.89 -	239.89	-	06/2021 -	03/2022	9	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	205.65	02/2019 -	04/2022	38	-
132	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	251.70	12/2019 -	04/2022	28	-
133	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,099.43	07/2020 -	04/2022	21	-
134	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION - [N18000317]PGCIL,MULTI STATE	11/2018	241.38 -	241.38	-	11/2021 -	05/2022	6	-
135	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 -	219.66	169.82	07/2019 -	08/2022	37	-
136	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	2,635.55	1,832.15	02/2020 -	04/2023	38	-
137	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,700.00	3,522.04	12/2018 -	01/2024	61	-
138	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,129.32	3,182.67	12/2018 -	03/2024	63	-
	<u>Satluj Jal Vidyut Nigam Limited</u>								
139	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	820.12	12/2021 -	06/2022	6	-
	<u>Thdc India Limited</u>								
140	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21 -	1,587.16	663.84	09/2020 -	08/2022	23	-
141	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 -	4,825.60	4,409.29	02/2016 -	06/2023	88	-
142	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	3,654.43	09/2023 -	08/2024	11	-
	Total		1,12,767.26 -	1,32,856.17	78,755.62				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Cpwd For Health</u>								
143	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD FOR HEALTH,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
144	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD FOR HEALTH,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hospital Services Consultancy Corporation Ltd</u>								
145	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	274.40	05/2018 -	06/2022	49	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Nbcc For Health</u>								
146	AIIMS BILASPUR - [N21000028]NBCC FOR HEALTH,HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	1,089.38	09/2021 -	06/2022	9	-
	Total		2,169.99 -	2,289.99	1,405.57				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
147	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,921.95	03/2021 -	03/2023	24	-
148	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	1,387.52	358.30	03/2021 -	03/2023	24	-
149	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	1,283.49	524.21	03/2022 -	03/2023	12	-
150	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	540.02	355.54	03/2022 -	03/2024	24	-
151	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	2,449.91	488.43	03/2023 -	03/2024	12	-
152	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	1,035.16	322.26	03/2022 -	03/2024	24	-
153	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	637.95	239.26	03/2023 -	03/2024	12	-
	<u>East Central Railways</u>								
154	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	347.96	03/2019 -	03/2022	36	-
155	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	581.48	03/2020 -	03/2023	36	-
156	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	1,059.76	03/2020 -	05/2023	38	-
157	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 967.29	1,090.00	1,093.59	03/2012 -	06/2023	135	-
158	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,570.66	03/2020 -	03/2024	48	-
159	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 1,185.73	1,185.73	452.12	03/2021 -	03/2024	36	-
160	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00 -	819.01	540.73	03/2020 -	12/2024	57	-
161	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 1,215.54	1,215.54	585.85	03/2021 -	12/2024	45	-
	<u>East Coast Railway</u>								
162	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,243.24	02/2019 -	03/2022	37	-
163	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	324.59	10/2020 -	03/2024	41	-
164	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 -	1,160.83	1,036.36	03/2020 03/2023	03/2024	48	12
165	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	758.80	03/2022 03/2023	03/2024	24	12
166	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	734.63	12/2018 -	03/2024	63	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,791.66	1,729.29	03/2009 -	12/2024	189	-
168	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	947.41	06/2021 -	03/2025	45	-
169	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	209.78	11/2018 -	03/2025	76	-
	<u>Eastern Railways</u>								
170	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	502.48	529.13	- 09/2021	02/2022	-	5
171	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	995.10	622.26	03/2016 -	03/2024	96	-
172	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,619.48	912.17	03/2019 12/2009	03/2025	72	183
173	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	2,137.81	472.06	03/2022 -	03/2025	36	-
174	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.32	204.40	03/2016 -	03/2025	108	-
175	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	508.16	03/2017 -	03/2025	96	-
	<u>Indian Railway Construction Company Limited</u>								
176	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,800.17	09/2018 -	06/2022	45	-
177	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	1,078.79	03/2022 -	09/2023	18	-
	<u>Metropolitan Rapid Transport Projects</u>								
178	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,868.04	03/2004 -	06/2022	219	-
179	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	774.51	539.14	06/2013 -	12/2022	114	-
	<u>North Central Railway</u>								
180	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	1,080.53	03/2021 -	06/2023	27	-
181	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	534.75	03/2022 -	12/2024	33	-
182	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	89.74	03/2023 -	06/2025	27	-
	<u>North East Frontier Railway</u>								
183	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,646.66	03/2021 -	03/2022	12	-
184	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	708.73	549.81	03/2020 06/2022	09/2022	30	3
185	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,986.82	03/2022 -	03/2023	12	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	14,322.00	12,156.19	03/2011 -	12/2023	153	-
187	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 -	6,527.00	4,766.68	03/2014 -	12/2023	117	-
188	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	8,600.00	2,504.91	12/2015 -	12/2023	96	-
189	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	2,047.51	586.70	03/2019 -	12/2023	57	-
190	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,145.79	937.36	03/2019 -	03/2024	60	-
191	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 -	2,145.00	1,108.94	03/2019 -	03/2024	60	-
192	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	6,663.00	1,534.31	03/2015 -	03/2026	132	-
<u>North Eastern Railway</u>									
193	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	728.92	613.91	01/2019 -	02/2022	37	-
194	AUNRIHAR - JAUNPUR PATCH DOUBLING - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	366.71	345.95	01/2022 -	03/2022	2	-
195	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
196	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	-
197	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
<u>North Western Railway</u>									
198	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	860.41	775.62	02/2019 -	06/2022	40	-
199	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	701.81	342.53	03/2020 -	10/2022	31	-
200	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	435.41	08/2022 -	11/2022	3	-
<u>Northern Railway</u>									
201	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,017.96	883.53	07/2012 -	11/2024	148	-
202	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	-
<u>Rail Vikas Nigam Ltd.</u>									
203	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,189.77	03/2020 -	03/2022	24	-
204	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	619.35	03/2016 -	04/2022	73	-
205	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	2,202.94	03/2020 -	04/2022	25	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
206	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	923.28	995.52	03/2021 -	05/2022	14	-
207	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,993.73	02/2015 -	06/2022	88	-
208	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,633.12	3,925.76	03/2020 -	06/2022	27	-
209	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,367.10	03/2020 -	06/2022	27	-
210	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	2,203.53	1,851.27	12/2020 -	06/2022	18	-
211	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	2,082.46	12/2020 -	09/2022	21	-
212	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	433.00	424.19	03/2009 03/2009	12/2022	165	165
213	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	2,538.01	2,234.42	12/2021 -	12/2022	12	-
214	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,500.00	1,042.79	03/2022 -	12/2022	9	-
215	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]RVNL,TAMIL NADU	02/2015	760.00 -	1,536.00	1,573.37	03/2020 -	12/2022	33	-
216	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,457.79	1,346.71	03/2019 -	03/2023	48	-
217	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,552.26	1,313.06	03/2019 -	03/2023	48	-
218	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]RVNL,TAMIL NADU	02/2015	1,700.00 -	1,305.00	1,137.46	03/2022 -	05/2023	14	-
219	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	1,129.41	03/2023 -	12/2024	21	-
220	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	24,659.00	6,259.16	12/2024 -	03/2025	3	-
221	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,834.54	1,586.17	03/2016 -	07/2025	112	-
222	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
223	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	3,139.94	03/2016 -	03/2026	120	-
224	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	2,139.84	12/2024 -	12/2026	24	-
<u>South Central Railway</u>									
225	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 -	927.94	713.38	03/2020 -	03/2022	24	-
226	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	2,094.82	03/2000 -	03/2023	276	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
227	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	803.75	03/2023 -	03/2024	12	-
228	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,676.08	03/2021 -	03/2024	36	-
229	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,373.74	695.73	03/2010 -	03/2025	180	-
230	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,495.93	03/2022 -	03/2025	36	-
231	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,068.77	03/2009 -	03/2027	216	-
232	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	347.14	03/2014 -	03/2027	156	-
	<u>South East Central Railway</u>								
233	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	1,268.32	1,162.05	02/2019 -	03/2022	37	-
234	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	36	-
	<u>South Eastern Railway</u>								
235	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.97	1,155.00	03/2020 -	06/2022	27	-
236	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509]SER,JHARKHAND	04/2018	390.39 -	511.75	149.63	12/2021 -	01/2023	13	-
237	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	1,153.09	03/2021 -	12/2023	33	-
238	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) - [N22000506]SER,MULTI STATE	03/2019	1,866.31 -	1,866.31	350.68	05/2023 -	12/2023	7	-
239	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510]SER,WEST BENGAL	04/2018	338.00 -	393.83	23.56	06/2022 -	12/2023	18	-
240	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508]SER,JHARKHAND	04/2018	428.65 -	472.50	1.62	06/2022 -	12/2025	42	-
	<u>South Western Railway</u>								
241	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,104.00	1,014.52	03/2020 -	02/2022	23	-
242	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	578.00 -	758.36	674.14	03/2020 -	02/2022	23	-
243	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,954.21	1,238.40	03/2020 -	12/2022	33	-
244	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 -	1,878.00	1,530.18	03/2019 -	02/2024	59	-
245	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	37.12	03/2016 -	03/2024	96	-
246	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	401.14	12/2018 -	06/2025	78	-
247	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2026	120	-
248	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 -	817.23	495.18	03/2017 -	03/2026	108	-
249	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	326.02	03/2016 -	12/2026	129	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
250	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,383.00	7.35	03/2002 -	03/2028	312	-
	<u>Southern Railway</u>								
251	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,549.09	715.89	03/2020 -	03/2025	60	-
252	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	3,081.20	1,726.52	02/2019 -	03/2025	73	-
253	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,111.88	314.32	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
254	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,875.12	1,035.16	03/2022 -	06/2023	15	-
255	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 -	1,247.64	561.88	03/2022 -	12/2023	21	-
256	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,439.82	03/2021 -	03/2024	36	-
257	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 2,445.30	2,445.30	1,392.72	03/2020 -	10/2024	55	-
258	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,908.60	05/2008 -	03/2025	202	-
	<u>Western Railway</u>								
259	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 -	1,383.69	1,250.31	03/2021 -	12/2022	21	-
260	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,016.39	1,056.11	808.35	03/2021 -	12/2022	21	-
261	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 -	603.69	358.78	06/2020 -	03/2023	33	-
262	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	126.35	03/2012 -	10/2023	139	-
263	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 -	2,223.37	1,996.61	03/2020 -	03/2024	48	-
264	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]WR,GUJARAT	04/2017	692.25 -	742.88	2.26	03/2020 -	03/2024	48	-
265	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS - [N22000505]WR,GUJARAT	04/2018	537.31 -	537.31	.64	03/2024 -	12/2024	9	-
266	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	883.21	03/2022 -	03/2025	36	-
267	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	1,378.11	558.66	03/2019 -	03/2025	72	-
268	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	6,383.82	2,404.99	03/2022 -	03/2026	48	-
269	NIMACH BADI SADRI NEW LINE PROJECT - [N22000503]WR,MADHYA PRADESH	04/2017	495.18 -	495.18	.63	03/2022 -	03/2026	48	-
270	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,524.68	1,010.81	03/2022 -	10/2027	67	-
	Total		1,66,859.45 -	2,71,062.94	1,39,778.95				

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
271	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	219.86	07/2018 -	02/2022	43	-
272	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	355.17	269.58	07/2019 -	02/2022	31	-
273	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	211.34	130.63	07/2019 -	02/2022	31	-
274	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	244.93	159.96	05/2020 -	02/2022	21	-
275	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	222.13	156.87	11/2019 -	02/2022	27	-
276	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	338.42	11/2017 -	02/2022	51	-
277	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 354.43	298.33	325.55	- 12/2021	03/2022	-	3
278	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	464.44	01/2020 -	03/2022	26	-
279	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.52	03/2018 -	03/2022	48	-
280	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	174.90	154.26	08/2018 -	03/2022	43	-
281	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	132.76	02/2018 -	03/2022	49	-
282	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	136.22	03/2017 -	03/2022	60	-
283	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	182.97	08/2018 -	03/2022	43	-
284	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	178.31	03/2018 -	03/2022	48	-
285	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	254.17	187.73	02/2018 -	03/2022	49	-
286	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	231.61	03/2018 -	03/2022	48	-
287	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	635.00	07/2018 -	03/2022	44	-

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
288	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	949.54	807.22	06/2019 -	03/2022	33	-
289	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	852.67	225.16	12/2019 -	03/2022	27	-
290	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	391.06	243.68	06/2019 -	03/2022	33	-
291	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	457.52	354.16	07/2019 -	03/2022	32	-
292	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	170.00	121.71	12/2019 -	03/2022	27	-
293	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	228.54	159.32	08/2019 -	03/2022	31	-
294	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	486.19	308.66	07/2019 -	03/2022	32	-
295	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	461.96	326.81	11/2019 -	03/2022	28	-
296	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	415.25	271.38	12/2019 -	03/2022	27	-
297	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	210.81	210.81	07/2019 -	03/2022	32	-
298	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	232.77	151.60	07/2019 -	03/2022	32	-
299	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	344.85	245.82	12/2019 -	03/2022	27	-
300	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	257.38	166.31	12/2019 -	03/2022	27	-
301	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	422.02	302.13	07/2019 -	03/2022	32	-
302	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	181.08	97.86	12/2019 -	03/2022	27	-
303	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	227.19	138.05	12/2019 -	03/2022	27	-
304	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	336.21	224.98	12/2019 -	03/2022	27	-
305	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	238.19	177.80	12/2019 -	03/2022	27	-
306	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	299.92	181.37	08/2020 -	03/2022	19	-
307	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	223.46	68.00	12/2019 -	03/2022	27	-
308	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	509.18	257.83	07/2019 -	03/2022	32	-
309	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	557.20	12/2019 -	03/2022	27	-
310	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	264.41	189.64	03/2019 -	03/2022	36	-
311	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	307.63	190.69	07/2019 -	03/2022	32	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
312	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	218.38	170.80	07/2019 -	03/2022	32	-
313	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	289.11	144.69	09/2018 -	03/2022	42	-
314	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	484.15	343.45	06/2019 -	03/2022	33	-
315	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	355.99	246.86	12/2019 -	03/2022	27	-
316	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	313.58	202.69	04/2020 -	03/2022	23	-
317	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 -	428.55	404.69	03/2018 -	03/2022	48	-
318	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	157.77	03/2021 -	03/2022	12	-
319	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	190.01	04/2020 -	03/2022	23	-
320	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	323.36	222.57	08/2020 -	03/2022	19	-
321	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 544.00	544.00	402.15	09/2016 -	03/2022	66	-
322	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	298.70	01/2018 -	03/2022	50	-
323	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	120.07	05/2019 -	03/2022	34	-
324	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	319.96	193.60	03/2016 -	04/2022	73	-
325	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	67.54	03/2018 -	04/2022	49	-
326	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	228.31	93.73	12/2019 -	04/2022	28	-
327	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	256.15	174.63	12/2019 -	04/2022	28	-
328	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1 - [N24001182]MoRTH,MIZORAM	01/2017	205.95 -	205.95	123.24	01/2021 -	04/2022	15	-

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
329	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	290.07	06/2017 -	04/2022	58	-
330	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	117.71	03/2021 -	04/2022	13	-
331	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 394.44	394.44	188.34	05/2019 -	05/2022	36	-
332	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	373.05	329.89	11/2017 -	05/2022	54	-
333	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	82.99	03/2018 -	06/2022	51	-
334	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	335.69	08/2017 -	06/2022	58	-
335	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	634.32	329.59	05/2020 -	06/2022	25	-
336	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	150.79	59.88	12/2019 -	06/2022	30	-
337	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	422.38	243.81	08/2019 -	06/2022	34	-
338	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	595.77	321.34	08/2019 -	06/2022	34	-
339	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	409.62	283.86	05/2019 -	06/2022	37	-
340	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	420.57	269.24	07/2019 -	06/2022	35	-
341	KAJJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	554.78	304.78	07/2019 -	06/2022	35	-
342	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	304.58	135.51	12/2019 -	06/2022	30	-
343	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	276.95	136.94	12/2019 -	06/2022	30	-
344	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	189.46	107.85	12/2019 -	06/2022	30	-
345	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	456.93	456.93	09/2019 -	06/2022	33	-
346	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	344.25	169.80	08/2020 -	06/2022	22	-
347	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	426.06	219.56	06/2020 -	06/2022	24	-
348	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	294.87	149.16	12/2019 -	06/2022	30	-
349	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	309.94	192.24	12/2019 -	06/2022	30	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
350	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	322.55	191.12	06/2019 -	06/2022	36	-
351	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	467.70	201.73	03/2019 -	06/2022	39	-
352	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	301.39	105.37	03/2018 -	06/2022	51	-
353	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	281.78	74.00	04/2019 -	06/2022	38	-
354	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	406.54	175.24	09/2019 -	06/2022	33	-
355	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	1,202.52	791.90	12/2019 -	06/2022	30	-
356	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	1,598.47	1,054.53	11/2019 -	06/2022	31	-
357	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	162.34	64.74	07/2019 -	06/2022	35	-
358	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	362.96	190.75	06/2019 -	06/2022	36	-
359	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	456.32	330.00	06/2019 -	06/2022	36	-
360	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	337.46	232.56	06/2019 -	06/2022	36	-
361	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	456.45	336.68	06/2019 -	06/2022	36	-
362	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	205.72	85.47	06/2019 -	06/2022	36	-
363	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 255.00	255.00	195.11	06/2021 -	06/2022	12	-
364	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 -	731.50	486.06	10/2016 -	06/2022	68	-
365	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	496.02	251.53	03/2015 -	06/2022	87	-
366	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 913.49	913.49	645.24	11/2018 06/2021	07/2022	44	13
367	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	545.64	195.79	07/2019 -	09/2022	38	-
368	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	313.95	109.24	06/2019 -	09/2022	39	-
369	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	376.19	91.77	05/2019 -	09/2022	40	-
370	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	420.63	200.00	05/2020 -	09/2022	28	-
371	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	407.19	196.83	06/2019 -	09/2022	39	-
372	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	301.38	176.39	08/2020 -	09/2022	25	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
373	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	653.46	284.02	07/2019 -	09/2022	38	-
374	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	488.60	233.89	07/2019 -	09/2022	38	-
375	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	381.77	186.62	06/2019 -	09/2022	39	-
376	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	743.21	350.07	06/2021 -	09/2022	15	-
377	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 2,226.11	983.14	726.13	12/2019 -	09/2022	33	-
378	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	247.25	186.63	03/2019 -	10/2022	43	-
379	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	293.64	261.09	08/2020 -	10/2022	26	-
380	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH	01/2017	263.45 263.45	263.45	122.71	09/2017 05/2022	11/2022	62	6
381	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	936.40	560.12	- 09/2022	12/2022	-	3
382	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	414.81	08/2017 -	12/2022	64	-
383	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 -	396.86	277.42	09/2019 01/2022	12/2022	39	11
384	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 -	426.18	258.00	09/2020 01/2022	12/2022	27	11
385	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	293.10	214.90	08/2020 -	12/2022	28	-
386	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	729.55	10/2019 -	12/2022	38	-
387	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 192.48	170.57	75.41	11/2020 -	12/2022	25	-
388	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	962.43	455.49	03/2018 -	12/2022	57	-
389	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	363.82	73.08	09/2019 -	12/2022	39	-
390	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	237.40	9.66	05/2020 -	12/2022	31	-

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
391	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	537.81	218.73	06/2019 -	12/2022	42	-
392	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	404.33	61.42	05/2020 -	12/2022	31	-
393	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	381.08	9.66	05/2020 -	12/2022	31	-
394	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	341.80	155.96	06/2019 -	12/2022	42	-
395	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	12/2022	37	-
396	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 -	572.66	288.50	08/2016 -	12/2022	76	-
397	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 -	435.61	128.55	07/2016 -	12/2022	77	-
398	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	28.78	05/2021 -	12/2022	19	-
399	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.51	11/2018 03/2022	03/2023	52	12
400	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 -	254.30	118.68	10/2020 12/2021	03/2023	29	15
401	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 -	213.97	27.41	08/2019 11/2022	03/2023	43	4
402	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 -	263.26	78.56	08/2019 08/2022	03/2023	43	7
403	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	11.71	03/2021 -	03/2023	24	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
404	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	389.26	05/2018 -	03/2022	46	-
405	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	110.95	12/2018 -	03/2022	39	-
406	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	229.26	01/2016 -	03/2022	74	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
407	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	141.40	01/2016 -	03/2022	74	-
408	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	284.09	197.27	04/2017 -	03/2022	59	-
409	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	158.08	04/2017 -	03/2022	59	-
410	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	159.83	04/2017 -	03/2022	59	-
411	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	252.05	159.32	04/2017 -	03/2022	59	-
412	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 -	03/2022	51	-
413	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	341.40	09/2018 -	03/2022	42	-
414	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	127.24	09/2018 -	03/2022	42	-
415	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	154.83	11/2017 -	03/2022	52	-
416	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	-
417	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	528.66	11/2018 -	04/2022	41	-
418	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	239.30	134.40	09/2018 -	05/2022	44	-
419	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	404.17	246.27	08/2018 -	05/2022	45	-
420	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 -	06/2022	44	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
421	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	403.36	224.23	06/2018 -	07/2022	49	-
422	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	186.85	09/2018 -	07/2022	46	-
423	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	299.26	07/2018 -	07/2022	48	-
424	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	216.00	120.10	11/2018 -	08/2022	45	-
425	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	274.31	136.62	05/2018 -	09/2022	52	-
426	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	417.24	276.32	05/2018 -	09/2022	52	-
427	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	100.70	09/2018 -	09/2022	48	-
428	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	306.28	135.84	05/2019 -	09/2022	40	-
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	87.49	09/2018 -	10/2022	49	-
430	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA	03/2020	247.76 -	247.76	36.82	01/2022 -	10/2022	9	-
431	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	156.49	09/2018 -	11/2022	50	-
432	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	12/2022	50	-
433	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	253.44	92.24	07/2019 -	12/2022	41	-
434	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	636.42	55.56	12/2022 -	01/2023	1	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	63.74	10/2018 -	03/2023	53	-
436	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	140.92	09/2019 -	04/2023	43	-
437	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	137.39	09/2019 -	04/2023	43	-
438	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	163.81	09/2019 -	04/2023	43	-
439	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM	03/2019	402.94 -	402.94	79.70	04/2022 -	05/2023	13	-
440	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	133.41	09/2019 -	06/2023	45	-
441	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	164.47	09/2019 -	06/2023	45	-
442	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	124.67	09/2019 -	07/2023	46	-
443	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	120.31	09/2019 -	09/2023	48	-
444	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	75.58	09/2019 -	04/2024	55	-
	<u>National Highways Authority Of India</u>								
445	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	84.29	05/2013 -	02/2022	105	-
446	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	03/2022	103	-
447	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 1,066.87	953.88	93.63	07/2013 03/2020	03/2022	104	24
448	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	03/2022	103	-
449	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	744.73	726.49	05/2018 -	03/2022	46	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
450	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM.55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	03/2022	47	-
451	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	1,020.25	11/2018 07/2019	03/2022	40	32
452	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	435.62	03/2019 -	03/2022	36	-
453	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	1,357.48	03/2020 -	03/2022	24	-
454	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	254.00	254.85	03/2020 -	03/2022	24	-
455	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	1,100.45	03/2020 -	03/2022	24	-
456	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,701.66	03/2013 -	04/2022	109	-
457	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	1,021.00	529.08	- 01/2022	04/2022	-	3
458	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	600.78	06/2018 12/2021	05/2022	47	5
459	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	1,048.10	1,203.21	- 12/2021	05/2022	-	5
460	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 1,023.23	1,023.23	980.59	07/2018 02/2022	05/2022	46	3
461	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,300.00	971.90	09/2017 12/2021	05/2022	56	5
462	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	1,827.00	1,766.52	03/2021 -	05/2022	14	-
463	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	717.24	638.69	05/2018 -	06/2022	49	-
464	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	2,510.04	653.06	08/2019 -	06/2022	34	-
465	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	06/2022	26	-
466	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	258.64	07/2017 -	06/2022	59	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
467	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	845.00	12/2019 -	06/2022	30	-
468	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	742.16	08/2017 -	07/2022	59	-
469	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	841.80	09/2017 -	07/2022	58	-
470	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	635.00	03/2020 -	08/2022	29	-
471	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	673.00	05/2020 -	08/2022	27	-
472	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	996.27	737.00	03/2020 -	08/2022	29	-
473	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	2,933.43	06/2014 -	09/2022	99	-
474	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	106.65	04/2014 -	09/2022	101	-
475	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	-
476	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 649.00	649.00	373.86	- 10/2021	12/2022	-	14
477	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	03/2023	44	-
478	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 736.01	830.31	105.50	03/2020 12/2018	03/2023	36	51
479	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	42.83	12/2017 -	05/2023	65	-
480	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,913.66	08/2013 -	06/2023	118	-
481	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	348.00	03/2019 -	06/2023	51	-
482	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 644.50	726.99	156.13	- 12/2019	06/2023	-	42
483	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 1,161.00	1,168.00	354.24	08/2017 08/2018	10/2023	74	62
484	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI - [N24001416]NHAI,PUNJAB	12/2020	989.66 -	989.66	-	01/2024 -	04/2024	3	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
485	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	982.00	-	03/2020 07/2022	07/2024	52	24
	Total		1,10,513.47 -	1,12,695.97	74,424.79				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
486	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 461.42	461.42	70.25	06/2021 11/2021	06/2022	12	7
	<u>Cpwd For Telecom</u>								
487	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD FOR TELECO,DELHI	10/2014	248.20 -	248.20	173.87	03/2018 -	03/2022	48	-
	<u>Department Of Telecommunication</u>								
488	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	20,545.00	07/2015 -	03/2022	80	-
	Total		14,013.36 -	25,373.62	20,789.12				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
489	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,925.22	10,015.98	12/2018 -	08/2022	44	-
490	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT	03/2019	12,020.32 -	12,020.32	439.23	03/2024 -	06/2024	3	-
	<u>Bangalore Metro Rail Corporation Limited</u>								
491	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	20,025.67	02/2021 -	03/2025	49	-
	<u>Central Public Works Department</u>								
492	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	217.00	187.17	04/2019 -	02/2022	34	-
493	CONSTRUCTION729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 -	299.97	27.44	09/2020 -	05/2023	32	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
494	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	2,561.78	03/2024 -	11/2024	8	-
495	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	593.47	03/2024 -	12/2025	21	-
	<u>Maharashtra Metro Rail Corporation Ltd.</u>								
496	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11,420.00	7,764.11	11/2021 -	12/2022	13	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
497	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	33,406.00	20,484.28	03/2020 -	03/2023	36	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Nagpur Metro Rail Corporation Ltd</u>								
498	NAGPUR METRO RAIL - [N28000085]NMRC, MAHARASHTRA	08/2014	8,680.00	9,759.79	8,462.32	03/2018	02/2022	47	-
	Total		1,12,387.86	1,25,909.54	70,561.45				
	<u>WATER RESOURCES</u>								
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
499	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO, BIHAR	12/2014	225.77	398.90	299.08	03/2020	03/2022	24	-
500	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO, BIHAR	05/2017	191.62	191.62	74.10	11/2020	03/2022	16	-
501	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO, BIHAR	04/2015	268.63	268.63	380.87	01/2021	05/2022	16	-
502	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO, BIHAR	03/2017	277.42	277.42	263.52	05/2021	05/2022	12	-
503	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO, BIHAR	05/2017	356.37	356.37	154.13	04/2021	06/2022	14	-
504	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO, BIHAR	11/2018	236.15	236.15	66.51	12/2020	07/2022	19	-
505	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO, BIHAR	03/2018	230.06	230.06	98.80	07/2021	03/2023	20	-
506	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO, BIHAR	03/2018	305.19	305.19	44.87	08/2021	04/2023	20	-
507	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO, BIHAR	03/2018	294.02	294.02	38.57	10/2021	12/2023	26	-
508	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO, BIHAR	08/2017	578.89	578.89	42.75	06/2022	12/2023	18	-
509	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO, BIHAR	08/2017	824.00	824.00	101.12	06/2022	12/2023	18	-
510	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO, BIHAR	10/2017	254.13	413.29	.07	09/2020	03/2024	42	-
	<u>Delhi Jal Board</u>								
511	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB, DELHI	12/2018	515.07	515.07	363.66	01/2021	02/2022	13	-
512	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB, DELHI	05/2016	211.79	211.79	261.19	12/2021	12/2022	12	-
513	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB, DELHI	05/2016	239.11	239.11	176.36	02/2022	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
514	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32	272.32	261.87	04/2020	03/2022	23	-
515	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76	274.76	225.99	12/2019	05/2022	29	-

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
516	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	185.22	38.00	12/2021 -	09/2023	21	-
517	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	172.10	38.00	12/2021 -	09/2023	21	-
518	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	164.93	34.69	12/2021 -	09/2023	21	-
519	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 -	224.69	-	02/2022 -	03/2024	25	-
520	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	165.16	-	06/2022 -	03/2024	21	-
521	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 -	154.73	-	02/2022 -	03/2024	25	-
522	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	384.96	-	04/2022 -	12/2024	32	-
523	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	287.53	-	04/2022 -	12/2024	32	-
524	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	234.31	-	04/2022 -	12/2024	32	-
525	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	307.12	-	09/2022 -	12/2024	27	-
	<u>Polavaram Project Authority</u>								
526	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	18,422.33	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
527	MATHURA SEWERAGE SCHEME - [N30000019]UP JalNigam, UTTAR PRADESH	12/2017	460.45 -	460.45	248.16	12/2020 -	03/2022	15	-
528	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UP JalNigam, UTTAR PRADESH	01/2019	206.05 -	206.05	95.91	10/2021 -	03/2022	5	-
529	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UP JalNigam, UTTAR PRADESH	03/2018	967.23 -	967.23	109.63	09/2021 -	09/2022	12	-
530	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UP JalNigam, UTTAR PRADESH	05/2017	767.59 -	767.59	152.31	09/2021 -	12/2022	15	-
531	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UP JalNigam, UTTAR PRADESH	01/2019	231.79 -	234.03	28.37	12/2021 -	06/2023	18	-
532	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UP JalNigam, UTTAR PRADESH	03/2019	271.39 -	271.39	-	08/2021 -	03/2024	31	-

Costing Rs. 150 Crore and above

(February 2022)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
533	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 -	213.91	-	07/2021 -	03/2024	32	-
534	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 -	261.12	-	03/2022 -	04/2024	25	-
535	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	690.71	-	06/2022 -	04/2024	22	-
	<u>Uttarakhand Pey Jal Nigam</u>								
536	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	158.00	87.59	11/2019 -	03/2022	28	-
	Total		22,222.12 -	67,947.69	22,108.45				
	<u>DEFENCE PRODUCTION</u>								
	<u>Cpwd For Defence</u>								
537	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD FOR DEFENC,KARNATAKA	12/2016	246.31 210.00	200.00	168.90	02/2020 03/2022	06/2022	28	3
	Total		246.31 -	200.00	168.90				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Cpwd Of Higher Education</u>								
538	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD EDUCATION,PUNJAB	01/2018	430.00 -	387.83	241.27	05/2020 -	08/2022	27	-
539	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD EDUCATION,ODISHA	01/2019	790.79 -	790.79	294.36	03/2022 -	09/2022	6	-
540	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD EDUCATION,CHHATTISGARH	03/2020	808.62 -	808.62	318.94	07/2022 -	10/2022	3	-
541	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD EDUCATION,PUNJAB	10/2019	348.24 -	348.24	35.43	05/2022 -	10/2022	5	-
542	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD EDUCATION,KARNATAKA	07/2019	851.00 851.00	851.00	361.47	03/2022 -	10/2022	7	-
543	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD EDUCATION,ANDHRA PRADESH	02/2019	655.34 -	655.34	375.85	06/2020 -	11/2022	29	-
544	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD EDUCATION,BIHAR	09/2018	375.00 -	375.00	125.38	09/2020 -	11/2022	26	-
545	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD EDUCATION,KERALA	07/2019	753.63 -	753.63	234.20	03/2021 -	02/2023	23	-

Costing Rs. 150 Crore and above

(February 2022)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
546	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD EDUCATION,GOA	05/2019	303.90 -	303.90	61.00	03/2020 -	02/2023	35	-
547	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD EDUCATION,WEST BENGAL	03/2020	193.83 -	193.83	77.27	06/2020 -	03/2023	33	-
548	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD EDUCATION,ANDHRA PRADESH	09/2019	588.72 -	588.72	142.46	09/2022 -	06/2023	9	-
549	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD EDUCATION,BIHAR	02/2016	496.18 496.00	498.99	318.32	06/2017 -	03/2022	57	-
	Total		6,595.25 -	6,555.89	2,585.95				
	<u>HOME AFFAIRS</u>								
	<u>Cpwd For Mha</u>								
550	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD FOR MHA,DELHI	10/2013	1,219.21 -	2,000.00	1,089.05	10/2019 -	06/2022	32	-
551	NSG AT KOLKATA - [N28000104]CPWD FOR MHA,WEST BENGAL	10/2014	162.88 -	228.63	173.62	04/2018 -	12/2022	56	-
552	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]CPWD FOR MHA,DELHI	06/2019	277.35 -	290.33	46.80	07/2022 -	12/2022	5	-
	Total		1,659.44 -	2,518.96	1,309.47				
	<u>DPIIT</u>								
	<u>Iicc For Dpiit</u>								
553	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC FOR DPIIT,DELHI	11/2017	4,773.00 -	5,178.00	3,062.37	12/2019 -	05/2022	29	-
	Total		4,773.00 -	5,178.00	3,062.37				
	Grand Total		7,64,840.70	9,99,931.57	5,86,756.34				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(February 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	09/2010	10/2022	95.88	145
	Total		3,492.00	6,840.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
2	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	09/2021	12/2023	38.72	27
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23	707.73	09/2018	10/2022	69.63	49
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	03/2021	03/2025	7.88	48
5	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]	06/2018	1,383.00	1,938.00	09/2021	12/2023	40.13	27
	Total		3,288.50	4,358.06				
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
6	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00	334.27	04/2018	06/2023	37.56	62
7	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13	341.22	03/2017	12/2022	12.20	69
	<u>Eastern Coal Fields Limited</u>							
8	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>							
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53	808.97	03/2013	03/2024	68.70	132
	<u>Neyveli Lignite Corporation</u>							
10	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11	7,980.79	12/2015	02/2021	35.10	62
11	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00	17,237.80	11/2021	06/2023	.00	19

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		26,832.50	31,849.53				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Cpwd Of Higher Education</u>							
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133	02/2019	186.00 199.00	210.60	09/2020 -	-	13.23	10
13	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	-	.57	57
14	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119	12/2016	549.31 -	580.00	07/2019 -	07/2021	5.59	24
	Total		1,231.49 -	1,289.59				
	<u>DPIIT</u>							
	<u>Dmic For Dpiit</u>							
15	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001	09/2011	12,579.09 -	13,812.30	09/2019 -	-	9.80	22
	<u>licc For Dpiit</u>							
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002	11/2017	4,773.00 -	5,178.00	12/2019 -	05/2022	8.49	29
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
17	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012	07/2016	152.95 -	177.92	02/2018 -	04/2021	16.33	38
18	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.20	05/2017 -	01/2021	13.20	44
19	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	205.00	- -	01/2022	30.94	0
20	CNCI KOLKATA WEST BENGAL - [N21000015	08/2016	244.00 -	248.00	09/2018 -	12/2021	1.64	39
21	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022	01/2018	249.01 -	249.07	- -	05/2021	.02	0
22	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44 -	250.00	05/2017 -	06/2021	22.29	49
23	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	280.00	03/2019 -	02/2021	2.87	23
24	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021	03/2018	268.84 -	284.67	- -	05/2021	5.89	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
25	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
26	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	586.50	11/2013 -	09/2021	41.63	94
27	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011]	09/2014	505.58 -	586.96	03/2018 -	04/2020	16.10	25
	<u>Nbcc For Health</u>							
28	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	09/2021 -	06/2022	8.88	9
	Total		4,281.23 -	4,855.32				
	<u>HEAVY INDUSTRY</u>							
	<u>Natip Implementation Society</u>							
29	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	09/2011 -		116.96	0
	Total		1,718.00 -	3,727.30				
	<u>HOME AFFAIRS</u>							
	<u>Cpwd For Mha</u>							
30	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	228.63	04/2018 -	12/2022	40.37	56
31	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI - [N45000002]	06/2019	277.35 -	290.33	07/2022 -	12/2022	4.68	5
32	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	06/2022	64.04	32
	Total		1,659.44 -	2,518.96				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
33	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	02/2017 -	08/2022	117.11	66
34	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	06/2019 -	02/2023	35.54	44
	<u>Gas Authority Of India Limited</u>							
35	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]	09/2018	225.54 -	247.90	02/2021 -	10/2022	9.91	20
36	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	08/2020 -	04/2022	14.17	20
37	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	04/2022 -	04/2022	20.06	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Hindustan Petroleum Corporation Limited</u>							
38	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00	3,072.00	06/2021	07/2022	14.76	13
39	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00	26,264.00	07/2020	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>							
40	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02	207.36	04/2020	10/2022	27.20	30
41	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336	03/2018	588.20	730.20	-	05/2023	24.14	0
	<u>Numaligarh Refinery Limited</u>							
42	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY [N16000379	01/2019	12,366.00	18,968.00	10/2024	10/2024	53.39	0
	<u>Oil & Natural Gas Corporation Limited</u>							
43	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	05/2019	763.92	829.58	12/2020	05/2022	8.60	17
	<u>Oil India Limited</u>							
44	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91	638.60	02/2020	06/2022	17.41	28
	Total		40,619.50	54,609.04				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
45	LOKTAK D/S HEP(NHPC) - [180100078	12/1999	578.62	1,311.05	06/2006	-	126.58	0
	<u>National Thermal Power Corporation</u>							
46	KAWAS SOLAR 56 MW - [N18000283	08/2020	261.80	293.03	10/2021	10/2022	11.93	12
47	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284	06/2019	401.90	442.03	04/2021	05/2022	9.99	13
48	DEVIKOT SOLAR 90MW - [N18000280	03/2020	501.29	524.83	09/2021	03/2022	4.70	6
49	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277	12/2016	529.68	679.00	11/2018	06/2022	28.19	43
50	DEVIKOT SOLAR 150MW - [N18000281	01/2020	798.24	852.90	09/2021	05/2022	6.85	8
51	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84	1,803.00	09/2019	07/2025	30.48	70
52	NOKHRA - [N18000282	03/2020	1,722.14	1,803.19	09/2021	10/2022	4.71	13
53	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276	05/2016	1,885.13	2,426.00	12/2018	03/2022	28.69	39

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
54	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	5,289.25	10/2017 -	-	24.81	0
55	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	07/2012 -	-	97.38	0
56	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,998.00	11/2020 -	02/2023	3.76	27
	<u>Power Grid Corporation Of India Limited</u>							
57	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	07/2019 -	08/2022	17.99	37
58	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	03/2022	4.61	64
59	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	08/2017	1,931.39 -	2,635.55	02/2020 -	04/2023	36.46	38
60	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020 -	04/2022	14.11	21
61	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	12/2018 -	01/2024	31.08	61
62	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	12/2018 -	03/2024	92.02	63
63	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,199.00	08/2013 -	03/2018	18.59	55
	<u>Satluj Jal Vidyut Nigam Limited</u>							
64	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	12/2021 -	06/2022	46.20	6
	<u>Thdc India Limited</u>							
65	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	02/2016 -	06/2023	191.23	88
	Total		57,691.70 -	79,185.66				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
66	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	03/2022 -	03/2023	.89	12
67	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	1,387.52	03/2021 -	03/2023	75.00	24
68	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94	0
69	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.49	03/2024 -	-	25.04	0
70	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2023	8.75	0
71	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
72	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	2,271.50 -	4,794.60	03/2021 -	03/2023	111.08	24
73	PUNE-NASIK (265 KM) - [N22000354	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
74	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50 -	235.00	03/2019 -	-	.21	0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
75	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT [N22000346	10/2006	11,589.00 30,357.00	51,219.00	- -	-	341.96	0
	<u>East Central Railways</u>							
76	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	03/2020 -	12/2024	49.45	57
77	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	03/2019 -	-	37.04	33
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240	04/1997	324.73 -	1,090.00	03/2012 -	06/2023	235.66	135
79	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,893.55	- -	-	400.20	0
80	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	- -	-	818.15	0
81	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	03/1999	1,033.07 -	3,650.00	- -	07/2022	253.32	0
	<u>East Coast Railway</u>							
82	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2025	15.45	76
83	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2024	.07	48
84	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2022	38.43	37
85	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	06/2021 -	03/2025	137.80	45
86	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	03/2009 -	12/2024	29.71	189
	<u>Eastern Railways</u>							
87	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
88	MONIGRAM- NIMITTA - [N22000301	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
89	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
90	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	- -	03/2022	181.63	0
91	BANDEL-BOINCHI 3RD LINE - [N22000221	04/2011	288.35 -	502.48	- -	02/2022	74.26	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
92	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	03/2016 -	03/2024	7.75	96
93	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
94	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>							
95	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	09/2018 -	06/2022	.00	45
96	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	03/2022 -	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>							
97	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	774.51	06/2013 -	12/2022	56.23	114
98	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	03/2004 -	06/2022	501.57	219
99	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	03/2013	4,874.58 -	8,574.97	03/2016 -	-	75.91	0
	<u>North Central Railway</u>							
100	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>							
101	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	401.65	- -	03/2023	66.30	0
102	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
103	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	708.73	03/2020 -	09/2022	24.42	30
104	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	750.00	03/2020 -	-	80.79	0
105	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,145.79	03/2019 -	03/2024	197.45	60
106	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	03/2021 -	03/2022	115.07	12
107	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,047.51	03/2019 -	12/2023	13.88	57
108	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60
109	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
110	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	03/2021 -	-	350.44	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
111	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	6,527.00	03/2014 -	12/2023	172.70	117
112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,663.00	03/2015 -	03/2026	186.39	132
113	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	12/2015 -	12/2023	542.04	96
114	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	14,322.00	03/2011 -	12/2023	221.54	153
	<u>North Eastern Railway</u>							
115	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	-	.16	68
116	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77	66
117	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP [N22000136]	03/2013	643.00 -	644.00	- -	-	.16	0
118	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	728.92	01/2019 -	-	147.09	37
119	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	800.00	- -	12/2023	32.78	0
120	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15	0
121	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99	0
122	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,824.00	03/2022 -	03/2022	40.80	0
	<u>North Western Railway</u>							
123	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
124	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40
	<u>Northern Railway</u>							
125	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
126	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
127	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	- -	09/2023	134.90	0
128	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	839.00	03/2016 -	-	34.24	0
129	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	-	211.31	0
130	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	03/2023 -	12/2025	369.35	33
131	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,017.96	07/2012 -	11/2024	348.44	148
132	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	37,012.26	11/2002 -	04/2023	1,380.49	245

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Rail Vikas Nigam Ltd.</u>							
133	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327	04/2000	133.41 207.00	433.00	03/2009 03/2009	12/2022	224.56	165
134	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
135	DHASA-JETALSAR (GC) - [N22000141	04/2012	644.38 -	923.28	03/2021 -	05/2022	43.28	14
136	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	950.00	03/2016 -	04/2022	50.15	73
137	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	04/2011	927.01 -	1,457.79	03/2019 -	03/2023	57.26	48
138	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	04/2015	943.60 -	1,500.00	03/2022 -	12/2022	58.97	9
139	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020 -	12/2022	102.11	33
140	BANASPANI- JAKHPURA - DOUBLING - [N22000412	03/2009	942.95 -	1,552.26	03/2019 -	03/2023	64.62	48
141	BINA - KOTA DOUBLING WITH RE - [N22000414	04/2011	1,485.85 -	1,835.83	12/2020 -	09/2022	23.55	21
142	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410	03/2006	948.04 -	2,009.00	03/2020 -	04/2022	111.91	25
143	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	03/2012	1,183.25 -	2,203.53	12/2020 -	06/2022	86.23	18
144	SUKINDA ROAD - ANGUL (NL)(ECOR) - [N220100325	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
145	PALANPUR-SAMAKHAYALI (DL) - [N22000144	04/2013	1,548.66 -	2,538.01	12/2021 -	12/2022	63.88	12
146	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	03/2009	713.48 -	2,725.00	03/2020 -	03/2022	281.93	24
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
148	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297	04/2010	2,127.00 -	3,300.00	03/2023 -	03/2023	55.15	0
149	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
150	VIJAYAWADA-GUDUR - [N22000369	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
151	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313	03/2012	1,503.71 -	3,633.12	03/2020 -	06/2022	141.61	27
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2026	7.78	120
153	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,834.54	03/2016 -	07/2025	65.94	112

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
154	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	12/2026 -	03/2025	127.62	-21
155	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	24,659.00	12/2024 -	03/2025	52.07	3
	<u>South Central Railway</u>							
156	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	242.28	03/2022 -	-	102.36	0
157	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	704.31 -	927.94	03/2020 -	03/2022	31.75	24
158	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	1,160.48 -	1,373.74	03/2010 -	03/2025	18.38	180
159	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
160	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2027	102.85	216
161	MANUGURU-RAMAGUNDAM - [N22000259	04/2013	1,112.00 -	2,911.84	-	-	161.86	0
162	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
163	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
164	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2025	7.06	36
	<u>South East Central Railway</u>							
165	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	12/2021 -	12/2024	378.60	36
166	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438	04/2010	585.93 -	1,268.32	02/2019 -	03/2022	116.46	37
167	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
168	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,176.60	03/2023 -	12/2023	66.44	9
	<u>South Eastern Railway</u>							
169	PURULIA TO KOTSHILA DOUBLING (39.1 KM) - [N22000510	04/2018	338.00 -	393.83	06/2022 -	12/2023	16.52	18
170	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) - [N22000508	04/2018	428.65 -	472.50	06/2022 -	12/2025	10.23	42
171	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM) - [N22000509	04/2018	390.39 -	511.75	12/2021 -	01/2023	31.09	13
172	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.97	03/2020 -	06/2022	35.38	27
	<u>South Western Railway</u>							
173	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300	04/2013	327.25 -	367.77	-	03/2027	12.38	0
174	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	-	03/2028	57.65	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
175	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL [N22000276]	04/2013	558.00 -	692.43	- -	03/2028	24.09	0
176	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	758.36	03/2020 -	02/2022	31.20	23
177	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	817.23	03/2017 -	03/2026	26.75	108
178	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,104.00	03/2020 -	02/2022	28.31	23
179	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,383.00	03/2002 -	03/2028	.02	312
180	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	03/2016 -	12/2026	55.13	129
181	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	03/2019 -	02/2024	16.31	59
182	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,954.21	03/2020 -	12/2022	68.91	33
183	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,000.97	- -	03/2025	11.10	0
184	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,404.03	- -	12/2025	16.57	0
185	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	- -	03/2028	123.51	0
<u>Southern Railway</u>								
186	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	448.10	- -	03/2025	136.79	0
187	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	591.00	- -	03/2022	259.47	0
188	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	709.69	- -	03/2025	180.55	0
189	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	749.40	- -	03/2022	177.41	0
190	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	- -	03/2030	.00	0
191	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 -	1,339.00	- -	03/2025	33.90	0
192	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,549.09	03/2020 -	03/2025	409.60	60
193	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	120.70 -	2,111.88	03/2019 -	12/2027	1,649.69	105
194	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80	0
195	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	3,081.20	02/2019 -	03/2025	325.17	73
196	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,444.00	- -	12/2025	490.91	0
<u>West Central Railway</u>								

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
197	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,247.64	03/2022 -	12/2023	114.32	21
198	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	06/2016	2,478.23 -	2,875.12	03/2022 -	06/2023	16.02	15
199	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,909.99	03/2021 -	03/2024	585.35	36
200	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	8,248.50	05/2008 -	03/2025	3,230.57	202
<u>Western Railway</u>								
201	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]	03/2010	265.88 -	311.36	- -	-	17.11	0
202	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123]	04/2008	318.24 -	321.62	03/2012 -	10/2023	1.06	139
203	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]	03/2012	217.38 -	393.62	- -	-	81.07	0
204	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]	03/2012	248.26 -	528.49	- -	-	112.88	0
205	ANAND GODHRA DOUBLING PROJECT 79 KMS - [N22000504]	04/2017	692.25 -	742.88	03/2020 -	03/2024	7.31	48
206	SURENDRA NAGAR RAJKOT - [N22000392]	04/2015	1,002.39 -	1,056.11	03/2021 -	12/2022	5.36	21
207	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	1,378.11	03/2019 -	03/2025	329.77	72
208	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 -	1,383.69	03/2021 -	12/2022	33.41	21
209	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26 -	1,524.68	03/2022 -	10/2027	13.17	67
210	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 -	2,223.37	03/2020 -	03/2024	167.96	48
211	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 -	6,383.82	03/2022 -	03/2026	82.20	48
	Total		1,92,253.60 -	4,13,082.96				
<u>RENEWABLE ENERGY</u>								
<u>Cpwd For Renewable Energy</u>								
212	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	365.00	11/2019 -	-	34.24	0
	Total		271.90 -	365.00				
<u>ROAD TRANSPORT AND HIGHWAYS</u>								
<u>Ministry Of Road Transport And Highways (State Pwds)</u>								

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
213	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	174.90	08/2018 -	03/2022	5.23	43
214	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00	177.84	12/2019 -	11/2020	.00	11
215	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00	189.46	12/2019 -	06/2022	.00	30
216	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00	194.23	02/2020 -	01/2021	.00	11
217	KHAMGAON TO SHEGAON - [N24001009]	02/2017	203.21 203.00	203.21	05/2019 -	09/2019	.00	4
218	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]	03/2016	160.27 -	213.97	08/2019 -	03/2023	33.51	43
219	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00	217.14	02/2020 -	06/2021	.00	16
220	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00	222.13	11/2019 -	02/2022	.00	27
221	KUNDRAI TO WAZAR - [N24001077]	01/2018	225.25 225.00	225.25	12/2019 -	12/2020	.00	12
222	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	08/2018 -	03/2022	4.45	43
223	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00	227.19	12/2019 -	03/2022	.00	27
224	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48	0
225	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	-	.08	23
226	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00	238.19	12/2019 -	03/2022	.00	27
227	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00	240.30	01/2020 -	-	.00	14
228	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00	244.04	03/2019 -	12/2021	.00	33
229	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00	257.38	12/2019 -	03/2022	.00	27
230	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	08/2019 -	03/2023	11.18	43
231	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]	01/2017	166.67 -	264.34	09/2017 -	-	58.60	0
232	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00	264.41	03/2019 -	03/2022	.00	36
233	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00	272.04	12/2019 -	09/2021	.00	21

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
234	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	- -	01/2020	3.72	0
235	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	11/2020	.31	16
236	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	09/2022	.00	25
237	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	10/2020	.00	10
238	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161	12/2017	297.30 -	318.28	01/2019 -	-	7.06	0
239	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211	11/2018	281.45 -	319.96	- -	03/2022	13.68	0
240	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	01/2014	282.41 -	319.96	03/2016 -	04/2022	13.30	73
241	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	-	72.36	0
242	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	03/2020	.00	10
243	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208	03/2018	288.30 -	323.36	08/2020 -	03/2022	12.16	19
244	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	03/2022	.00	27
245	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	12/2020	.00	12
246	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	12/2020	.00	18
247	OSMANNAGAR TO KUNDRAI - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	06/2022	.00	22
248	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	03/2022	.00	27
249	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	12/2015 -	-	6.07	0
250	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178	11/2016	336.25 -	369.96	09/2019 -	11/2020	10.03	14
251	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	11/2020	.00	18
252	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	12/2022	.00	31
253	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 -	386.41	10/2018 -	-	18.58	0
254	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	05/2017 -	06/2022	45.75	61

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
255	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	03/2022	.00	33
256	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	12/2020	.00	12
257	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.52	08/2017 -	-	42.48	30
258	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	12/2022	.00	31
259	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	09/2022	.00	39
260	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	03/2022	.00	32
261	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	06/2022	.00	24
262	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33 -	428.55	03/2018 -	03/2022	9.23	48
263	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
264	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939	03/2018	504.19 504.00	504.19	11/2018 -	-	.00	0
265	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00	536.65	12/2019 -	03/2022	.00	27
266	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	01/2020	.00	7
267	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14 -	572.66	08/2016 -	12/2022	15.19	76
268	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98 -	731.50	10/2016 -	06/2022	17.04	68
269	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	09/2022	.00	15
270	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75	0
271	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899	03/2016	877.79 -	949.54	06/2019 -	03/2022	8.17	33
272	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	10/2022	.00	77
273	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	12/2022	.00	37
274	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	06/2022	.00	31

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
275	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00	2,036.90	-	12/2021	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
276	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22	252.05	04/2017	03/2022	27.16	59
277	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23	252.79	04/2017	03/2022	29.48	59
278	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36	263.31	04/2017	03/2022	29.48	59
279	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07	387.00	08/2016	-	3.73	57
280	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00	447.37	10/2017	-	15.30	0
	<u>National Highways Authority Of India</u>							
281	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04	255.23	11/2008	-	64.62	0
282	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46	276.17	-	-	.99	0
283	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81	340.14	04/2009	-	70.23	0
284	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72	355.24	08/2018	-	9.74	0
285	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73	359.60	-	-	23.69	0
286	2-LANING WITH PAVED SHOULDERS OF RAEARELI - BANDA SECTION OF NH-232 - [N24000360	04/2014	351.34	417.68	01/2016	-	18.88	0
287	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64	435.78	11/2008	-	159.95	0
288	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94	448.18	-	-	10.68	0
289	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	07/2012	291.36	469.31	01/2014	-	61.08	0
290	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00	475.00	05/2013	-	46.15	0
291	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594	07/2016	458.03	486.00	-	-	6.11	0
292	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20	537.17	-	-	8.26	0
293	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	05/2011	511.54	591.00	11/2013	-	15.53	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
294	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379	02/2019	594.75 -	606.75	11/2019 -	-	2.02	0
295	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367	04/2014	495.78 -	627.93	01/2016 -	-	26.66	0
296	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	639.58	04/2019 -	07/2022	-38.57	39
297	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
298	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299	09/2018	617.41 -	668.45	02/2019 -	-	8.27	0
299	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506	01/1991	642.41 -	681.67	-	-	6.11	0
300	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	717.24	05/2018 -	06/2022	20.90	49
301	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723	01/2018	573.70 -	726.99	-	06/2023	26.72	0
302	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377	02/2019	731.89 -	732.34	11/2019 -	-	.06	0
303	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	-	06/2022	.00	0
304	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	05/2018 -	03/2022	40.22	46
305	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	-	-	25.68	0
306	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	-	-	1.37	0
307	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	830.31	03/2020 -	03/2023	23.39	36
308	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	-	11/2022	27.86	0
309	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	-	10/2022	305.58	0
310	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	-	-	15.98	0
311	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	925.96	-	-	45.89	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
312	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691]	04/2017	894.00	929.32	04/2020	06/2022	3.95	26
313	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 [N24000459]	06/2015	845.24	941.00	-	01/2020	11.33	0
314	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) [N24000656]	03/2017	744.64	982.00	03/2020	07/2024	31.88	52
315	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24	987.94	-	-	44.60	0
316	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80	1,038.56	-	-	21.50	0
317	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) [N24000658]	03/2017	988.34	1,043.28	03/2020	01/2022	5.56	22
318	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) [N24000657]	03/2017	1,030.44	1,065.51	03/2020	01/2022	3.40	22
319	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]	03/2018	809.07	1,065.70	-	-	31.72	0
320	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) [N24000659]	03/2017	1,059.73	1,071.00	03/2017	-	1.06	0
321	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]	03/2018	1,016.92	1,071.00	-	12/2022	5.32	0
322	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67	1,096.52	04/2018	-	50.90	0
323	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69	1,108.00	08/2019	-	16.55	0
324	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]	03/2018	478.74	1,135.08	-	-	137.10	0
325	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) [N24000661]	03/2017	1,098.06	1,160.64	03/2020	-	5.70	0
326	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]	08/2017	950.64	1,168.00	08/2017	10/2023	22.86	74
327	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58	1,177.00	03/2020	-	41.54	0
328	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 [N24000507]	12/2015	1,167.45	1,182.94	-	-	1.33	0
329	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62	1,187.10	03/2020	-	13.97	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
330	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	- -	-	29.35	0
331	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703	10/2017	964.17 -	1,198.64	10/2017 -	-	24.32	0
332	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	-	22.44	0
333	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
334	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	- -	05/2022	11.20	0
335	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,300.00	09/2017 -	05/2022	15.65	56
336	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	22
337	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300	11/2019	1,226.88 -	1,321.60	02/2021 -	-	7.72	0
338	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
339	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649	01/2017	1,251.11 -	1,361.00	- -	-	8.78	0
340	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,361.00	- -	-	29.35	0
341	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2022	10.24	24
342	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
343	FOUR LANING OF PARWANOO -SOLAN - [N24000479	09/2015	934.46 -	1,457.82	03/2018 -	-	56.01	0
344	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
345	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	1,588.29	09/2019 -	-	14.40	0
346	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	1,827.00	03/2021 -	05/2022	19.21	14
347	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	- -	-	30.09	0

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
348	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]	03/2018	1,261.98 -	1,952.20	- -	-	54.69	0
349	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88 -	1,993.81	06/2020 -	-	1.78	0
350	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96 -	2,169.00	- -	-	4.99	0
351	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	- -	-	94.94	0
352	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	- -	-	41.78	0
353	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34 -	2,400.00	- -	-	20.28	0
354	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	-	18.50	0
355	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80 -	2,450.00	- -	-	12.50	0
356	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
357	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	04/2019 -	-	87.84	0
358	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
359	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]	07/2020	3,426.00 -	5,148.00	12/2021 -	-	50.26	0
	Total		1,04,557.17 -	1,24,422.77				
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
360	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	05/2015 -	06/2022	41.32	85
	Total		15,525.00 -	21,940.00				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
361	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	03/2022	84.97	80
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							

Costing Rs. 150 Crore and above

(February 2022)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>Ahmedabad Metro Rail</u>							
362	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00	12,925.22	12/2018	08/2022	19.98	44
	<u>Central Public Works Department</u>							
363	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33	217.00	04/2019	02/2022	9.97	34
	<u>Chennai Metro Rail Ltd</u>							
364	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00	18,380.00	12/2015	-	25.89	0
	<u>Delhi Metro Rail Corporation</u>							
365	DELHI MRTS PHASE-III - [N28000056]	09/2011	38,585.00	40,180.91	03/2016	-	4.14	0
	<u>Kochi Metro Rail Corporation Ltd</u>							
366	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79	6,218.14	07/2017	-	20.00	38
	<u>Mumbai Metro Rail Corporation Ltd</u>							
367	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00	33,406.00	03/2020	03/2023	44.39	36
	<u>Nagpur Metro Rail Corporation Ltd</u>							
368	NAGPUR METRO RAIL - [N28000085]	08/2014	8,680.00	9,759.79	03/2018	02/2022	12.44	47
	<u>Patna Metro Rail Corporation</u>							
369	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77	13,925.50	06/2024	06/2024	4.19	0
	Total		1,14,518.89	1,35,012.56				
	<u>WATER RESOURCES</u>							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
370	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77	398.90	03/2020	03/2022	76.68	24
371	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13	413.29	09/2020	03/2024	62.63	42
	<u>Delhi Jal Board</u>							
372	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD - 10MG/L - [N30000014]	03/2017	665.78	942.18	12/2022	12/2022	41.52	0
	<u>Kolkata Metropolitan Development Authority</u>							
373	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43	224.69	02/2022	03/2024	13.23	25
	<u>Uttar Pradesh Jal Nigam</u>							
374	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79	234.03	12/2021	06/2023	.97	18

Costing Rs. 150 Crore and above					(February 2022)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
375	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008	10/2017	213.62 -	261.12	03/2022 -	04/2024	22.24	25
376	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 -	690.71	06/2022 -	04/2024	1.31	22
	Total		2,471.30 -	3,164.92				
	Grand Total		6,01,098.31	9,30,875.97				

FLASH REPORT

North East Projects Costing Rs.150 crore and above (as on					28.02.2022)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (10/2023) [10/2023]	645.63 (-) [645.63]	296.53 (0.00) [14]
	<u>Power</u>				
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	15,300.08 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
4	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [10/2021]	210.50 (-) [210.50]	145.76 (0.00) [0]
5	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [0/0]	496.47 (-) [496.47]	8.93 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [2/2022]	243.89 (-) [243.89]	229.09 (0.00) [-]
7	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [0/0]	437.60 (-) [437.60]	7.78 (0.00) [0]
8	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	108.20 (0.00) [0]
9	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	49.89 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [2/2023]	403.68 (-) [403.68]	108.53 (0.00) [-49]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [0/0]	543.05 (-) [543.05]	183.06 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [0/0]	450.65 (-) [450.65]	71.20 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [0/0]	486.70 (-) [486.70]	127.93 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [0/0]	560.39 (-) [560.39]	252.02 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25	3/2019	3/2027 (-)	347.78 (-)	168.44 (0.00)

	(PACKAGE		[0/0]	[347.78]	[0]
16	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [0/0]	394.27 (-) [394.27]	73.42 (0.00) [0]
17	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	3/2027 (-) [0/0]	342.55 (-) [342.55]	212.53 (0.00) [0]
18	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [0/0]	421.48 (-) [421.48]	79.40 (0.00) [0]
19	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (-) [12/2022]	200.44 (-) [200.44]	128.67 (0.00) [-]
20	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (-) [3/2022]	568.92 (-) [568.92]	360.28 (0.00) [-]
21	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (-) [12/2022]	188.78 (-) [188.78]	129.11 (0.00) [-]
22	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [3/2022]	245.79 (-) [245.79]	217.41 (0.00) [-]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (-) [3/2022]	1,718.59 (-) [1,718.59]	520.71 (0.00) [-]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	30.42 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	31.06 (0.00) [0]
26	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
27	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	9.31 (0.00) [0]
28	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
29	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022 (-) [4/2022]	228.71 (-) [228.71]	48.24 (0.00) [0]
30	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022 (-) [4/2022]	294.04 (-) [294.04]	91.30 (0.00) [0]
31	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022 (-) [4/2022]	199.03 (-) [199.03]	59.12 (0.00) [0]
32	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022 (-) [4/2022]	184.88 (-) [184.88]	48.06 (0.00) [0]
33	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
34	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
35	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [3/2022]	284.09 (-) [284.09]	197.27 (0.00) [59]

36	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	158.08 (57.56) [59]
37	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	159.83 (59.95) [59]
38	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	159.32 (53.83) [59]
39	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	61.40 (0.00) [0]
40	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (-) [4/2022]	175.06 (-) [175.06]	101.99 (0.00) [-]
41	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	87.87 (0.00) [-]
42	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [12/2021]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
43	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [9/2021]	182.55 (-) [182.55]	7.59 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
44	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2025) [3/2025]	1,142.00 (-) [1,232.00]	391.13 (90.00) [48]
	<u>Health And Family Welfare</u>				
45	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (890.14) [860.00]	446.44 (-15.00) [0]
46	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
47	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (3/2022) [3/2022]	224.75 (-) [198.00]	189.00 (-26.75) [19]
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2022]	543.91 (-) [638.60]	412.80 (94.69) [28]
49	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	30.01 (0.00) [0]
50	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	33.82 (0.00) [0]
51	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	940.95 (6,602.00) [0]
52	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	1,966.98 (-1,170.00) [0]
	<u>Railways</u>				
53	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,986.82 (717.68) [12]
54	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-)	870.96 (-)	1,646.66 (1,002.25)

			[3/2022]	[1,873.21]	[12]
55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2024]	385.20 (-) [1,145.79]	937.36 (760.59) [60]
	Road Transport And Highways				
56	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (6/2022) [6/2022]	268.08 (-) [390.73]	368.28 (122.65) [61]
57	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	31.46 (0.00) [0]
58	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
59	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	50.81 (0.00) [0]
60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	207.71 (0.00) [0]
61	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [4/2022]	588.95 (-) [588.95]	528.66 (0.00) [41]
62	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [3/2022]	289.99 (-) [289.99]	110.95 (0.00) [39]
63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	141.40 (0.00) [74]
64	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	113.03 (0.00) [0]
65	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	229.26 (0.00) [74]
66	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	624.88 (0.00) [0]
67	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	45.79 (0.00) [0]
68	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	64.22 (0.00) [0]
69	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.06 (0.00) [0]
70	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	33.72 (0.00) [0]
71	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	78.09 (0.00) [0]
72	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
73	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	169.08 (0.00) [0]
74	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE	10/2017	/ (-)	818.00 (-)	302.72 (0.00)

	STATE		[4/2023]	[818.00]	[-]
75	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	182.43 (0.00) [0]
76	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	389.26 (0.00) [46]
78	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	93.33 (0.00) [0]
79	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
80	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
81	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
82	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [0]
83	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (12/2022) [12/2022]	160.00 (-) [160.00]	135.75 (0.00) [15]
84	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [1/2023]	636.42 (-) [636.42]	55.56 (0.00) [1]
85	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
86	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	155.57 (0.00) [0]
87	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	27.45 (0.00) [0]
88	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	71.71 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				
89	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [1,311.05]	200.27 (732.43) [0]
	<u>Railways</u>				
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [14,322.00]	12,156.19 (9,867.83) [153]
	<u>Road Transport And Highways</u>				
91	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	50.50 (0.00) [0]
92	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	59.71 (0.00) [0]
93	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-)	365.53 (-)	91.93 (0.00)

			[8/2022]	[365.53]	[0]
94	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	42.83 (0.00) [0]
95	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	36.05 (0.00) [0]
96	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	11.12 (0.00) [0]
97	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
98	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
99	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	5.57 (0.00) [0]
100	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	46.59 (0.00) [0]
101	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
102	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
103	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	12.26 (0.00) [0]
104	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	167.94 (0.00) [0]
105	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	16.08 (0.00) [0]
106	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	10.48 (0.00) [0]
107	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	6.70 (0.00) [0]
108	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	6.41 (0.00) [0]
109	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
110	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	6.20 (0.00) [0]
111	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	22.78 (0.00) [0]
112	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	15.09 (0.00) [0]
113	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	6.59 (0.00) [0]

114	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [0]
	MEGHALAYA				
	Department Of Higher Education				
115	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (6/2022) [6/2022]	484.32 (429.70) [429.70]	233.00 (-54.62) [93]
	Doner				
116	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	149.33 (0.00) [0]
	Health And Family Welfare				
117	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [6/2022]	363.99 (-) [363.99]	274.40 (0.00) [49]
	Railways				
118	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (-) [4,083.02]	265.38 (3,176.56) [0]
	Road Transport And Highways				
119	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.47 (0.00) [0]
120	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [9/2022]	306.28 (-) [306.28]	135.84 (0.00) [40]
121	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	44.52 (0.00) [0]
122	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	301.78 (0.00) [0]
123	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	174.37 (0.00) [0]
124	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	66.51 (0.00) [0]
125	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	68.77 (0.00) [0]
126	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	211.57 (0.00) [0]
	MIZORAM				
	Railways				
127	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [6,527.00]	4,766.68 (4,133.53) [117]
	Road Transport And Highways				
128	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [4/2022]	205.95 (-) [205.95]	123.24 (0.00) [15]
129	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	384.74 (182.95) [0]
130	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (3/2022) [0/0]	186.96 (-) [322.24]	308.85 (135.28) [0]
131	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM	8/2010	10/2010	193.69	329.03

	71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD		(12/2022) [0/0]	(374.59) [327.92]	(134.23) [0]
132	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	32.96 (0.00) [0]
133	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	39.88 (0.00) [0]
134	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	70.76 (0.00) [0]
135	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	72.45 (0.00) [0]
136	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	120.63 (0.00) [0]
137	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	43.39 (0.00) [0]
138	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	16.96 (0.00) [0]
139	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	60.00 (0.00) [0]
140	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
141	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	140.92 (0.00) [43]
143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	642.96 (-) [642.96]	133.41 (0.00) [45]
144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	164.47 (0.00) [45]
145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	137.39 (0.00) [43]
146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	124.67 (0.00) [46]
147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	163.81 (0.00) [43]
148	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	75.58 (0.00) [55]
149	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	120.31 (0.00) [48]
150	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	978.43 (368.26) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				

151	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
152	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2026]	2,326.52 (-) [6,663.00]	1,534.31 (4,336.48) [132]
Road Transport And Highways					
153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	134.40 (0.00) [44]
154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	100.70 (0.00) [48]
155	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	183.30 (0.00) [0]
156	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	341.40 (0.00) [42]
157	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	156.49 (0.00) [50]
158	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	64.91 (0.00) [0]
159	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	79.81 (0.00) [0]
160	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	41.90 (0.00) [0]
161	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	72.60 (0.00) [0]
162	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	53.72 (0.00) [0]
163	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	101.27 (0.00) [0]
164	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	88.93 (0.00) [0]
165	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (4/2022) [0/0]	217.35 (-) [217.35]	115.36 (0.00) [0]
166	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	55.18 (0.00) [0]
167	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	7.02 (0.00) [0]
168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	33.95 (0.00) [0]
169	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	186.85 (0.00) [46]
170	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	120.99 (0.00) [0]

171	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	125.87 (0.00) [0]
172	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [3/2022]	215.12 (-) [215.12]	127.24 (0.00) [42]
173	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	82.09 (0.00) [0]
174	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	87.49 (0.00) [49]
175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	157.06 (0.00) [0]
176	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	134.89 (0.00) [0]
177	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	356.14 (13.93) [0]
178	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	312.71 (0.00) [0]
179	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [11/2020]	336.25 (-) [369.96]	322.13 (33.71) [0]
180	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
181	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	31.67 (0.00) [0]
182	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
183	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	167.62 (-) [167.62]	142.40 (0.00) [0]
184	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	9.39 (0.00) [0]
185	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [7/2022]	237.51 (-) [237.51]	110.76 (0.00) [-5]
	<u>SIKKIM</u>				
	<u>Railways</u>				
186	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [8,600.00]	2,504.91 (7,260.52) [96]
	<u>Road Transport And Highways</u>				
187	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
188	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
189	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	32.50 (0.00) [0]
190	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD	7/2020	4/2023	345.38	96.67

	TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV		(-) [4/2023]	(-) [345.38]	(0.00) [0]
191	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	76.84 (0.00) [0]
192	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	120.72 (0.00) [0]
193	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [4/2023]	375.80 (-) [375.80]	81.82 (0.00) [-]
194	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [3/2022]	290.05 (-) [290.05]	154.83 (0.00) [52]
195	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
196	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
197	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [5/2023]	402.94 (-) [402.94]	79.70 (0.00) [13]
198	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	48.15 (0.00) [0]
199	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	59.98 (0.00) [0]
200	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	42.83 (0.00) [0]
201	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
202	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
203	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
204	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [12/2021]	438.28 (-) [402.00]	398.21 (-36.28) [0]
	<u>Railways</u>				
205	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [9/2022]	569.63 (-) [708.73]	549.81 (139.10) [30]
	<u>Road Transport And Highways</u>				
206	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
207	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
208	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [10/2022]	247.76 (-) [247.76]	36.82 (0.00) [9]
209	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022	347.36	116.18

			(-) [1/2022]	(-) [347.36]	(0.00) [0]
210	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	13.63 (0.00) [0]
211	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	14.10 (0.00) [0]
212	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	87.79 (0.00) [0]
213	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	99.97 (0.00) [0]
214	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	12.02 (0.00) [0]
215	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	10.93 (0.00) [0]
216	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	14.79 (0.00) [0]
217	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	22.21 (0.00) [0]
218	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	47.29 (0.00) [0]
219	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	114.77 (0.00) [0]
220	STRENGTHENING OF CHURAI BARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	122.81 (0.00) [0]
221	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	86.74 (38.51) [0]
222	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [0]
	Total			1,28,771.33 (23,231.39) [1,81,822.59]	71,092.44 (53,051.26)

State wise Projects Costing Rs.150 crore and above (as on					28.02.2022)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (10/2022) [10/2022]	417.23 (-) [707.73]	507.91 (290.50) [49]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [3/2022]	409.85 (-) [409.85]	135.48 (0.00) [51]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	260.07 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [10/2021]	277.17 (-) [277.17]	202.59 (0.00) [0]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [3/2023]	262.97 (-) [262.97]	63.74 (0.00) [53]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [6/2021]	257.34 (-) [238.00]	214.90 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [12/2022]	391.00 (-) [391.00]	77.75 (0.00) [50]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [6/2022]	234.27 (-) [234.27]	75.22 (0.00) [44]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [10/2021]	237.80 (-) [238.00]	148.90 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (3/2023) [3/2023]	611.80 (-) [611.80]	88.95 (0.00) [0]
11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (12/2022) [12/2022]	177.10 (-) [177.10]	115.40 (0.00) [34]
	<u>Department Of Higher Education</u>				
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [7/2021]	186.00 (199.00) [210.60]	206.20 (24.60) [0]
13	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (-) [6/2023]	588.72 (-) [588.72]	142.46 (0.00) [9]
14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [11/2022]	655.34 (-) [655.34]	375.85 (0.00) [29]

	Health And Family Welfare				
15	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [3/2022]	601.02 (-) [601.02]	538.47 (0.00) [-]
16	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [2/2021]	272.19 (-) [280.00]	273.40 (7.81) [0]
	Petroleum				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [12/2021]	303.40 (-) [303.40]	224.20 (0.00) [0]
18	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (-) [8/2027]	2,880.00 (-) [2,880.00]	117.00 (0.00) [0]
19	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (9/2022) [9/2022]	466.00 (-) [466.00]	313.36 (0.00) [17]
20	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	291.62 (0.00) [25]
21	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY	9/2021	6/2024 (-) [6/2024]	160.00 (-) [160.00]	0.13 (0.00) [0]
22	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (5/2023) [5/2023]	34,012.00 (-) [31,040.00]	16,067.78 (-2,972.00) [35]
23	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [2/2023]	167.00 (-) [167.00]	22.01 (0.00) [7]
24	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	135.36 (0.00) [10]
25	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (3/2022) [9/2022]	316.20 (-) [316.20]	152.91 (0.00) [11]
26	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	30.88 (0.00) [0]
27	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [3/2022]	210.94 (-) [210.94]	130.17 (0.00) [7]
28	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [1/2022]	196.26 (-) [196.26]	107.95 (0.00) [0]
29	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2022]	20,928.00 (-) [26,264.00]	18,232.09 (5,336.00) [24]
	Railways				
30	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2025]	3,631.00 (-) [3,887.48]	1,495.93 (256.48) [36]
31	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2027]	1,045.20 (-) [2,120.16]	1,068.77 (1,074.96) [216]
32	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,499.71 (-) [2,499.71]	835.30 (0.00) [48]
33	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
34	VIJAYAWADA-GUDUR	4/2015	12/2023	3,246.26	3,683.68

			(-) [12/2023]	(-) [3,548.68]	(302.42) [0]
35	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [6/2022]	1,503.71 (-) [3,633.12]	3,925.76 (2,129.41) [27]
	<u>Road Transport And Highways</u>				
36	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (4/2021) [0/0]	1,226.88 (1,240.13) [1,321.60]	405.54 (94.72) [0]
37	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [0/0]	1,601.10 (-) [1,601.10]	111.79 (0.00) [0]
38	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
39	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	464.83 (0.00) [0]
40	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2022) [11/2022]	263.45 (263.45) [263.45]	122.71 (0.00) [62]
41	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (-) [5/2022]	429.43 (373.05) [373.05]	329.89 (-56.38) [54]
42	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [6/2022]	314.43 (-) [314.43]	85.61 (0.00) [-]
43	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD	8/2016	1/2017 (6/2022) [6/2022]	350.61 (-) [350.61]	328.03 (0.00) [65]
44	FOUR LANING OF 5,122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (1/2021) [0/0]	333.21 (-) [353.43]	334.89 (20.22) [0]
45	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [5/2022]	1,532.62 (-) [1,827.00]	1,766.52 (294.38) [14]
46	REHABILITATION AND UPGRADATION OF REPALLE TO EPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	1/2017	1/2018 (10/2022) [0/0]	576.48 (686.13) [686.13]	438.61 (109.65) [0]
47	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (5/2022) [7/2021]	348.95 (-) [348.95]	257.45 (0.00) [0]
48	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	3/2020	3/2021 (-) [4/2022]	207.79 (-) [207.79]	117.71 (0.00) [13]
49	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (6/2022) [6/2022]	386.09 (316.06) [316.06]	214.31 (-70.03) [73]
50	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (4/2022) [4/2022]	290.15 (290.15) [290.15]	164.56 (0.00) [59]
51	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	661.98 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (10/2022) [10/2022]	995.09 (995.00) [995.09]	609.49 (0.00) [77]
54	REHABILITATION AND UPGRADATION OF LOSARI-	3/2016	9/2016	444.84	365.54

	MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216		(5/2022) [5/2022]	(-) [444.84]	(0.00) [68]
55	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (-) [6/2022]	376.25 (-) [376.25]	335.69 (0.00) [58]
56	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (8/2022) [0/0]	289.67 (234.73) [234.73]	221.79 (-54.94) [0]
57	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (2/2022) [0/0]	504.19 (504.00) [504.19]	479.00 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (6/2021) [0/0]	271.45 (-) [271.45]	243.29 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (5/2022) [5/2022]	319.28 (319.28) [319.28]	222.37 (0.00) [57]
60	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (2/2022) [2/2022]	372.68 (309.37) [309.37]	270.19 (-63.31) [60]
61	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (7/2022) [0/0]	228.32 (202.83) [202.83]	148.81 (-25.49) [0]
62	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (2/2022) [0/0]	418.03 (386.99) [386.99]	350.05 (-31.04) [0]
63	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (-) [3/2023]	222.61 (-) [222.61]	11.71 (0.00) [24]
64	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/	1,959.00	1,389.19
65	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	(-) [10/2021]	(-) [1,959.00]	(0.00) [0]
66	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN	9/2018	1/2020 (8/2021) [0/0]	597.67 (570.98) [570.98]	346.85 (-26.69) [0]
67	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	2/2019 (4/2021) [0/0]	617.41 (655.64) [668.45]	546.69 (51.04) [0]
68	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/	1,550.98	1,666.08
69	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	(-) [9/2021]	(-) [1,550.98]	(0.00) [0]
70	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,287.35 (0.00) [0]
71	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	970.99 (145.48) [0]
72	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
73	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	6/2020	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	0.00 (0.00) [0]
74	POLAVARAM IRRIGATION PROJECT	2/2009	5/2021 (-) [12/2022]	221.40 (-) [221.40]	28.78 (0.00) [19]
	<u>Water Resources</u>				
74	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020	10,151.04	18,422.33

			(11/2021) [4/2022]	(55,548.87) [55,548.87]	(45,397.83) [25]
	ARUNACHAL PRADESH				
	Civil Aviation				
75	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH	2/2019	8/2022 (10/2023) [10/2023]	645.63 (-) [645.63]	296.53 (0.00) [14]
	Power				
76	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	15,300.08 (13,707.10) [155]
	Road Transport And Highways				
77	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (-) [394.00]	390.07 (0.00) [0]
78	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/	210.50	145.76
			(-) [10/2021]	(-) [210.50]	(0.00) [0]
79	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	3/2027 (-) [0/0]	496.47 (-) [496.47]	8.93 (0.00) [0]
80	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/	243.89	229.09
			(-) [2/2022]	(-) [243.89]	(0.00) [-]
81	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	3/2027 (-) [0/0]	437.60 (-) [437.60]	7.78 (0.00) [0]
82	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	108.20 (0.00) [0]
83	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	49.89 (0.00) [0]
84	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	3/2027 (-) [2/2023]	403.68 (-) [403.68]	108.53 (0.00) [-49]
85	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	3/2027 (-) [0/0]	543.05 (-) [543.05]	183.06 (0.00) [0]
86	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	3/2027 (-) [0/0]	450.65 (-) [450.65]	71.20 (0.00) [0]
87	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	3/2027 (-) [0/0]	486.70 (-) [486.70]	127.93 (0.00) [0]
88	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	3/2027 (-) [0/0]	560.39 (-) [560.39]	252.02 (0.00) [0]
89	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	3/2027 (-) [0/0]	347.78 (-) [347.78]	168.44 (0.00) [0]
90	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	3/2027 (-) [0/0]	394.27 (-) [394.27]	73.42 (0.00) [0]
91	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	3/2027 (-) [0/0]	342.55 (-) [342.55]	212.53 (0.00) [0]
92	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	3/2027 (-) [0/0]	421.48 (-) [421.48]	79.40 (0.00) [0]
93	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI	12/2016	/	200.44	128.67

	ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.		(-) [12/2022]	(-) [200.44]	(0.00) [-]
94	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/	568.92	360.28
			(-) [3/2022]	(-) [568.92]	(0.00) [-]
95	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/	188.78	129.11
			(-) [12/2022]	(-) [188.78]	(0.00) [-]
96	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/	245.79	217.41
			(-) [3/2022]	(-) [245.79]	(0.00) [-]
97	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/	1,718.59	520.71
			(-) [3/2022]	(-) [1,718.59]	(0.00) [-]
98	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022	301.06	30.42
			(-) [4/2022]	(-) [301.06]	(0.00) [0]
99	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022	353.90	31.06
			(-) [5/2022]	(-) [353.90]	(0.00) [0]
100	DEMBUEN - BRUNI	12/2020	3/2023	606.63	0.00
			(-) [3/2023]	(-) [606.63]	(0.00) [0]
101	DOGINALA - GAU	12/2020	9/2022	242.30	9.31
			(-) [9/2022]	(-) [242.30]	(0.00) [0]
102	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/	392.60	0.00
			(-) [0/0]	(-) [392.60]	(0.00) [0]
103	JORAM – KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3)	8/2020	4/2022	228.71	48.24
			(-) [4/2022]	(-) [228.71]	(0.00) [0]
104	JORAM – KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4)	8/2020	4/2022	294.04	91.30
			(-) [4/2022]	(-) [294.04]	(0.00) [0]
105	JORAM – KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6)	8/2020	4/2022	199.03	59.12
			(-) [4/2022]	(-) [199.03]	(0.00) [0]
106	JORAM – KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7)	8/2020	4/2022	184.88	48.06
			(-) [4/2022]	(-) [184.88]	(0.00) [0]
107	LADDA - BASAI	2/2021	4/2023	445.96	0.00
			(-) [4/2023]	(-) [445.96]	(0.00) [0]
108	TADADEGE - HENKAR	2/2021	3/2023	550.45	13.03
			(-) [3/2023]	(-) [550.45]	(0.00) [0]
109	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017	284.09	197.27
			(-) [3/2022]	(-) [284.09]	(0.00) [59]
110	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017	195.23	158.08
			(-) [3/2022]	(-) [252.79]	(57.56) [59]
111	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017	203.36	159.83
			(-) [3/2022]	(-) [263.31]	(59.95) [59]
112	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017	198.22	159.32
			(-) [3/2022]	(-) [252.05]	(53.83) [59]
113	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036	2/2017	4/2017	180.57	61.40
			(-)	(-)	(0.00)

	[EX		[2/2021]	[180.57]	[0]
114	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (-) [4/2022]	175.06 (-) [175.06]	101.99 (0.00) [-]
115	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	87.87 (0.00) [-]
116	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (-) [12/2021]	1,979.00 (-) [2,036.90]	1,251.08 (57.90) [0]
117	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	3/2027 (-) [9/2021]	182.55 (-) [182.55]	7.59 (0.00) [0]
	<u>ASSAM</u>				
	<u>Civil Aviation</u>				
118	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2025) [3/2025]	1,142.00 (-) [1,232.00]	391.13 (90.00) [48]
	<u>Health And Family Welfare</u>				
119	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [0/0]	875.00 (890.14) [860.00]	446.44 (-15.00) [0]
120	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	<u>Petroleum</u>				
121	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (3/2022) [3/2022]	224.75 (-) [198.00]	189.00 (-26.75) [19]
122	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [6/2022]	543.91 (-) [638.60]	412.80 (94.69) [28]
123	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN	5/2021	10/2023 (-) [10/2023]	412.00 (-) [412.00]	30.01 (0.00) [0]
124	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON	8/2021	2/2023 (-) [2/2023]	218.38 (-) [218.38]	33.82 (0.00) [0]
125	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-) [10/2024]	12,366.00 (-) [18,968.00]	940.95 (6,602.00) [0]
126	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [9,058.00]	1,966.98 (-1,170.00) [0]
	<u>Railways</u>				
127	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,986.82 (717.68) [12]
128	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,646.66 (1,002.25) [12]
129	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2024]	385.20 (-) [1,145.79]	937.36 (760.59) [60]
	<u>Road Transport And Highways</u>				
130	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (6/2022) [6/2022]	268.08 (-) [390.73]	368.28 (122.65) [61]
131	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	31.46 (0.00) [0]

132	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
133	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	50.81 (0.00) [0]
134	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	207.71 (0.00) [0]
135	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [4/2022]	588.95 (-) [588.95]	528.66 (0.00) [41]
136	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [3/2022]	289.99 (-) [289.99]	110.95 (0.00) [39]
137	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	141.40 (0.00) [74]
138	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	113.03 (0.00) [0]
139	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	229.26 (0.00) [74]
140	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	624.88 (0.00) [0]
141	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	45.79 (0.00) [0]
142	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [0/0]	166.94 (-) [166.94]	64.22 (0.00) [0]
143	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHESOVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN	2/2021	7/2025 (-) [7/2025]	925.47 (-) [925.47]	0.06 (0.00) [0]
144	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	33.72 (0.00) [0]
145	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	78.09 (0.00) [0]
146	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
147	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	169.08 (0.00) [0]
148	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [4/2023]	818.00 (-) [818.00]	302.72 (0.00) [-]
149	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	182.43 (0.00) [0]
150	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
151	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	389.26 (0.00) [46]
152	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023	804.00	93.33

			(-) [8/2023]	(-) [804.00]	(0.00) [0]
153	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
154	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
155	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
156	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	155.61 (0.00) [0]
157	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (12/2022) [12/2022]	160.00 (-) [160.00]	135.75 (0.00) [15]
158	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [1/2023]	636.42 (-) [636.42]	55.56 (0.00) [1]
159	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
160	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	155.57 (0.00) [0]
161	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	27.45 (0.00) [0]
162	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	71.71 (0.00) [0]
	BIHAR				
	<u>Civil Aviation</u>				
163	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (3/2024) [3/2024]	1,216.90 (-) [1,216.90]	283.65 (0.00) [17]
	<u>Department Of Higher Education</u>				
164	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2022]	496.18 (496.00) [498.99]	318.32 (2.81) [57]
165	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	125.38 (0.00) [26]
	<u>Petroleum</u>				
166	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	2,561.63 (0.00) [0]
167	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	12/2029 (-) [12/2029]	988.00 (-) [988.00]	49.65 (0.00) [0]
168	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	439.00 (-) [439.00]	133.31 (0.00) [0]
169	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (-) [8/2027]	176.00 (-) [176.00]	90.56 (0.00) [0]
170	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (-) [12/2029]	163.00 (-) [163.00]	28.39 (0.00) [0]
171	CGD PROJECT AT LAKHISARAI, MUNGER AND	6/2019	2/2028	347.00	114.50

	BHAGALPUR DISTRICTS		(-) [2/2028]	(-) [347.00]	(0.00) [0]
172	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	2,996.00 (-) [2,996.00]	329.06 (0.00) [0]
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2023]	359.25 (-) [359.25]	200.37 (0.00) [12]
174	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (3/2022) [3/2022]	522.00 (-) [522.00]	423.89 (0.00) [12]
175	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	112.94 (0.00) [22]
176	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021) [3/2022]	189.00 (-) [189.00]	185.52 (0.00) [14]
177	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (3/2022) [2/2022]	206.50 (-) [206.50]	174.10 (0.00) [11]
178	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	126.54 (0.00) [0]
	<u>Power</u>				
179	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	19,738.00 (12,619.14) [141]
180	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (-) [0/0]	5,353.00 (-) [10,566.00]	9,014.00 (5,213.00) [0]
181	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (-) [10,439.09]	4,677.91 (0.00) [0]
182	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [3/2022]	12,964.60 (19,413.00) [17,304.00]	16,748.00 (4,339.40) [46]
183	TRANSMISSION SYSTEM FOR POWER EVACUATION FROM ARUN-3 (900MW) HEP, NEPAL OF M/S SAPDC-INDIAN PORTION	5/2021	4/2023 (-) [4/2023]	179.29 (-) [179.29]	5.66 (0.00) [0]
	<u>Railways</u>				
184	ARARIA-SUPAUL (NL)	4/2008	/ (-) [12/2025]	1,605.17 (1,605.17) [1,605.17]	159.03 (0.00) [-]
185	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	2.55 (2,668.81) [-]
186	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2023]	378.56 (-) [1,893.55]	386.78 (1,514.99) [-]
187	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/ (-) [3/2024]	329.39 (1,483.14) [1,483.14]	1,469.46 (1,153.75) [-]
188	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [12/2024]	528.65 (2,066.78) [2,066.78]	1,610.87 (1,538.13) [-]
189	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [6/2023]	324.73 (967.29) [1,090.00]	1,093.59 (765.27) [135]
190	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (-) [12/2024]	548.00 (-) [819.01]	540.73 (271.01) [57]

191	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	353.25
			(-)	(614.45)	(451.58)
			[3/2025]	[614.45]	[-]
192	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	1,059.76
			(-)	(-)	(0.00)
			[5/2023]	[1,200.20]	[38]
193	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	4/2016	3/2021	731.64	452.12
			(-)	(1,185.73)	(454.09)
			[3/2024]	[1,185.73]	[36]
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	532.87	1,108.94
			(-)	(-)	(1,612.13)
			[3/2024]	[2,145.00]	[60]
195	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020	1,491.47	581.48
			(-)	(-)	(0.00)
			[3/2023]	[1,491.47]	[36]
196	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021	744.04	585.85
			(-)	(1,215.54)	(471.50)
			[12/2024]	[1,215.54]	[45]
197	SAKRI-HASANPUR ROAD (NL)	4/1999	/	325.00	392.88
			(-)	(735.20)	(410.20)
			[12/2024]	[735.20]	[-]
198	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	1,536.32
			(-)	(1,470.50)	(1,098.36)
			[3/2024]	[1,470.50]	[-]
199	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	320.25
			(-)	(519.33)	(139.33)
			[12/2024]	[519.33]	[-]
<u>Road Transport And Highways</u>					
200	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	578.00
			(-)	(-)	(79.46)
			[0/0]	[591.00]	[0]
201	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-)	(-)	(0.00)
			[0/0]	[375.09]	[0]
202	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	506.88
			(-)	(-)	(0.00)
			[0/0]	[575.00]	[0]
203	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	0.00
			(-)	(-)	(0.00)
			[0/0]	[581.84]	[0]
204	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020	464.09	60.06
			(-)	(-)	(0.00)
			[0/0]	[464.09]	[0]
205	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020	649.90	44.00
			(-)	(-)	(0.00)
			[0/0]	[649.90]	[0]
206	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020	446.97	0.00
			(-)	(-)	(0.00)
			[0/0]	[446.97]	[0]
207	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	2/2020	1,101.99	270.71
			(-)	(-)	(0.00)
			[0/0]	[1,101.99]	[0]
208	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/	2,926.42	370.19
			(-)	(-)	(0.00)
			[0/0]	[2,926.42]	[0]
209	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/	1,478.40	81.56
			(-)	(-)	(0.00)
			[0/0]	[1,478.40]	[0]
210	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00	363.79
			(-)	(-)	(-635.50)
			[0/0]	[1,962.50]	[0]

211	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	11.00 (-7.71) [0]
212	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/	496.20 (-) [537.17]	80.68 (40.97) [0]
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (6/2022) [6/2022]	683.83 (698.82) [698.82]	709.80 (14.99) [71]
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (6/2022) [6/2022]	178.85 (225.06) [225.06]	168.79 (46.21) [73]
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (3/2022) [3/2022]	553.30 (587.41) [587.41]	537.14 (34.11) [70]
216	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45 (-) [1,182.94]	296.90 (15.49) [0]
217	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41 (-) [681.67]	550.29 (39.26) [0]
218	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [0/0]	322.09 (-) [322.09]	217.73 (0.00) [0]
219	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (3/2022) [3/2022]	1,408.85 (2,138.16) [2,138.16]	1,241.55 (729.31) [65]
220	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04 (-) [10/2021]	846.15 (11.13) [0]
221	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07 (-) [556.07]	0.00 (0.00) [0]
222	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (7/2022) [7/2022]	1,041.10 (567.00) [639.58]	501.61 (-401.52) [39]
223	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.92 (0.00) [0]
224	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	1,199.64 (0.00) [0]
225	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (5/2022) [5/2022]	1,742.01 (-) [1,742.01]	1,605.30 (0.00) [65]
226	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70 (644.50) [726.99]	156.13 (153.29) [-]
227	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/	319.68 (404.10) [404.10]	345.06 (84.42) [-]
228	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/	675.00 (780.77) [780.77]	424.27 (105.77) [-]
229	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/	895.39 (-) [895.39]	0.00 (0.00) [0]
230	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (8/2018) [10/2023]	950.64 (1,161.00) [1,168.00]	354.24 (217.36) [74]
231	STRENGTHENING AND WIDENING TO 2 LANE WITH	3/2018	/	153.24	97.01

	PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH		(3/2022) [3/2022]	(-) [153.24]	(0.00) [-]
232	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80	1,034.54
			(-) [0/0]	(-) [1,038.56]	(183.76) [0]
233	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018	516.13	651.41
			(-) [0/0]	(-) [649.27]	(133.14) [0]
234	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (12/2018) [3/2023]	672.89 (736.01) [830.31]	105.50 (157.42) [36]
	<u>Urban Development</u>				
235	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024	13,365.77	307.63
			(-) [6/2024]	(-) [13,925.50]	(559.73) [0]
	<u>Water Resources</u>				
236	I AND D AND STP AT CHAPRA	11/2018	12/2020	236.15	66.51
			(-) [7/2022]	(-) [236.15]	(0.00) [19]
237	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020	254.13	0.07
			(-) [3/2024]	(-) [413.29]	(159.16) [42]
238	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021	268.63	380.87
			(-) [5/2022]	(-) [268.63]	(0.00) [16]
239	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021	230.06	98.80
			(-) [3/2023]	(-) [230.06]	(0.00) [20]
240	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021	305.19	44.87
			(-) [4/2023]	(-) [305.19]	(0.00) [20]
241	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021	294.02	38.57
			(-) [12/2023]	(-) [294.02]	(0.00) [26]
242	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021	356.37	154.13
			(-) [6/2022]	(-) [356.37]	(0.00) [14]
243	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022	824.00	101.12
			(-) [12/2023]	(-) [824.00]	(0.00) [18]
244	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022	578.89	42.75
			(-) [12/2023]	(-) [578.89]	(0.00) [18]
245	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020	225.77	299.08
			(-) [3/2022]	(-) [398.90]	(173.13) [24]
246	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021	277.42	263.52
			(-) [5/2022]	(-) [277.42]	(0.00) [12]
247	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020	191.62	74.10
			(-) [3/2022]	(-) [191.62]	(0.00) [16]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
248	AMERA OC RCE	2/2015	3/2018	335.97	48.36
			(-) [3/2023]	(-) [335.97]	(0.00) [60]
249	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020	316.10	152.47
			(-) [3/2023]	(-) [316.10]	(0.00) [36]
250	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029	2,309.80	362.52

			(-) [3/2029]	(-) [2,309.80]	(0.00) [0]
251	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2025]	610.63 (-) [610.63]	179.09 (0.00) [36]
252	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	1,881.55 (0.00) [0]
253	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	12.61 (0.00) [0]
254	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	4,768.67 (0.00) [0]
255	JAGANNATHPUR OC RCE (3.0 MTY)	7/2016	3/2020 (-) [3/2022]	459.49 (-) [459.49]	0.00 (0.00) [24]
256	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	190.30 (0.00) [0]
257	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	2.02 (0.00) [0]
258	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	9.23 (0.00) [144]
259	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	3,393.76 (0.00) [0]
260	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
261	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	63.39 (0.00) [0]
262	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2023]	321.50 (-) [321.50]	224.43 (0.00) [108]
263	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	10.32 (0.00) [0]
264	PORDA CHIMTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
265	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	86.57 (0.00) [0]
	<u>Department Of Higher Education</u>				
266	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [10/2022]	808.62 (-) [808.62]	318.94 (0.00) [3]
	<u>Petroleum</u>				
267	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	88.45 (0.00) [0]
	<u>Railways</u>				
268	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (6/2022) [6/2022]	393.98 (-) [393.98]	371.86 (0.00) [27]
269	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-)	2,288.00 (-)	1,078.79 (2,682.11)

			[9/2023]	[4,970.11]	[18]
270	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	833.36 (162.34) [33]
271	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [6/2022]	3,055.00 (-) [3,055.15]	2,800.17 (0.15) [45]
272	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2024]	1,160.00 (-) [1,160.83]	1,036.36 (0.83) [48]
273	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [6/2022]	1,402.02 (-) [1,300.00]	1,367.10 (-102.02) [27]
	Road Transport And Highways				
274	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	402.95 (231.09) [0]
275	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [0/0]	726.67 (-) [1,096.52]	518.73 (369.85) [0]
276	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
277	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
278	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [2/2022]	291.05 (-) [291.05]	252.61 (0.00) [-]
279	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (-) [4/2022]	335.32 (-) [335.32]	290.07 (0.00) [58]
280	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (-) [3/2022]	476.20 (544.00) [544.00]	402.15 (67.80) [66]
281	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (-) [6/2022]	496.02 (-) [496.02]	251.53 (0.00) [87]
282	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (-) [12/2022]	497.14 (-) [572.66]	288.50 (75.52) [76]
283	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (-) [6/2022]	624.98 (-) [731.50]	486.06 (106.52) [68]
284	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (-) [12/2022]	452.94 (-) [435.61]	128.55 (-17.33) [77]
285	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (-) [3/2022]	423.79 (-) [423.79]	298.70 (0.00) [50]
286	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (-) [3/2022]	188.80 (-) [188.80]	120.07 (0.00) [34]
287	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (-) [2/2022]	379.16 (-) [379.16]	338.42 (0.00) [51]
	Steel				
288	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (1/2022) [6/2022]	15,525.00 (-) [21,940.00]	19,611.48 (6,415.00) [85]
289	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023	2,907.00	636.12

			(-) [6/2024]	(-) [2,907.00]	(0.00) [12]
290	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	89.30 (0.00) [0]
	<u>Urban Development</u>				
291	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (-) [5/2023]	299.97 (-) [299.97]	27.44 (0.00) [32]
	<u>DELHI</u>				
	<u>Commerce</u>				
292	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	6/2018	10/2020 (-) [0/0]	302.64 (-) [302.64]	30.00 (0.00) [0]
	<u>Dpiit</u>				
293	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (-) [5/2022]	4,773.00 (-) [5,178.00]	3,062.37 (405.00) [29]
	<u>Health And Family Welfare</u>				
294	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [6/2021]	204.44 (-) [250.00]	249.24 (45.56) [0]
295	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
296	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [1/2022]	156.56 (-) [205.00]	191.36 (48.44) [0]
297	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2021]	414.11 (-) [586.50]	586.50 (172.39) [0]
	<u>Home Affairs</u>				
298	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI	6/2019	7/2022 (-) [12/2022]	277.35 (-) [290.33]	46.80 (12.98) [5]
299	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [6/2022]	1,219.21 (-) [2,000.00]	1,089.05 (780.79) [32]
	<u>Power</u>				
300	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (-) [3/2022]	1,394.52 (-) [1,394.52]	580.89 (0.00) [58]
	<u>Railways</u>				
301	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	167.23 (123.32) [-]
302	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [359.00]	118.38 (202.35) [-]
	<u>Renewable Energy</u>				
303	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [365.00]	282.96 (93.10) [0]
	<u>Telecommunications</u>				
304	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [3/2022]	248.20 (-) [248.20]	173.87 (0.00) [48]
	<u>Urban Development</u>				
305	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [2/2022]	197.33 (-) [217.00]	187.17 (19.67) [34]

306	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-) [3/2025]	24,948.65 (-) [24,948.65]	2,949.03 (0.00) [0]
307	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (9/2021) [0/0]	565.00 (-) [565.00]	498.21 (0.00) [0]
308	DELHI MRTS PHASE-III	9/2011	3/2016 (8/2021) [0/0]	38,585.00 (-) [40,180.91]	39,728.58 (1,595.91) [0]
309	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (6/2024) [6/2024]	1,180.00 (-) [1,100.80]	35.90 (-79.20) [35]
310	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (4/2022) [4/2022]	392.00 (-) [392.00]	204.84 (0.00) [20]
311	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (6/2024) [6/2024]	1,128.00 (-) [1,128.00]	30.00 (0.00) [27]
312	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (6/2022) [6/2022]	422.00 (-) [422.00]	139.55 (0.00) [15]
313	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [3/2023]	2,694.00 (-) [2,694.00]	1,034.98 (0.00) [-]
	<u>Water Resources</u>				
314	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
315	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [2/2022]	515.07 (-) [515.07]	363.66 (0.00) [13]
316	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [942.18]	261.19 (276.40) [0]
317	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	261.19 (0.00) [12]
318	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	176.36 (0.00) [10]
	<u>GOA</u>				
	<u>Department Of Higher Education</u>				
319	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [2/2023]	303.90 (-) [303.90]	61.00 (0.00) [35]
	<u>Health And Family Welfare</u>				
320	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2021]	249.01 (-) [249.07]	245.78 (0.06) [0]
	<u>Road Transport And Highways</u>				
321	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (2/2019) [1/2020]	280.16 (-) [290.59]	244.36 (10.43) [0]
322	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (12/2021) [12/2021]	184.05 (-) [184.05]	118.37 (0.00) [0]
323	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE	10/2015	/ (9/2022) [12/2022]	936.40 (-) [936.40]	560.12 (0.00) [-]
324	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00)	3/2015	/ (12/2021) [12/2021]	298.33 (354.43)	325.55 (0.00)

	TO K		[3/2022]	[298.33]	[-]
325	KARASWADA TO BAMBOLIM	3/2017	12/2019 (-) [3/2022]	852.67 (-) [852.67]	225.16 (0.00) [27]
326	PATRADEVI TO KARASWADA 4L	3/2017	5/2020 (-) [6/2022]	634.32 (-) [634.32]	329.59 (0.00) [25]
327	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [3/2022]	773.98 (-) [773.98]	400.90 (0.00) [-]
328	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [3/2022]	819.95 (-) [819.95]	410.10 (0.00) [-]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
329	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (-) [12/2022]	11,459.00 (19,220.00) [19,220.00]	17,806.00 (7,761.00) [84]
	<u>Civil Aviation</u>				
330	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022 (8/2023) [8/2023]	1,405.00 (-) [1,405.00]	439.69 (0.00) [12]
	<u>Petroleum</u>				
331	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023 (-) [5/2023]	5,251.00 (-) [5,251.00]	836.13 (0.00) [0]
332	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (5/2023) [5/2023]	588.20 (-) [730.20]	226.83 (142.00) [-]
333	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023 (-) [8/2023]	1,614.00 (-) [1,614.00]	66.18 (0.00) [0]
334	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [6/2022]	327.78 (-) [220.00]	200.10 (-107.78) [50]
335	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2021) [7/2022]	906.00 (-) [906.00]	376.32 (0.00) [29]
336	LAB REVAMP AT GUJARAT REFINERY	10/2019	4/2022 (-) [4/2022]	403.00 (-) [403.00]	208.61 (0.00) [0]
337	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024 (-) [8/2024]	18,936.00 (-) [18,936.00]	953.51 (0.00) [-1]
338	REDEVELOPMENT OF LINCH FIELD	4/2021	3/2025 (-) [3/2025]	631.03 (-) [631.03]	228.08 (0.00) [0]
339	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022 (-) [8/2022]	444.87 (-) [444.87]	171.45 (0.00) [0]
340	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (-) [3/2026]	1,162.56 (-) [1,162.56]	947.93 (0.00) [0]
341	REDEVELOPMENT OF SOBHASAN COMPLEX	8/2021	2/2026 (-) [2/2026]	885.63 (-) [885.63]	206.93 (0.00) [0]
342	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022 (-) [12/2022]	1,378.00 (-) [1,378.00]	187.71 (0.00) [0]
343	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND	9/2018	2/2021 (-)	225.54 (-)	120.91 (22.36)

	PIPELINE CONNECTI		[10/2022]	[247.90]	[20]
	<u>Power</u>				
344	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR)	5/2021	9/2022 (-) [9/2022]	674.92 (-) [674.92]	76.91 (0.00) [0]
345	Bagodara Solar Power Project	5/2021	10/2022 (-) [10/2022]	296.20 (-) [296.20]	0.43 (0.00) [0]
346	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (-) [7/2022]	842.27 (-) [842.27]	93.92 (0.00) [0]
347	KAWAS SOLAR 56 MW	8/2020	10/2021 (-) [10/2022]	261.80 (-) [293.03]	118.68 (31.23) [12]
348	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BHUJ-II (2000 MW) IN GUJARAT	10/2019	8/2021 (-) [8/2021]	1,031.00 (-) [1,031.00]	654.77 (0.00) [0]
	<u>Railways</u>				
349	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (-) [3/2024]	829.74 (-) [2,223.37]	1,996.61 (1,393.63) [48]
350	ANAND GODHRA DOUBLING PROJECT 79 KMS	4/2017	3/2020 (-) [3/2024]	692.25 (-) [742.88]	2.26 (50.63) [48]
351	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [10/2023]	318.24 (-) [321.62]	126.35 (3.38) [139]
352	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [5/2022]	644.38 (-) [923.28]	995.52 (278.90) [14]
353	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS	4/2018	3/2024 (-) [12/2024]	537.31 (-) [537.31]	0.64 (0.00) [9]
354	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [10/2025]	844.10 (-) [844.10]	294.10 (0.00) [-]
355	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
356	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2022]	1,548.66 (-) [2,538.01]	2,234.42 (989.35) [12]
357	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (-) [3/2025]	320.66 (-) [1,378.11]	558.66 (1,057.45) [72]
358	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (-) [12/2022]	1,002.39 (1,016.39) [1,056.11]	808.35 (53.72) [21]
359	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (-) [12/2022]	1,037.15 (-) [1,383.69]	1,250.31 (346.54) [21]
360	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [528.49]	123.75 (280.23) [0]
	<u>Road Transport And Highways</u>				
361	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	199.86 (0.00) [0]
362	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	311.41 (0.00) [0]

363	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [0/0]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
364	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	439.98 (0.00) [0]
365	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
366	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]
367	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,043.00]	2,021.55 (-659.05) [0]
368	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [5/2022]	400.76 (394.44) [394.44]	188.34 (-6.32) [36]
369	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [12/2022]	962.43 (-) [962.43]	455.49 (0.00) [57]
370	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (6/2021) [7/2022]	867.97 (913.49) [913.49]	645.24 (45.52) [44]
371	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	772.39 (0.00) [0]
372	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	528.22 (0.00) [0]
373	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	427.78 (0.00) [0]
374	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.44 (0.00) [0]
375	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
376	KANDLA - MUNDRA PORT	1/2011	7/2013 (3/2020) [3/2022]	953.88 (1,066.87) [953.88]	93.63 (0.00) [104]
377	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [0/0]	1,052.21 (-) [1,361.00]	461.82 (308.79) [0]
378	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,361.00]	461.82 (109.89) [0]
379	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
380	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2022]	351.00 (255.00) [255.00]	195.11 (-96.00) [12]
381	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEE	3/2018	11/2018 (-) [7/2021]	464.07 (-) [464.07]	319.03 (0.00) [0]
	<u>Urban Development</u>				
382	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,925.22]	10,015.98 (2,152.22) [44]

383	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	431.21 (0.00) [0]
384	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [6/2024]	12,020.32 (-) [12,020.32]	439.23 (0.00) [3]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
385	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [1/2022]	215.92 (-) [215.92]	186.27 (0.00) [0]
	<u>Health And Family Welfare</u>				
386	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [4/2020]	505.58 (-) [586.96]	586.96 (81.38) [0]
	<u>Home Affairs</u>				
387	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (4/2024) [4/2024]	166.98 (166.98) [166.98]	7.84 (0.00) [6]
	<u>Petroleum</u>				
388	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	538.73 (0.00) [0]
389	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [8/2022]	909.00 (-) [909.00]	551.04 (0.00) [19]
390	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (7/2022) [7/2022]	206.63 (340.76) [340.76]	172.39 (134.13) [29]
391	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (-) [2/2027]	520.00 (-) [520.00]	215.09 (0.00) [5]
392	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [8/2022]	164.69 (-) [164.69]	45.60 (0.00) [13]
393	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (7/2022) [7/2022]	598.00 (753.89) [753.89]	495.80 (155.89) [29]
394	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	12/2018	6/2021 (7/2022) [7/2022]	278.60 (-) [278.60]	139.82 (0.00) [13]
395	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [9/2022]	1,636.00 (-) [1,636.00]	1,012.58 (0.00) [25]
396	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	12/2021 (1/2023) [1/2023]	1,255.00 (-) [1,255.00]	473.01 (0.00) [13]
397	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (3,219.94) [2,281.94]	703.22 (0.00) [7]
398	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (12/2021) [4/2022]	286.42 (327.00) [327.01]	233.20 (40.59) [20]
	<u>Power</u>				
399	IMPLEMENTATION OF 500 MVAR THYRISTOR CONTROLLED REACTOR AT KURUKSHETRA	1/2019	3/2022 (-) [3/2022]	267.33 (-) [267.33]	31.72 (0.00) [0]
	<u>Railways</u>				
400	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [0/0]	287.00 (-) [893.45]	760.84 (606.45) [0]

	Road Transport And Highways				
401	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2018 (-) [0/0]	991.59 (-) [507.70]	0.00 (-483.89) [0]
402	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	0.00 (-37.12) [0]
403	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2021]	2,128.72 (2,408.72) [2,408.72]	1,577.44 (280.00) [0]
404	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [10/2022]	247.25 (-) [247.25]	186.63 (0.00) [43]
405	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [12/2020]	1,484.30 (-) [1,484.30]	739.08 (0.00) [0]
406	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
407	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (5/2022) [5/2022]	996.65 (1,173.65) [1,173.65]	1,070.65 (177.00) [-]
408	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (4/2022) [4/2022]	1,243.45 (1,407.35) [1,407.35]	1,162.45 (163.90) [-]
409	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (5/2022) [5/2022]	889.36 (986.10) [986.10]	837.89 (96.74) [-]
410	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (5/2022) [5/2022]	1,018.79 (1,072.08) [1,072.08]	956.46 (53.29) [-]
411	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (5/2022) [5/2022]	1,051.91 (1,118.07) [1,118.07]	957.15 (66.16) [-]
412	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (7/2022) [7/2022]	1,120.06 (1,206.48) [1,206.48]	1,006.03 (86.42) [-]
413	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (6/2022) [6/2022]	1,137.42 (1,238.29) [1,238.29]	1,111.87 (100.87) [-]
414	ISMAILABAD-NARNAUL PKG-8	1/2019	/ (3/2022) [3/2022]	1,033.19 (1,044.32) [1,044.32]	899.01 (11.13) [-]
415	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [0/0]	275.12 (-) [275.12]	214.83 (0.00) [0]
416	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	191.96 (0.00) [0]
417	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [0/0]	198.05 (-) [198.05]	170.71 (0.00) [0]
418	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/ (-) [2/2018]	795.50 (-) [922.64]	387.49 (127.14) [0]
419	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [2/2018]	634.70 (-) [925.96]	341.09 (291.26) [0]
	HIMACHAL PRADESH				
	Department Of Higher Education				
420	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT	11/2012	11/2014	270.83	243.03

	MANDI AT KAMAND		(11/2021) [11/2021]	(-) [244.00]	(-26.83) [0]
421	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022 (10/2022) [10/2022]	392.51 (-) [392.51]	85.88 (0.00) [4]
	<u>Health And Family Welfare</u>				
422	AIIMS BILASPUR	4/2018	9/2021 (-) [6/2022]	1,351.00 (-) [1,471.00]	1,089.38 (120.00) [9]
423	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021 (-) [5/2022]	260.00 (-) [260.00]	25.38 (0.00) [11]
	<u>Power</u>				
424	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025 (-) [11/2025]	687.97 (-) [687.97]	215.23 (0.00) [0]
425	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026 (-) [1/2026]	1,810.56 (-) [1,810.56]	622.39 (0.00) [0]
426	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (3/2023) [3/2023]	3,919.59 (9,897.59) [9,897.59]	9,558.69 (5,978.00) [162]
	<u>Railways</u>				
427	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [3/2025]	2,966.99 (-) [6,753.42]	2,006.69 (3,786.43) [-21]
	<u>Road Transport And Highways</u>				
428	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	1,079.89 (0.00) [0]
429	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
430	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (3/2021) [0/0]	934.46 (-) [1,457.82]	1,347.64 (523.36) [0]
431	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (11/2022) [0/0]	478.74 (-) [1,135.08]	802.65 (656.34) [0]
432	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	905.56 (0.00) [0]
433	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	1,344.55 (0.00) [0]
434	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI-SHRI KYARI SECTION (KM 50.000 TO K	2/2021	9/2021 (-) [0/0]	345.89 (-) [345.89]	27.32 (0.00) [0]
435	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [0/0]	242.80 (-) [242.80]	22.78 (0.00) [0]
436	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [0/0]	272.98 (-) [272.98]	14.07 (0.00) [0]
437	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [0/0]	349.20 (-) [349.20]	110.47 (0.00) [0]
438	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	<u>JAMMU AND KASHMIR</u>				

	<u>Department Of Higher Education</u>				
439	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (4/2023) [4/2023]	676.00 (676.00) [676.00]	42.51 (0.00) [0]
440	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (10/2022) [10/2022]	424.93 (-) [424.93]	86.21 (0.00) [3]
	<u>Health And Family Welfare</u>				
441	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	232.40 (0.00) [-16]
442	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	439.65 (0.00) [0]
	<u>Power</u>				
443	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (8/2024) [7/2025]	4,287.59 (-) [4,287.59]	670.22 (0.00) [-]
444	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (7/2025) [7/2025]	8,112.12 (-) [8,112.12]	2,169.01 (0.00) [63]
	<u>Railways</u>				
445	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (4/2023) [4/2023]	2,500.00 (27,949.00) [37,012.26]	27,846.00 (34,512.26) [245]
	<u>Road Transport And Highways</u>				
446	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D	8/2020	9/2026 (-) [9/2026]	6,808.69 (-) [6,808.69]	439.59 (0.00) [0]
447	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (-) [1,339.00]	1,058.70 (-132.75) [0]
448	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	878.00 (0.00) [0]
449	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	0.00 (0.00) [0]
450	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [0/0]	2,168.66 (-) [2,168.66]	1,158.40 (0.00) [0]
451	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,763.58 (0.00) [0]
452	GOHA-KHELLANI PKG-3	2/2021	3/2023 (-) [3/2023]	431.28 (-) [431.28]	40.41 (0.00) [0]
453	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,654.58 (0.00) [0]
454	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	78.46 (0.00) [0]
455	KHELLANI-KHANABAL PKG-2	7/2021	2/2023 (-) [2/2023]	512.43 (-) [512.43]	16.50 (0.00) [0]
456	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	11.84 (0.00) [0]
457	KHELLANI-KHANABAL PKG-4	7/2021	8/2023 (-)	859.67 (-)	9.03 (0.00)

			[8/2023]	[859.67]	[0]
458	KHELLANI-KHANABAL PKG-5	7/2021	2/2023 (-) [2/2023]	497.09 (-) [497.09]	10.16 (0.00) [0]
459	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	36.42 (0.00) [0]
460	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,758.92 (360.00) [0]
461	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,116.66 (0.00) [0]
462	SRINAGAR TO BANIHAI	6/2011	6/2014 (-) [9/2022]	1,100.70 (-) [1,100.70]	2,933.43 (0.00) [99]
463	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	29.96 (0.00) [0]
464	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	25.14 (0.00) [0]
465	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [12/2022]	253.44 (-) [253.44]	92.24 (0.00) [41]
466	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [5/2022]	404.17 (-) [404.17]	246.27 (0.00) [45]
467	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [8/2022]	216.00 (-) [216.00]	120.10 (0.00) [45]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
468	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	165.05 (0.00) [0]
469	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2023]	163.51 (-) [163.51]	124.86 (0.00) [144]
470	EXPANSION PROJECT AMRAPALI OCP	8/2020	3/2028 (-) [3/2028]	5,136.15 (-) [5,136.15]	0.00 (0.00) [0]
471	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	260.95 (0.00) [0]
472	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2023]	162.46 (-) [162.46]	98.68 (0.00) [108]
473	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [3/2022]	289.45 (-) [289.45]	288.42 (0.00) [94]
474	MOONIDIH XV SEAM UG	8/2011	3/2019 (-) [4/2024]	1,230.27 (-) [1,230.27]	515.18 (0.00) [61]
475	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2025]	339.88 (-) [339.88]	91.62 (0.00) [138]
476	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2023]	555.52 (-) [555.52]	5.87 (0.00) [24]
477	PACHWARA SOUTH COAL BLOCK	7/2013	9/2028	1,795.01	38.76

			(-) [9/2023]	(-) [1,795.01]	(0.00) [-60]
478	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [6/2023]	243.00 (-) [334.27]	32.60 (91.27) [62]
479	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2023]	510.85 (-) [510.85]	502.12 (0.00) [84]
480	REVISED PROJECT REPORT MAGADH EXPANSION OCP	8/2020	3/2028 (-) [3/2028]	7,254.37 (-) [7,254.37]	0.00 (0.00) [0]
481	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	42.98 (0.00) [0]
482	UCE OF EPR OF NORTH URIMARI OCP	7/2021	3/2026 (-) [3/2026]	778.80 (-) [778.80]	0.00 (0.00) [0]
	<u>Department Of Higher Education</u>				
483	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (3/2022) [3/2022]	171.86 (171.86) [171.86]	144.27 (0.00) [72]
	<u>Petroleum</u>				
484	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [3/2022]	161.50 (-) [161.50]	136.30 (0.00) [21]
485	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (-) [12/2029]	613.00 (-) [613.00]	171.20 (0.00) [0]
486	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	152.67 (0.00) [0]
487	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [8/2023]	221.45 (-) [221.45]	113.23 (0.00) [10]
488	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	784.66 (314.52) [-12]
489	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [9/2022]	248.55 (-) [248.55]	149.47 (0.00) [3]
	<u>Power</u>				
490	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [1/2024]	14,366.58 (17,007.00) [17,007.00]	12,634.00 (2,640.42) [55]
491	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (4/2019) [0/0]	4,237.96 (4,238.00) [5,289.25]	3,776.81 (1,051.29) [0]
492	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [2/2025]	18,668.00 (-) [17,667.00]	5,021.00 (-1,001.00) [23]
	<u>Railways</u>				
493	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2023]	1,724.20 (-) [1,724.20]	1,153.09 (0.00) [33]
494	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [7/2022]	1,033.07 (3,020.95) [3,650.00]	3,679.49 (2,616.93) [-]
495	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [3/2024]	459.91 (1,625.87) [1,625.87]	981.50 (1,165.96) [-]
496	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI	4/2018	6/2022	428.65	1.62

	WITH Y CONNECTION (17.2 KM)		(-) [12/2025]	(-) [472.50]	(43.85) [42]
497	TALGARIA TO BOKARO N/CABIN DOUBLING(38 KM)	4/2018	12/2021 (-) [1/2023]	390.39 (-) [511.75]	149.63 (121.36) [13]
	<u>Road Transport And Highways</u>				
498	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (2/2023) [2/2023]	1,005.08 (-) [1,005.08]	0.00 (0.00) [-]
499	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	123.65 (2.71) [0]
500	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [355.24]	322.26 (31.52) [0]
501	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [950.49]	537.17 (-204.67) [0]
502	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [486.00]	406.73 (27.97) [0]
503	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	109.08 (0.00) [0]
	<u>Steel</u>				
504	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [11/2022]	1,034.01 (-) [1,034.01]	572.49 (0.00) [61]
505	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (2/2022) [5/2022]	262.87 (-) [262.87]	212.42 (0.00) [35]
	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
506	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (3/2022) [6/2022]	246.31 (210.00) [200.00]	168.90 (-46.31) [28]
	<u>Department Of Higher Education</u>				
507	C/O ADDITIONAL INFRASTRUCTURE AT IISC, BANGALORE.SH- RCC MONOLITHIC FOR MEN HOSTEL(S 14), WOMEN HOST	8/2021	11/2021 (-) [0/0]	316.25 (-) [316.25]	0.00 (0.00) [0]
508	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [10/2022]	851.00 (851.00) [851.00]	361.47 (0.00) [7]
	<u>Petroleum</u>				
509	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [3/2022]	1,810.00 (1,810.00) [1,810.00]	1,809.28 (0.00) [27]
510	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	185.98 (0.00) [0]
511	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (1/2024) [1/2024]	200.00 (304.00) [304.00]	2.61 (104.00) [7]
512	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	1,539.20 (0.00) [0]
513	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (3/2022) [3/2022]	380.00 (-) [380.00]	348.51 (0.00) [4]
	<u>Railways</u>				
514	ARSIKERE-TUMKUR	3/2015	3/2020	578.00	674.14

			(-) [2/2022]	(-) [758.36]	(180.36) [23]
515	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2026]	986.30 (-) [1,530.09]	326.02 (543.79) [129]
516	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2028]	1,382.78 (-) [1,383.00]	7.35 (0.22) [312]
517	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [3/2027]	327.25 (-) [367.77]	0.00 (40.52) [-]
518	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [3/2028]	558.00 (-) [692.43]	0.00 (134.43) [-]
519	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	401.14 (0.00) [78]
520	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [3,300.00]	2,564.14 (1,173.00) [0]
521	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [12/2022]	1,156.94 (-) [1,954.21]	1,238.40 (797.27) [33]
522	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [3/2028]	2,315.00 (-) [5,174.30]	158.11 (2,859.30) [-]
523	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2026]	644.78 (-) [817.23]	495.18 (172.45) [108]
524	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [3/2024]	279.54 (-) [279.54]	37.12 (0.00) [96]
525	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2026]	832.47 (-) [832.47]	0.94 (0.00) [120]
526	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [3/2025]	1,801.01 (-) [2,000.97]	83.08 (199.96) [-]
527	WHITE FIELD-KOLAR NL	4/2011	/ (-) [3/2025]	348.85 (-) [348.85]	0.36 (0.00) [-]
	Road Transport And Highways				
528	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [6/2023]	1,167.42 (-) [870.00]	348.00 (-297.42) [51]
529	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	171.98 (0.00) [0]
530	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (3/2023) [3/2023]	1,655.01 (2,639.00) [1,655.01]	1,867.51 (0.00) [79]
531	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [3/2022]	701.40 (-) [701.40]	435.62 (0.00) [36]
532	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (10/2021) [10/2021]	870.00 (1,418.78) [1,418.78]	36.30 (548.78) [0]
533	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019 (12/2022) [12/2022]	423.15 (-) [423.15]	159.07 (0.00) [36]
534	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865	2/2017	5/2019	157.32	0.95

	ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION		(-) [0/0]	(187.61) [157.32]	(0.00) [0]
535	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [0/0]	171.60 (-) [171.60]	86.09 (0.00) [0]
536	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [0/0]	1,388.00 (-) [1,388.00]	1,311.10 (0.00) [0]
537	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	1,232.91 (0.00) [0]
538	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (7/2022) [7/2022]	946.00 (1,046.56) [946.00]	818.53 (0.00) [49]
539	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [386.41]	351.36 (60.55) [0]
540	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	172.75 (0.00) [0]
541	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2	3/2018	6/2019 (-) [0/0]	159.97 (-) [159.97]	79.74 (0.00) [0]
542	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,319.54 (440.84) [0]
543	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
544	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,547.20 (272.20) [0]
545	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,442.06 (404.66) [0]
546	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	122.21 (0.00) [0]
547	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [9/2019]	709.00 (-) [709.00]	541.35 (0.00) [0]
548	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (-) [1,108.00]	1,482.29 (157.31) [0]
549	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	303.49 (0.00) [0]
550	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	228.23 (0.00) [0]
551	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	239.82 (0.00) [0]
552	WIDENING TO 2-LANE WIH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (-) [0/0]	264.34 (-) [264.34]	187.00 (0.00) [0]
553	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	111.52 (0.00) [0]
554	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI	1/2017	8/2017 (-)	291.49 (-)	226.46 (0.00)

	SECTION U		[0/0]	[291.49]	[0]
555	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [264.34]	187.00 (97.67) [0]
556	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [318.28]	234.82 (20.98) [0]
557	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	122.86 (0.00) [0]
558	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	127.96 (0.00) [0]
	<u>Urban Development</u>				
559	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B	6/2021	6/2026 (-) [6/2026]	14,788.10 (-) [14,788.10]	2,290.84 (0.00) [0]
560	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2021 (-) [3/2025]	26,405.14 (-) [26,405.14]	20,025.67 (0.00) [49]
	<u>KERALA</u>				
	<u>Department Of Higher Education</u>				
561	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [2/2023]	753.63 (-) [753.63]	234.20 (0.00) [23]
562	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [0/0]	165.23 (-) [165.23]	118.52 (0.00) [0]
	<u>Health And Family Welfare</u>				
563	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	74.24 (0.00) [0]
	<u>Petroleum</u>				
564	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2023]	1,112.00 (-) [1,507.24]	855.28 (395.24) [44]
565	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [12/2022]	607.06 (1,236.00) [1,236.00]	568.65 (628.94) [62]
566	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	425.30 (0.00) [0]
	<u>Power</u>				
567	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (1/2022) [7/2022]	403.62 (-) [403.62]	123.49 (0.00) [13]
	<u>Railways</u>				
568	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (-) [2,815.62]	264.51 (1,249.62) [0]
569	ERNAKULAM-KUMBALAM	4/2010	/ (-) [3/2025]	189.24 (-) [448.10]	268.74 (258.86) [-]
570	KUMBALAM-TURAVUR	4/2011	/ (-) [3/2025]	252.96 (-) [709.69]	256.71 (456.73) [-]
571	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
572	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-)	1,431.90 (-)	942.65 (0.00)

			[3/2024]	[1,431.90]	[-]
573	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [3/2025]	1,000.00 (-) [1,339.00]	0.83 (339.00) [-]
	<u>Road Transport And Highways</u>				
574	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (1/2020) [1/2020]	845.24 (-) [941.00]	902.51 (95.76) [0]
575	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018 (12/2021) [5/2022]	804.97 (-) [804.97]	600.78 (0.00) [47]
576	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (12/2021) [5/2022]	1,124.11 (-) [1,300.00]	971.90 (175.89) [56]
577	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,853.42]	14.19 (428.65) [0]
578	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [0/0]	617.00 (-) [617.00]	0.00 (0.00) [0]
579	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK	2/2017	8/2017 (-) [0/0]	294.28 (-) [294.26]	184.57 (-0.02) [0]
580	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (-) [0/0]	380.76 (-) [380.76]	263.70 (0.00) [0]
	<u>Urban Development</u>				
581	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [9/2020]	5,181.79 (-) [6,218.14]	6,065.82 (1,036.35) [0]
	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
582	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (12/2023) [12/2023]	346.27 (-) [480.33]	145.28 (134.06) [27]
	<u>Road Transport And Highways</u>				
583	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	10.11 (0.00) [0]
584	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	1.98 (0.00) [0]
585	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	8.23 (0.00) [0]
586	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	48.49 (0.00) [0]
587	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	36.62 (0.00) [0]
588	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	38.81 (0.00) [0]
589	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	9.04 (0.00) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
590	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (3/2023)	412.24 (-)	243.86 (0.00)

			[3/2023]	[412.24]	[21]
	<u>Coal</u>				
591	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2025]	869.44 (-) [869.44]	137.22 (0.00) [48]
592	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
593	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	2.59 (0.00) [0]
594	BATURA WEST OC PROJECT (0.80 MTPA)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
595	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	2.45 (0.00) [0]
596	DHANKASA UG (RECAST) (1 MTPA)	2/2020	3/2025 (-) [3/2025]	289.30 (-) [289.30]	0.00 (0.00) [0]
597	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	584.00 (0.00) [12]
598	GANDHIGRAM UG MINE	8/2019	3/2026 (-) [3/2026]	414.16 (-) [414.16]	2.65 (0.00) [0]
599	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2023]	1,783.09 (-) [1,783.09]	954.78 (0.00) [24]
600	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	79.50 (0.00) [36]
601	NIGAH EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
602	RAJNAGAR OCP RPR (1.70 MTPA)	12/2014	3/2021 (-) [0/0]	357.80 (-) [357.80]	86.60 (0.00) [0]
603	RAMPUR BATURA OC (4.0 MTPA)	7/2019	3/2026 (-) [3/2026]	1,248.93 (-) [1,248.93]	0.00 (0.00) [0]
604	RPR FOR JAMUNIA UG	8/2020	3/2026 (-) [3/2026]	281.25 (-) [281.25]	0.00 (0.00) [0]
605	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
606	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (-) [2/2027]	177.00 (-) [177.00]	68.94 (0.00) [0]
607	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (12/2021) [12/2021]	236.00 (319.61) [319.61]	237.99 (83.61) [0]
	<u>Power</u>				
608	AMELIA COAL MINE	1/2017	9/2020 (-) [8/2022]	2,104.21 (-) [1,587.16]	663.84 (-517.05) [23]
	<u>Railways</u>				
609	ANUPPUR-KATNI	4/2015	12/2021 (12/2023)	1,370.00 (-)	795.59 (0.94)

			[12/2023]	[1,370.94]	[24]
610	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [9/2022]	1,485.85 (-) [1,835.83]	2,082.46 (349.98) [21]
611	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [3/2022]	585.93 (-) [1,268.32]	1,162.05 (682.39) [37]
612	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (-) [3/2023]	700.00 (-) [603.69]	358.78 (-96.31) [33]
613	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2024]	1,763.93 (2,445.30) [2,445.30]	1,392.72 (681.37) [55]
614	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [12/2023]	582.13 (-) [1,247.64]	561.88 (665.51) [21]
615	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [6/2023]	2,478.23 (-) [2,875.12]	1,035.16 (396.89) [15]
616	NIMACH BADI SADRI NEW LINE PROJECT	4/2017	3/2022 (-) [3/2026]	495.18 (-) [495.18]	0.63 (0.00) [48]
617	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2024]	424.60 (-) [2,909.99]	1,439.82 (2,485.39) [36]
618	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (-) [3/2026]	3,503.69 (5,839.02) [6,383.82]	2,404.99 (2,880.13) [48]
Road Transport And Highways					
619	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (-) [2/2022]	249.05 (-) [249.05]	219.86 (0.00) [43]
620	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (-) [0/0]	716.00 (-) [716.00]	59.57 (0.00) [0]
621	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	324.22 (0.00) [0]
622	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [3/2022]	950.27 (-) [950.27]	352.62 (0.00) [-]
623	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (-) [3/2022]	392.33 (-) [428.55]	404.69 (36.22) [48]
624	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	193.99 (0.00) [0]
625	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	215.49 (-169.75) [0]
626	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [12/2021]	990.61 (-) [990.61]	727.78 (0.00) [0]
627	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (-) [3/2022]	390.51 (-) [390.51]	306.63 (0.00) [-]
628	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	470.00 (183.02) [-]
629	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI	10/2019	/ (-)	743.88 (-)	557.00 (0.01)

	VILLAGE TO MANDSA		[6/2022]	[743.89]	[-]
630	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [5/2022]	1,094.97 (-) [1,094.97]	897.00 (0.00) [-]
631	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	671.00 (666.04) [-]
632	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (-) [3/2022]	205.05 (-) [205.05]	136.22 (0.00) [60]
633	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (-) [3/2022]	264.50 (-) [264.50]	157.77 (0.00) [12]
634	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-) [0/0]	928.83 (-) [928.83]	867.83 (0.00) [0]
635	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/ (-) [0/0]	794.30 (-) [691.38]	669.35 (-102.92) [0]
636	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/ (-) [0/0]	795.76 (-) [686.13]	669.94 (-109.63) [0]
637	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/ (-) [0/0]	810.22 (-) [810.22]	742.47 (0.00) [0]
638	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017 (-) [0/0]	639.97 (-) [639.97]	485.68 (0.00) [0]
639	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/ (-) [0/0]	770.73 (-) [770.73]	452.13 (0.00) [0]
640	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020 (-) [1/2022]	957.54 (-) [927.73]	780.19 (-29.81) [0]
641	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [475.00]	469.54 (150.00) [0]
642	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,509.96 (0.00) [0]
643	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020 (-) [3/2022]	628.45 (-) [628.45]	464.44 (0.00) [26]
644	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	410.72 (-) [410.72]	392.42 (0.00) [0]
645	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019 (-) [6/2022]	990.97 (-) [990.97]	845.00 (0.00) [30]
646	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020 (-) [8/2022]	1,047.00 (-) [1,047.00]	673.00 (0.00) [27]
647	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020 (-) [8/2022]	847.00 (-) [847.00]	635.00 (0.00) [29]
648	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020 (-) [8/2022]	996.27 (-) [996.27]	737.00 (0.00) [29]
649	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [4/2022]	169.63 (-) [169.63]	67.54 (0.00) [49]

650	REHABILITATION AND UPGADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [3/2022]	877.79 (-) [949.54]	807.22 (71.75) [33]
651	REHABILITATION AND UPGADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [3/2022]	809.16 (-) [809.16]	635.00 (0.00) [44]
652	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [12/2022]	511.83 (-) [511.83]	414.81 (0.00) [64]
653	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [3/2022]	254.17 (-) [254.17]	187.73 (0.00) [49]
654	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [3/2022]	233.04 (-) [233.04]	178.31 (0.00) [48]
655	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [3/2022]	279.44 (-) [279.44]	231.61 (0.00) [48]
656	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [3/2022]	166.21 (-) [174.90]	154.26 (8.69) [43]
657	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [3/2022]	184.62 (-) [184.62]	132.76 (0.00) [49]
658	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [6/2022]	214.69 (-) [214.69]	82.99 (0.00) [51]
659	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [3/2022]	217.22 (-) [226.88]	182.97 (9.66) [43]
660	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [3/2022]	162.56 (-) [162.56]	137.52 (0.00) [48]
661	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [12/2021]	373.82 (-) [373.82]	238.66 (0.00) [0]
	<u>Social Justice</u>				
662	CENTRE FOR DISABILITY SPORTS	2/2019	3/2024 (-) [3/2024]	170.99 (-) [170.99]	0.00 (0.00) [0]
	<u>Urban Development</u>				
663	BHOPAL METRO RAIL	11/2018	2/2023 (5/2025) [5/2025]	6,941.40 (-) [6,941.40]	409.75 (0.00) [27]
664	INDORE METRO RAIL	11/2018	2/2023 (7/2025) [7/2025]	7,500.80 (-) [7,500.80]	264.77 (0.00) [29]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
665	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (8/2023) [8/2023]	475.39 (-) [475.39]	202.52 (0.00) [28]
	<u>Coal</u>				
666	DINESH (MAKARDHOKDA-III) OC (8.0 MTY)	2/2020	3/2027 (-) [3/2027]	1,184.33 (-) [1,184.33]	0.00 (0.00) [0]
667	ADASA UG TO OC (1.50 MTY)	11/2018	3/2024 (-) [3/2024]	333.43 (-) [333.43]	0.00 (0.00) [0]
668	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY)	9/2018	3/2024 (-)	313.34 (-)	0.00 (0.00)

			[3/2024]	[313.34]	[0]
669	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (745.83) [745.03]	456.01 (17.75) [0]
670	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	252.71 (-) [252.71]	107.27 (0.00) [18]
671	BHANEGAON OC (1MTY)	2/2017	3/2023 (-) [3/2023]	409.68 (-) [409.68]	0.00 (0.00) [0]
672	BHATADI EXPASION OC (0.975 MTY)	2/2016	3/2019 (-) [9/2026]	327.41 (-) [327.41]	0.00 (0.00) [90]
673	DHUPTALA OC(SASTI UG TO OC)	2/2019	3/2028 (-) [3/2028]	720.87 (-) [720.87]	108.38 (0.00) [0]
674	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]
675	MUNGOLI NIRGUDA EXTENSION (DEEP) OC	11/2020	3/2026 (-) [3/2026]	826.80 (-) [826.80]	0.00 (0.00) [0]
676	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2022]	295.56 (299.67) [299.67]	213.93 (4.11) [36]
677	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]
678	UKNI DEEP OC	11/2018	3/2021 (-) [9/2022]	318.14 (-) [318.14]	226.62 (0.00) [18]
	<u>Department Of Higher Education</u>				
679	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [12/2021]	223.37 (-) [223.37]	117.64 (0.00) [0]
	<u>Fertilisers</u>				
680	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (3/2022) [3/2022]	426.72 (-) [426.72]	363.71 (0.00) [23]
	<u>Health And Family Welfare</u>				
681	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [12/2021]	582.99 (-) [582.99]	554.43 (0.00) [0]
682	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]
	<u>Petroleum</u>				
683	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [3/2022]	249.26 (-) [249.26]	212.46 (0.00) [21]
684	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [8/2022]	348.00 (437.00) [437.00]	226.74 (89.00) [19]
685	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (5/2022) [5/2022]	861.79 (2,001.34) [2,001.34]	1,613.65 (1,139.55) [108]
686	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (12/2022) [12/2022]	2,292.46 (-) [2,292.46]	2,255.02 (0.00) [19]
687	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-)	640.00 (-)	380.90 (0.00)

			[6/2022]	[640.00]	[6]
688	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2023]	2,494.68 (-) [2,354.72]	1,824.00 (-139.96) [12]
689	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	338.87 (0.00) [0]
690	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [7/2022]	1,945.00 (-) [1,945.00]	1,657.30 (0.00) [5]
691	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2022) [5/2022]	3,190.69 (3,375.90) [3,375.90]	2,892.72 (185.21) [49]
692	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,790.56 (747.87) [14]
693	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (5/2022) [5/2022]	3,660.71 (3,740.05) [3,740.05]	3,233.86 (79.34) [12]
694	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (5/2022) [5/2022]	763.92 (-) [829.58]	829.58 (65.66) [17]
695	PIPELINE REPLACEMENT PROJECT - VII	1/2022	5/2024 (-) [5/2024]	3,183.58 (-) [3,183.58]	0.00 (0.00) [0]
696	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND	5/2019	4/2025 (-) [4/2025]	8,797.00 (-) [8,797.00]	210.01 (0.00) [0]
Railways					
697	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,794.60]	2,921.95 (2,523.10) [24]
698	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [6/2022]	495.44 (-) [2,980.41]	1,868.04 (2,484.97) [219]
699	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	667.42 (205.27) [0]
700	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2022]	713.48 (-) [2,725.00]	2,189.77 (2,011.52) [24]
701	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
702	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
703	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	488.43 (0.00) [12]
704	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [1,387.52]	358.30 (594.63) [24]
705	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	322.26 (0.00) [24]
706	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [311.36]	0.00 (45.48) [0]
707	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-)	5,300.00 (-)	284.75 (-4,381.47)

			[0/0]	[918.53]	[0]
708	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,764.97 (0.00) [-12]
709	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
710	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (-) [3,176.60]	1,576.19 (1,268.09) [9]
711	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.49]	0.00 (688.49) [0]
712	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [393.62]	152.98 (176.24) [0]
713	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2024]	229.00 (-) [1,096.00]	40.47 (867.00) [36]
714	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	239.26 (0.00) [12]
715	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	524.21 (11.30) [12]
716	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,445.48]	1,418.98 (277.19) [0]
717	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	355.54 (0.00) [24]
Road Transport And Highways					
718	4 LANNING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
719	4-LANNING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	595.00 (0.00) [0]
720	4-LANNING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	868.72 (0.00) [0]
721	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (7/2022) [7/2024]	744.64 (-) [982.00]	0.00 (237.36) [52]
722	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (12/2021) [5/2022]	1,071.61 (-) [1,048.10]	1,203.21 (-23.51) [-]
723	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [0/0]	446.17 (-) [446.17]	171.45 (0.00) [0]
724	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (1/2022) [0/0]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]
725	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [7/2021]	1,142.62 (1,907.03) [1,142.62]	978.04 (0.00) [0]
726	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [3/2023]	1,101.58 (-) [1,101.58]	334.55 (0.00) [-]
727	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF	11/2016	3/2019 (-)	400.25 (-)	206.24 (0.00)

	CHHATTI		[0/0]	[400.25]	[0]
728	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (1/2022) [4/2022]	1,064.88 (-) [1,021.00]	529.08 (-43.88) [-]
729	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	18.75 (11.27) [0]
730	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (1/2022) [1/2022]	1,030.44 (-) [1,065.51]	0.00 (35.07) [0]
731	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (1/2022) [1/2022]	988.34 (-) [1,043.28]	0.00 (54.94) [0]
732	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-) [6/2021]	505.00 (-) [504.00]	489.00 (-1.00) [0]
733	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [6/2022]	422.38 (-) [422.38]	243.81 (0.00) [34]
734	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [8/2021]	955.40 (-) [955.40]	470.17 (0.00) [0]
735	AKOLA TO AKOT	1/2017	6/2019 (-) [9/2022]	313.95 (-) [313.95]	109.24 (0.00) [39]
736	AKOT TO ANJANGAON	1/2017	6/2019 (-) [11/2020]	245.77 (246.00) [245.77]	220.54 (0.00) [0]
737	AMD I TO SAONER	1/2017	6/2019 (-) [2/2020]	396.91 (397.00) [396.91]	289.79 (0.00) [0]
738	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [6/2022]	426.06 (426.00) [426.06]	219.56 (0.00) [24]
739	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [6/2022]	309.94 (310.00) [309.94]	192.24 (0.00) [30]
740	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [6/2022]	456.32 (-) [456.32]	330.00 (0.00) [36]
741	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [3/2021]	241.69 (242.00) [241.69]	167.95 (0.00) [0]
742	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [3/2022]	289.11 (290.00) [289.11]	144.69 (0.00) [42]
743	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [12/2020]	259.55 (260.00) [259.55]	204.49 (0.00) [0]
744	BHANDARA TO GHOTITOK	1/2017	6/2019 (-) [12/2019]	392.83 (393.00) [392.83]	274.75 (0.00) [0]
745	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [9/2022]	743.21 (743.00) [743.21]	350.07 (0.00) [15]
746	BHOKAR TO SARSAM	2/2017	7/2019 (-) [11/2020]	295.09 (-) [295.99]	169.64 (0.90) [0]
747	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [11/2020]	178.26 (-) [178.26]	159.96 (0.00) [0]

748	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [3/2021]	206.97 (207.00) [206.97]	145.87 (0.00) [0]
749	CHIKALI TO DHAD	3/2018	12/2019 (-) [6/2022]	189.46 (189.00) [189.46]	107.85 (0.00) [30]
750	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [1/2020]	548.03 (548.00) [548.03]	401.46 (0.00) [0]
751	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [12/2020]	393.10 (393.00) [393.10]	251.00 (0.00) [0]
752	CHIMUR TO WARORA	11/2016	3/2019 (-) [6/2022]	467.70 (-) [467.70]	201.73 (0.00) [39]
753	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (1,182.87) [1,182.87]	69.25 (19.95) [0]
754	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (6/2022) [6/2022]	649.50 (-) [649.50]	244.16 (0.00) [39]
755	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (2/2022) [2/2022]	291.53 (-) [291.53]	252.05 (0.00) [-]
756	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH- 53 (OLD NH-6)	3/2018	/ (2/2022) [2/2022]	289.21 (-) [289.21]	237.47 (0.00) [-]
757	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [6/2022]	593.26 (-) [717.24]	638.69 (123.98) [49]
758	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [3/2022]	531.13 (-) [744.73]	726.49 (213.60) [46]
759	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [6/2019]	168.30 (-) [168.30]	106.56 (0.00) [0]
760	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	31.97 (-89.53) [0]
761	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (414.00) [414.00]	410.01 (-0.51) [0]
762	DAHEGAON TO KUIH	1/2017	6/2019 (-) [9/2020]	228.89 (229.00) [228.89]	154.69 (0.00) [0]
763	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [9/2020]	182.63 (-) [182.63]	137.99 (0.00) [0]
764	DEORI TO AMGAON	1/2017	5/2019 (-) [6/2022]	409.62 (410.00) [409.62]	283.86 (0.00) [37]
765	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [12/2019]	219.91 (-) [219.91]	146.73 (0.00) [0]
766	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [3/2022]	296.19 (-) [254.00]	254.85 (-42.19) [24]
767	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [3/2022]	336.21 (336.00) [336.21]	224.98 (0.00) [27]
768	DHANGIPIMPRI TO JALNA AND AMBAD CHOWK TO	3/2018	2/2020	217.14	137.57

	MANTH CHOWK		(-) [6/2021]	(217.00) [217.14]	(0.00) [0]
769	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [3/2022]	391.06 (391.00) [391.06]	243.68 (0.00) [33]
770	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [6/2022]	456.45 (-) [456.45]	336.68 (0.00) [36]
771	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	748.98 (164.87) [0]
772	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (3/2022) [3/2022]	904.16 (-) [904.16]	0.00 (0.00) [25]
773	GADCHIROLI TO MUL	12/2016	6/2019 (-) [3/2022]	484.15 (-) [484.15]	343.45 (0.00) [33]
774	HELWAK TO KARAD	2/2017	7/2019 (-) [7/2021]	416.99 (-) [416.99]	223.81 (0.00) [0]
775	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [6/2022]	294.87 (295.00) [294.87]	149.16 (0.00) [30]
776	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [2/2022]	355.17 (-) [355.17]	269.58 (0.00) [31]
777	INDAPUR TO VADPALE	1/2017	12/2019 (-) [6/2022]	1,202.52 (1,203.00) [1,202.52]	791.90 (0.00) [30]
778	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [3/2022]	461.96 (-) [461.96]	326.81 (0.00) [28]
779	JALGAON TO BHADGAON	1/2018	11/2019 (-) [1/2021]	307.54 (308.00) [307.54]	204.36 (0.00) [0]
780	JALGAON TO NANDURA	3/2018	12/2019 (-) [11/2020]	177.84 (177.00) [177.84]	110.20 (0.00) [0]
781	JALKOT TO TOGRI	7/2018	8/2020 (-) [3/2022]	299.92 (300.00) [299.92]	181.37 (0.00) [19]
782	JINTUR TO PARBHANI	1/2017	/ (-) [9/2022]	356.66 (-) [356.66]	132.98 (0.00) [-]
783	KAIJ TO KUSALAM	1/2017	7/2019 (-) [6/2022]	554.78 (-) [554.78]	304.78 (0.00) [35]
784	KALMAB TO RALEGAON	1/2017	6/2019 (-) [8/2020]	467.78 (-) [467.78]	467.78 (0.00) [0]
785	KALMATH TO ZARAP	9/2016	3/2020 (-) [3/2020]	1,338.13 (2,617.44) [1,338.13]	1,346.39 (0.00) [0]
786	KANTE TO WAKED	3/2016	11/2019 (-) [12/2022]	1,230.02 (1,230.00) [1,230.02]	631.68 (0.00) [37]
787	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [9/2022]	407.19 (407.00) [407.19]	196.83 (0.00) [39]
788	KARAD TO TAGAON	1/2017	6/2019 (-)	537.81 (538.00)	218.73 (0.00)

			[12/2022]	[537.81]	[42]
789	KARAD TO VITA	1/2018	12/2019 (-) [3/2022]	344.85 (245.00) [344.85]	245.82 (0.00) [27]
790	KARWANDI TO RAJURI	3/2018	12/2019 (-) [6/2022]	276.95 (277.00) [276.95]	136.94 (0.00) [30]
791	KATOL TO WARUD	1/2017	6/2019 (-) [1/2020]	463.62 (664.00) [463.62]	265.78 (0.00) [0]
792	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [3/2020]	249.29 (-) [249.29]	155.48 (0.00) [0]
793	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [9/2019]	203.21 (203.00) [203.21]	160.15 (0.00) [0]
794	KHERDA TO NAGZARI	3/2018	12/2019 (-) [9/2020]	181.30 (-) [181.30]	137.37 (0.00) [0]
795	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	594.75 (-) [606.75]	245.90 (12.00) [0]
796	KOLDE TO KHETIYA	1/2017	7/2019 (-) [3/2022]	509.18 (-) [509.18]	257.83 (0.00) [32]
797	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [6/2022]	281.78 (282.00) [281.78]	74.00 (0.00) [38]
798	KOTHARI TO DHANORA	9/2018	8/2020 (-) [9/2022]	301.38 (301.00) [301.38]	176.39 (0.00) [25]
799	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [6/2019]	406.51 (-) [406.51]	290.64 (0.00) [0]
800	KUNDRAI TO WAZAR	1/2018	12/2019 (-) [12/2020]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
801	KURUDWADI TO PANDHARPUR	1/2017	7/2019 (-) [3/2022]	307.63 (-) [307.63]	190.69 (0.00) [32]
802	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [7/2021]	243.45 (244.00) [243.45]	169.24 (0.00) [0]
803	LATUR TO PANGAON	3/2018	12/2019 (-) [12/2020]	336.47 (336.00) [336.47]	203.39 (0.00) [0]
804	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [12/2022]	237.40 (-) [237.40]	9.66 (0.00) [31]
805	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [4/2022]	256.15 (-) [256.15]	174.63 (0.00) [28]
806	MALEGAON TO RISOD	2/2018	12/2019 (-) [10/2020]	303.24 (303.00) [303.24]	196.00 (0.00) [0]
807	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [6/2022]	322.55 (-) [322.55]	191.12 (0.00) [36]
808	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [3/2022]	457.52 (-) [457.52]	354.16 (0.00) [32]

809	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [2/2022]	222.13 (222.00) [222.13]	156.87 (0.00) [27]
810	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [3/2022]	228.54 (-) [228.54]	159.32 (0.00) [31]
811	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [6/2021]	418.36 (-) [418.36]	263.13 (0.00) [0]
812	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [3/2022]	486.19 (-) [486.19]	308.66 (0.00) [32]
813	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [3/2022]	232.77 (-) [232.77]	151.60 (0.00) [32]
814	MEHKAR TO CHIICALI	2/2017	5/2019 (-) [3/2020]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
815	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [9/2022]	488.60 (-) [488.60]	233.89 (0.00) [38]
816	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	731.89 (-) [732.34]	401.61 (0.45) [0]
817	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [12/2020]	341.16 (341.00) [341.16]	234.67 (0.00) [0]
818	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [12/2019]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
819	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [6/2022]	162.34 (-) [162.34]	64.74 (0.00) [35]
820	NAGAJ TO VAIJAPUR	1/2017	6/2019 (-) [12/2020]	376.72 (377.00) [376.72]	261.86 (0.00) [0]
821	NAGBHID TO ARMORI	9/2016	7/2019 (-) [11/2019]	269.05 (-) [269.05]	222.40 (0.00) [0]
822	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [3/2023]	546.00 (-) [546.00]	309.98 (0.00) [44]
823	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (8/2023) [8/2023]	591.66 (-) [591.66]	319.05 (0.00) [49]
824	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [12/2021]	244.04 (244.00) [244.04]	170.33 (0.00) [0]
825	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [12/2020]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
826	NANDED TO JALKOT	12/2017	9/2019 (-) [6/2022]	456.93 (457.00) [456.93]	456.93 (0.00) [33]
827	NANDGAON TO MORSHI	1/2017	6/2019 (-) [11/2019]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
828	NASHIK TO PETH	12/2015	11/2018 (-) [4/2021]	289.60 (-) [289.60]	210.10 (0.00) [0]
829	NASRATPUR TO BARASGAON	7/2016	9/2019	406.54	175.24

			(-) [6/2022]	(407.00) [406.54]	(0.00) [33]
830	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [9/2022]	420.63 (421.00) [420.63]	200.00 (0.00) [28]
831	OMREGA TO AUSA	3/2018	12/2019 (-) [9/2021]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
832	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [6/2022]	344.25 (344.00) [344.25]	169.80 (0.00) [22]
833	PAHUR TO BODHWAD	1/2017	5/2020 (-) [2/2022]	244.93 (-) [244.93]	159.96 (0.00) [21]
834	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [12/2022]	341.80 (-) [341.80]	155.96 (0.00) [42]
835	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [3/2022]	227.19 (227.00) [227.19]	138.05 (0.00) [27]
836	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [12/2022]	381.08 (302.00) [381.08]	9.66 (0.00) [31]
837	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [3/2022]	218.38 (-) [218.38]	170.80 (0.00) [32]
838	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [3/2022]	238.19 (238.00) [238.19]	177.80 (0.00) [27]
839	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [6/2022]	205.72 (206.00) [205.72]	85.47 (0.00) [36]
840	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [9/2022]	983.14 (2,226.11) [983.14]	726.13 (0.00) [33]
841	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [6/2022]	420.57 (-) [420.57]	269.24 (0.00) [35]
842	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [3/2022]	170.00 (-) [170.00]	121.71 (0.00) [27]
843	PEN TO KHOPOLI	3/2018	3/2018 (-) [6/2022]	301.39 (302.00) [301.39]	105.37 (0.00) [51]
844	PIMPLA TO MANJARSUMBHA	1/2017	8/2019 (-) [6/2022]	595.77 (-) [595.77]	321.34 (0.00) [34]
845	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [3/2022]	223.46 (-) [223.46]	68.00 (0.00) [27]
846	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [4/2022]	228.31 (-) [228.31]	93.73 (0.00) [28]
847	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [4/2022]	1,724.55 (-) [1,724.55]	2,701.66 (0.00) [109]
848	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [3/2022]	210.81 (-) [210.81]	210.81 (0.00) [32]
849	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-)	446.77 (-)	303.72 (0.00)

			[0/0]	[446.77]	[0]
850	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [9/2022]	225.81 (-) [225.81]	112.51 (0.00) [-]
851	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (-) [3/2022]	536.65 (356.00) [536.65]	557.20 (0.00) [27]
852	RISOD TO HINGOLI	2/2018	12/2019 (-) [3/2022]	355.99 (-) [355.99]	246.86 (0.00) [27]
853	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [6/2022]	362.96 (-) [362.96]	190.75 (0.00) [36]
854	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [3/2022]	415.25 (415.25) [415.25]	271.38 (0.00) [27]
855	SANGOLA TO JATH	1/2018	12/2019 (-) [3/2022]	257.38 (257.00) [257.38]	166.31 (0.00) [27]
856	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [3/2021]	250.46 (-) [250.46]	174.16 (0.00) [0]
857	SARSAM TO KOTHARI	2/2016	7/2019 (-) [9/2022]	545.64 (-) [545.64]	195.79 (0.00) [38]
858	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [6/2022]	388.44 (-) [388.44]	199.61 (0.00) [-]
859	SATARA TO MHASWAD	1/2017	7/2019 (-) [9/2022]	653.46 (-) [653.46]	284.02 (0.00) [38]
860	SELDOH TO PANVAR	7/2018	5/2020 (-) [12/2022]	404.33 (404.00) [404.33]	61.42 (0.00) [31]
861	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [6/2022]	150.79 (-) [150.79]	59.88 (0.00) [30]
862	SHEGAON TO DEORI PHATA	2/2017	5/2019 (-) [11/2020]	373.10 (373.00) [373.10]	314.20 (0.00) [0]
863	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [2/2022]	211.34 (-) [211.34]	130.63 (0.00) [31]
864	SHIRUR TO KHARDA	2/2017	6/2019 (-) [9/2022]	381.77 (-) [381.77]	186.62 (0.00) [39]
865	SHIVUR TO YEOLA	3/2018	12/2019 (-) [3/2022]	181.08 (-) [181.08]	97.86 (0.00) [27]
866	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [6/2022]	337.46 (-) [337.46]	232.56 (0.00) [36]
867	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [9/2021]	404.94 (-) [448.18]	495.92 (43.24) [0]
868	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2017]	290.73 (-) [359.60]	340.48 (68.87) [0]
869	TAKARKHED TO JALNA	9/2017	6/2019 (-) [11/2020]	417.90 (418.00) [417.90]	260.48 (0.00) [0]

870	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [3/2022]	264.41 (264.00) [264.41]	189.64 (0.00) [36]
871	TALGAON TO KALMATH	10/2016	3/2020 (-) [10/2020]	904.70 (1,428.09) [904.70]	969.90 (0.00) [0]
872	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [7/2019]	195.64 (196.00) [195.64]	116.92 (0.00) [0]
873	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [3/2022]	422.02 (422.00) [422.02]	302.13 (0.00) [32]
874	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [6/2022]	1,598.47 (1,560.00) [1,598.47]	1,054.53 (0.00) [31]
875	VITA TO NAGAJ	3/2018	12/2019 (-) [6/2022]	304.58 (305.00) [304.58]	135.51 (0.00) [30]
876	WADI TO ASOLA	1/2017	9/2019 (-) [12/2022]	363.82 (364.00) [363.82]	73.08 (0.00) [39]
877	WADIGODRI TO DHANGRIPIPRI	3/2018	2/2020 (-) [1/2021]	194.23 (194.00) [194.23]	116.21 (0.00) [0]
878	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [9/2022]	376.19 (-) [376.19]	91.77 (0.00) [40]
879	WAKED TO TALEGAON	2/2016	2/2019 (-) [11/2021]	1,244.75 (1,245.00) [1,244.75]	840.10 (0.00) [0]
880	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [0/0]	362.46 (-) [362.46]	243.39 (0.00) [0]
881	WARDHA TO ARVI	2/2018	4/2020 (-) [3/2022]	313.58 (-) [313.58]	202.69 (0.00) [23]
882	WARDHA TO HINGAGHAT	1/2018	12/2019 (-) [7/2021]	216.90 (217.00) [216.90]	160.37 (0.00) [0]
883	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [9/2020]	165.51 (-) [165.51]	133.93 (0.00) [0]
884	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
885	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (-) [3/2023]	23,136.00 (-) [33,406.00]	20,484.28 (10,270.00) [36]
886	NAGPUR METRO RAIL	8/2014	3/2018 (-) [2/2022]	8,680.00 (-) [9,759.79]	8,462.32 (1,079.79) [47]
887	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [12/2022]	11,420.00 (-) [11,420.00]	7,764.11 (0.00) [13]
	<u>Water Resources</u>				
888	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [0/0]	233.57 (-) [233.57]	193.05 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Power</u>				

889	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (-) [1,311.05]	200.27 (732.43) [0]
	Railways				
890	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [14,322.00]	12,156.19 (9,867.83) [153]
	Road Transport And Highways				
891	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	50.50 (0.00) [0]
892	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	59.71 (0.00) [0]
893	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	91.93 (0.00) [0]
894	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	42.83 (0.00) [0]
895	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	36.05 (0.00) [0]
896	CHURACHANPUR TUIVAI PKG-3	7/2021	10/2023 (-) [10/2023]	673.27 (-) [673.27]	11.12 (0.00) [0]
897	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
898	IMPHAL - KHONGSANG PKG-3	7/2021	3/2023 (-) [3/2023]	467.00 (-) [467.00]	0.00 (0.00) [0]
899	IMPHAL – MOREH (PACKAGE 4)	3/2021	1/2023 (-) [1/2023]	277.99 (-) [277.99]	5.57 (0.00) [0]
900	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	46.59 (0.00) [0]
901	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
902	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
903	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	12.26 (0.00) [0]
904	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	167.94 (0.00) [0]
905	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	16.08 (0.00) [0]
906	MARIAM - PEREN (PKG 2A)	7/2021	3/2023 (-) [3/2023]	204.58 (-) [204.58]	10.48 (0.00) [0]
907	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	6.70 (0.00) [0]
908	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	6.41 (0.00) [0]

			[12/2022]	[232.26]	[0]
909	SENAPATI- IMPHAL PKG-5B	3/2021	1/2023 (-) [1/2023]	211.70 (-) [211.70]	0.00 (0.00) [0]
910	TAMENGLONG - MAHUR PKG-1	7/2021	3/2023 (-) [3/2023]	185.80 (-) [185.80]	6.20 (0.00) [0]
911	TAMENGLONG - MAHUR PKG-2	7/2021	3/2023 (-) [3/2023]	483.87 (-) [483.87]	22.78 (0.00) [0]
912	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	15.09 (0.00) [0]
913	TAMENGLONG - MAHUR PKG-4	7/2021	3/2023 (-) [3/2023]	198.77 (-) [198.77]	6.59 (0.00) [0]
914	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [0]
	MEGHALAYA				
	Department Of Higher Education				
915	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (6/2022) [6/2022]	484.32 (429.70) [429.70]	233.00 (-54.62) [93]
	Doner				
916	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	149.33 (0.00) [0]
	Health And Family Welfare				
917	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [6/2022]	363.99 (-) [363.99]	274.40 (0.00) [49]
	Railways				
918	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (-) [4,083.02]	265.38 (3,176.56) [0]
	Road Transport And Highways				
919	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	171.47 (0.00) [0]
920	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [9/2022]	306.28 (-) [306.28]	135.84 (0.00) [40]
921	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	44.52 (0.00) [0]
922	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	301.78 (0.00) [0]
923	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	174.37 (0.00) [0]
924	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	66.51 (0.00) [0]
925	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	68.77 (0.00) [0]
926	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [9/2021]	553.51 (-) [553.51]	211.57 (0.00) [0]

	MIZORAM				
	Railways				
927	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [12/2023]	2,393.47 (-) [6,527.00]	4,766.68 (4,133.53) [117]
	Road Transport And Highways				
928	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF FLEXIBLE PAVEMENT FROM KM 42.80 TO KM 60.30 ON NH NO.1	1/2017	1/2021 (-) [4/2022]	205.95 (-) [205.95]	123.24 (0.00) [15]
929	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2022) [0/0]	195.04 (434.65) [377.99]	384.74 (182.95) [0]
930	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (3/2022) [0/0]	186.96 (-) [322.24]	308.85 (135.28) [0]
931	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2022) [0/0]	193.69 (374.59) [327.92]	329.03 (134.23) [0]
932	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	32.96 (0.00) [0]
933	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	39.88 (0.00) [0]
934	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	70.76 (0.00) [0]
935	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	72.45 (0.00) [0]
936	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	120.63 (0.00) [0]
937	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	43.39 (0.00) [0]
938	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	16.96 (0.00) [0]
939	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	60.00 (0.00) [0]
940	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
941	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
942	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	140.92 (0.00) [43]
943	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [7/2023]	640.07 (-) [640.07]	124.67 (0.00) [46]
944	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [6/2023]	518.53 (-) [518.53]	164.47 (0.00) [45]
945	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	473.18 (-) [473.18]	137.39 (0.00) [43]
946	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED	4/2017	9/2019	642.96	133.41

	SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO		(-) [6/2023]	(-) [642.96]	(0.00) [45]
947	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	537.82 (-) [537.82]	163.81 (0.00) [43]
948	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2023]	428.11 (-) [428.11]	120.31 (0.00) [48]
949	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2024]	404.29 (-) [404.29]	75.58 (0.00) [55]
950	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2022) [0/0]	624.41 (1,109.88) [992.67]	978.43 (368.26) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
951	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
952	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [9/2023]	328.00 (-) [328.00]	298.48 (0.00) [30]
953	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (404.45) [404.45]	252.90 (84.69) [0]
	<u>Dpiit</u>				
954	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (-) [7/2021]	12,579.09 (-) [13,812.30]	9,574.07 (1,233.21) [0]
	<u>Heavy Industry</u>				
955	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,727.30]	3,526.63 (2,009.30) [0]
	<u>Petroleum</u>				
956	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (12/2021) [5/2022]	1,823.00 (3,027.90) [3,027.90]	2,315.92 (1,204.90) [14]
957	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [3/2022]	571.66 (-) [510.00]	494.68 (-61.66) [27]
958	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [6/2023]	3,308.00 (-) [3,060.00]	2,727.90 (-248.00) [18]
959	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	466.13 (0.00) [0]
960	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2022]	3,437.00 (-) [3,048.00]	2,271.40 (-389.00) [18]
961	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (-) [12/2029]	169.00 (-) [169.00]	43.28 (0.00) [0]
962	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	140.07 (0.00) [0]
963	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	365.30 (0.00) [0]
964	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2022]	2,433.00 (-) [2,433.00]	2,209.40 (0.00) [18]

965	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (-) [7/2022]	2,677.00 (-) [3,072.00]	2,730.95 (395.00) [13]
966	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2025]	2,915.00 (5,909.00) [5,909.00]	3,781.00 (2,994.00) [146]
967	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [3/2022]	2,881.40 (-) [2,000.00]	1,661.00 (-881.40) [15]
968	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	2,002.80 (0.00) [0]
969	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (3/2022) [3/2022]	2,321.00 (3,338.00) [3,338.00]	3,154.79 (1,017.00) [15]
970	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [3/2022]	690.00 (-) [690.00]	609.43 (0.00) [44]
971	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2022]	406.00 (-) [340.00]	287.12 (-66.00) [17]
972	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	555.30 (0.00) [0]
	<u>Power</u>				
973	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [3/2024]	4,754.42 (-) [9,129.32]	3,182.67 (4,374.90) [63]
974	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [2/2022]	358.83 (-) [358.83]	262.29 (0.00) [21]
975	EASTERN REGION STRENGTHENING SCHEME - XXIII	7/2020	6/2021 (-) [3/2022]	239.89 (-) [239.89]	0.00 (0.00) [9]
976	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (-) [3/2022]	522.29 (-) [546.36]	480.89 (24.07) [64]
977	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [4/2022]	3,500.00 (3,500.00) [3,994.00]	3,099.43 (494.00) [21]
978	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [3/2022]	235.53 (-) [235.53]	159.02 (0.00) [33]
979	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [4/2022]	322.30 (-) [322.30]	205.65 (0.00) [38]
980	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [3/2022]	197.40 (-) [197.40]	90.97 (0.00) [48]
981	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [4/2023]	1,931.39 (-) [2,635.55]	1,832.15 (704.16) [38]
982	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [1/2024]	5,111.33 (-) [6,700.00]	3,522.04 (1,588.67) [61]
983	NORTH EASTERN REGION STRENGTHENING SCHEME - III	9/2015	12/2017 (-) [3/2022]	167.31 (-) [167.31]	0.00 (0.00) [51]
984	NORTH EASTERN REGION STRENGTHENING SCHEME-VIII	9/2018	3/2021 (-) [2/2022]	221.36 (-) [221.36]	0.00 (0.00) [11]

985	NORTH EASTERN REGION STRENGTHENING SCHEME-XII	5/2021	3/2023 (-) [3/2023]	576.42 (-) [576.42]	0.00 (0.00) [0]
986	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (-) [3/2018]	11,130.19 (-) [13,199.00]	12,394.95 (2,068.81) [0]
987	NORTHERN REGION SYSTEM STRENGTHENING - XL	2/2019	12/2020 (-) [12/2020]	572.98 (-) [572.98]	0.00 (0.00) [0]
988	RELIABLE COMMUNICATION SCHEME UNDER CENTRAL SECTOR FOR NORTHERN REGION	11/2018	11/2021 (-) [5/2022]	241.38 (-) [241.38]	0.00 (0.00) [6]
989	SOUTHERN REGION SYSTEM STRENGTHENING - XXV	7/2019	7/2021 (-) [2/2022]	154.72 (-) [154.72]	0.00 (0.00) [7]
990	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [4/2022]	379.95 (-) [379.95]	251.70 (0.00) [28]
991	SYSTEM STRENGTHENING SCHEMES AT TUTICORIN-II (ERSTWHILE TIRUNELVELLI GIS) AND BHUJ PS	11/2018	6/2020 (-) [3/2022]	496.11 (-) [496.11]	0.00 (0.00) [21]
992	WESTERN REGION SYSTEM STRENGTHENING - XX	7/2019	8/2021 (-) [2/2022]	226.98 (-) [226.98]	0.00 (0.00) [6]
	<u>Railways</u>				
993	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	21,986.54 (0.00) [0]
994	BANDEL-BOINCHI 3RD LINE	4/2011	/ (9/2021) (-) [2/2022]	288.35 (-) [502.48]	529.13 (214.13) [-]
995	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [3/2022]	704.31 (-) [927.94]	713.38 (223.63) [24]
996	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (9/2021) (-) [3/2022]	175.80 (-) [495.10]	333.93 (319.30) [-]
997	CHANDIGARH-BADDI	4/2007	3/2023 (12/2025) [12/2025]	328.14 (-) [1,540.13]	480.97 (1,211.99) [33]
998	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [728.92]	613.91 (433.92) [37]
999	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (-) [10/2027]	1,347.26 (-) [1,524.68]	1,010.81 (177.42) [67]
1000	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (-) [3/2025]	1,640.04 (-) [1,640.04]	883.21 (0.00) [36]
1001	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	508.16 (74.13) [96]
1002	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (9/2021) (-) [9/2023]	336.91 (-) [791.39]	689.83 (454.48) [-]
1003	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (9/2021) (-) [12/2027]	2,030.50 (-) [2,030.50]	0.00 (0.00) [-]
1004	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (6/2022) (-) [0/0]	11,589.00 (28,181.00) [51,219.00]	35,951.00 (39,630.00) [0]

1005	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [12/2024]	2,912.96 (-) [3,845.60]	534.75 (932.64) [33]
1006	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [12/2021]	678.54 (-) [929.86]	964.41 (251.32) [0]
1007	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [2/2024]	1,614.59 (-) [1,878.00]	1,530.18 (263.41) [59]
1008	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [0/0]	625.00 (-) [839.00]	839.36 (214.00) [0]
1009	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2027]	2,132.77 (-) [3,037.95]	347.14 (905.18) [156]
1010	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2024]	923.52 (-) [995.10]	622.26 (71.58) [96]
1011	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,676.08 (0.00) [36]
1012	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [1,952.68]	803.75 (95.73) [12]
1013	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [3/2022]	270.14 (-) [749.40]	591.35 (479.26) [-]
1014	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,908.60 (8,000.84) [202]
1015	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [12/2027]	120.70 (-) [2,111.88]	314.32 (1,991.18) [105]
1016	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	418.15 (59.77) [-]
1017	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	2,094.82 (1,698.35) [276]
1018	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [0/0]	414.84 (-) [750.00]	157.78 (335.16) [0]
1019	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [11/2024]	450.00 (-) [2,017.96]	883.53 (1,567.96) [148]
1020	NARAYANGARH TO BHADRAK 3RD LINE (155 KM)	3/2019	5/2023 (-) [12/2023]	1,866.31 (-) [1,866.31]	350.68 (0.00) [7]
1021	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [0/0]	242.22 (-) [471.00]	76.57 (228.78) [0]
1022	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [3/2023]	241.52 (-) [401.65]	338.00 (160.13) [-]
1023	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [12/2023]	1,798.00 (-) [2,047.51]	586.70 (249.51) [57]
1024	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	342.53 (101.81) [31]
1025	PIRPAINTI-JASIDIH	4/2013	3/2022	915.98	472.06

			(-) [3/2025]	(-) [2,137.81]	(1,221.83) [36]
1026	RAYADURGA-TUMKUR NL	4/2007	/	2,062.30	1,108.07
			(-) [12/2025]	(-) [2,404.03]	(341.73) [-]
1027	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016	277.28	204.40
			(-) [3/2025]	(-) [266.32]	(-10.96) [108]
1028	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(-) [3/2028]	(-) [466.65]	(170.65) [-]
1029	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020	16,592.00	47,476.00
			(6/2022) [0/0]	(72,785.00) [51,101.00]	(34,509.00) [0]
1030	YELAHANKA-PENUKONDA	5/2015	3/2020	860.43	1,014.52
			(-) [2/2022]	(-) [1,104.00]	(243.57) [23]
	<u>Road Transport And Highways</u>				
1031	4 LANING OF NAGPUR-BETUL	2/2011	8/2014	2,498.76	2,531.46
			(3/2022) [3/2022]	(-) [2,498.76]	(0.00) [91]
1032	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015	1,928.22	1,890.04
			(3/2022) [3/2022]	(-) [1,928.22]	(0.00) [83]
1033	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/	1,294.47	0.00
			(-) [11/2021]	(-) [1,296.00]	(1.53) [0]
1034	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/	998.70	0.00
			(-) [11/2018]	(-) [962.00]	(-36.70) [0]
1035	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013	754.00	1,364.18
			(6/2021) [0/0]	(2,047.64) [2,047.64]	(1,293.64) [0]
1036	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011	1,693.75	2,848.49
			(-) [0/0]	(-) [1,693.75]	(0.00) [0]
1037	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014	2,848.00	3,379.45
			(-) [12/2022]	(-) [3,379.45]	(531.45) [105]
	<u>Shipping And Ports</u>				
1038	JAL MARG VIKAS PROJECT	1/2018	3/2023	5,369.18	2,013.22
			(-) [3/2023]	(-) [4,633.81]	(-735.37) [0]
	<u>Telecommunications</u>				
1039	NETWORK FOR SPECTRUM	3/2012	7/2015	13,334.00	20,545.00
			(-) [3/2022]	(-) [24,664.00]	(11,330.00) [80]
1040	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021	431.16	70.25
			(11/2021) [6/2022]	(461.42) [461.42]	(30.26) [12]
	<u>Urban Development</u>				
1041	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025	30,274.00	6,762.86
			(-) [6/2025]	(-) [30,274.00]	(0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
1042	DIMAPUR-TIZIT NL	4/2013	3/2020	4,274.00	0.00
			(-) [0/0]	(-) [4,274.00]	(0.00) [0]
1043	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015	2,326.52	1,534.31
			(-)	(-)	(4,336.48)

			[3/2026]	[6,663.00]	[132]
	Road Transport And Highways				
1044	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	134.40 (0.00) [44]
1045	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	100.70 (0.00) [48]
1046	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	183.30 (0.00) [0]
1047	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	341.40 (0.00) [42]
1048	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	156.49 (0.00) [50]
1049	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	64.91 (0.00) [0]
1050	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	79.81 (0.00) [0]
1051	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	41.90 (0.00) [0]
1052	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	72.60 (0.00) [0]
1053	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	53.72 (0.00) [0]
1054	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	101.27 (0.00) [0]
1055	CHANGTONGYA TO LONGLENG ROAD PKG-2	3/2020	6/2022 (-) [6/2022]	206.53 (-) [206.53]	88.93 (0.00) [0]
1056	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (4/2022) [0/0]	217.35 (-) [217.35]	115.36 (0.00) [0]
1057	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	55.18 (0.00) [0]
1058	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	7.02 (0.00) [0]
1059	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	33.95 (0.00) [0]
1060	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	186.85 (0.00) [46]
1061	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	120.99 (0.00) [0]
1062	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [12/2021]	240.64 (-) [240.64]	125.87 (0.00) [0]
1063	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING	3/2018	9/2018 (-)	215.12 (-)	127.24 (0.00)

	KM 00.000 TO		[3/2022]	[215.12]	[42]
1064	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	82.09 (0.00) [0]
1065	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	87.49 (0.00) [49]
1066	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	157.06 (0.00) [0]
1067	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	134.89 (0.00) [0]
1068	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	356.14 (13.93) [0]
1069	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	312.71 (0.00) [0]
1070	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [11/2020]	336.25 (-) [369.96]	322.13 (33.71) [0]
1071	PEREN-DIMAPUR PKG-5	2/2021	3/2023 (-) [3/2023]	207.33 (-) [207.33]	0.00 (0.00) [0]
1072	PEREN-DIMAPUR SECTION PKG-2	7/2021	3/2023 (-) [3/2023]	258.52 (-) [258.52]	31.67 (0.00) [0]
1073	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	172.63 (-) [172.63]	132.43 (0.00) [0]
1074	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (12/2021) [0/0]	167.62 (-) [167.62]	142.40 (0.00) [0]
1075	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	9.39 (0.00) [0]
1076	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [7/2022]	237.51 (-) [237.51]	110.76 (0.00) [-5]
	<u>ODISHA</u>				
	<u>Coal</u>				
1077	ANANTA OCP EXPANSION PH III	8/2008	3/2012 (-) [3/2012]	228.08 (-) [228.08]	0.00 (0.00) [0]
1078	BALARAM EXPANSION OCP	8/2020	3/2029 (-) [3/2029]	3,504.21 (-) [3,504.21]	0.00 (0.00) [0]
1079	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	254.83 (0.00) [60]
1080	BHUBANESWARI EXPANSION OCP	8/2020	3/2031 (-) [3/2031]	3,145.45 (-) [3,145.45]	0.00 (0.00) [0]
1081	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2026]	1,375.38 (-) [1,375.38]	710.64 (0.00) [60]
1082	GOPALJI-KANIHA OCP	8/2020	3/2028 (-) [3/2028]	8,416.19 (-) [8,416.19]	0.00 (0.00) [0]
1083	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013	479.53	815.72

			(-) [3/2024]	(-) [808.97]	(329.44) [132]
1084	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	841.95 (0.00) [0]
1085	NAINI COAL MINE	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	137.86 (0.00) [0]
1086	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,341.19 (0.00) [0]
1087	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,718.35 (0.00) [0]
1088	TALABIRA II AND III OCP	7/2017	1/2027 (-) [4/2020]	2,401.07 (-) [2,401.07]	920.53 (0.00) [0]
	<u>Department Of Higher Education</u>				
1089	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [9/2022]	790.79 (-) [790.79]	294.36 (0.00) [6]
	<u>Mines</u>				
1090	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (1/2024) [1/2024]	5,540.00 (6,435.90) [6,435.90]	1,268.54 (895.90) [33]
1091	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (12/2023) [12/2023]	355.00 (581.00) [581.00]	96.18 (226.00) [37]
1092	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (12/2023) [12/2023]	483.00 (483.00) [483.00]	10.96 (0.00) [32]
1093	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (11/2023) [11/2023]	534.00 (667.23) [667.23]	395.98 (133.23) [46]
	<u>Petroleum</u>				
1094	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (543.00) [543.00]	176.32 (80.70) [9]
1095	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [2/2022]	315.00 (-) [315.00]	232.78 (0.00) [2]
1096	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [8/2023]	243.53 (-) [243.53]	167.21 (0.00) [13]
1097	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [8/2023]	182.20 (-) [182.20]	101.14 (0.00) [13]
1098	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [7/2022]	1,933.00 (-) [1,933.00]	1,620.10 (0.00) [19]
1099	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (7/2022) [7/2022]	5,654.00 (-) [5,654.00]	3,652.22 (0.00) [9]
1100	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021 (9/2022) [9/2022]	3,361.00 (-) [3,361.00]	2,141.68 (0.00) [13]
1101	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	88.43 (0.00) [0]
1102	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023)	371.00 (427.10)	41.54 (56.10)

			[3/2023]	[427.10]	[6]
1103	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	763.89 (0.00) [0]
1104	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [1/2023]	161.59 (-) [161.59]	71.65 (0.00) [37]
1105	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [6/2022]	1,297.50 (-) [1,297.50]	914.85 (0.00) [8]
1106	Setting up of Integrated 2G and 1G Bio-Ethanol Refinery at Bargarh, Odisha	8/2019	8/2022 (-) [6/2023]	1,607.00 (-) [1,607.00]	338.29 (0.00) [10]
	<u>Power</u>				
1107	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (3/2022) [3/2022]	1,885.13 (2,311.80) [2,426.00]	2,027.32 (540.87) [39]
	<u>Railways</u>				
1108	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2023]	942.95 (-) [1,552.26]	1,313.06 (609.31) [48]
1109	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2024]	843.04 (-) [843.04]	324.59 (0.00) [41]
1110	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2024]	1,172.92 (-) [1,172.92]	734.63 (0.00) [63]
1111	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2024]	1,547.38 (1,547.38) [1,547.38]	758.80 (0.00) [24]
1112	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2025]	701.61 (-) [810.02]	209.78 (108.41) [76]
1113	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2022]	133.41 (207.00) [433.00]	424.19 (299.59) [165]
1114	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [12/2024]	2,923.13 (-) [3,791.66]	1,729.29 (868.53) [189]
1115	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (3/2026) [3/2026]	2,361.74 (2,361.74) [2,361.74]	564.03 (0.00) [48]
1116	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [6/2022]	969.83 (-) [1,312.97]	1,155.00 (343.14) [27]
1117	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [4/2022]	948.04 (-) [2,009.00]	2,202.94 (1,060.96) [25]
1118	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2022]	1,111.99 (-) [1,539.28]	1,243.24 (427.29) [37]
1119	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,993.73 (1,237.83) [88]
1120	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2025]	810.78 (-) [1,928.07]	947.41 (1,117.29) [45]
1121	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	2,139.84 (992.05) [24]
	<u>Road Transport And Highways</u>				

1122	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [2/2022]	1,282.94 (-) [1,282.94]	720.08 (0.00) [-]
1123	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [6/2022]	2,510.04 (-) [2,510.04]	653.06 (0.00) [34]
1124	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [5/2022]	752.28 (-) [752.28]	289.28 (0.00) [-]
1125	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [4/2022]	1,069.65 (-) [1,069.65]	856.33 (0.00) [-]
1126	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	14.80 (0.00) [0]
1127	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [3/2022]	1,008.96 (-) [1,008.96]	1,148.65 (0.00) [-]
1128	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [3/2022]	564.66 (-) [564.66]	432.74 (0.00) [-]
1129	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [6/2022]	476.56 (-) [476.56]	258.64 (0.00) [59]
1130	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [3/2023]	633.68 (-) [633.68]	200.00 (0.00) [-]
1131	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [6/2022]	953.09 (-) [953.09]	514.05 (0.00) [-]
1132	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [2/2022]	668.86 (-) [668.86]	415.26 (0.00) [-]
1133	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [6/2022]	614.48 (-) [614.48]	359.38 (0.00) [-]
1134	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2022]	503.88 (-) [503.88]	158.96 (0.00) [-]
1135	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2022]	1,288.07 (-) [1,420.00]	1,100.45 (131.93) [24]
1136	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [6/2022]	686.65 (-) [686.65]	290.00 (0.00) [-]
1137	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [6/2022]	686.65 (-) [686.65]	254.00 (0.00) [-]
1138	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [3/2022]	417.51 (-) [417.51]	294.69 (0.00) [-]
1139	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [3/2023]	999.00 (-) [999.00]	221.63 (0.00) [-]
1140	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	107.06 (0.04) [0]
1141	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	525.19 (0.00) [0]
1142	SIX LANING OF CHANDIKHOL-JAGATPUR-	12/2011	6/2014	1,047.00	1,874.47

	BHUBANESWAR		(-) [0/0]	(-) [1,047.00]	(0.00) [0]
1143	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/	806.11	450.59
			(-) [6/2022]	(-) [806.11]	(0.00) [-]
1144	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016	191.50	183.94
			(-) [0/0]	(192.00) [192.00]	(0.50) [0]
1145	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015	191.08	182.41
			(-) [0/0]	(-) [191.08]	(0.00) [0]
1146	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017	287.70	226.26
			(-) [0/0]	(-) [287.70]	(0.00) [0]
1147	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018	214.23	132.67
			(-) [0/0]	(-) [214.23]	(0.00) [0]
1148	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018	223.50	149.61
			(-) [0/0]	(-) [223.50]	(0.00) [0]
1149	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018	199.16	135.38
			(-) [0/0]	(-) [199.16]	(0.00) [0]
1150	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017	295.67	220.15
			(-) [0/0]	(-) [295.67]	(0.00) [0]
1151	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018	206.88	133.36
			(-) [0/0]	(-) [206.88]	(0.00) [0]
Steel					
1152	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP	1/2022	5/2025	970.18	0.00
			(-) [5/2025]	(-) [970.18]	(0.00) [0]
1153	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023	377.18	57.81
			(-) [5/2023]	(-) [377.18]	(0.00) [0]
PONDICHERRY					
Health And Family Welfare					
1154	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020	195.00	16.41
			(-) [4/2022]	(-) [195.00]	(0.00) [19]
PUNJAB					
Department Of Higher Education					
1155	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022	348.24	35.43
			(-) [10/2022]	(-) [348.24]	(0.00) [5]
1156	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020	430.00	241.27
			(-) [8/2022]	(-) [387.83]	(-42.17) [27]
Health And Family Welfare					
1157	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020	703.00	557.97
			(-) [0/0]	(-) [635.00]	(-68.00) [0]
1158	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018	152.95	177.21
			(-) [4/2021]	(-) [177.92]	(24.97) [0]
Petroleum					
1159	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023	1,421.46	281.96
			(-) [2/2023]	(-) [1,421.46]	(0.00) [0]
Railways					

1160	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]
	Road Transport And Highways				
1161	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/	1,169.61	1,367.00
			(-) [0/0]	(-) [2,280.00]	(1,110.39) [0]
1162	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/	889.24	851.32
			(-) [0/0]	(-) [904.82]	(15.58) [0]
1163	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019	1,388.34	798.71
			(-) [0/0]	(-) [1,588.29]	(199.95) [0]
1164	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (3/2023) [3/2023]	754.54 (756.27) [756.27]	466.03 (1.73) [36]
1165	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1	12/2020	1/2024 (4/2024) [1/2024]	733.00 (-) [733.00]	0.00 (0.00) [0]
1166	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH-	2/2021	4/2024 (-) [4/2024]	1,269.96 (-) [1,269.96]	0.00 (0.00) [0]
1167	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR-	2/2021	4/2024 (-) [4/2024]	853.66 (-) [853.66]	0.00 (0.00) [0]
1168	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO	12/2020	4/2024 (-) [4/2024]	1,094.46 (-) [1,094.46]	0.00 (0.00) [0]
1169	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MALERKOTLA ROAD (SH-11) NEAR BHOGI WAL VI	12/2020	1/2024 (-) [4/2024]	989.66 (-) [989.66]	0.00 (0.00) [3]
1170	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO	12/2020	4/2024 (-) [4/2024]	1,234.40 (-) [1,234.40]	0.00 (0.00) [0]
1171	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA-BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO	12/2020	4/2024 (-) [4/2024]	881.00 (-) [881.00]	0.00 (0.00) [0]
1172	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	456.80
			(3/2023) [3/2023]	(479.00) [479.00]	(0.00) [-]
1173	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [12/2022]	1,069.59 (-) [1,069.59]	729.55 (0.00) [38]
1174	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/	196.05	143.03
			(-) [0/0]	(-) [196.05]	(0.00) [0]
1175	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/	199.90	124.52
			(-) [0/0]	(-) [199.90]	(0.00) [0]
1176	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0.000	3/2018	11/2020 (-) [12/2022]	170.57 (192.48) [170.57]	75.41 (0.00) [25]
1177	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [10/2022]	293.64 (-) [293.64]	261.09 (0.00) [26]
1178	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA	3/2018	8/2020 (-) [12/2022]	293.10 (-) [293.10]	214.90 (0.00) [28]
	RAJASTHAN				
	Atomic Energy				
1179	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700	10/2009	12/2016	12,320.00	14,142.00

	MW)		(-) [12/2023]	(17,079.00) [17,079.00]	(4,759.00) [84]
	<u>Coal</u>				
1180	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	93.05 (0.00) [0]
1181	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1182	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	113.42 (0.00) [0]
1183	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Department Of Higher Education</u>				
1184	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (7/2021) [7/2021]	549.31 (559.49) [580.00]	559.49 (30.69) [0]
	<u>Petroleum</u>				
1185	LPG BP PROJECT JODHPUR	3/2018	/ (5/2022) [3/2023]	229.80 (-) [229.80]	101.10 (0.00) [-]
1186	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE	12/2021	10/2024 (-) [10/2024]	9,028.00 (-) [9,028.00]	0.00 (0.00) [0]
	<u>Power</u>				
1187	ANTA SOLAR 90 MW	1/2021	3/2022 (-) [10/2022]	382.22 (-) [382.22]	8.24 (0.00) [7]
1188	BHENSARA 320 MW	1/2021	7/2022 (-) [7/2022]	1,221.73 (-) [1,221.73]	140.11 (0.00) [0]
1189	CHHATTARGARH 150 MW	2/2021	7/2022 (-) [7/2022]	599.99 (-) [599.99]	71.06 (0.00) [0]
1190	FATEHGARH SOLAR 296MW	3/2020	9/2021 (-) [3/2022]	1,749.31 (-) [1,749.31]	1,362.64 (0.00) [6]
1191	JETSAR SOLAR 160 MW	12/2019	3/2021 (12/2021) [3/2022]	702.28 (-) [702.28]	609.51 (0.00) [12]
1192	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (8/2022) [3/2022]	1,522.71 (-) [1,522.71]	1,114.48 (0.00) [6]
1193	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (10/2022) [10/2022]	1,782.00 (-) [1,782.00]	910.29 (0.00) [13]
1194	TRANSMISSION SYSTEM FOR PROVIDING CONNECTIVITY TO RE PROJECTS AT BIKANER (PG), FATEHGARH-II & BHADLA	1/2020	1/2021 (-) [3/2022]	562.86 (-) [562.86]	0.00 (0.00) [14]
1195	TRANSMISSION SYSTEM FOR SOLAR ENERGY ZONES IN RAJASTHAN	8/2019	12/2020 (-) [2/2022]	2,578.47 (-) [2,578.47]	0.00 (0.00) [14]
1196	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [12/2022]	353.85 (-) [353.85]	22.91 (0.00) [0]
1197	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [12/2022]	1,006.00 (-) [1,006.00]	253.02 (0.00) [0]
1198	TRANSMISSION SYSTEM STRENGTHENING SCHEME	6/2021	12/2022	713.82	130.01

	FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA		(-) [12/2022]	(-) [713.82]	(0.00) [0]
1199	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	3/2021	12/2022 (-) [12/2022]	1,340.81 (-) [1,340.81]	151.70 (0.00) [0]
1200	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	5/2021	9/2022 (-) [9/2022]	1,184.88 (-) [1,184.88]	12.83 (0.00) [0]
1201	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA	6/2021	12/2022 (-) [12/2022]	1,562.00 (-) [1,562.00]	249.63 (0.00) [0]
<u>Railways</u>					
1202	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	775.62 (450.33) [40]
1203	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	435.41 (0.00) [3]
1204	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [322.98]	0.00 (-0.02) [0]
<u>Road Transport And Highways</u>					
1205	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [0/0]	370.36 (-) [370.36]	245.15 (0.00) [0]
1206	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (9/2021) [9/2021]	597.00 (-) [597.00]	0.00 (0.00) [0]
1207	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1208	2L+PS FROM KM 148/170 TO 211 /100 (DEVAL-DUNGARPUR-HIRATA - VARDASAGWARA) SECTION OF NH-927A. PKG-	2/2021	11/2021 (-) [11/2021]	240.99 (-) [240.99]	0.00 (0.00) [0]
1209	4L+PS OF BEAWAR-ASIND SECTION (KM 30.00 TO KM 74.00) OF NH-158 (GNHCP) WORLD BANK. PKG-II	8/2020	12/2020 (-) [0/0]	216.72 (-) [216.72]	63.57 (0.00) [0]
1210	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 108.600 TO KM 144 KM 158.419 TO KM 173.300 PKG-II.	12/2020	10/2021 (-) [0/0]	339.65 (-) [339.65]	28.60 (0.00) [0]
1211	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG-I.	12/2020	10/2021 (-) [0/0]	379.23 (-) [379.23]	25.84 (0.00) [0]
1212	4L+PS OF RAS-BEAWAR SECTION (KM 0.00 TO KM 30.00) OF NH-158 (GNHCP) WORLD BANK. PKG-I.	7/2020	9/2021 (-) [0/0]	319.09 (-) [319.09]	12.93 (0.00) [0]
1213	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	1,518.41 (0.00) [-]
1214	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	164.94 (0.00) [0]
1215	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [3/2022]	822.90 (-) [822.90]	844.08 (0.00) [47]
1216	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [7/2020]	163.95 (-) [163.95]	122.04 (0.00) [0]
1217	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (10/2021) [12/2022]	741.86 (649.00) [649.00]	373.86 (-92.86) [-]

1218	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	330.46 (0.00) [0]
1219	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM	6/2016	6/2019 (-) [0/0]	649.00 (-) [649.00]	690.17 (0.00) [0]
1220	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (1,140.64) [1,198.64]	1,014.01 (234.47) [0]
1221	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1222	REHABILITATION AND UPGRADE TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020 (-) [0/0]	196.23 (-) [196.00]	63.07 (-0.23) [0]
1223	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [6/2022]	894.00 (-) [929.32]	810.00 (35.32) [26]
1224	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FROM	3/2020	8/2020 (-) [0/0]	255.23 (-) [255.23]	70.90 (0.00) [0]
1225	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	328.71 (0.00) [0]
1226	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	248.67 (0.00) [0]
1227	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	134.77 (0.00) [0]
	SIKKIM				
	Railways				
1228	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [12/2023]	1,339.48 (-) [8,600.00]	2,504.91 (7,260.52) [96]
	Road Transport And Highways				
1229	CONSTRUCTION AND UPGRADE OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	2.58 (0.00) [0]
1230	CONSTRUCTION AND UPGRADE OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
1231	CONSTRUCTION AND UPGRADE OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	32.50 (0.00) [0]
1232	CONSTRUCTION AND UPGRADE OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	96.67 (0.00) [0]
1233	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	76.84 (0.00) [0]
1234	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	120.72 (0.00) [0]
1235	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [4/2023]	375.80 (-) [375.80]	81.82 (0.00) [-]
1236	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [3/2022]	290.05 (-) [290.05]	154.83 (0.00) [52]
1237	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF	10/2020	12/2023	816.79	2.20

	NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0		(-) [12/2023]	(-) [816.79]	(0.00) [0]
1238	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
1239	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [5/2023]	402.94 (-) [402.94]	79.70 (0.00) [13]
1240	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	48.15 (0.00) [0]
1241	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	59.98 (0.00) [0]
1242	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	42.83 (0.00) [0]
1243	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	295.14 (59.37) [0]
1244	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
1245	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1246	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6	6/2017	9/2027 (-) [9/2027]	49,621.00 (-) [49,621.00]	5,453.00 (0.00) [0]
1247	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	30,143.00 (0.00) [36]
1248	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2022]	3,492.00 (-) [6,840.00]	6,268.20 (3,348.00) [145]
	<u>Civil Aviation</u>				
1249	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (3/2024) [3/2024]	380.87 (-) [380.87]	20.42 (0.00) [24]
1250	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (12/2024) [12/2024]	2,467.00 (-) [2,467.00]	838.87 (0.00) [34]
1251	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (4/2023) [4/2023]	951.28 (-) [951.28]	548.93 (0.00) [18]
	<u>Coal</u>				
1252	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (-) [9/2027]	1,458.17 (-) [709.06]	496.44 (-749.11) [147]
1253	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (-) [7,980.79]	7,429.39 (2,073.68) [0]
	<u>Finance</u>				
1254	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2021]	209.00 (-) [208.96]	208.93 (-0.04) [0]
1255	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	204.00 (0.00) [0]

	Mines				
1256	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2022) [12/2022]	166.62 (163.17) [163.17]	135.00 (-3.45) [42]
	Petroleum				
1257	CBR 9 MMTPA PROJECT	1/2021	6/2025 (-) [6/2025]	31,580.00 (-) [31,580.00]	571.14 (0.00) [0]
1258	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	210.74 (0.00) [0]
1259	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	49.47 (0.00) [0]
1260	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (-) [2/2024]	921.00 (-) [921.00]	5.70 (0.00) [5]
1261	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [3/2022]	466.43 (-) [466.43]	304.44 (0.00) [17]
1262	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (2/2022) [6/2022]	4,497.00 (6,025.00) [6,025.00]	4,270.46 (1,528.00) [42]
1263	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1264	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [5/2023]	650.82 (-) [650.82]	457.24 (0.00) [50]
1265	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [8/2022]	678.00 (-) [1,472.00]	19.44 (794.00) [66]
1266	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [2/2024]	1,398.00 (-) [1,398.00]	164.75 (0.00) [2]
	Power				
1267	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (-) [8/2022]	1,316.22 (-) [1,316.22]	948.04 (0.00) [11]
1268	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [8/2022]	186.17 (-) [219.66]	169.82 (33.49) [37]
	Railways				
1269	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [12/2022]	495.74 (-) [774.51]	539.14 (278.77) [114]
1270	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [12/2022]	760.00 (-) [1,536.00]	1,573.37 (776.00) [33]
1271	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2022]	164.41 (-) [591.00]	430.16 (426.59) [-]
1272	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [5/2023]	1,700.00 (-) [1,305.00]	1,137.46 (-395.00) [14]
1273	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [3,081.20]	1,726.52 (2,356.51) [73]
1274	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [3/2030]	839.00 (-) [839.01]	0.63 (0.01) [-]

1275	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [3,444.00]	241.49 (2,861.17) [-]
1276	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-) [3/2025]	303.98 (-) [1,549.09]	715.89 (1,245.11) [60]
	Road Transport And Highways				
1277	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [0/0]	485.00 (-) [485.00]	271.64 (0.00) [0]
1278	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014 (-) [9/2022]	624.00 (-) [624.00]	106.65 (0.00) [101]
1279	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	178.41 (0.00) [0]
1280	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	841.80 (0.00) [58]
1281	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [9/2021]	600.00 (-) [600.00]	8.12 (0.00) [0]
1282	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [12/2022]	1,016.92 (-) [1,071.00]	383.75 (54.08) [-]
1283	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [3/2022]	628.71 (-) [628.71]	411.17 (0.00) [-]
1284	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [12/2021]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1285	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [5/2022]	1,166.26 (-) [1,296.93]	346.17 (130.67) [-]
1286	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [12/2021]	641.17 (-) [641.17]	403.81 (0.00) [0]
1287	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [12/2022]	505.35 (-) [505.35]	255.05 (0.00) [-]
1288	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	742.16 (0.00) [59]
1289	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [1/2022]	707.82 (-) [707.82]	434.89 (0.00) [0]
1290	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (-) [848.45]	252.08 (0.00) [0]
1291	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [12/2021]	641.17 (-) [641.17]	403.81 (0.00) [0]
1292	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [5,148.00]	0.00 (1,722.00) [0]
1293	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [12/2021]	379.90 (-) [379.90]	254.10 (0.00) [0]
1294	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,342.23 (0.00) [0]

1295	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1296	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [2/2022]	374.00 (-) [166.90]	84.29 (-207.10) [105]
1297	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (8/2023) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1298	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [5/2023]	563.92 (-) [563.92]	42.83 (0.00) [65]
1299	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (-) [240.38]	143.36 (0.00) [0]
1300	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [0/0]	302.62 (-) [302.62]	87.40 (0.00) [0]
1301	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	250.73 (0.00) [0]
<u>Urban Development</u>					
1302	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (2/2021) [0/0]	3,770.00 (-) [3,770.00]	3,346.80 (0.00) [0]
1303	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [18,380.00]	18,051.27 (3,780.00) [0]
<u>TELANGANA</u>					
<u>Civil Aviation</u>					
1304	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (12/2023) [12/2023]	353.61 (-) [353.61]	109.92 (0.00) [19]
<u>Coal</u>					
1305	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	95.10 (0.00) [0]
1306	KAKATHIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2022 (-) [3/2022]	413.84 (-) [413.84]	290.90 (0.00) [0]
1307	RCE OF INDARAM OPENCAST PROJECT	8/2017	3/2021 (-) [3/2021]	349.28 (-) [349.28]	0.00 (0.00) [0]
1308	RCE OF KAKATHIYAKHANI OC - 2 PROJECT	8/2017	3/2020 (-) [3/2020]	442.42 (-) [442.42]	0.00 (0.00) [0]
1309	RCE OF KALYANIKHANI OPENCAST PROJECT	3/2016	3/2020 (-) [3/2020]	384.32 (-) [384.32]	0.00 (0.00) [0]
1310	RCE OF KISTARAM OPENCAST PROJECT	3/2017	3/2021 (-) [3/2021]	164.04 (-) [164.04]	0.00 (0.00) [0]
1311	RCE OF RAMAGUNDAM OPENCAST II EXTENSION PROJECT	11/2015	3/2023 (-) [3/2023]	489.62 (-) [489.62]	0.00 (0.00) [0]
1312	RCE-II OF JALAGAM VENGALRAO OPENCAST PROJECT-II	3/2019	3/2021 (-) [3/2021]	473.22 (-) [473.22]	0.00 (0.00) [0]
1313	SRP OC-II EXPANSION PROJECT	11/2016	3/2018 (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [48]

1314	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2023]	484.51 (-) [484.51]	27.52 (0.00) [0]
	<u>Health And Family Welfare</u>				
1315	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	202.48 (0.00) [0]
	<u>Petroleum</u>				
1316	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	139.54 (0.00) [16]
	<u>Power</u>				
1317	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (-) [5/2022]	401.90 (-) [442.03]	293.40 (40.13) [13]
1318	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [2/2023]	10,598.98 (-) [10,998.00]	9,223.00 (399.02) [27]
	<u>Railways</u>				
1319	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [4/2022]	632.68 (-) [950.00]	619.35 (317.32) [73]
1320	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (12/2022) [0/0]	636.38 (-) [636.38]	661.74 (0.00) [0]
1321	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [0/0]	119.73 (185.00) [242.28]	75.42 (122.55) [0]
1322	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2025]	1,160.48 (-) [1,373.74]	695.73 (213.26) [180]
1323	MANUGURU-RAMAGUNDAM	4/2013	/	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1324	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	1,248.22 (76.06) [0]
	<u>Road Transport And Highways</u>				
1325	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1326	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	162.89 (0.00) [0]
1327	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	218.04 (0.00) [0]
1328	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1329	FOUR LANING OF KHAMMAM-DEVARAPALLE SECTION (GREENFIELD)	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1330	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/	857.62 (-) [857.62]	373.21 (0.00) [0]
1331	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65 (-) [802.65]	476.66 (0.00) [0]
1332	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN	3/2018	/	950.63 (-) [0]	686.55 (0.00) [0]

	KM		[0/0]	[950.63]	[0]
1333	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (3/2021) [0/0]	828.29 (1,140.50) [828.29]	287.90 (0.00) [0]
1334	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (7/2019) [3/2022]	1,423.96 (-) [1,056.08]	1,020.25 (-367.88) [40]
1335	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019 (-) [0/0]	192.67 (-) [192.67]	165.04 (0.00) [0]
1336	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR)	1/2017	10/2019 (-) [0/0]	605.08 (-) [605.08]	410.21 (0.00) [0]
1337	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020 (-) [0/0]	426.52 (-) [426.52]	395.25 (0.00) [0]
1338	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	0.00 (0.00) [0]
1339	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019 (-) [0/0]	294.13 (-) [294.13]	160.81 (0.00) [0]
1340	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019 (-) [0/0]	220.28 (-) [220.28]	170.34 (0.00) [0]
1341	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020 (-) [0/0]	322.81 (-) [322.81]	239.94 (0.00) [0]
1342	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [295.47]	207.71 (0.00) [0]
1343	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019 (-) [0/0]	248.83 (-) [248.83]	126.24 (0.00) [0]
1344	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019 (-) [0/0]	298.32 (-) [298.32]	135.18 (0.00) [0]
1345	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019 (-) [0/0]	230.03 (-) [230.03]	220.35 (0.00) [0]
1346	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020 (-) [0/0]	206.13 (-) [206.13]	184.68 (0.00) [0]
1347	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/ (-) [0/0]	193.19 (-) [193.19]	147.53 (0.00) [0]
1348	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019 (-) [0/0]	196.52 (-) [196.52]	116.85 (0.00) [0]
1349	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019 (-) [0/0]	283.00 (-) [283.00]	245.68 (0.00) [0]
1350	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019 (-) [0/0]	244.54 (-) [244.54]	166.41 (0.00) [0]
1351	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT	1/2017	5/2019 (-) [0/0]	359.27 (-) [359.27]	306.88 (0.00) [0]
1352	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	208.95 (0.00) [0]

	<u>TRIPURA</u>				
	<u>Civil Aviation</u>				
1353	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AND ASSOCIATED WORKS AT AGARTALA AIRPORT	9/2015	6/2019 (12/2021) [12/2021]	438.28 (-) [402.00]	398.21 (-36.28) [0]
	<u>Railways</u>				
1354	AGARTALA-AKHAURA NL	4/2012	3/2020 (6/2022) [9/2022]	569.63 (-) [708.73]	549.81 (139.10) [30]
	<u>Road Transport And Highways</u>				
1355	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	358.78 (0.00) [0]
1356	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	18.87 (0.00) [0]
1357	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [10/2022]	247.76 (-) [247.76]	36.82 (0.00) [9]
1358	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	116.18 (0.00) [0]
1359	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	13.63 (0.00) [0]
1360	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	14.10 (0.00) [0]
1361	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	87.79 (0.00) [0]
1362	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	99.97 (0.00) [0]
1363	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	12.02 (0.00) [0]
1364	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	10.93 (0.00) [0]
1365	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	14.79 (0.00) [0]
1366	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	22.21 (0.00) [0]
1367	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	47.29 (0.00) [0]
1368	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	114.77 (0.00) [0]
1369	STRENGTHENING OF CHURAI BARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	122.81 (0.00) [0]
1370	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	86.74 (38.51) [0]
1371	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [11/2021]	171.90 (-) [171.90]	142.81 (0.00) [0]

	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1372	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [12/2023]	1,383.00 (-) [1,938.00]	579.75 (555.00) [27]
	<u>Coal</u>				
1373	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	0.00 (0.00) [0]
1374	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [6/2023]	17,237.00 (-) [17,237.80]	13,185.30 (0.80) [19]
	<u>Health And Family Welfare</u>				
1375	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [0/0]	785.00 (-) [760.00]	604.15 (-25.00) [0]
1376	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [5/2021]	268.84 (-) [284.67]	279.53 (15.83) [0]
	<u>Home Affairs</u>				
1377	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAUJI	5/2019	1/2022 (12/2022) [12/2022]	199.31 (-) [199.31]	75.31 (0.00) [11]
	<u>Petroleum</u>				
1378	60 KTA POLYPROPYLENE PROJECT	3/2019	4/2024 (-) [4/2024]	910.56 (-) [910.56]	141.31 (0.00) [0]
1379	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	546.09 (0.00) [0]
1380	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [345.15]	265.22 (57.66) [0]
1381	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (-) [8/2029]	3,450.20 (-) [3,450.20]	621.42 (0.00) [5]
1382	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (3/2022) [10/2022]	217.92 (-) [217.92]	106.90 (0.00) [18]
1383	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (3/2022) [10/2022]	255.40 (-) [255.40]	154.50 (0.00) [26]
1384	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (3/2023) [3/2023]	318.80 (-) [318.80]	188.36 (0.00) [19]
	<u>Power</u>				
1385	DEVIKOT SOLAR 150MW	1/2020	9/2021 (-) [5/2022]	798.24 (-) [852.90]	596.05 (54.66) [8]
1386	DEVIKOT SOLAR 90MW	3/2020	9/2021 (-) [3/2022]	501.29 (-) [524.83]	400.95 (23.54) [6]
1387	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	3,654.43 (0.00) [11]
1388	NOKHRA	3/2020	9/2021 (-) [10/2022]	1,722.14 (-) [1,803.19]	612.20 (81.05) [13]
1389	PARASAN SOLAR POWER PROJECT	8/2021	12/2022 (-) [12/2022]	313.58 (-) [313.58]	298.99 (0.00) [0]

	<u>Railways</u>				
1390	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1391	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	345.95 (-233.29) [2]
1392	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1393	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [6/2022]	1,183.25 (-) [2,203.53]	1,851.27 (1,020.28) [18]
1394	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [12/2023]	602.50 (-) [800.00]	164.95 (197.50) [-]
1395	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1396	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	88.76 (0.35) [0]
1397	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [6/2023]	2,001.00 (-) [2,001.00]	1,080.53 (0.00) [27]
1398	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [6/2025]	4,329.53 (-) [4,329.53]	89.74 (0.00) [27]
1399	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1400	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2022]	528.57 (-) [528.57]	347.96 (0.00) [36]
1401	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2023]	927.01 (-) [1,457.79]	1,346.71 (530.78) [48]
1402	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	2,601.90 (0.00) [0]
1403	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	1,129.41 (0.00) [21]
1404	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.00 (191.66) [66]
1405	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1406	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,570.66 (0.00) [48]
1407	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,824.00]	1,518.04 (528.58) [0]
1408	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	493.91 (-149.01) [0]
1409	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2022]	943.60 (-) [1,500.00]	1,042.79 (556.40) [9]

	Road Transport And Highways				
1410	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (503.36) [368.73]	487.13 (0.00) [0]
1411	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [417.68]	433.68 (66.34) [0]
1412	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [627.93]	633.24 (132.15) [0]
1413	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [469.31]	459.07 (177.95) [0]
1414	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1415	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,525.15 (211.43) [0]
1416	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (2/2022) [0/0]	1,668.00 (2,501.85) [2,501.85]	946.08 (833.85) [0]
1417	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1418	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (7/2022) [7/2022]	1,408.00 (1,330.02) [1,330.02]	920.72 (-77.98) [-]
1419	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (12/2021) [12/2021]	1,737.00 (2,421.37) [2,421.37]	2,192.68 (684.37) [0]
1420	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	2,977.58 (0.00) [0]
1421	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1422	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1423	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,118.76 (382.01) [0]
1424	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1425	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	985.40 (0.00) [0]
1426	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1427	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD	7/2018	2/2024 (-) [2/2024]	1,948.25 (-) [1,948.25]	313.56 (0.00) [0]
1428	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1429	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]

1430	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [0]
1431	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1432	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [4/2022]	282.41 (-) [319.96]	193.60 (37.55) [73]
1433	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	1,084.94 (-145.21) [0]
1434	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	772.56 (0.00) [0]
1435	ETAWAH CHAKERI	3/2013	9/2015 (-) [1/2016]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1436	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	75.10 (0.00) [0]
1437	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [1,065.70]	930.46 (256.63) [0]
1438	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,176.70 (271.60) [0]
1439	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1440	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	464.05 (0.00) [0]
1441	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1442	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1443	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1444	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [3/2022]	288.30 (-) [323.36]	222.57 (35.06) [19]
1445	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [3/2022]	1,373.28 (-) [1,373.28]	1,357.48 (0.00) [24]
1446	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [1/2022]	1,184.71 (-) [1,310.00]	1,307.68 (125.29) [0]
1447	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (6/2022) [6/2022]	899.00 (1,376.86) [1,376.86]	887.23 (477.86) [38]
1448	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [3/2022]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [103]
1449	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [3/2022]	281.45 (-) [319.96]	126.00 (38.51) [-]
1450	MEERUT-BULANDSHAHR	1/2016	/	683.24	0.00

			(-) [0/0]	(-) [987.94]	(304.70) [0]
1451	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/	326.99	137.90
			(-) [3/2022]	(327.00) [326.99]	(0.00) [-]
1452	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020	296.50	237.81
			(-) [12/2021]	(-) [296.50]	(0.00) [0]
1453	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/	1,025.80	222.94
			(-) [0/0]	(-) [677.07]	(-348.73) [0]
1454	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/	1,115.28	332.69
			(-) [0/0]	(-) [770.04]	(-345.24) [0]
1455	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020	263.89	190.01
			(-) [3/2022]	(-) [242.05]	(-21.84) [23]
1456	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020	185.18	124.69
			(-) [1/2021]	(-) [185.18]	(0.00) [0]
1457	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/	306.59	197.64
			(-) [1/2022]	(-) [306.59]	(0.00) [0]
1458	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020	240.30	200.10
			(-) [3/2021]	(240.00) [240.30]	(0.00) [0]
1459	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14	11/2017	1/2019	2,159.00	1,720.10
			(-) [1/2019]	(2,262.00) [2,262.00]	(103.00) [0]
1460	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/	2,140.93	1,315.69
			(-) [0/0]	(-) [2,140.93]	(0.00) [0]
1461	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023	724.60	0.00
			(-) [3/2023]	(-) [724.60]	(0.00) [0]
1462	VARANASI RING ROAD PKG - I	1/2018	/	450.77	0.00
			(-) [0/0]	(-) [450.77]	(0.00) [0]
1463	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015	164.54	141.33
			(-) [1/2021]	(-) [164.54]	(0.00) [0]
	<u>Urban Development</u>				
1464	AGRA METRO RAIL PROJECT	5/2019	3/2024	8,379.62	593.47
			(-) [12/2025]	(-) [8,379.62]	(0.00) [21]
1465	KANPUR METRO RAIL PROJECT	5/2019	3/2024	11,076.48	2,561.78
			(-) [11/2024]	(-) [11,076.48]	(0.00) [8]
	<u>Water Resources</u>				
1466	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022	213.62	0.00
			(-) [4/2024]	(-) [261.12]	(47.50) [25]
1467	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021	206.05	95.91
			(-) [3/2022]	(-) [206.05]	(0.00) [5]
1468	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021	231.79	28.37
			(-) [6/2023]	(-) [234.03]	(2.24) [18]
1469	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021	271.39	0.00
			(-) [3/2024]	(-) [271.39]	(0.00) [31]

1470	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [3/2024]	298.12 (-) [213.91]	0.00 (-84.21) [32]
1471	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [12/2022]	767.59 (-) [767.59]	152.31 (0.00) [15]
1472	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [3/2022]	460.45 (-) [460.45]	248.16 (0.00) [15]
1473	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [4/2024]	681.78 (-) [690.71]	0.00 (8.93) [22]
1474	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2022]	967.23 (-) [967.23]	109.63 (0.00) [12]
	UTTARAKHAND				
	Civil Aviation				
1475	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (12/2022) [12/2022]	456.86 (-) [456.86]	340.28 (0.00) [27]
	Petroleum				
1476	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [10/2022]	160.10 (-) [160.10]	106.27 (0.00) [32]
	Power				
1477	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,527.00]	149.93 (0.00) [0]
1478	NAITWAR MORI HEP	10/2017	12/2021 (-) [6/2022]	648.33 (-) [947.89]	820.12 (299.56) [6]
1479	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [12/2024]	2,978.48 (5,867.38) [5,867.38]	5,247.00 (2,888.90) [141]
1480	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2023]	1,657.00 (-) [4,825.60]	4,409.29 (3,168.60) [88]
1481	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (6/2025) [6/2025]	2,491.58 (3,860.35) [3,860.35]	2,416.30 (1,368.77) [144]
	Railways				
1482	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [24,659.00]	6,259.16 (8,443.00) [3]
	Road Transport And Highways				
1483	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [7/2022]	403.36 (-) [403.36]	224.23 (0.00) [49]
1484	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [9/2022]	417.24 (-) [417.24]	276.32 (0.00) [52]
1485	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (2/2022) [5/2022]	605.84 (1,023.23) [1,023.23]	980.59 (417.39) [46]
1486	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (2/2022) [2/2022]	1,443.00 (2,330.79) [2,330.79]	1,246.85 (887.79) [-]
1487	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [9/2022]	274.31 (-) [274.31]	136.62 (0.00) [52]
1488	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL	3/2018	7/2018	1,383.78	299.26

	BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)		(-) [7/2022]	(-) [1,383.78]	(0.00) [48]
1489	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [12/2021]	248.00 (-) [248.00]	109.23 (0.00) [0]
1490	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/ (9/2022) [9/2022]	720.00 (793.63) [793.63]	291.10 (73.63) [-]
1491	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (3/2022) [3/2022]	478.51 (1,082.40) [1,082.40]	1,023.73 (603.89) [101]
1492	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [7/2021]	232.81 (-) [232.81]	171.22 (0.00) [0]
1493	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [5/2021]	283.51 (-) [283.51]	259.90 (0.00) [0]
1494	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [7/2021]	257.34 (-) [257.34]	214.90 (0.00) [0]
1495	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [7/2021]	200.34 (-) [200.34]	185.44 (0.00) [0]
1496	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [12/2021]	282.08 (-) [282.08]	207.83 (0.00) [0]
1497	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [9/2021]	418.88 (-) [418.88]	287.56 (0.00) [0]
1498	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [10/2020]	266.52 (-) [266.52]	186.16 (0.00) [0]
1499	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (-) [12/2020]	234.88 (-) [234.88]	174.51 (0.00) [0]
1500	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [10/2021]	293.68 (-) [293.68]	183.73 (0.00) [0]
1501	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	116.25 (0.27) [0]
1502	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [8/2021]	248.22 (-) [248.22]	234.12 (0.00) [0]
	<u>Water Resources</u>				
1503	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (-) [3/2022]	158.00 (-) [158.00]	87.59 (0.00) [28]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1504	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (4/2023) [4/2023]	389.71 (-) [389.71]	233.91 (0.00) [17]
1505	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA	1/2016	3/2020 (3/2024) [3/2024]	458.00 (-) [458.00]	171.37 (0.00) [48]
	<u>Coal</u>				
1506	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [12/2022]	304.13 (-) [341.22]	91.55 (37.09) [69]
1507	EXPANSION PR OF JHANJRA UG (5.00 MTY)	4/2020	3/2029	1,210.12	0.00

			(-) [3/2029]	(-) [1,210.12]	(0.00) [0]
1508	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	26.86 (0.00) [0]
1509	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	1.49 (0.00) [0]
1510	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	625.60 (2,484.75) [60]
1511	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	9.64 (0.00) [0]
1512	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.75 (0.00) [0]
1513	SONEPUR BAZARI EXPANSION OC	7/2021	3/2029 (-) [3/2029]	5,365.88 (5,366.00) [5,365.88]	0.00 (0.00) [0]
1514	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	4.48 (0.00) [0]
	<u>Department Of Higher Education</u>				
1515	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [3/2023]	193.83 (-) [193.83]	77.27 (0.00) [33]
	<u>Health And Family Welfare</u>				
1516	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [12/2021]	244.00 (-) [248.00]	224.92 (4.00) [0]
1517	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [1/2021]	168.90 (-) [191.20]	169.51 (22.30) [0]
1518	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [12/2021]	651.99 (-) [651.99]	609.49 (0.00) [0]
1519	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [12/2021]	355.15 (-) [355.15]	321.31 (0.00) [0]
	<u>Home Affairs</u>				
1520	NSG AT KOLKATA	10/2014	4/2018 (-) [12/2022]	162.88 (-) [228.63]	173.62 (65.75) [56]
	<u>Mines</u>				
1521	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR-V, SA	4/2019	4/2022 (-) [10/2024]	255.37 (-) [255.37]	1.16 (0.00) [30]
	<u>Petroleum</u>				
1522	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [9/2022]	3,712.00 (3,696.00) [3,696.00]	2,441.32 (-16.00) [0]
1523	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (-) [8/2031]	5,830.20 (-) [5,830.20]	174.36 (0.00) [5]
1524	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (12/2021) [6/2023]	1,740.00 (-) [1,740.00]	983.90 (0.00) [30]
1525	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [1/2023]	1,019.00 (-) [1,019.00]	177.06 (0.00) [0]

1526	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2022]	163.02 (-) [207.36]	135.65 (44.34) [30]
	Power				
1527	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (6/2022) [6/2022]	529.68 (633.80) [679.00]	513.91 (149.32) [43]
1528	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [7/2025]	1,381.84 (-) [1,803.00]	754.00 (421.16) [70]
	Railways				
1529	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	311.86 (16.56) [-]
1530	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1531	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]
1532	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1533	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [7/2025]	2,913.51 (-) [4,834.54]	1,586.17 (1,921.03) [112]
1534	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1535	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2026]	3,951.98 (-) [4,259.48]	3,139.94 (307.50) [120]
1536	PURULIA TO KOTSHILA DOUBLING (39.1 KM)	4/2018	6/2022 (-) [12/2023]	338.00 (-) [393.83]	23.56 (55.83) [18]
1537	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	912.17 (430.57) [72]
	Road Transport And Highways				
1538	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (1,414.01) [1,414.01]	990.95 (331.01) [0]
1539	4-LANING OF BRAHAMPUR-FARAKA	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	1,913.66 (0.00) [118]
1540	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [3/2022]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [103]
1541	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]
1542	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (416.00) [363.93]	277.34 (2.78) [0]
1543	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (3/2022) [3/2023]	271.17 (291.20) [291.20]	120.51 (20.03) [52]
1544	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (11/2022) [3/2023]	160.27 (-) [213.97]	27.41 (53.70) [43]
1545	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS	6/2016	8/2019	236.78	78.56

	APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N		(8/2022) [3/2023]	(-) [263.26]	(26.48) [43]
1546	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO)	3/2018	10/2020 (12/2021) [3/2023]	254.30 (-) [254.30]	118.68 (0.00) [29]
1547	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	708.78 (0.00) [0]
1548	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,952.20]	97.16 (690.22) [0]
1549	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (-) [2/2020]	279.70 (398.22) [398.52]	331.86 (118.82) [0]
1550	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (1/2022) [12/2022]	396.86 (-) [396.86]	277.42 (0.00) [39]
1551	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,516.44 (695.65) [0]
1552	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [6/2021]	218.70 (-) [218.70]	122.50 (0.00) [0]
1553	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (1/2022) [12/2022]	426.18 (-) [426.18]	258.00 (0.00) [27]
	Water Resources				
1554	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (-) [5/2022]	274.76 (-) [274.76]	225.99 (0.00) [29]
1555	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [12/2024]	384.96 (-) [384.96]	0.00 (0.00) [32]
1556	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [12/2024]	234.31 (-) [234.31]	0.00 (0.00) [32]
1557	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [3/2024]	165.16 (-) [165.16]	0.00 (0.00) [21]
1558	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [3/2024]	160.00 (-) [154.73]	0.00 (-5.27) [25]
1559	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [12/2024]	287.53 (-) [287.53]	0.00 (0.00) [32]
1560	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [9/2023]	164.93 (-) [164.93]	34.69 (0.00) [21]
1561	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [3/2024]	198.43 (-) [224.69]	0.00 (26.26) [25]
1562	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [12/2024]	307.12 (-) [307.12]	0.00 (0.00) [27]
1563	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [9/2023]	172.10 (-) [172.10]	38.00 (0.00) [21]
1564	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [9/2023]	185.22 (-) [185.22]	38.00 (0.00) [21]
1565	SEWERAGE SYSTEM WITH SEWER NETWORK AT	12/2014	4/2020	272.32	261.87

	BARRACKPORE		(-) [3/2022]	(-) [272.32]	(0.00) [23]
	Total			21,86,542.05 (5,31,147.48) [26,59,914.61]	13,26,569.75 (4,73,372.56)

FLASH REPORT
