

**339th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
January 2014**



NHAI - TRICHY - KORUR NH-67



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

जनवरी, 2014 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 722 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जनवरी, 2014 के दौरान रेलवे क्षेत्र की 23 परियोजनाओं (सड़क क्षेत्र की 20, विद्युत क्षेत्र की 2 तथा पेट्रोलियम क्षेत्र की 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 722 परियोजनाओं में से 204 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 38 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 38 परियोजनाओं में से, 13 परियोजनाएं ₹1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं। परमाणु ऊर्जा, कोयला, नागर विमानन, इस्पात, दूरसंचार, सड़क, पोत परिवहन तथा पत्तन, विद्युत, रेलवे तथा पेट्रोलियम क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 24 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	284	37	4	1
2.	सड़क परिवहन एवं राजमार्ग	132	8	2	0
3.	विद्युत	102	53	9	4
4.	पेट्रोलियम	82	53	13	6
5.	कोयला	55	29	3	1
6.	इस्पात	20	10	1	0
7.	पोत परिवहन एवं पत्तन	19	2	1	0
8.	दूरसंचार	10	4	3	0
9.	नागर विमानन	8	3	1	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	शहरी विकास	4	1	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		722	204	38	13

3. 722 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ₹9,00,150.20 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 10,80,739.25 करोड़ रुपए होने की संभावना है जो ₹1,80,589.05 करोड़ (मूल लागत का 20.10%) की समग्र लागत वृद्धि को दर्शाता है। जनवरी, 2014 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,13,988.97 करोड़ है जो परियोजनाओं की अनुमानित लागत का 46.60% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	00.00	2000.00	985.42

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	जिरीबाम से इंफाल (तुपु) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
3	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.33	11609.00	5214.00
4	सुबानश्री लोअर एचईपी (एनएचपीसी)	विद्युत	09/2003	6285.33	10667.00	4381.67
5	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 722 परियोजनाओं में से, 3 परियोजनाएं समय से पहले चल रही हैं, 161 समय पर तथा 204 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 229 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 23 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 331 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 204 विलंबित परियोजनाओं में से, 47 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 51 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 68 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 38 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2013	238
3	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	143
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	181

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, कार्य-क्षेत्र में बदलाव, माओवादी गतिविधियां, संविदा संबंधी मामले, कार्य प्रदान करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी

परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि

संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.01.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

1. पोत परिवहन तथा पत्तन क्षेत्र में 19 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं । 'मेसर्स जियांगसू रोंगशेंग हेवी, भारतीय जहाजरानी निगम से 317000 डीडब्ल्यूटी के बहुत बड़े कच्चे माल के दो जहाजों का अधिग्रहण' नामक परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना दी गई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

- II. नागर विमानन क्षेत्र** में 8 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । 'नए अंतर्राष्ट्रीय टर्मिनल भवन का निर्माण (जीओए) एएआई' नामक परियोजना के संबंध में संरचना संबंधी डिजाइन एवं श्रमिकों की कमी के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- III. परमाणु ऊर्जा क्षेत्र** में सभी 4 परियोजनाएं विलंबित हैं । 'कुंडकुलम परमाणु ऊर्जा संयंत्र, एनपीसीआईएल' (मेगा परियोजना) के संबंध में उपस्करों की आपूर्ति में विलंब के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- IV. इस्पात क्षेत्र** में 20 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं । 'आरएमएचपी में लौह अयस्क भंडारण का संवर्धन, आरआईएनएल' परियोजना के संबंध में प्रौद्योगिकी-वाणिज्यिक मामलों में बदलाव के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- V. सड़क क्षेत्र** में 132 परियोजनाओं में से 8 परियोजनाएं विलंबित हैं । माह के दौरान 2 परियोजनाओं के संबंध में 3 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'सिल्चर-उदरबेंड (चरण-II) एनएच-54, 309 किमी से 275 किमी एनएचएआई' तथा 'पानीपत-रोहतक, एनएचएआई' नामक परियोजनाओं के संबंध में क्रमशः 3 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।
- VI. कोयला क्षेत्र** में 55 परियोजनाओं में से 29 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 5-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 1 मेगा परियोजना है । 'आद्रियाला शाफ्ट परियोजना, एससीसीएल' परियोजना के संबंध में उपस्करों की आपूर्ति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'काकतिया लॉगवाल, एससीसीएल' परियोजना के संबंध में टीपीओ (प्रौद्योगिकी प्रदानकर्ता तथा आपरेटर) द्वारा कार्य में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'अनंत ओसी विस्तार चरण-III (15.0 एमटीवाई), एमसीएल' नामक परियोजना के संबंध में वन संबंधी अनुमति के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- VII. दूरसंचार क्षेत्र** में 10 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'उत्तरांचल में 283000 लाईन (2जी) तथा 75000 लाईन (3जी) के जीएसएम उपकरण, बीएसएनएल', 'असम टेलीकॉम सर्किल, चरण-VI, 2जी तथा 3 जी, बीएसएनएल' एवं 'ग्रामीण बीमेक्स नेटवर्क चरण-II, हेतु आपूर्ति, संस्थापन, जांच शुरू करना, बीएसएनएल' नामक

परियोजनाओं के संबंध में क्रमशः भूमि अधिग्रहण में विलंब, नगरपालिका से अनुमति में विलंब तथा न्यायालय संबंधी मामलों के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

VII. रेलवे क्षेत्र में 284 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं। माह के दौरान, 4 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इनमें से 1 मेगा परियोजना है। 'लांझीगढ़-जूनागढ़, नई लाइन, ईसीओआर' परियोजना के संबंध में निधि की कमियों के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बाडानगर से बेरकपुर तथा दक्षिणेश्वर (एमटीपी) तक मेट्रो रेलवे के निर्माण हेतु नए कार्य, आरवीएनएल' नामक परियोजना के संबंध में मेट्रो रेलवे की सीध में बैरकों द्वारा अतिक्रमण होने के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा 'वेलाचेरी से स्टेशन थॉमस एमटीपी तक एमआरटीएस का विस्तार, एमआरटीपी' एवं 'जुबिली पुल सं.8, ईआर के स्थान पर बंदेल-नेहाटी नया रेल पुल' नामक परियोजनाओं के संबंध में प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

IX. विद्युत क्षेत्र में, 102 परियोजनाओं में से 53 परियोजनाएं विलंबित हैं। माह के दौरान, 9 परियोजनाओं के संबंध में 2-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 4 मेगा परियोजनाएं हैं। 'यूटी डीएनएच में काला में 400/220 केवी जीआईएस उप स्टेशनों की स्थापना के लिए पारेषण प्रणाली, पीजीसीआईएल', 'एसआर ग्रिड का प्रणाली सुदृढीकरण XII, पीजीसीआईएल', तथा 'एस्सार पावर गुजरात लिमिटेड की कनेक्टिविटी के लिए पारेषण प्रणाली, पीजीसीआईएल' परियोजनाओं के संबंध में आरओडव्ल्यू समस्याओं के कारण क्रमशः 2, 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'तीस्ता लो डेम, एचईपी, स्टेज-IV एनएचपीसी' परियोजना के संबंध में संविदा संबंधी मामलों के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बार एसटीपीपी चरण-II, एनटीपीसी' परियोजना के संबंध में उपस्करों की आपूर्ति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'कोल्डाम एचईपी, एनटीपीसी' परियोजना के संबंध में मुख्य बांध में रिसन के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'टुइरियल जल विद्युत परियोजना के संबंध में कानूनी मामलों के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'पारे जल विद्युत परियोजना, एनईईपीसीओ' परियोजना के संबंध में भूतकनीकी पैरामीटर में बदलाव के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'त्रिपुरा गैस आधारित विद्युत परियोजना,

एनईईपीसीओ' परियोजना में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

X पेट्रोलियम क्षेत्र में 82 परियोजनाओं में से 53 परियोजनाएं विलंबित हैं । माह के दौरान, 13 परियोजनाओं के संबंध में 1-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 6 मेगा परियोजनाएं हैं । 'पारादीप रिफाइनरी परियोजना, आईओसीएल', 'हाइड्रोक्रैकर रिवैम्प तथा मुंबई रिफाइनरी में नया सीसीआर स्थापित करना, वीपीसीएल' तथा 'गैस टर्बाइन जेनरेशन सेट, ओआईएल' परियोजनाओं के संबंध में क्रमशः पर्यावरण संबंधी अनुमति, निर्माण कार्य के पूरा होने में विलंब तथा सामग्री की आपूर्ति में विलंब के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'विशाख रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना एचपीसीएल' परियोजना के संबंध में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'एमआरपीएल चरण-III विस्तार मंगलौर रिफाइनरी' तथा '102 मेवा. पवन विद्युत परियोजना, ओएनजीसी' परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'एसबी-14 फील्ड का विकास, ओएनजीसी' तथा 'मुंबई रिफाइनरी में सीडीयू/वीडीयू का प्रतिस्थापन, वीपीसीएल' नामक परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'जी1 तथा जीएस-15 का विकास, ओएनजीसी' तथा '23 तात्कालिक आपूर्ति जहाज (आईएसवी) का निर्माण, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः 4 और 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है 'जीजीएस-एनएडीए में एक ईटीपी का निर्माण, अंकलेश्वर, ओएनजीसी' तथा '6 ईपीटीएस का निर्माण, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः 8 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'तीन ईटीपीएस का निर्माण, मेहसाना, ओएनजीसी' परियोजना के संबंध में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

10. दिनांक 31.01.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for January 2014 contains information on the status of the 722 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During January 2014, 23 projects (20 projects in Road, 2 projects in Power and 1 project in Petroleum Sector) have reported completion.

2. During the reference month, out of 722 projects, 204 projects are delayed with respect to latest schedule and 38 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 38 projects, 13 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 24 months in respect of projects relating to Atomic Energy, Coal, Civil Aviation, Steel, Telecommunication, Road, Shipping & Ports, Power, Railways and Petroleum Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	284	37	4	1
2.	ROAD TRANSPORT AND HIGHWAYS	132	8	2	0
3.	POWER	102	53	9	4
4.	PETROLEUM	82	53	13	6
5.	COAL	55	29	3	1
6.	STEEL	20	10	1	0
7.	SHIPPING AND PORTS	19	2	1	0
8.	TELECOMMUNICATIONS	10	4	3	0
9.	CIVIL AVIATION	8	3	1	0
10.	ATOMIC ENERGY	4	4	1	1
11.	URBAN DEVELOPMENT	4	1	0	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		722	204	38	13

3. Total original cost of implementation of the 722 projects was about ₹ 9,00,150.20 crore and their anticipated completion cost is likely to be ₹ 10,80,739.25 crore, which reflects overall cost overruns of ₹ 1,80,589.05 crore (20.10 % of original cost). The expenditure incurred on these projects till January 2014 is ₹ 5,13,988.97 crore, which is 47.60 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-01 -2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	AKOLA-KHANDWA GC AKOLA-AKOT	Railways	04/2008	184.26	00.00	2000.00	985.42

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-01-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	5996.00	5268.44
3	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.33	11609.00	5214.00
4	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
5	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 722 projects, 3 projects are ahead of schedule, 161 are on schedule and 204 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 229 if delay is calculated on the basis of original schedule of completion. Further, 23 projects have been sanctioned without any commissioning schedule/date and for 331 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 204 delayed projects, 47 projects have overall delay in the range of 1 to 12 months, 51 projects have a delay in the range of 13 to 24 months, 68 projects have a delay in the range of 25 to 60 months and 38 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-01-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	238
3	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	143
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	181

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, fund constraints, geological surprises, change in scope of work, maoist activities, contractual issue, delay in award of works, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-01-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-01-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.01.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Shipping & Ports Sector**, out of 19 projects, 2 projects are delayed. The project 'Acquisition of Two (2) Nos. of 317000 DWT Very Large Crude Carriers from M/S Jiangsu Rongsheng Heavy, Shipping Corporation of India' has reported additional delay of 2 months (however, no specific reasons have been reported by the project authority for the delay in this project).

ii) In the **Civil Aviation Sector**, out of 8 projects, 3 projects are delayed. The project 'Construction of New International Terminal Building (GOA), AAI' has reported additional delay of 3 months due to change in structural design and shortage of labour.

iii) In the **Atomic Energy Sector**, all the 4 projects reported delay. The project 'Kudankulam APP, NPCIL' (Mega Project) has reported additional delay of 7 months due to delay in supply of equipments.

iv) In the **Steel Sector**, out of 20 projects, 10 projects are delayed. The project 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 1 month due to change in techno-commercial issues.

v) In the **Road Sector**, out of 132 projects, 8 projects are delayed. During the month 2 projects have reported additional delays of 3 and 10 months. The projects 'Silchar-Udarband (PH.II) HN-54, KM.309 to KM.275, NHAI' and 'Panipat-Rohtak, NHAI' have reported additional delays of 3 and 10 months respectively (however, no specific reasons have been reported by the project authority for the delay in these projects).

vi) In the **Coal Sector**, out of 55 projects, 29 projects are delayed. During the month 3 projects have reported additional delays in the range of 5-24 months, out of which 1 is Mega project. The project 'Adriyala Shaft Project, SCCL' has reported additional delay of 5 months due to delay in supply of equipments; the project 'Kakatiya Longwall, SCCL' has reported additional delay of 12 months due to delay in work by TPO (Technology provider cum operator); and the project 'Ananta OC Expansion PH-III (15.0 MTY), MCL' has reported additional delay of 24 months due to forest clearance

vi) In the **Telecommunication Sector**, out of 10 projects, 4 projects are delayed. During the month 3 projects have reported additional delays 3 months each. The projects 'GSM Equipment of 283000 Lines (2G) and 75000 LINES (3G) in Uttranchal, BSNL' ,

‘Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL’ and ‘Supply Installation Testing and Commissioning of Rural Wimax Network Phase-II, BSNL’ have reported additional delays of 3 months each due to delay in land acquisition, delay in municipal permission and court cases respectively.

viii) In the **Railways Sector**, out of 284 projects, 37 projects are delayed. During the month 4 projects have reported additional delays in the range of 1- 24 months, out of which 1 is Mega project. The project ‘Lanjigarh-Junagarh, New Line, ECOR’ has reported additional delay of 1 month due to fund constraints; the project ‘New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL’ has reported additional delay of 24 months due to encroachment by hutments along the alignment; and the projects ‘Extension of MRTS from Velachery to Stn. Thomas, MTP, MRTP’ and ‘Bandel-Naihati New Rail Bridge in Replacement of Jubilee Bridge No.8, ER’ have reported additional delays of 12 months each (however, no specific reasons have been reported by the project authorities for the delay in these projects).

ix) In the **Power Sector**, out of 102 projects, 53 projects are delayed. During the month 9 projects have reported additional delays in the range of 2-12 months, out of which 4 are Mega projects. The project ‘Transmission System for Establishment of 400/220 KV GIS Sub Station at Kala in UT DNH, PGCIL’ , ‘System Strengthening XIII of SR Grid, PGCIL’ and ‘Transmission System for Connectivity of Essar Power Gujarat Limited, PGCIL’ have reported additional delays of 2, 3 and 4 months respectively due to ROW problems; the project ‘Teesta Low Dam HEP, Stage-IV, NHPC’ has reported additional delay of 3 months due to contractual issue; the project ‘Barh STPP Stage –II, NTPC’ has reported additional delay of 5 months due to delay in supply of equipments; the project ‘Koldam HEP, NTPC’ has reported additional delay of 8 months due to seepage in main dam; the project ‘Tuirial Hydro Electric Project (60MW), NEEPCO’ has reported additional delay of 10 months due to legal issues; the project ‘Pare Hydro Electric Project, NEEPCO’ has reported additional delay of 12 months due to change in geotechnical parameter; and the project ‘Tripura Gas Based Power Project, NEEPCO’ has reported additional delay of 6 months (however, no specific reasons have been reported by the project authority for the delay in this project).

x) In the **Petroleum Sector**, out of 82 projects, 53 projects are delayed. During the month 13 projects have reported additional delays in the range of 1-12 months, out of which 6 are Mega projects. The projects ‘Paradip Refinery Project IOCL’ , ‘Hydrocracker Revamp and Setting up a New CCR at Mumbai Refinery,

BPCL' and 'Gas Turbine Generation Set, OIL' have reported additional delays of 3 months each due to delay in environmental clearance, delay in completion of construction work and delay in supply of materials respectively; the project 'Diesel Hydrotreater Project at Visakh Refinery, HPCL' has reported additional delay of 1 month; the projects 'MRPL Phase-III Expansion Mangalore Refinery' and '102 MW Wind Power Project, ONGC' have reported additional delays of 2 months each; the projects 'Development Of SB-14 Field, ONGC' and 'Replacement of CDU/VDU at Mumbai Refinery, BPCL' have reported additional delays of 3 months each; the projects 'Development of G1 and GS-15, ONGC' and 'Construction of 23 Immediate Supply Vessels (ISV), ONGC' have reported additional delays of 4 and 6 months respectively; the projects 'Construction of One ETP at GGS-NADA, Ankleshwar, ONGC' and 'Construction of 6 ETPS, ONGC' have reported additional delays of 8 and 9 months respectively; and the project 'Construction of Three ETPS, Mehsana, ONGC' has reported additional delay of 12 months (however, no specific reasons have been reported by the project authorities for the delay in these projects).


10. The status as on 31.01.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	284	4
2	ROAD TRANSPORT AND HIGHWAYS	132	2
3	POWER	102	9
4	PETROLEUM	82	13
5	COAL	55	3
6	STEEL	20	1
7	SHIPPING AND PORTS	19	1
8	TELECOMMUNICATIONS	10	3
9	CIVIL AVIATION	8	1
10	ATOMIC ENERGY	4	1
11	URBAN DEVELOPMENT	4	0
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	722	38

Sectoral break up of on-going infrastructure projects.

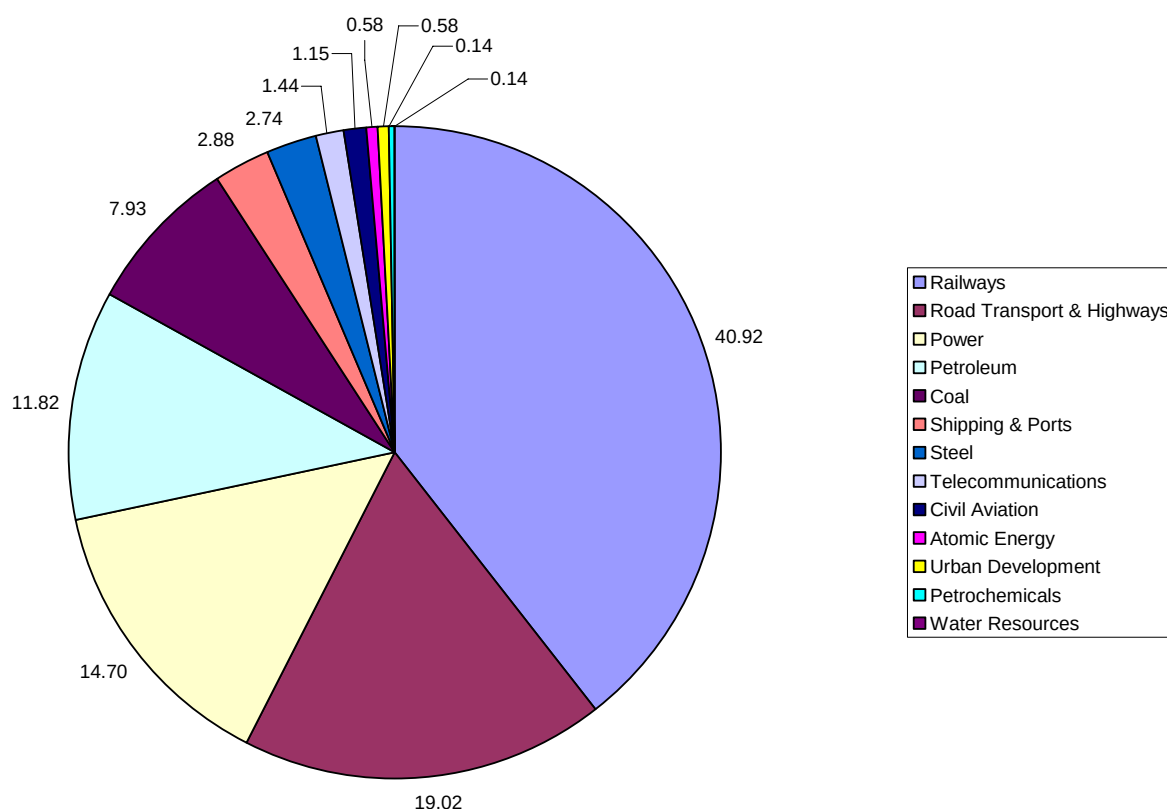

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>POWER</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>RAILWAYS</u>			
2	RENIGUNTA-GUNTAKAL(RE) (RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL) (RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>FERTILISERS</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT (NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>POWER</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-II (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>RAILWAYS</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) (RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE (RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>PETROLEUM</u>			
10	NORTH TAPTI GAS FIELD DEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53
12	CHUTAK HYDRO-ELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93
	August,2013			
13	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND BANGLADESH -INDIAN PORTION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000089]	160.32	10/2012	87.63
	<u>RAILWAYS</u>			
14	MADURAI-RAMESWARAM-GC (SOUTHERN RAILWAY) - [N22000200]	240.00	-	367.21
15	KRISHNANAGAR-BETHUA DAHRI DOUBLING (EASTERN RAILWAYS) - [N22000226]	151.65	03/2015	90.21
16	DHARMAVARAM-PAKALA GC (SAUTH COST RAILWAY) - [N22000284]	294.99	-	658.53
	September,2013			
	<u>PETROLEUM</u>			
17	BUTADIENE EXTRACTION UNIT(BDEU) AT PANIPAT (INDIAN OIL CORPORATION LIMITED) - [N16000108]	341.50	02/2013	198.81
	<u>POWER</u>			
18	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000046]	7,031.88	12/2012	4591.9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
19	GWALIOR BYPASS, NH-75,3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000088]	300.93	10/2009	302.7
	October,2013			
	<u>POWER</u>			
20	NIMOO BAZGO HYDROELECTRIC PROJECT (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000006]	611.01	08/2010	883.85
21	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000018]	557.24	01/2010	648.43
	<u>RAILWAYS</u>			
22	CHANDIGARH-LUDHIANA(NEW BG LINE),NR (NORTHERN RAILWAY) - [220100241]	248.44	12/2012	972.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
23	RUPSA-BANGRIPOSI (GC)(SER) (SOUTH EASTERN RAILWAY) - [220100323]	57.94	03/1998	176.14
	<u>TELECOMMUNICATIONS</u>			
24	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 (MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000029]	231.38	10/2007	86.11
	November,2013			
	<u>RAILWAYS</u>			
25	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) (SOUTH WESTERN RAILWAY) - [220100190]	157.00	03/2012	330.38
	December,2013			
	<u>PETROLEUM</u>			
26	RESITMENT OF MARKETING INSTALATION AT VISAKH (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000057]	756.00	-	913.72
27	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000066]	224.00	-	312.61
28	FLUIDIZED CATALYTIC CRACKING UNIT(FCCU) REVAMP AT MATHURA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000107]	1,000.00	01/2013	755.25
29	CAPACITY AUGMENTATION OF KOTA PIYALA SECTION OF MMBPL PIPELINE (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000153]	152.89	06/2013	128.53
	<u>RAILWAYS</u>			
30	KOLAR-CHICKBALAPUR GC (SOUTH WESTERN RAILWAY) - [N22000275]	287.99	01/1999	434.57
	January,2014			
	<u>PETROLEUM</u>			
31	ADDITIONAL GAS PROCESSING UNITS AT URAN (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000064]	1,797.35	12/2011	841.98
	<u>POWER</u>			
32	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000079]	1,075.12	05/2012	N.A.
33	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000092]	1,719.52	08/2013	N.A.
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
34	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101132]	241.00	08/2004	67.03
35	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101133]	318.00	08/2004	71.35
36	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101153]	225.00	04/2004	109.99
37	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106205]	220.00	09/2007	282.7
38	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106237]	284.00	05/2008	350.7
39	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106243]	240.00	10/2008	295.51
40	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106260]	190.00	01/2009	264.65
41	NEW MANGALORE PORT NH-17 AND 48 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000040]	196.50	06/2011	290.98
42	NAGPUR-KONDHALI,NH-6(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000055]	168.00	12/2008	457.3
43	THANJAUR-TRICHY,NH-67(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000056]	280.00	06/2009	581.5
44	GANJAM-ICCHAPURUM,NH-5(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000057]	263.27	02/2004	263.96
45	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000094]	407.60	06/2010	186.77
46	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000095]	263.17	09/2009	235.19
47	JHANSI TO LALITPUR, NH-25,26 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000096]	355.06	09/2009	507.99
48	TRICHY - KORUR NH-67 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000101]	516.00	07/2010	866.86
49	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000102]	941.00	01/2011	1901
50	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000116]	228.70	02/2004	182.07
51	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000124]	1,170.52	06/2011	4.41
52	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000130]	1,673.70	10/2011	2866.54
53	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000131]	1,693.75	08/2011	2760.82

Projects Added / Completed / Dropped / Frozen

No of Projects in previous month	741
No of Projects Completed/Dropped/Frozen in current month	23
No of Projects not reported in current month	1
No of Projects added in current month	5
No of Projects in current month	722

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	229	3	136	23	331	722	31.72
Latest Approved (Date)	204	3	161	23	331	722	28.25

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	562	7,79,958.94	8,37,375.20	3,73,389.38	44.60	57,416.26	7.40
Latest Approved (RCE)	160	1,82,737.59	2,43,364.05	1,40,599.59	57.80	60,626.46	33.20
Total (RCE)	722	9,62,696.53	10,80,739.25	5,13,988.97	47.56	118042.72	12.26
Original Cost of All Projects							
Original Cost	722	9,00,150.20	10,80,739.25	5,13,988.97	47.60	1,80,589.05	20.10

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	229	450,764.90	552,964.66	327,498.02	59.20	102,199.76	22.70
Latest Approved (RCE)	204	466,337.09	532,835.34	318,208.53	59.70	66,498.25	14.30

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	38	88,874.71	101,978.02	80,786.67	79.20	13,103.31	14.70


Summary of projects in the Flash Report for the month of January, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	741
Number of Projects completed/dropped/frozen in Current Month	23
Number of Projects not Reported in Current Month	1
Number of Projects Added in Current Month	5
Number of Projects in Current Month	722


Brief Analysis

Project Status with respect to Original Schedule: Out of 722 projects, 3 projects are ahead of schedule, 136 projects are on schedule and 229 projects are delayed. Of the balance, 331 projects do not have fixed dates of commissioning while 23 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

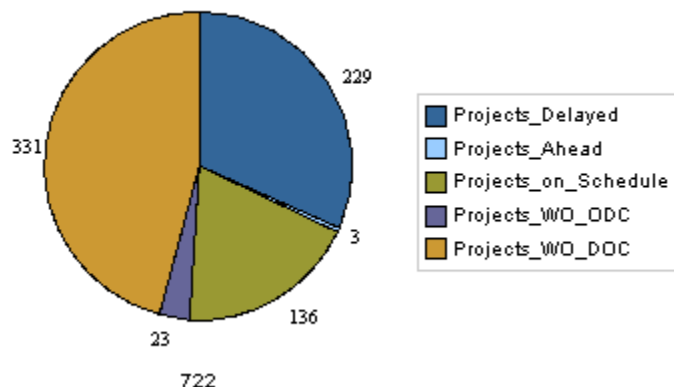

Investment Scenario

The Total Original cost of implementation of 722 projects when sanctioned, was of the order of Rs. 900150.2 crore but this was subsequently revised to Rs. 1080739.25 crore implying a cost overrun of 20.1%. The expenditure incurred on these projects till January, 2014 is Rs. 513988.97 crore, which is 47.6% of the revised cost of the projects.

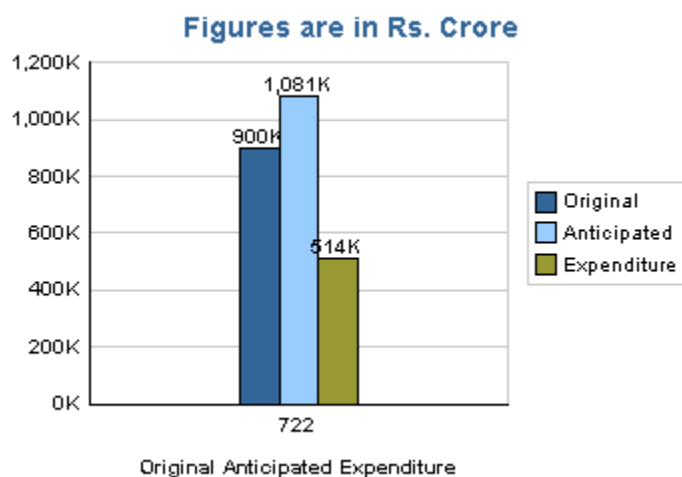

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	4,086.1	4,996.7	22.3
3	COAL	55	38,127.1	41,525.2	8.9	7	8,579.5	12,575.3	46.6
4	STEEL	20	65,959.3	72,162.3	9.4	7	24,238.0	30,471.0	25.7
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	82	181,913.1	197,623.8	8.6	24	58,765.5	79,786.2	35.8
7	POWER	102	248,230.6	265,932.3	7.1	17	48,595.4	66,297.1	36.4
8	RAILWAYS	284	148,717.5	265,448.1	78.5	150	64,474.5	181,299.2	181.2
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	13	3,680.5	5,821.2	58.2
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	9	8,629.0	11,187.6	29.7
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	4	47,588.2	52,861.1	11.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		722	900,150.2	1,080,739.3	20.1	239	251,618.1	438,751.8	74.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	47	37,177.3	45,353.9	22.0	14	12,772.4	21,816.0	70.8
2	ARUNACHAL PRADESH	4	9,512.2	16,857.3	77.2	4	9,512.2	16,857.3	77.2
3	ASSAM	41	24,155.5	39,221.8	62.4	21	12,677.8	27,830.4	119.5
4	BIHAR	45	32,339.0	40,760.0	26.0	17	13,347.2	21,784.5	63.2
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	33	38,022.7	39,924.3	5.0	8	3,415.2	5,628.7	64.8
7	HARYANA	9	4,399.9	6,104.1	38.7	2	1,298.8	3,028.0	133.1
8	HIMACHAL PRADESH	5	13,845.2	19,510.6	40.9	4	11,798.2	17,463.6	48.0
9	JAMMU AND KASHMIR	8	13,694.7	32,976.6	140.8	4	6,634.2	25,916.1	290.6
10	KARNATAKA	34	53,120.5	65,228.5	22.8	14	11,651.4	24,097.7	106.8
11	KERALA	12	22,610.7	25,135.4	11.2	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	5	3,317.9	4,963.7	49.6
13	MAHARASHTRA	53	94,835.2	109,387.7	15.3	19	33,512.3	49,648.1	48.1
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	29	55,889.0	62,601.1	12.0	12	32,775.6	39,487.6	20.5
19	PUNJAB	4	1,680.2	1,680.2	0.0	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	6	2,489.1	3,400.6	36.6
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	38	51,742.7	67,974.4	31.4	20	30,997.2	47,228.9	52.4
23	TRIPURA	6	2,966.3	4,737.3	59.7	3	2,129.4	3,934.7	84.8
24	UTTAR PRADESH	28	21,357.8	25,954.0	21.5	11	4,111.1	8,755.6	113.0
25	WEST BENGAL	36	49,851.1	61,412.4	23.2	15	22,672.9	34,234.2	51.0
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,533.9	41,531.3	-0.0	0	0.0	0.0	0.0
28	CHHATISGARH	22	56,368.8	57,453.4	1.9	5	1,396.8	2,481.4	77.6
29	JHARKHAND	27	16,118.8	20,384.1	26.5	8	2,534.9	6,971.9	175.0
30	UTTARAKHAND	6	7,844.0	9,331.5	19.0	3	2,860.6	4,348.0	52.0
31	MULTI STATE	175	180,260.6	204,015.6	13.2	34	20,360.6	46,269.7	127.3
Total		722	900,150.2	1,080,739.3	20.1	239	251,618.1	438,751.8	74.4

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 73
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 50
3	COAL	55	38,127.1	41,525.2	8.9	29	25,052.8	28,822.2	12 - 72
4	STEEL	20	65,959.3	72,162.3	9.4	13	64,208.3	70,162.3	10 - 66
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	82	181,913.1	197,623.8	8.6	57	143,281.2	160,093.5	1 - 120
7	POWER	102	248,230.6	265,932.3	7.1	55	133,968.0	150,327.6	1 - 113
8	RAILWAYS	284	148,717.5	265,448.1	78.5	38	28,661.1	80,279.6	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	21	6,793.7	7,637.5	2 - 82
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	4	2,856.3	3,535.8	2 - 99
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	34 - 62
12	URBAN DEVELOPMENT	4	47,588.2	52,861.1	11.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		722	900,150.2	1,080,739.3	20.1	229	450,764.9	552,964.7	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	47	37,177.3	45,353.9	22.0	9	14,967.8	19,374.4	24 - 66
2	ARUNACHAL PRADESH	4	9,512.2	16,857.3	77.2	3	9,356.2	16,449.3	25 - 93
3	ASSAM	41	24,155.5	39,221.8	62.4	30	16,066.3	26,680.7	3 - 120
4	BIHAR	45	32,339.0	40,760.0	26.0	5	17,679.5	22,340.7	18 - 98
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	21 - 21
6	GUJARAT	33	38,022.7	39,924.3	5.0	9	20,963.1	20,901.8	4 - 27
7	HARYANA	9	4,399.9	6,104.1	38.7	3	1,417.1	1,417.1	2 - 50
8	HIMACHAL PRADESH	5	13,845.2	19,510.6	40.9	4	12,798.3	16,543.6	29 - 106
9	JAMMU AND KASHMIR	8	13,694.7	32,976.6	140.8	3	6,468.0	25,723.0	10 - 181
10	KARNATAKA	34	53,120.5	65,228.5	22.8	7	17,259.3	17,503.3	10 - 48
11	KERALA	12	22,610.7	25,135.4	11.2	3	15,900.0	16,600.0	5 - 45
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	3	1,372.1	1,484.9	6 - 69
13	MAHARASHTRA	53	94,835.2	109,387.7	15.3	21	42,101.8	50,779.8	2 - 129
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	108 - 108
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	MIZORAM	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	35 - 113
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	24 - 24
18	ODISHA	29	55,889.0	62,601.1	12.0	14	48,830.8	52,183.6	3 - 143
19	PUNJAB	4	1,680.2	1,680.2	0.0	0	0.0	0.0	-
20	RAJASTHAN	25	25,380.5	25,805.9	1.7	2	13,426.0	12,998.0	3 - 23
21	SIKKIM	2	1,648.9	3,684.9	123.5	2	1,648.9	3,684.9	15 - 50
22	TAMIL NADU	38	51,742.7	67,974.4	31.4	7	30,151.2	39,580.2	21 - 99
23	TRIPURA	6	2,966.3	4,737.3	59.7	4	2,417.4	4,188.4	16 - 120
24	UTTAR PRADESH	28	21,357.8	25,954.0	21.5	7	4,312.0	6,902.6	10 - 84
25	WEST BENGAL	36	49,851.1	61,412.4	23.2	12	28,559.0	33,585.0	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,533.9	41,531.3	-0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	22	56,368.8	57,453.4	1.9	12	38,130.8	38,442.1	5 - 33
29	JHARKHAND	27	16,118.8	20,384.1	26.5	10	8,991.6	9,501.1	10 - 126
30	UTTARAKHAND	6	7,844.0	9,331.5	19.0	4	6,097.2	7,360.3	5 - 57
31	MULTI STATE	175	180,260.6	204,015.6	13.2	49	85,910.4	94,107.6	1 - 240
Total		722	900,150.2	1,080,739.3	20.1	229	450,764.9	552,964.7	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 73
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 50
3	COAL	55	38,127.1	41,525.2	8.9	29	25,052.8	28,822.2	12 - 72
4	STEEL	20	65,959.3	72,162.3	9.4	10	62,441.9	68,084.6	10 - 66
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	82	181,913.1	197,623.8	8.6	53	138,443.2	150,268.7	1 - 98
7	POWER	102	248,230.6	265,932.3	7.1	53	132,480.4	148,285.6	1 - 106
8	RAILWAYS	284	148,717.5	265,448.1	78.5	37	28,336.1	79,163.1	3 - 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.2	98,553.2	2.2	8	3,343.0	3,681.1	2 - 80
10	SHIPPING AND PORTS	19	15,617.1	17,871.5	14.4	2	2,194.5	2,423.9	2 - 51
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	34 - 62
12	URBAN DEVELOPMENT	4	47,588.2	52,861.1	11.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		722	900,150.2	1,080,739.3	20.1	204	438,235.3	532,835.3	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,946.0	4.8	2	2,660.6	2,981.7	12.1
3	COAL	55	41,499.6	41,525.2	0.1	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,162.3	2.8	2	14,680.1	16,662.9	13.5
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	82	196,535.8	197,623.8	0.6	11	33,581.4	38,023.2	13.2
7	POWER	102	252,168.7	265,932.3	5.5	12	40,165.5	53,929.1	34.3
8	RAILWAYS	284	181,680.3	265,448.1	46.1	117	65,493.8	149,315.8	128.0
9	ROAD TRANSPORT AND HIGHWAYS	132	97,317.9	98,553.2	1.3	5	1,969.8	3,229.7	64.0
10	SHIPPING AND PORTS	19	17,488.0	17,871.5	2.2	5	3,157.6	3,783.5	19.8
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	4	47,647.1	52,861.1	10.9	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		722	962,696.5	1,080,739.3	12.3	166	193,596.1	315,786.9	63.1

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	0	0.00	0.00	0- 0
3	COAL	55	38,127.05	41,525.17	8.91	0	0.00	0.00	0- 0
4	STEEL	20	65,959.26	72,162.25	9.40	1	295.89	607.17	33- 33
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	82	181,913.11	197,623.79	8.64	2	3,631.12	8,313.05	20- 120
7	POWER	102	248,230.58	265,932.27	7.13	1	1,657.00	2,978.86	79- 79
8	RAILWAYS	284	148,717.49	265,448.07	78.49	0	0.00	0.00	0- 0
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	98,553.16	2.19	5	940.10	1,445.92	65- 73
10	SHIPPING AND PORTS	19	15,617.12	17,871.52	14.44	1	150.00	600.00	99- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	4	47,588.18	52,861.08	11.08	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		722	900150.2	1080739.25	20.06	10	6674.11	13945	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 73
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	335.61	388.53	21- 21
3	COAL	55	38,127.05	41,525.17	8.91	5	7,938.86	11,886.62	24- 57
4	STEEL	20	65,959.26	72,162.25	9.40	4	23,538.89	29,522.85	30- 66
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	82	181,913.11	197,623.79	8.64	20	55,566.37	75,789.89	3- 120
7	POWER	102	248,230.58	265,932.27	7.13	14	40,760.37	57,119.96	10- 106
8	RAILWAYS	284	148,717.49	265,448.07	78.49	34	23,261.74	74,880.23	9- 240
9	ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	98,553.16	2.19	8	1,628.10	2,471.98	57- 80
10	SHIPPING AND PORTS	19	15,617.12	17,871.52	14.44	3	2,344.46	3,023.92	2- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	1	149.15	158.72	57- 57
12	URBAN DEVELOPMENT	4	47,588.18	52,861.08	11.08	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		722	900150.2	1080739.25	20.06	92	172186.55	278189.7	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	ADDITIONAL GAS PROCESSING UNITS AT URAN	10/2008	1,797.35	12/2011	977.00	12/2013	841.98
	<u>POWER</u>						
2	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID - PART-III	11/2009	1,075.12	05/2012	1,075.12	12/2013	.00
3	ESTABLISHMENT OF POOLING STATIONS AT RAJGARH AND RAIPUR FOR IPP GENERATION PROJECTS IN CHATTISGARH	12/2010	1,719.52	08/2013	1,719.52	12/2013	.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	04/2000	241.00	08/2004	196.65	10/2013	67.03
5	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	04/2000	318.00	08/2004	207.56	N.A.	71.35
6	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	04/2000	225.00	04/2004	241.53	10/2013	109.99
7	NAGPUR-KONDHALI,NH-6(NHAI)	03/2005	168.00	12/2008	168.00	N.A.	457.30
8	GANJAM-ICCHAPURUM,NH-5(NHAI)	04/2000	263.27	02/2004	263.27	N.A.	263.96
9	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	12/2003	263.17	09/2009	263.17	N.A.	235.19
10	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1,693.75	08/2011	1,693.75	N.A.	2,760.82
11	GURGAON-KOTPUTLI KM 42.70 TO 54.4 KM	04/2009	1,673.70	10/2011	1,673.70	N.A.	2,866.54
12	FOUR LANNING FROM MP/MAHARASHTRA BORDER TO NAGPUR, NAGPUR BYPASS	04/2010	1,170.52	06/2011	1,170.52	12/2013	4.41
13	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5	04/2000	228.70	02/2004	228.70	N.A.	182.07
14	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	03/2005	941.00	01/2011	941.00	09/2013	1,901.00
15	TRICHY - KORUR NH-67	03/2005	516.00	07/2010	516.00	N.A.	866.86
16	JHANSI TO LALITPUR, NH-25,26	12/2003	355.06	09/2009	355.06	N.A.	507.99
17	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7	12/2003	407.60	06/2010	407.60	N.A.	186.77
18	THANJAUR-TRICHY,NH-67(NHAI)	03/2005	280.00	06/2009	280.00	N.A.	581.50
19	NEW MANGALORE PORT NH-17 AND 48	04/2000	196.50	06/2011	196.50	N.A.	290.98
20	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	03/2005	220.00	09/2007	220.00	11/2013	282.70

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
21	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	12/2003	284.00	05/2008	359.00	N.A.	350.70
22	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	12/2003	240.00	10/2008	240.00	N.A.	295.51
23	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	03/2005	190.00	01/2009	190.00	N.A.	264.65

List of projects added						(All Cost in Rs. crore)
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	LPG TERMINAL AT KOCHI	12/2012	607.06	1/2016	607.06	1/2016
	<u>POWER</u>					
2	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	539.82	6/2016	539.82	6/2016
3	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	2/2014	908.08	6/2016	908.08	6/2016
4	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII	2/2014	243.53	8/2014	243.53	8/2014
5	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS	2/2014	167.40	12/2015	167.40	12/2015

Milestones (Cumulative due & achieved)		
Total	3690	
Achieved up to month	1399	


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	06/2014	01/2015	7
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) AAI	335.61	388.53	05/2012	11/2013	02/2014	3
	<u>COAL</u>						
3	ADRIYALA SHAFT PROJECT SCCL	212.34	1,228.39	03/2013	10/2014	03/2015	5
4	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
5	ANANTA OC EXPANSION PH-III (15.0 MTY) MCL	207.28	207.28	03/2012	03/2014	03/2016	24
	<u>STEEL</u>						
6	AUGMENTATION OF IRON ORE STORAGE IN RMHP RINL	480.00	450.00	09/2009	06/2014	07/2014	1
	<u>PETROLEUM</u>						
7	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	02/2014	03/2014	1
8	MRPL PHASE-III EXPANSION MANGALORE REFIN	12,412.00	12,160.26	01/2012	01/2014	03/2014	2
9	102 MW WIND POWER PROJECT ONGC	1,106.00	678.02	06/2012	03/2014	05/2014	2
10	PARADIP REFINERY PROJECT IOCL	29,777.00	32,710.00	11/2012	09/2014	12/2014	3
11	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY BPCL	825.00	1,827.00	04/2013	12/2013	03/2014	3
12	DEVELOPMENT OF SB-14 FIELD ONGC	410.44	410.44	11/2012	02/2014	05/2014	3
13	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY BPCL	1,419.00	1,419.00	12/2014	12/2014	03/2015	3
14	GAS TURBINE GENERATION SET OIL	216.88	216.88	10/2011	12/2013	03/2014	3
15	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	02/2014	06/2014	4

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) ONGC	331.20	269.10	08/2013	03/2014	09/2014	6
17	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR ONGC	200.69	200.69	07/2014	07/2014	03/2015	8
18	CONSTRUCTION OF 6 ETPS ONGC	302.26	240.95	09/2012	03/2014	12/2014	9
19	CONSTRUCTION OF THREE ETPS, MEHSANA ONGC	260.74	260.74	11/2014	11/2014	11/2015	12
	<u>POWER</u>						
20	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH PGCIL	181.93	181.93	07/2013	01/2014	03/2014	2
21	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	04/2015	07/2015	3
22	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	06/2014	09/2014	3
23	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED PGCIL	552.44	552.44	02/2014	02/2014	06/2014	4
24	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	09/2014	02/2015	5
25	TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	951.48	07/2013	05/2014	11/2014	6
26	KOLDAM HEP (NTPC) NTPC	4,527.15	6,414.56	04/2009	09/2014	05/2015	8
27	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) NEEPCO	913.63	913.63	07/2006	02/2015	12/2015	10
28	PARE HYDRO ELECTRIC PROJECT NEEPCO	573.99	1,128.38	08/2013	09/2014	09/2015	12
	<u>RAILWAYS</u>						
29	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	01/2014	02/2014	1
30	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRTD	495.74	495.74	06/2013	03/2014	03/2015	12
31	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) ER	207.52	207.52	12/2012	12/2013	12/2014	12
32	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
33	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHA	157.47	157.42	09/2007	12/2013	03/2014	3
34	PANIPAT-ROHTAK NHA	807.00	807.00	10/2014	12/2013	10/2014	10
	<u>SHIPPING AND PORTS</u>						
35	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY SHIPP.	966.46	994.82	02/2014	02/2014	04/2014	2
	<u>TELECOMMUNICATIONS</u>						
36	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL BSNL	149.15	158.72	06/2009	12/2013	03/2014	3
37	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	12/2013	03/2014	3
38	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II BSNL	1,148.19	964.37	05/2011	12/2013	03/2014	3
	38						

Graphical Presentation of All Projects w.r.t. Original Schedule

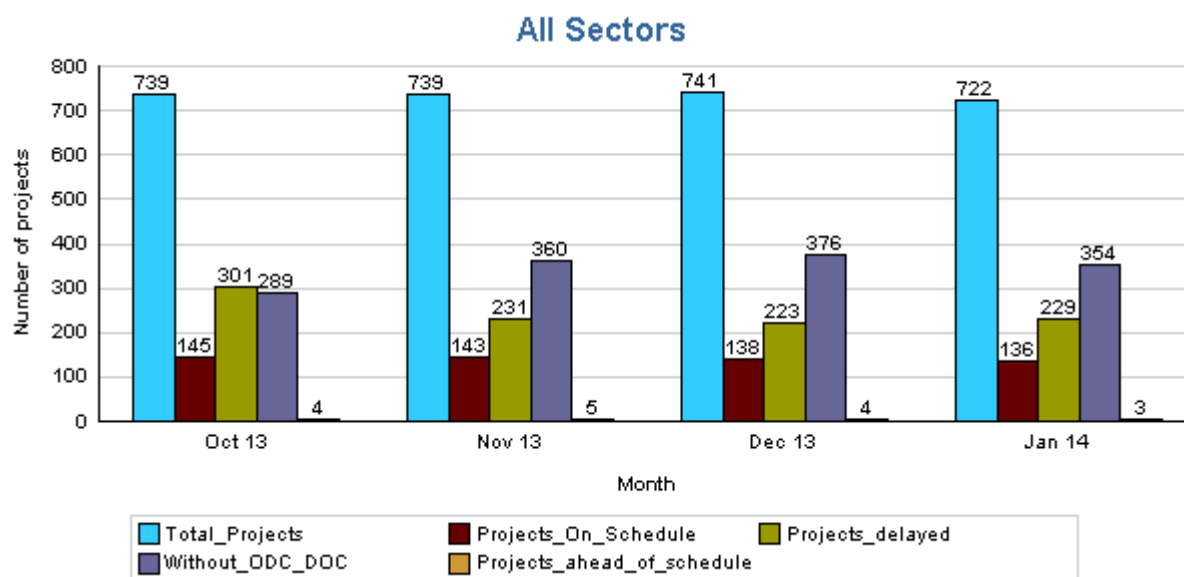


Break-up of 229 Delayed projects in January 2014

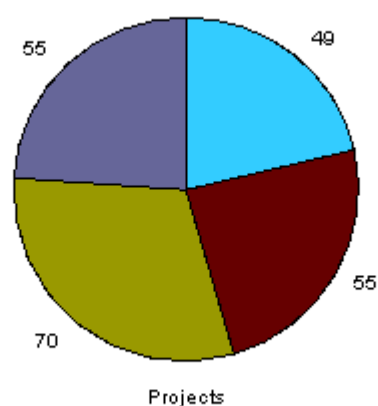


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Revised Schedule

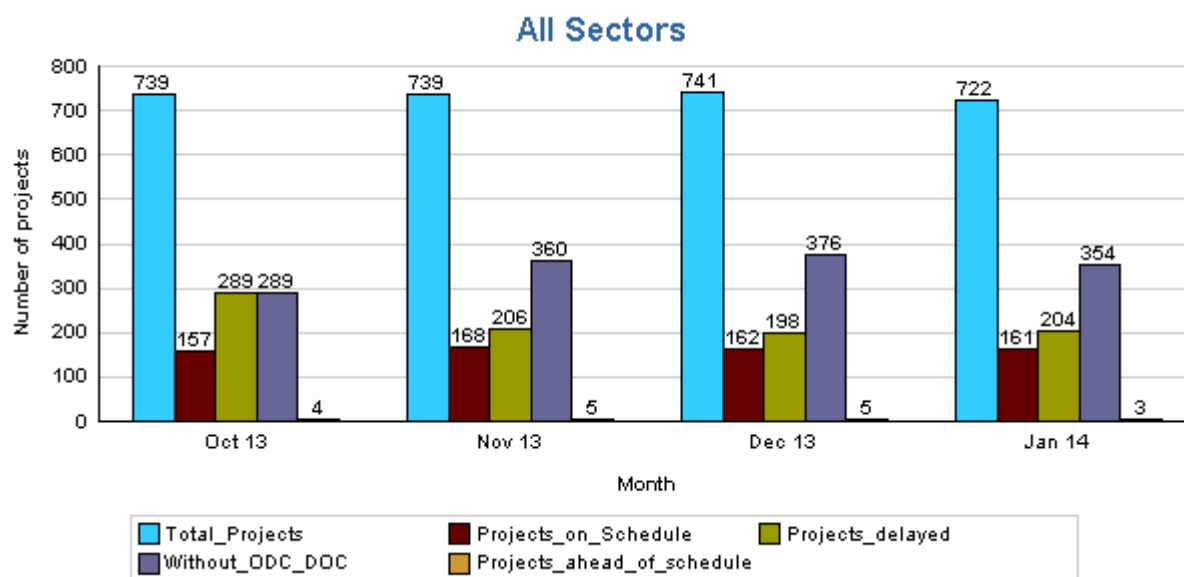


Break-up of 204 Delayed projects in January 2014

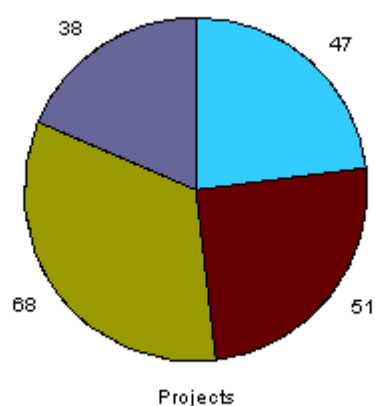


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

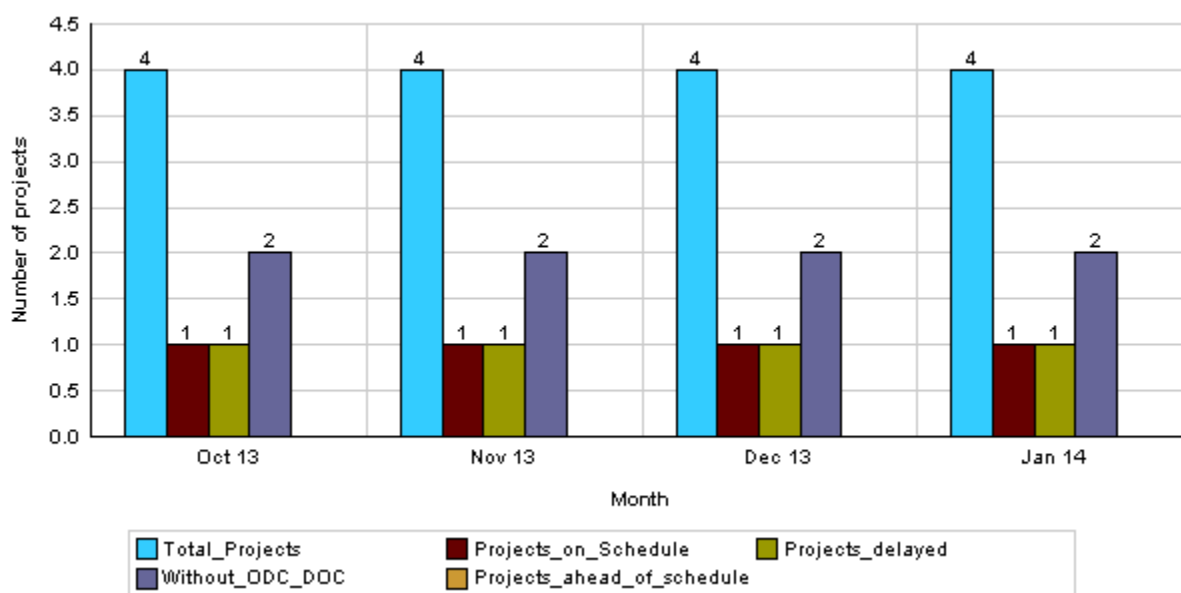


Break-up of 1 Delayed projects in January 2014




Delay in Months



Graphical Presentation of TELECOMMUNICATIONS Sector

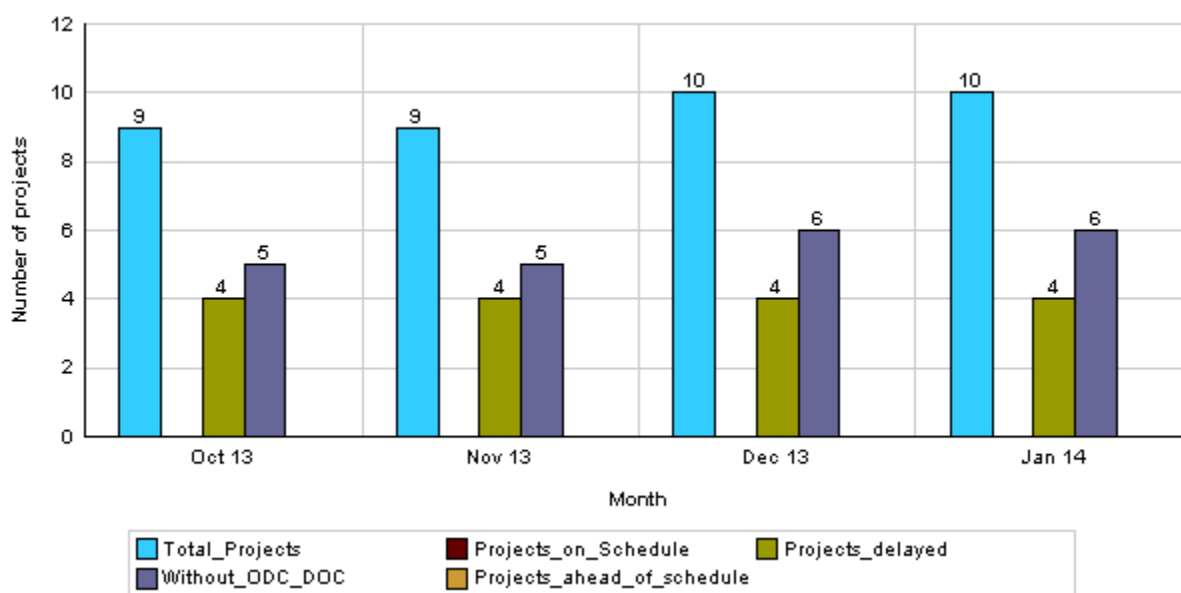


Break-up of 4 Delayed projects in January 2014

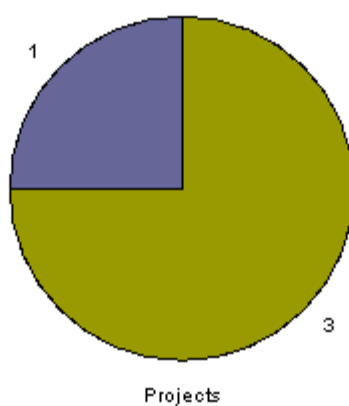


Delay in Months



Graphical Presentation of SHIPPING AND PORTS Sector

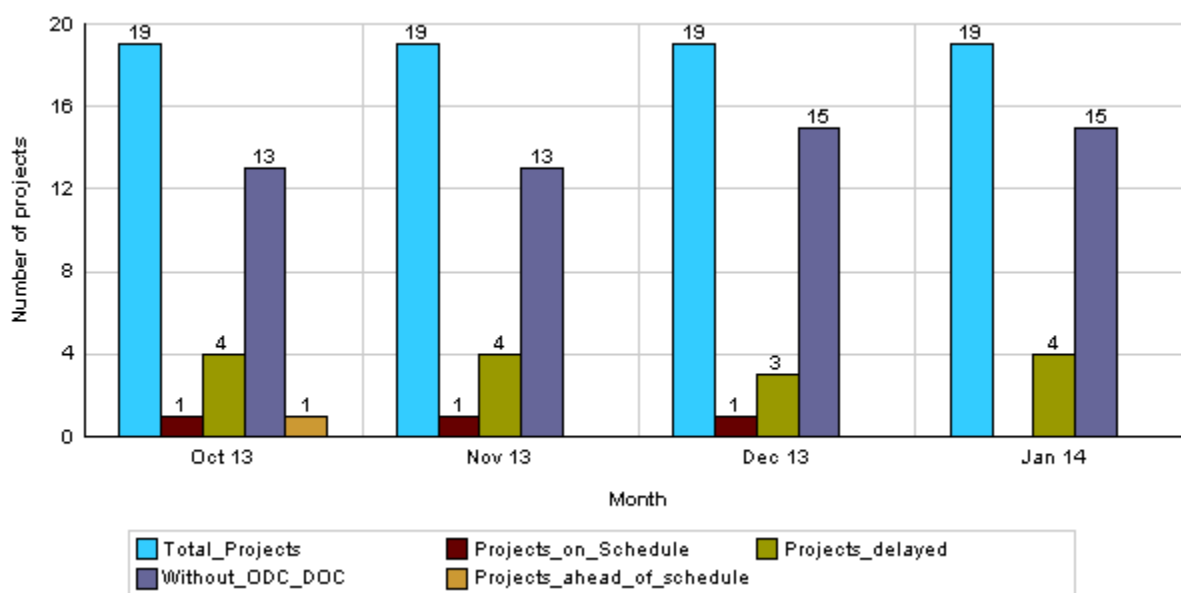


Break-up of 4 Delayed projects in January 2014

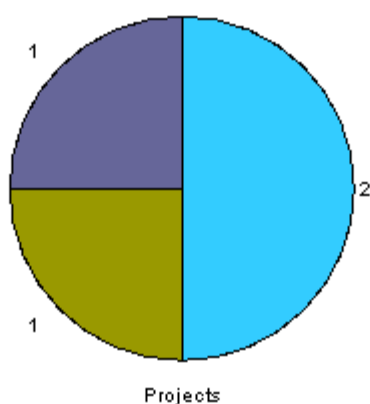


Delay in Months



Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

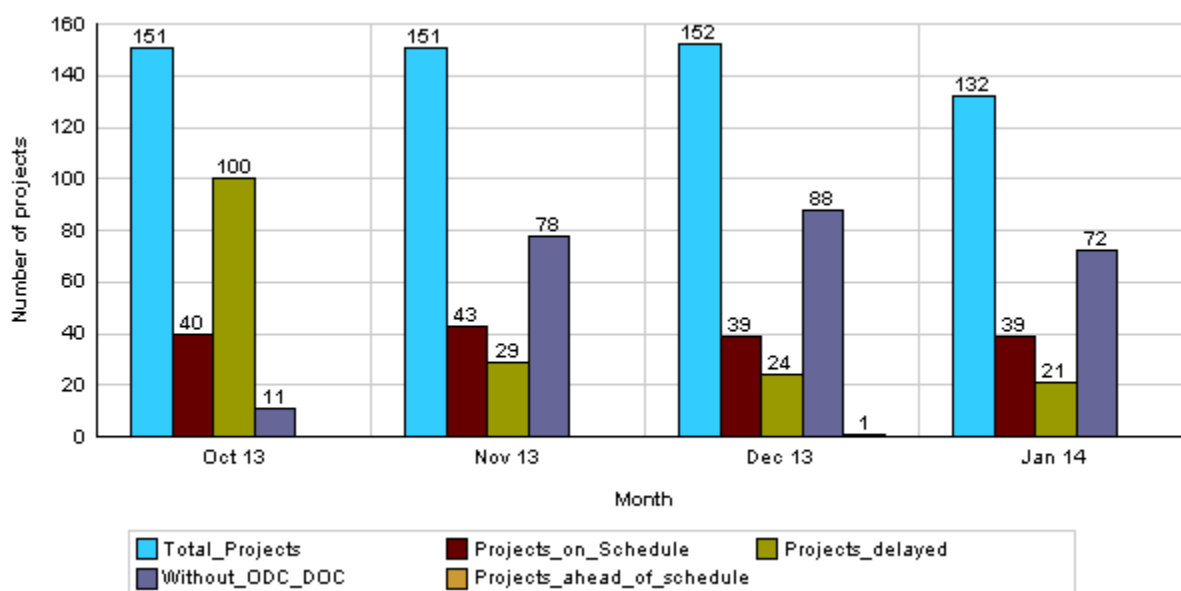


Break-up of 21 Delayed projects in January 2014

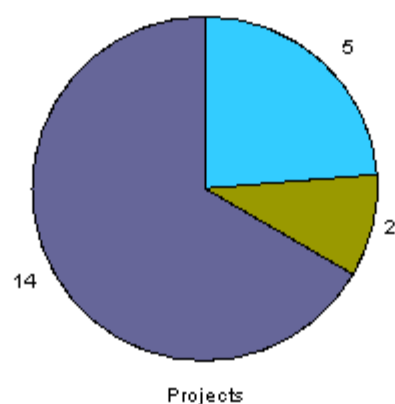


Delay in Months



Graphical Presentation of RAILWAYS Sector

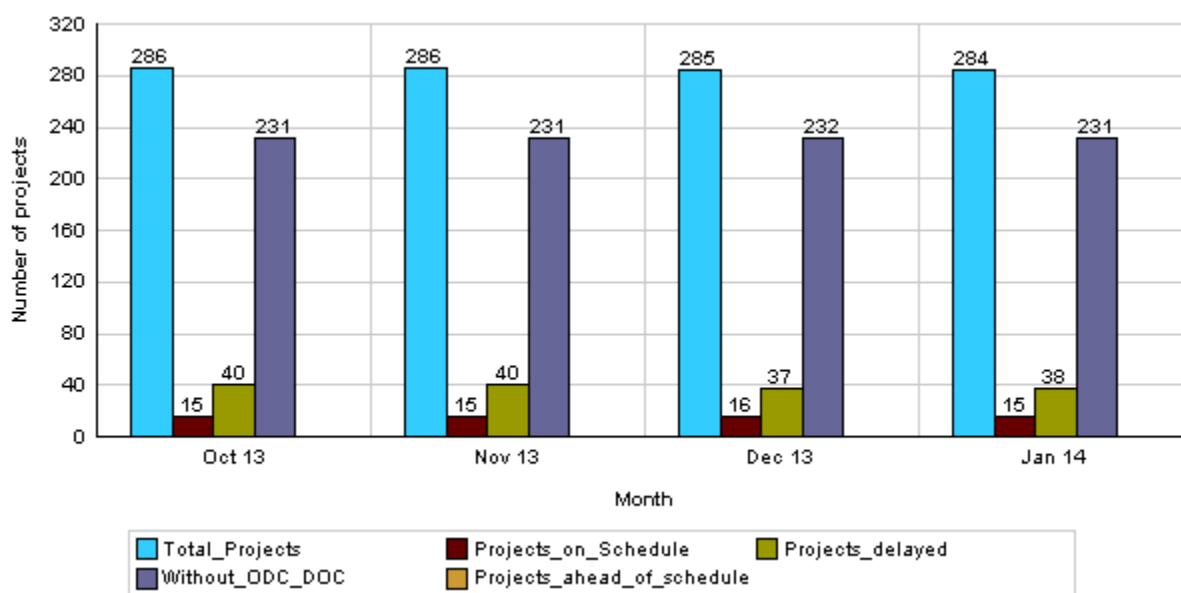


Break-up of 38 Delayed projects in January 2014

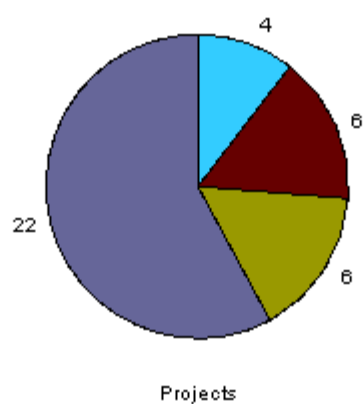


Delay in Months



Graphical Presentation of POWER Sector

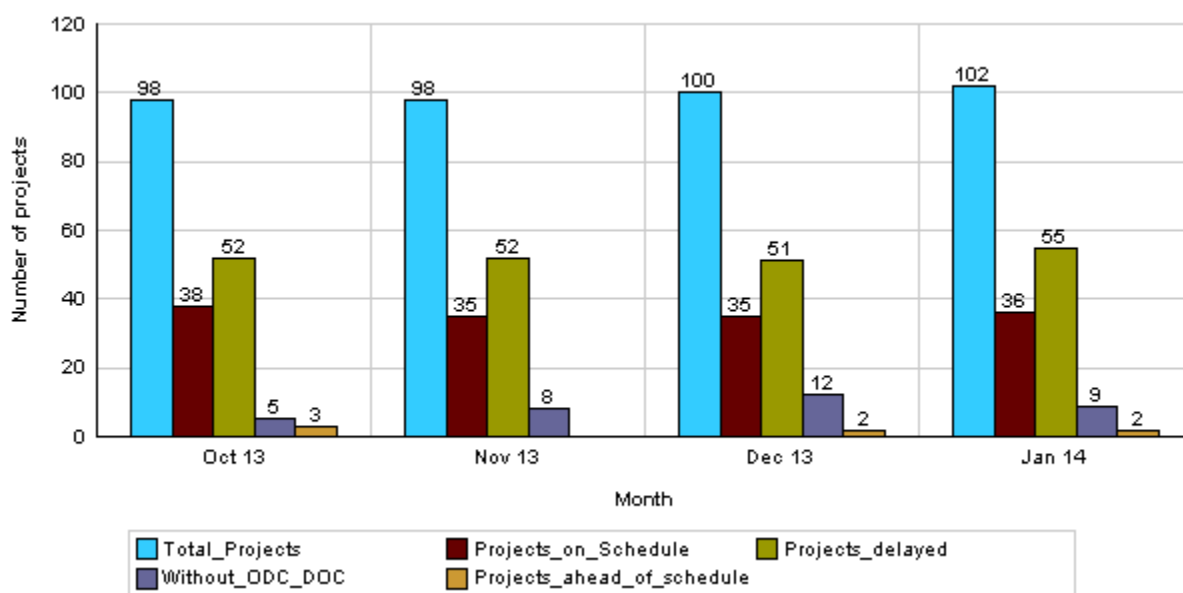


Break-up of 55 Delayed projects in January 2014

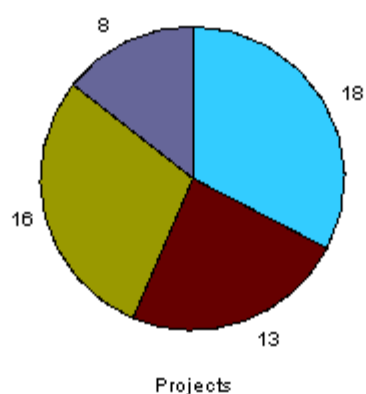


Delay in Months



Graphical Presentation of PETROLEUM Sector

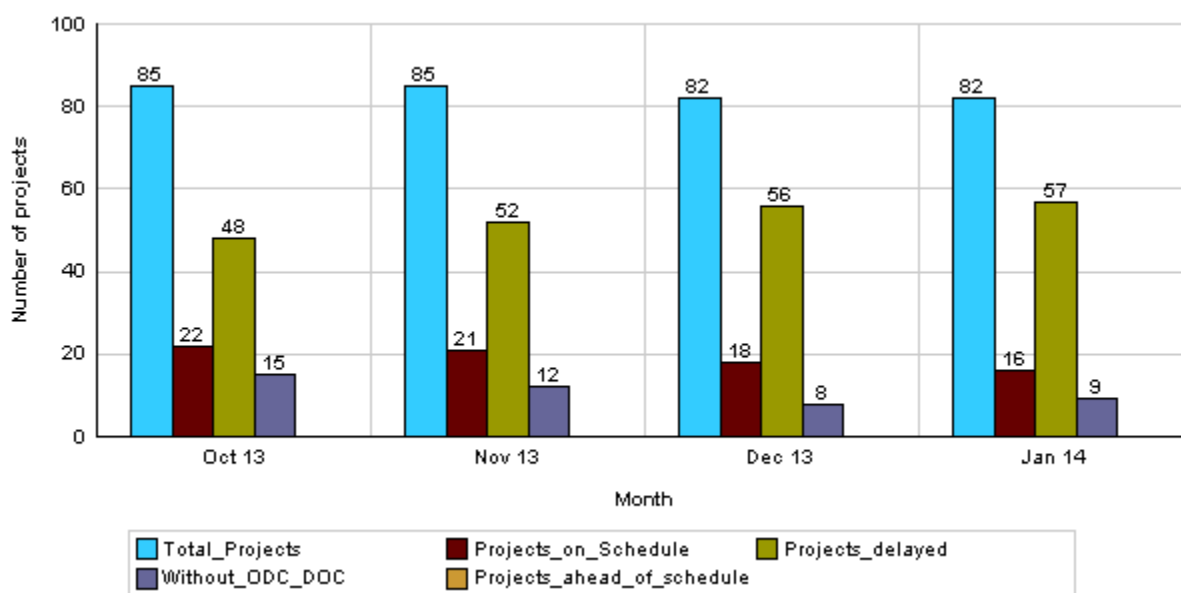


Break-up of 57 Delayed projects in January 2014

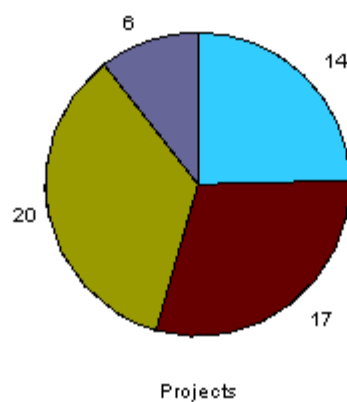


Delay in Months



Graphical Presentation of STEEL Sector

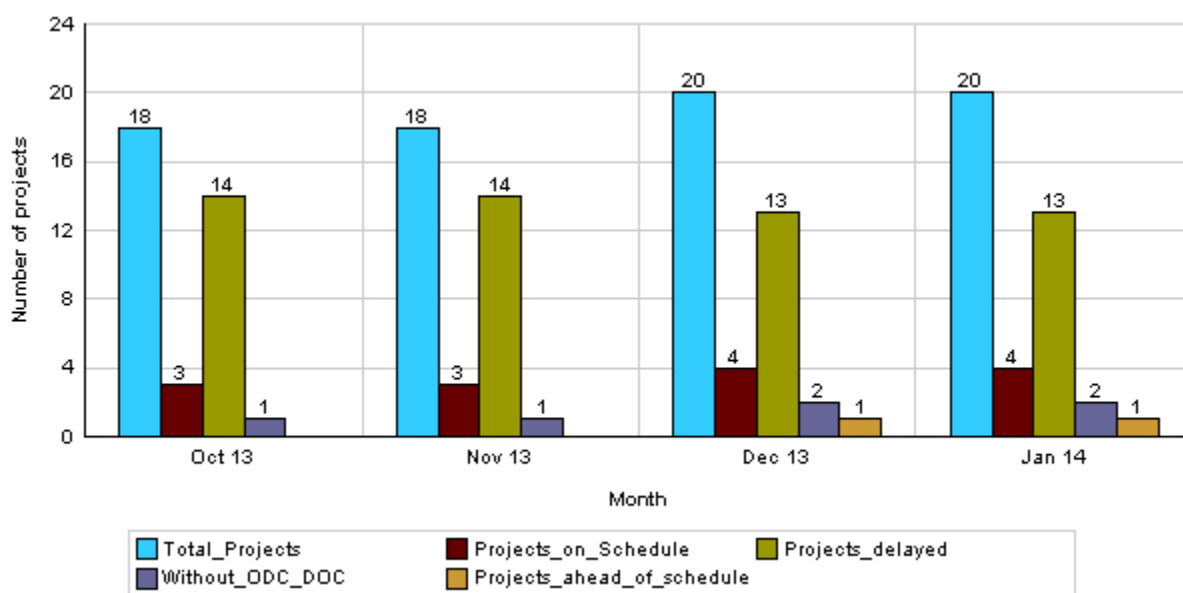


Break-up of 13 Delayed projects in January 2014

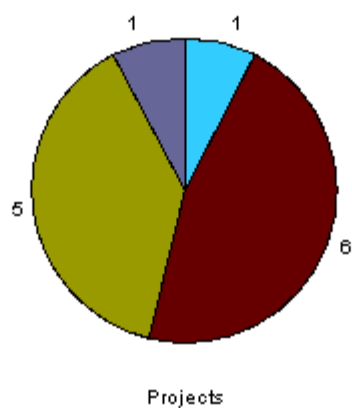


Delay in Months



Graphical Presentation of COAL Sector

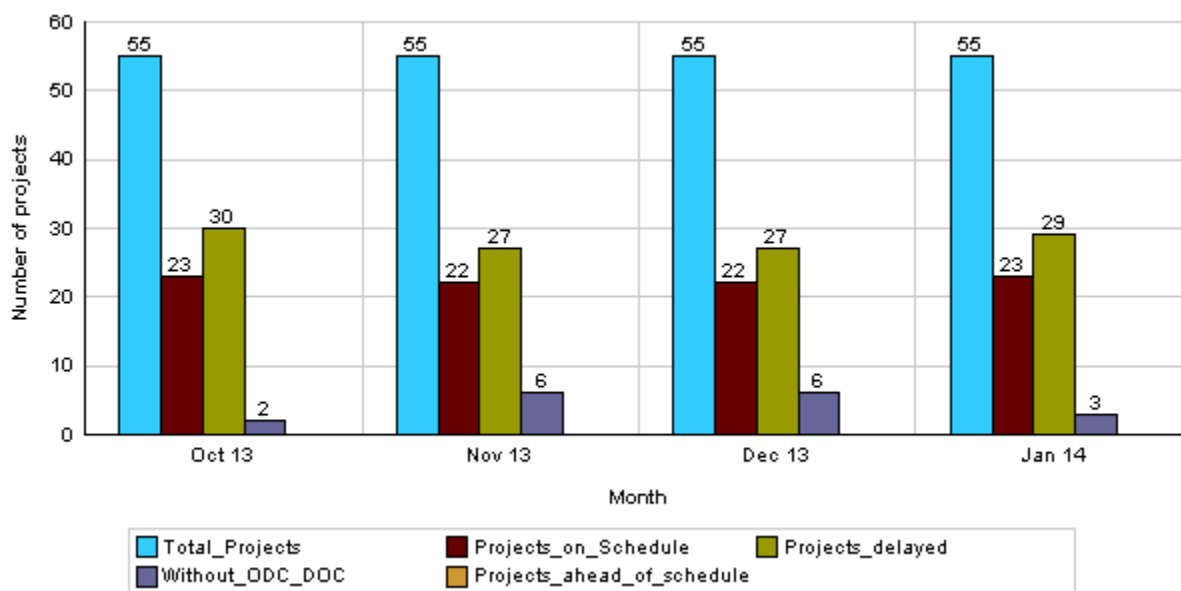


Break-up of 29 Delayed projects in January 2014

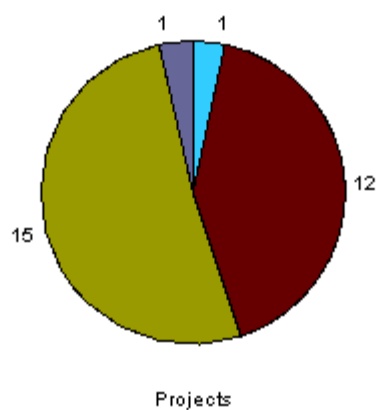


Delay in Months



Graphical Presentation of CIVIL AVIATION Sector

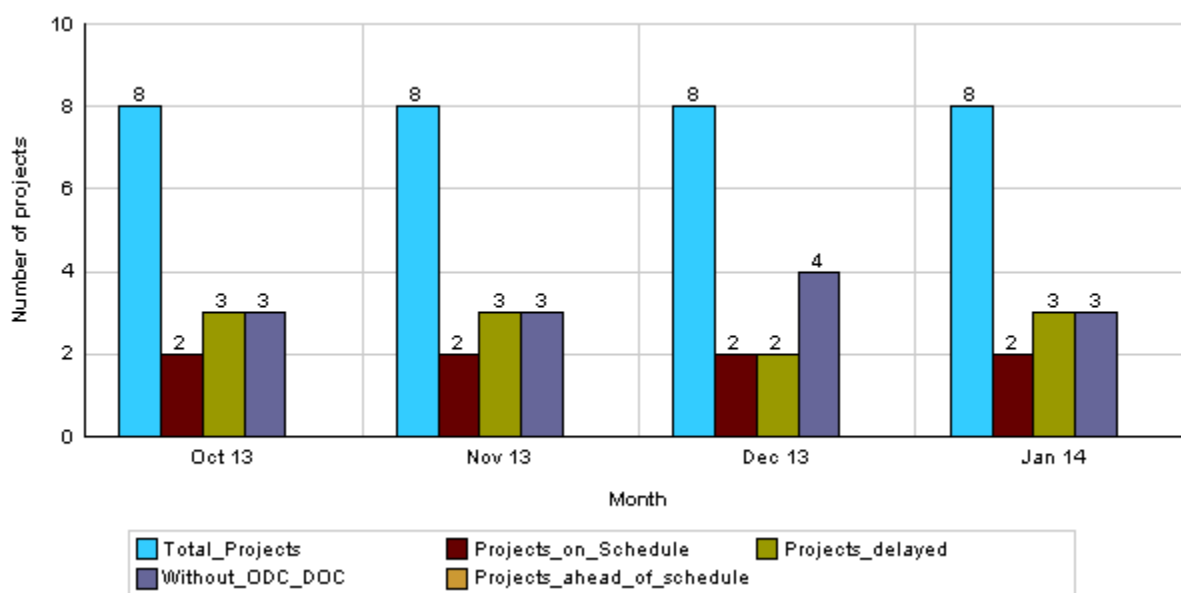


Break-up of 3 Delayed projects in January 2014

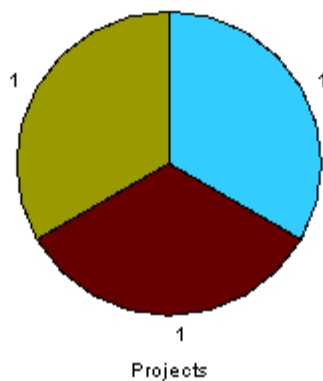


Delay in Months



Graphical Presentation of ATOMIC ENERGY Sector

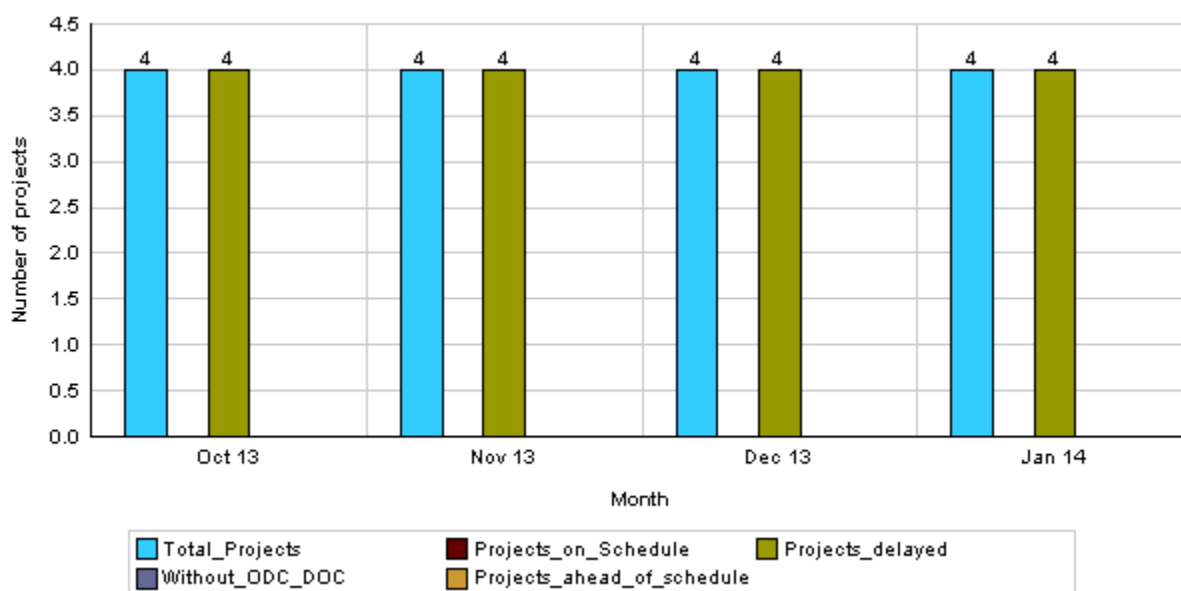

Break-up of 4 Delayed projects in January 2014

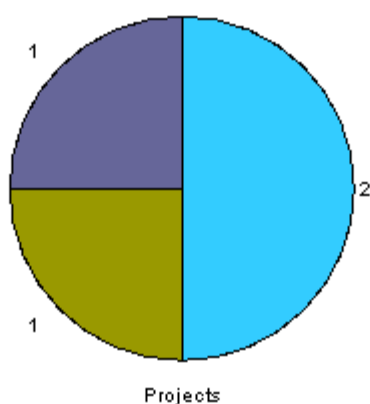

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	21,755.16
CIVIL AVIATION	8	6,035.46	6,624.95	6,946.00	5,574.92
COAL	55	38,127.05	41,499.58	41,525.17	16,436.87
STEEL	20	65,959.26	70,209.44	72,162.25	57,573.37
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	4,510.51
PETROLEUM	82	181,913.11	196,535.83	197,623.79	102,090.20
POWER	102	248,230.58	252,168.68	265,932.27	132,098.62
RAILWAYS	284	148,717.49	181,680.30	265,448.07	78,477.31
ROAD TRANSPORT AND HIGHWAYS	132	96,437.15	97,317.92	98,553.16	75,648.39
SHIPPING AND PORTS	19	15,617.12	17,487.95	17,871.52	8,793.03
TELECOMMUNICATIONS	10	5,079.29	5,079.29	4,982.94	1,752.17
URBAN DEVELOPMENT	4	47,588.18	47,647.08	52,861.08	9,242.93
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	722	900,150.20	962,696.53	1,080,739.25	513,988.97

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(Jan,2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11(O) -	3/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,089.00	12/2008 -	01/2015	73(O) -	40/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54(O) -	9/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3(O) -	2/69
	Total		40,442.00 -	46,726.00	21,755.16				54/327
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	2,593.13	2,483.65	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	256.77	01/2011 04/2013	03/2015	50(O) 23(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	264.45	05/2012 -	02/2014	21(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,908.57	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	199.83	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	461.63	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,946.00	5,574.92				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,159.43	03/2013 09/2012	03/2015	24(O) 30(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	613.44	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	49.66	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	125.63	03/2012 -	03/2016	48(O) -	5/6
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.25	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.12	03/2010 -	03/2015	60(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	53.49	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	158.53	03/2017 -	03/2017	0(O) -	4/12
23	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]NCL,MULTI STATE	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014	0(O) -	0/2
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	163.23	03/2015 -	03/2015	0(O) -	0/3
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.44	03/2014 -	03/2016	24(O) -	2/8
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,302.22	03/2014 -	03/2016	24(O) -	6/12
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,601.63	03/2014 -	03/2016	24(O) -	10/15
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	75.42	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	119.43	03/2013 -	03/2015	24(O) -	3/8
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,ANDHRA PRADESH	07/2011	447.06 -	447.06	29.04	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.81	12/2012 -	03/2016	39(O) -	10/44
36	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,ANDHRA PRADESH	07/2012	417.33 -	417.33	0.17	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	114.67	03/2013 -	03/2015	24(O) -	5/10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	53.88	03/2014 -	03/2014	0(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018	0(O) -	0/4
41	KISTARAM OCP - [N06000089]SCCL,ANDHRA PRADESH	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.36	03/2013 -	03/2014	12(O) -	0/2
43	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.77	03/2010 -	03/2014	48(O) -	9/10
44	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	1,188.31	-	03/2013 -	-	-	0/9
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.15	03/2012 -	03/2015	36(O) -	4/6
48	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	MURAIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	249.46	12/2015 -	04/2018	28(O) -	2/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
52	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.19	03/2014 -	03/2016	24(O) -	0/1
55	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	103.47	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	31.29	03/2014 -	03/2016	24(O) -	0/2
57	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	265.57	03/2016 -	03/2016	0(O) -	0/2
58	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	242.96	03/2012 -	03/2015	36(O) -	24/27
59	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,ANDHRA PRADESH	07/2011	162.76 -	162.76	2.56	03/2015 -	03/2015	0(O) -	4/29
60	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,ANDHRA PRADESH	11/2012	430.14 -	430.14	59.12	03/2016 -	03/2016	0(O) -	4/48
61	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,ANDHRA PRADESH	06/2012	365.01 -	365.01	3.62	06/2015 -	06/2015	0(O) -	2/51
62	RKP OCP PHASE-I - [N06000079]SCCL,ANDHRA PRADESH	03/2010	209.78 -	209.78	57.53	03/2015 -	03/2015	0(O) -	8/31
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	249.03	60.75	03/2012 -	-	-	16/42
64	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	50.46	03/2016 -	03/2016	0(O) -	0/12
65	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	141.54	03/2012 -	03/2016	48(O) -	0/2
66	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,869.96	06/2009 -	03/2014	57(O) -	19/23

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,991.82	03/2012 -	05/2014	26(O) -	19/38
	Total		38,127.05 -	41,525.17	16,436.87				198/777
	<u>STEEL</u>								
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	356.11	04/2013 09/2014	09/2014	17(O) 0(R)	17/18
69	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016	0(O) -	0/0
70	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	257.79	12/2009 08/2010	06/2013	-	1/1
71	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	289.60	01/2010 02/2011	11/2013	-	3/3
72	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	274.17	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
73	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	302.63	09/2009 05/2012	07/2014	58(O) 26(R)	1/1
74	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	364.11	12/2011 09/2014	09/2014	33(O) 0(R)	15/20
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.83	09/2008 12/2013	03/2014	66(O) 3(R)	3/4
76	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	92.77	08/2014 -	08/2014	0(O) -	1/2
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	100.11	11/2013 -	06/2015	19(O) -	1/3
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,982.04	03/2013 -	03/2015	24(O) -	25/32
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,356.27	12/2011 -	03/2014	27(O) -	18/21
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,007.48	12/2012 -	12/2014	24(O) -	13/16
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,487.23	12/2011 -	06/2014	30(O) -	21/23
82	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,729.46	10/2009 10/2012	03/2014	53(O) 17(R)	66/67
83	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,605.40	03/2013 -	09/2014	18(O) -	16/19
84	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	114.44	10/2013 -	08/2014	10(O) -	0/3
85	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	14.26	09/2017 -	09/2014	-36(O) -	0/2
86	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	53.59	06/2015 -	06/2015	0(O) -	0/2
87	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	254.90	19.17	12/2014 -	12/2014	0(O) -	0/1

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		65,959.26 -	72,162.25	57,573.37				214/258
	<u>PETROCHEMICALS</u>								
88	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012 -	-	-	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>PETROLEUM</u>								
89	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	60.87	06/2012 -	05/2014	23(O) -	0/4
90	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,888.97	06/2012 -	05/2014	23(O) -	0/0
91	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24(O) -	0/0
92	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24(O) -	0/0
93	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
94	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	111.01	08/2015 -	08/2015	0(O) -	0/0
95	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	333.96	07/2012 07/2012	-	-	6/7
96	BUTENE-1 PROJECT AT PANIPAT - [N16000139]IOCL,HARYANA	02/2012	190.00 -	165.00	116.65	03/2014 -	03/2014	0(O) -	23/24
97	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	148.68	06/2012 -	03/2014	21(O) -	0/0
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	445.97	09/2011 -	12/2014	39(O) -	0/0
99	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21(O) -	0/0
100	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	155.10	08/2013 -	09/2014	13(O) -	0/5
101	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	101.83	09/2012 -	12/2014	27(O) -	0/0
102	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
103	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8(O) -	0/5
104	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
105	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	-	0/5
106	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12(O) -	0/5
107	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	450.52	05/2013 06/2014	06/2014	13(O) 0(R)	0/5

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49(O) -	0/0
109	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	79.36	09/2013 -	09/2013	-	0/1
110	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	616.20	- -	-	-	0/0
111	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2014	98(O) 24(R)	0/0
112	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.50	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
113	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
114	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44(O) 22(R)	0/0
115	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12(O) -	0/5
116	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	143.66	05/2014 -	05/2015	12(O) -	0/9
117	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
118	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
119	DEVELOPMENT OF SB-14 FIELD - [N16000116]ONGC,MULTI STATE	01/2011	410.44 -	410.44	237.16	11/2012 -	05/2014	18(O) -	0/9
120	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	186.78	12/2014 -	12/2014	0(O) -	0/8
121	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.31	01/2014 -	12/2015	23(O) -	0/9
122	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32(O) 24(R)	6/76
123	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,969.18	09/2011 03/2012	03/2014	30(O) 24(R)	56/59
124	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	2.13	- -	-	-	0/0
125	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	03/2014	29(O) -	0/9
126	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	1,844.55	05/2015 -	05/2015	0(O) -	0/17
127	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,514.22	04/2013 12/2013	03/2014	11(O) 3(R)	2/167
128	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	490.10	03/2015 -	03/2015	0(O) -	0/12
129	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
130	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,265.85	12/2015 -	05/2016	5(O) -	0/0
131	IOR GELEKI (ONGCL) - [160100216]ONGC,ASSAM	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
132	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,ASSAM	09/2001	345.10 663.69	750.00	743.72	03/2007 03/2014	03/2014	84(O) 0(R)	3/3

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
133	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	40.85	03/2014 -	12/2014	9(O) -	0/5
134	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95(O) 11(R)	6/6
135	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
136	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
137	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	-	0/1
138	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,273.58	12/2012 -	-	-	0/10
139	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	-	03/2015 -	03/2015	0(O) -	0/64
140	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	36.23	01/2016 -	01/2016	0(O) -	0/0
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	181.48	11/2015 -	11/2015	0(O) -	14/29
142	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	99.11	06/2014 -	06/2014	0(O) -	0/0
143	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23(O) -	0/0
144	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	48.93	12/2014 -	12/2014	0(O) -	0/0
145	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,944.65	01/2012 -	03/2014	26(O) -	0/108
146	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18(O) -	0/0
147	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
148	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	737.45	03/2010 03/2012	02/2014	47(O) 23(R)	0/0
149	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	56.41	07/2015 -	07/2015	0(O) -	0/0
150	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	24,340.00	11/2012 -	12/2014	25(O) -	60/100
151	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	938.72	09/2012 -	08/2015	35(O) -	5/11
152	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,161.80	02/2014 -	03/2014	1(O) -	0/0
153	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	244.03	04/2012 -	03/2014	23(O) -	0/0
154	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	-	07/2016 -	07/2016	0(O) -	0/5
155	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	879.55	05/2014 -	05/2014	0(O) -	0/5
156	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	780.21	07/2012 -	03/2014	20(O) -	0/31

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
157	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8(O) -	0/0
158	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	1,138.50	2.11	04/2015 -	04/2015	0(O) -	0/0
159	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	320.99	12/2014 -	03/2015	3(O) -	0/0
160	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	428.26	11/2015 -	11/2015	0(O) -	10/25
161	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	-	0/0
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	776.92	10/2011 -	10/2015	48(O) -	0/0
163	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,084.00	01/2012 -	10/2015	45(O) -	0/0
164	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	930.83	10/2011 -	06/2014	32(O) -	0/0
165	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	-	0/0
166	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22(O) -	0/5
167	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	9.66	03/2015 -	06/2015	3(O) -	0/5
168	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12(O) -	0/0
169	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	268.90	03/2012 -	03/2015	36(O) -	13/20
170	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	422.91	12/2013 -	03/2014	3(O) -	0/0
	Total		181,913.11 -	197,623.79	102,090.20				210/910
	<u>POWER</u>								
171	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,133.03	08/2012 -	03/2014	19(O) -	0/11
172	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	-	- -	-	-	0/17
173	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	6.51	10/2014 -	10/2014	0(O) -	0/7
174	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,683.00	08/2013 -	02/2015	18(O) -	13/19
175	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,036.00	12/2009 -	03/2017	87(O) -	24/49
176	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,252.00	07/2011 -	06/2016	59(O) -	5/28

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
177	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	11.89	12/2015 -	12/2015	0(O) -	2/20
178	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,174.99	09/2014 -	09/2014	0(O) -	7/20
179	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	1,909.24	336.37	06/2015 -	06/2015	0(O) -	0/0
180	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,ANDHRA PRADESH	08/2011	1,637.34 -	1,637.34	1,228.88	08/2014 -	08/2014	0(O) -	7/20
181	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	42.36	06/2014 -	06/2014	0(O) -	0/20
182	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
183	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	4.86	10/2014 -	10/2014	0(O) -	2/2
184	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.78	10/2009 -	05/2014	55(O) -	5/15
185	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016	0(O) -	0/0
186	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	789.56	11/2012 -	03/2015	28(O) -	2/13
187	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
188	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,306.06	05/2014 -	05/2014	0(O) -	3/11
189	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	912.00	09/2017 -	09/2017	0(O) -	4/41
190	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	541.52	08/2014 -	08/2014	0(O) -	1/16
191	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATTISGARH	08/2011	1,391.97 -	1,391.97	1,201.02	12/2013 -	05/2014	5(O) -	3/12
192	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016	0(O) -	0/0
193	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 1,007.16	1,007.16	915.46	12/2007 12/2009	-	-	2/11
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,712.05	12/2009 06/2016	03/2017	87(O) 9(R)	11/26

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
195	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,118.93	01/2016 -	11/2016	10(O) -	5/6
196	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,553.00	04/2009 -	05/2015	73(O) -	1/9
197	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	2,692.00	12/2016 -	12/2016	0(O) -	15/21
198	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,872.65	09/2008 -	03/2013	-	15/23
199	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,227.00	05/2017 -	05/2017	0(O) -	7/38
200	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	44.00	08/2017 -	08/2017	0(O) -	0/8
201	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
202	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	1,623.00	09/2016 -	09/2016	0(O) -	16/17
203	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,570.34	08/2013 -	06/2015	22(O) -	0/17
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	358.95	07/2013 -	12/2014	17(O) -	2/11
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	267.38	02/2012 -	12/2013	-	1/13
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37(O) -	0/11
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	392.98	11/2011 -	12/2013	-	1/14
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,MULTI STATE	10/2010	182.68 -	182.68	139.73	01/2013 -	02/2014	13(O) -	4/6
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	962.89	04/2013 -	03/2015	23(O) -	0/11
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	278.18	11/2014 -	11/2014	0(O) -	2/12
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	169.16	03/2015 -	03/2015	0(O) -	4/15
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	77.98	04/2015 -	05/2015	1(O) -	0/16
216	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	622.71	11/2012 -	03/2014	16(O) -	0/11
217	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,265.17	10/2010 -	03/2014	41(O) -	0/2
218	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,239.17	09/2009 -	07/2018	106(O) -	3/6
219	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	794.02	08/2013 09/2015	09/2015	25(O) 0(R)	17/26

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
220	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	2,952.80	01/2012 -	06/2014	29(O) -	14/28
221	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	6,230.81	4,544.00	10/2012 -	10/2013	-	16/16
222	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	1,889.00	11/2016 -	11/2016	0(O) -	16/17
223	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/0
224	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,468.31	09/2010 -	06/2018	93(O) -	0/0
225	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	112.01	04/2013 -	03/2014	11(O) -	6/15
226	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,086.34	08/2012 -	03/2014	19(O) -	0/5
227	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	212.73	06/2016 -	12/2015	-6(O) -	0/20
228	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	161.64	06/2012 -	01/2014	19(O) -	0/3
229	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	539.87	12/2014 -	11/2014	-1(O) -	2/2
230	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	100.33	03/2014 -	03/2014	0(O) -	2/7
231	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	257.99	08/2014 -	05/2015	9(O) -	2/19
232	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	946.16	08/2012 -	12/2014	28(O) -	0/11
233	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,ANDHRA PRADESH	02/2014	243.53 -	243.53	-	08/2014 -	08/2014	0(O) -	0/0
234	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	618.38	02/2015 -	02/2015	0(O) -	0/14
235	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	532.78	11/2014 -	11/2014	0(O) -	0/16
236	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	590.66	01/2015 -	01/2015	0(O) -	4/19
237	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	202.63	08/2014 -	08/2014	0(O) -	7/20
238	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	252.39	06/2014 -	09/2014	3(O) -	8/20
239	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	2,978.48	1,962.00	03/2013 -	03/2017	48(O) -	0/13
240	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,436.24	09/2009 -	07/2015	70(O) -	0/4
241	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	576.41	07/2010 02/2016	02/2017	79(O) 12(R)	1/10

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
242	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	129.10	01/2014 -	06/2014	5(O) -	3/18
243	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	723.27	08/2014 -	06/2015	10(O) -	2/19
244	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,264.35	10/2014 -	06/2015	8(O) -	3/18
245	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,641.19	10/2012 -	03/2015	29(O) -	0/11
246	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	160.75	11/2011 -	03/2014	28(O) -	0/4
247	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,555.07	12/2012 -	03/2015	27(O) -	0/11
248	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	431.56	01/2015 -	12/2015	11(O) -	2/20
249	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,ANDHRA PRADESH	02/2012	324.33 -	324.33	75.80	08/2014 -	08/2014	0(O) -	9/20
250	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,ANDHRA PRADESH	02/2012	1,927.16 -	1,927.16	812.46	10/2014 -	10/2014	0(O) -	3/16
251	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
252	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	375.59	02/2014 -	06/2014	4(O) -	4/17
253	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	356.37	10/2013 -	04/2014	6(O) -	2/13
254	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	145.81	07/2013 -	03/2014	8(O) -	0/13
255	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	-	12/2013 -	-	-	4/13
256	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	225.45	11/2013 -	09/2014	10(O) -	7/20
257	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,402.61	03/2013 -	05/2014	14(O) -	5/15
258	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12(O) -	5/15
259	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3(O) -	1/13
260	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	63.72	01/2013 -	06/2015	29(O) -	5/18

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
261	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,140.80	11/2013 -	06/2015	19(O) -	5/16
262	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,883.00	11/2012 -	03/2015	28(O) -	0/15
263	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,570.92	07/2014 -	12/2014	5(O) -	2/14
264	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	714.20	07/2013 -	11/2014	16(O) -	18/25
265	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	913.63 -	913.63	512.83	07/2006 12/2015	12/2015	113(O) 0(R)	2/14
266	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
267	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50(O) -	2/2
268	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	736.00	08/2015 -	08/2015	0(O) -	14/14
269	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
270	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	383.30	07/2014 -	05/2016	22(O) -	1/1
271	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	466.16	09/2010 -	03/2014	42(O) -	0/5
272	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,353.98	06/2015 -	12/2015	6(O) -	3/28
	Total		248,230.58 -	265,932.27	132,098.62				395/1349
	<u>RAILWAYS</u>								
273	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	1.97	- -	-	-	0/0
274	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	533.44	03/2014 -	03/2019	60(O) -	0/0
275	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
276	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	398.93	12/2009 03/2011	03/2014	51(O) 36(R)	0/0
277	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	0.75	- -	-	-	0/0
278	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 385.60	1,215.30	43.74	03/2013 -	03/2013	-	0/0
279	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	2,820.00	272.85	- -	-	-	0/0
280	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	19.86	- -	-	-	0/0
281	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
282	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	153.00	-	- -	-	-	0/0
283	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	2,000.00	24.46	- -	-	-	0/0
284	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	416.04	03/2011 03/2011	03/2011	-	0/0
285	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
286	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	98.44	- -	-	-	0/0
287	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	64.93	- -	03/2017	- -	0/0
288	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.10	725.00	563.39	06/1999 03/2011	03/2011	-	0/0
289	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.67	- -	-	-	0/0
290	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
291	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	123.10	- -	-	-	0/0
292	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
293	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
294	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.94	- -	-	-	0/0
295	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	199.75	36.88	- -	-	-	0/0
296	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	22.58	- -	-	-	0/0
297	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	4.30	- -	-	-	0/0
298	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	189.71	12/2012 -	12/2014	24(O) -	0/0
299	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	901.62	0.61	- -	-	-	0/0
300	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	1.28	- -	-	-	0/0
301	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
302	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	1,106.62	225.72	12/2010 03/2011	03/2011	-	0/0
303	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	10.46	- -	-	-	0/0
304	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
305	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	338.87	03/2004 12/2010	12/2014	129(O) 48(R)	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
306	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	337.49	0.12	- -	-	-	0/0
307	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	923.23	-	- -	-	-	0/0
308	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
309	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	128.84	04/2014 -	03/2017	35(O) -	0/0
310	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	38.15	- -	-	-	0/0
311	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	193.82	03/2011 -	-	-	0/0
312	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	70.64	- -	-	-	0/0
313	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	783.15	03/2010 -	12/2015	69(O) -	0/0
314	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	1.90	03/2012 -	-	-	0/0
315	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.67	- -	-	-	0/0
316	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.09	- -	-	-	0/0
317	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	267.37	33.96	- -	-	-	0/0
318	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,993.95	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
319	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
320	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9(O) -	0/0
321	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	2.32	- -	-	-	0/0
322	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	59.50	- -	-	-	0/0
323	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	532.10	- -	-	-	0/0
324	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	92.44	- -	-	-	0/0
325	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	460.61	- -	-	-	0/0
326	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	1.91	- -	-	-	0/0
327	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	0.18	- -	-	-	0/0
328	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	103.76	- -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
329	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
330	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
331	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.08	- -	-	-	0/0
332	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	-	-	0/0
333	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	558.00	-	- -	-	-	0/0
334	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.20	- -	-	-	0/0
335	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	139.76	- -	-	-	0/0
336	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
337	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	391.24	- -	03/2014	- -	0/0
338	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	951.99	03/2007 -	03/2017	120(O) -	0/0
339	CUDDALORE- SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	266.48	- -	-	-	0/0
340	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
341	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	159.33	- -	-	-	0/0
342	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	533.38	102.35	12/2011 02/2012	02/2012	-	0/0
343	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	134.55	12/2012 -	-	-	0/0
344	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	56.07	12/2015 -	12/2015	0(O) -	0/0
345	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	406.92	138.93	- -	-	-	0/0
346	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	3.67	- -	-	-	0/0
347	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	366.73	4.20	- -	-	-	0/0
348	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	236.88	- -	03/2014	- -	0/0
349	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
350	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	142.87	- -	-	-	0/0
351	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	607.09	519.47	12/2012 12/2012	02/2013	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
352	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	0.75	- -	-	-	0/0
353	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	1.47	02/2019 -	02/2019	0(O) -	0/0
354	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.08	- -	-	-	0/0
355	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
356	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	727.35	- -	12/2012	-	0/0
357	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
358	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
359	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	2.06	- -	-	-	0/0
360	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
361	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.71	12/2008 -	09/2014	69(O) -	0/0
362	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	261.04	06/2013 06/2013	03/2015	21(O) 21(R)	0/0
363	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
364	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240(O) -	0/0
365	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,117.00	-	- -	-	-	0/0
366	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.09	270.00	287.69	02/2011 02/2011	03/2013	-	0/0
367	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.88	- -	-	-	0/0
368	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	0.97	- -	-	-	0/0
369	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 611.03	611.03	135.49	12/2011 11/2013	11/2013	-	0/0
370	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	261.70	137.85	02/2006 -	-	-	0/0
371	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	863.23	764.01	- -	03/2012	-	0/0
372	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
373	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	156.65	50.42	- -	-	-	0/0
374	GUDUR-DURGARAJAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
375	GULBARGA-BIDAR,SCR(NL) - [N220100254]SCR,KARNATAKA	02/1998	242.42 369.70	832.00	383.74	- 05/2009	05/2009	-	0/0
376	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [N220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	580.26	03/1994 -	01/2014	238(O) -	0/0
377	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	4.15	- -	-	-	0/0
378	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
379	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]JER,MULTI STATE	04/2000	157.17 -	157.17	76.30	- -	-	-	0/0
380	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]JECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
381	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [N220100303]JECR,BIHAR	04/2003	324.66 528.65	528.65	195.19	- -	-	-	0/0
382	HANSDIHA-GODDA NL - [N22000236]JER,MULTI STATE	04/2011	267.09 -	267.09	0.91	- -	-	-	0/0
383	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]JER,MULTI STATE	04/2010	172.03 -	172.03	4.68	- -	-	-	0/0
384	HARIDASPUR-PARADEEP(NL) - [N220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	259.60	- 09/2009	-	-	0/0
385	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	444.18	-	- -	-	-	0/0
386	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
387	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [N220100183]SWR,KARNATAKA	02/1997	295.00 412.91	412.91	794.35	- -	01/2013	-	0/0
388	HATHUA-BHATNI (N L) (NER) - [N220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	148.48	- -	03/2014	- -	0/0
389	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	829.74	45.67	03/2015 -	03/2015	0(O) -	0/0
390	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
391	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.25	- -	-	-	0/0
392	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]JER,MULTI STATE	04/2010	157.94 -	157.94	41.05	- -	-	-	0/0
393	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208]RE, WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
394	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]JER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
395	HUBLI-ANKOLA(NL),SWR - [N220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	110.08	- -	-	-	0/0
396	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.61	04/2012 -	03/2016	47(O) -	0/0
397	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	313.24	170.83	01/1999 -	-	-	0/0
398	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.47	257.47	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
399	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	165.65	135.03	- -	-	-	0/0
400	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	847.75	838.53	06/2007 -	06/2007	-	0/0
401	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	726.24	03/2012 08/2012	-	-	0/0
402	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	34.32	- -	-	-	0/0
403	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	740.00	510.66	03/2012 03/2012	12/2012	-	0/0
404	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	1,924.82	03/2011 03/2014	03/2020	108(O) 72(R)	0/0
405	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	2,050.00	92.37	- -	-	-	0/0
406	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	235.00	- -	-	-	0/0
407	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	49.84	- -	-	-	0/0
408	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	2.15	- -	-	-	0/0
409	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,532.34	- -	03/2013	-	0/0
410	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
411	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	513.32	- -	03/2014	- -	1/1
412	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	767.01	- -	10/2012	-	0/0
413	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	131.15	12/2012 -	03/2018	63(O) -	0/0
414	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.02	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
415	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	150.62	03/2017 -	03/2017	0(O) -	0/0
416	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	1,054.35	0.42	- -	-	-	0/0
417	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	162.87	125.04	- -	-	-	0/0
418	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	270.46	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
419	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	282.50	- -	12/2014	- -	0/0
420	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
421	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	768.87	512.34	- 03/2010	03/2010	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	491.19 2,957.21	2,957.21	1,721.58	07/2005 -	-	-	0/0
423	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91 418.17	418.17	198.60	- -	-	-	0/0
424	KONDAPALLI-KOTHAGUDEM - [N22000260] (SCR), ANDHRA PRADESH	04/2013	723.00 -	723.00	-	- -	-	-	0/0
425	KOSI BRIDGE (NL), ECR - [220100304] ECR, BIHAR	04/2002	323.41 322.95	341.41	289.97	03/2012 03/2013	03/2013	-	0/0
426	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
427	KOTTUR-HARIHAR (NL), (SWR) - [220100212] SWR, KARNATAKA	04/1995	65.94 302.23	302.23	362.56	- -	12/2012	-	0/0
428	KUMBALAM-TURAVUR - [N22000191] SR, KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
429	KURSELA-BIHARIGANJ (NL) - [N22000178] ECR, BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
430	KURUPPANTHARA-CHINGAVANAM - [N22000190] SR, MULTI STATE	04/2007	270.14 -	346.15	8.35	- -	-	-	0/0
431	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216] ER, MULTI STATE	04/1999	406.99 -	406.99	139.07	- -	-	-	0/0
432	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, MULTI STATE	09/1998	925.00 -	1,630.97	406.06	05/2008 03/2011	-	-	0/0
433	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148] ECR, ODISHA	04/1993	100.00 142.98	227.94	234.32	03/2002 -	02/2014	143(O) -	0/0
434	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244] ER, MULTI STATE	04/2009	257.42 -	257.42	33.79	03/2014 -	03/2014	0(O) -	0/0
435	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211] NEFR, ASSAM	04/2012	246.07 -	364.06	0.11	- -	-	-	0/0
436	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127] NEFR, ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,872.29	03/2009 -	03/2017	96(O) -	0/0
437	MACHERLA-NALGONDA (NL) (SCR) - [220100220] SCR, ANDHRA PRADESH	07/1998	125.00 363.26	480.00	0.86	07/2008 -	07/2008	-	0/0
438	MADURAI-BODINAYAKKANUR - [N22000201] SR, TAMIL NADU	04/2008	164.41 -	450.00	11.31	- -	-	-	0/0
439	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215] SR, MULTI STATE	04/2011	601.43 -	800.00	0.15	- -	-	-	0/0
440	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRATHAT-KULPI NL - [N22000243] ER, MULTI STATE	04/2009	493.96 -	493.96	116.99	- -	-	-	0/0
441	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316] NER, BIHAR	04/2003	218.19 218.19	472.00	186.33	- -	02/2013	-	0/0
442	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168] ER, JHARKHAND	04/1995	184.00 900.05	900.05	736.73	12/2011 12/2011	03/2013	-	0/0
443	MANOHARABAD-KOTHPALL NEW LINE (SCR) - [N22000032] SCR, ANDHRA PRADESH	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
444	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165] SER, JHARKHAND	04/2012	258.20 -	258.20	0.61	- -	03/2016	- -	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
445	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	396.04	80.52	- -	-	-	0/0
446	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	477.88	444.11	03/2012 03/2013	03/2013	-	0/0
447	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
448	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	0.10	01/1999 -	-	-	0/0
449	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	965.16	558.03	- -	-	-	0/0
450	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	386.48	- -	-	-	0/0
451	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	377.44	0.33	- -	-	-	0/0
452	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.70	- -	-	-	0/0
453	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
454	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
455	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
456	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
457	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	390.60	1.62	- -	-	-	0/0
458	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,506.46	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
459	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	217.74	- -	03/2014	-	0/0
460	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	199.27	- -	-	-	0/0
461	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.25	- -	-	-	0/0
462	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
463	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	1.29	- -	-	-	0/0
464	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	32.10	- -	-	-	0/0
465	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	0.52	- -	-	-	0/0
466	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	883.00	669.71	02/2009 -	03/2012	-	0/0
467	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	1,036.78	358.32	07/2012 -	-	-	0/0
468	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
469	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
470	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	532.87	42.67	- -	-	-	0/0
471	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	156.37	- -	03/2017	- -	0/0
472	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	38.96	- -	-	-	0/0
473	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	3.04	- -	-	-	0/0
474	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	173.87	- -	03/2014	- -	0/0
475	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	156.37	- -	03/2016	- -	0/0
476	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	21.83	- -	-	-	0/0
477	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.17	250.62	- -	03/2015	- -	0/0
478	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
479	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	33.56	- -	03/2017	- -	0/0
480	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	0.57	- -	03/2015	- -	0/0
481	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,418.21	1,033.06	- -	-	-	0/0
482	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	8.98	03/2015 -	03/2017	24(O) -	0/0
483	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,543.15	12/2008 -	03/2018	111(O) -	0/0
484	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	62.70	03/2014 -	03/2016	24(O) -	0/0
485	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,619.02 -	2,913.51	372.15	03/2016 -	03/2016	0(O) -	0/0
486	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	68.18	03/2016 -	06/2016	3(O) -	0/0
487	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	3,951.98	273.79	03/2016 -	03/2016	0(O) -	0/0
488	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
490	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	293.74	139.45	12/2010 12/2010	12/2010	-	0/0
491	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	191.00	204.59	- -	01/2014	-	0/0
492	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	1,966.06	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
493	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	925.30	652.71	- -	02/2014	-	0/0
494	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	203.00	172.58	- -	03/2014	-	0/0
495	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	261.38	15.67	- -	-	-	0/0
496	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
497	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	248.07	9.97	03/2015 -	03/2015	0(O) -	0/0
498	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
499	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
500	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
501	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	791.40	01/1999 -	-	-	0/0
502	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 842.35	1,122.00	828.58	- -	03/2013	-	0/6
503	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	273.49	12/2007 03/2010	-	-	0/0
504	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,291.27	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
505	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	298.57	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
506	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	461.67	- -	-	-	0/0
507	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	565.61	03/2013 -	03/2014	12(O) -	0/0
508	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	1,225.90	226.84	- -	-	-	0/0
509	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126(O) -	0/0
510	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	3,019.17	2,500.48	- -	03/2015	-	0/0
511	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	-	- -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	785.31	- -	-	-	0/0
513	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	13.66	- -	-	-	0/0
514	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	1,421.25	305.08	03/2012 -	-	-	0/0
515	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	970.34	245.06	- -	-	-	0/0
516	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	287.00	1.01	- -	-	-	0/0
517	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	18.16	- 12/2017	12/2017	- 0(R)	0/0
518	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	14.06	- -	-	-	0/0
519	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	240.38	- -	-	-	0/0
520	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	365.77	- -	-	-	0/0
521	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
522	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.84	- -	-	-	0/0
523	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	64.63	12/2015 -	03/2017	15(O) -	0/0
524	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	562.74	0.58	- -	-	-	0/0
525	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	16.35	- -	-	-	0/0
526	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.91	- -	-	-	0/0
527	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	42.29	- -	-	-	0/0
528	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	296.00	-	- -	-	-	0/0
529	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.00	0.01	- -	-	-	0/0
530	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	111.21	02/2015 -	02/2015	0(O) -	0/0
531	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.98	- -	-	-	0/0
532	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	516.23	452.07	03/2014 -	03/2014	0(O) -	0/0
533	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	810.78	130.02	- -	-	-	0/0
534	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132(O) 59(R)	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12(O) -	0/0
536	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.39	- -	-	-	0/0
537	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	157.96 1,188.91	1,188.91	648.78	- 12/2009	02/2012	-	0/0
538	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
539	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	820.00	186.35	- -	-	-	0/0
540	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	420.00	59.74	- -	-	-	0/0
541	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	167.73	65.82	03/2012 -	02/2013	-	0/0
542	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	900.00	561.28	- -	-	-	0/0
543	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	907.69 3,156.32	3,176.10	3,522.47	12/2006 08/2010	08/2010	-	0/0
544	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	0.54	- -	-	-	0/0
545	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181(O) -	0/0
546	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	751.93	03/2014 -	03/2014	0(O) -	0/0
547	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	0.36	- -	-	-	0/0
548	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	250.35	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
549	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
550	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 356.87	548.01	198.51	- 03/2010	-	-	0/0
551	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	41.51	- -	-	-	0/0
552	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	138.27	- -	04/2014	- -	0/0
553	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	1,604.00	46.40	- -	-	-	0/0
554	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	2.91	- -	-	-	0/0
555	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.31	- -	-	-	0/0
556	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		148,717.49 -	265,448.07	78,477.31				1/7
	ROAD TRANSPORT AND HIGHWAYS								

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
557	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	330.59	08/2013 -	-	-	0/0
558	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
559	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014	0(O) -	0/0
560	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	42.12	07/2014 -	07/2014	0(O) -	0/0
561	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	394.61	05/2013 -	-	-	0/0
562	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	647.94	11/2013 -	-	-	0/0
563	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	413.79	04/2014 -	04/2014	0(O) -	0/0
564	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014	0(O) -	0/0
565	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	3.26	07/2014 -	07/2014	0(O) -	0/0
566	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	100.21	01/2014 -	01/2014	0(O) -	0/0
567	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	332.50	02/2014 -	02/2014	0(O) -	0/0
568	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	611.24	02/2014 -	02/2014	0(O) -	0/0
569	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014	0(O) -	0/0
570	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014	0(O) -	0/0
571	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	582.60	09/2014 -	09/2014	0(O) -	0/3
572	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014	0(O) -	0/0
573	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,356.04	06/2013 -	-	-	0/3
574	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10(O) -	0/0
575	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	848.81	08/2013 -	-	-	0/3
576	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	454.33	02/2014 -	02/2014	0(O) -	0/0
577	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,324.51	08/2013 -	-	-	0/0
578	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,388.00	08/2013 -	-	-	0/0
579	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	301.97	08/2013 -	-	-	0/0
580	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	714.59	07/2013 -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
581	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014	0(O) -	0/0
582	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	385.15	266.26	09/2007 07/2011	-	-	0/0
583	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015	0(O) -	0/3
584	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,161.40	11/2012 -	12/2013	-	0/0
585	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0
586	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	361.07	09/2013 -	-	-	0/0
587	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.56	02/2015 -	02/2015	0(O) -	0/0
588	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014	0(O) -	0/0
589	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	597.22	- -	-	-	2/2
590	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	36.47	01/2013 -	-	-	0/0
591	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	528.15	08/2013 -	-	-	0/0
592	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	292.51	06/2008 -	-	-	0/0
593	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	262.98	06/2008 -	-	-	0/0
594	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	240.09	06/2005 -	-	-	0/0
595	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 09/2015	09/2015	65(O) 0(R)	0/0
596	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.06	02/2010 -	-	-	0/0
597	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	857.70	03/2013 -	-	-	0/0
598	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.24	10/2011 -	-	-	0/0
599	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.91	10/2011 -	-	-	0/0
600	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	839.00	825.42	- -	-	-	0/1
601	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	-	-	0/0
602	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	181.32	10/2008 -	-	-	0/0
603	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015	0(O) -	0/0
604	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46(O) -	0/0
605	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	621.67	07/2013 -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
606	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	294.35	06/2013 -	-	-	0/0
607	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	723.34	- -	-	-	1/1
608	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	257.33	06/2008 -	-	-	0/0
609	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 07/2014	07/2014	74(O) 0(R)	0/0
610	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	308.77	09/2010 -	-	-	0/0
611	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015	0(O) -	0/0
612	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	487.69	09/2008 -	-	-	0/0
613	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015	0(O) -	0/0
614	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5(O) -	0/0
615	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	150.62	09/2008 -	-	-	0/0
616	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,294.08	08/2013 06/2014	06/2014	10(O) 0(R)	0/0
617	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	1,925.62	09/2012 -	-	-	2/3
618	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	-	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
619	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	-	04/2008 03/2014	03/2014	71(O) 0(R)	0/0
620	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	-	-	0/0
621	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	-	02/2009 -	05/2014	63(O) -	0/0
622	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57(O) -	0/0
623	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	-	09/2007 -	05/2014	80(O) -	0/0
624	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5(O) -	0/0
625	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	948.41	01/2013 -	-	-	0/0
626	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	1,842.77	- -	-	-	3/3
627	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	548.40	05/2013 -	-	-	0/0
628	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	-	-	0/0
629	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	683.48	02/2013 -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
630	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,979.78	12/2012 -	-	-	0/0
631	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	822.18	07/2013 -	-	-	0/0
632	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	554.09	01/2014 -	01/2014	0(O) -	0/0
633	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	711.11	07/2013 -	-	-	0/0
634	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,127.12	05/2012 -	-	-	0/0
635	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	281.66	10/2008 -	-	-	0/0
636	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	588.54	07/2014 -	07/2014	0(O) -	0/0
637	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	- -	2/3
638	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	320.70	07/2012 -	-	-	0/0
639	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	241.28	151.77	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
640	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	382.02	107.55	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
641	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	265.63	92.14	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
642	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	247.43	180.36	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
643	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	1,936.00	06/2013 -	-	-	0/0
644	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	517.00	03/2013 -	-	-	0/0
645	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	303.05	06/2008 -	-	-	0/0
646	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	283.09	10/2014 -	10/2014	0(O) -	0/0
647	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
648	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 05/2014	05/2014	71(O) 0(R)	0/0
649	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	308.16	06/2008 -	-	-	0/0
650	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015	0(O) -	0/0
651	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	524.67	09/2013 -	-	-	0/0
652	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,129.29	02/2010 -	-	-	0/0
653	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	01/2014	0(O) -	0/0
654	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014	0(O) -	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
655	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	-	-	0/0
656	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014	0(O) -	0/0
657	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014	0(O) -	0/0
658	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	662.29	03/2014 -	03/2014	0(O) -	0/0
659	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	-	-	0/0
660	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,333.25	07/2012 -	-	-	0/0
661	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,206.67	03/2013 -	-	-	0/0
662	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	394.31	01/2014 -	01/2014	0(O) -	0/0
663	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	-	-	0/0
664	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015	0(O) -	0/0
665	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	345.30	10/2008 -	-	-	0/0
666	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015	0(O) -	0/0
667	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	256.68	09/2014 -	09/2014	0(O) -	0/0
668	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2(O) -	0/0
669	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	765.39	03/2013 -	-	-	0/0
670	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014	0(O) -	0/0
671	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	157.42	260.30	09/2007 03/2014	03/2014	78(O) 0(R)	0/0
672	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0
673	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014	0(O) -	0/0
674	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	12/2013	-	0/0
675	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,117.37	12/2013 -	12/2013	-	0/0
676	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014	0(O) -	0/0
677	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.50	08/2012 -	-	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
678	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 01/2015	01/2015	82(O) 0(R)	0/0
679	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014	0(O) -	0/0
680	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,260.86	11/2013 -	-	-	0/0
681	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	-	0/0
682	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	124.73	05/2013 -	-	-	0/0
683	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	366.60	-	-	-	2/2
684	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014	0(O) -	0/0
685	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	193.10	198.80	03/2008 -	-	-	0/0
686	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	56.65	11/2012 -	-	-	0/0
687	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015	0(O) -	0/0
688	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	-	-	-	0/0
	Total		96,437.15 -	98,553.16	75,648.39				12/27
	<u>SHIPPING AND PORTS</u>								
689	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	358.78	04/2011 11/2011	11/2011	-	0/0
690	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
691	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
692	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
693	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
694	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 02/2014	04/2014	2(O) 2(R)	0/0
695	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
696	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	990.28	12/2010 09/2012	03/2015	51(O) 30(R)	0/0
697	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
698	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
699	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
700	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
701	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
702	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
703	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
704	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
705	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
706	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
707	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	17,871.52	8,793.03				0/1
	<u>TELECOMMUNICATIONS</u>								
708	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	03/2014	62(O) -	0/0
709	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41(O) 24(R)	0/0
710	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	-	0/0
711	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
712	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	03/2014	57(O) -	0/0
713	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0

Sector Wise Details

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
714	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
715	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
716	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
717	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	03/2014	34(O) -	0/0
	Total		5,079.29 -	4,982.94	1,752.17				0/0
	<u>URBAN DEVELOPMENT</u>								
718	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
719	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
720	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	6,445.67	03/2016 -	03/2016	0(O) -	0/0
721	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	529.69	09/2014 -	05/2015	8(O) -	0/0
	Total		47,588.18 -	52,861.08	9,242.93				3/3
	<u>WATER RESOURCES</u>								
722	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		900,150.20	1,080,739.25	513,988.97				1106/3690

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

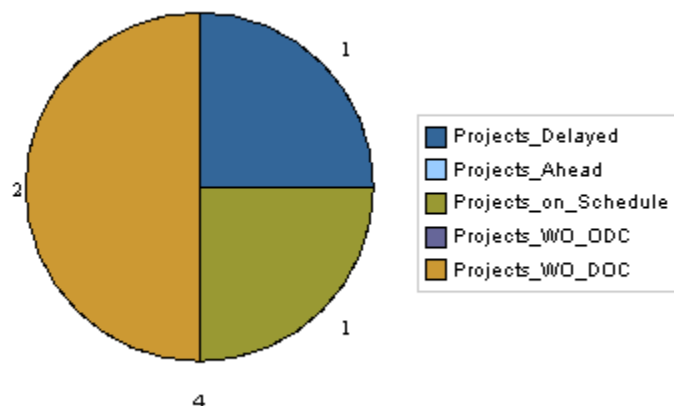

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 47588.18 crore but this was subsequently revised to Rs. 52861.08 crore implying a cost overrun of 11.1%. The expenditure incurred on these projects till January, 2014 is Rs. 9242.93 crore, which is 17.5% of the revised cost of the projects.

Figures are in Rs. Crore

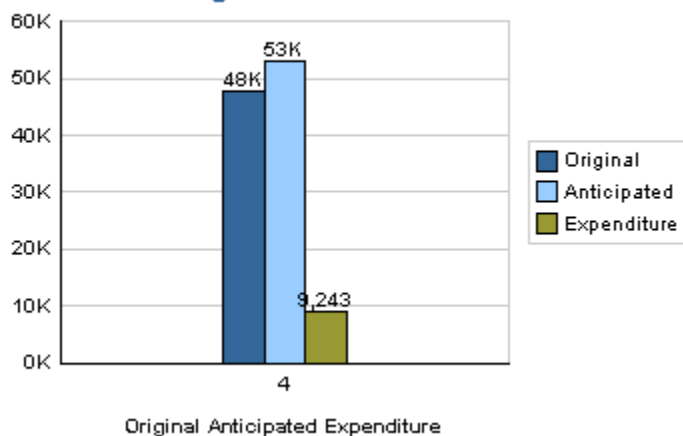

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	10
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 10 projects, 4 projects are delayed .6 projects do not have fixed dates of commissioning.

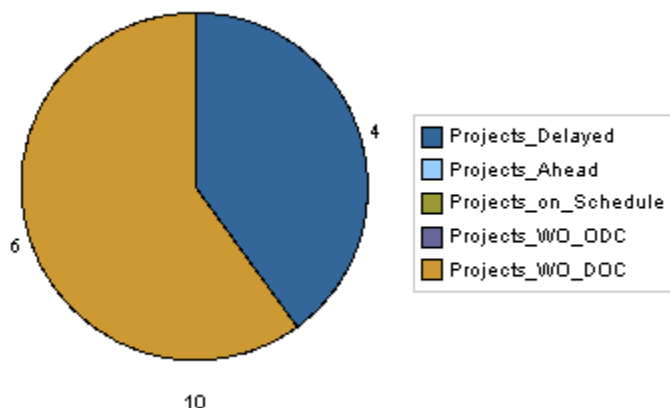

Investment Scenario

The Total Original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 5079.29 crore but this was subsequently revised to Rs. 4982.94 crore implying a cost overrun of -1.9%. The expenditure incurred on these projects till January, 2014 is Rs. 1752.17 crore, which is 35.2% of the revised cost of the projects.

Figures are in Rs. Crore

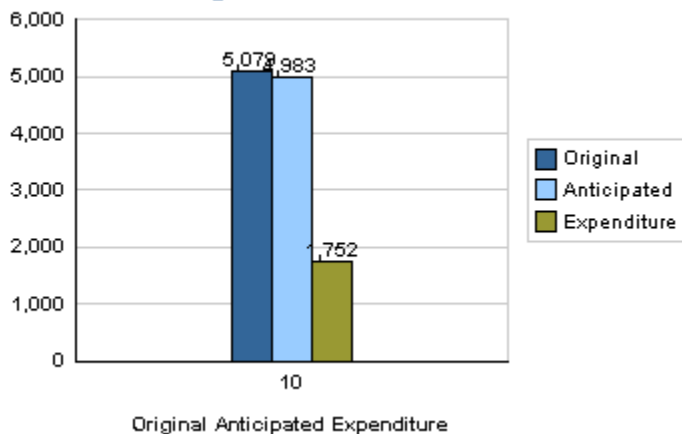

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **19**

Number of Projects Delayed **4**

Number of Projects Without Date Of Commissioning **15**

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 4 projects are delayed .15 projects do not have fixed dates of commissioning.

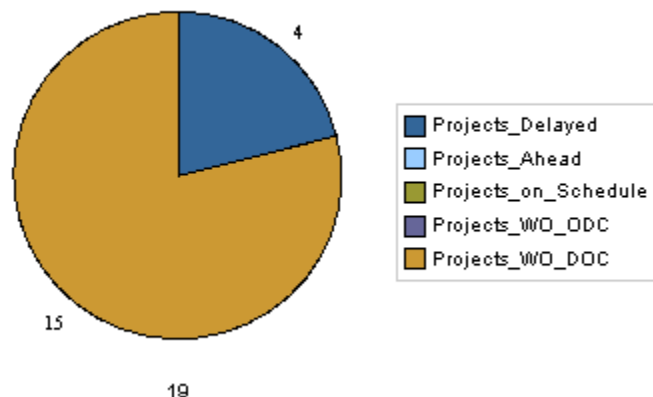

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17871.52 crore implying a cost overrun of 14.4%. The expenditure incurred on these projects till January, 2014 is Rs. 8793.03 crore, which is 49.2% of the revised cost of the projects.

Figures are in Rs. Crore

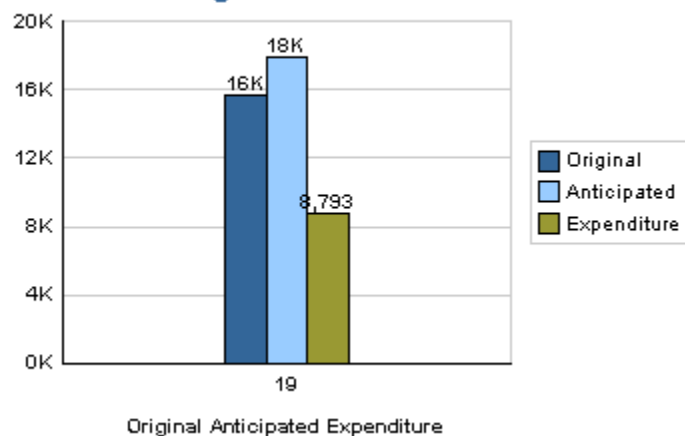

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	132
Number of Projects On Schedule	39
Number of Projects Delayed	21

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	71

Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 39 projects are on schedule and 21 projects are delayed .71 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

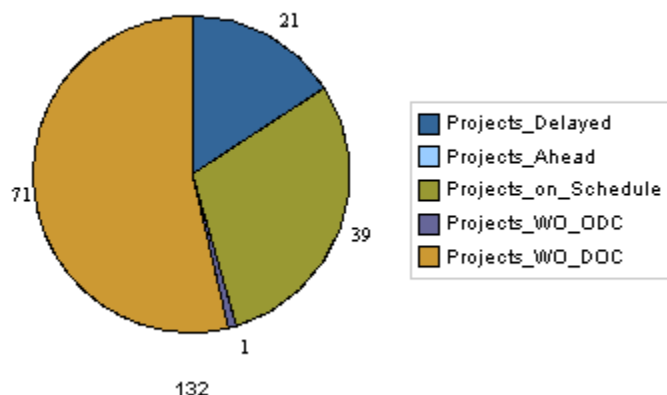

Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 96437.15 crore but this was subsequently revised to Rs. 98553.16 crore implying a cost overrun of 2.2%. The expenditure incurred on these projects till January, 2014 is Rs. 75648.39 crore, which is 76.8% of the revised cost of the projects.

Figures are in Rs. Crore

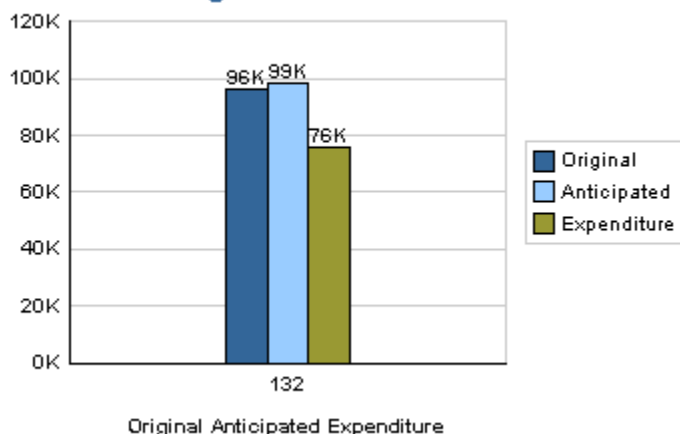

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	284
Number of Projects On Schedule	15
Number of Projects Delayed	38

Number of Projects Without Original Date of Commissioning	21
Number of Projects Without Date Of Commissioning	210

Brief Analysis


Project Status with respect to Original Schedule: Out of 284 projects, 15 projects are on schedule and 38 projects are delayed .210 projects do not have fixed dates of commissioning.21 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

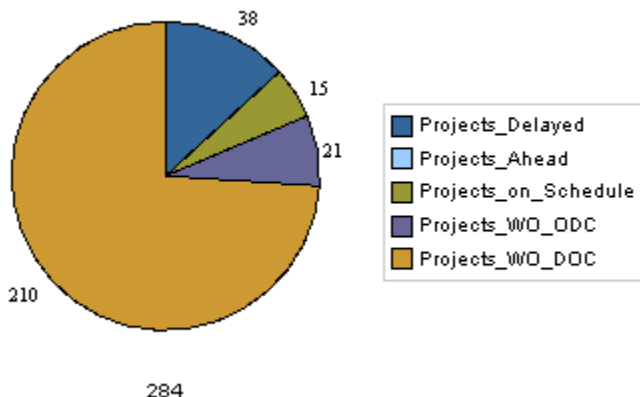

Investment Scenario

The Total Original cost of implementation of 284 projects when sanctioned, was of the order of Rs. 148717.49 crore but this was subsequently revised to Rs. 265448.07 crore implying a cost overrun of 78.5%. The expenditure incurred on these projects till January, 2014 is Rs. 78477.31 crore, which is 29.6% of the revised cost of the projects.

Figures are in Rs. Crore

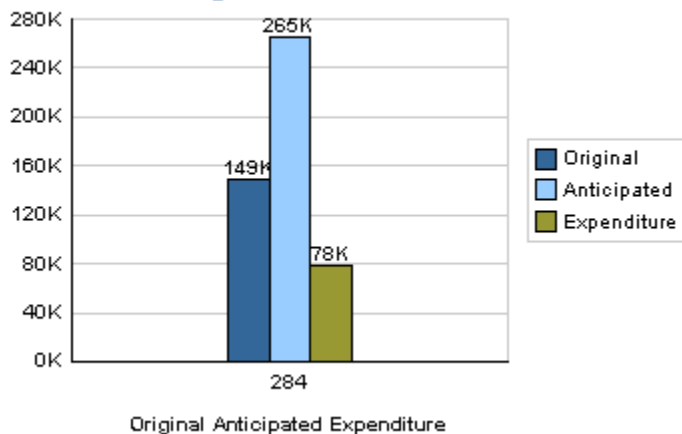

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	102
Number of Projects On Schedule	36
Number of Projects Delayed	55
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	9

Brief Analysis


Project Status with respect to Original Schedule: Out of 102 projects, 2 projects are ahead of schedule, 36 projects are on schedule and 55 projects are delayed .9 projects do not have fixed dates of commissioning.

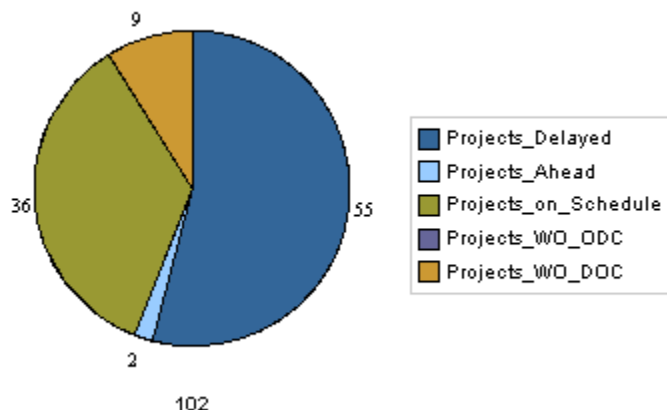

Investment Scenario

The Total Original cost of implementation of 102 projects when sanctioned, was of the order of Rs. 248230.58 crore but this was subsequently revised to Rs. 265932.27 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till January, 2014 is Rs. 132098.62 crore, which is 49.7% of the revised cost of the projects.

Figures are in Rs. Crore

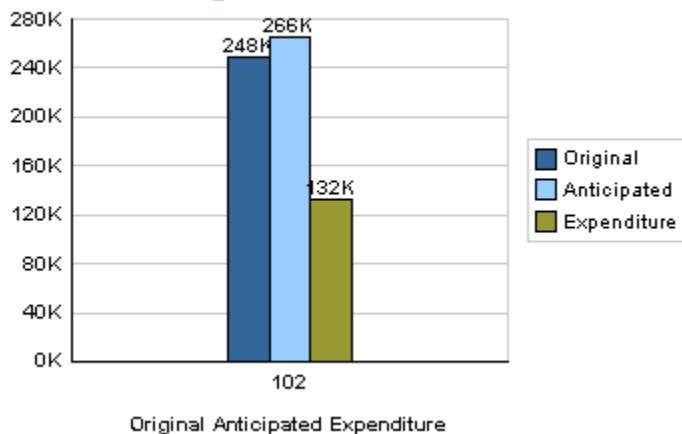

Sector wise current status of projects on the Flash Report

PETROLEUM


Current Status:

Number of Projects	82
Number of Projects On Schedule	16
Number of Projects Delayed	57

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 82 projects, 16 projects are on schedule and 57 projects are delayed .8 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

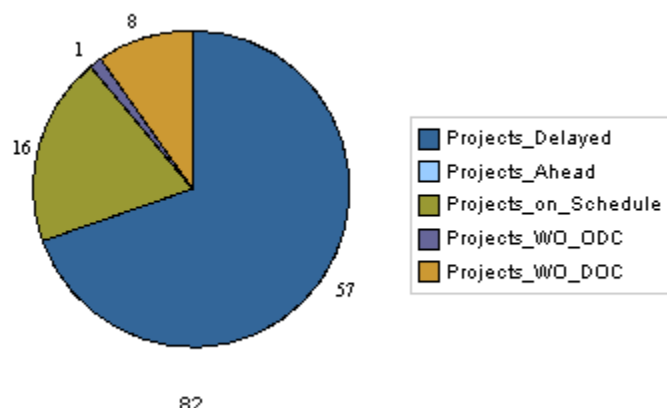

Investment Scenario

The Total Original cost of implementation of 82 projects when sanctioned, was of the order of Rs. 181913.11 crore but this was subsequently revised to Rs. 197623.79 crore implying a cost overrun of 8.6%. The expenditure incurred on these projects till January, 2014 is Rs. 102090.2 crore, which is 51.7% of the revised cost of the projects.

Figures are in Rs. Crore

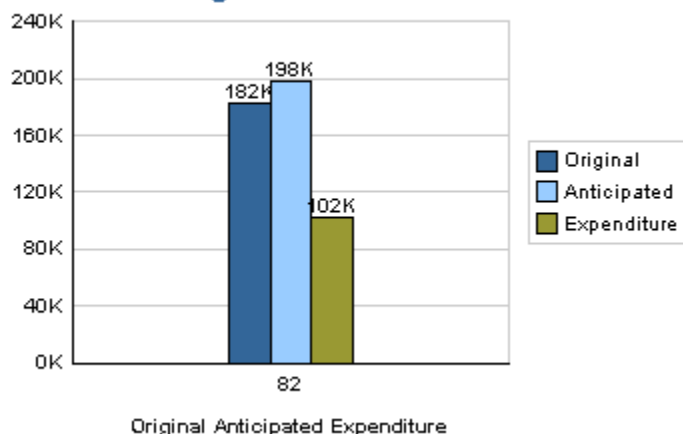

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	20
Number of Projects On Schedule	4
Number of Projects Delayed	13
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 1 project are ahead of schedule, 4 projects are on schedule and 13 projects are delayed .2 projects do not have fixed dates of commissioning.

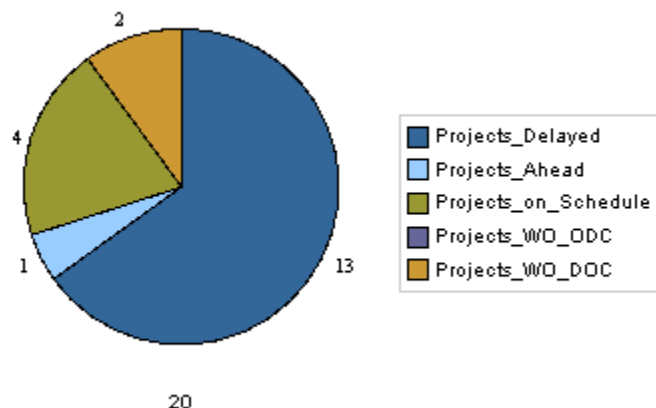

Investment Scenario

The Total Original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 65959.26 crore but this was subsequently revised to Rs. 72162.25 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till January, 2014 is Rs. 57573.37 crore, which is 79.8% of the revised cost of the projects.

Figures are in Rs. Crore

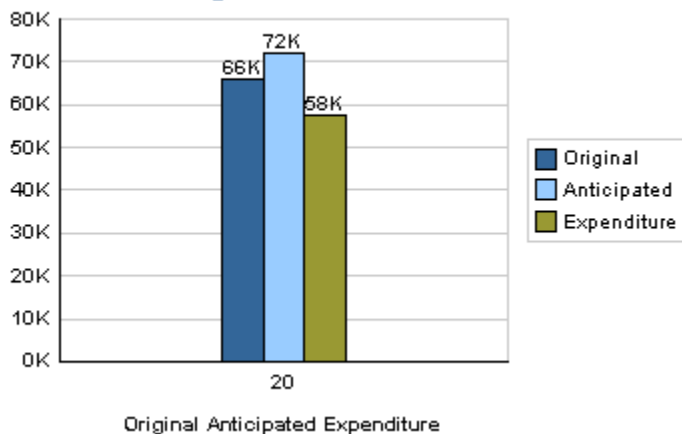

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	55
Number of Projects On Schedule	23
Number of Projects Delayed	29

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 23 projects are on schedule and 29 projects are delayed .3 projects do not have fixed dates of commissioning.

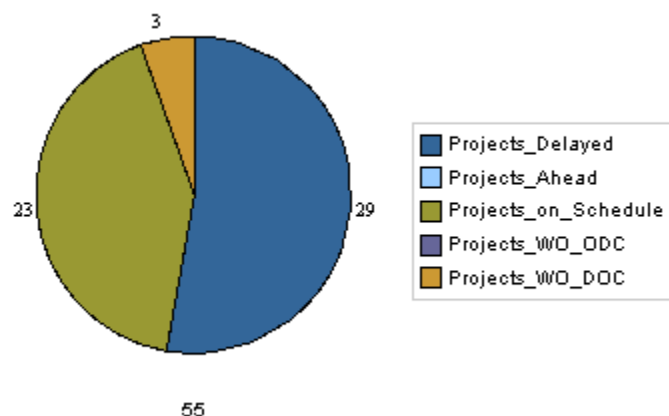

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41525.17 crore implying a cost overrun of 8.9%. The expenditure incurred on these projects till January, 2014 is Rs. 16436.87 crore, which is 39.6% of the revised cost of the projects.

Figures are in Rs. Crore

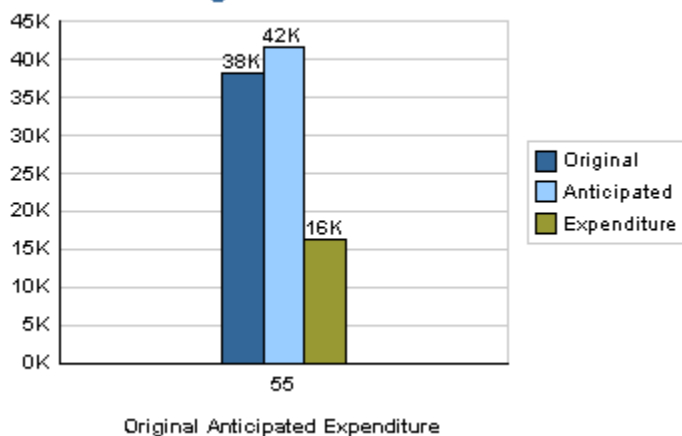

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

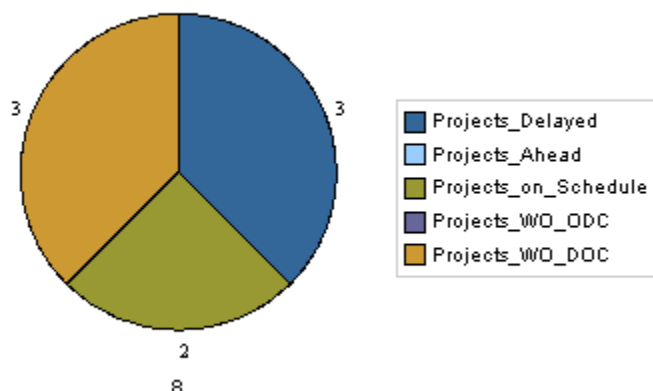

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6946 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till January, 2014 is Rs. 5574.92 crore, which is 80.3% of the revised cost of the projects.

Figures are in Rs. Crore

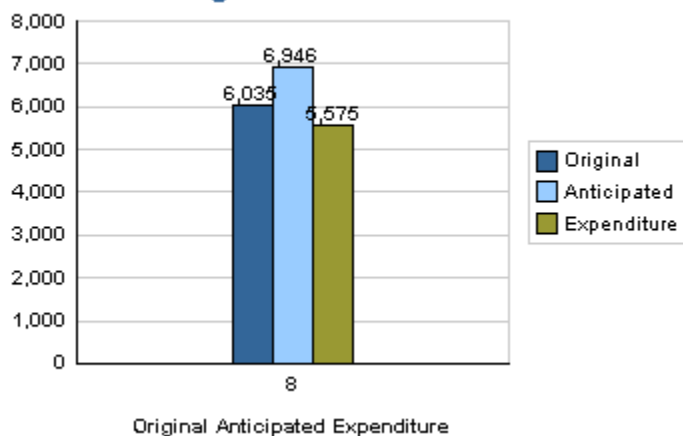

Sector wise current status of projects on the Flash Report

ATOMIC ENERGY


Current Status:

Number of Projects 4

Number of Projects Delayed 4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

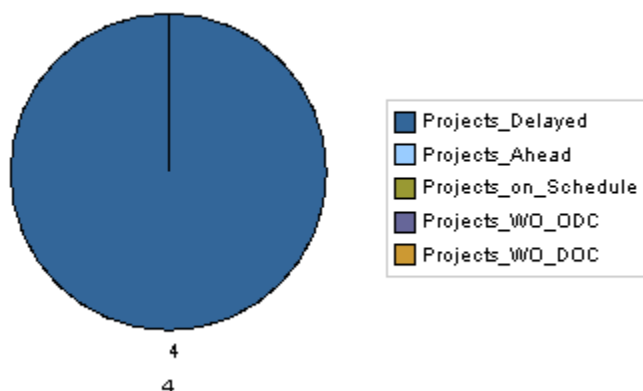**Investment Scenario**

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till January, 2014 is Rs. 21755.16 crore, which is 46.6% of the revised cost of the projects.

Figures are in Rs. Crore

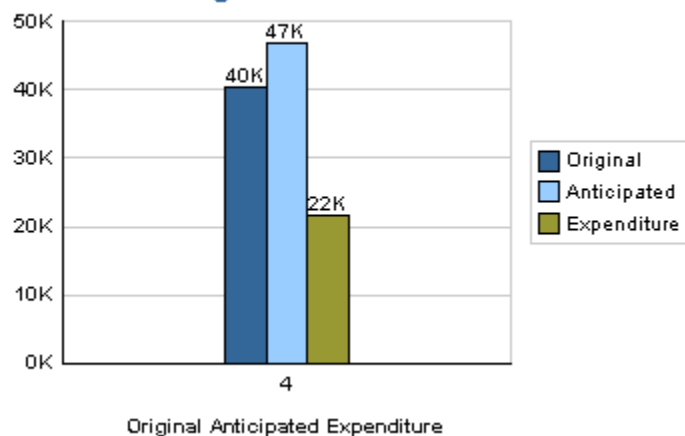

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	47	37177.32	45353.92	24320.81
2	ARUNACHAL PRADESH	4	9512.22	16857.31	10365.62
3	ASSAM	41	24155.49	39221.76	24103.74
4	BIHAR	45	32339.04	40759.96	29152.84
5	CHANDIGARH	1	452.00	452.00	199.83
6	CHHATISGARH	22	56368.80	57453.40	23608.46
7	DELHI	4	41533.88	41531.33	7026.45
8	GOA	1	335.61	388.53	264.45
9	GUJARAT	33	38022.74	39924.34	11345.21
10	HARYANA	9	4399.88	6104.07	7239.27
11	HIMACHAL PRADESH	5	13845.21	19510.58	15048.29
12	JAMMU AND KASHMIR	8	13694.69	32976.56	16558.48
13	JHARKHAND	27	16118.82	20384.09	10831.05
14	KARNATAKA	34	53120.49	65228.53	27665.14
15	KERALA	12	22610.65	25135.43	8148.41
16	MADHYA PRADESH	19	30777.43	32003.81	10605.45
17	MAHARASHTRA	53	94835.18	109387.66	52982.29
18	MANIPUR	1	727.56	5996.00	1924.82
19	MEGHALAYA	3	4845.02	4845.02	889.63
20	MIZORAM	2	1532.97	3307.11	641.67
21	MULTI STATE	175	180260.59	204015.61	82520.53
22	NAGALAND	2	5124.00	6720.57	8.98
23	ODISHA	29	55889.04	62601.07	41204.06
24	PUNJAB	4	1680.20	1680.20	2471.04
25	RAJASTHAN	25	25380.48	25805.94	9277.34
26	SIKKIM	2	1648.94	3684.88	321.40
27	TAMIL NADU	38	51742.73	67974.43	44665.97
28	TRIPURA	6	2966.26	4737.26	2404.20
29	UTTAR PRADESH	28	21357.79	25954.00	13687.52
30	UTTARAKHAND	6	7844.04	9331.46	2782.47
31	WEST BENGAL	36	49851.13	61412.42	31723.55
TOTAL		722	900150.20	1080739.25	513988.97

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	17,089
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	4,666.16
3	IOR LAKWA - LAKHMANI (ONGCL)	PETROLEUM	09/2001	345.1	663.69	743.72
4	IOR GELEKI (ONGCL)	PETROLEUM	09/2001	390.09	1674.11	1,759.52
5	IOR, RUDRASAGAR (ONGCL)	PETROLEUM	09/2001	113.9	438.85	452.91
6	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,239.17
7	KOLDAM HEP (NTPC)	POWER	10/2002	4,527.15	-	5,553
8	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,468.31
9	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,712.05
10	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	9,036
11	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,436.24
12	URI H.E.P STAGE -II (NHPC)	POWER	08/2005	1,729.29	-	2,096.81
13	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	652.71
14	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,822.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	LANJHIGARH- JUNAGARH NL(ECOR)	RAILWAYS	04/1993	100	142.98	234.32
16	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
17	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	412.91	794.35
18	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	767.01
19	NANDYAL-YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	669.71
20	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,000	1500	2,993.95
21	KOTTUR-HARIHAR(NL), (SWR)	RAILWAYS	04/1995	65.94	302.23	362.56
22	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	355.23
23	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	726.24
24	KATI HAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	100	492.98	742.02
25	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	383.74
26	JALANDHAR-PATHANKOT- JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	409	625.3	838.53
27	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	561.28
28	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,543.15

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	907.69	3156.32	3,522.47
30	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	228.09	287.69
31	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	190.81	238.56	510.66
32	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	298.57
33	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	1,924.82
34	DANIAWAN-BIHARSARIF (NL), ECR	RAILWAYS	04/2001	104.79	-	138.93
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,500.48
36	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	270.46
37	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	273.49
38	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	-	260.3
39	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	240.09
40	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	ROAD TRANSPORT AND HIGHWAYS	12/2003	166.27	-	198.8
41	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	262.98
42	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	292.51

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	487.69
44	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	281.66
45	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	345.3
46	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,483.65
47	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	15,487.23
48	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	293.12
49	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	PETROLEUM	04/2008	825	-	1,514.22
50	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	2,952.8
51	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	794.02
52	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	714.2
53	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	148.68
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	444.11
55	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	783.15
56	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	727.35

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	416.04
58	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	RAILWAYS	09/1996	156	156	391.24
59	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	482.7	565.61
60	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	3,872.29
61	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	461.67
62	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	558.03
63	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	785.31
64	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	240.38
65	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	266.48
66	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	460.61
67	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	951.99
68	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	532.1
69	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,033.06
70	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	204.59

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	199.27
72	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	791.4
73	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	308.16
74	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	303.05
75	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	257.33
76	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,129.29
77	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	308.77
78	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	661.01
79	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,333.25
80	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	1,925.62
81	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,802
82	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,127.12
83	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.24
84	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.91

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
86	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,979.78
87	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	ROAD TRANSPORT AND HIGHWAYS	09/2010	946	-	1,842.77
88	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,260.86
89	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	948.41
90	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	772.4
91	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	857.7
92	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	938.4
93	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,161.4
94	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	621.67
95	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,325.75
96	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	723.34
97	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	1,936
98	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	597.22

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	548.4
100	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	394.61
101	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,356.04
102	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	848.81
103	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,153.77
104	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	1,294.08
105	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	554.09
106	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	332.5
107	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	662.29
108	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	714.59
109	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	647.94
110	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	454.33
111	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	528.15
112	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	958.69

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	683.48
114	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,388
115	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,324.51
116	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	268.96
117	ACQUISITION OF TWO NOS. OF 3060 DWT	SHIPPING AND PORTS	04/2009	277.03	280	294.87
118	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

							(Jan,2014)
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
1	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48	160.48	14.26	09/2017 -	09/2014
	Total		160.48 -	160.48	14.26		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74	1,508.74	212.73	06/2016 -	12/2015
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	539.87	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	752.60		
	Grand Total		3,604.57	3,604.57	766.86		

List of projects without Original Date of Commissioning

(Jan,2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	-	0/0
	Total		10,281.00 -	10,281.00	.04				0/0
	<u>RAILWAYS</u>								
2	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	191.00	204.59	- -	01/2014	-	0/0
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	925.30	652.71	- -	02/2014	-	0/0
4	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	410.08	236.88	- -	03/2014	-	0/0
5	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	217.74	- -	03/2014	-	0/0
6	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	513.32	- -	03/2014	-	0/1
7	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	148.48	- -	03/2014	-	0/0
8	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	391.24	- -	03/2014	-	0/0
9	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	173.87	- -	03/2014	-	0/0
10	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	203.00	172.58	- -	03/2014	-	0/0
11	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	138.27	- -	04/2014	-	0/0
12	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	1,995.25	282.50	- -	12/2014	-	0/0
13	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.17	250.62	- -	03/2015	-	0/0
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	3,019.17	2,500.48	- -	03/2015	-	0/0
15	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
16	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	0.57	- -	03/2015	-	0/0
17	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	0.61	- -	03/2016	-	0/0

(Jan,2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	156.37	- -	03/2016	-	0/0
19	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	156.37	- -	03/2017	-	0/0
20	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	33.56	- -	03/2017	-	0/0
21	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	64.93	- -	03/2017	-	0/0
22	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	18.16	- 12/2017	12/2017	0(R3)	0/0
	Total		5,862.83 -	12,811.29	6,315.07				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
23	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
	Total		671.00 -	671.00	938.40				2/3
	Grand Total		16,814.83	23,763.29	7,253.51				2/4

List of projects without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>COAL</u>				
4	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 -	03/2013 -	-
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,ANDHRA PRADESH	10/2006	249.03 -	03/2012 -	-
6	JALLARAM SHAFT PROJECT - [N06000025]SCCL,ANDHRA PRADESH	09/2007	467.78 -	03/2013 -	-
	Total		1,905.12 -		
	<u>STEEL</u>				
7	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
8	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROCHEMICALS</u>				
9	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
10	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013
11	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	09/2012 -	09/2013
12	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	09/2013 -	09/2013
13	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	- -	-
15	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
16	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
17	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-
	Total		7,753.95 -		
	<u>POWER</u>				
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
19	MOUDA STPP - [N18000048]NTPC, MAHARASHTRA	11/2008	5,459.28 -	08/2012 -	03/2013
20	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC, MADHYA PRADESH	01/2009	5,915.00 -	10/2012 -	03/2013
21	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC, UTTAR PRADESH	01/2009	6,230.81 -	10/2012 -	10/2013
22	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	11/2011 -	12/2013
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	02/2012 -	12/2013
24	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL, MULTI STATE	09/2011	1,366.34 -	12/2013 -	-
25	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO, TRIPURA	07/2012	296.87 -	- -	-
26	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, KARNATAKA	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		22,563.99 -		
	<u>RAILWAYS</u>				
27	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007
28	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, ANDHRA PRADESH	07/1998	125.00 363.26	07/2008 -	07/2008
29	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009
30	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010
31	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
32	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010
33	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	120.90 663.10	06/1999 03/2011	03/2011
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
35	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
36	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
37	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012
38	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
39	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
40	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012
41	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO 50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
43	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
44	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, KARNATAKA	04/1995	65.94 302.23	- -	12/2012
45	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012
46	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
47	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 412.91	- -	01/2013
48	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013
49	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
50	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 167.73	03/2012 -	02/2013
51	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013
52	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 842.35	- -	03/2013
54	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 228.09	02/2011 02/2011	03/2013
55	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013
57	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 385.60	03/2013 -	03/2013
58	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 611.03	12/2011 11/2013	11/2013
59	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	12/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
61	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
62	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
63	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
64	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
65	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
66	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	02/2006 -	-
67	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
68	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
69	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
70	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
71	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
72	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-
73	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
74	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
75	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
76	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
77	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
78	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
79	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
80	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
81	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-
82	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
83	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
84	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
86	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
87	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
88	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
89	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
90	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
91	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
92	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
93	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
94	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
95	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-
96	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
97	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
98	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
99	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
100	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
101	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
102	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
103	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
104	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-
105	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
106	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
107	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
108	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
109	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
110	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
111	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
112	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
113	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
114	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
115	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
116	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
117	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
118	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
119	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
120	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
121	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
122	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
123	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
124	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
125	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
126	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
127	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
128	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	-
129	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
130	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
131	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-
132	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
133	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
134	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
135	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
136	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
137	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
138	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
139	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
140	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
141	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
142	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
143	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
144	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
145	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
146	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
147	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
148	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
149	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
150	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
151	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-
152	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
153	BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
154	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
155	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
156	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
158	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
159	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
160	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
161	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
162	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
163	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
164	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
165	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
166	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
167	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
168	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
169	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
170	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-
171	KONDAPALLI-KOTHAGUDEM - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-
172	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-
173	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-
174	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-
175	GUDUR-DURGARAJPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-
176	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-
177	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-
178	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
179	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
180	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
181	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
182	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
183	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
184	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
185	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
186	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
187	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
188	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-
189	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-
190	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-
191	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
192	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-
193	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-
194	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
195	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-
196	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
197	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
198	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
199	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
200	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
201	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
202	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
203	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
204	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
205	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
207	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-
208	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
209	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
210	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
211	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 356.87	- 03/2010	-
212	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	- -	-
213	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
214	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
215	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-
216	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-
217	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
218	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-
219	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-
220	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
221	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	- -	-
222	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-
223	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-
224	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-
225	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	- -	-
226	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	- -	-
227	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDIL'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-
228	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-
229	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-
230	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
231	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	03/2012 -	-
232	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
233	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
234	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
235	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
236	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
	Total		95,839.24 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
237	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	10/2013 -	10/2013
238	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	12/2013
239	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013
240	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
241	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	12/2013
242	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2013
243	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-
244	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-
245	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-
246	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
247	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-
248	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-
249	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-
250	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-
251	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-
252	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
253	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
254	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-
255	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
256	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
257	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
258	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-
259	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
260	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-
261	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-
262	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
263	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-
264	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-
265	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-
266	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
267	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-
268	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-
269	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
270	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
271	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
272	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
273	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-
274	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-
275	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
276	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-
277	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
278	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
279	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
280	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-
281	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
282	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	- -	-
283	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
284	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
285	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
286	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
287	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
288	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	-
289	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
290	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
291	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
292	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
293	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-
294	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-
295	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-
296	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
297	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
298	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-
299	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-
300	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
301	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-
302	4-LANING OF FARAHA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-
303	4-LANING OF BRAHMAPORE-FARAHA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
304	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-
305	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
306	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
307	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
	Total		47,124.04 -		
	<u>SHIPPING AND PORTS</u>				
308	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
309	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
310	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
311	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
312	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
313	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
314	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
315	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
316	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
317	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
318	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
319	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
320	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
321	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
322	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		12,760.79 -		
	<u>TELECOMMUNICATIONS</u>				

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
323	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
324	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
325	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
326	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
327	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEPOE EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-
328	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,061.14 -		
	<u>URBAN DEVELOPMENT</u>				
329	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
330	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>WATER RESOURCES</u>				
331	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		208,359.47		

List of on schedule Projects w.r.t. Original Schedule

(Jan,2014)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	199.83	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	199.85		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	163.23	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	57.53	03/2015 -	03/2015
8	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.57	03/2016 -	03/2016
9	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	59.12	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.17	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	3.62	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.49	03/2016 -	03/2016
14	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	MURADIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.04	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.66	03/2020 -	03/2020
20	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	53.88	03/2014 -	03/2014

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016
22	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
23	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
24	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	158.53	03/2017 -	03/2017
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
	Total		11,169.15 -	10,797.81	1,775.14		
	<u>PETROLEUM</u>						
26	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	490.10	03/2015 -	03/2015
27	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	36.23	01/2016 -	01/2016
28	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	-	03/2015 -	03/2015
29	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	99.11	06/2014 -	06/2014
30	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	2.11	04/2015 -	04/2015
31	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
32	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
33	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	48.93	12/2014 -	12/2014
34	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	111.01	08/2015 -	08/2015
35	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	56.41	07/2015 -	07/2015
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	181.48	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	428.26	11/2015 -	11/2015
38	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	165.00	116.65	03/2014 -	03/2014
39	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	879.55	05/2014 -	05/2014
40	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,844.55	05/2015 -	05/2015
41	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	186.78	12/2014 -	12/2014
	Total		20,596.99 -	20,040.66	4,481.17		
	<u>POWER</u>						

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	1,306.06	05/2014 -	05/2014
43	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	9/2011	1,940.13 -	1,940.13	1,174.99	09/2014 -	09/2014
44	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	1,228.88	08/2014 -	08/2014
45	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	202.63	08/2014 -	08/2014
46	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	618.38	02/2015 -	02/2015
47	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	812.46	10/2014 -	10/2014
48	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160	2/2014	243.53 -	243.53	-	08/2014 -	08/2014
50	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,889.00	11/2016 -	11/2016
51	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	1,623.00	09/2016 -	09/2016
52	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	2,692.00	12/2016 -	12/2016
53	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	532.78	11/2014 -	11/2014
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	278.18	11/2014 -	11/2014
55	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	541.52	08/2014 -	08/2014
56	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	42.36	06/2014 -	06/2014
57	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	100.33	03/2014 -	03/2014
58	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
61	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
62	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016
63	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
64	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
66	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	912.00	09/2017 -	09/2017
67	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	336.37	06/2015 -	06/2015
68	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	11.89	12/2015 -	12/2015
69	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
70	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	44.00	08/2017 -	08/2017
71	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,227.00	05/2017 -	05/2017
72	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	4.86	10/2014 -	10/2014
73	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	6.51	10/2014 -	10/2014
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	169.16	03/2015 -	03/2015
75	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	736.00	08/2015 -	08/2015
76	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	75.80	08/2014 -	08/2014
77	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	590.66	01/2015 -	01/2015
	Total		88,254.53 -	88,254.53	17,156.82		
	<u>RAILWAYS</u>						
78	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	111.21	02/2015 -	02/2015
79	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	273.79	03/2016 -	03/2016
80	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,619.02 -	2,913.51	372.15	03/2016 -	03/2016
81	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	653.47	257.47	03/2014 -	03/2014
82	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	751.93	03/2014 -	03/2014
83	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
84	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	150.62	03/2017 -	03/2017
85	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	4/2009	257.42 -	257.42	33.79	03/2014 -	03/2014
86	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
87	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	9.97	03/2015 -	03/2015
88	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	388.67	56.07	12/2015 -	12/2015
89	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	1.47	02/2019 -	02/2019
90	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
91	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]	4/2008	516.23 -	516.23	452.07	03/2014 -	03/2014
92	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	45.67	03/2015 -	03/2015
	Total		18,354.28 -	23,440.94	2,519.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
93	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014
94	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015
95	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014
96	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015
97	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	332.50	02/2014 -	02/2014
98	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
99	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	662.29	03/2014 -	03/2014
100	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014
101	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	582.60	09/2014 -	09/2014
102	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015
103	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
104	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	42.12	07/2014 -	07/2014
105	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014
106	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
108	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014
109	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
110	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015
111	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	256.68	09/2014 -	09/2014
112	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014
113	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014
114	NIROLI-ROXY-RAJAMUNDA - [N24000194]	7/2011	586.00 -	586.00	237.60	01/2014 -	01/2014
115	PUNE-SHOLAPUR,PKG-II - [N24000193]	9/2011	835.00 -	835.00	394.31	01/2014 -	01/2014
116	4-LANING OF BARHI-HAZARIBAGH - [N24000191]	2/2012	398.00 -	398.00	454.33	02/2014 -	02/2014
117	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014
118	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014
119	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014
120	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014
121	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015
122	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	413.79	04/2014 -	04/2014
123	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	3.26	07/2014 -	07/2014
124	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	283.09	10/2014 -	10/2014
125	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	588.54	07/2014 -	07/2014
126	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	100.21	01/2014 -	01/2014
127	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014
128	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014
129	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]	5/2011	664.00 -	664.00	611.24	02/2014 -	02/2014
130	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014
131	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	554.09	01/2014 -	01/2014

(Jan,2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		41,848.42 -	41,848.42	20,555.85		
	<u>STEEL</u>						
132	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	92.77	08/2014 -	08/2014
133	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	19.17	12/2014 -	12/2014
134	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	53.59	06/2015 -	06/2015
135	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016
	Total		1,128.46 -	1,146.27	172.44		
	<u>URBAN DEVELOPMENT</u>						
136	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	6,445.67	03/2016 -	03/2016
	Total		38,585.00 -	38,585.00	6,445.67		
	Grand Total		220,606.43	224,783.23	53,306.17		

List of Delayed Projects w.r.t. Original and Revised Schedule

(Jan,2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,089.00	12/2008 -	01/2015	73	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	21,755.16				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	264.45	05/2012 -	02/2014	21	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	256.77	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	1,042.27	521.22				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,869.96	06/2009 -	03/2014	57	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.77	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.25	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.36	03/2013 -	03/2014	12	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,991.82	03/2012 -	05/2014	26	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,159.43	03/2013 09/2012	03/2015	24	30
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	114.67	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.12	03/2010 -	03/2015	60	-
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	119.43	03/2013 -	03/2015	24	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	242.96	03/2012 -	03/2015	36	-
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.15	03/2012 -	03/2015	36	-
20	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	103.47	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,601.63	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,302.22	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44	-
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.44	03/2014 -	03/2016	24	-
25	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.81	12/2012 -	03/2016	39	-
26	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	31.29	03/2014 -	03/2016	24	-
27	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.19	03/2014 -	03/2016	24	-
28	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	125.63	03/2012 -	03/2016	48	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24	-
31	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60	-
32	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	141.54	03/2012 -	03/2016	48	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	249.46	12/2015 -	04/2018	28	-
	Total		25,052.78 -	28,822.24	14,588.67				
	STEEL								
37	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,729.46	10/2009 10/2012	03/2014	53	17
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.83	09/2008 12/2013	03/2014	66	3
39	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,356.27	12/2011 -	03/2014	27	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,487.23	12/2011 -	06/2014	30	-
41	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	302.63	09/2009 05/2012	07/2014	58	26
42	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	114.44	10/2013 -	08/2014	10	-
43	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	364.11	12/2011 09/2014	09/2014	33	0
44	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,605.40	03/2013 -	09/2014	18	-
45	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	356.11	04/2013 09/2014	09/2014	17	0
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,007.48	12/2012 -	12/2014	24	-
47	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	274.17	05/2013 01/2015	01/2015	20	0
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,982.04	03/2013 -	03/2015	24	-
49	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	100.11	11/2013 -	06/2015	19	-
	Total		64,208.32 -	70,162.28	56,839.28				
	<u>PETROLEUM</u>								
50	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95	11
51	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	737.45	03/2010 03/2012	02/2014	47	23
52	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,ASSAM	09/2001	345.10 663.69	750.00	743.72	03/2007 03/2014	03/2014	84	0
53	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
54	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46	12
55	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
56	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18	-
57	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,969.18	09/2011 03/2012	03/2014	30	24
58	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,514.22	04/2013 12/2013	03/2014	11	3
59	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	422.91	12/2013 -	03/2014	3	-
60	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,161.80	02/2014 -	03/2014	1	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
61	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	780.21	07/2012 -	03/2014	20	-
62	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,944.65	01/2012 -	03/2014	26	-
63	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12	-
64	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	244.03	04/2012 -	03/2014	23	-
65	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	03/2014	29	-
66	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	148.68	06/2012 -	03/2014	21	-
67	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21	-
68	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.50	08/2010 03/2012	05/2014	45	26
69	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32	24
70	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,888.97	06/2012 -	05/2014	23	-
71	DEVELOPMENT OF SB-14 FIELD - [N16000116]ONGC,MULTI STATE	01/2011	410.44 -	410.44	237.16	11/2012 -	05/2014	18	-
72	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	60.87	06/2012 -	05/2014	23	-
73	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2014	98	24
74	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22	-
75	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	450.52	05/2013 06/2014	06/2014	13	0
76	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	930.83	10/2011 -	06/2014	32	-
77	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	155.10	08/2013 -	09/2014	13	-
78	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
79	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
80	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	24,340.00	11/2012 -	12/2014	25	-
81	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	445.97	09/2011 -	12/2014	39	-
82	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	101.83	09/2012 -	12/2014	27	-
83	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	40.85	03/2014 -	12/2014	9	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
84	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
85	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24	12
86	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	268.90	03/2012 -	03/2015	36	-
87	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8	-
88	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	320.99	12/2014 -	03/2015	3	-
89	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	143.66	05/2014 -	05/2015	12	-
90	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	9.66	03/2015 -	06/2015	3	-
91	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	938.72	09/2012 -	08/2015	35	-
92	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8	-
93	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12	-
94	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPR,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	776.92	10/2011 -	10/2015	48	-
95	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KERALA	01/2006	993.00 1,693.00	1,693.00	1,084.00	01/2012 -	10/2015	45	-
96	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12	-
97	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
98	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
99	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.31	01/2014 -	12/2015	23	-
100	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,265.85	12/2015 -	05/2016	5	-
101	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
102	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49	-
103	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
104	ANKLESHWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
105	IOR GELEKI (ONGCL) - [160100216]ONGC,ASSAM	09/2001	390.09 1,674.11	1,674.11	1,759.52	03/2007 03/2017	03/2017	120	0
106	MEHSANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		143,281.17 -	160,093.47	94,257.92				
	<u>POWER</u>								
107	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	161.64	06/2012 -	01/2014	19	-
108	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,MULTI STATE	10/2010	182.68 -	182.68	139.73	01/2013 -	02/2014	13	-
110	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,265.17	10/2010 -	03/2014	41	-
111	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	466.16	09/2010 -	03/2014	42	-
112	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	160.75	11/2011 -	03/2014	28	-
113	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,086.34	08/2012 -	03/2014	19	-
114	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,133.03	08/2012 -	03/2014	19	-
115	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	622.71	11/2012 -	03/2014	16	-
116	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3	-
117	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	112.01	04/2013 -	03/2014	11	-
118	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	145.81	07/2013 -	03/2014	8	-
119	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	356.37	10/2013 -	04/2014	6	-
120	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.78	10/2009 -	05/2014	55	-
121	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,402.61	03/2013 -	05/2014	14	-
122	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,201.02	12/2013 -	05/2014	5	-
123	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	2,952.80	01/2012 -	06/2014	29	-
124	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	375.59	02/2014 -	06/2014	4	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
125	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	129.10	01/2014 -	06/2014	5	-
126	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	225.45	11/2013 -	09/2014	10	-
127	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	252.39	06/2014 -	09/2014	3	-
128	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	714.20	07/2013 -	11/2014	16	-
129	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37	-
130	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	946.16	08/2012 -	12/2014	28	-
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	358.95	07/2013 -	12/2014	17	-
132	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 -	2,127.51	1,570.92	07/2014 -	12/2014	5	-
133	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,683.00	08/2013 -	02/2015	18	-
134	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,641.19	10/2012 -	03/2015	29	-
135	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,883.00	11/2012 -	03/2015	28	-
136	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,555.07	12/2012 -	03/2015	27	-
137	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	962.89	04/2013 -	03/2015	23	-
138	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12	-
139	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	789.56	11/2012 -	03/2015	28	-
140	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,553.00	04/2009 -	05/2015	73	-
141	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 -	1,746.65	257.99	08/2014 -	05/2015	9	-
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	77.98	04/2015 -	05/2015	1	-
143	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,570.34	08/2013 -	06/2015	22	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
144	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	63.72	01/2013 -	06/2015	29	-
145	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,140.80	11/2013 -	06/2015	19	-
146	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	723.27	08/2014 -	06/2015	10	-
147	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,264.35	10/2014 -	06/2015	8	-
148	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,436.24	09/2009 -	07/2015	70	-
149	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	794.02	08/2013 09/2015	09/2015	25	0
150	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	431.56	01/2015 -	12/2015	11	-
151	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	01/2011	913.63 -	913.63	512.83	07/2006 12/2015	12/2015	113	0
152	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	1,353.98	06/2015 -	12/2015	6	-
153	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	383.30	07/2014 -	05/2016	22	-
154	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 -	4,375.35	4,252.00	07/2011 -	06/2016	59	-
155	KISHANGANGA HEP - [N18000031]NHPC, JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,118.93	01/2016 -	11/2016	10	-
156	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	576.41	07/2010 02/2016	02/2017	79	12
157	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,712.05	12/2009 06/2016	03/2017	87	9
158	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	12/2003	8,692.97 -	8,693.00	9,036.00	12/2009 -	03/2017	87	-
159	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 -	2,978.48	1,962.00	03/2013 -	03/2017	48	-
160	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,468.31	09/2010 -	06/2018	93	-
161	PARBATI HEP (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,239.17	09/2009 -	07/2018	106	-
	Total		133,967.97 -	150,327.56	98,739.73				
	<u>RAILWAYS</u>								
162	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	608.02	580.26	03/1994 -	01/2014	238	-
163	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, ODISHA	04/1993	100.00 142.98	227.94	234.32	03/2002 -	02/2014	143	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
164	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	398.93	12/2009 03/2011	03/2014	51	36
165	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
166	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	565.61	03/2013 -	03/2014	12	-
167	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12	-
168	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	298.57	02/2009 02/2009	08/2014	66	66
169	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	270.46	03/2009 03/2009	08/2014	65	65
170	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.71	12/2008 -	09/2014	69	-
171	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	338.87	03/2004 12/2010	12/2014	129	48
172	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126	-
173	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,291.27	03/2009 12/2012	12/2014	69	24
174	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	189.71	12/2012 -	12/2014	24	-
175	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
176	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96	96
177	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.02	12/2010 12/2010	03/2015	51	51
178	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	261.04	06/2013 06/2013	03/2015	21	21
179	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	1,966.06	10/2007 12/2012	12/2015	98	36
180	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	783.15	03/2010 -	12/2015	69	-
181	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9	-
182	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	62.70	03/2014 -	03/2016	24	-
183	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.61	04/2012 -	03/2016	47	-
184	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132	59
185	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	68.18	03/2016 -	06/2016	3	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
186	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141	96
187	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,506.46	03/2014 03/2016	12/2016	33	9
188	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 325.00	1,116.53	250.35	03/2010 03/2017	03/2017	84	0
189	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	128.84	04/2014 -	03/2017	35	-
190	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,375.42	64.63	12/2015 -	03/2017	15	-
191	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	2,446.57	8.98	03/2015 -	03/2017	24	-
192	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,872.29	03/2009 -	03/2017	96	-
193	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	951.99	03/2007 -	03/2017	120	-
194	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
195	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,993.95	04/2008 03/2014	12/2017	116	45
196	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	2,483.04	1,543.15	12/2008 -	03/2018	111	-
197	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	331.40	131.15	12/2012 -	03/2018	63	-
198	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,741.00	533.44	03/2014 -	03/2019	60	-
199	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	5,996.00	1,924.82	03/2011 03/2014	03/2020	108	72
	Total		28,661.14 -	80,279.63	33,411.97				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
200	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2	-
201	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 -	157.42	260.30	09/2007 03/2014	03/2014	78	0
202	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	-	04/2008 03/2014	03/2014	71	0
203	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46	-
204	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5	-
205	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5	-
206	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
207	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [N240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	-	02/2009 -	05/2014	63	-
208	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	-	06/2008 05/2014	05/2014	71	0
209	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	-	09/2007 -	05/2014	80	-
210	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	1,294.08	08/2013 06/2014	06/2014	10	0
211	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	-	05/2008 07/2014	07/2014	74	0
212	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10	-
213	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [N240106278]NHAI,ASSAM	12/2003	199.81 382.02	382.02	107.55	04/2009 12/2014	12/2014	68	0
214	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [N240106279]NHAI,ASSAM	12/2003	167.64 265.53	265.63	92.14	11/2008 12/2014	12/2014	73	0
215	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [N240106280]NHAI,ASSAM	12/2003	155.04 241.28	241.28	151.77	11/2008 12/2014	12/2014	73	0
216	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [N240106281]NHAI,ASSAM	12/2003	200.00 247.43	247.43	180.36	04/2009 12/2014	12/2014	68	0
217	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	-	03/2008 01/2015	01/2015	82	0
218	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	-	04/2008 01/2015	01/2015	81	0
219	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	208.00	-	04/2008 01/2015	01/2015	81	0
220	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	-	04/2010 09/2015	09/2015	65	0
	Total		6,793.69 -	7,637.52	4,658.83				
	<u>SHIPPING AND PORTS</u>								
221	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 02/2014	04/2014	2	2
222	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99	0
223	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
224	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	990.28	12/2010 09/2012	03/2015	51	30
	Total		2,856.33 -	3,535.79	1,664.34				
	<u>TELECOMMUNICATIONS</u>								

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
225	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	03/2014	57	-
226	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	03/2014	62	-
227	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
228	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	03/2014	34	-
	Total		2,018.15 -	1,843.90	531.21				
	URBAN DEVELOPMENT								
229	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	529.69	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	529.69				
	Grand Total		450,764.90	552,964.66	327,498.02				

List of Projects without Milestones w.r.t. Original Schedule

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	02/2014	0/0
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	03/2015	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	03/2015	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
	Total		4,092.95 -			0/0
	<u>COAL</u>					
8	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
	<u>STEEL</u>					
10	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	05/2016 -	05/2016	0/0
	Total		245.67 -			0/0
	<u>PETROLEUM</u>					
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
12	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	03/2010 03/2012	02/2014	0/0
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
14	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	07/2010 05/2012	03/2014	0/0
16	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	03/2014	0/0
17	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	12/2013 -	03/2014	0/0
18	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	03/2014	0/0
19	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	03/2014	0/0
20	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	06/2012 -	03/2014	0/0
21	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,ASSAM	08/2008	126.18 -	06/2012 -	03/2014	0/0
22	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
23	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	06/2014	0/0
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	06/2014	0/0
25	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	06/2014 -	06/2014	0/0
26	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	12/2014	0/0
27	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2014	0/0
28	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	09/2012 -	12/2014	0/0
29	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	12/2014 -	12/2014	0/0
30	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	12/2014 -	03/2015	0/0
31	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
32	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	- -	04/2015	0/0
33	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	07/2015 -	07/2015	0/0
34	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	08/2015 -	08/2015	0/0
35	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	12/2014 -	08/2015	0/0
36	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	10/2014 -	10/2015	0/0
37	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
38	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
39	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0

							(Jan,2014)
			Date of Commissioning				
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total	
1	2	3	4	5	6	7	
40	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0	
41	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	01/2016	0/0	
42	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0	
43	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	12/2015 -	05/2016	0/0	
44	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0	
45	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	09/2012 -	10/2016	0/0	
46	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2016	0/0	
47	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2016	0/0	
48	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	03/2017	0/0	
49	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	- -	-	0/0	
50	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0	
	Total		89,788.13 -			0/0	
	<u>POWER</u>						
51	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,ANDHRA PRADESH	02/2014	243.53 -	08/2014 -	08/2014	0/0	
52	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	09/2014	0/0	
53	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	06/2015 -	06/2015	0/0	
54	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,ANDHRA PRADESH	06/2012	1,909.24 -	06/2015 -	06/2015	0/0	
55	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	12/2015 -	12/2015	0/0	
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	03/2016 -	03/2016	0/0	
57	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0	
58	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0	
59	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	05/2016 -	05/2016	0/0	
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	06/2016 -	06/2016	0/0	
61	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	06/2016 -	06/2016	0/0	

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
62	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	11/2016 -	11/2016	0/0
63	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	06/2018	0/0
	Total		16,077.27 -			0/0
	<u>RAILWAYS</u>					
64	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
65	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,ANDHRA PRADESH	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
66	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
67	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
68	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
69	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
70	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
71	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
72	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
73	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
74	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
75	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
76	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
77	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012	0/0
78	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
79	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
80	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
81	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,KARNATAKA	04/1995	65.94 302.23	- -	12/2012	0/0
82	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
83	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
84	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 412.91	- -	01/2013	0/0
85	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
86	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
87	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
88	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
89	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2013	0/0
90	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
91	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
92	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
93	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
94	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
95	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
96	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	01/2014	0/0
97	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	01/2014	0/0
98	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,ANDHRA PRADESH	12/1994	124.43 495.68	- -	02/2014	0/0
99	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	03/2002 -	02/2014	0/0
100	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	151.84 410.08	- -	03/2014	0/0
101	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014	0/0
102	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	03/2014	0/0
103	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
104	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014	0/0
105	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
106	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
107	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
108	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 516.23	03/2014 -	03/2014	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
109	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
110	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014	0/0
111	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
112	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
113	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
114	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	06/2013 -	06/2014	0/0
115	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
116	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
117	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
118	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
119	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	12/2014	0/0
120	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	355.38 470.21	- -	12/2014	0/0
121	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
122	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2014	0/0
123	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
124	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
125	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0
126	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
127	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
128	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	- -	03/2015	0/0
129	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2015	0/0
130	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
131	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
132	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	- -	03/2015	0/0
133	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
134	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
135	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2015	0/0
137	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	12/2015	0/0
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2016	0/0
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
140	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
141	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
142	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
143	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
144	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP, ANDHRA PRADESH	04/2012	632.68 -	04/2012 -	03/2016	0/0
145	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
147	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
148	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
149	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
150	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
151	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
152	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
153	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
154	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
155	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
156	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
157	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR, ASSAM	04/2011	312.12 -	- -	03/2017	0/0
158	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
159	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
160	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
161	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2017	0/0
162	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0
163	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
164	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	12/2012 -	03/2018	0/0
165	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
166	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2019	0/0
167	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
168	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2020	0/0
169	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
170	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
171	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
172	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
173	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
174	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
175	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 261.70	02/2006 -	-	0/0
176	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
177	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
178	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
179	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
180	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
181	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-	0/0
182	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
183	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
184	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
185	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
186	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
187	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
188	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
189	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
190	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
191	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
192	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
193	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
194	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
195	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
196	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
197	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
198	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
199	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
200	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
201	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
202	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
203	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-	0/0
204	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
205	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-	0/0
206	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
207	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
208	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
209	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
210	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
211	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
212	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
213	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
214	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
215	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
216	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
217	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
218	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
219	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
220	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
221	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
222	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
223	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
224	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
225	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
226	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
227	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
228	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
229	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
230	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
231	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
232	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
233	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
234	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
235	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
236	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
237	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	-	0/0
238	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
239	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
240	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
241	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
242	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
243	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
244	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0
245	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
246	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
247	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0
248	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
249	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
250	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
251	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
252	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
253	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
254	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR -CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
255	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
256	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
257	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
258	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
259	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
260	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-	0/0
261	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
262	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
263	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
264	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
265	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
266	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
267	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
268	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
269	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
270	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
271	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
272	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
273	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
274	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
275	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
276	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
277	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
278	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
279	MANUGURU-RAMAGUNDAM - [N22000259](SCR),ANDHRA PRADESH	04/2013	1,112.00 -	- -	-	0/0
280	KONDAPALLI-KOTHAGUDEM - [N22000260](SCR),ANDHRA PRADESH	04/2013	723.00 -	- -	-	0/0
281	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
282	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
283	BHADRACHALAM-KOVVUR - [N22000264](SCR),ANDHRA PRADESH	04/2012	923.23 -	- -	-	0/0
284	GUDUR-DURGARAJPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
285	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	289.79 -	- -	-	0/0
286	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-	0/0
287	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
288	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
289	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
290	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
291	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
292	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
293	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
294	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
295	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
296	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
297	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
298	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
299	AKKANAPET-MEDAK - [N22000285](SCR),ANDHRA PRADESH	04/2012	153.00 -	- -	-	0/0
300	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
301	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),ANDHRA PRADESH	04/2010	337.49 -	- -	-	0/0
302	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
303	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
304	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	165.65 -	- -	-	0/0
305	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
306	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
307	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0

				(Jan,2014)		
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
308	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
309	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
310	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
311	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
312	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
313	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
314	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
315	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
316	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,ANDHRA PRADESH	04/2007	313.24 -	01/1999 -	-	0/0
317	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
318	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
319	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
320	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 356.87	- 03/2010	-	0/0
321	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 514.68	- -	-	0/0
322	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
323	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
324	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-	0/0
325	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-	0/0
326	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
327	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-	0/0
328	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
329	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
330	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 901.62	- -	-	0/0
331	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-	0/0
332	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-	0/0

							(Jan,2014)
			Date of Commissioning				
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total	
1	2	3	4	5	6	7	
333	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-	0/0	
334	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 810.78	- -	-	0/0	
335	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,ANDHRA PRADESH	04/2006	378.56 671.82	- -	-	0/0	
336	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0	
337	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0	
338	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0	
339	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0	
340	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 603.04	03/2012 -	-	0/0	
341	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0	
342	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0	
343	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0	
344	DELHI-SOHNANU-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0	
345	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0	
	Total		148,114.09 -			0/0	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
346	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2014	0/0	
347	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,TAMIL NADU	04/2011	571.00 -	10/2013 -	10/2013	0/0	
348	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	12/2013	0/0	
349	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,ANDHRA PRADESH	02/2010	390.56 -	02/2012 -	06/2013	0/0	
350	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0	
351	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	12/2013	0/0	
352	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2013	0/0	
353	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	01/2014	0/0	
354	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	01/2014	0/0	

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
355	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	01/2014	0/0
356	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	01/2014	0/0
357	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	01/2014	0/0
358	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
359	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
360	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014	0/0
361	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 -	09/2007 03/2014	03/2014	0/0
362	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 03/2014	03/2014	0/0
363	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	03/2014	0/0
364	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
365	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	03/2014	0/0
366	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	03/2014	0/0
367	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	03/2014	0/0
368	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	04/2014	0/0
369	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	04/2014	0/0
370	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	04/2014	0/0
371	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	02/2009 -	05/2014	0/0
372	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 05/2014	05/2014	0/0
373	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	09/2007 -	05/2014	0/0
374	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
375	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
376	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	05/2014	0/0
377	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	06/2014	0/0
378	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
379	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	06/2014	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
380	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	06/2014	0/0
381	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2014	07/2014	0/0
382	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	07/2014	0/0
383	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	07/2014	0/0
384	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
385	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
386	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
387	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
388	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
389	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
390	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
391	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	10/2014	0/0
392	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
393	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
394	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 382.02	04/2009 12/2014	12/2014	0/0
395	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 265.53	11/2008 12/2014	12/2014	0/0
396	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	12/2014	0/0
397	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 247.43	04/2009 12/2014	12/2014	0/0
398	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2015	0/0
399	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2015	0/0
400	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 01/2015	01/2015	0/0
401	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2015	0/0
402	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
403	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
404	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
405	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
406	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
407	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2015	09/2015	0/0
408	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
409	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
410	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	-	0/0
411	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	-	0/0
412	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	-	0/0
413	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
414	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	-	0/0
415	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	-	0/0
416	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	-	0/0
417	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	-	0/0
418	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
419	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
420	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
421	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	-	0/0
422	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
423	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
424	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
425	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 385.15	09/2007 07/2011	-	0/0
426	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-	0/0
427	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	-	0/0
428	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	-	0/0
429	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	-	0/0

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
430	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	-	0/0
431	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	-	0/0
432	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
433	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	-	0/0
434	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	-	0/0
435	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
436	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
437	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
438	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
439	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	-	0/0
440	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
441	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
442	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
443	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	-	0/0
444	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	-	0/0
445	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
446	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
447	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
448	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
449	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
450	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
451	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
452	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
453	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	-	0/0
454	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	-	0/0

							(Jan,2014)
			Date of Commissioning				
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total	
1	2	3	4	5	6	7	
455	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	-	0/0	
456	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0	
457	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0	
458	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	-	0/0	
459	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	-	0/0	
460	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0	
461	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0	
462	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	-	0/0	
463	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	-	0/0	
464	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	-	0/0	
465	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0	
466	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0	
	Total		86,111.81 -			0/0	
	<u>SHIPPING AND PORTS</u>						
467	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0	
468	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0	
469	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0	
470	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0	
471	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0	
472	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0	
473	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0	
474	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0	
475	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0	
476	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0	

							(Jan,2014)
				Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total	
1	2	3	4	5	6	7	
477	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0	
478	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0	
479	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 02/2014	04/2014	0/0	
480	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0	
481	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0	
482	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2015	0/0	
483	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0	
484	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0	
	Total		15,462.28 -			0/0	
	<u>TELECOMMUNICATIONS</u>						
485	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0	
486	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0	
487	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0	
488	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	03/2014	0/0	
489	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	03/2014	0/0	
490	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 03/2012	03/2014	0/0	
491	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	03/2014	0/0	
492	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0	
493	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0	
494	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0	
	Total		5,079.29 -			0/0	
	<u>URBAN DEVELOPMENT</u>						
495	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0	
496	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0	

			(Jan,2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
497	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		41,193.18 -			0/0
	<u>WATER RESOURCES</u>					
498	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		408,277.72			0/0

List of ongoing projects having time and cost overrun w.r.t original schedule

(Jan,2014)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	01/2015	31.12	73
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2014	15.77	21
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09	57
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2014	34.63	26
	Total		7,938.86 -	35,222.15				
	<u>PETROLEUM</u>							
9	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42	95
10	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44	21
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85	21
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16	23
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00	12
14	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33	84

(Jan,2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
15	IOR GELEKI (ONGCL) - [N160100216	09/2001	390.09 -	1,674.11	03/2007 -	03/2017	329.16	120
16	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	06/2014	536.46	98
17	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25	3
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46	32
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
20	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	03/2014	121.45	11
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
22	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76	23
23	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
24	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50	63
25	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
26	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40	45
27	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27	46
28	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85	25
	Total		55,566.37 -	111,012.04				
	<u>POWER</u>							
29	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00	16
30	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
31	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49	70
32	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
33	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34	50
34	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69	10
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85	41

(Jan,2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
36	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32	19
37	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	05/2016	50.31	22
38	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
39	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
40	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	05/2015	41.69	73
41	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71	93
42	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87
	Total		40,760.37 -	168,132.00				
	<u>RAILWAYS</u>							
43	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01	96
44	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	03/2002 -	02/2014	127.94	143
45	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64	51
46	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67	51
47	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141
48	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69
49	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
50	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38	12
51	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33	9
52	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	01/2014	282.96	238
53	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
54	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03	24
55	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57	126
56	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41	63

(Jan,2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
57	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50	132
58	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
59	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58	129
60	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15	12
61	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
62	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35
63	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
64	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
65	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
66	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12	108
67	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75	111
68	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06	60
69	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83	24
70	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80	120
71	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
72	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62	116
73	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99	15
74	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34	96
75	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
76	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24	33
	Total		23,261.74 -	243,012.23				
	ROAD TRANSPORT AND HIGHWAYS							

(Jan,2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
77	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62	73
78	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45	73
79	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99	57
80	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19	68
81	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72	68
82	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47	80
83	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2015	42.25	65
84	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93	63
	Total		1,628.10 -	245,484.21				
	<u>SHIPPING AND PORTS</u>							
85	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
86	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93	2
87	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38	51
	Total		2,344.46 -	248,508.13				
	<u>STEEL</u>							
88	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	03/2014	100.63	66
89	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	09/2014	105.20	33
90	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41	53
91	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61	30
	Total		23,538.89 -	278,030.98				
	<u>TELECOMMUNICATIONS</u>							
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	06/2009 -	03/2014	6.42	57

(Jan,2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	Total		149.15 -	278,189.70				
	Grand Total		172,186.55	1,653,873.97				

List of ongoing projects having cost overrun w.r.t. to original schedule

(Jan,2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	01/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2014	15.77
	Total		4,086.12 -	27,943.66			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	03/2014	49.09
7	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
8	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
9	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2014	34.63
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,579.45 -	40,518.97			
	<u>PETROCHEMICALS</u>						
13	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	49,438.97			

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
14	IOR LAKWA - LAKHMANI (ONGCL) - [N160100215	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33
15	IOR GELEKI (ONGCL) - [N160100216	09/2001	390.09 -	1,674.11	03/2007 -	03/2017	329.16
16	IOR, RUDRASAGAR (ONGCL) - [N160100217	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42
17	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	06/2014	536.46
18	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85
23	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
24	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	03/2014	121.45
25	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
26	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
27	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
28	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
29	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	06/2014	54.46
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
36	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85
37	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		58,765.46 -	129,225.15			
	<u>POWER</u>						
38	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
39	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	05/2015	41.69
40	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71
41	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
42	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
43	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49
44	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
45	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
46	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34
47	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
48	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
49	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
50	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	05/2016	50.31
51	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
52	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
53	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
54	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00
	Total		48,595.39 -	195,522.23			
	<u>RAILWAYS</u>						

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	01/2014	282.96
56	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
57	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
58	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
59	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
60	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
61	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
62	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	02/2014	127.94
63	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
64	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
66	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
67	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
68	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
69	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
70	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
71	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
72	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
73	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
74	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
75	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
76	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
77	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
79	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	- -	12/2012	358.34
80	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57
81	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
82	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
83	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
84	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
85	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67
86	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64
87	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
88	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
89	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
90	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
92	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
93	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
94	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
95	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
96	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75
97	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
98	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
99	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
100	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
101	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
102	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
103	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
104	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44
105	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
106	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
107	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12
108	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
109	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
110	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
111	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
112	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
113	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
114	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
115	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
116	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
117	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49
118	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
119	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
120	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
121	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
122	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
123	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [220000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
124	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
125	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	186.92 -	261.70	02/2006 -	-	40.01
126	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
127	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
128	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
129	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
130	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
131	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
132	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
133	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
134	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	407.98	- -	03/2014	161.53
135	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
136	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
137	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2017	115.17
138	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
139	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
140	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
141	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
142	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
143	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
144	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06
145	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
146	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
148	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
150	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
151	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
152	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
153	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
154	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
155	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
156	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
157	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
158	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
159	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41
160	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
161	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
162	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
163	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
164	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
165	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
166	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH- UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
167	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
168	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
169	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
170	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
171	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
172	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
173	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
174	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
175	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
176	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
177	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
178	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
179	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
180	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
181	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
182	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
183	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
184	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
185	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
186	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
187	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
188	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
189	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,418.21	- -	-	171.08

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
190	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	-	47.95
191	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
192	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
193	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	1,604.00	- -	-	130.13
194	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
195	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
196	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
197	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
198	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
199	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
200	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]	04/2012	289.79 -	377.44	- -	-	30.25
201	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
202	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
203	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	444.18	- -	-	102.06
204	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		64,474.53 -	376,821.47			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
205	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	-	30.10
206	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	-	16.14
207	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93
208	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	382.02	04/2009 -	12/2014	91.19
209	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45
210	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	241.28	11/2008 -	12/2014	55.62

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
211	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	247.43	04/2009 -	12/2014	23.72
212	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	333.83	09/2007 -	05/2014	57.47
213	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99
214	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2015	42.25
215	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
216	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	385.15	09/2007 -	-	10.62
217	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		3,680.53 -	382,642.67			
	<u>SHIPPING AND PORTS</u>						
218	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
219	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
220	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,429.10	12/2010 -	03/2015	16.38
221	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
222	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
223	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
224	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
225	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
226	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	393,830.27			
	<u>STEEL</u>						
227	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	03/2014	41.41

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
228	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	09/2014	105.20
229	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	06/2006	108.00 -	216.68	09/2008 -	03/2014	100.63
230	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61
231	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
232	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48
233	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
	Total		24,237.98 -	424,301.24			
	<u>TELECOMMUNICATIONS</u>						
234	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	03/2014	6.42
235	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
236	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	425,782.69			
	<u>URBAN DEVELOPMENT</u>						
237	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
238	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	437,564.77			
	<u>WATER RESOURCES</u>						
239	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	438,751.77			
	Grand Total		251,618.10	3,345,290.86			

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Jan,2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
1	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP [N12000082]	10/2012	160.48	160.48	14.26	09/2017 -	09/2014
	Total		160.48 -	160.48	14.26		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144]	9/2012	1,508.74	1,508.74	212.73	06/2016 -	12/2015
3	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID [N18000137]	9/2012	1,935.35 -	1,935.35	539.87	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	752.60		
	Grand Total		3,604.57	3,604.57	766.86		

List of Projects on schedule w.r.t. Latest Schedule

(Jan,2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	199.83	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	199.85		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	163.23	03/2015 -	03/2015
4	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	613.44	03/2016 03/2016	03/2016
5	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
6	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
7	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.42	03/2016 -	03/2016
8	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	53.88	03/2014 -	03/2014
9	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
10	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.66	03/2020 -	03/2020
11	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	59.12	03/2016 -	03/2016
12	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.17	07/2016 -	07/2016
13	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	3.62	06/2015 -	06/2015
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	53.49	03/2016 -	03/2016
15	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
16	MURAI DIH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
17	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.04	03/2015 -	03/2015

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
19	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	265.57	03/2016 -	03/2016
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	57.53	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
23	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
24	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	158.53	03/2017 -	03/2017
25	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]	11/2006	168.97 -	168.97	44.08	03/2014 -	03/2014
	Total		11,169.15 -	10,797.81	1,775.14		
	<u>PETROLEUM</u>						
26	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	9/2001	345.10 -	750.00	743.72	03/2007 03/2014	03/2014
27	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	36.23	01/2016 -	01/2016
28	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	-	03/2015 -	03/2015
29	MARKETING TERMINAL AT PARADEEP - [N16000168]	7/2009	199.75 -	199.75	99.11	06/2014 -	06/2014
30	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	1,138.50	2.11	04/2015 -	04/2015
31	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
32	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
33	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	48.93	12/2014 -	12/2014
34	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	111.01	08/2015 -	08/2015
35	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	56.41	07/2015 -	07/2015
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	181.48	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	428.26	11/2015 -	11/2015
38	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	165.00	116.65	03/2014 -	03/2014
39	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	879.55	05/2014 -	05/2014

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	186.78	12/2014 -	12/2014
41	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	1,844.55	05/2015 -	05/2015
42	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	490.10	03/2015 -	03/2015
43	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	761.68	450.52	05/2013 06/2014	06/2014
44	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
45	IOR GELEKI (ONGCL) - [160100216]	9/2001	390.09 -	1,674.11	1,759.52	03/2007 03/2017	03/2017
	Total		25,435.00 -	29,865.39	8,886.35		
	<u>POWER</u>						
46	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	794.02	08/2013 09/2015	09/2015
47	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	1,306.06	05/2014 -	05/2014
48	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	1,940.13	1,174.99	09/2014 -	09/2014
49	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,228.88	08/2014 -	08/2014
50	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	590.66	01/2015 -	01/2015
51	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	618.38	02/2015 -	02/2015
52	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
53	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	-	08/2014 -	08/2014
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
55	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	2,692.00	12/2016 -	12/2016
56	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	532.78	11/2014 -	11/2014

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	278.18	11/2014 -	11/2014
58	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	541.52	08/2014 -	08/2014
59	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	42.36	06/2014 -	06/2014
60	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	100.33	03/2014 -	03/2014
61	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
62	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	812.46	10/2014 -	10/2014
63	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	75.80	08/2014 -	08/2014
64	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
65	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	44.00	08/2017 -	08/2017
66	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,227.00	05/2017 -	05/2017
67	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	4.86	10/2014 -	10/2014
68	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	6.51	10/2014 -	10/2014
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	169.16	03/2015 -	03/2015
70	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	736.00	08/2015 -	08/2015
71	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,889.00	11/2016 -	11/2016
72	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,623.00	09/2016 -	09/2016
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
74	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
75	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	-	05/2016 -	05/2016

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	-	11/2016 -	11/2016
77	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
79	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	912.00	09/2017 -	09/2017
80	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	336.37	06/2015 -	06/2015
81	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	11.89	12/2015 -	12/2015
82	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	1/2011	913.63 -	913.63	512.83	07/2006 12/2015	12/2015
83	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	202.63	08/2014 -	08/2014
	Total		89,742.15 -	90,296.54	18,463.67		
	<u>RAILWAYS</u>						
84	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	111.21	02/2015 -	02/2015
85	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,116.53	250.35	03/2010 03/2017	03/2017
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	273.79	03/2016 -	03/2016
87	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	45.67	03/2015 -	03/2015
88	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]	4/2008	516.23 -	516.23	452.07	03/2014 -	03/2014
89	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
90	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	150.62	03/2017 -	03/2017
91	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	4/2009	257.42 -	257.42	33.79	03/2014 -	03/2014
92	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
93	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	9.97	03/2015 -	03/2015

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
94	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	4/2010	309.44 -	388.67	56.07	12/2015 -	12/2015
95	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR- BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	1.47	02/2019 -	02/2019
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
97	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	751.93	03/2014 -	03/2014
98	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113	4/2008	653.19 -	653.47	257.47	03/2014 -	03/2014
99	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	4/2010	2,619.02 -	2,913.51	372.15	03/2016 -	03/2016
	Total		18,679.28 -	24,557.47	2,769.58		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
100	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207	12/2003	157.47 -	157.42	260.30	09/2007 03/2014	03/2014
101	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	382.02	107.55	04/2009 12/2014	12/2014
102	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	265.63	92.14	11/2008 12/2014	12/2014
103	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	241.28	151.77	11/2008 12/2014	12/2014
104	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	247.43	180.36	04/2009 12/2014	12/2014
105	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	153.76	09/2014 -	09/2014
106	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	958.69	05/2014 -	05/2014
107	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.60	01/2014 -	01/2014
108	PUNE-SHOLAPUR,PKG-II - [N24000193	9/2011	835.00 -	835.00	394.31	01/2014 -	01/2014
109	4-LANING OF BARHI-HAZARIBAGH - [N24000191	2/2012	398.00 -	398.00	454.33	02/2014 -	02/2014
110	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190	12/2011	325.00 -	325.00	161.49	05/2014 -	05/2014
111	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014
112	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.34	04/2014 -	04/2014
113	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,424.72	08/2014 -	08/2014
114	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225	3/2012	828.00 -	828.00	582.60	09/2014 -	09/2014

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	334.61	04/2015 -	04/2015
116	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	61.44	12/2015 -	12/2015
117	2 LANING WITH PS KANPUR KABRAI - [N24000221	1/2013	373.47 -	373.47	42.12	07/2014 -	07/2014
118	2 LANING WITH PS AGRA ALIGARH - [N24000220	10/2012	250.50 -	250.50	268.96	10/2014 -	10/2014
119	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	20.71	09/2015 -	09/2015
120	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
121	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	263.68	06/2014 -	06/2014
122	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	248.77	06/2015 -	06/2015
123	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	598.56	02/2015 -	02/2015
124	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	52.18	11/2015 -	11/2015
125	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	256.68	09/2014 -	09/2014
126	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC [N24000226	10/2011	1,565.00 -	1,565.00	908.44	10/2014 -	10/2014
127	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213	4/2012	624.00 -	624.00	413.79	04/2014 -	04/2014
128	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211	7/2012	356.40 -	356.40	3.26	07/2014 -	07/2014
129	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	283.09	10/2014 -	10/2014
130	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	588.54	07/2014 -	07/2014
131	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	100.21	01/2014 -	01/2014
132	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,113.79	09/2014 -	09/2014
133	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR [N24000205	12/2011	1,047.00 -	1,047.00	233.48	06/2014 -	06/2014
134	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,725.30	06/2014 -	06/2014
135	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,325.75	10/2014 -	10/2014
136	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	-	04/2010 09/2015	09/2015
137	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	160.00	-	05/2008 07/2014	07/2014

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	-	04/2008 01/2015	01/2015
139	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	-	06/2008 05/2014	05/2014
140	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	-	04/2008 01/2015	01/2015
141	SONAPUR TO GUWAHATI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	-	03/2008 01/2015	01/2015
142	GUWAHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	-	04/2008 03/2014	03/2014
143	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	662.29	03/2014 -	03/2014
144	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]	5/2011	664.00 -	664.00	611.24	02/2014 -	02/2014
145	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.51	05/2014 -	05/2014
146	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	930.16	03/2014 -	03/2014
147	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	332.50	02/2014 -	02/2014
148	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	554.09	01/2014 -	01/2014
149	GHAZIABAD-ALIGARH NH-91 - [N24000170]	2/2011	1,141.00 -	1,141.00	1,294.08	08/2013 06/2014	06/2014
150	NASHRI CHANANI - [N24000162]	6/2010	2,159.00 -	2,159.00	240.31	06/2015 -	06/2015
151	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	1,004.65	07/2015 -	07/2015
	Total		45,299.11 -	45,804.88	22,642.05		
	<u>SHIPPING AND PORTS</u>						
152	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 06/2014	06/2014
153	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		661.87 -	1,111.87	246.52		
	<u>STEEL</u>						
154	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	1/2007	295.89 -	607.17	364.11	12/2011 09/2014	09/2014
155	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]	4/2011	572.00 -	572.00	356.11	04/2013 09/2014	09/2014
156	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	274.17	05/2013 01/2015	01/2015

(Jan,2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
157	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	92.77	08/2014 -	08/2014
158	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	19.17	12/2014 -	12/2014
159	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	53.59	06/2015 -	06/2015
160	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	6.91	05/2016 -	05/2016
	Total		2,894.90 -	3,223.99	1,166.83		
	<u>URBAN DEVELOPMENT</u>						
161	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	6,445.67	03/2016 -	03/2016
	Total		38,585.00 -	38,585.00	6,445.67		
	Grand Total		233,136.06	244,912.55	62,595.66		

List of Delayed Projects w.r.t. Latest Schedule

(Jan,2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,089.00	12/2008 -	01/2015	73	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,666.16	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	-	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	-	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	21,755.16				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	264.45	05/2012 -	02/2014	21	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	256.77	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	1,042.27	521.22				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,869.96	06/2009 -	03/2014	57	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	116.77	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	119.25	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	381.36	03/2013 -	03/2014	12	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	4,991.82	03/2012 -	05/2014	26	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,ANDHRA PRADESH	12/2009	212.34 1,228.39	1,228.39	1,159.43	03/2013 09/2012	03/2015	24	30
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	114.67	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.12	03/2010 -	03/2015	60	-
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	119.43	03/2013 -	03/2015	24	-
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,ANDHRA PRADESH	12/2009	418.97 -	418.97	242.96	03/2012 -	03/2015	36	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,ANDHRA PRADESH	03/2010	181.19 -	181.19	35.15	03/2012 -	03/2015	36	-
20	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	103.47	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,601.63	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,302.22	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	27.80	07/2012 -	03/2016	44	-
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	269.44	03/2014 -	03/2016	24	-
25	KAKATIYA LONGWALL - [N06000048]SCCL,ANDHRA PRADESH	12/2008	453.63 -	453.63	100.81	12/2012 -	03/2016	39	-
26	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	31.29	03/2014 -	03/2016	24	-
27	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	2.19	03/2014 -	03/2016	24	-
28	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	125.63	03/2012 -	03/2016	48	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	210.16	03/2014 -	03/2016	24	-
31	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.38	03/2011 -	03/2016	60	-
32	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	141.54	03/2012 -	03/2016	48	-
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.31	03/2011 -	03/2017	72	-
34	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	62.43	03/2012 -	03/2017	60	-
36	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	249.46	12/2015 -	04/2018	28	-
	Total		25,052.78 -	28,822.24	14,588.67				
	STEEL								
37	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,729.46	10/2009 10/2012	03/2014	53	17
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	159.83	09/2008 12/2013	03/2014	66	3
39	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,356.27	12/2011 -	03/2014	27	-
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,487.23	12/2011 -	06/2014	30	-
41	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	302.63	09/2009 05/2012	07/2014	58	26

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	114.44	10/2013 -	08/2014	10	-
43	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	10,605.40	03/2013 -	09/2014	18	-
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,007.48	12/2012 -	12/2014	24	-
45	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	11,982.04	03/2013 -	03/2015	24	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	100.11	11/2013 -	06/2015	19	-
	Total		62,441.88 -	68,084.56	55,844.89				
	PETROLEUM								
47	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,ASSAM	09/2001	113.90 438.85	480.00	452.91	03/2006 03/2013	02/2014	95	11
48	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,MAHARASHTRA	01/2007	740.02 -	740.02	737.45	03/2010 03/2012	02/2014	47	23
49	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
50	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,351.12	05/2010 03/2013	03/2014	46	12
51	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
52	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,543.40	09/2012 -	03/2014	18	-
53	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	1,969.18	09/2011 03/2012	03/2014	30	24
54	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,MAHARASHTRA	04/2008	825.00 -	1,827.00	1,514.22	04/2013 12/2013	03/2014	11	3
55	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	422.91	12/2013 -	03/2014	3	-
56	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,161.80	02/2014 -	03/2014	1	-
57	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	780.21	07/2012 -	03/2014	20	-
58	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	10,944.65	01/2012 -	03/2014	26	-
59	DEVELOPMENT OF BHE AND BH-35 AREA. - [N16000118]ONGC,MULTI STATE	08/2010	372.11 -	372.11	234.31	03/2013 -	03/2014	12	-
60	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCL TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	244.03	04/2012 -	03/2014	23	-
61	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	03/2014	29	-
62	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	148.68	06/2012 -	03/2014	21	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
63	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL, ASSAM	08/2008	126.18 -	159.54	62.95	06/2012 -	03/2014	21	-
64	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,190.50	08/2010 03/2012	05/2014	45	26
65	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,848.86	09/2011 05/2012	05/2014	32	24
66	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	1,888.97	06/2012 -	05/2014	23	-
67	DEVELOPMENT OF SB-14 FIELD - [N16000116]ONGC, MULTI STATE	01/2011	410.44 -	410.44	237.16	11/2012 -	05/2014	18	-
68	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	60.87	06/2012 -	05/2014	23	-
69	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2014	98	24
70	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	204.57	08/2012 -	06/2014	22	-
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	930.83	10/2011 -	06/2014	32	-
72	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	155.10	08/2013 -	09/2014	13	-
73	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
74	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 -	32,710.00	24,340.00	11/2012 -	12/2014	25	-
75	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	445.97	09/2011 -	12/2014	39	-
76	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	240.95	101.83	09/2012 -	12/2014	27	-
77	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	40.85	03/2014 -	12/2014	9	-
78	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
79	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24	12
80	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	330.47	268.90	03/2012 -	03/2015	36	-
81	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC, GUJARAT	10/2011	200.69 -	200.69	8.08	07/2014 -	03/2015	8	-
82	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	01/1999	1,419.00 -	1,419.00	320.99	12/2014 -	03/2015	3	-
83	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 -	2,592.17	143.66	05/2014 -	05/2015	12	-
84	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	871.35	9.66	03/2015 -	06/2015	3	-
85	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	938.72	09/2012 -	08/2015	35	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	08/2015	8	-
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.47	10/2014 -	10/2015	12	-
88	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	776.92	10/2011 -	10/2015	48	-
89	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,084.00	01/2012 -	10/2015	45	-
90	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12	-
91	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
92	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-
93	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,002.31	01/2014 -	12/2015	23	-
94	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	1,265.85	12/2015 -	05/2016	5	-
95	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
96	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	10/2016	49	-
97	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
98	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
99	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	703.14	04/2015 -	03/2017	23	-
	Total		138,443.16 -	150,268.74	89,852.74				
	<u>POWER</u>								
100	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	161.64	06/2012 -	01/2014	19	-
101	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,JAMMU AND KASHMIR	08/2005	1,729.29 -	2,081.00	2,096.81	11/2009 -	01/2014	50	-
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,MULTI STATE	10/2010	182.68 -	182.68	139.73	01/2013 -	02/2014	13	-
103	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,265.17	10/2010 -	03/2014	41	-
104	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	466.16	09/2010 -	03/2014	42	-
105	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	160.75	11/2011 -	03/2014	28	-
106	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,086.34	08/2012 -	03/2014	19	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
107	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,133.03	08/2012 -	03/2014	19	-
108	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	622.71	11/2012 -	03/2014	16	-
109	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	-	12/2013 -	03/2014	3	-
110	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR TPS - [N18000097]PGCIL,MULTI STATE	08/2010	170.36 -	170.36	112.01	04/2013 -	03/2014	11	-
111	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,MAHARASHTRA	07/2011	181.93 -	181.93	145.81	07/2013 -	03/2014	8	-
112	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	356.37	10/2013 -	04/2014	6	-
113	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,MULTI STATE	10/2006	975.96 -	975.96	887.78	10/2009 -	05/2014	55	-
114	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,402.61	03/2013 -	05/2014	14	-
115	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,201.02	12/2013 -	05/2014	5	-
116	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	2,952.80	01/2012 -	06/2014	29	-
117	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	375.59	02/2014 -	06/2014	4	-
118	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL, GUJARAT	01/2012	259.28 -	259.28	129.10	01/2014 -	06/2014	5	-
119	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	225.45	11/2013 -	09/2014	10	-
120	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	252.39	06/2014 -	09/2014	3	-
121	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 623.44	951.48	714.20	07/2013 -	11/2014	16	-
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,MULTI STATE	02/2009	520.48 -	520.48	370.39	11/2011 -	12/2014	37	-
123	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	946.16	08/2012 -	12/2014	28	-
124	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	358.95	07/2013 -	12/2014	17	-
125	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,570.92	07/2014 -	12/2014	5	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	6,683.00	08/2013 -	02/2015	18	-
127	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,641.19	10/2012 -	03/2015	29	-
128	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	2,883.00	11/2012 -	03/2015	28	-
129	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,555.07	12/2012 -	03/2015	27	-
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	962.89	04/2013 -	03/2015	23	-
131	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,162.88	03/2014 -	03/2015	12	-
132	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	789.56	11/2012 -	03/2015	28	-
133	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 -	6,414.56	5,553.00	04/2009 -	05/2015	73	-
134	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	257.99	08/2014 -	05/2015	9	-
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	77.98	04/2015 -	05/2015	1	-
136	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	7,570.34	08/2013 -	06/2015	22	-
137	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	63.72	01/2013 -	06/2015	29	-
138	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,140.80	11/2013 -	06/2015	19	-
139	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	723.27	08/2014 -	06/2015	10	-
140	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,264.35	10/2014 -	06/2015	8	-
141	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,436.24	09/2009 -	07/2015	70	-
142	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	431.56	01/2015 -	12/2015	11	-
143	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,353.98	06/2015 -	12/2015	6	-
144	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	383.30	07/2014 -	05/2016	22	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
145	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,252.00	07/2011 -	06/2016	59	-
146	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	3,642.00	3,118.93	01/2016 -	11/2016	10	-
147	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDC,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	576.41	07/2010 02/2016	02/2017	79	12
148	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,712.05	12/2009 06/2016	03/2017	87	9
149	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,036.00	12/2009 -	03/2017	87	-
150	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	2,978.48	1,962.00	03/2013 -	03/2017	48	-
151	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,468.31	09/2010 -	06/2018	93	-
152	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,239.17	09/2009 -	07/2018	106	-
	Total		132,480.35 -	148,285.55	97,432.88				
	<u>RAILWAYS</u>								
153	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	580.26	03/1994 -	01/2014	238	-
154	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,ODISHA	04/1993	100.00 142.98	227.94	234.32	03/2002 -	02/2014	143	-
155	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	398.93	12/2009 03/2011	03/2014	51	36
156	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
157	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 482.70	482.70	565.61	03/2013 -	03/2014	12	-
158	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	126.82	06/2013 -	06/2014	12	-
159	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	298.57	02/2009 02/2009	08/2014	66	66
160	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	270.46	03/2009 03/2009	08/2014	65	65
161	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	224.71	12/2008 -	09/2014	69	-
162	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRT,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	338.87	03/2004 12/2010	12/2014	129	48
163	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.90	355.23	06/2004 -	12/2014	126	-
164	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,291.27	03/2009 12/2012	12/2014	69	24
165	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	189.71	12/2012 -	12/2014	24	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
166	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	622.92	03/1995 -	03/2015	240	-
167	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE, WEST BENGAL	04/1974	31.42 393.46	535.40	179.02	03/2007 03/2007	03/2015	96	96
168	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	1,022.64	742.02	12/2010 12/2010	03/2015	51	51
169	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	261.04	06/2013 06/2013	03/2015	21	21
170	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	1,966.06	10/2007 12/2012	12/2015	98	36
171	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	783.15	03/2010 -	12/2015	69	-
172	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	177.38	44.91	03/2015 -	12/2015	9	-
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	62.70	03/2014 -	03/2016	24	-
174	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213]MRTP,ANDHRA PRADESH	04/2012	632.68 -	816.55	0.61	04/2012 -	03/2016	47	-
175	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,074.47	448.82	06/2005 07/2011	06/2016	132	59
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	68.18	03/2016 -	06/2016	3	-
177	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	483.68	03/2005 12/2008	12/2016	141	96
178	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,506.46	03/2014 03/2016	12/2016	33	9
179	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	128.84	04/2014 -	03/2017	35	-
180	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	64.63	12/2015 -	03/2017	15	-
181	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	8.98	03/2015 -	03/2017	24	-
182	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,185.44	3,872.29	03/2009 -	03/2017	96	-
183	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	951.99	03/2007 -	03/2017	120	-
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
185	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	2,993.95	04/2008 03/2014	12/2017	116	45
186	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,543.15	12/2008 -	03/2018	111	-
187	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	131.15	12/2012 -	03/2018	63	-
188	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	533.44	03/2014 -	03/2019	60	-

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
189	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	1,924.82	03/2011 03/2014	03/2020	108	72
	Total		28,336.14 -	79,163.10	33,161.62				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
190	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,153.77	11/2013 -	01/2014	2	-
191	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.01	05/2010 -	03/2014	46	-
192	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	308.49	10/2013 -	03/2014	5	-
193	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	226.29	10/2013 -	03/2014	5	-
194	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	183.67	07/2009 -	04/2014	57	-
195	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	-	02/2009 -	05/2014	63	-
196	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	-	09/2007 -	05/2014	80	-
197	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.40	09/2013 -	07/2014	10	-
	Total		3,343.00 -	3,681.06	2,572.63				
	<u>SHIPPING AND PORTS</u>								
198	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 02/2014	04/2014	2	2
199	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	1,429.10	990.28	12/2010 09/2012	03/2015	51	30
	Total		2,194.46 -	2,423.92	1,417.82				
	<u>TELECOMMUNICATIONS</u>								
200	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.68	06/2009 -	03/2014	57	-
201	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	170.57	01/2009 -	03/2014	62	-
202	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	03/2014	41	24
203	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	246.51	05/2011 -	03/2014	34	-
	Total		2,018.15 -	1,843.90	531.21				

(Jan,2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>URBAN DEVELOPMENT</u>								
204	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	529.69	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	529.69				
	Grand Total		438,235.27	532,835.34	318,208.53				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	01/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2014	15.77
	Total		2,278.12 -	25,928.66			
	<u>COAL</u>						
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		1,431.79 -	27,645.25			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	36,565.25			
	<u>PETROLEUM</u>						
10	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	03/2007 -	03/2014	117.33
11	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	480.00	03/2006 -	02/2014	321.42
12	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
14	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	04/2008	825.00 -	1,827.00	04/2013 -	03/2014	121.45
15	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
16	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	03/2014	17.25
17	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	03/2014	12.16
18	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
19	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	03/2014	41.85
20	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		32,937.88 -	74,588.42			
	POWER						
21	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
22	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	05/2015	41.69
23	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	06/2018	69.71
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
25	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
26	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	07/2015	41.49
27	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
28	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	01/2014	20.34
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	05/2016	50.31
30	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
31	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
32	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00
	Total		39,963.03 -	128,517.51			

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
33	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
34	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
35	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
37	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-TAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
38	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	02/2014	127.94
39	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
40	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
42	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
43	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
44	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
45	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
46	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
47	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
48	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
49	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
50	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
51	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.90	06/2004 -	12/2014	207.57
52	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
53	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
54	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	03/2014	300.67
56	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,022.64	12/2010 -	03/2015	922.64
57	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
58	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
59	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
61	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
62	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2018	238.75
63	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
64	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
65	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
66	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
67	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	12/2014	461.44
68	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
69	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2020	724.12
71	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
72	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
73	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
74	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
75	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
76	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
77	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
79	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
80	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
81	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
82	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
83	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N220000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
84	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
85	BHOPAL BINA 3D LINE DOUBLING - [N220000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
86	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N220000079	09/2007	404.19 -	1,383.45	- -	-	242.28
87	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080	09/2006	343.17 -	914.98	- -	12/2012	166.63
88	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
89	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR [N220000083	09/1996	156.00 -	407.98	- -	03/2014	161.53
90	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084	09/2006	125.00 -	420.00	- -	-	236.00
91	TIDIVANAM-NAGARI (NL) - [N220000085	09/2006	456.00 -	820.00	- -	-	79.82
92	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086	09/2006	200.00 -	430.33	- -	03/2017	115.17
93	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N220000087	09/2006	300.00 -	532.87	- -	-	77.62
94	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
95	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
96	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03
97	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
98	AGARTALA SABROOM, NL, NEFR - [N220000099	04/2008	813.34 -	1,741.00	03/2014 -	03/2019	114.06
99	BHAIRABI SAIRONG, NL, NEFR - [N220000100	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
100	KISHANGANJ JALALGARH, NL, NEFR - [N220000101	04/2008	282.92 -	359.86	- -	03/2015	27.20

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,619.02 -	2,913.51	03/2016 -	03/2016	11.24
103	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
104	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
105	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
106	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
107	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
108	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2018	45.41
109	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2017	209.34
110	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
111	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
112	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
113	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
114	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
115	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
116	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
117	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
118	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
119	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
120	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
121	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
122	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
124	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1999	271.24 -	520.00	- -	-	91.71
125	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	- -	-	55.74
126	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14
127	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192	04/1999	175.43 -	247.75	- -	03/2014	41.22
128	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
129	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.22	- -	-	109.04
130	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71
131	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	-	285.12
132	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29
133	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	165.82 -	545.64	- -	-	229.06
134	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,418.21	- -	-	171.08
135	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	-	47.95
136	HYDERABAD/SECUNDERABD MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II - [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
137	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
138	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	697.00 -	1,604.00	- -	-	130.13
139	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
140	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10
141	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
142	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97
143	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97
144	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
145	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267	04/2012	289.79 -	377.44	- -	-	30.25
146	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
147	WHITE FIELD-KOLAR NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
148	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	444.18	- -	-	102.06
149	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		53,140.77 -	277,833.28			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
150	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	-	30.10
151	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	03/2008 -	-	16.14
152	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	265.63	11/2008 -	12/2014	58.45
153	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
154	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50
	Total		1,871.91 -	281,062.98			
	<u>SHIPPING AND PORTS</u>						
155	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
156	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
157	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
158	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
159	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		2,946.13 -	284,846.52			
	<u>STEEL</u>						
160	EXPANSION OF IISCO STEEL PLANT - [N12000051	06/2008	14,443.00 -	16,408.00	12/2011 -	06/2014	13.61

(Jan,2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
161	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
	Total		14,680.09 -	301,509.42			
	<u>TELECOMMUNICATIONS</u>						
162	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	03/2014	6.42
163	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
164	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	302,990.87			
	<u>URBAN DEVELOPMENT</u>						
165	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	314,599.87			
	<u>WATER RESOURCES</u>						
166	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	315,786.87			
	Grand Total		179,705.21	2,394,821.90			
