

**351st FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
January 2015**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

कार्यकारी सारांश

- जनवरी, 2015 की फ्लैश रिपोर्ट में रु.150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 745 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जनवरी, 2015 के दौरान 3 परियोजनाओं (विद्युत में 2 परियोजनाएं और रेलवे में 1 परियोजना) के पूरा होने की सूचना दी गई है।
- संदर्भाधीन माह के दौरान, 745 परियोजनाओं में से, 317 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 63 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 63 परियोजनाओं में से, 14 परियोजनाएं रु.1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	290	31	4	1
2.	सड़क परिवहन एवं राजमार्ग	135	102	33	1
3.	विद्युत	104	63	15	10
4.	पेट्रोलियम	70	43	7	2
5.	कोयला	68	36	4	0
6.	शहरी विकास	31	14	0	0
7.	इस्पात	24	17	0	0
8.	नागर विमानन	7	4	0	0
9.	पोत परिवहन एवं पत्तन	6	1	0	0
10.	परमाणु ऊर्जा	4	4	0	0
11.	दूरसंचार	3	2	0	0
12.	उर्वरक	1	0	0	0
13.	खादान	1	0	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		745	317	63	14

- 745 परियोजनाओं के कार्यान्वयन की कुल मूल लागत रु.10,30,625.70 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत रु.12,34,992.39 करोड़ होने की संभावना है, जो रु.2,04,366.69 करोड़ (मूल लागत का 19.80%) की समग्र लागत वृद्धि को दर्शाता है। जनवरी, 2015 तक इन परियोजनाओं पर किया गया व्यय रु.5,35,408.60 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 43.40% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.01.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	अनुमानित लागत(करोड़ रु. में)	लागत वृद्धि(%)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
	नागर विमानन				
1	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	15.77
	कोयला				
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
2	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3388.61	66.86
3	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	50.37
4	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
	पेट्रोसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	8920.00	63.35
	पेट्रोलियम				
1	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	820.20
2	क्लस्टर-7 क्षेत्रों का विकास	03/2010	3241.03	6638.94	104.84
3	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	73.40
4	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
5	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
	विद्युत				
1	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1259.80	241.67
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	143.42
3	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	842.77	100.18
4	पारे जल विद्युत परियोजना	12/2008	573.99	1128.38	96.59
5	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेगा.) (एनएचपीसी)	09/2005	1061.38	1929.15	81.76

	रेलवे				
1	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
2	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
3	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
4	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
5	हुबली-अंकोला (एनएल) एसडब्ल्यूआर	04/1997	227.00	2135.00	840.53
	सड़क परिवहन एवं राजमार्ग				
1	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	106.50
2	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
3	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	363.74	85.58
4	हरंगाजो से मैबंग, 164.08-190.587 किमी. एनएच-54	12/2003	212.00	386.10	82.12
5	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
	पोत परिवहन एवं पत्तन				
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
2	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	2098.56	70.89
3	कोचीन पोर्ट ट्रस्ट के वल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	51.92
	इस्पात				
1	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
2	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
	शहरी विकास				
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53
2	सी/ओ बांद्रा कुर्ली कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन,	11/2006	114.18	173.08	51.59

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

अधिकतम लागतवृद्धि वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची (31.01.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
	नागर विमानन				
1	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	52.92
	कोयला				
1	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
2	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3388.61	1357.83
3	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
4	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	236.62
5	अम्लई ओसी विस्तार सेक्टर बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	8920.00	3459.39
	पेट्रोलियम				
1	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
2	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
3	क्लस्टर-7 क्षेत्रों का विकास	03/2010	3241.03	6638.94	3397.91
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	2384.66
5	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
	विद्युत				

1	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67
2	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	कोल्डम एचईपी (एनटीपीसी)	01/2011	4527.15	7220.00	2692.85
4	बोंगाइगांव थर्मल विद्युत परियोजना	01/2008	4375.35	6749.18	2373.83
5	किशनगंगा एचईपी (3X110 मेगावाट)	01/2009	3642.04	5497.72	1855.68
	रेलवे				
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	19565.00	17065.00
2	जिरिबाम से इम्फाल (तुपुई) (एनएल) (एनईएफआर)	04/2003	727.56	6570.75	5843.19
3	लुमडिंग-सिलचर जिरिबाम, बदरपुर-बराईग्राम कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	5500.00	3823.69
4	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्रपुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
5	सीवोक रंगपो, एनईएफआर	04/2008	1339.48	4190.00	2850.52
	सड़क परिवहन एवं राजमार्ग				
1	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी.	05/2009	1108.00	2288.00	1180.00
2	मैबंग से लुमडिंग (एस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
3	हरंगाजो से मैबंग, 164.08 किमी. से 190.587 किमी. एनएच-54	12/2003	212.00	386.10	174.10
4	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	363.74	167.74
5	मैबंग से लुमडिंग, (एस-24) 111.000 किमी. से 126.450 किमी. एनएच-54	12/2003	155.04	280.13	125.09
	पोत परिवहन एवं पत्तन				
1	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	1228.00	2098.56	870.56
2	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
3	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	373.22	127.55

	इस्पात				
1	तरल इस्पात क्षमता के विस्तार 3 एमटी से 6.3एमटी तक (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00
2	सिंटर मंशीन -1 और 2का सुधार	12/2009	343.00	488.40	145.40
	शहरी विकास				
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00
2	सी/ओ बांद्रा कुर्ला कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन,	11/2006	114.18	173.08	58.90

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 745 परियोजनाओं में से, 6 परियोजनाएं समय से पहले चल रही हैं, 122 समय पर तथा 317 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 296 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 35 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 265 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 317 विलंबित परियोजनाओं में से, 71 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 72 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 101 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 73 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

अधिकतम समयवृद्धि वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची (31.01.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीने में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	04/2015	76
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	09/2010	09/2016	72
3	काकरापार परमाणु ऊर्जा परियोजना-3	10/2009	12/2015	10/2017	22

	और 4				
4	राजस्थान परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2016	05/2018	17
	नागर विमानन				
1	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	01/2011	06/2016	65
2	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	01/2015	32
3	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	03/2015	03/2016	12
4	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	03/2014	01/2015	10
	कोयला				
1	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
2	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2017	84
3	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
4	गोपाल प्रसाद ओसीपी (15 एमटीवाई)	02/2008	03/2015	03/2021	72
5	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
	पेट्रोलियम				
1	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	04/2006	06/2015	110
2	जगदीशपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	02/2019	73
3	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	08/2010	05/2015	57
4	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओएसवी)	06/2007	09/2011	12/2015	51
5	वीकेपीएल उन्नयन तथा स्परलाइन को बिछाना (भिलवाड़ा तथा चित्तौड़गढ़ के लिए)	12/2009	06/2011	07/2015	49
	विद्युत				
1	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
2	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	03/2019	114
3	बाढ़ एसटीपीपी (3X660 मेगावाट) एनटीपीसी	02/2005	12/2009	03/2018	99

4	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	03/2016	99
5	टेहरी पंचड भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
	रेलवे				
1	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
2	गुना-इटावा वाया शिवपुरी-ग्वालियर भिंड एनएल, (एनसीआर)	04/1986	03/1994	10/2014	247
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193
4	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
5	अमरावती-नरखेर एनएल, (सीआर)	06/1994	06/1999	07/2012	157
	सड़क परिवहन एवं राजमार्ग				
1	असम/पश्चिम बंगाल सीमा से बिजनी चरण-III, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	06/2015	120
2	आगरा-बाड़पास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	06/2015	93
3	हरंगाजो से मैबंग, 164.08 किमी. से 190.587 किमी. एनएच-54	12/2003	09/2007	03/2015	90
4	सिलचर-उदरबंद (चरण.II) एनएच-54, 309 किमी. से 275 किमी.	12/2003	09/2007	01/2015	88
5	रामदेवी क्रॉसिंग से गंगा पुल चरण.II एनएच-25, 75 किमी. से 80.06 किमी.	12/2003	09/2008	12/2015	87
	पोत परिवहन एवं पत्तन				
1	एन्नोर मनाली एक्सप्रेस मार्ग, एफ/ओ स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	03/2006	11/2014	104
2	2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण और विकास	11/2007	12/2010	01/2016	61
3	कोचीन पोर्ट्स के बल्लापाडम में आसीटीटी के लिए रेल कनेक्टिविटी	03/2007	04/2009	02/2011	22
	इस्पात				
1	आरएमएचपी में लौह अयस्क भंडारण की वृद्धि	07/2007	09/2009	06/2015	69
2	3 एमटी से 6.3एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	10/2009	04/2015	66
3	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	05/2015	41
4	बैलाडिला लौह अयस्क परियोजना डिपोजिट-11बी (एनएमडीसी)	01/2007	12/2011	03/2015	39
5	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	09/2015	30
	दूरसंचार				

1	असम टेलीकॉम सर्कल, चरण-V.I, 2जी और 3जी	06/2007	01/2009	03/2015	74
2	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59
	शहरी विकास				
1	आरएसवीआई पटना के अंतर्गत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	03/2010	10/2014	55
2	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	05/2015	35
3	नागपुर महाराष्ट्र में राष्ट्रीय फायर सेवा कॉलेज का उन्नयन	06/2010	03/2012	01/2015	34
4	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	10/2015	29
5	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	12/2014	12/2016	24

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल, 2014 में इस मंत्रालय के प्रबोधन पर 727 परियोजनाओं में से 235 परियोजनाओं के संबंध में लागतवृद्धि तथा 282 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि जनवरी, 2015 के दौरान 745 परियोजनाओं में से 229 परियोजनाओं के संबंध में लागतवृद्धि तथा 317 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है । अप्रैल, 2014 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 32% से घटकर 31% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या में वृद्धि 39% से 43% हो गई है (अनुबंध 9 (क) तथा 9 (ख)) ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना लक्ष्यों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना लक्ष्यों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.01.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजना	अनुमोदन की तारीख	मूल लागत	अनुमानित लागत	संचयी व्यय	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	उपलब्धि
नागर विमानन								
1	वीएसआई हवाई अड्डे, पोर्टब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	16.59	एन.आर.	एन.आर.	0
2	विभिन्न हवाई अड्डों पर 56 एनओएस एयर फील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	217.60	0.04	03/2015	03/2016	0
3	गगन परियोजना	09/2008	626.00	626.00	499.08	06/2013	06/2013	0
4	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	335.61	388.53	285.00	05/2012	11/2014	0
5	चंडीगढ़ अंतरराष्ट्रीय हवाई अड्डा (मोहाली) का विकास चरण-II	02/2011	452.00	452.00	321.56	03/2015	02/2015	0
कोयला								
1	राजमहल ओसी विस्तार	09/2009	153.82	153.82	44.47	03/2014	03/2016	0
2	सोनपुर बजारी (सीओएमबी) ओसीपी (8.0 एमटीवाई)	08/2012	1055.05	1055.05	40.13	03/2018	03/2018	0
3	कपूरियायूजी (पीएसएलडब्ल्यू)	08/2011	988.35	988.35	6.84	04/2017	04/2017	0
4	मूनिडीह XV सीम यूजी	08/2011	1230.27	1230.27	1000.00	04/2015	04/2019	0
5	बिजारी ओसीआरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020	0
पेट्रोलियम								
1	विजयपुर और पाटा में पेट्रोलसायन परिसर-II	08/2010	8140.00	8140.00	7117.42	02/2014	12/2014	0

2	बीपीसीआर /एचपीसीआर से एलपीजी संयंत्र उरानतक एलपीजी के हस्तांतरण के लिए पाइपलाइन	08/2009	246.81	276.83	262.21	08/2012	10/2014	0
3	केन्द्रीय गैस गैदरिंग स्टेशन और ऑफ टेक प्वाइंट	08/2008	144.02	204.29	155.22	06/2012	12/2014	0
4	12 ऑफशोर सप्लाई वेसल्स का निर्माण (ओएसवी)	06/2007	736.65	736.65	470.27	09/2011	12/2015	0
5	2000 एचपी ड्रिलिंगरिंग के 2संख्या की खरीद	04/2010	270.00	270.00	एनआर	12/2014	03/2016	0
विद्युत								
1	सुबानसिरीलोअर एच.ई.पी. (एनएचपीसी)	09/2003	6285.33	15300.00	7019.81	09/2010	12/2018	0
2	ईस्टकोस्ट एनर्जीप्राइवेट लिमिटेड और एनसीसी बिजली परियोजना लिमिटेड एलटीओए जनरेशन से जुड़ी सामान्य प्रणाली	06/2012	1909.24	1909.24	639.63	06/2015	06/2015	0
3	पूर्वी क्षेत्र को सुदृढ़ बनाने की योजना-XII	05/2014	522.29	522.29	एनआर	11/2016	11/2016	0
4	उत्तरी क्षेत्र भाग ख में ट्रांसफार्मर की वृद्धि	03/2014	155.57	155.57	एनआर	03/2016	05/2016	0
5	उत्तरी क्षेत्र में फाइबर ऑप्टिक संचारप्रणाली की स्थापना	03/2012	198.63	198.63	12.80	09/2014	06/2016	0
रेलवे								
1	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	155.66	548.01	199.92	एनआर	एनआर	0
2	नामखाना-चंद्रनगर, काकद्वीप-बुदाखली और चंद्रनाग के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एम.एम.	04/1987	406.99	406.99	141.55	एनआर	एनआर	0
3	गुना-इटावावाया शिवपुरी-ग्वालियर-भिंडानएल, (एनसीआर)	04/1986	158.77	608.02	595.67	03/1994	10/2014	0
4	गजोली-इटाहर (एनएल), एनईएफआर सहित एकलाखी-बलुरघाट से नई बीजी रेलवे लाइन	04/1983	36.80	703.18	255.54	एनआर	एनआर	0
5	हावड़ा-आमता-चंपादंगाएनएल (एसईआर)	04/1974	393.46	445.40	180.72	03/2007	03/2015	0
सड़क परिवहन एवं राजमार्ग								
1	लखनऊ-रायबरेली	07/1999	635.90	635.90	608.30	07/2012	09/2014	0

2	पानीपत-जालंधर 6 लेन (96 किमी. से 387.1 किमी)	05/2009	1108.00	2288.00	3466.00	11/2011	03/2015	0
3	चिल्कालुरीपेट- विजयवाड़ा 6 लेन (355 किमी से किमी 434.15)	05/2009	572.30	572.30	886.90	10/2011	06/2015	0
4	चेन्नई-टाडा (छह लेन)	04/2009	353.37	353.37	446.20	10/2011	12/2014	0
5	दिल्ली / हरियाणा सीमा से रोहतक	04/2007	486.00	486.00	667.10	05/2010	12/2014	0
पोत परिवहन एवं पतन								
1	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	702.00	755.50	219.00	03/2011	03/2013	0
2	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत बनाना	10/2005	800.00	1571.60	9.70	10/2008	एनआर	0
3	एन्नोर मनाली एक्सप्रेस मार्ग, एफ / ओस्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	139.80	03/2006	11/2014	0
4	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एनआर	0
5	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	882.00	1060.00	0.93	02/2011	12/2012	0
इस्पात								
1	एनएमडीसीए की कृत इस्पात संयंत्र	01/2010	15525.00	15525.00	5615.00	05/2015	12/2016	0
दूरसंचार								
1	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	384.00	384.00	48.95	10/2010	03/2015	0
2	असम टेलीकॉम सर्किल, चरण-V.I, 2जी और 3जी	06/2007	336.81	336.81	195.94	01/2009	12/2014	0
3	उत्तरांचल में 283,000 लाइनों (2 जी) और 75,000 लाइनों (3 जी) का जीएसएम उपकरण	01/2009	149.15	158.72	86.05	06/2009	12/2014	0
शहरी विकास								
1	पातालगंगा रासयानी जिला रायगढ़ महाराष्ट्र में सी / ओएनआईएसएम परिसर	12/2012	315.00	315.00	53.96	06/2015	08/2015	0
2	सार्वजनिक ट्रेनिंग (सीएपीटी) भोपाल के लिए सेंट्रल अकादमी का निर्माण	12/2012	188.87	188.87	10.64	12/2014	12/2016	0

3	टीडब्ल्यूआइ सं, प्रयोगशाला सहित अवसंरचना स्कूल के मुख्य भवन का निर्माण	11/2012	238.43	238.43	0.00	02/2015	08/2015	0
4	कमंद में आईआईटी मंडी के लि एचरण 1 उत्तर के अंतर्गत विभिन्न भवन	11/2012	270.83	270.83	15.60	11/2014	10/2015	0
5	आरएसवीवाई पटना के तहत बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	2727.89	2727.89	2637.11	03/2010	10/2014	0

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना लागत अनुमान के पहले शुरू की गई परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की परियोजनाओं की क्षेत्र-वार सूची (31-01-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	नागर विमानन				
1	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	एनआर	318.28
	कोयला				
1	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3095.79
2	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1228.77
	पेट्रोरसायन				
1	असम गैस क्रैकर परियोजना	04/2006	5460.61	एनआर	8156.90
	पेट्रोलियम				
1	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5867.78
	विद्युत				
1	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	368.72	एनआर	712.66

2	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	एनआर	4789.81
3	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	एनआर	7057.12
4	कामेंगजल विद्युत परियोजना (नीपको)	12/2004	2496.90	एनआर	3509.85
5	तीस्ता लो डैम एचईपी, चरण-IV (4X40 मेगावाट) (एनएचपीसी)	09/2005	1061.38	एनआर	1606.79
	रेलवे				
1	गजोली-इटाहार सहित एकलाखी-बलूरघाट से नए बिजी रेलवे लाइन (एनएल) एनईएफआर	04/1983	36.80	36.00	255.54
2	विरमगम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	155.66	एनआर	201.25
3	पेड़ापल्ली-करीमनगर-निजामबाद एनएल (एससीआर)	12/1994	124.43	एनआर	710.57
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10205.04
5	कटक-बारंग (एलडी)	04/1995	127.13	एनआर	211.48
	सड़क परिवहन एवं राजमार्ग				
1	ब्रह्मपुत्र पुल एनएच सं.-31	12/2003	217.61	309.56	457.70
2	धरमतुल से सोनापुर (एएस-19)	12/2003	200.00	एनआर	289.50
3	धरमतुल से सोनापुर, 205 किमी. -183 किमी.(एएस-20)	12/2003	160.00	एनआर	211.80
4	नलबारी से बिजनी (एएस-7)	12/2003	208.00	230.00	334.10
5	नलबारी से बिजनी (एएस-6)	12/2003	225.00	एनआर	276.70
	पोत परिवहन एवं पत्तन				
1	कोचीन पोर्ट्स के बल्लापाड़म में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	298.17	373.22

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं की क्षेत्र-वार सूची (अधिकतम संख्या पांच में) इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की परियोजनाओं की क्षेत्र-वार सूची (31.01.2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगन परियोजना	09/2008	06/2013	एनआर	06/2013
2	वीएसआई हवाई अड्डे, पोर्ट ब्लेयर में नए एकीकृत टर्मिनल भवन का निर्माण	10/2013	एनआर	एन.आर.	एन.आर.
कोयला					
1	शांतिखानी लॉग वॉल परियोजना-एससीसीएल	10/2006	03/2012	एन.आर.	एन.आर.
2	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.आर.	एन.आर.
3	रामागुंडम ओसी II विस्तार	12/2009	03/2012	एन.आर.	एन.आर.
4	मुराडडीहयूजी टर्न की परियोजना	02/2011	04/2014	एन.आर.	04/2014
5	कृष्णाशिला (एनसीएल) (4एमटीवाई)	06/2011	03/2013	एन.आर.	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एन.आर.	एन.आर.
पेट्रोलियम					
1	एन्नोर में नई विपणन टर्मिनल	11/2006	एन.आर.	एन.आर.	एन.आर.
2	बीपीसीआर /एचपीसीआरसे उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइपलाइन	08/2009	08/2012	एन.आर.	एन.आर.
3	एन्नोर-त्रिची-मदुरै एलपीजी पाइपलाइन	05/2013	एन.आर.	एन.आर.	एन.आर.
विद्युत					
1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एन.आर.
2	कुंदनकुलम एपीपी ट्रांसप्रणाली (पीजीसीआईएल)	05/2005	09/2008	एन.आर.	03/2013
3	एसआर -XII की व्यवस्था कासुद्रीकरण	02/2010	06/2012	एन.आर.	एन.आर.
4	आंध्रप्रदेश भाग-ए1 के वैमागिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी सामान्य प्रणाली	03/2012	06/2014	एन.आर.	एन.आर.
रेलवे					

1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.आर.	एन.आर.
2	गजोली-ईटाहर(एनएल), एनईएफआर सहित एकलाखी-बालुरघाट से नई बीजी रेलवेलाइन	04/1983	एन.आर.	एन.आर.	एन.आर.
3	तामलुकदीघा, लाइनदोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एन.आर.
4	नामखाना चंद्रनगर काकद्वीप- बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एन.आर.	एन.आर.	एन.आर.
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एन.आर.	03/2010	एन.आर.
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.आर.	09/2014
2	दीवापुरसे यूपी/बिहारसीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एन.आर.	एन.आर.
3	सिलिगुडी से इस्लामपुर (पश्चिमबंगाल-7)	12/2003	07/2008	एन.आर.	एन.आर.
4	नलबाड़ी सेबिजनी (एएस-8)	12/2003	06/2008	एन.आर.	एन.आर.
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपीचरणा।।।)	03/2005	07/2012	एन.आर.	07/2012
पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एन.आर.	12/2012
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एन.आर.
3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एन.आर.	एन.आर.
4	पारादीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एन.आर.	01/2009	12/2010
5	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	03/2011	एन.आर.	03/2013
शहरी विकास					
1	सी/ओ सैन्य रक्षामंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय	08/2005	08/2007	एन.आर.	एन.आर.
2	बंगलोर मेट्रो रेल परियोजना	05/2006	06/2011	एन.आर.	03/2013

3	सी/ओ बांद्रा कुर्ला कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन	11/2006	04/2009	एन.आर.	एन.आर.
4	सी/ओएन आईटी कालीकट के रेल के लिए मेगाहॉस्टल।	01/2010	10/2012	एन.आर.	एन.आर.
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एन.आर.	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और शुरू करने की संशोधित तारीख से निर्धारित करनेके लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

i) **कोयला क्षेत्र में,** 68 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 8-36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'कल्याणीखानी ओपनकास्ट परियोजना, एससीसीएल' के संबंध में भूमि अधिग्रहण में विलंब तथा पुनर्वास तथा पुनर्स्थापन की समस्याओं के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'काकतिया लांगवाल, एससीसीएल' में संविदात्मक मुद्दे के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'किस्ताराम ओसीपी, एससीसीएल' तथा 'जलगाम वेंगाला राव ओसीपी-II, एससीसीएल' के संबंध में वन-भूमि के परिवर्तन में विलंब तथा पुनर्वास व पुनर्स्थापन की समस्याओं के कारण प्रत्येक में 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

ii) **रेलवे क्षेत्र में** 290 परियोजनाओं में से 31 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 2-11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 1 मेगा परियोजना है । परियोजनाएं 'जुबली पुल संख्या 8 के स्थान पर बंडेल-नैहाटी नई रेल पुल, ईआर तथा हार्बर लाईन पर 12 कार ट्रेनों का दौड़ना, एमआरटीपी' के संबंध में क्रमशः 2 तथा 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; और परियोजनाएं 'मुनीराबाद-महबूबनगर (नई लाईन), एससीआर' तथा 'आनंद नगर-नौटनवा जीसी के साथ गोंडा-गोरखपुर, एनईआर' प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iii) **पेट्रोलियम क्षेत्र में,** 70 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं । माह के दौरान 7 परियोजनाओं के संबंध में 1-23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं । परियोजना 'पारादीप में विपणन टर्मिनल, आईओसीएल' में पूर्व तटीय रेलवे से अनुमोदन में हुए विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना '102 मेवा. विंड पावर परियोजना, ओएनजीसी' में कार्य-क्षेत्र में हुए परिवर्तन के कारण 3 माह के अतिरिक्त

विलंब की सूचना प्राप्त हुई है; परियोजना 'माउंडेड बुलेट परियोजना, सीपीसीएल' में निर्माण कार्य स्थल पर रेत भरने में हुए विलंब के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'मंगलौर हासन मैसूर सोलर एलपीजी पाईपलाइन, एचपीसीएल' तथा 'उरानचकन/शिकरापुर एलपीजी पाईपलाइन, एचपीसीएल' के संबंध में कानून और व्यवस्था तथा वन संबंधी अनुमति में विलंब के कारण प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा 'बी-127 क्षेत्रों का विकास, ओएनजीसी' तथा 'एमएच तथा एनएच परिसंपत्तियों में मानव-रहित प्लेटफार्म चरण-II की मरम्मत करना, ओएनजीसी' के संबंध में क्रमशः 12 तथा 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iv) विद्युत क्षेत्र में, 104 परियोजनाओं में से 63 परियोजनाएं विलंबित हैं । माह के दौरान, 15 परियोजनाओं के संबंध में 1-11 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 10 मेगा परियोजनाएं हैं । परियोजनाएं 'छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए वर्धा-औरंगाबाद कोरिडोर में प्रणाली को सुदृढ़ करना, पीजीसीआईएल' और 'दक्षिणी क्षेत्र ग्रिड में प्रणाली को सुदृढ़ करना-XIX पीजीसीआईएल' के संबंध में क्रमशः आरओडब्ल्यू समस्याओं तथा सामग्रियों की आपूर्ति में विलंब के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'मध्य प्रदेश और छत्तीसगढ़ में आईपीपी जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' तथा 'छत्तीसगढ़ में आईपीपीएस जनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली को सुदृढ़ करना, पीजीसीआईएल' के संबंध में क्रमशः भूमि अधिग्रहण में विलंब तथा आरओडब्ल्यू समस्याओं के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'विंधुआचल-IV और रिहंद-III जनरेशन परियोजनाओं की पारेषण प्रणाली, पीजीसीआईएल' और 'उत्तरी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-XVI, पीजीसीआईएल' के संबंध में वन्य जीव अभ्यारण्य संबंधी अनुमति में विलंब के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'झारखंड और पश्चिम बंगाल-भाग-ए1 में चरण-I जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' और 'उत्तरी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-XXIV पीजीसीआईएल' के संबंध में वन संबंधी अनुमति में विलंब के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'एसआर ग्रिड की प्रणाली को सुदृढ़ करना XIII पीजीसीआईएल' के संबंध में आरओडब्ल्यू समस्याओं के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'दक्षिणी क्षेत्र-XIV की प्रणाली का सुदृढीकरण, पीजीसीआईएल' और 'दक्षिणी क्षेत्र ग्रिड में प्रणाली का सुदृढीकरण-XVIII, पीजीसीआईएल' के संबंध में आरओडब्ल्यू समस्याओं के कारण प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'उड़ीसा भाग बी में चरण-I जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' के संबंध में वन संबंधी अनुमति में विलंब के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'ईस्ट-कोस्ट एनर्जी प्राइवेट लिमिटेड के साथ जुड़ी सामान्य प्रणाली तथा एनसीसी पावर प्रोजेक्ट्स लिमिटेड, पीजीसीआईएल' तथा 'छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए रायपुर-वर्धा

कोरिडोर में प्रणाली का सुदृढीकरण, पीजीसीआईएल' के संबंध में वन संबंधी अनुमति में विलंब के कारण क्रमशः 6 तथा 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'साइकल एक्सटेंशन परियोजना (51 मेवा.) सहित अगरतला गैस टर्बाइन संयंत्र, नीपको के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

V) सड़क परिवहन एवं राजमार्ग क्षेत्र में 135 परियोजनाओं में से 102 परियोजनाएं विलंबित हैं । माह के दौरान, 33 परियोजनाओं के संबंध में 1-27 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 मेगा परियोजना है । 7 परियोजनाओं के संबंध में भूमि अधिग्रहण में विलंब तथा यूटिलिटी की शिफ्टिंग के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 4 परियोजनाओं के संबंध में निधियों की कमी तथा यूटिलिटी की शिफ्टिंग के कारण 2, 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 4 परियोजनाओं के संबंध में भूमि अधिग्रहण में विलंब तथा निधि की कमियों के कारण प्रत्येक में 5 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाओं के संबंध में भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 2 परियोजनाओं के संबंध में भूमि अधिग्रहण में विलंब के कारण क्रमशः 7 तथा 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 3 परियोजनाओं के संबंध में भूमि अधिग्रहण में विलंब तथा निधि की कमियों के कारण प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पटना-बक्सर-जयपुर 181.3 किमी से 231.95 किमी, एनएचएआई' के संबंध में भूमि अधिग्रहण में विलंब के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'समयखाली-गांधीधाम, एनएचएआई' के संबंध में वन संबंधी अनुमति में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पटना-मुजफ्फरपुर, एनएचएआई' तथा 'चेन्नई-टाडा (छह लेन), एनएचएआई' के संबंध में यूटिलिटी की शिफ्टिंग के कारण क्रमशः 14 तथा 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'देवली-कोटा, एनएचएआई' के संबंध में निधियों की कमी के कारण 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'बरसात-कृष्णानगर, एनएचएआई' तथा 'रोहतक-बावल, एनएचएआई' के संबंध में 10 तथा 19 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पीएस खगड़िया-पूर्णिया के साथ 2 लेनिंग, एनएचएआई' तथा 'जयपुर-रिंगस, एनएचएआई' के संबंध में 20 और 25 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'हजारीबाग-रांची, एनएचएआई' तथा 'जयपुर-टोंक-देवली, एनएचएआई' के संबंध में 26 तथा 27 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

11. दिनांक 31.01.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।

12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for January 2015 contains information on the status of the 745 Central Sector Infrastructure Projects costing ₹150 crore and above. During January 2015, 3 projects (2 projects are in Power and 1 project is in Railways) have reported completion.

2. During the reference month, out of 745 projects, 317 projects are delayed with respect to original schedule and 63 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 63 projects, 14 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1	RAILWAYS	290	31	4	1
2	ROAD TRANSPORT AND HIGHWAYS	135	102	33	1
3	POWER	104	63	15	10
4	PETROLEUM	70	43	7	2
5	COAL	68	36	4	0
6	URBAN DEVELOPMENT	31	14	0	0
7	STEEL	24	17	0	0
8	CIVIL AVIATION	7	4	0	0
9	SHIPPING AND PORTS	6	1	0	0
10	ATOMIC ENERGY	4	4	0	0
11	TELECOMMUNICATIONS	3	2	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	0	0	0
Total		745	317	63	14

3. Total original cost of implementation of the 745 projects was ₹10,30,625.70 crore and their anticipated completion cost is likely to be ₹12,34,992.39 crore, which reflects overall cost overruns of ₹2,04,366.69 crore (19.80 % of original cost). The expenditure incurred on these projects till January 2015 is ₹5,35,408.60 crore, which is 43.40 % of the anticipated cost of the projects. The sector wise list of projects (maximum five in numbers) having maximum percentage of cost overruns are as follows:-

Sector Wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-01-2015)

SN	PROJECT	SECTOR	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	ANTICIPATED COST (Rs; crore)	COST OVERRUN(%)
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3492.00	5677.00	2185.00
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	CIVIL AVIATION	05/2010	335.61	388.53	52.92
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	COAL	05/2008	4904.54	6602.74	1698.20
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2030.78	3388.61	1357.83
6	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1016.05
7	MAGADH OC 20 MTY (CCL)	COAL	08/2008	469.78	706.40	236.62
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	COAL	11/2009	150.59	198.59	48.00
9	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5460.61	8920.00	3459.39
10	PARADIP REFINERY PROJECT	PETROLEUM	02/2009	29777.00	34555.00	4778.00
11	DEV OF G1 AND GS-15 (ONGCL)	PETROLEUM	04/2003	429.82	3955.21	3525.39
12	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3248.78	5633.44	2384.66
13	INTEGRATED REFINERY EXPANSION PROJECT	PETROLEUM	03/2012	14225.00	16504.00	2279.00
14	DEVELOPMENT OF CLUSTER-7 FIELDS	PETROLEUM	03/2010	4550.40	6638.94	2088.54
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6285.33	15300.00	9014.67
16	BARH STPP(3X660MW) NTPC	POWER	02/2005	8692.97	15095.67	6402.70
17	KOLDAM HEP (NTPC)	POWER	01/2011	4527.15	7220.00	2692.85
18	BONGAIGAON THERMAL POWER PROJECT	POWER	01/2008	4375.35	6749.18	2373.83
19	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3642.04	5497.72	1855.68
20	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	19565.00	17065.00
21	JIRIBAM TO IMPHAL	RAILWAYS	04/2003	727.56	6570.75	5843.19

	(TUPUI)(NL)(NEFR)					
22	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1676.31	5500.00	3823.69
23	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	RAILWAYS	09/1997	1500.00	4996.19	3496.19
24	SEVOK RANGPO, NEFR	RAILWAYS	04/2008	1339.48	4190.00	2850.52
25	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1108.00	2288.00	1180.00
26	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	ROAD TRANSPORT AND HIGHWAYS	12/2003	199.81	385.13	185.32
27	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	212.00	386.10	174.10
28	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196.00	363.74	167.74
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	280.13	125.09
30	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	SHIPPING AND PORTS	11/2007	1228.00	2098.56	870.56
31	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	SHIPPING AND PORTS	10/2002	150.00	600.00	450.00
32	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	373.22	127.55
33	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	STEEL	10/2005	8692.00	12291.00	3599.00
34	REVAMPING OF SINTER MACHINES - 1 AND 2	STEEL	12/2009	343.00	488.40	145.40
35	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	5214.00
36	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	URBAN DEVELOPMENT	11/2006	114.18	173.08	58.90

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns in absolute term are as below:-

Sector Wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns
(as on 31-01-2015)

SN	PROJECT	SECTOR	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	ANTICIPATED COST (Rs; crore)	COST OVERRUN (Rs; crore)
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13171.00	22462.00	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3492.00	5677.00	62.57
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	CIVIL AVIATION	05/2010	335.61	388.53	15.77
4	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	478.50
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2030.78	3388.61	66.86
6	MAGADH OC 20 MTY (CCL)	COAL	08/2008	469.78	706.40	50.37
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	COAL	05/2008	4904.54	6602.74	34.63
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	COAL	11/2009	150.59	198.59	31.87
9	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5460.61	8920.00	63.35
10	DEV OF G1 AND GS-15 (ONGCL)	PETROLEUM	04/2003	429.82	3955.21	820.20
11	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3248.78	5633.44	73.40
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	PETROLEUM	01/2006	993.00	1693.00	70.49
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	PETROLEUM	01/2006	732.00	1227.00	67.62
14	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	232.00	63.54
15	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	07/1998	368.72	1259.80	241.67
16	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6285.33	15300.00	143.42

17	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	842.77	100.18
18	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	1128.38	96.59
19	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1061.38	1929.15	81.76
20	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL),NEFR	RAILWAYS	04/1983	36.80	1336.57	3531.98
21	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	111.90	2371.85	2019.62
22	AKOLA-KHANDWA GC AKOLA-AKOT	RAILWAYS	04/2008	184.26	2000.00	985.42
23	BANGLORE - SATYAMANGALAM (NL)(SWR)	RAILWAYS	04/1996	138.00	1382.78	902.01
24	HUBLI- ANKOLA(NL),SWR	RAILWAYS	04/1997	227.00	2135.00	840.53
25	PANIPAT- JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1108.00	2288.00	106.50
26	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	ROAD TRANSPORT AND HIGHWAYS	12/2003	199.81	385.13	92.75
27	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196.00	363.74	85.58
28	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH- 54	ROAD TRANSPORT AND HIGHWAYS	12/2003	212.00	386.10	82.12
29	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	280.13	80.68
30	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	SHIPPING AND PORTS	10/2002	150.00	600.00	300.00
31	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	SHIPPING AND PORTS	11/2007	1228.00	2098.56	70.89
32	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	373.22	51.92
33	REVAMPING OF SINTER MACHINES - 1 AND 2	STEEL	12/2009	343.00	488.40	42.39
34	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT	STEEL	10/2005	8692.00	12291.00	41.41

	(RINL)					
35	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	81.53
36	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	URBAN DEVELOPMENT	11/2006	114.18	173.08	51.59

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 745 projects, 6 projects are ahead of schedule, 122 are on schedule and 317 are delayed with respect to original schedule. However, the number of delayed projects decreases to 296 if delay is calculated on the basis of latest schedule of completion. Further, 35 projects have been sanctioned without any commissioning schedule/date and for 265 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 317 delayed projects, 71 projects have overall delay in the range of 1 to 12 months, 72 projects have delay in the range of 13 to 24 months, 101 projects have delay in the range of 25 to 60 months and 73 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns are as below:-

Sector Wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (as on 31-01-2015)

SN	PROJECT	SECTOR	DATE OF APPROVAL	ORIGINAL DTE OF COMMISSIO NING	ANTICIPATE D DATE OF COMMISSIO NING	TIME OVERRUNS (in months)
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	12/2008	04/2015	76
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	09/2010	09/2016	72
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	ATOMIC ENERGY	10/2009	12/2015	10/2017	22
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	ATOMIC ENERGY	10/2009	12/2016	05/2018	17
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	01/2011	06/2016	65
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	CIVIL AVIATION	05/2010	05/2012	02/2015	33

7	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	CIVIL AVIATION	02/2010	03/2014	03/2015	12
8	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	CIVIL AVIATION	10/2012	03/2015	09/2015	6
9	BALRAM OCP EXTENSION,MCL 8.00 MTY	COAL	12/2007	03/2010	03/2017	84
10	KULDA OCP (MAHANADI COALFIELDS LTD)	COAL	01/2005	03/2010	03/2017	84
11	ASHOK EXPN OCP CCL (10 MTY)	COAL	12/2007	03/2011	03/2017	72
12	JHANJRA R-VI SEAM PSLW	COAL	11/2006	03/2011	03/2017	72
13	GOPAL PRASAD OCP (15MTY)	COAL	02/2008	03/2015	03/2021	72
14	DEV OF G1 AND GS-15 (ONGCL)	PETROLEUM	04/2003	04/2006	06/2015	110
15	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	01/2013	02/2019	73
16	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	08/2010	05/2015	57
17	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	PETROLEUM	06/2007	09/2011	12/2015	51
18	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	PETROLEUM	12/2009	06/2011	07/2015	49
19	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	07/1998	07/2006	10/2016	123
20	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	09/2009	03/2019	114
21	BARH STPP(3X660MW) NTPC	POWER	02/2005	12/2009	03/2018	99
22	TEHRI PUMPED STORAGE PLANT(1000MW)	POWER	07/2006	07/2010	05/2018	94
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	12/2007	06/2015	90
24	GONDIA-JABALPUR(GC),(SECR)	RAILWAYS	02/1997	03/1998	12/2019	261
25	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	11/2002	12/2018	193
26	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	03/2005	12/2019	177
27	TAMLUK DIGHA,LINE DOUBLING (SER)	RAILWAYS	03/1984	06/2005	12/2019	174
28	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	RAILWAYS	03/1996	03/2004	03/2016	144
29	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	ROAD TRANSPORT AND HIGHWAYS	12/2003	06/2005	12/2015	126
30	AGRA-BYPASS(NS-1/UP-1), NH-2,3	ROAD TRANSPORT AND HIGHWAYS	12/2003	09/2007	06/2015	93

31	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	09/2007	03/2015	90
32	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	09/2007	02/2015	89
33	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHA)	ROAD TRANSPORT AND HIGHWAYS	12/2003	06/2008	09/2015	87
34	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	SHIPPING AND PORTS	11/2007	12/2010	01/2016	61
35	AUGMENTATION OF IRON ORE STORAGE IN RMHP	STEEL	07/2007	09/2009	06/2015	69
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	STEEL	10/2005	10/2009	04/2015	66
37	EXPANSION OF BOKARO STEEL PLANT	STEEL	05/2010	12/2011	05/2015	41
38	BAILADILA IRON ORE PROJECT DEPOSIT-11B (NMDC)	STEEL	01/2007	12/2011	03/2015	39
39	EXPANSION OF BHILAI STEEL PLANT	STEEL	08/2010	03/2013	09/2015	30
40	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	TELECOMMUNICATIONS	06/2007	01/2009	03/2015	74
41	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	TELECOMMUNICATIONS	10/2009	10/2010	09/2015	59
42	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	URBAN DEVELOPMENT	01/2009	06/2012	05/2015	35
43	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	URBAN DEVELOPMENT	06/2010	03/2012	01/2015	34
44	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	URBAN DEVELOPMENT	05/2009	05/2013	10/2015	29
45	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	URBAN DEVELOPMENT	12/2012	12/2014	12/2016	24
46	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	URBAN DEVELOPMENT	07/2012	08/2014	01/2016	17

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during January 2015, out of 745 projects, 229 projects reported cost overruns and 317 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 31% whereas projects reporting time overruns have increased to 39% from 43% (Annexure 9 (a) & 9 (b)).

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector Wise List of Earliest Projects (Maximum Five in Numbers) Without Milestones
(as on 31-01-2015)**

S N	PROJECT	DATE OF APPROVAL	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING	MILESTONE
CIVIL AVIATION								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	314.61	16.59	N.R.	N.R.	0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	217.60	0.04	03/2015	03/2016	0
3	GAGAN PROJECT	09/2008	626.00	626.00	499.08	06/2013	06/2013	0
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	285.00	05/2012	11/2014	0
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	452.00	321.56	03/2015	02/2015	0
COAL								
1	RAJMAHAL OC EXP.	09/2009	153.82	153.82	44.47	03/2014	03/2016	0
2	SONEPUR BAZARI (COMB) OCP (8.0	08/2012	1055.05	1055.05	40.13	03/2018	03/2018	0

	MTY)							
3	KAPURIA UG(PSLW)	08/2011	988.35	988.35	6.84	04/2017	04/2017	0
4	MOONIDIH XV SEAM UG	08/2011	1230.27	1230.27	1000.00	04/2015	04/2019	0
5	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020	0
	PETROLEUM							
1	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	08/2010	8140.00	8140.00	7117.42	02/2014	12/2014	0
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	246.81	276.83	262.21	08/2012	10/2014	0
3	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	08/2008	144.02	204.29	155.22	06/2012	12/2014	0
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	470.27	09/2011	12/2015	0
5	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	270.00	270.00	NR	12/2014	03/2016	0
	POWER							
1	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	6285.33	15300.00	7019.81	09/2010	12/2018	0
2	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION	06/2012	1909.24	1909.24	639.63	06/2015	06/2015	0
3	EASTERN REGION STRENGTHENING SCHEME-XII	05/2014	522.29	522.29	NR	11/2016	11/2016	0
4	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	03/2014	155.57	155.57	NR	03/2016	05/2016	0
5	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	03/2012	198.63	198.63	12.80	09/2014	06/2016	0
	RAILWAYS							
1	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	548.01	199.92	NR	NR	0
2	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	406.99	141.55	NR	NR	0
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	595.67	03/1994	10/2014	0
4	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	703.18	255.54	NR	NR	0
5	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	445.40	180.72	03/2007	03/2015	0
	ROAD TRANSPORT AND HIGHWAYS							
1	LUCKNOW-RAIBAREILI	07/1999	635.90	635.90	608.30	07/2012	09/2014	0

2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	3466.00	11/2011	03/2015	0
3	CHILKALURIPET- VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	05/2009	572.30	572.30	886.90	10/2011	06/2015	0
4	CHENNAI-TADA(SIX LANE)	04/2009	353.37	353.37	446.20	10/2011	12/2014	0
5	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	486.00	486.00	667.10	05/2010	12/2014	0
SHIPPING AND PORTS								
1	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	702.00	755.50	219.00	03/2011	03/2013	0
2	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	800.00	1571.60	9.70	10/2008	NR	0
3	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	11/2014	0
4	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	NR	0
5	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	882.00	1060.00	0.93	02/2011	12/2012	0
STEEL								
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	15525.00	5615.00	05/2015	12/2016	0
TELECOMMUNICATIONS								
1	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	48.95	10/2010	03/2015	0
2	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	195.94	01/2009	12/2014	0
3	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL	01/2009	149.15	158.72	86.05	06/2009	12/2014	0
URBAN DEVELOPMENT								
1	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	12/2012	315.00	315.00	53.96	06/2015	08/2015	0
2	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL	12/2012	188.87	188.87	10.64	12/2014	12/2016	0
3	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB	11/2012	238.43	238.43	0.00	02/2015	08/2015	0
4	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	270.83	270.83	15.60	11/2014	10/2015	0

5	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	2727.89	2727.89	2637.11	03/2010	10/2014	0
---	--	---------	---------	---------	---------	---------	---------	---

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest projects (maximum five in numbers) without revised cost estimates are as below:

Sector Wise List of Earliest Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-01-2015)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL COST (Rs; crore)	REVISED COST (Rs; crore)	CUMMULATIVE EXPENDITURE (Rs; crore)
	CIVIL AVIATION				
1	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	NR	318.28
	COAL				
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3027.59	3095.79
2	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1228.77
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	NR	8156.90
	PETROLEUM				
1	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5867.78
	POWER				
1	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	NR	712.66
2	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	NR	4789.81
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	NR	7057.12
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	NR	3509.85
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	NR	1606.79
	RAILWAYS				
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	36.00	255.54
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	NR	201.25

3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	NR	710.57
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10205.04
5	CUTTACK - BARANG (LD)	04/1995	127.13	NR	211.48
	ROAD TRANSPORT AND HIGHWAYS				
1	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	457.70
2	DHARAMTUL TO SONAPUR (AS-19)	12/2003	200.00	NR	289.50
3	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	NR	211.80
4	NALBARI T BIJNI (AS-7)	12/2003	208.00	230.00	334.10
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	NR	276.70
	SHIPPING AND PORTS				
1	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	298.17	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector Wise List of Earliest Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule(as on 31.01.2015)

SN	PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
	COAL				
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
	PETROLEUM				
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.

2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING - XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.

3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.
4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10.The Sector-wise details of additional delays are as under:-

i) In the Coal Sector, out of 68 projects, 36 projects are delayed. During the month, 4 projects have reported additional delay in the range of 8-36 months. The project 'Kalyanikhani Opencast Project, SCCL' has reported additional delay of 8 months due to delay in land acquisition and rehabilitation & resettlement problems; the project 'Kakatiya Longwall, SCCL' has reported additional delay of 24 months due to contractual issue; the projects 'Kistaram OCP, SCCL' and 'JalagamVengala Rao OCP-II, SCCL' have reported additional delays of 36 months each due to delay in diversion of forest land and rehabilitation & resettlement problems.

ii) In the Railways Sector, out of 290 projects, 31 projects are delayed. During the month, 4 projects have reported additional delays in the range of 2-11 months, out of which 1 is mega projects. The projects 'Bandel-Naihati New Rail Bridge in Replacement of Jubilee Bridge No.8, ER' and 'Running of 12 Car Trains on Harbour Line, MRTP' have reported additional delays of 2 and 11 months respectively; and the projects 'Muneerabad-Mahaboobnagar (New Line), SCR' and 'Gonda-Gorakhpur Loop with

Anand Nagar-Nautanwa GC, NER' have reported additional delays of 3 months each (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

- iii) In the **Petroleum Sector**, out of 70 projects, 43 projects are delayed. During the month, 7 projects have reported additional delays in the range of 1-23 months, out of which 2 are Mega projects. The project 'Marketing Terminal at Paradeep IOCL' has reported additional delay of 1 month due to delay in approval from East Coast Railway; the project '102 MW Wind Power Project ONGC' has reported additional delay of 3 months due to change in scope of works; the project 'Mounded Bullet Project, CPCL' has reported additional delay of 4 months due to delay in sand filling at construction site; the projects 'Mangalore Hassan Mysore Solur LPG Pipeline, HPCL' and 'Uran Chakan/Shikrapur LPG Pipeline, HPCL' have reported additional delays of 12 months each due to law & order and delay in forest clearance; and the projects 'Integrated Development of B-127 Fields, ONGC' and 'Revamp of Unmanned Platforms PH-II in MH and NH Assets, ONGC' have reported additional delays of 12 and 23 months respectively (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).
- iv) In the **Power Sector**, out of 104 projects, 63 projects are delayed. During the month, 15 projects have reported additional delays in the range of 1-11 months, out of which 10 are Mega projects. The projects 'System Strengthening In Wardha-Aurangabad Corridor for IPP Projects in Chattisgarh, PGCIL' and 'System Strengthening -XIX in Southern Regional Grid, PGCIL' have reported additional delays of 1 month each due to ROW problems and delay in supply of materials respectively; the projects 'Transmission System for IPP Generation Projects in MP and Chattisgarh, PGCIL' and 'Transmission System Strengthening in Western Part of WR for IPPS Generation Projects in Chattisgarh, PGCIL' have reported additional delays of 2 months each due to delay in land acquisition and ROW problems respectively; the projects 'Transmission System of Vindhuachal-IV and Rihand -III Generation Projects, PGCIL' and 'Northern Region System Strengthening Scheme XVI, PGCIL' have reported additional delays of 3 months each due to delay in wild life sanctuary clearance; the projects 'Transmission System for Phase-1 Generation Projects in Jharkhand and West Bengal-Part-A1, PGCIL' and 'Northern Region System Strengthening Scheme-XXIV, PGCIL' have reported additional delays of 3 months each due to delay in forest clearance; the project 'System Strengthening XIII of SR Grid, PGCIL' has reported additional delay of 3 months due to ROW problems; the Projects 'System Strengthening of Southern Region- XIV, PGCIL' and 'System Strengthening-

XVIII in Southern Region Grid, PGCIL' have reported additional delays of 4 months each due to ROW problems; the project 'Transmission System for Phase-I Generation Projects in Orissa-Part B, PGCIL' has reported additional delay of 4 months due to forest clearance; the projects 'Common System Associated With East Coast Energy Pvt. Ltd. and NCC Power Projects Ltd., PGCIL' and 'System Strengthening in Raipur-Wardha Corridor for IPP Projects in Chhattisgarh, PGCIL' have reported additional delays of 6 and 11 months respectively due to delay in forest clearance; and the project 'Agartala Gas Turbine Plant Combined Cycle Extension Project (51 MW), NEEPCO' has reported additional delay of 2 months (however, no specific reasons have been reported by the project implementing agency for the delay in this project).

- v) In the **Road and Transport Highways Sector**, out of 135 projects, 102 projects are delayed. During the month 33 projects have reported additional delays in the range of 1-27 months, out of which 1 is Mega project. 7 projects have reported additional delay of 1 month each due to delay in land acquisition and utility of shifting; 4 projects have reported additional delay of 2, 3 and 4 months due to fund constraints and utility of shifting; 4 projects have reported additional delay of 5 months each due to delay in land acquisition and fund constraints; 2 projects have reported additional delay of 6 month each due to delay in land acquisition; 2 projects have reported additional delay of 7 and 8 months respectively due to delay in land acquisition; 3 projects have reported additional delay of 9 months each due to delay in land acquisition and fund constraints; the projects 'Patna-Baktzarpur Km.181.3 To Km.231.95, NHAI' has reported additional delay of 10 months due to delay in land acquisition; the project 'Samaikhiali-Gandhidham, NHAI' has reported additional delay of 12 months due to delay in forest clearance; the projects 'Patna-Muzzaffarpur, NHAI' and 'Chennai-Tada(Six Lane), NHAI' have reported additional delays of 14 and 18 months respectively due to utility shifting; the project 'Deoli-Kota, NHAI' has reported additional delay of 15 months due to fund constraints; the projects 'Barsat-Krishnanagar, NHAI' and 'Rohtak-Bawal, NHAI' have reported additional delays of 10 and 19 months; the projects '2-Lanning With PS Khagaria-Purnea, NHAI' and 'Jaipur-Reengus, NHAI' have reported additional delays of 20 and 25 months; and the projects 'Hazaribagh-Ranchi, NHAI' and 'Jaipur-Tonk-Deoli, NHAI' has reported additional delay of 26 and 27 months respectively (however, no specific reasons have been reported by the project implementing agency for the delay in this project).


11. The status as on 31.01.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	290	4
2	ROAD TRANSPORT AND HIGHWAYS	135	33
3	POWER	104	15
4	PETROLEUM	70	7
5	COAL	68	4
6	URBAN DEVELOPMENT	31	0
7	STEEL	24	0
8	CIVIL AVIATION	7	0
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	0
11	TELECOMMUNICATIONS	3	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
	Total	745	63

Sectoral break up of on-going infrastructure projects.

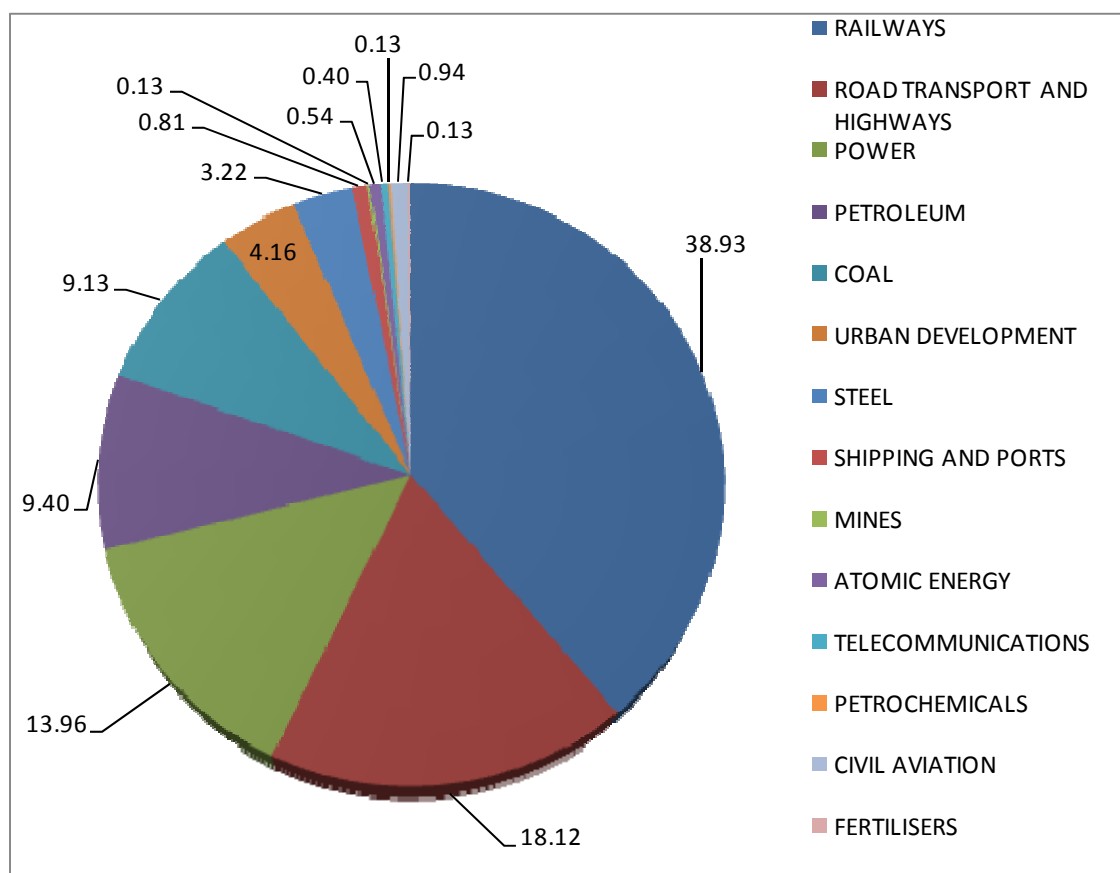

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	COAL			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	POWER			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2,349.46
	June,2014			
	PETROLEUM			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3,918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1,165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2,795.50
	POWER			
6	MOUDA STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4,056.00
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	3,401.00
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4,357.00
	RAILWAYS			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	ROAD TRANSPORT AND HIGHWAYS			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.40
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.50
	July,2014			
	STEEL			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000068]	202.00	01/2010	294.84
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM (RASTRIYA ISPAT NIGAM LIMITED) - [N12000069]	260.00	12/2009	260.75
	PETROLEUM			
14	DEVELOPMENT OF C-SERIES FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000023]	3,195.16	12/2008	3,886.15
15	DEVELOPMENT OF B-22 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000032]	2,323.40	09/2010	1,916.10
16	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000069]	3,284.00	09/2011	1,916.30
17	ADDITIONAL DEV. OF D-1 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000086]	2,163.64	06/2012	2,182.31
	POWER			
18	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000106]	425.51	10/2013	386.32
	TELECOMMUNICATIONS			
19	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB (BHARAT SANCHAR NIGAM LIMITED) - [N26000041]	373.94	12/2008	227.58
20	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT (BHARAT SANCHAR NIGAM LIMITED) - [N26000072]	952.88	03/2010	20.00
21	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT (BHARAT SANCHAR NIGAM LIMITED) - [N26000073]	152.65	03/2010	29.05
22	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000088]	328.13	03/2009	164.58
23	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000090]	916.70	11/2010	828.48
	August,2014			
	PETROLEUM			
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000070]	238.68	01/2012	293.12
25	SINGLE POINT MOORING FACILITY(SMP) PROJECT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000152]	1,043.57	04/2012	648.92
	SHIPPING AND PORTS			
26	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN (PORT TRUST) - [N25000048]	3,500.00	01/2012	3,661.95

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	September,2014			
	CIVIL AVIATION			
27	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000037]	1,942.51	05/2011	2,573.92
28	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000038]	1,808.00	01/2011	1,939.20
	October,2014			
	PETROLEUM			
29	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) (GAS AUTHORITY OF INDIA LIMITED) - [N16000094]	540.92	06/2011	340.94
30	MRPL PHASE-III EXPANSION (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000114]	12,412.00	01/2012	12,205.74
	POWER			
31	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000063]	184.19	11/2011	165.67
32	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000111]	1,637.34	08/2014	1,499.95
	TELECOMMUNICATIONS			
33	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II (BHARAT SANCHAR NIGAM LIMITED) - [N26000100]	1,148.19	05/2011	251.27
	November,2014			
	PETROLEUM			
34	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000138]	246.81	08/2012	263.59
	POWER			
35	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000107]	1,391.97	12/2013	1,472.35
36	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000121]	324.33	08/2014	211.36
	SHIPPING AND PORTS			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
37	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL (PORT TRUST) - [N25000003]	800.00	10/2008	9.70
38	DEEPENING OF CHANNEL AT PARADIP PORT (PORT TRUST) - [N25000004]	154.84	-	247.89
39	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS (SHIPPING CRP. OF INDIA) - [N25000014]	359.44	04/2011	218.00
40	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA, KANDLA PORT TRUST (PORT TRUST) - [N25000037]	882.00	02/2011	1,098.00
41	ACQUISITION OF TWO NOS. OF 3060 DWT (SHIPPING CRP. OF INDIA) - [N25000043]	277.03	12/2011	263.08
42	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES (SHIPPING CRP. OF INDIA) - [N25000051]	612.72	12/2012	513.36
43	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. (SHIPPING CRP. OF INDIA) - [N25000052]	1,028.10	12/2013	554.60
44	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY (SHIPPING CRP. OF INDIA) - [N25000053]	966.46	02/2014	427.54
45	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER (SHIPPING CRP. OF INDIA) - [N25000061]	220.49	01/2013	47.32
46	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY (SHIPPING CRP. OF INDIA) - [N25000062]	511.87	03/2014	106.72
	TELECOMMUNICATIONS			
47	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL (BHARAT SANCHAR NIGAM LIMITED) - [N26000058]	149.15	06/2009	86.34
	December, 2014			
	STEEL			
48	COKE OVEN BATTERY NO. 4 PHASE-II (RASTRIYA ISPAT NIGAM LIMITED) - [N12000038]	108.00	09/2008	168.10
49	EXPANSION OF IISCO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000051]	14,443.00	12/2011	16,640.88
50	EXPANSION OF ROURKELA STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000056]	11,812.00	03/2013	11,681.80
	PETROLEUM			
51	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000068]	3,597.00	09/2011	2,299.22
52	POLYPROPYLENE UNIT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000113]	1,803.78	07/2012	995.25
53	GAS TURBINE GENERATION SET (OIL INDIA LIMITED) - [N18000146]	216.88	10/2011	187.14
54	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT (OIL INDIA LIMITED) - [N18000149]	144.02	06/2012	161.88

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	POWER			
55	RAMPUR HEP(412 MW) (SATLUJ JAL VIDYUT NIGAM LIMITED) - [N18000024]	2,047.03	03/2012	3,350.71
56	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000065]	2,360.95	08/2012	2,150.11
57	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000069]	7,075.33	08/2012	6,413.96
	ROAD TRANSPORT AND HIGHWAYS			
58	AMRITSAR-PATHANKOT (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000147]	705.00	11/2012	2,208.00
	SHIPPING AND PORTS			
59	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS (PORT TRUST) - [N25000049]	444.10	06/2010	0.01
	January,2015			
	POWER			
60	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000118]	259.28	01/2014	210.02
61	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000138]	156.04	10/2014	92.86
	RAILWAYS			
62	NEW BG LINE FROM DUDHNOI-MENDIPATAR (NORTH EAST FRONTIER RAILWAY) - [N22000192]	175.43	-	248.12

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2014-2015				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	October,2015			
	<u>PETROLEUM</u>			
1	JHAJJAR HISSAR PIPE LINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N06000019]	281.07	10/2010	6.18
	<u>WATER RESOURCES</u>			
2	PAGLADIYA DAM PROJECT (MINISTRY OF WATER RESOURCES) - [180100250]	542.90	12/2007	35.49


Summary of projects in the Flash Report for the month of January, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	738
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	12
Number of Projects in Current Month	745

Brief Analysis


Project Status with respect to Original Schedule: Out of 745 projects, 6 projects are ahead of schedule, 122 projects are on schedule and 317 projects are delayed. Of the balance, 265 projects do not have fixed dates of commissioning while 35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

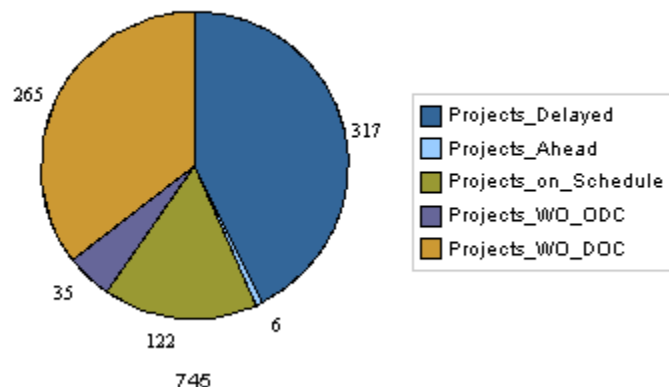

Investment Scenario

Total original cost of implementation of 745 projects when sanctioned, was of the order of Rs. 1030625.7 crore but this was subsequently revised to Rs. 1234992.39 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till January, 2015 is Rs. 535408.6 crore, which is 43.4% of the revised cost of the projects.

Figures are in Rs. Crore

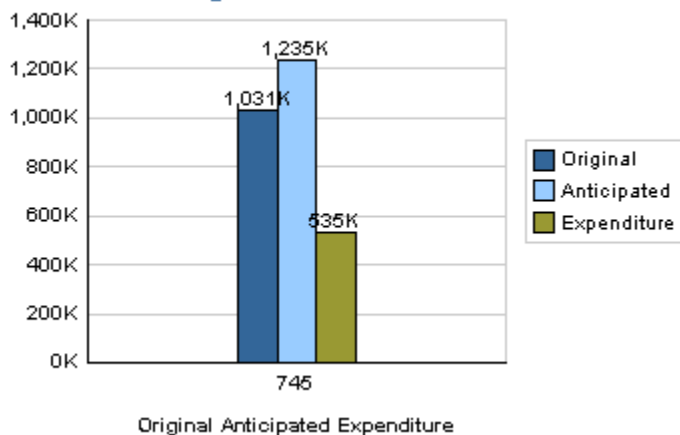

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	738
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects added in Current Month	12
No of Projects in Current Month	745

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	317	6	122	35	265	745	42.55
Latest Approved (Date)	296	8	141	35	265	745	39.73

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	645	8,73,260.85	9,61,034.44	3,64,025.56	37.90	87,773.59	10.10
Project with Revision in Cost	100	2,22,150.17	2,73,957.95	1,71,383.04	62.60	51,807.78	23.30
Total	745	10,95,411.02	12,34,992.39	5,35,408.60	43.35	139581.37	12.74
Original Cost of All Projects							
Original Cost	745	10,30,625.70	12,34,992.39	5,35,408.60	43.40	2,04,366.69	19.80

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	317	527,074.32	645,046.17	390,109.44	60.50	117,971.85	22.40
Latest Approved (RCE)	299	537,891.77	596,100.67	366,011.70	61.40	58,208.90	10.80
Total	616	1,064,966.09	1,241,146.84	756,121.14	60.92	176180.75	16.54

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	71	99,435.90	104,415.94	62,305.38	59.70	4,980.04	5.00
Total	71	99,435.90	104,415.94	62,305.38	59.67	4980.04	5.01

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	15.77
3	COAL	68	56,782.14	54,116.57	-4.69	6	8,258.03	12,614.83	52.76
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	24	59,425.03	63,139.43	6.25	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
8	PETROLEUM	70	160,327.93	177,780.38	10.89	19	72,745.78	92,727.18	27.47
9	POWER	104	279,823.29	314,625.85	12.44	23	54,636.73	89,439.29	63.70
10	RAILWAYS	290	164,087.03	291,582.03	77.70	161	83,322.14	211,725.89	154.11
11	ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	103,683.44	2.03	9	2,866.62	4,961.13	73.07
12	SHIPPING AND PORTS	6	5,158.07	6,397.71	24.03	3	1,623.67	3,071.78	89.19
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	31	138,795.00	144,067.90	3.80	2	6,509.18	11,782.08	81.01
Total		745	1,030,625.70	1,234,992.39	19.83	229	261,456.37	476,549.11	82.27

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	26	24,304.01	30,386.09	25.03	7	11,072.36	17,154.44	54.93
2	ARUNACHAL PRADESH	3	9,356.22	21,082.33	125.33	3	9,356.22	21,082.33	125.33
3	ASSAM	37	24,084.64	41,735.39	73.29	16	17,342.47	35,110.88	102.46
4	BIHAR	48	37,027.18	51,529.33	39.17	16	14,834.46	29,556.93	99.25
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	29	36,037.34	36,616.51	1.61	4	1,202.26	2,117.22	76.10
7	HARYANA	8	4,259.81	6,230.43	46.26	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	11,681.24	17,740.61	51.87	3	9,493.62	15,552.99	63.83
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	32	64,122.20	78,947.89	23.12	17	13,700.79	28,532.51	108.25
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	18	25,308.88	27,292.80	7.84	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	47	100,936.03	112,834.02	11.79	12	18,391.48	30,841.50	67.69
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,080.05	312.94	2	988.06	4,080.05	312.94
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	41	69,075.15	78,123.21	13.10	14	35,729.75	44,799.15	25.38
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	25	25,638.72	25,694.20	0.22	7	2,850.42	3,418.90	19.94
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	42	68,133.49	90,782.21	33.24	20	30,028.23	52,676.95	75.42
23	TRIPURA	6	2,966.26	7,231.71	143.80	5	2,678.22	6,978.05	160.55
24	UTTAR PRADESH	28	26,759.70	29,864.04	11.60	9	2,951.38	6,103.98	106.82
25	WEST BENGAL	39	42,838.90	52,232.80	21.93	13	5,877.48	15,794.72	168.73
26	CHANDIGARH	1	452.00	452.00	0.00	0	0.00	0.00	0.00
27	DELHI	10	48,728.60	48,728.60	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	27	80,345.96	75,102.05	-6.53	5	1,747.92	2,928.33	67.53
29	JHARKHAND	32	35,868.09	36,532.76	1.85	6	1,641.96	2,478.40	50.94
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	21	9,410.62	12,179.13	29.42	5	1,473.01	4,241.83	187.97
33	MULTI STATE	179	213,390.18	241,772.44	13.30	41	35,013.78	64,707.06	84.80
Total		745	1,030,625.70	1,234,992.39	19.83	229	261,456.37	476,549.11	82.27

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	17 - 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	4	1,206.95	1,259.87	6 - 65
3	COAL	68	56,782.14	54,116.57	-4.69	36	27,555.48	31,685.88	5 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	24	59,425.03	63,139.43	6.25	17	56,370.71	59,939.71	8 - 69
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
8	PETROLEUM	70	160,327.93	177,780.38	10.89	43	92,391.59	106,938.21	3 - 110
9	POWER	104	279,823.29	314,625.85	12.44	63	165,762.16	190,715.54	1 - 123
10	RAILWAYS	290	164,087.03	291,582.03	77.70	31	25,945.26	82,251.23	3 - 261
11	ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	103,683.44	2.03	102	71,897.83	73,964.83	5 - 126
12	SHIPPING AND PORTS	6	5,158.07	6,397.71	24.03	1	1,228.00	2,098.56	61 - 61
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	2	720.81	720.81	59 - 74
14	URBAN DEVELOPMENT	31	138,795.00	144,067.90	3.80	14	43,553.53	43,553.53	2 - 35
Total		745	1,030,625.70	1,234,992.39	19.83	317	527,074.32	645,046.17	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	26	24,304.01	30,386.09	25.03	9	15,170.93	19,863.19	8 - 73
2	ARUNACHAL PRADESH	3	9,356.22	21,082.33	125.33	2	3,070.89	5,782.33	31 - 87
3	ASSAM	37	24,084.64	41,735.39	73.29	28	15,781.02	26,547.87	8 - 126
4	BIHAR	48	37,027.18	51,529.33	39.17	13	22,113.50	32,170.53	7 - 99
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	33 - 33
6	GUJARAT	29	36,037.34	36,616.51	1.61	10	24,354.18	24,277.49	6 - 48
7	HARYANA	8	4,259.81	6,230.43	46.26	3	2,244.00	3,424.00	19 - 61
8	HIMACHAL PRADESH	5	11,681.24	17,740.61	51.87	3	8,717.57	12,856.83	11 - 114
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	10 - 193
10	KARNATAKA	32	64,122.20	78,947.89	23.12	8	19,882.90	20,805.47	2 - 90
11	KERALA	13	24,457.67	28,611.45	16.98	4	2,849.00	3,549.00	25 - 59
12	MADHYA PRADESH	18	25,308.88	27,292.80	7.84	9	4,874.28	4,987.08	5 - 75
13	MAHARASHTRA	47	100,936.03	112,834.02	11.79	25	70,902.38	78,822.33	1 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	536.00	536.00	13 - 13
16	MIZORAM	2	988.06	4,080.05	312.94	2	988.06	4,080.05	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	41	69,075.15	78,123.21	13.10	20	41,703.75	46,835.36	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	25	25,638.72	25,694.20	0.22	10	19,145.38	18,699.10	6 - 84
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 65
22	TAMIL NADU	42	68,133.49	90,782.21	33.24	18	53,100.77	68,012.58	5 - 87
23	TRIPURA	6	2,966.26	7,231.71	143.80	4	2,417.39	5,214.68	25 - 108
24	UTTAR PRADESH	28	26,759.70	29,864.04	11.60	13	10,157.49	11,614.06	5 - 93
25	WEST BENGAL	39	42,838.90	52,232.80	21.93	15	15,551.44	20,445.70	3 - 177
26	CHANDIGARH	1	452.00	452.00	0.00	0	0.00	0.00	-
27	DELHI	10	48,728.60	48,728.60	0.00	4	4,045.16	4,045.16	8 - 29
28	CHHATISGARH	27	80,345.96	75,102.05	-6.53	15	56,292.51	56,292.51	6 - 39
29	JHARKHAND	32	35,868.09	36,532.76	1.85	16	10,850.42	11,371.50	2 - 138
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,605.06	11,048.24	26 - 94
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	21	9,410.62	12,179.13	29.42	8	2,737.82	3,753.87	8 - 51
33	MULTI STATE	179	213,390.18	241,772.44	13.30	62	95,217.81	103,455.90	1 - 261
Total		745	1,030,625.70	1,234,992.39	19.83	317	527,074.32	645,046.17	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	3	36,950.00	46,241.00	17 - 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	4	1,206.95	1,259.87	6 - 65
3	COAL	68	56,782.14	54,116.57	-4.69	36	27,555.48	31,685.88	5 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	24	59,425.03	63,139.43	6.25	16	40,845.71	44,414.71	8 - 69
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	-
8	PETROLEUM	70	160,327.93	177,780.38	10.89	38	87,028.35	96,668.40	3 - 73
9	POWER	104	279,823.29	314,625.85	12.44	59	158,833.35	179,581.75	1 - 123
10	RAILWAYS	290	164,087.03	291,582.03	77.70	28	19,470.26	70,891.98	3 - 261
11	ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	103,683.44	2.03	96	70,676.10	72,651.15	5 - 126
12	SHIPPING AND PORTS	6	5,158.07	6,397.71	24.03	1	1,228.00	2,098.56	61 - 61
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	1	336.81	336.81	74 - 74
14	URBAN DEVELOPMENT	31	138,795.00	144,067.90	3.80	14	43,553.53	43,553.53	2 - 35
Total		745	1,030,625.70	1,234,992.39	19.83	296	487,684.54	589,383.64	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	51,918.00	51,918.00	0.00	0	0.00	0.00	0.00
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	15.77
3	COAL	68	60,363.17	54,116.57	-10.35	4	4,137.96	4,783.70	15.61
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	24	63,024.03	63,139.43	0.18	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	63.35
8	PETROLEUM	70	176,624.17	177,780.38	0.65	6	25,195.31	28,880.47	14.63
9	POWER	104	295,329.03	314,625.85	6.53	11	22,939.25	42,236.07	84.12
10	RAILWAYS	290	177,752.43	291,582.03	64.04	154	87,729.63	202,467.98	130.79
11	ROAD TRANSPORT AND HIGHWAYS	135	101,987.45	103,683.44	1.66	8	2,906.07	4,651.57	60.06
12	SHIPPING AND PORTS	6	5,390.07	6,397.71	18.69	3	1,855.67	3,071.78	65.53
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	31	138,853.90	144,067.90	3.76	1	6,395.00	11,609.00	81.53
Total		745	1,095,411.02	1,234,992.39	12.74	190	157,298.11	307,497.50	95.49

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	1	3,492.00	5,677.00	72- 72
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	0	0.00	0.00	0- 0
3	COAL	68	56,782.14	54,116.57	-4.69	0	0.00	0.00	0- 0
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	24	59,425.03	63,139.43	6.25	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	PETROLEUM	70	160,327.93	177,780.38	10.89	4	5,124.05	10,237.94	8- 110
9	POWER	104	279,823.29	314,625.85	12.44	2	3,023.34	4,585.24	16- 94
10	RAILWAYS	290	164,087.03	291,582.03	77.70	1	5,300.00	6,821.29	60- 60
11	ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	103,683.44	2.03	2	425.61	517.56	69- 86
12	SHIPPING AND PORTS	6	5,158.07	6,397.71	24.03	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	31	138,795.00	144,067.90	3.80	0	0.00	0.00	0- 0
Total		745	1030625.7	1234992.39	19.83	10	17365	27839.03	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 76
2	CIVIL AVIATION	7	2,599.56	2,652.48	2.04	1	335.61	388.53	33- 33
3	COAL	68	56,782.14	54,116.57	-4.69	4	7,617.44	11,926.14	30- 67
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	24	59,425.03	63,139.43	6.25	1	8,692.00	12,291.00	66- 66
7	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	PETROLEUM	70	160,327.93	177,780.38	10.89	12	47,822.86	64,389.97	8- 110
9	POWER	104	279,823.29	314,625.85	12.44	19	42,145.54	64,406.07	7- 123
10	RAILWAYS	290	164,087.03	291,582.03	77.70	27	22,454.90	78,760.89	3- 261
11	ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	103,683.44	2.03	9	2,866.62	4,961.13	40- 93
12	SHIPPING AND PORTS	6	5,158.07	6,397.71	24.03	1	1,228.00	2,098.56	61- 61
13	TELECOMMUNICATIONS	3	14,054.81	14,054.81	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	31	138,795.00	144,067.90	3.80	0	0.00	0.00	0- 0
Total		745	1030625.7	1234992.39	19.83	76	149825.97	267361.29	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	POWER						
1	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	01/2012	259.28	01/2014	259.28	01/2015	210.02
2	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A	12/2012	156.04	10/2014	156.04	01/2015	92.86
	RAILWAYS						
3	NEW BG LINE FROM DUDHNOI-MENDIPATAR	04/1999	175.43	N.A.	275.00	01/2015	248.12

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	COAL					
1	GARJANBAHAL OCP	11/2014	1,375.38	3/2021	1,375.38	3/2021
2	DINESH OCP	11/2014	611.16	3/2020	611.16	3/2020
3	MAKARDHOKRA I OC	9/2014	266.23	3/2021	266.23	3/2021
4	GOKUL	11/2014	267.67	3/2018	267.67	3/2018
	POWER					
5	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	268.80	3/2018	268.80	3/2018
6	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	871.62	10/2017	871.62	10/2017
7	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	203.28	7/2017	203.28	7/2017
8	WARDHA-HYDERABAD 765 KV LINK	1/2015	3,662.02	5/2018	3,662.02	5/2018
	URBAN DEVELOPMENT					
9	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	8/2007	246.90	/	246.90	-
10	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	14,600.00	12/2015	14,600.00	8/2016
11	NAGPUR METRO RAIL	8/2014	8,680.00	3/2018	8,680.00	3/2018
12	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	23,136.00	1/2015	23,136.00	12/2015

Milestones (Cumulative due & achieved)

Total	3591
Achieved up to month	1450

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	KALYANIKHANI OPENCAST PROJECT SCCL	417.33	417.33	07/2016	07/2016	03/2017	8
2	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2017	24
3	KISTARAM OCP SCCL	242.29	242.29	03/2015	03/2015	03/2018	36
4	JALAGAM VENGALA RAO OCP-II SCCL	447.06	447.06	03/2015	03/2015	03/2018	36
	<u>PETROLEUM</u>						
5	MARKETING TERMINAL AT PARADEEP IOCL	199.75	199.75	07/2013	02/2015	03/2015	1
6	102 MW WIND POWER PROJECT ONGC	1,106.00	678.02	06/2012	12/2014	03/2015	3
7	MOUNDED BULLET PROJECT AT CPCL CPCL	279.00	279.00	12/2014	02/2015	06/2015	4
8	INTEGRATED DEVELOPMENT OF B-127 FIELDS ONGC	2,059.63	2,665.65	03/2015	05/2015	05/2016	12
9	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) HPCL	666.00	701.00	11/2015	11/2015	11/2016	12
10	URAN CHAKAN/SHIKRAPUR LPG PIPELINE HPCL	309.81	462.79	10/2014	10/2015	10/2016	12
11	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS ONGC	2,913.10	2,913.10	05/2016	05/2016	04/2018	23
	<u>POWER</u>						
12	SYSTEM STRENGTHENING IN WARDHA- AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH PGCIL	1,310.85	1,310.85	02/2015	02/2015	03/2015	1
13	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID PGCIL	1,935.35	1,935.35	12/2014	02/2015	03/2015	1
14	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH PGCIL	1,366.34	1,606.38	12/2013	02/2015	04/2015	2
15	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	03/2015	05/2015	2

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) NEEPCO	296.87	1,128.38	N.A.	01/2015	03/2015	2
17	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. PGCIL	4,672.99	4,672.99	11/2012	03/2015	06/2015	3
18	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI PGCIL	752.64	752.64	07/2013	03/2015	06/2015	3
19	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 PGCIL	558.26	558.26	11/2013	03/2015	06/2015	3
20	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	03/2015	06/2015	3
21	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	03/2015	06/2015	3
22	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B PGCIL	2,743.19	2,743.19	12/2013	02/2015	06/2015	4
23	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	02/2015	06/2015	4
24	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID PGCIL	1,263.26	1,263.26	11/2014	02/2015	06/2015	4
25	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI PGCIL	1,909.24	1,909.24	06/2015	06/2015	12/2015	6
26	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	01/2015	12/2015	11
	<u>RAILWAYS</u>						
27	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) ER	207.52	207.52	12/2012	07/2015	09/2015	2
28	MUNEERABAD-MAHABOONAGAR(NL),SCR SCR	218.24	645.00	N.A.	12/2014	03/2015	3
29	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) NER	863.23	1,072.51	N.A.	03/2015	06/2015	3
30	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE MRTPT	714.10	714.10	04/2016	04/2016	03/2017	11
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
31	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO NHAI	157.47	154.57	09/2007	01/2015	02/2015	1

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	01/2015	02/2015	1
33	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	01/2015	02/2015	1
34	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY NHAI	600.00	600.00	06/2013	01/2015	02/2015	1
35	JORBAT - BARAPANI NHAI	536.00	536.00	01/2014	01/2015	02/2015	1
36	LUCKNOW-RAIBAREILI NHAI	635.90	635.90	07/2012	01/2015	02/2015	1
37	2 LANING WITH PS KANPUR KABRAI NHAI	373.47	373.47	07/2014	02/2015	03/2015	1
38	REENGUS SIKAR NHAI	333.51	333.51	09/2014	01/2015	03/2015	2
39	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	385.13	04/2009	03/2015	06/2015	3
40	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	03/2015	06/2015	3
41	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	01/2015	05/2015	4
42	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 NHAI	200.00	200.00	04/2009	01/2015	06/2015	5
43	BIJNI TO ASSAM WB BORDER (NH- 31.C)(1)(NHAI) NHAI	195.00	195.00	06/2008	03/2015	08/2015	5
44	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	01/2015	06/2015	5
45	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS NHAI	374.00	374.00	05/2013	12/2014	05/2015	5
46	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C NHAI	230.00	230.00	06/2005	06/2015	12/2015	6
47	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) NHAI	237.80	237.80	06/2008	03/2015	09/2015	6
48	CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	07/2016	02/2017	7
49	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 NHAI	1,813.76	1,813.76	07/2013	01/2015	09/2015	8
50	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 NHAI	232.45	232.45	09/2010	03/2015	12/2015	9
51	KISHANGARH-AJMER-BEAWER NHAI	795.00	795.00	05/2012	12/2014	09/2015	9
52	4-LANNING OF CHAPRA-HAJIPUR NHAI	575.00	575.00	07/2013	03/2015	12/2015	9
53	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI	574.00	574.00	03/2014	01/2015	11/2015	10

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
54	BARSAT-KRISHNANAGAR NHAI	867.00	867.00	02/2015	02/2016	12/2016	10
55	SAMAIKHALI - GANDHIDHAM NHAI	805.39	805.39	03/2013	12/2014	12/2015	12
56	PATNA-MUZZAFFARPUR NHAI	671.30	671.30	02/2013	01/2015	03/2016	14
57	DEOLI-KOTA NHAI	593.00	593.00	07/2013	01/2015	04/2016	15
58	CHENNAI-TADA(SIX LANE) NHAI	353.37	353.37	10/2011	12/2014	06/2016	18
59	ROHTAK-BAWAL NHAI	650.00	650.00	11/2013	11/2013	06/2015	19
60	2-LANNING WITH PS KHAGARIA-PURNEA NHAI	664.00	664.00	02/2014	02/2014	10/2015	20
61	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	02/2013	03/2015	25
62	HAZARIBAGH-RANCHI NHAI	625.07	625.07	01/2013	01/2013	03/2015	26
63	JAIPUR-TONK-DEOLI NHAI	792.06	792.06	12/2012	12/2012	03/2015	27

Graphical Presentation of All Projects w.r.t. Original Schedule

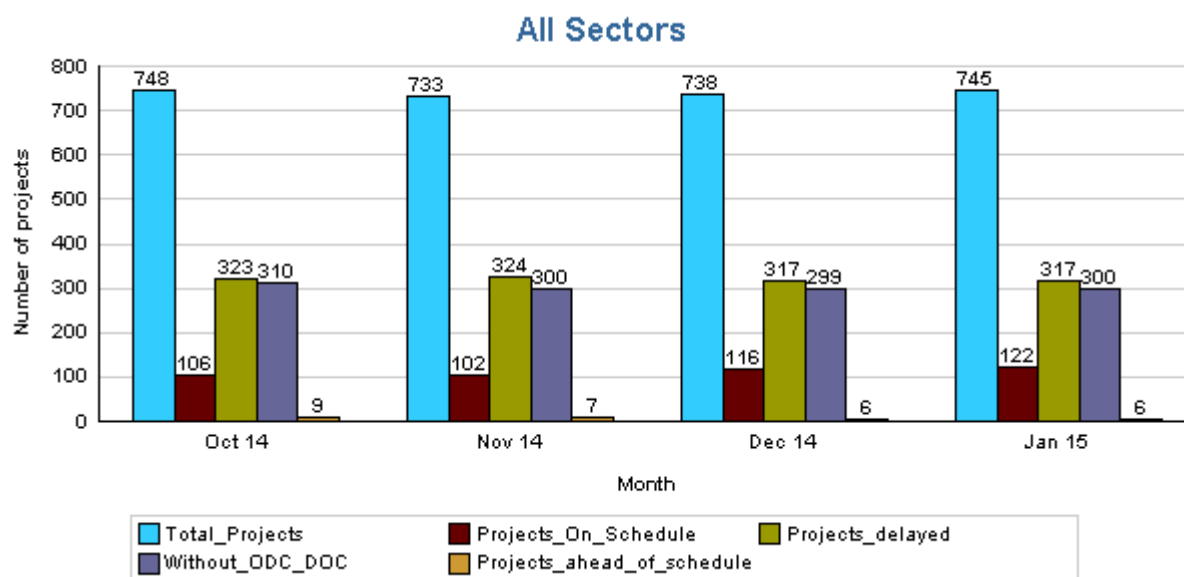

Break-up of 317 Delayed projects in January 2015

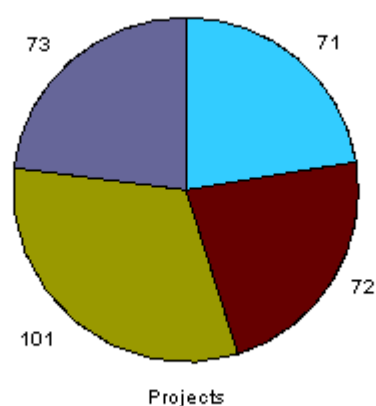


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

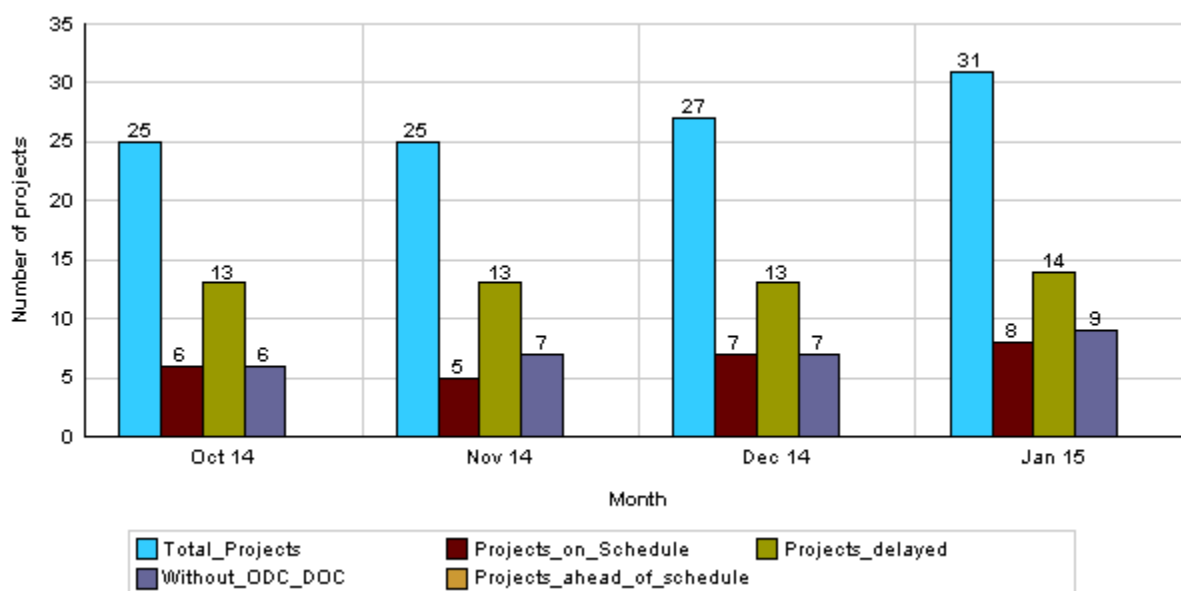


Break-up of 14 Delayed projects in January 2015

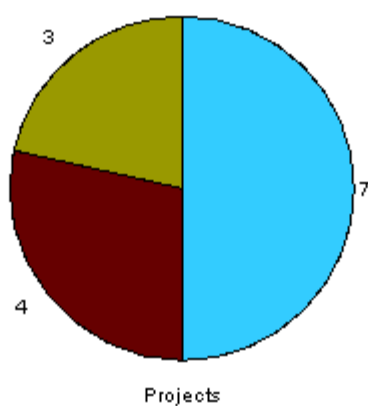


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	7	4	3	0

Graphical Presentation of TELECOMMUNICATIONS Sector

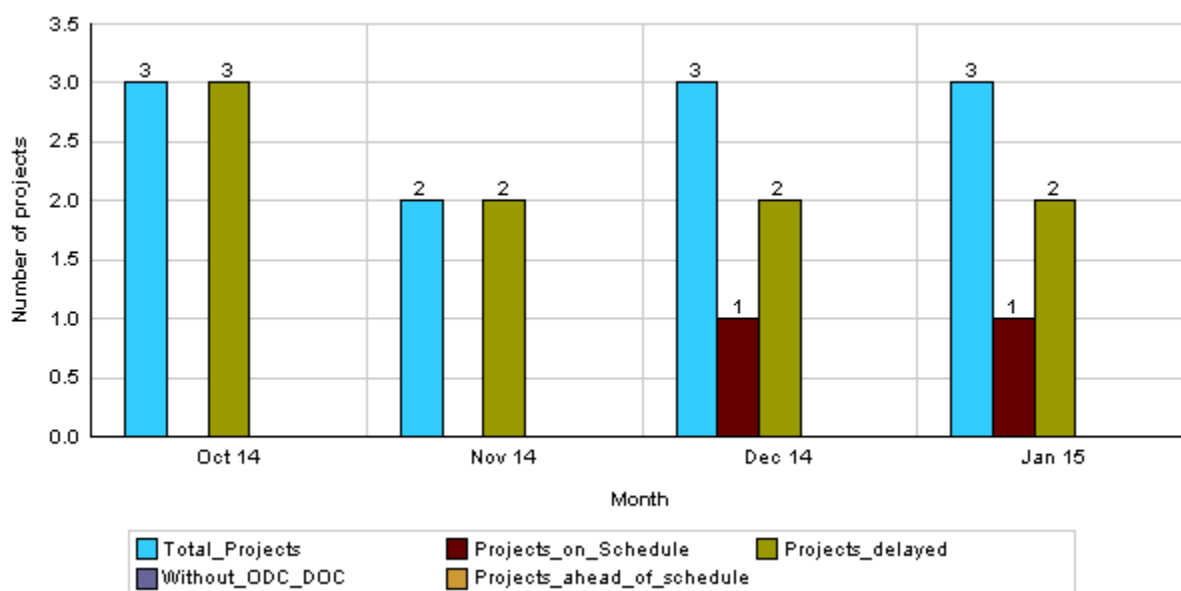


Break-up of 2 Delayed projects in January 2015

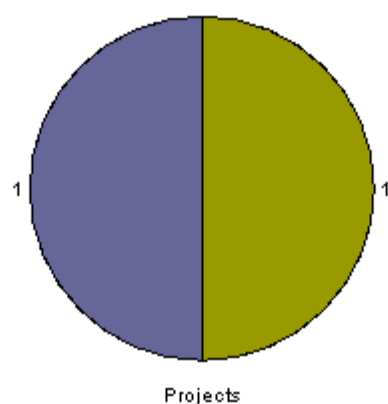

Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of STEEL Sector

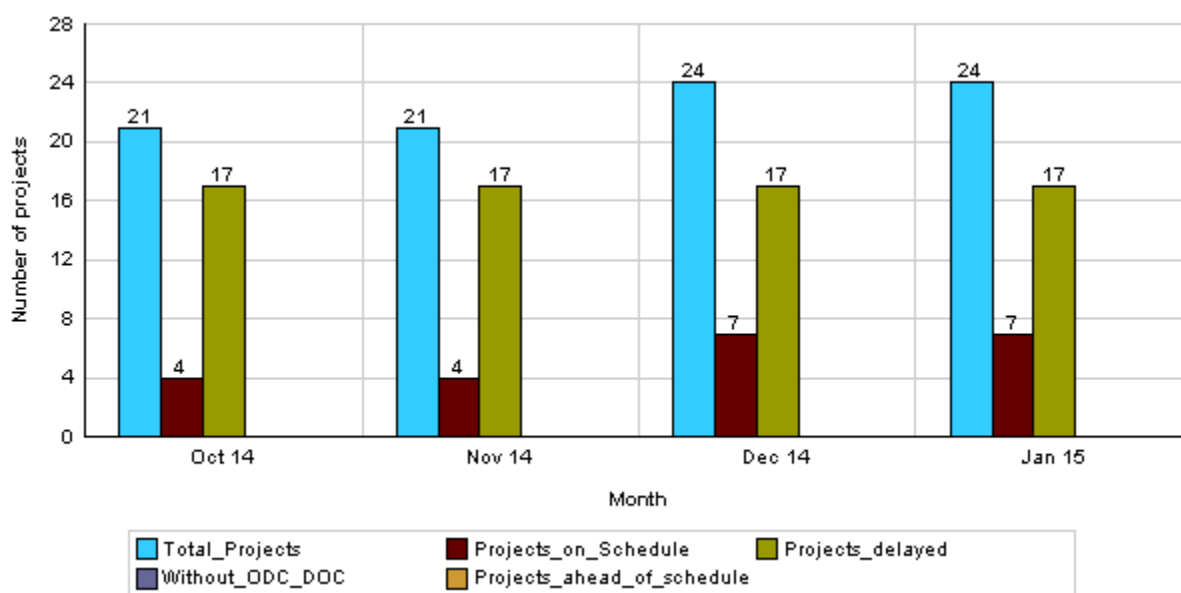


Break-up of 17 Delayed projects in January 2015




Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of SHIPPING AND PORTS Sector

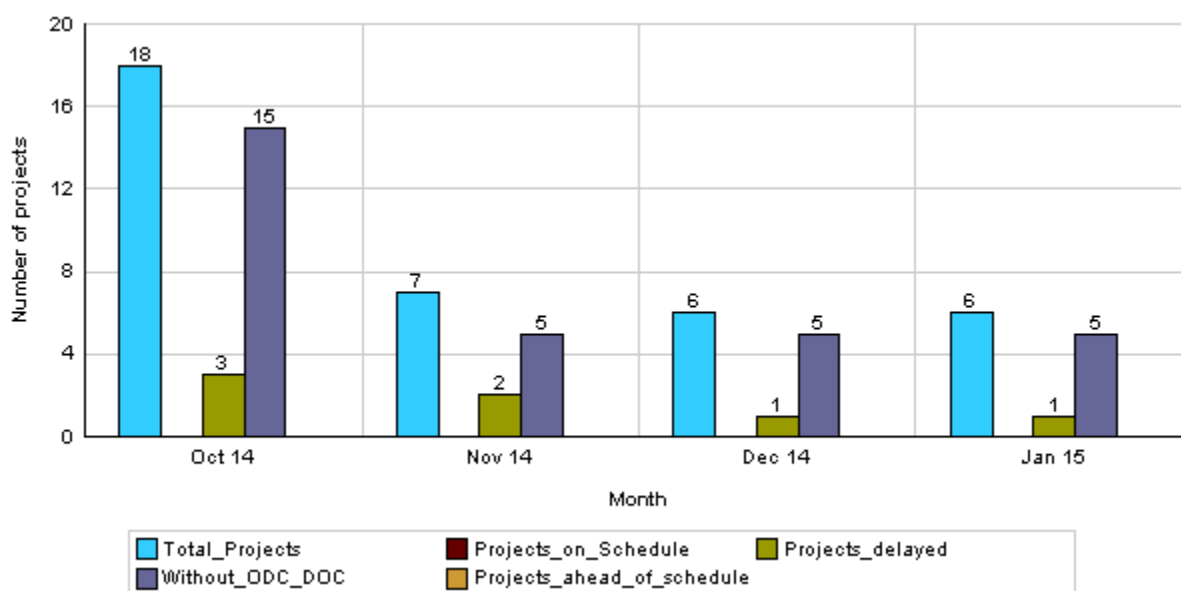


Break-up of 1 Delayed projects in January 2015

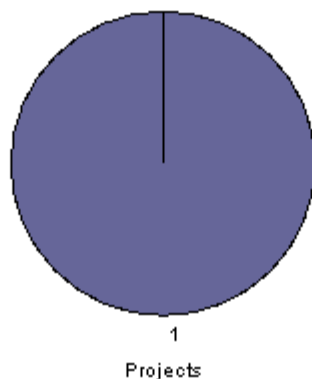


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Count	0	0	0	1

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

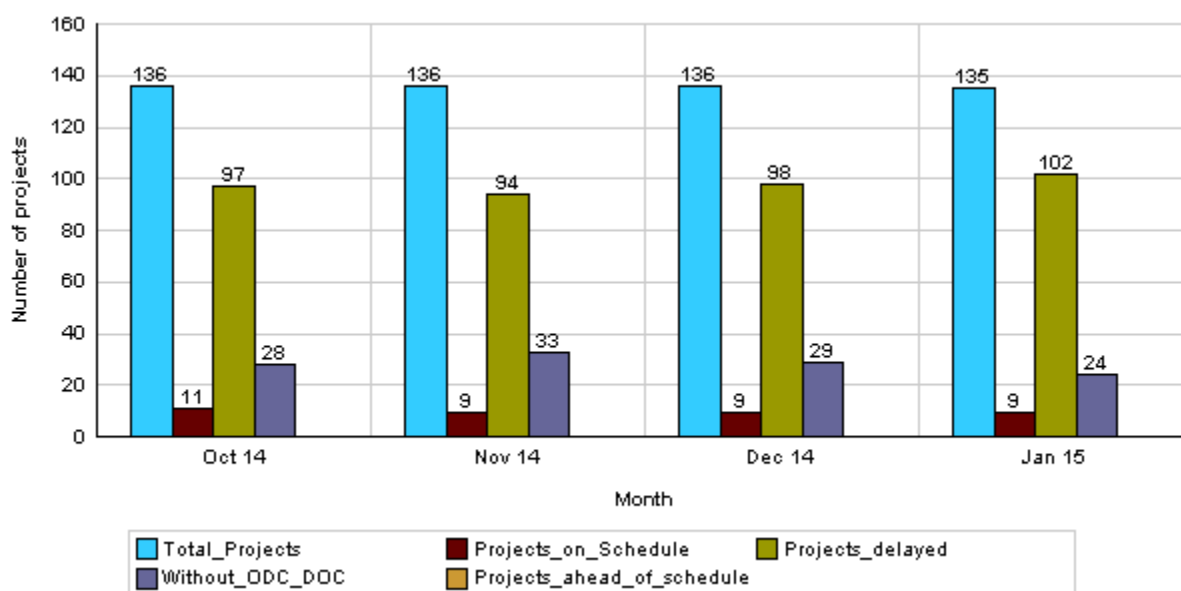


Break-up of 102 Delayed projects in January 2015

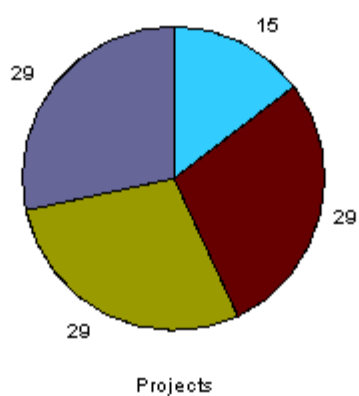


Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of RAILWAYS Sector

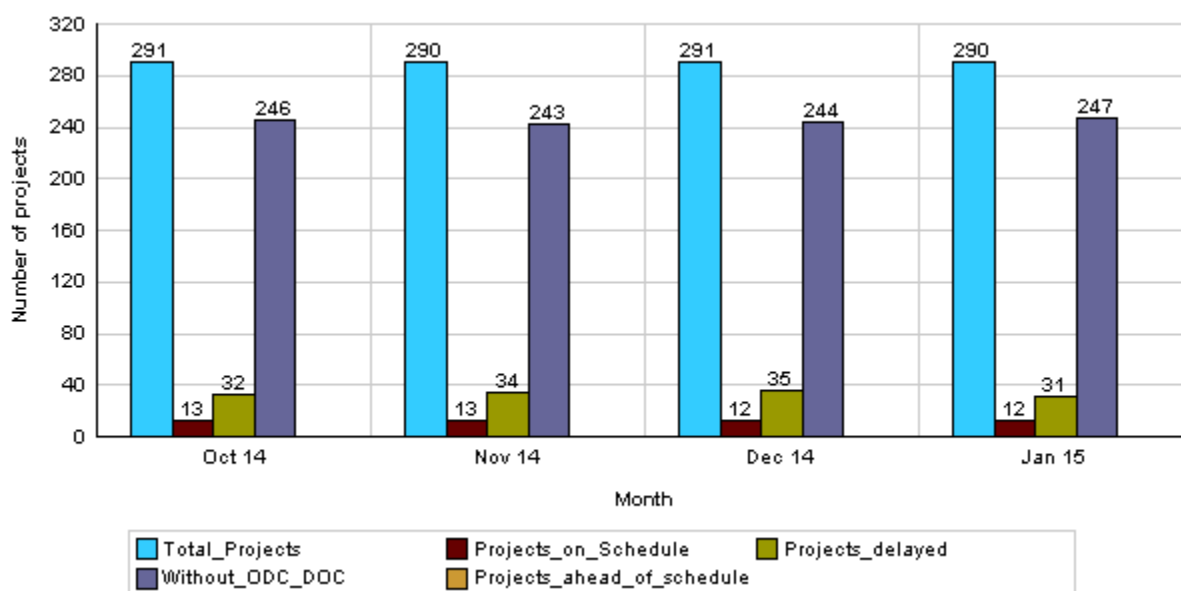

Break-up of 31 Delayed projects in January 2015

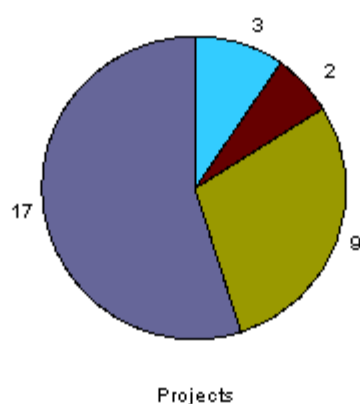


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of POWER Sector

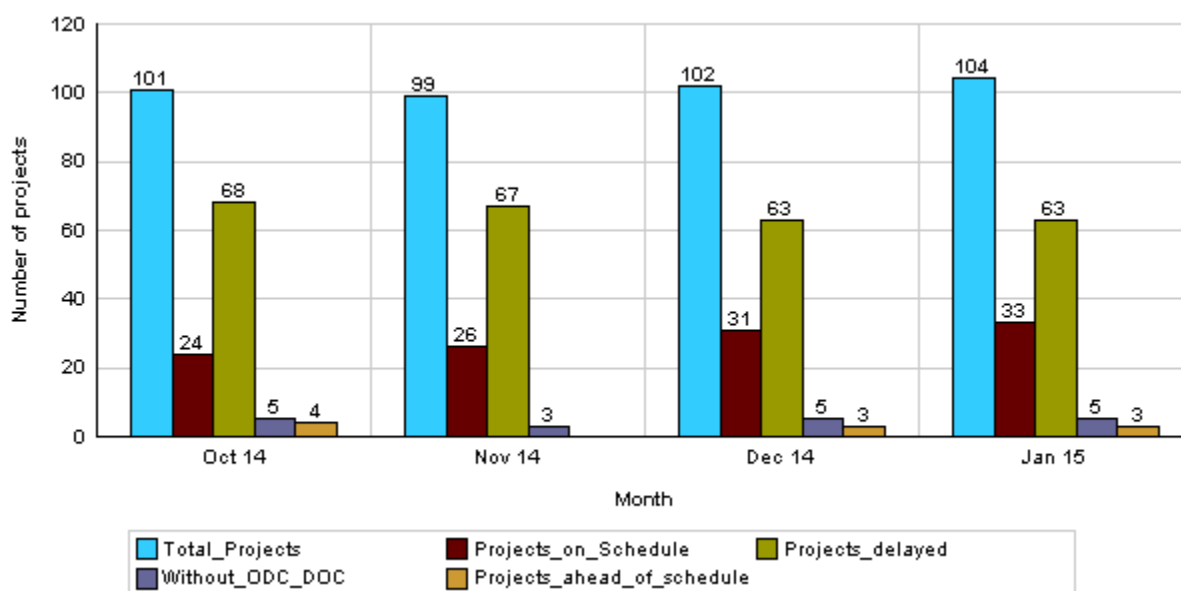


Break-up of 63 Delayed projects in January 2015

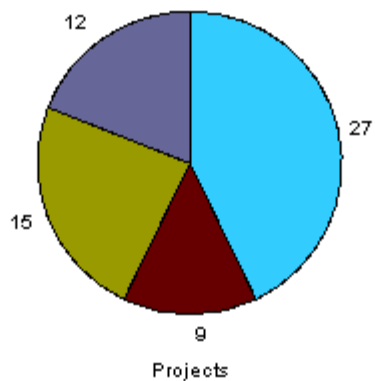


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

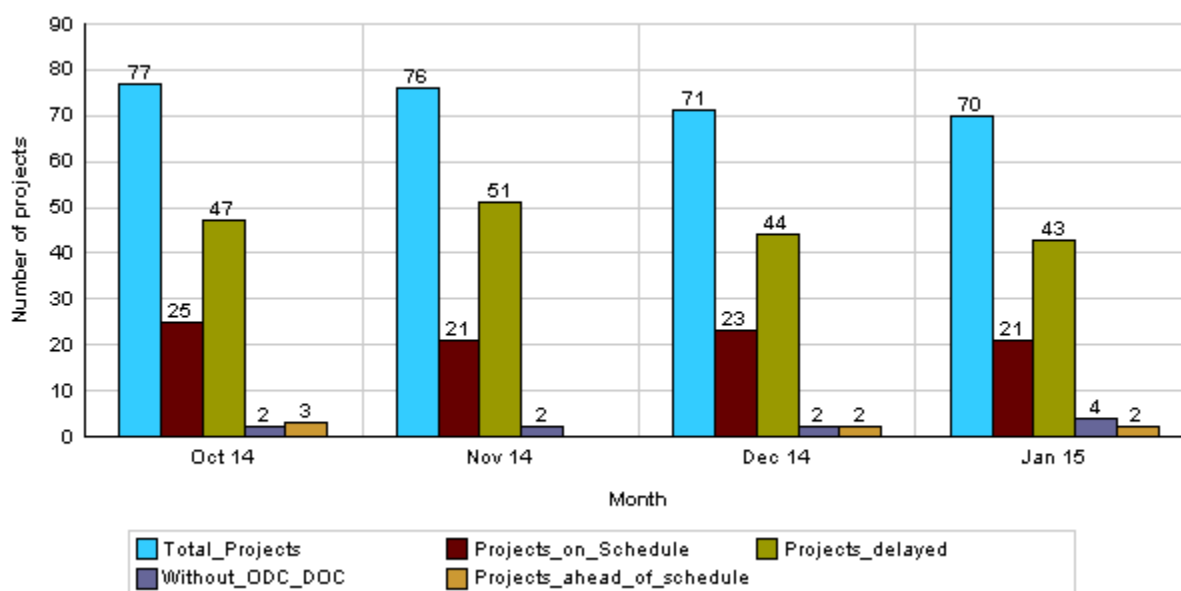


Break-up of 43 Delayed projects in January 2015

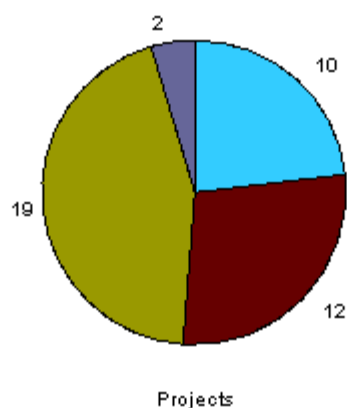


Delay in Months: 1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of COAL Sector

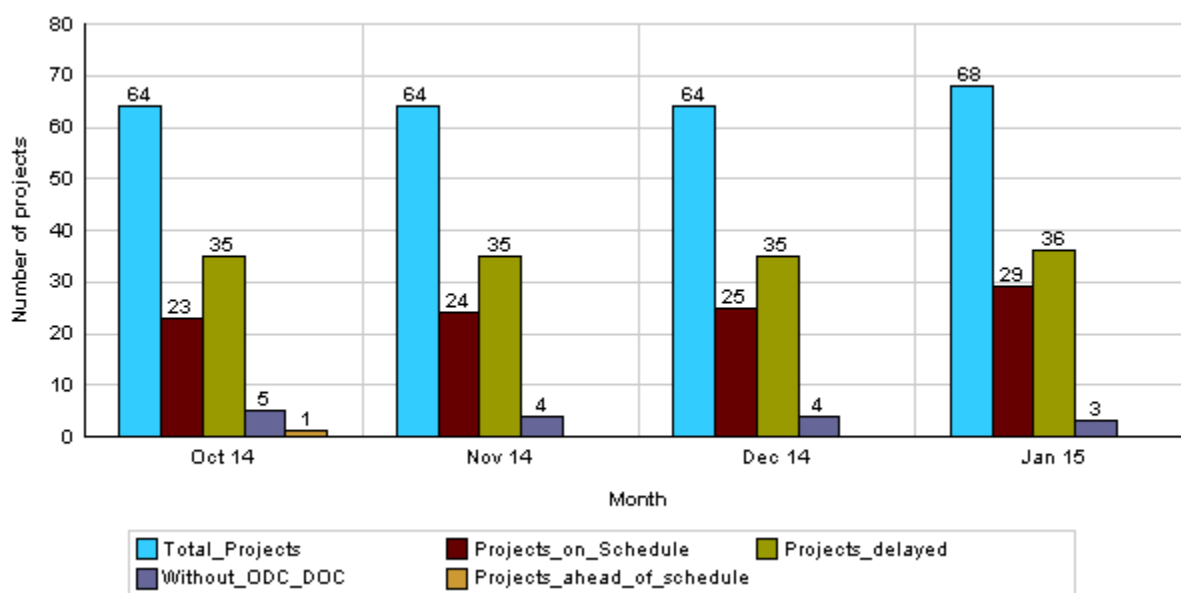


Break-up of 36 Delayed projects in January 2015

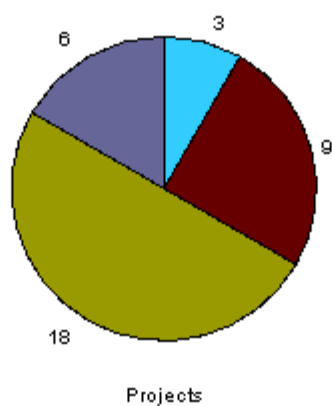


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	3	9	18	6

Graphical Presentation of CIVIL AVIATION Sector

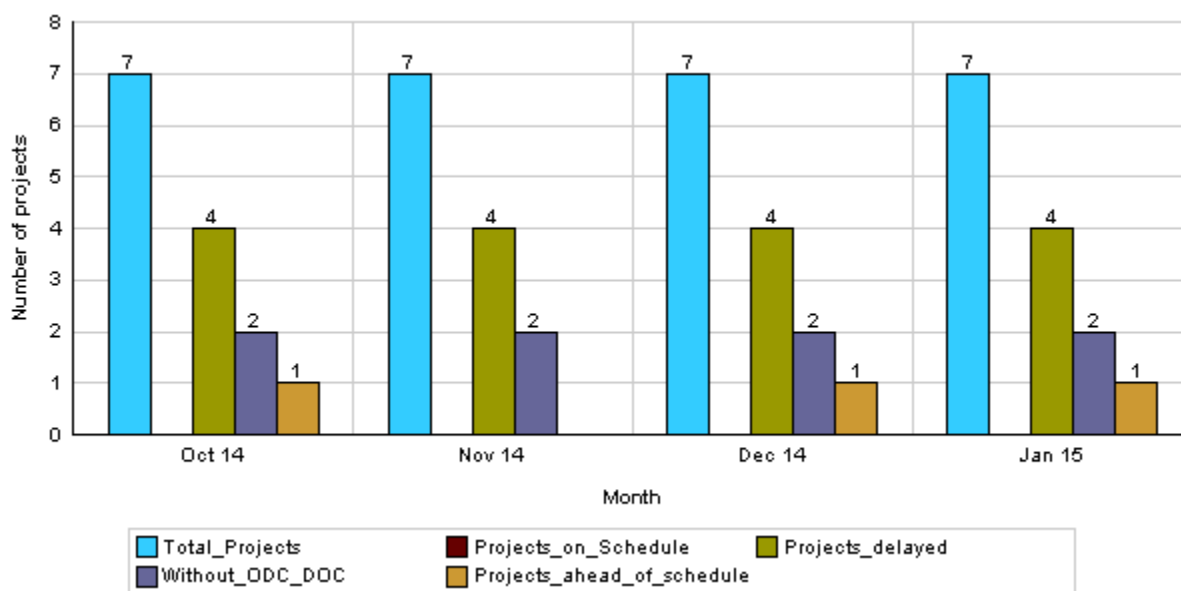


Break-up of 4 Delayed projects in January 2015

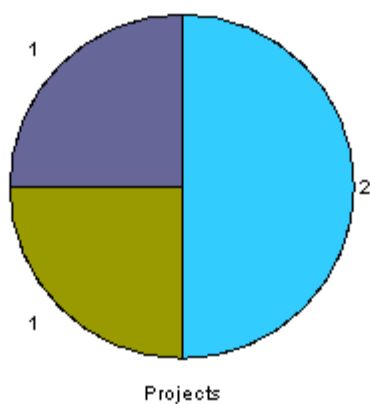


Delay in Months

Delay in Months	Count
1-12	2
13-24	1
25-60	1
MORE THAN 60	0

Graphical Presentation of ATOMIC ENERGY Sector

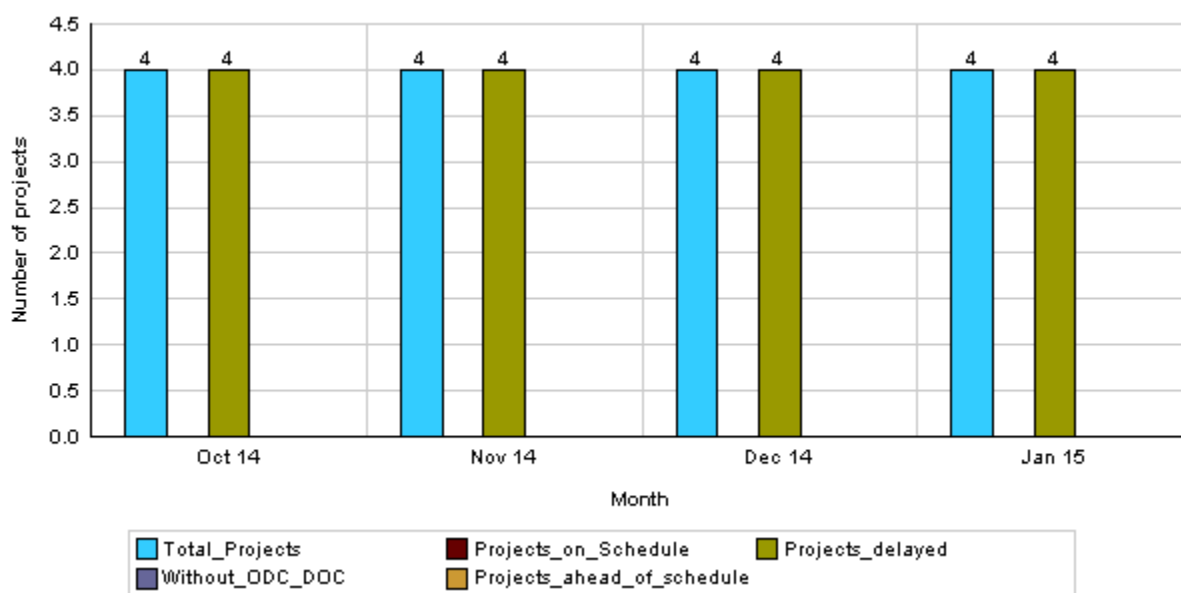

Break-up of 4 Delayed projects in January 2015

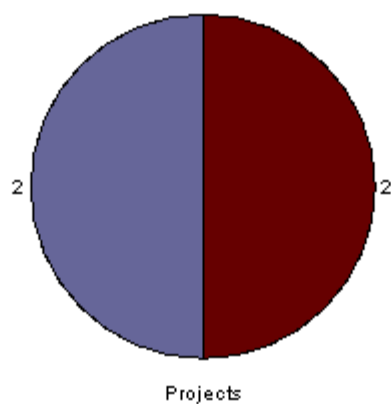

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	0	2	0	2

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	51,918.00	51,918.00	32,749.78
CIVIL AVIATION	7	2,599.56	2,599.56	2,652.48	1,560.82
COAL	68	56,782.14	60,363.17	54,116.57	19,639.50
FERTILISERS	1	197.79	197.79	197.79	0.79
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	24	59,425.03	63,024.03	63,139.43	41,860.40
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	8,222.57
PETROLEUM	70	160,327.93	176,624.17	177,780.38	78,921.95
POWER	104	279,823.29	295,329.03	314,625.85	146,514.50
RAILWAYS	290	164,087.03	177,752.43	291,582.03	94,043.72
ROAD TRANSPORT AND HIGHWAYS	135	101,616.44	101,987.45	103,683.44	95,582.90
SHIPPING AND PORTS	6	5,158.07	5,390.07	6,397.71	1,768.72
TELECOMMUNICATIONS	3	14,054.81	14,054.81	14,054.81	606.87
URBAN DEVELOPMENT	31	138,795.00	138,853.90	144,067.90	13,936.08
Grand total	745	1,030,625.70	1,095,411.02	1,234,992.39	535,408.60

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,998.00	12/2015 -	10/2017	22(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,132.00	12/2008 10/2013	04/2015	76(O) 18(R)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,836.78	09/2010 09/2016	09/2016	72(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,783.00	12/2016 -	05/2018	17(O) -	4/69
	Total		40,442.00 -	51,918.00	32,749.78				60/329
	CIVIL AVIATION								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	323.48	01/2011 -	06/2016	65(O) -	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	314.61	15.42	- -	09/2018	- -	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	388.53	292.44	05/2012 -	02/2015	33(O) -	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	377.99	03/2015 -	02/2015	-1(O) -	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	43.38	03/2014 -	03/2015	12(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	508.07	06/2013 -	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6(O) -	0/0
	Total		2,599.56 -	2,652.48	1,560.82				0/0
	COAL								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30(O) 36(R)	21/22
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016	0(O) -	3/7
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 -	1,143.54	750.68	03/2016 -	03/2016	0(O) -	0/4
15	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND	02/2012	858.11 -	858.11	98.45	03/2020 -	03/2020	0(O) -	3/3
16	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.66	03/2012 -	03/2017	60(O) -	4/5

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ASHOK EXPN OCP CCL (10 MTY) - [060100096]JCL,JHARKHAND	12/2007	471.66 341.63	341.63	109.79	03/2011 -	03/2017	72(O) -	1/2
18	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84(O) -	2/4
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	68.67	03/2016 -	03/2016	0(O) -	3/6
20	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15 -	479.15	-	03/2019 -	03/2019	0(O) -	1/8
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	185.26	03/2017 -	03/2017	0(O) -	3/11
23	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	164.49	22.10	03/2020 -	03/2020	0(O) -	0/0
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	325.23	03/2015 -	03/2015	0(O) -	0/3
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	0(O) -	1/7
26	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	-	03/2014 -	03/2016	24(O) -	2/9
27	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60(O) -	0/1
28	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	611.16	-	03/2020 -	03/2020	0(O) -	0/0
29	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,595.91	03/2014 -	03/2016	24(O) -	7/13
30	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021	0(O) -	0/9
31	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,620.21	03/2014 -	03/2016	24(O) -	11/16
32	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	267.67	7.33	03/2018 -	03/2018	0(O) -	0/0
33	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	1/12
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	118.51	03/2013 -	03/2017	48(O) -	2/7
35	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66 -	337.66	-	03/2019 -	03/2019	0(O) -	2/5
36	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/31
38	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
39	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72(O) -	4/15
40	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.48	12/2012 -	03/2017	51(O) -	11/44
41	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.29	07/2016 -	03/2017	8(O) -	3/39
42	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	159.57	03/2013 -	03/2017	48(O) -	3/9

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
44	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.52	03/2014 -	03/2017	36(O) -	1/2
45	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
46	KHADIA EXPANSION OPENCST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	46.30	03/2018 -	03/2018	0(O) -	0/4
47	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36(O) -	0/28
48	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	439.43	03/2013 -	03/2015	24(O) -	0/2
49	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	0/5
50	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.61	03/2010 -	03/2017	84(O) -	8/10
51	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	7,612.33 7,612.33	1,188.31	756.49	03/2023 03/2023	03/2023	0(O) 0(R)	1/16
52	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44(O) -	0/1
53	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA	09/2014	266.23 -	266.23	7.14	03/2021 -	03/2021	0(O) -	0/0
54	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24(O) -	3/6
55	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.80	03/2012 -	03/2016	48(O) -	4/6
56	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
57	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	-	-	0/0
58	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	472.62	12/2015 -	04/2018	28(O) -	10/35
59	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	8.02	03/2012 -	03/2016	48(O) -	0/2
60	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
61	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	61.79	03/2012 -	03/2017	60(O) -	0/1
62	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	1,624.59 1,624.59	1,624.59	-	03/2023 03/2023	03/2023	0(O) 0(R)	1/1
63	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	441.82 -	441.82	42.32	03/2020 -	03/2020	0(O) -	0/1
64	PURNADIDH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	151.27	03/2013 -	03/2015	24(O) -	2/2
65	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	46.04	03/2014 -	03/2016	24(O) -	0/9
66	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016	0(O) -	2/2
67	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	232.39	03/2012 -	03/2016	48(O) -	24/27

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
69	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	430.14	68.25	03/2016 -	03/2016	0(O) -	6/48
70	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9(O) -	4/51
71	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	71.67	03/2015 -	03/2015	0(O) -	8/31
72	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	73.63	03/2012 -	-	-	25/42
73	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026	0(O) -	3/14
74	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	109.65	03/2018 -	03/2018	0(O) -	0/10
75	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	0/11
76	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND	08/2008	264.68 -	264.68	145.09	03/2012 -	03/2016	48(O) -	1/2
77	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,111.82	06/2009 03/2013	01/2015	67(O) 22(R)	21/23
78	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,866.43	03/2012 05/2014	03/2015	36(O) 10(R)	25/39
79	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	122.11	10/2014 -	03/2015	5(O) -	6/11
	Total		56,782.14 -	54,116.57	19,639.50				260/866
	FERTILISERS								
80	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	197.79	0.79	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	.79				0/0
	MINES								
81	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL,MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0
	STEEL								
82	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	438.26	04/2013 09/2014	06/2015	26(O) 9(R)	17/18
83	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	21.05	05/2016 -	05/2016	0(O) -	1/3
84	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	35.15	07/2016 -	07/2016	0(O) -	0/1
85	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	356.17	05/2013 01/2015	08/2015	27(O) 7(R)	16/20

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
86	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	353.72	09/2009 05/2012	06/2015	69(O) 37(R)	1/1
87	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	383.84	12/2011 01/2015	03/2015	39(O) 2(R)	19/20
88	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	75.67	07/2015 -	03/2016	8(O) -	0/0
89	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	483.99	09/2013 -	05/2015	20(O) -	0/1
90	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	165.14	08/2014 -	06/2015	10(O) -	3/4
91	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	8.28	04/2015 -	04/2015	0(O) -	1/3
92	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	119.25	11/2013 -	06/2015	19(O) -	2/4
93	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,996.99	03/2013 -	09/2015	30(O) -	30/35
94	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,007.37	12/2011 -	05/2015	41(O) -	20/24
95	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,489.55	12/2012 -	03/2015	27(O) -	18/20
96	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,159.76	10/2009 10/2012	04/2015	66(O) 30(R)	68/68
97	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	144.40	10/2013 -	08/2015	22(O) -	2/5
98	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	111.04	09/2014 -	06/2015	9(O) -	1/2
99	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,012.46	05/2015 12/2016	12/2016	19(O) 0(R)	9/79
100	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	181.17	06/2015 -	06/2015	0(O) -	2/3
101	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	134.21	12/2014 -	08/2015	8(O) -	0/2
102	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	8.52	10/2016 -	10/2016	0(O) -	0/0
103	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	110.00	07/2015 -	03/2017	20(O) -	0/1
104	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	-	09/2016 -	09/2016	0(O) -	0/0
105	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	64.41	04/2016 -	04/2016	0(O) -	1/2
	Total		59,425.03 -	63,139.43	41,860.40				211/316
	PETROCHEMICALS								
106	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	8,222.57	04/2012 -	-	-	23/29

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		5,460.61	8,920.00	8,222.57				23/29
	PETROLEUM								
107	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00	678.02	405.00	06/2012	03/2015	33(O)	0/3
108	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82	2,476.82	-	12/2018	12/2018	0(O)	0/0
109	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	1,916.10	1,161.74	12/2014	12/2017	36(O)	0/0
110	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63	2,189.63	1,040.60	12/2014	12/2018	48(O)	0/0
111	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15	2,378.89	1,718.31	03/2013 03/2015	03/2016	36(O) 12(R)	0/5
112	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]OCL,MULTI STATE	08/2011	586.00	586.00	245.20	08/2015	12/2015	4(O)	0/12
113	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04	419.04	7.89	01/2017	01/2017	0(O)	0/0
114	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65	736.65	471.19	09/2011	12/2015	51(O)	0/0
115	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20	269.10	190.04	08/2013	05/2015	21(O)	0/5
116	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64	240.95	107.05	09/2012	04/2015	31(O)	0/0
117	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94	188.89	2.00	01/2014	11/2017	46(O)	0/5
118	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64	723.64	-	03/2013	06/2016	39(O)	0/0
119	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79	761.68	715.05	05/2013 06/2014	03/2015	22(O) 9(R)	0/5
120	DE-BOTTLENECKING OF SMPL - [N16000089]OCL,MAHARASHTRA	12/2009	1,584.00	1,584.00	1,145.99	08/2015	12/2015	4(O)	0/12
121	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015	110(O) -10(R)	0/0
122	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,886.37	08/2010 03/2012	05/2015	57(O) 38(R)	0/10
123	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17	2,592.17	534.53	05/2014	03/2016	22(O)	0/9
124	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	01/2015	22(O) 2(R)	0/10
125	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	284.82	-	04/2015	04/2015	0(O)	0/0
126	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17	600.17	249.01	12/2014	05/2015	5(O)	0/8
127	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00	2,523.00	1,013.67	01/2014	12/2015	23(O)	0/9
128	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06	429.06	-	10/2014	10/2015	12(O)	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
129	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	80.42	09/2017 -	09/2017	0(O) -	0/0
130	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	711.00	4.80	- -	-	-	0/0
131	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC, MAHARASHTRA	03/2012	5,608.40 -	5,608.40	3,334.97	05/2015 -	05/2015	0(O) -	0/17
132	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC, MAHARASHTRA	01/2012	352.49 -	352.49	101.09	03/2014 -	04/2015	13(O) -	0/0
133	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL, ASSAM	02/2014	163.88 -	163.88	7.60	07/2016 -	07/2016	0(O) -	0/0
134	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.16	03/2015 -	05/2016	14(O) -	0/12
135	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.27	02/2016 04/2017	04/2017	14(O) 0(R)	0/0
136	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016	0(O) -	0/0
137	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	03/2012	14,225.00 -	16,504.00	4,831.09	05/2016 -	05/2016	0(O) -	0/30
138	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	101.82	03/2014 -	04/2015	13(O) -	0/5
139	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	7,596.18 -	7,596.18	16.27	01/2013 -	02/2019	73(O) -	0/0
140	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,915.00	1,334.01	12/2012 -	06/2015	30(O) -	0/14
141	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL, RAJASTHAN	04/2011	276.26 -	276.27	209.97	12/2015 -	03/2015	-9(O) -	0/10
142	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	12/2012	607.06 -	607.06	57.76	01/2016 -	01/2016	0(O) -	0/0
143	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA	02/2012	666.00 701.00	701.00	378.54	11/2015 -	11/2016	12(O) -	24/29
144	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 -	199.75	162.26	07/2013 -	03/2015	20(O) -	0/0
145	MARKETING TOP AT KORBA - [N16000186]IOCL, CHHATISGARH	01/2011	141.86 -	232.00	117.87	09/2016 -	12/2015	-9(O) -	0/12
146	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC, GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32(O) -	0/0
147	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA	06/2014	5,706.47 -	5,706.47	110.18	05/2017 -	05/2017	0(O) -	0/0
148	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	122.07	12/2014 06/2015	06/2015	6(O) 0(R)	48/58
149	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
150	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	913.00	360.03	08/2015 -	08/2015	0(O) -	0/0
151	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,011.15	11/2012 11/2013	03/2015	28(O) 16(R)	75/100
152	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,058.49	09/2012 -	03/2016	42(O) -	6/7

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
153	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,752.00	7,268.01	02/2014 -	12/2014	-	0/0
154	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	39.33	07/2016 -	07/2016	0(O) -	0/5
155	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.40	05/2014 -	05/2015	12(O) -	0/5
156	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
157	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41(O) 0(R)	0/0
158	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	260.98	04/2015 -	04/2015	0(O) -	0/0
159	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,038.06	12/2014 -	03/2015	3(O) -	0/20
160	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	11.10	02/2016 -	02/2016	0(O) -	0/0
161	RESID UPGRADEMENT PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	383.78	11/2015 -	11/2015	0(O) -	32/52
162	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	64.31	05/2015 -	12/2015	7(O) -	0/12
163	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 -	04/2018	23(O) -	0/0
164	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	1.94	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
165	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	879.16	11/2015 -	11/2015	0(O) -	16/25
166	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	906.97	10/2011 -	10/2015	48(O) -	0/0
168	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,352.08	01/2012 -	10/2015	45(O) -	0/0
169	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	1,011.80	10/2011 -	02/2015	40(O) -	0/0
170	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015	0(O) -	0/0
171	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	-	12/2016 -	12/2016	0(O) -	0/0
172	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	214.78	08/2012 -	03/2015	31(O) -	0/5
173	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	104.64	03/2015 11/2015	11/2015	8(O) 0(R)	0/5
174	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	199.87	10/2014 10/2015	10/2016	24(O) 12(R)	0/0
175	VKPL UPGRADEMENT AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	275.67	06/2011 03/2012	07/2015	49(O) 40(R)	13/20

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
176	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	596.64	12/2013 03/2014	12/2014	-	69/69
	Total		160,327.93 -	177,780.38	78,921.95				283/605
	POWER								
177	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	1,128.38	298.09	- -	03/2015	- -	8/17
178	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2(O) -	0/0
179	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,306.00	10/2013 -	03/2015	17(O) -	20/20
180	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,586.00	12/2009 10/2014	03/2018	99(O) 41(R)	25/46
181	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	4,982.00	09/2011 -	03/2017	66(O) -	10/36
182	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	346.65	12/2015 -	12/2015	0(O) -	9/19
183	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,583.46	09/2014 -	06/2015	9(O) -	12/19
184	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	719.23	06/2015 -	12/2015	6(O) -	0/0
185	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	5/20
186	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	0.95	06/2015 -	06/2015	0(O) -	5/7
187	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	94.03	10/2014 -	03/2015	5(O) -	11/14
188	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,124.00	08/2018 -	08/2018	0(O) -	10/11
189	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	-	02/2016 -	02/2016	0(O) -	3/7
190	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	933.03	11/2012 -	03/2016	40(O) -	2/12
191	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	66.14	05/2016 -	04/2016	-1(O) -	8/20
192	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
193	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	57.64	09/2014 -	06/2016	21(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
194	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,604.75	05/2014 -	03/2015	10(O) -	5/11
195	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	328.00	12/2016 -	05/2017	5(O) -	12/14
196	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	2,137.00	09/2017 -	09/2017	0(O) -	16/39
197	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	801.40	08/2014 -	03/2015	7(O) -	11/15
198	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0
199	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	264.87	11/2016 -	03/2016	-8(O) -	8/17
200	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018	0(O) -	0/0
201	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	953.21	12/2007 12/2009	06/2015	90(O) 66(R)	3/10
202	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,561.01	12/2009 03/2017	03/2017	87(O) 0(R)	12/29
203	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,841.20	01/2016 -	11/2016	10(O) -	4/6
204	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,407.00	04/2009 -	06/2015	74(O) -	4/9
205	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	6,644.00	01/2017 -	03/2017	2(O) -	22/25
206	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 08/2010	12/2015	87(O) 64(R)	16/23
207	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	3,135.00	06/2017 -	06/2017	0(O) -	17/38
208	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	147.00	08/2017 -	-	-	0/9
209	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,569.00	09/2016 -	02/2017	5(O) -	21/25
210	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	1,960.00	02/2019 -	02/2019	0(O) -	1/1
211	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,902.60	08/2013 -	03/2016	31(O) -	3/17
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	10/20
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	458.32	07/2013 -	06/2015	23(O) -	3/10
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	307.17	02/2012 -	03/2016	49(O) -	3/13
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	425.16	11/2011 -	03/2016	52(O) -	3/13
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	4.20	06/2016 -	06/2016	0(O) -	9/20

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
217	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,104.52	04/2013 -	03/2016	35(O) -	1/11
218	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	466.32	11/2014 -	06/2015	7(O) -	11/16
219	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	118.89	03/2016 -	03/2016	0(O) -	8/17
220	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	513.59	03/2015 -	03/2015	0(O) -	12/17
221	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	161.12	04/2015 -	05/2015	1(O) -	11/18
222	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	710.74	11/2012 -	12/2015	37(O) -	1/11
223	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
224	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,828.46	09/2009 -	03/2019	114(O) -	7/12
225	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	956.75	08/2013 03/2016	03/2016	31(O) 0(R)	22/37
226	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,384.84	77.00	09/2019 -	09/2019	0(O) -	2/2
227	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,944.00	11/2016 -	08/2017	9(O) -	19/21
228	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	08/2016 -	08/2016	0(O) -	0/0
229	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	5/7
230	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/0
231	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,108.50	09/2010 -	-	-	0/0
232	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	473.88	06/2016 -	12/2015	-6(O) -	10/19
233	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	-	02/2017 -	02/2017	0(O) -	0/0
234	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	187.19	06/2012 -	-	-	1/3
235	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	1,147.58	12/2014 -	03/2015	3(O) -	10/13
236	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	187.34	03/2014 -	03/2015	12(O) -	7/7
237	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	802.93	08/2014 -	05/2015	9(O) -	10/17
238	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,037.69	08/2012 -	06/2015	34(O) -	2/6
239	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	26.80	08/2016 -	08/2016	0(O) -	10/20

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
240	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	-	07/2017 -	07/2017	0(O) -	0/0
241	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	980.43	02/2015 -	03/2015	1(O) -	9/14
242	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	878.18	11/2014 -	06/2015	7(O) -	8/15
243	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	921.72	01/2015 -	12/2015	11(O) -	12/20
244	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	252.57	08/2014 -	06/2015	10(O) -	13/19
245	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	321.72	06/2014 -	06/2015	12(O) -	12/19
246	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	529.00	03/2019 -	03/2019	0(O) -	5/5
247	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,348.00	03/2013 -	05/2018	62(O) -	1/14
248	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,633.27	09/2009 -	07/2016	82(O) -	2/5
249	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,079.08	07/2010 02/2016	05/2018	94(O) 27(R)	5/21
250	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,390.96	08/2014 -	06/2015	10(O) -	11/19
251	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,960.41	10/2014 -	06/2015	8(O) -	8/17
252	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,013.88	10/2012 -	03/2016	41(O) -	0/11
253	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	04/2017 -	04/2017	0(O) -	0/0
254	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,964.50	12/2012 -	12/2015	36(O) -	2/11
255	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
256	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	440.60	03/2018 -	03/2018	0(O) -	0/0
257	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,102.25	01/2015 -	12/2015	11(O) -	8/21
258	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	22.00	10/2016 -	10/2016	0(O) -	6/20
259	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	-	03/2018 -	03/2018	0(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
260	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,402.67	10/2014 -	03/2015	5(O) -	9/15
261	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	186.80	05/2016 -	05/2016	0(O) -	8/18
262	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	-	10/2017 -	10/2017	0(O) -	0/0
263	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	461.60	02/2014 -	06/2015	16(O) -	12/16
264	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,253.06	12/2013 04/2015	04/2015	16(O) 0(R)	9/12
265	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	358.71	11/2013 -	06/2015	19(O) -	12/20
266	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,709.43	03/2013 -	06/2015	27(O) -	6/14
267	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,655.67	03/2014 -	06/2015	15(O) -	8/14
268	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,600.10	12/2013 -	06/2015	18(O) -	7/12
269	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	91.30	01/2013 -	06/2015	29(O) -	8/21
270	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,394.76	11/2013 -	06/2015	19(O) -	7/15
271	TRANSMISSION SYSTEM OF VINHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,521.57	11/2012 -	06/2015	31(O) -	2/10
272	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,072.43	07/2014 -	05/2015	10(O) -	8/13
273	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	842.77	869.41	07/2013 02/2011	08/2015	25(O) 54(R)	24/25
274	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 -	1,259.80	733.11	07/2006 12/2015	10/2016	123(O) 10(R)	4/13
275	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	3.07	04/2016 -	04/2016	0(O) -	0/0
276	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,548.00	08/2015 -	08/2015	0(O) -	20/20
277	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	571.03	07/2014 11/2018	11/2018	52(O) 0(R)	2/8
278	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018	0(O) -	0/0
279	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	512.79	09/2010 -	12/2015	63(O) -	0/7

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,403.49	06/2015 -	12/2015	6(O) -	15/28
	Total		279,823.29 -	314,625.85	146,514.50				723/1378
	RAILWAYS								
281	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	36.31	03/2016 -	03/2016	0(O) -	0/0
282	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
283	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
284	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	888.65	-	- -	03/2018	- -	0/0
285	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	416.44	12/2009 03/2011	12/2014	-	0/0
286	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
287	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
288	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
289	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	21.57	- -	-	-	0/0
290	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
291	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
292	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
293	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	0.05	- -	-	-	0/0
294	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
295	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	- -	0/0
296	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
297	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
298	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
299	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
300	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
301	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
302	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
303	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0
304	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	77.58	- -	-	-	0/0
305	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	9.60	- -	-	-	0/0
306	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33(O) -	0/0
307	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	1,382.78	0.82	- -	-	-	0/0
308	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	3.87	- -	-	-	0/0
309	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
310	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
311	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	13.53	- -	-	-	0/0
312	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
313	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	408.79	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
314	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	337.49	0.21	- -	-	-	0/0
315	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	923.23	1.01	- -	-	-	0/0
316	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	837.33	1.15	- -	-	-	0/0
317	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	760.00	0.09	- -	-	-	0/0
318	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
319	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
320	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
321	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	94.11	- -	-	-	0/0
322	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69(O) -	0/0
323	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
324	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
325	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.46	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
326	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	434.00	35.90	- -	-	-	0/0
327	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0
328	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
329	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
330	CHANDIGARH-BADDI NL - [N22000296]NR, MULTI STATE	04/2007	328.14 -	328.14	0.30	- -	-	-	0/0
331	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER, MULTI STATE	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0
332	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	951.24	619.87	- -	03/2015	- -	0/0
333	CHENGANNUR-CHINGAVANAM - [N22000203]SR, KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
334	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 -	520.00	462.69	- -	-	-	0/0
335	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0
336	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
337	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	378.56	107.03	- -	-	-	0/0
338	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
339	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	- -	0/0
340	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
341	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
342	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
343	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
344	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
345	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
346	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
347	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
348	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
349	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	225.00	211.48	- 10/2014	10/2014	-	0/0
350	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
351	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]JER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
352	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	150.78	12/2012 -	-	-	0/0
353	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
354	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]JECR,BIHAR	04/2001	406.92 -	406.92	155.87	- -	-	-	0/0
355	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]JER,MULTI STATE	04/2010	296.44 -	296.44	4.55	- -	-	-	0/0
356	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]JECR,BIHAR	04/2005	205.00 -	205.00	5.20	- -	-	-	0/0
357	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	258.93	- -	-	-	0/0
358	DELANG-PURI DOUBLING - [N22000320]JECOR,ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	0(O) -	0/0
359	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
360	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	144.05	- -	-	-	0/0
361	DEOGHAR - SULTANGANJ (INL), ER - [220100273]JER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
362	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	4.58	- -	-	-	0/0
363	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	4.66	02/2019 -	02/2019	0(O) -	0/0
364	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
365	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	-	-	0/0
366	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	- -	03/2015	- -	0/0
367	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016	0(O) -	0/0
368	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]JRE, UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36(O) 15(R)	0/0
369	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
370	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
371	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	235.70	12/2008 -	12/2014	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
372	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	495.74	300.15	06/2013 06/2013	-	-	0/0
373	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
374	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	1,117.00 -	1,922.00	1.16	- -	-	-	0/0
375	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
376	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	415.67	13.98	- -	-	-	0/0
377	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
378	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	197.73	-	- -	-	-	0/0
379	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
380	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	280.00	147.94	02/2006 -	-	-	0/0
381	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	- -	06/2015	-	0/0
382	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
383	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR, DELHI	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
384	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	- -	-	-	0/0
385	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	- 70(R)	0/0
386	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	608.02	595.67	03/1994 -	10/2014	-	0/0
387	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	179.32	24.98	- -	-	-	0/0
388	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.03	02/2020 -	02/2020	0(O) -	0/0
389	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER, MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
390	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	367.17	10.38	- -	-	-	0/0
391	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	324.66	216.09	- -	-	-	0/0
392	HANSDIHA-GODDA NL - [N22000236]ER, MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
393	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER, MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
394	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	334.04	- 09/2009	-	-	0/0
395	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0
396	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
397	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,006.03	- -	-	-	0/0
398	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
399	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	86.31	03/2015 -	03/2015	0(O) -	0/0
400	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
401	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	108.64	- -	-	-	0/0
402	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	282.11	- -	-	-	0/0
403	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
404	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
405	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
406	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	116.82	- -	-	-	0/0
407	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
408	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	250.16	03/2014 -	-	-	0/0
409	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	- -	-	-	0/0
410	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
411	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	768.20	03/2012 -	-	-	0/0
412	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]JECR,BIHAR	04/2009	470.00 -	470.00	19.44	- -	-	-	0/0
413	JHARSUGUDA-RENGALI DOUBLING - [N22000317]JECOR,ODISHA	03/2006	201.00 -	230.00	218.67	- -	-	-	0/0
414	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
415	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
416	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	- -	-	-	0/0
417	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
418	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
419	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
420	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2015	- -	0/0
421	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
422	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	- -	1/1
423	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.66	- -	-	-	0/0
424	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
425	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
426	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	250.37	03/2017 -	03/2017	0(O) -	0/0
427	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.96	- -	-	-	0/0
428	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	162.87	139.56	- -	-	-	0/0
429	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	284.12	03/2009 03/2009	08/2014	-	0/0
430	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
431	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	- -	0/0
432	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
433	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	567.94	- 03/2010	03/2010	-	0/0
434	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,857.31	07/2005 -	-	-	0/0
435	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	237.93	- -	-	-	0/0
436	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
437	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	301.09	03/2012 -	-	-	0/0
438	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
439	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
440	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
441	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
442	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
443	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
444	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
445	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
446	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84(O) -	0/0
447	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
448	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
449	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.69	- -	-	-	0/0
450	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	121.27	- -	-	-	0/0
451	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
452	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
453	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
454	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
455	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	108.93	- -	-	-	0/0
456	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	482.01	03/2012 -	-	-	0/0
457	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
458	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	279.54	2.53	01/1999 -	-	-	0/0
459	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.72	- -	-	-	0/0
460	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0
461	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	7.50	- -	-	-	0/0
462	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
463	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
464	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
465	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.14	- -	-	-	0/0
466	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.51	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
467	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	390.60	4.69	- -	-	-	0/0
468	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	1,815.37	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
469	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	- -	0/0
470	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	324.92	- -	-	-	0/0
471	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	- -	0/0
472	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]JECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
473	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR	04/2008	228.05 -	228.05	0.05	- -	-	-	0/0
474	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
475	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73(O) -	0/0
476	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
477	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
478	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]JER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
479	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
480	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
481	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	- -	0/0
482	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
483	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
484	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	- -	03/2019	- -	0/0
485	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	- -	0/0
486	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
487	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
488	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
489	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
490	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
491	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
492	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	64.72	03/2014 -	03/2014	-	0/0
493	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.02	480.06	03/2016 -	03/2016	0(O) -	0/0
494	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	134.30	03/2016 -	06/2016	3(O) -	0/0
495	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,951.98	478.77	03/2016 -	03/2016	0(O) -	0/0
496	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	465.19	03/2008 06/2008	-	-	0/0
497	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
498	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
499	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	- -	01/2015	- -	0/0
500	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
501	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	- -	02/2014	-	0/0
502	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	- -	03/2015	- -	0/0
503	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	- -	-	-	0/0
504	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
505	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	0(O) -	0/0
506	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
507	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
508	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
509	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
510	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
511	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	284.82	12/2007 03/2010	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR,BIHAR	04/2002	921.00 -	2,363.00	1,548.90	03/2009 12/2012	12/2014	-	0/0
513	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	311.89	02/2009 02/2009	08/2014	-	0/0
514	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
515	RAJKOT-VERAVAL, WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
516	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	657.06	03/2013 -	03/2016	36(O) -	0/0
517	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
518	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
519	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	3,700.00	3,198.30	- -	03/2015	- -	0/0
520	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.53	- -	-	-	0/0
521	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	792.98	- -	-	-	0/0
522	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	44.92	- -	-	-	0/0
523	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
524	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	313.85	- -	-	-	0/0
525	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
526	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	55.61	04/2016 -	03/2017	11(O) -	0/0
527	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
528	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECOR,BIHAR	04/1999	175.69 -	325.00	251.16	- -	-	-	0/0
529	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]JECR,BIHAR	04/2004	372.14 -	355.81	342.64	- -	-	-	0/0
530	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	233.44	03/2010 -	-	-	0/0
531	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]JECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	-	-	0/0
532	SAMBALPUR-TALCHER DOUBLING - [N22000315]JECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
533	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
534	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
535	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
536	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.85	- -	-	-	0/0
537	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
538	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
539	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.02	- -	-	-	0/0
540	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
541	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	116.37	02/2015 -	-	-	0/0
542	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0
543	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	596.08	03/2014 -	-	-	0/0
544	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
545	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
546	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	19(O) -	0/0
547	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
548	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
549	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
550	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	-	- -	-	-	0/0
551	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
552	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0
553	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
554	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
555	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,536.83	12/2006 -	-	-	0/0
556	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.31	- -	-	-	0/0
557	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.12	- -	-	-	0/0
558	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]JNR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
560	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
561	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
562	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	85.93	- -	-	-	0/0
563	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
564	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
565	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0
566	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
567	WARDHA-NANDED MAHARASHTRA - [N22000231]JR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
568	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]JR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
569	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
570	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		164,087.03 -	291,582.03	94,043.72				1/7
	ROAD TRANSPORT AND HIGHWAYS								
571	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18(O) -	0/0
572	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
573	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	363.40	10/2014 -	03/2015	5(O) -	0/0
574	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	03/2015	8(O) -	0/0
575	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	05/2013	-	0/0
576	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18(O) -	0/0
577	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13(O) -	0/0
578	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	03/2015	5(O) -	0/0
579	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8(O) -	0/0
580	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
581	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
582	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20(O) -	0/0
583	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11(O) -	0/0
584	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	171.00	05/2014 -	05/2014	-	0/0
585	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6(O) -	0/3
586	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11(O) -	0/0
587	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	06/2013	-	0/3
588	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O) -	0/0
589	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	941.00	08/2013 -	08/2013	-	0/3
590	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	177.78	09/2016 -	09/2016	0(O) -	0/0
591	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19(O) -	0/0
592	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	08/2015	24(O) -	0/0
593	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22(O) -	0/0
594	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	03/2015	19(O) -	0/0
595	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015	0(O) -	0/0
596	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29(O) -	0/0
597	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6(O) -	0/0
598	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93(O) -	0/0
599	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(O) -	0/3
600	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
601	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27(O) -	0/0
602	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2016	22(O) -	0/0
603	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O) -	0/0
604	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	665.80	- -	03/2015	- -	2/2
605	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
606	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19(O) -	0/0
607	BIJUNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87(O) -	0/0
608	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86(O) -	0/0
609	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126(O) -	0/0
610	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
611	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84(O) -	0/0
612	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33(O) -	0/0
613	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56(O) -	0/0
614	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
615	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	05/2015	24(O) -	0/0
616	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
617	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015	0(O) -	0/0
618	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61(O) -	0/0
619	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33(O) -	0/0
620	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	02/2015	20(O) -	0/0
621	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	808.70	- -	05/2013	-	1/1
622	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	02/2015	80(O) -	0/0
623	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 06/2015	06/2015	85(O) 0(R)	0/0
624	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	12/2015	63(O) -	0/0
625	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015	0(O) -	0/0
626	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	03/2015	78(O) -	0/0
627	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016	0(O) -	0/0
628	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015	0(O) -	0/0
629	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
630	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78(O) -	0/0
631	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	04/2015	20(O) -	0/0
632	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	06/2015	33(O) -	2/3
633	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
634	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 04/2015	04/2015	84(O) 0(R)	0/0
635	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
636	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2015	82(O) -	0/0
637	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	06/2015	71(O) -	0/0
638	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90(O) -	0/0
639	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26(O) -	0/0
640	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26(O) -	0/0
641	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
642	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31(O) -	0/0
643	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	06/2015	26(O) -	0/0
644	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25(O) -	0/0
645	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27(O) -	0/0
646	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26(O) -	0/0
647	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	02/2015	13(O) -	0/0
648	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23(O) -	0/0
649	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40(O) -	0/0
650	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79(O) -	0/0
651	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17(O) -	0/0
652	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	-	2/3
653	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	02/2015	31(O) -	0/0
654	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
655	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74(O) -	0/0
656	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	06/2015	79(O) -	0/0
657	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74(O) -	0/0
658	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21(O) -	0/0
659	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33(O) -	0/0
660	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	02/2015	80(O) -	0/0
661	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5(O) -	0/0
662	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	06/2015	86(O) 2(R)	0/0
663	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82(O) 0(R)	0/0
664	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
665	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11(O) -	0/0
666	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	655.20	09/2013 -	09/2013	-	0/0
667	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	01/2015	59(O) -	0/0
668	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
669	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13(O) -	0/0
670	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
671	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	-	0/0
672	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18(O) -	0/0
673	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20(O) -	0/0
674	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37(O) -	0/0
675	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,601.00	07/2012 -	07/2012	-	0/0
676	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33(O) -	0/0
677	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14(O) -	0/0
678	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
679	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
680	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	01/2015	75(O) -	0/0
681	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2015	0(O) -	0/0
682	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	03/2015	6(O) -	0/0
683	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19(O) -	0/0
684	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33(O) -	0/0
685	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10(O) -	0/0
686	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	02/2015	89(O) 11(R)	0/0
687	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
688	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2015	9(O) -	0/0
689	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15(O) -	0/0
690	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	03/2015	15(O) -	0/0
691	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12(O) -	0/0
692	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43(O) -	0/0
693	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015	84(O) 0(R)	0/0
694	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18(O) -	0/0
695	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	-	2/2
696	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	567.00	1,388.00	11/2013 -	11/2013	-	0/0
697	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	12/2014	-	0/0
698	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24(O) -	0/0
699	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	680.00	383.20	- -	07/2014	-	2/2
700	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21(O) -	0/0
701	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	606.00	-	- -	-	-	0/0
702	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
703	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015	0(O) -	0/0
704	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30(O) -	0/0
705	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		101,616.44 -	103,683.44	95,582.90				14/28
	SHIPPING AND PORTS								
706	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	937.28	12/2010 09/2012	01/2016	61(O) 40(R)	0/0
707	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	-	03/2006 -	-	-	0/0
708	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	-	-	0/0
709	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	373.22	-	04/2009 -	-	-	0/0
710	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
711	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	-	-	0/0
	Total		5,158.07 -	6,397.71	1,768.72				0/0
	TELECOMMUNICATIONS								
712	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74(O) -	0/0
713	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	50.93	10/2010 11/2015	09/2015	59(O) -2(R)	0/0
714	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015	0(O) -	0/0
	Total		14,054.81 -	14,054.81	606.87				0/0
	URBAN DEVELOPMENT								
715	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
716	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35(O) -	0/0
717	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	-	06/2011 -	-	-	3/3
718	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
719	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	191.24	8.78	08/2007 -	-	-	0/0
720	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
721	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2(O) -	0/0
722	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
723	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8(O) -	0/23
724	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24(O) -	0/0
725	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
726	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17(O) -	0/0
727	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29(O) -	0/0
728	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
729	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15(O) -	0/0
730	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	2.04	03/2017 -	03/2017	0(O) -	0/0
731	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
732	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	2,637.11	03/2010 -	10/2014	-	0/0
733	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11(O) -	0/0
734	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
735	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
736	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	5,181.79	688.45	07/2017 -	07/2017	0(O) -	0/0
737	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	111.33	07/2012 -	07/2012	-	0/0
738	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0

Sector Wise Details

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
739	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
740	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	22.43	11/2014 -	12/2014	-	0/0
741	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019	0(O) -	0/7
742	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	177.77	-	-	-	0/0
743	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	85.60	09/2014 -	09/2014	-	0/0
744	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	0.08	09/2016 -	09/2016	0(O) -	0/0
745	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34(O) -	0/0
	Total		138,795.00 -	144,067.90	13,936.08				3/33
	Grand Total		1,030,625.70	1,234,992.39	535,408.60				1578/3591


Summary of projects in the Flash Report for the month of January, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	738
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	12
Number of Projects in Current Month	745

Brief Analysis


Project Status with respect to Original Schedule: Out of 745 projects, 6 projects are ahead of schedule, 122 projects are on schedule and 317 projects are delayed. Of the balance, 265 projects do not have fixed dates of commissioning while 35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

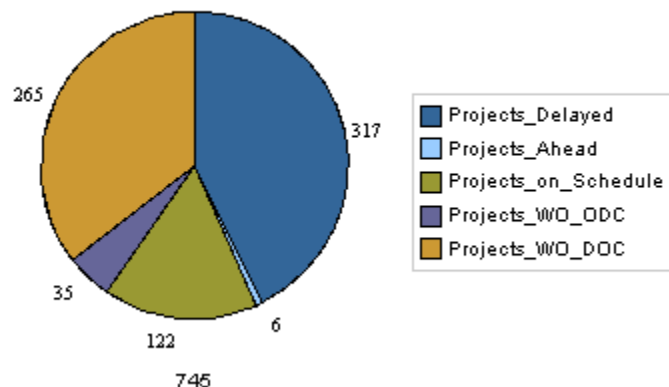

Investment Scenario

Total original cost of implementation of 745 projects when sanctioned, was of the order of Rs. 1030625.7 crore but this was subsequently revised to Rs. 1234992.39 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till January, 2015 is Rs. 535408.6 crore, which is 43.4% of the revised cost of the projects.

Figures are in Rs. Crore

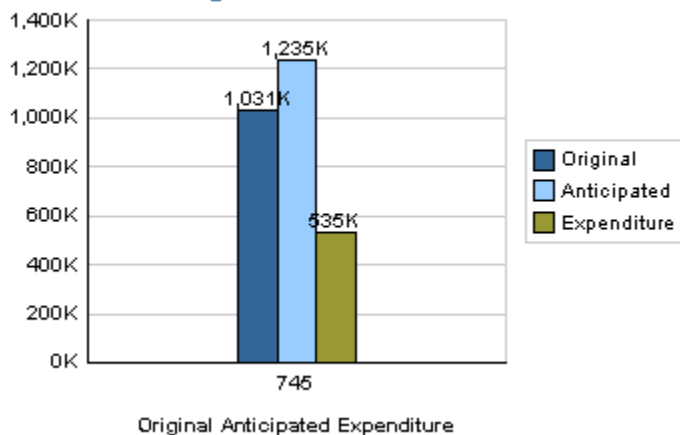

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	31
Number of Projects On Schedule	8
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	9
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 31 projects, 8 projects are on schedule and 14 projects are delayed .9 projects do not have fixed dates of commissioning.

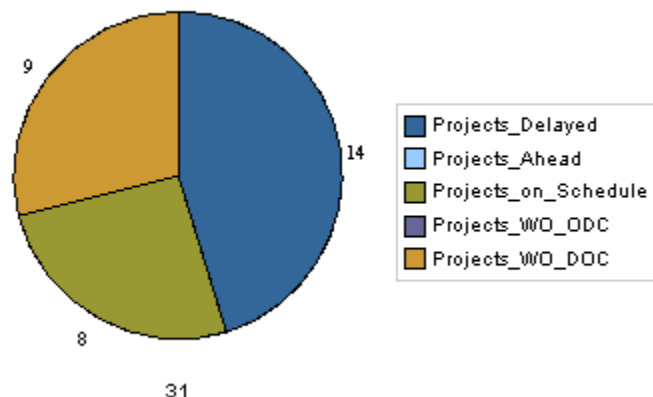

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 138795 crore but this was subsequently revised to Rs. 144067.9 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till January, 2015 is Rs. 13936.08 crore, which is 9.7% of the revised cost of the projects.

Figures are in Rs. Crore

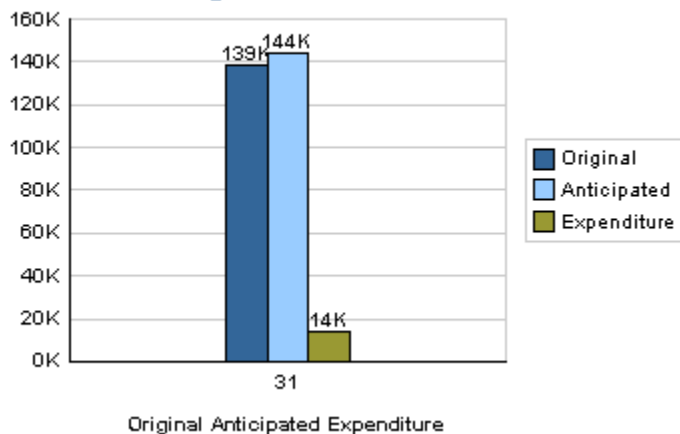

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects On Schedule	1
Number of Projects Delayed	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 1 project are on schedule and 2 projects are delayed .

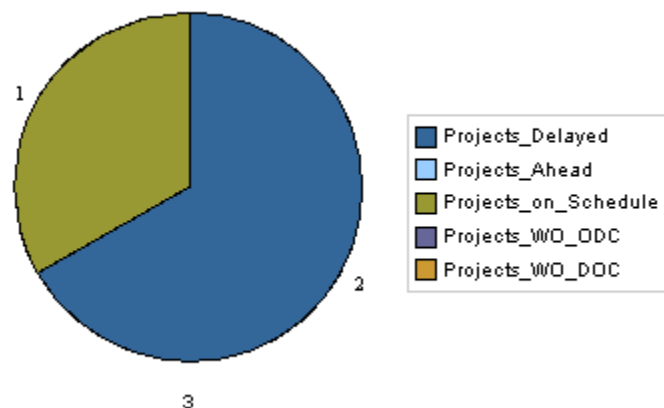

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14054.81 crore but this was subsequently revised to Rs. 14054.81 crore implying a cost overrun of 0%. The expenditure incurred on these projects till January, 2015 is Rs. 606.87 crore, which is 4.3% of the revised cost of the projects.

Figures are in Rs. Crore

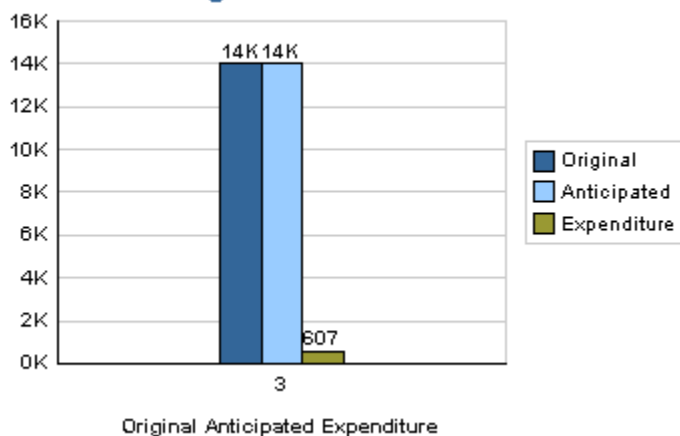

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	24
Number of Projects On Schedule	7
Number of Projects Delayed	17

Brief Analysis


Project Status with respect to Original Schedule: Out of 24 projects, 7 projects are on schedule and 17 projects are delayed.

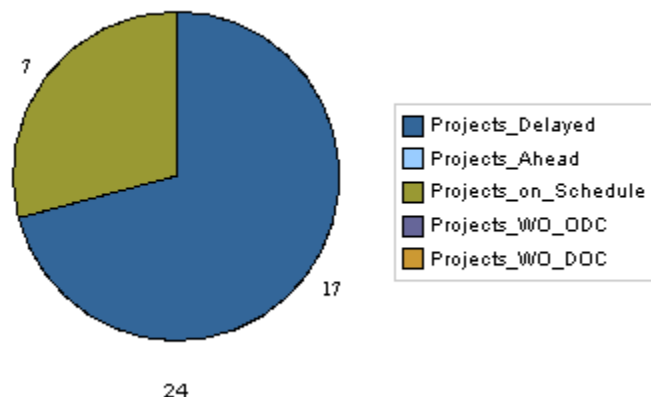

Investment Scenario

Total original cost of implementation of 24 projects when sanctioned, was of the order of Rs. 59425.03 crore but this was subsequently revised to Rs. 63139.43 crore implying a cost overrun of 6.3%. The expenditure incurred on these projects till January, 2015 is Rs. 41860.4 crore, which is 66.3% of the revised cost of the projects.

Figures are in Rs. Crore

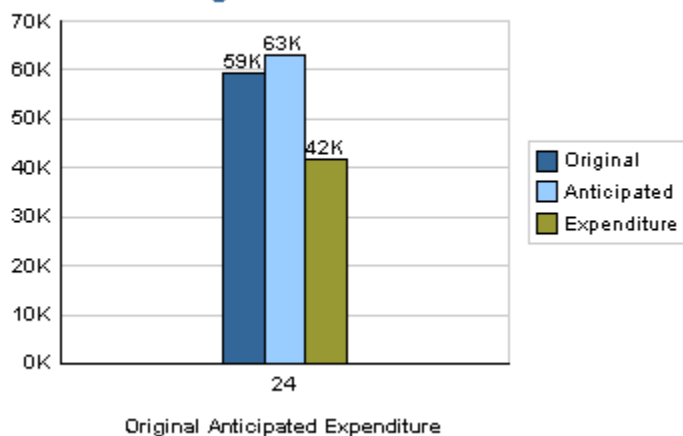

Sector wise current status of projects on the Flash Report


SHIPPING AND PORTS

Current Status:

Number of Projects	6
Number of Projects Delayed	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 1 project are delayed .5 projects do not have fixed dates of commissioning.

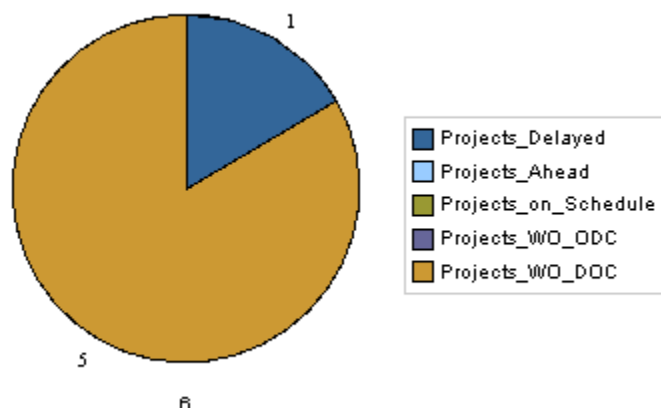

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5158.07 crore but this was subsequently revised to Rs. 6397.71 crore implying a cost overrun of 24%. The expenditure incurred on these projects till January, 2015 is Rs. 1768.72 crore, which is 27.6% of the revised cost of the projects.

Figures are in Rs. Crore

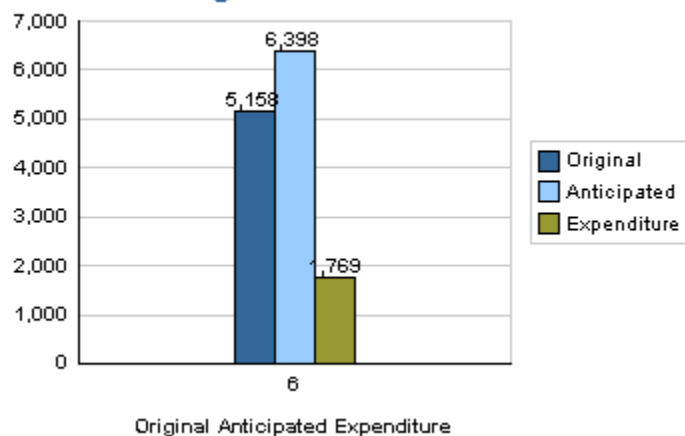

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	135
Number of Projects On Schedule	9
Number of Projects Delayed	102

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	22

Brief Analysis


Project Status with respect to Original Schedule: Out of 135 projects, 9 projects are on schedule and 102 projects are delayed .22 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

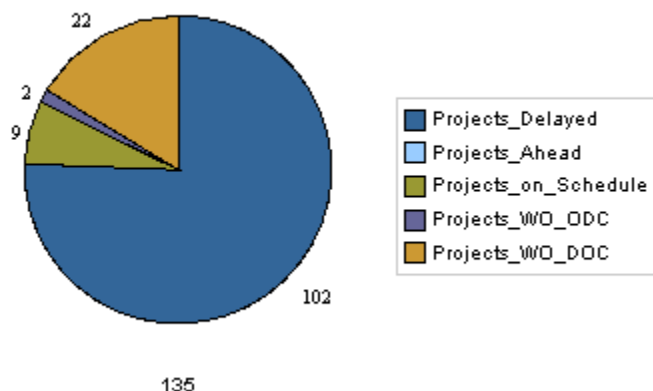

Investment Scenario

Total original cost of implementation of 135 projects when sanctioned, was of the order of Rs. 101616.44 crore but this was subsequently revised to Rs. 103683.44 crore implying a cost overrun of 2%. The expenditure incurred on these projects till January, 2015 is Rs. 95582.9 crore, which is 92.2% of the revised cost of the projects.

Figures are in Rs. Crore

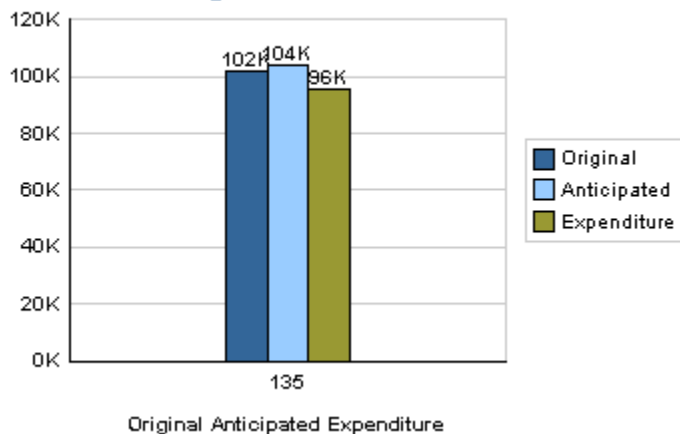

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	290
Number of Projects On Schedule	12
Number of Projects Delayed	31

Number of Projects Without Original Date of Commissioning	31
Number of Projects Without Date Of Commissioning	216

Brief Analysis


Project Status with respect to Original Schedule: Out of 290 projects, 12 projects are on schedule and 31 projects are delayed .216 projects do not have fixed dates of commissioning.31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

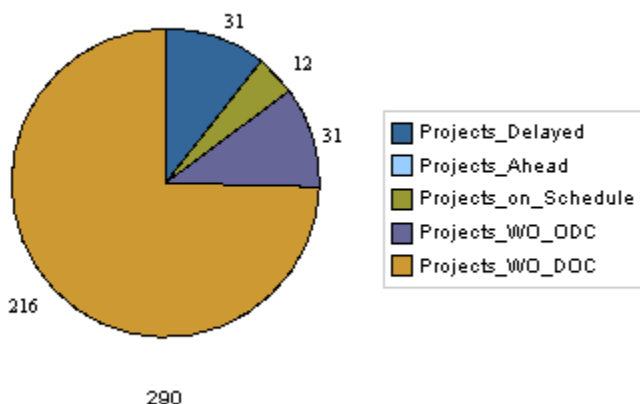

Investment Scenario

Total original cost of implementation of 290 projects when sanctioned, was of the order of Rs. 164087.03 crore but this was subsequently revised to Rs. 291582.03 crore implying a cost overrun of 77.7%. The expenditure incurred on these projects till January, 2015 is Rs. 94043.72 crore, which is 32.3% of the revised cost of the projects.

Figures are in Rs. Crore

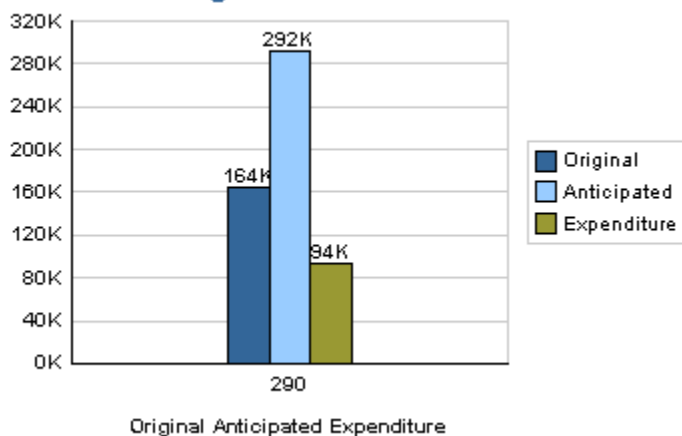

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	104
Number of Projects On Schedule	33
Number of Projects Delayed	63
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 104 projects, 3 projects are ahead of schedule, 33 projects are on schedule and 63 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

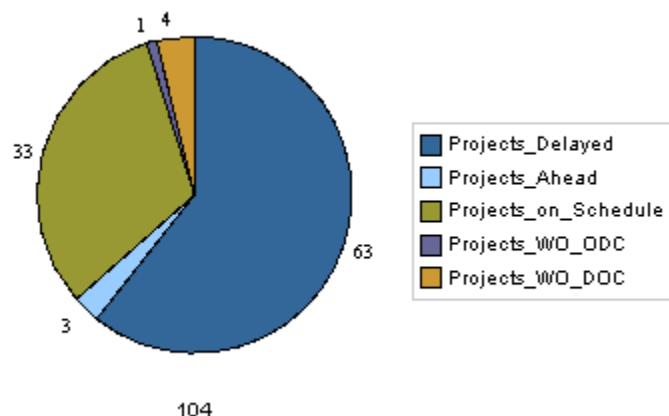

Investment Scenario

Total original cost of implementation of 104 projects when sanctioned, was of the order of Rs. 279823.29 crore but this was subsequently revised to Rs. 314625.85 crore implying a cost overrun of 12.4%. The expenditure incurred on these projects till January, 2015 is Rs. 146514.5 crore, which is 46.6% of the revised cost of the projects.

Figures are in Rs. Crore

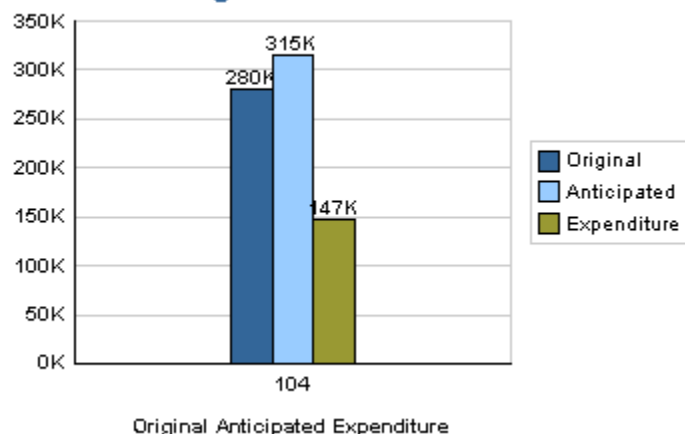

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	70
Number of Projects On Schedule	21
Number of Projects Delayed	43
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 2 projects are ahead of schedule, 21 projects are on schedule and 43 projects are delayed .4 projects do not have fixed dates of commissioning.

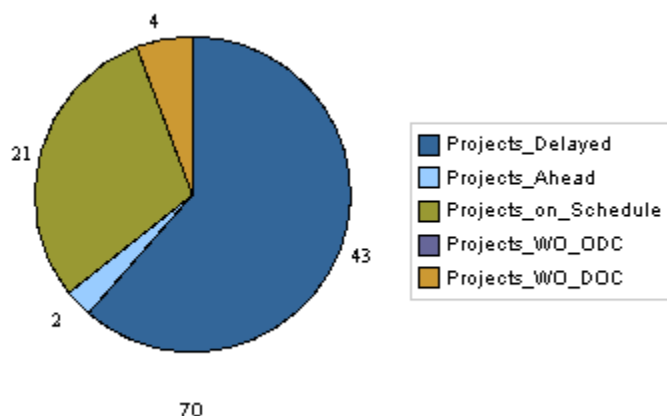

Investment Scenario

Total original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 160327.93 crore but this was subsequently revised to Rs. 177780.38 crore implying a cost overrun of 10.9%. The expenditure incurred on these projects till January, 2015 is Rs. 78921.95 crore, which is 44.4% of the revised cost of the projects.

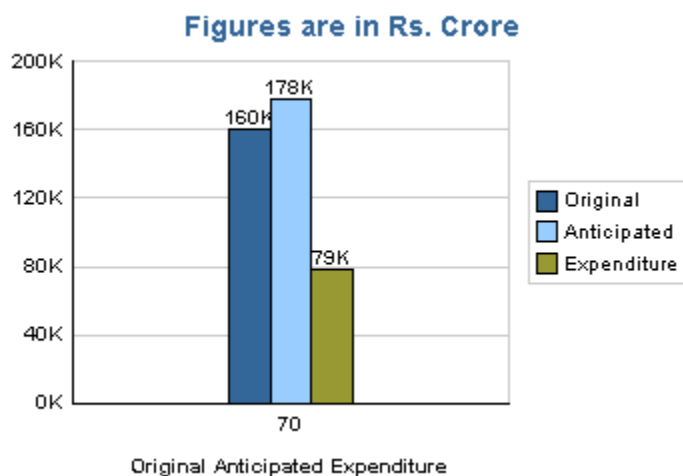

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	68
Number of Projects On Schedule	29
Number of Projects Delayed	36

Number of Projects Without Date Of Commissioning 3


Brief Analysis

Project Status with respect to Original Schedule: Out of 68 projects, 29 projects are on schedule and 36 projects are delayed .3 projects do not have fixed dates of commissioning.

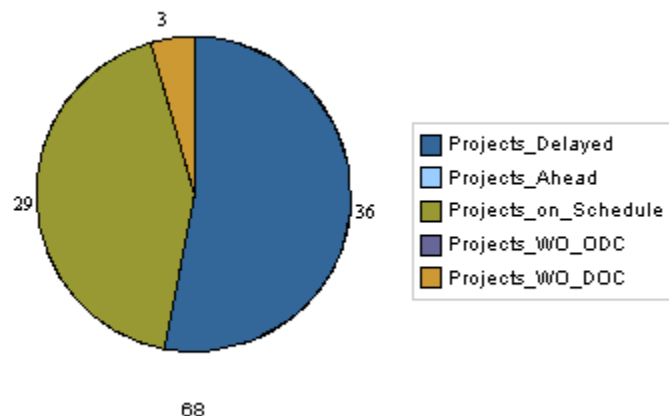

Investment Scenario

Total original cost of implementation of 68 projects when sanctioned, was of the order of Rs. 56782.14 crore but this was subsequently revised to Rs. 54116.57 crore implying a cost overrun of -4.7%. The expenditure incurred on these projects till January, 2015 is Rs. 19639.5 crore, which is 36.3% of the revised cost of the projects.

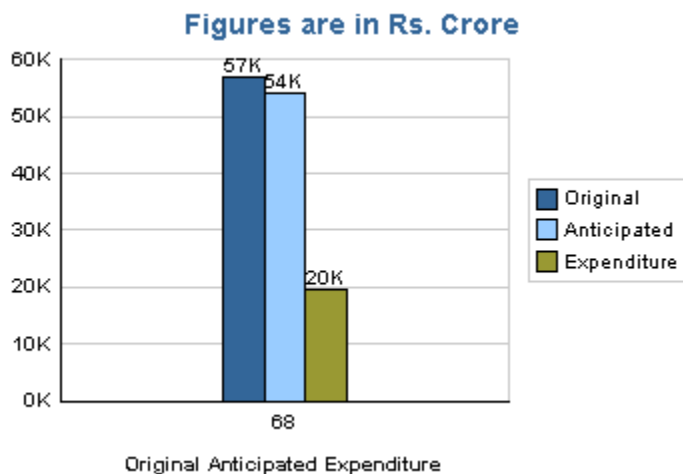

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 1 project are ahead of schedule, 4 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

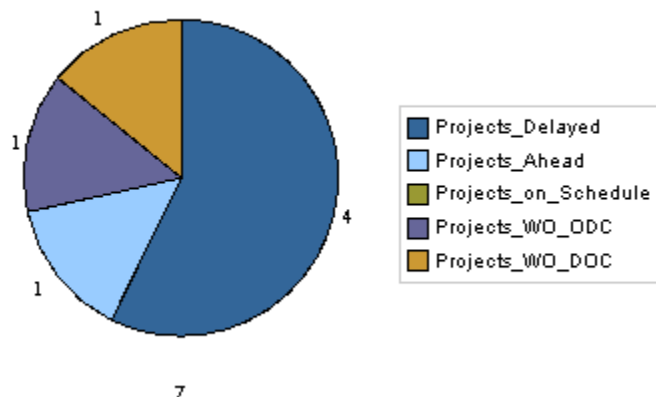

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently revised to Rs. 2652.48 crore implying a cost overrun of 2%. The expenditure incurred on these projects till January, 2015 is Rs. 1560.82 crore, which is 58.8% of the revised cost of the projects.

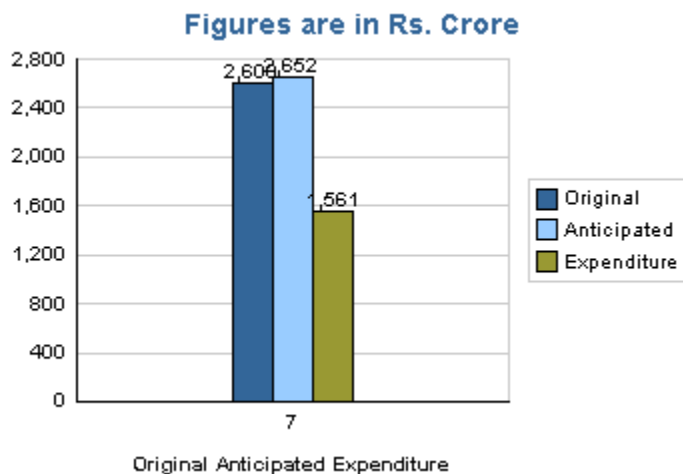

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

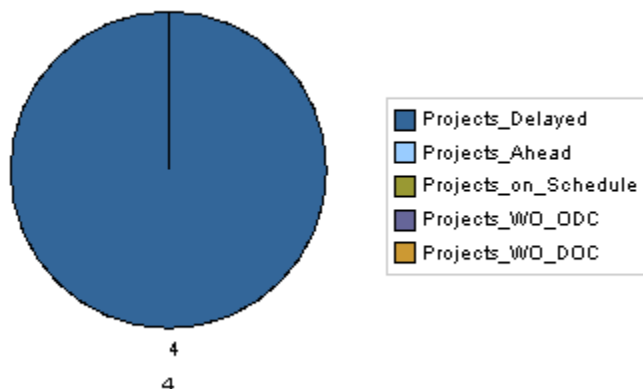

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till January, 2015 is Rs. 32749.78 crore, which is 63.1% of the revised cost of the projects.

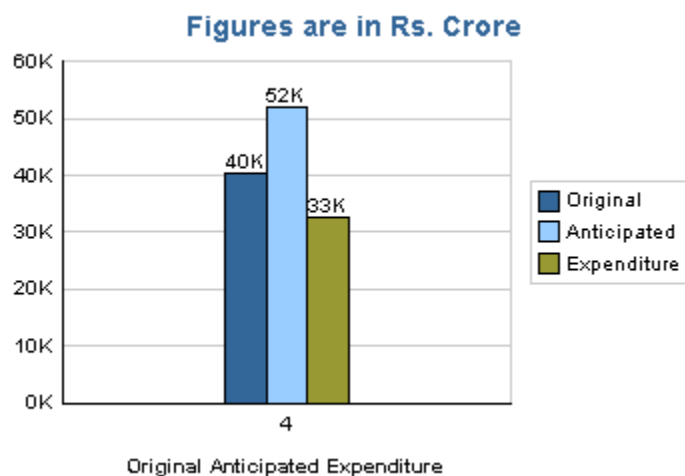

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	15.42
2	ANDHRA PRADESH	26	24,304.01	30,386.09	18,786.43
3	ARUNACHAL PRADESH	3	9,356.22	21,082.33	11,626.26
4	ASSAM	37	24,084.64	41,735.39	33,221.84
5	BIHAR	48	37,027.18	51,529.33	37,850.82
6	CHANDIGARH	1	452	452	377.99
7	CHHATISGARH	27	80,345.96	75,102.05	37,589.78
8	DELHI	10	48,728.6	48,728.6	10,176.14
9	GOA	1	335.61	388.53	292.44
10	GUJARAT	29	36,037.34	36,616.51	19,948.51
11	HARYANA	8	4,259.81	6,230.43	7,382.5
12	HIMACHAL PRADESH	5	11,681.24	17,740.61	11,565.06
13	JAMMU AND KASHMIR	7	21,314.62	40,235.3	17,788.24
14	JHARKHAND	32	35,868.09	36,532.76	14,028.38
15	KARNATAKA	32	64,122.2	78,947.89	16,964.15
16	KERALA	13	24,457.67	28,611.45	9,227.92
17	MADHYA PRADESH	18	25,308.88	27,292.8	9,404.58
18	MAHARASHTRA	47	1,00,936.03	1,12,834.02	35,148.66
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	3	4,845.02	6,069.9	1,049.99
21	MIZORAM	2	988.06	4,080.05	932.42
22	MULTI STATE	179	2,13,390.18	2,41,772.44	92,473.2
23	NAGALAND	2	5,124	7,461.12	10.44
24	ODISHA	41	69,075.15	78,123.21	40,236
25	PUNJAB	3	792.5	765.46	119.25
26	RAJASTHAN	25	25,638.72	25,694.2	14,606.05
27	SIKKIM	2	1,648.94	4,499.46	412.04
28	TAMIL NADU	42	68,133.49	90,782.21	47,779.44
29	TELANGANA	21	9,410.62	12,179.13	3,424.96
30	TRIPURA	6	2,966.26	7,231.71	3,211.92
31	UTTAR PRADESH	28	26,759.7	29,864.04	13,442.17
32	UTTARAKHAND	6	9,351.89	12,905.21	4,476.19
33	WEST BENGAL	39	42,838.9	52,232.8	19,051.42
TOTAL		745	10,30,625.7	12,34,992.39	5,35,408.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,111.82
2	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	4,828.46
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,108.5
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	3,561.01
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,633.27
6	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	1,006.03
12	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	800.66
13	NANDYAL-YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR-KASGANJ-MATHURA(GC), NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06
16	MUNEERABAD-MAHABOONAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	309.19
17	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	230.67
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	501.69	768.2
20	KATIHAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	743.74
21	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	798.87
22	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	04/1997	863.23	-	888.87
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	RAILWAYS	03/2002	625.3	408.76	835.14
24	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	596.66
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	889.95
26	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,732.43
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,536.83
28	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	301.84

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	639.77
30	HARIDASPUR-PARADEEP(NL)	RAILWAYS	04/1996	301.64	-	334.04
31	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	311.89
32	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	RAILWAYS	04/2002	921	-	1,548.9
34	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,339.6
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	3,198.3
36	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	211.48
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	284.12
38	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	284.82
39	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	268.5
40	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8
41	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	251.5
42	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	366.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
44	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	207.6
45	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	280.3
46	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	328.6
47	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	550.3
48	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	285.3
49	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	385.1
50	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	323.48
51	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,228.77
52	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,886.37
53	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	8,222.57
54	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	3,841.2
55	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	956.75
56	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	8,306

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	-	869.41
58	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	POWER	07/1998	368.72	-	733.11
59	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW)	POWER	07/2012	296.87	-	298.09
60	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	482.01
61	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	798.47
62	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
63	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
64	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
65	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
66	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
67	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
68	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	657.06
69	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	RAILWAYS	04/2008	516.23	-	596.08
70	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
72	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
73	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.72
74	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	792.98
75	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	251.16
76	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
77	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
78	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
79	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
80	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
81	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
82	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
83	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
84	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	324.92

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
86	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
87	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
88	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
89	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	315.9
90	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
91	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	345.8
92	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	276.7
93	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	334.8
94	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.6
95	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
96	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,125
97	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.5
98	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	667.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601
100	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,686
101	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
102	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,133
103	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
104	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
105	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
106	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
107	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
108	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,388
109	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
110	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
111	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	901.6
112	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	761.3
114	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
115	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	808.7
116	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
117	4 LANNING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,786
118	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	665.8
119	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	611.8
120	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.6
121	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,392
122	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	941
123	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
124	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,445
125	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,374
126	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	842.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	759.9
128	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
129	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
130	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
131	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	991.7
132	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	408.1
133	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	835.6
134	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
135	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	462
136	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	633.3
137	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
138	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
139	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,922
140	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,610

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
141	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,934
142	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	726.4
143	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	752.7
144	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	363.4
145	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC	ROAD TRANSPORT AND HIGHWAYS	10/2011	1,565	-	1,592

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		626.00 -		
	<u>COAL</u>				
2	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
4	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
	Total		1,056.69 -		
	<u>PETROCHEMICALS</u>				
5	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
6	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	12/2013 03/2014	12/2014
7	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	12/2014
8	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
9	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		9,599.43 -		
	<u>POWER</u>				
10	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
11	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
12	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
13	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		8,251.11		
	RAILWAYS				
14	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00	07/2008	07/2008
15	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87	-	03/2010
16	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00	-	02/2012
17	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74	-	03/2012
18	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09	-	03/2012
19	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01	06/1999	07/2012
20	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56	03/2012	12/2012
21	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03	12/2011	11/2013
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43	-	02/2014
23	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42	03/2014	03/2014
24	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42	03/2014	03/2014
25	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16	02/2009	08/2014
26	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41	03/2009	08/2014
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77	03/1994	10/2014
28	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13	-	10/2014
29	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00	12/2009	12/2014
30	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00	03/2009	12/2014
31	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00	12/2008	12/2014
32	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70	02/2006	-
33	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90	03/2010	-
34	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66	-	-
35	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00	12/2012	-
36	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05	12/2011	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
38	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
39	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
40	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
41	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
42	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
43	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
44	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
45	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
46	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
47	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
48	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
51	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
52	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
53	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
54	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
55	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
56	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
58	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
59	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
60	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
61	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]JECR,BIHAR	04/2001	406.92 -	- -	-
63	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
64	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
65	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
66	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]JECOR,ODISHA	04/2005	810.78 -	- -	-
67	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
68	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]JECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
69	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N220000028]MRT, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
70	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
72	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N220000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
73	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
74	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
75	TIDIVANAM-NAGARI (NL) - [N220000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
76	BARDHAMAN-KATWA (GC) - [N220000091]JER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
77	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N220000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
78	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N220000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
79	TINPAHAR - SAHIBGANJ (ER) - [N220000115]JER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
80	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N220000116]JER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
81	PANDABESWAR-CHINPAI DOUBLING (ER) - [N220000118]JER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
82	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N220000120]JWR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
83	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N220000121]JWR,GUJARAT	04/2008	394.14 -	03/2013 -	-
84	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N220000122]JWR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-
85	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N220000123]JWR,GUJARAT	04/2008	318.24 -	03/2012 -	-
86	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N220000125]JWR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
87	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N220000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
88	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
89	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
90	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
91	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
92	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
93	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
94	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
95	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
96	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
97	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
98	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
99	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
100	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
101	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
102	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
103	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
104	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
105	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
106	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
107	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
108	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
109	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
110	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
111	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
112	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
113	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
114	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
115	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
116	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
117	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
118	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
119	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
120	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
121	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
122	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
123	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
124	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
125	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
126	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
127	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
128	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
129	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
130	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
131	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
132	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-
133	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-
134	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
135	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	- -	-
136	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR, TAMIL NADU	04/1998	271.24 -	- -	-
137	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
138	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
139	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
140	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-
141	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
142	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
143	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
144	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
145	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
146	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
147	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
148	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
149	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
150	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
151	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
152	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
153	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
154	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
155	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
156	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
157	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
158	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
159	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
160	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
161	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
163	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
164	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
165	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
166	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
167	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
168	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
169	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
170	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
171	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
172	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
173	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
174	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
175	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
176	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
177	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
178	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
179	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
180	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
181	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
182	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
183	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
184	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
185	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
186	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
187	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
188	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
189	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
190	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
191	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
192	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
193	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
194	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
195	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
196	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
197	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
198	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
199	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
200	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
201	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
202	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
203	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
204	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
205	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
206	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
207	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
208	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
209	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
210	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
211	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
213	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
214	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
215	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
216	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
217	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
218	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
219	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
220	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
221	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
222	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
223	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
224	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
225	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
226	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
227	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
228	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
229	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
	Total		105,516.67 -		
	ROAD TRANSPORT AND HIGHWAYS				
230	PUNE-SHOLAPUR,PKG 1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
231	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
232	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
233	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013
234	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
235	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
236	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
237	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT - MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
238	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
239	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	11/2013
240	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
241	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	05/2014 -	05/2014
242	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	- -	07/2014
243	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	10/2014 -	10/2014
244	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	12/2014
245	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2014
246	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	10/2008 -	-
247	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-
248	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-
249	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	- -	-
250	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-
251	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-
	Total		15,475.56 -		
	SHIPPING AND PORTS				
252	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 -	-
253	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	03/2012 -	-
254	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-
255	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST, GUJARAT	02/2011	830.00 -	05/2013 -	-
256	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		3,930.07 -		
	URBAN DEVELOPMENT				

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012
258	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014
259	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
260	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
261	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
262	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
263	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
264	REHABILITATION AND STRENGTHENING OF SEWEWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
265	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		10,415.77 -		
	Grand Total		160,331.91		

Details of On Schedule Projects w.r.t. Original Schedule

						(January 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
	COAL						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	6/2008	7,612.33 -	1,188.31	756.49	03/2023 03/2023	03/2023
2	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	325.23	03/2015 -	03/2015
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	750.68	03/2016 -	03/2016
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.00 -	490.10	185.26	03/2017 -	03/2017
5	PELMA OCP(10.00MTY) - [N06000045	7/2008	1,624.59 -	1,624.59	-	03/2023 03/2023	03/2023
6	BATURA OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
7	PENGANGA OC - [N06000066	10/2008	441.82 -	441.82	42.32	03/2020 -	03/2020
8	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	71.67	03/2015 -	03/2015
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
10	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016
11	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	46.30	03/2018 -	03/2018
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
13	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	68.67	03/2016 -	03/2016
15	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	430.14	68.25	03/2016 -	03/2016
16	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	98.45	03/2020 -	03/2020
17	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
18	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
19	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
20	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	109.65	03/2018 -	03/2018
21	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	-	03/2019 -	03/2019

(January 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026
24	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
25	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
26	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021
27	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	-	03/2020 -	03/2020
28	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	7.14	03/2021 -	03/2021
29	GOKUL - [N06000120]	11/2014	267.67 -	267.67	7.33	03/2018 -	03/2018
	Total		28,169.97 -	21,374.00	2,897.42		
	<u>DUMMY SECTOR</u>						
30	TEST DUMMY - [N35000004]	1/2014	200.00 -	200.00	15.00	03/2018 -	03/2018
	Total		200.00 -	200.00	15.00		
	<u>FERTILISERS</u>						
31	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	0.79	11/2016 -	11/2016
	Total		197.79 -	197.79	.79		
	<u>MINES</u>						
32	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
33	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,334.97	05/2015 -	05/2015
34	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
35	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	-	12/2016 -	12/2016
36	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	1.94	02/2016 02/2016	02/2016
37	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	7.89	01/2017 -	01/2017
38	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,706.47	110.18	05/2017 -	05/2017

(January 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
39	RESID UPGRADE PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	383.78	11/2015 -	11/2015
40	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
41	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	7.60	07/2016 -	07/2016
42	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
43	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	11.10	02/2016 -	02/2016
44	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	80.42	09/2017 -	09/2017
45	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
46	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016
47	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.76	01/2016 -	01/2016
48	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015
49	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	4,831.09	05/2016 -	05/2016
50	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	360.03	08/2015 -	08/2015
51	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	39.33	07/2016 -	07/2016
52	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	260.98	04/2015 -	04/2015
53	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	879.16	11/2015 -	11/2015
	Total		57,918.79 -	60,023.02	10,545.92		
	POWER						
54	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,548.00	08/2015 -	08/2015
55	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	186.80	05/2016 -	05/2016
56	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018
57	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
58	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	-	10/2017 -	10/2017
59	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
60	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018
61	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,384.84	77.00	09/2019 -	09/2019

(January 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
62	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	1,960.00	02/2019 -	02/2019
63	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	22.00	10/2016 -	10/2016
64	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
65	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
66	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
67	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
68	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	26.80	08/2016 -	08/2016
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	4.20	06/2016 -	06/2016
71	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	3.07	04/2016 -	04/2016
72	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,124.00	08/2018 -	08/2018
73	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	529.00	03/2019 -	03/2019
74	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
75	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
76	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
77	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
78	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
79	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	440.60	03/2018 -	03/2018
80	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	118.89	03/2016 -	03/2016
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	513.59	03/2015 -	03/2015
83	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	0.95	06/2015 -	06/2015
84	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	346.65	12/2015 -	12/2015

(January 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	2,137.00	09/2017 -	09/2017
86	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,135.00	06/2017 -	06/2017
	Total		101,323.99 -	101,326.99	12,173.55		
	RAILWAYS						
87	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	478.77	03/2016 -	03/2016
88	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
89	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
90	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	137.01	03/2015 -	03/2015
91	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	250.37	03/2017 -	03/2017
92	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
93	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	36.31	03/2016 -	03/2016
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. [N22000111]	4/2010	2,913.51 -	2,619.02	480.06	03/2016 -	03/2016
95	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.03	02/2020 -	02/2020
97	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANTPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	4.66	02/2019 -	02/2019
98	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	86.31	03/2015 -	03/2015
	Total		16,286.25 -	20,383.01	3,249.36		
	ROAD TRANSPORT AND HIGHWAYS						
99	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2015
100	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
101	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015
102	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
103	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	177.78	09/2016 -	09/2016
104	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015

(January 2015)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
105	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015
106	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
107	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
	Total		13,092.05 -	13,092.05	3,909.08		
	STEEL						
108	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080	11/2012	313.05 -	313.05	181.17	06/2015 -	06/2015
109	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	21.05	05/2016 -	05/2016
110	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084	6/2014	708.91 -	708.91	64.41	04/2016 -	04/2016
111	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT [N12000085	4/2014	188.93 -	188.93	8.28	04/2015 -	04/2015
112	3RD CONVERTER AND 4TH CASTER - [N12000088	7/2011	974.76 -	974.76	35.15	07/2016 -	07/2016
113	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	8.52	10/2016 -	10/2016
114	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	-	09/2016 -	09/2016
	Total		3,054.32 -	3,199.72	318.58		
	TELECOMMUNICATIONS						
115	NETWORK FOR SPECTRUM - [N26000101	3/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	360.00		
	URBAN DEVELOPMENT						
116	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
117	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
118	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
119	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
120	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017
121	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019
122	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	5,181.79	688.45	07/2017 -	07/2017

(January 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
123	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		84,825.70 -	84,825.70	9,811.34		
	Grand Total		320,258.86	319,812.28	43,281.04		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

							(January 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	CIVIL AVIATION						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00	452.00	377.99	03/2015	02/2015
	Total		452.00	452.00	377.99		
	POWER						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74	1,508.74	473.88	06/2016	12/2015
	Total		1,508.74	1,508.74	473.88		
	PETROLEUM						
3	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26	276.27	209.97	12/2015	03/2015
4	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86	232.00	117.87	09/2016	12/2015
	Total		418.12	508.27	327.84		
	POWER						
5	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90	1,315.90	264.87	11/2016	03/2016
6	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52	1,364.52	66.14	05/2016	04/2016
	Total		2,680.42	2,680.42	331.01		
	Grand Total		5,059.28	5,149.43	1,510.72		

Details of Delayed Projects w.r.t. Original and Revised Schedule

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,132.00	12/2008 10/2013	04/2015	76	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,836.78	09/2010 09/2016	09/2016	72	62.57
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,998.00	12/2015 -	10/2017	22	0
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,783.00	12/2016 -	05/2018	17	0
	Total		40,442.00 -	51,918.00	32,749.78				
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	388.53	292.44	05/2012 -	02/2015	33	15.77
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	43.38	03/2014 -	03/2015	12	0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	0
8	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	323.48	01/2011 -	06/2016	65	0
	Total		1,206.95 -	1,259.87	659.34				
	COAL								
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,111.82	06/2009 03/2013	01/2015	67	66.86
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	439.43	03/2013 -	03/2015	24	-6.11
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,866.43	03/2012 05/2014	03/2015	36	34.63
12	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	151.27	03/2013 -	03/2015	24	0
13	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	122.11	10/2014 -	03/2015	5	0
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30	478.5
15	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,620.21	03/2014 -	03/2016	24	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
16	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,595.91	03/2014 -	03/2016	24	0
17	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44	50.37
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	8.02	03/2012 -	03/2016	48	0
19	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	-	03/2014 -	03/2016	24	0
20	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	46.04	03/2014 -	03/2016	24	0
21	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	232.39	03/2012 -	03/2016	48	0
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.80	03/2012 -	03/2016	48	0
24	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	0
25	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60	0
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.09	03/2012 -	03/2016	48	0
27	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	0
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.61	03/2010 -	03/2017	84	0
29	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	109.79	03/2011 -	03/2017	72	-27.57
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72	0
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	159.57	03/2013 -	03/2017	48	0
32	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84	0
33	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.48	12/2012 -	03/2017	51	0
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.66	03/2012 -	03/2017	60	0
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	118.51	03/2013 -	03/2017	48	0
36	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0
37	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	61.79	03/2012 -	03/2017	60	0
38	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.52	03/2014 -	03/2017	36	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
39	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.29	07/2016 -	03/2017	8	0
40	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0
42	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	472.62	12/2015 -	04/2018	28	0
43	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0
44	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0
	Total		27,555.48 -	31,685.88	16,665.60				
	STEEL								
45	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	383.84	12/2011 01/2015	03/2015	39	0
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,489.55	12/2012 -	03/2015	27	0
47	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,159.76	10/2009 10/2012	04/2015	66	41.41
48	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,007.37	12/2011 -	05/2015	41	0
49	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	483.99	09/2013 -	05/2015	20	0
50	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	353.72	09/2009 05/2012	06/2015	69	-6.25
51	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	438.26	04/2013 09/2014	06/2015	26	0
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	119.25	11/2013 -	06/2015	19	0
53	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	165.14	08/2014 -	06/2015	10	0
54	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	111.04	09/2014 -	06/2015	9	0
55	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	356.17	05/2013 01/2015	08/2015	27	0
56	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	144.40	10/2013 -	08/2015	22	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
57	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	134.21	12/2014 -	08/2015	8	0
58	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,996.99	03/2013 -	09/2015	30	0
59	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	75.67	07/2015 -	03/2016	8	0
60	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,012.46	05/2015 12/2016	12/2016	19	0
61	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	110.00	07/2015 -	03/2017	20	0
	Total		56,370.71 -	59,939.71	41,541.82				
	PETROLEUM								
62	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	01/2015	22	45.9
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	1,011.80	10/2011 -	02/2015	40	54.46
64	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,011.15	11/2012 11/2013	03/2015	28	16.05
65	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	214.78	08/2012 -	03/2015	31	-11.94
66	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	03/2015	33	-38.7
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	715.05	05/2013 06/2014	03/2015	22	-11.62
68	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,038.06	12/2014 -	03/2015	3	0
69	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	162.26	07/2013 -	03/2015	20	0
70	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	107.05	09/2012 -	04/2015	31	-24.14
71	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	101.82	03/2014 -	04/2015	13	0
72	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	101.09	03/2014 -	04/2015	13	0
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,886.37	08/2010 03/2012	05/2015	57	73.4
74	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-18.75

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5	0
76	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.40	05/2014 -	05/2015	12	-44.37
77	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015	110	820.2
78	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,334.01	12/2012 -	06/2015	30	0
79	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	122.07	12/2014 06/2015	06/2015	6	0
80	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	275.67	06/2011 03/2012	07/2015	49	-7.41
81	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	906.97	10/2011 -	10/2015	48	67.62
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,352.08	01/2012 -	10/2015	45	70.49
83	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2015	12	0
84	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13
85	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	104.64	03/2015 11/2015	11/2015	8	37.72
86	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	471.19	09/2011 -	12/2015	51	0
87	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,145.99	08/2015 -	12/2015	4	0
88	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.67	01/2014 -	12/2015	23	0
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	245.20	08/2015 -	12/2015	4	0
90	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	64.31	05/2015 -	12/2015	7	0
91	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,718.31	03/2013 03/2015	03/2016	36	-3.5
92	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,058.49	09/2012 -	03/2016	42	0
93	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	534.53	05/2014 -	03/2016	22	0
94	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.16	03/2015 -	05/2016	14	29.42

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
95	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0
96	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	199.87	10/2014 10/2015	10/2016	24	49.38
97	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 701.00	701.00	378.54	11/2015 -	11/2016	12	5.26
98	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.27	02/2016 04/2017	04/2017	14	31.51
99	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46	-6.92
100	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0
101	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	0
102	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 -	04/2018	23	0
103	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48	0
104	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	16.27	01/2013 -	02/2019	73	0
	Total		92,391.59 -	106,938.21	60,178.74				
	POWER								
105	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,306.00	10/2013 -	03/2015	17	0
106	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,604.75	05/2014 -	03/2015	10	0
107	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	980.43	02/2015 -	03/2015	1	0
108	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,402.67	10/2014 -	03/2015	5	0
109	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	187.34	03/2014 -	03/2015	12	0
110	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	801.40	08/2014 -	03/2015	7	13.7

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
111	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	1,147.58	12/2014 -	03/2015	3	0
112	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	94.03	10/2014 -	03/2015	5	0
113	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,253.06	12/2013 04/2015	04/2015	16	17.57
114	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPSS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,072.43	07/2014 -	05/2015	10	0
115	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	802.93	08/2014 -	05/2015	9	0
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	161.12	04/2015 -	05/2015	1	0
117	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,407.00	04/2009 -	06/2015	74	59.48
118	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	953.21	12/2007 12/2009	06/2015	90	0
119	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,521.57	11/2012 -	06/2015	31	0
120	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,037.69	08/2012 -	06/2015	34	0
121	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,709.43	03/2013 -	06/2015	27	13.18
122	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,600.10	12/2013 -	06/2015	18	0
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	458.32	07/2013 -	06/2015	23	0
124	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,655.67	03/2014 -	06/2015	15	20.87
125	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	91.30	01/2013 -	06/2015	29	0
126	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,394.76	11/2013 -	06/2015	19	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
127	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,583.46	09/2014 -	06/2015	9	0
128	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	358.71	11/2013 -	06/2015	19	0
129	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	321.72	06/2014 -	06/2015	12	0
130	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,390.96	08/2014 -	06/2015	10	0
131	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	461.60	02/2014 -	06/2015	16	0
132	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	252.57	08/2014 -	06/2015	10	16.63
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	466.32	11/2014 -	06/2015	7	0
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,960.41	10/2014 -	06/2015	8	0
135	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	878.18	11/2014 -	06/2015	7	0
136	TRIPURA GAS BASED POWER PROJECT - [N18000071]NNEPCO,TRIPURA	07/2009	421.01 -	842.77	869.41	07/2013 02/2011	08/2015	25	100.18
137	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 08/2010	12/2015	87	21.34
138	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	512.79	09/2010 -	12/2015	63	51.1
139	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,102.25	01/2015 -	12/2015	11	0
140	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,964.50	12/2012 -	12/2015	36	0
141	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	710.74	11/2012 -	12/2015	37	0
142	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	921.72	01/2015 -	12/2015	11	0
143	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	3,403.49	06/2015 -	12/2015	6	0

(January 2015) All Cost/ Expenditure in Rs. crore									
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
144	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	719.23	06/2015 -	12/2015	6	0
145	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	956.75	08/2013 03/2016	03/2016	31	96.59
146	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	425.16	11/2011 -	03/2016	52	0
147	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	307.17	02/2012 -	03/2016	49	0
148	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,013.88	10/2012 -	03/2016	41	0
149	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,902.60	08/2013 -	03/2016	31	0
150	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,104.52	04/2013 -	03/2016	35	0
151	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	933.03	11/2012 -	03/2016	40	0
152	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	0
153	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	57.64	09/2014 -	06/2016	21	0
154	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,633.27	09/2009 -	07/2016	82	81.76
155	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 -	1,259.80	733.11	07/2006 12/2015	10/2016	123	241.67
156	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,841.20	01/2016 -	11/2016	10	50.95
157	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,569.00	09/2016 -	02/2017	5	0
158	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,561.01	12/2009 03/2017	03/2017	87	86.39
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	4,982.00	09/2011 -	03/2017	66	54.25
160	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	6,644.00	01/2017 -	03/2017	2	0
161	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	328.00	12/2016 -	05/2017	5	0
162	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,944.00	11/2016 -	08/2017	9	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
163	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,586.00	12/2009 10/2014	03/2018	99	73.65
164	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,079.08	07/2010 02/2016	05/2018	94	79.77
165	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,348.00	03/2013 -	05/2018	62	29.14
166	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	571.03	07/2014 11/2018	11/2018	52	50.31
167	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,828.46	09/2009 -	03/2019	114	36.9
	Total		165,762.16 -	190,715.54	125,751.31				
	RAILWAYS								
168	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	19	-01
169	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73	466.97
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96	160.76
171	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	59.2
172	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0
173	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62
174	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	367.76
175	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41
176	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 495.44	1,781.98	408.79	03/2004 12/2010	03/2016	144	259.68
177	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	874.57	657.06	03/2013 -	03/2016	36	81.45
178	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41
179	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1
180	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4
181	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
182	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	134.30	03/2016 -	06/2016	3	0
183	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44
184	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4
185	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRT, MAHARASHTRA	04/2012	714.10 -	714.10	55.61	04/2016 -	03/2017	11	0
186	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08
187	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37
188	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34
189	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6
190	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6
192	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12
193	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRT, MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	1,815.37	03/2014 03/2019	03/2019	60	28.7
194	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79
195	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62
196	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76
197	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81
198	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81
	Total		25,945.26 -	82,251.23	36,462.77				
	ROAD TRANSPORT AND HIGHWAYS								
199	RAJMARG CHORHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	01/2015	75	0
200	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	01/2015	81	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
201	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	01/2015	59	0
202	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	02/2015	89	-1.84
203	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	02/2015	80	0
204	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	02/2015	80	0
205	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	02/2015	20	0
206	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18	0
207	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	02/2015	13	0
208	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	02/2015	31	0
209	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78	30.1
210	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	03/2015	78	0
211	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015	84	0
212	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90	82.12
213	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5
214	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27	0
215	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26	0
216	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	0
217	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	0
218	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	03/2015	15	0
219	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	0
220	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	0
221	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	0
222	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10	0

						(January 2015)	All Cost/ Expenditure in Rs. crore		
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
223	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25	0
224	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	03/2015	19	0
225	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2015	9	0
226	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6	0
227	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5	0
228	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8	0
229	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	250.50	363.40	10/2014 -	03/2015	5	0
230	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	03/2015	8	0
231	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6	0
232	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	03/2015	5	0
233	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	03/2015	6	0
234	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 04/2015	04/2015	84	0
235	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82	0
236	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	04/2015	20	0
237	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79	-8.95
238	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	05/2015	24	0
239	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	0
240	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	0
241	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	0
242	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
243	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74	92.75
244	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	06/2015	79	0
245	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	80.68
246	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74	0
247	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	06/2015	86	0
248	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 06/2015	06/2015	85	0
249	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	06/2015	71	85.58
250	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	33.7
251	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61	0
252	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	06/2015	33	0
253	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0
254	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	06/2015	26	0
255	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19	0
256	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	0
257	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22	0
258	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0
259	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86	0
260	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	08/2015	24	0
261	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87	0
262	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40	0
263	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26	0
264	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	0
265	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0

(January 2015) All Cost/ Expenditure in Rs. crore									
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
266	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13	0
267	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	0
268	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0
269	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	0
270	BIJUI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	0
271	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2015	82	0
272	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0
273	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	12/2015	63	0
274	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	0
275	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	0
276	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	0
277	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	0
278	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21	0
279	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	0
280	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0
281	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0
282	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27	0
283	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	0
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	0
285	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17	0
286	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	0
287	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
288	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25
289	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION (KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0
290	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	0
291	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	0
292	NASHRI CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0
293	CHENNAI-TADA (SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	0
294	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0
295	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	0
296	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	0
297	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0
298	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0
299	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2016	22	0
300	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	2.29
	Total		71,897.83 -	73,964.83	73,834.21				
	SHIPPING AND PORTS								
301	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	937.28	12/2010 09/2012	01/2016	61	70.89
	Total		1,228.00 -	2,098.56	937.28				
	TELECOMMUNICATIONS								
302	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL, ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74	0
303	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	50.93	10/2010 11/2015	09/2015	59	0
	Total		720.81 -	720.81	246.87				

						(January 2015)		All Cost/ Expenditure in Rs. crore	
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/ Year)	Original/ Revised Cost (Rs. crore)	Anticip ated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	URBAN DEVELOPMENT								
304	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	0
305	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0
306	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	0
307	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0
308	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	0
309	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	0
310	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	0
311	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0
312	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	0
313	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0
314	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0
315	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8	0
316	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	0
317	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0
	Total		43,553.53 -	43,553.53	1,081.72				
	Grand Total		527,074.32	645,046.17	390,109.44				

List of Projects having cost overrun with respect to Anticipated/Cumulative Expenditure

Detail of Cost Overrun projects (All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
1	ATOMIC ENERGY	NPCIL	KUDANKULAM APP (NPCIL)	13,171.00	22,462.00	18,132.00	9,291.00
2	ATOMIC ENERGY	BHAVNI	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	5,677.00	4,836.78	2,185.00
3	CIVIL AVIATION	AAI	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	309.46	309.46	323.48	14.00
4	CIVIL AVIATION	AAI	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	335.61	388.53	292.44	53.00
5	COAL	NLC	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	3,388.61	3,111.82	1,358.00
6	COAL	CCL	MAGADH OC 20 MTY (CCL)	469.78	706.40	46.55	237.00
7	COAL	SCCL	ADRIYALA SHAFT PROJECT	212.34	1,228.39	1,228.77	1,016.00
8	COAL	SECL	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	150.59	198.59	94.90	48.00
9	COAL	NLC	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	4,904.54	6,602.74	5,866.43	1,698.00
10	PETROCHEMICALS	BCPL	ASSAM GAS CRACKER PROJECT	5,460.61	8,920.00	8,222.57	3,459.00
11	PETROLEUM	ONGC	DEV OF G1 AND GS-15 (ONGCL)	429.82	3,955.21	3,439.48	3,525.00
12	PETROLEUM	IOCL	PARADIP REFINERY PROJECT	29,777.00	34,555.00	28,011.15	4,778.00
13	PETROLEUM	NRL	WAX PROJECT	576.60	676.05	596.64	99.00
14	PETROLEUM	ONGC	DEVELOPMENT OF B-193 CLUSTER FIELDS	3,248.78	5,633.44	5,886.37	2,638.00
15	PETROLEUM	GAIL	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	8,140.00	8,752.00	7,268.01	612.00
16	PETROLEUM	BPCL	INTEGRATED REFINERY EXPANSION PROJECT	14,225.00	16,504.00	4,831.09	2,279.00
17	PETROLEUM	HPCL	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	666.00	701.00	378.54	35.00
18	PETROLEUM	OIL	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	871.35	1,200.00	104.64	329.00
19	PETROLEUM	IOCL	MARKETING TOP AT KORBA	141.86	232.00	117.87	90.00
20	PETROLEUM	ISPR	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	993.00	1,693.00	1,352.08	700.00
21	PETROLEUM	OIL	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	352.56	450.55	10.60	98.00
22	PETROLEUM	ONGC	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	3,513.07	4,619.94	0.27	1,107.00
23	PETROLEUM	ISPR	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	732.00	1,227.00	906.97	495.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
24	PETROLEUM	ISPRL	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	672.00	1,038.00	1,011.80	366.00
25	PETROLEUM	HPCL	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	309.81	462.79	199.87	153.00
26	PETROLEUM	HPCL	REWARI KANPUR PIPELINE PROJECT	1,210.64	1,446.34	879.16	236.00
27	PETROLEUM	ONGC	INTEGRATED DEVELOPMENT OF B-127 FIELDS	2,059.63	2,665.65	605.16	606.00
28	PETROLEUM	ONGC	DEVELOPMENT OF CLUSTER-7 FIELDS	4,550.40	6,638.94	2,306.51	2,089.00
29	POWER	NHPC	PARBATI HEP (4X200 MW) (NHPC) II	3,919.59	5,366.00	4,828.46	1,446.00
30	POWER	NTPC	BARH STPP(3X660MW) NTPC	8,692.97	15,095.67	10,586.00	6,403.00
31	POWER	PGCIL	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	1,779.29	2,159.07	1,881.55	380.00
32	POWER	NHPC	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	1,061.38	1,929.15	1,633.27	868.00
33	POWER	NEEPC O	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	2,496.90	4,653.95	3,561.01	2,157.00
34	POWER	NTPC	RAMMAM-III HEPP (3X40 MW)	1,381.84	1,384.84	77.00	3.00
35	POWER	NEEPC O	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW)	296.87	1,128.38	298.09	832.00
36	POWER	PGCIL	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	901.77	1,025.28	801.40	124.00
37	POWER	NEEPC O	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	368.72	1,259.80	733.11	891.00
38	POWER	PGCIL	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	297.33	346.79	252.57	49.00
39	POWER	PGCIL	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	1,366.34	1,606.38	1,253.06	240.00
40	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	2,569.25	3,105.51	2,655.67	536.00
41	POWER	PGCIL	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	2,074.86	2,348.37	1,709.43	274.00
42	POWER	NEEPC O	TRIPURA GAS BASED POWER PROJECT	421.01	842.77	869.41	448.00
43	POWER	NTPC	BARH STPP STAGE -II	7,341.04	7,341.04	8,306.00	965.00
44	POWER	NEEPC O	PARE HYDRO ELECTRIC PROJECT	573.99	1,128.38	956.75	554.00
45	POWER	THDCIL	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	3,745.08	571.03	1,254.00
46	POWER	NTPC	BONGAIGAON THERMAL POWER PROJECT	4,375.35	6,749.18	4,982.00	2,374.00
47	POWER	PGCIL	WESTERN REGION STRENGTHENING SCHEME-V	477.69	721.81	512.79	244.00
48	POWER	NHPC	KISHANGANGA HEP (3X110 MW)	3,642.04	5,497.72	3,841.20	1,856.00
49	POWER	NTPC	TAPOVAN-VISHNUGAD HEP (4X130MW)	2,978.48	3,846.30	2,348.00	868.00
50	POWER	THDCIL	TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	2,978.86	1,079.08	1,322.00
51	POWER	NTPC	KOLDAM HEP (NTPC)	4,527.15	7,220.00	6,407.00	2,693.00
52	POWER	NHPC	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	6,285.33	15,300.00	7,108.50	9,015.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
53	RAILWAYS	NCR	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	158.77	608.02	595.67	449.00
54	RAILWAYS	CR	AMRAVATI-NARKHER NL(CR)	663.01	725.00	586.75	62.00
55	RAILWAYS	NFR	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	36.80	1,336.57	255.55	1,300.00
56	RAILWAYS	SR	CALICUT-MANGALORE (DL) (SR)	240.00	579.37	599.40	359.00
57	RAILWAYS	CR	AHMEDNAGAR-PARLI VAJNATH(NL) CR	514.68	2,820.00	329.67	2,305.00
58	RAILWAYS	SECR	GONDIA-JABALPUR(GC),(SECR)	386.30	1,544.40	590.26	1,158.00
59	RAILWAYS	NER	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	863.23	1,072.51	888.87	209.00
60	RAILWAYS	SCR	GULBARGA-BIDAR,SCR(NL)	242.42	844.00	798.87	602.00
61	RAILWAYS	SR	ANGAMALI-SABARIMALA (N.L.)(SR)	550.00	1,566.00	138.10	1,016.00
62	RAILWAYS	NFR	KATIHAR - JOGBANI (GC)(NEFR)	492.98	1,727.27	743.74	1,234.00
63	RAILWAYS	NCR	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	108.00	432.72	416.44	325.00
64	RAILWAYS	ECR	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	501.69	1,043.56	768.20	542.00
65	RAILWAYS	WCR	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	247.66	1,630.97	488.76	1,383.00
66	RAILWAYS	SCR	MACHERLA-NALGONDA(NL)(SCR)	125.00	480.00	3.51	355.00
67	RAILWAYS	SER	RANCHI-LOHARDAGA(GC),SER	194.07	335.00	230.67	141.00
68	RAILWAYS	NR	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	325.00	1,564.54	420.71	1,240.00
69	RAILWAYS	NFR	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	300.00	827.73	53.52	528.00
70	RAILWAYS	NFR	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	200.00	496.24	213.72	296.00
71	RAILWAYS	SR	TIDIVANAM-NAGARI (NL)	456.00	1,080.00	194.61	624.00
72	RAILWAYS	SR	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	125.00	490.00	67.57	365.00
73	RAILWAYS	NFR	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	170.00	485.00	417.70	315.00
74	RAILWAYS	SR	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	343.17	914.98	846.18	572.00
75	RAILWAYS	SR	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	404.19	1,383.45	457.88	979.00
76	RAILWAYS	RVNL	BHOPAL BINA 3D LINE DOUBLING	687.20	800.00	798.47	113.00
77	RAILWAYS	SWR	CHIKBALLA-PUR-GOWRIBIDANUR NL	327.25	367.77	0.00	41.00
78	RAILWAYS	SWR	GADAG-WADI NL	1,117.00	1,922.00	1.16	805.00
79	RAILWAYS	SWR	TORANAGALLU-RANJITPURA DL	146.75	167.50	0.31	21.00
80	RAILWAYS	NR	HARIDWAR-LAKSAR	219.83	329.97	2.38	110.00
81	RAILWAYS	SWR	WHITE FIELD-KOLAR NL	341.05	348.85	0.34	8.00
82	RAILWAYS	SWR	RAYADURGA-TUMKUR NL	970.34	1,743.00	313.85	773.00
83	RAILWAYS	SWR	SHIMOGA-HARIHAR NL	562.74	832.47	0.94	270.00
84	RAILWAYS	SWR	SRINIVASA-PURA-MADANAPALLI NL	296.00	466.65	0.02	171.00
85	RAILWAYS	SWR	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	558.00	692.43	0.00	134.00
86	RAILWAYS	NR	BHANUPALI-BILASPUR BERI NL	1,046.88	2,966.99	40.80	1,920.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
87	RAILWAYS	NR	ROHTAK-MEHAM HANSI	287.00	576.18	3.40	289.00
88	RAILWAYS	SCR	AKOLA-KHANDWA GC AKOLA-AKOT	184.26	2,000.00	17.32	1,816.00
89	RAILWAYS	SWR	BAGALKOT-KUDACHI NL	377.93	986.30	77.58	608.00
90	RAILWAYS	SWR	MUNIRABAD (GINGERA) -RAICHUR NL	179.65	1,350.91	324.92	1,171.00
91	RAILWAYS	SWR	TUMKUR-CHITRADURGA-DAVENGERE NL	913.00	1,801.01	1.12	888.00
92	RAILWAYS	CR	PANVEL PEN DOUBLING	96.16	260.16	240.21	164.00
93	RAILWAYS	CR	PEN ROHA DOUBLING	98.74	203.00	227.84	129.00
94	RAILWAYS	CR	KALYAN-KASARA 3RD LINE	277.70	279.70	4.73	2.00
95	RAILWAYS	CR	WARDHA-NANDED MAHARASHTRA	499.30	2,501.05	84.11	2,002.00
96	RAILWAYS	SR	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	601.43	800.00	0.69	199.00
97	RAILWAYS	M RTP	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	632.68	816.55	36.31	184.00
98	RAILWAYS	NFR	LUMDING-HOJAI PATCH DOUBLING PROJECT	246.07	364.06	0.30	118.00
99	RAILWAYS	NFR	AMBARI FALAKATA TO NEW MAYNAGURI	312.12	453.10	134.79	141.00
100	RAILWAYS	NFR	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	523.17	1,653.55	1,040.11	1,130.00
101	RAILWAYS	NFR	MURKONGSELEK-PASIGHAT NL	165.82	435.58	0.56	270.00
102	RAILWAYS	NFR	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	241.52	394.28	233.46	153.00
103	RAILWAYS	NFR	NEW BG LINE FROM BALURGHAT TO HILLY NFR	242.22	679.57	40.41	437.00
104	RAILWAYS	NFR	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4,083.02	5,307.90	7.79	1,225.00
105	RAILWAYS	SR	CHENGANNUR-CHINGAVANAM	191.72	222.95	122.80	31.00
106	RAILWAYS	SR	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	247.00	951.24	619.87	704.00
107	RAILWAYS	SR	MADURAI-BODINAYAKKANUR	164.41	450.00	16.97	286.00
108	RAILWAYS	SR	ERODE-PALANI	288.57	603.22	1.64	315.00
109	RAILWAYS	NFR	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	283.55	288.81	11.74	5.00
110	RAILWAYS	NFR	NEW COOCHBEHAR TO SAMUKTALA	209.77	441.45	85.78	232.00
111	RAILWAYS	NFR	DIMAPUR-TIZIT NL	4,274.00	4,487.70	0.00	214.00
112	RAILWAYS	NFR	AGARTALA-AKHAURA NL	252.00	888.65	0.00	637.00
113	RAILWAYS	NFR	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	895.00	1,242.25	1,005.81	347.00
114	RAILWAYS	NFR	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	221.42	563.13	22.29	342.00
115	RAILWAYS	SR	KURUPPANTHARA-CHINGAVANAM	270.14	346.15	14.82	76.00
116	RAILWAYS	SR	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	822.39	1,280.83	1,031.83	458.00
117	RAILWAYS	SR	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	271.24	520.00	462.69	249.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
118	RAILWAYS	SR	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	198.68	556.64	268.56	358.00
119	RAILWAYS	SR	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	839.00	1,500.00	0.01	661.00
120	RAILWAYS	SR	CHENNAI-CUDDALORE VIA MAMALLAPURAM	523.52	1,200.00	2.07	676.00
121	RAILWAYS	SR	ATTIPPATTU-PUTTUR	446.87	528.00	2.96	81.00
122	RAILWAYS	NFR	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	1,798.00	1,887.90	0.00	90.00
123	RAILWAYS	ECR	HAJIPUR-RAMDAYALUNAGAR DOUBLING	213.01	367.17	10.38	154.00
124	RAILWAYS	ECOR	CHHAPRA-MUZAFFARPUR (NL)	285.07	378.56	107.03	93.00
125	RAILWAYS	ECOR	SAKRI-HASANPUR ROAD (NL)	175.69	325.00	251.16	149.00
126	RAILWAYS	SER	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	258.20	365.00	2.52	107.00
127	RAILWAYS	SER	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	309.44	583.00	144.66	274.00
128	RAILWAYS	SER	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	149.90	230.00	68.67	80.00
129	RAILWAYS	SER	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	289.64	760.00	0.09	470.00
130	RAILWAYS	SER	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	553.63	1,009.00	7.50	455.00
131	RAILWAYS	SER	BOWAICHANDI-ARAMBAGH	267.37	434.00	35.90	167.00
132	RAILWAYS	NCR	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	622.41	2,030.50	4.66	1,408.00
133	RAILWAYS	NWR	AJMER-BANGURGRAM	213.39	218.39	21.57	5.00
134	RAILWAYS	NWR	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	739.65	872.22	792.98	133.00
135	RAILWAYS	NWR	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	456.00	855.16	557.72	399.00
136	RAILWAYS	NWR	THIYAT HAMIRA-SANU	236.93	262.00	0.00	25.00
137	RAILWAYS	NCR	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	1,176.09	3,845.60	2.03	2,670.00
138	RAILWAYS	NWR	RATLAM-DUNGARPUR VIA BANSWARA (NL)	2,082.75	3,500.00	44.92	1,417.00
139	RAILWAYS	WR	VIRAMGAM-SAMAKHIALI (DL)	446.00	685.17	206.59	239.00
140	RAILWAYS	WR	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	320.66	913.48	457.67	593.00
141	RAILWAYS	NER	CHHAPRA-BALLIA UP	295.00	494.92	4.22	200.00
142	RAILWAYS	NFR	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	1,676.31	5,500.00	4,734.45	3,824.00
143	RAILWAYS	NFR	KATAKHAL TO BHAIRABI	227.90	331.40	182.22	104.00
144	RAILWAYS	WR	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	117.36	196.95	198.83	81.00
145	RAILWAYS	NFR	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	850.00	2,973.42	10.44	2,123.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
146	RAILWAYS	WR	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	318.24	321.62	2.91	3.00
147	RAILWAYS	WR	RATLAM-MHOW-KHANDWA-AKOLA (GC)	603.04	1,421.25	420.33	818.00
148	RAILWAYS	ER	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	207.52	207.52	223.44	16.00
149	RAILWAYS	NWR	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	516.23	516.23	596.08	80.00
150	RAILWAYS	SER	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	148.77	209.00	2.64	60.00
151	RAILWAYS	NER	GHAZIPUR - AUNRIHAR (40 KM)	182.92	197.73	0.00	15.00
152	RAILWAYS	ECOR	DELANG-PURI DOUBLING	165.16	234.71	137.01	70.00
153	RAILWAYS	ECOR	KIRANDUL - JAGDALPUR DOUBLING	826.57	1,143.60	189.12	317.00
154	RAILWAYS	ECOR	JHARSUGUDA-RENGALI DOUBLING	201.00	230.00	218.67	29.00
155	RAILWAYS	ECOR	SAMBALPUR-TALCHER DOUBLING	679.27	1,111.99	60.31	433.00
156	RAILWAYS	SER	MM FROM PANSKURA-GHATAL NL	276.69	426.00	0.00	149.00
157	RAILWAYS	SER	MM FROM BURAMARA-CHAKULIA	466.48	800.00	0.83	334.00
158	RAILWAYS	SR	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	460.94	1,030.00	804.20	569.00
159	RAILWAYS	SWR	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	482.00	874.57	657.06	393.00
160	RAILWAYS	NFR	SEVOK RANGPO, NEFR	1,339.48	4,190.00	88.56	2,851.00
161	RAILWAYS	NFR	KISHANGANJ JALALGARH, NL, NEFR	282.92	565.13	2.80	282.00
162	RAILWAYS	NFR	BHAIRABI SAIRONG, NL, NEFR	619.34	2,820.25	199.31	2,201.00
163	RAILWAYS	NFR	AGARTALA SABROOM, NL, NEFR	813.34	2,876.00	823.83	2,063.00
164	RAILWAYS	SER	TAMLUK DIGHA,LINE DOUBLING (SER)	293.97	1,428.00	466.36	1,134.00
165	RAILWAYS	RE	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	171.10	272.39	141.55	101.00
166	RAILWAYS	M RTP	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	5,300.00	6,821.29	1,815.37	1,521.00
167	RAILWAYS	RVNL	SALKA ROAD -ANUPNAGAR LINE DOUBLING	324.90	385.54	233.44	61.00
168	RAILWAYS	WS&PU	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	470.09	1,417.97	1,011.09	948.00
169	RAILWAYS	WS&PU	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU	98.74	337.30	222.07	239.00
170	RAILWAYS	RVNL	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	743.00	1,117.11	465.19	374.00
171	RAILWAYS	SER	GOELKERA-MANOHARPUR,(LD)(SER)	261.70	280.00	147.94	18.00
172	RAILWAYS	SCR	MANOHARABAD-KOTHPALL NEW LINE(SCR)	378.56	791.59	5.41	413.00
173	RAILWAYS	ECR	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	332.92	477.88	482.01	149.00
174	RAILWAYS	ECR	PATNA GANGA BRIDGE (NL), ECR	624.47	2,921.00	2,339.60	2,297.00
175	RAILWAYS	ECR	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	921.00	2,363.00	1,548.90	1,442.00
176	RAILWAYS	ECR	KOSI BRIDGE (NL), ECR	322.95	341.41	301.09	18.00
177	RAILWAYS	NFR	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	727.56	6,570.75	2,787.99	5,843.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
178	RAILWAYS	RVNL	RAJATGARH-BARANG(LD),ECOR	166.16	288.00	311.89	146.00
179	RAILWAYS	RVNL	HARIDASPUR-PARADEEP(NL)	301.64	1,185.64	334.04	884.00
180	RAILWAYS	ECOR	KHURDA ROAD-BOLANGIR(NL)ECOR	470.21	1,995.25	355.02	1,525.00
181	RAILWAYS	NR	JIND-SONEPAT (NL),NR	238.56	740.00	639.77	501.00
182	RAILWAYS	SER	BANKURA - DAMODAR (GC) (SER)	111.90	2,371.85	486.25	2,260.00
183	RAILWAYS	RVNL	RAICHUR-GUNTAKAL(DL)(SCR)	136.62	289.93	284.82	153.00
184	RAILWAYS	RVNL	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	133.41	276.00	284.12	151.00
185	RAILWAYS	RVNL	CUTTACK - BARANG (LD)	127.13	225.00	211.48	98.00
186	RAILWAYS	RVNL	SUKINDA ROAD - ANGUL (NL)(ECOR)	183.23	818.29	116.37	635.00
187	RAILWAYS	SECR	CHHINDWARA - NAGPUR (GC)(SECR)	383.79	1,101.16	194.91	717.00
188	RAILWAYS	NCR	ETAWAH-MAINPURI (NL),NCR	120.00	245.39	235.70	125.00
189	RAILWAYS	NER	MAHARAJGANJ-MASRAKH (NL) - NER	218.19	343.00	216.17	125.00
190	RAILWAYS	NFR	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	915.70	3,700.00	3,198.30	2,784.00
191	RAILWAYS	WCR	RAMGANJMUUNDI-BHOPAL (NL),WCR	470.92	1,225.90	257.59	755.00
192	RAILWAYS	SWR	BANGLORE - SATYAMANGALAM (NL)(SWR)	138.00	1,382.78	0.82	1,245.00
193	RAILWAYS	SCR	GADWAL - RAICHUR (NL), SCR	92.63	270.00	301.84	209.00
194	RAILWAYS	M RTP	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	1,049.69	3,404.92	3,536.83	2,487.00
195	RAILWAYS	NFR	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	733.00	2,531.34	1,732.43	1,798.00
196	RAILWAYS	SCR	KOTLPALLI-NARASAPUR (NL) (SCR)	330.00	1,047.00	1.29	717.00
197	RAILWAYS	SR	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	280.00	1,122.00	889.95	842.00
198	RAILWAYS	SR	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	100.00	980.00	596.66	880.00
199	RAILWAYS	NR	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	625.30	847.75	835.14	222.00
200	RAILWAYS	SER	HOWRAH-AMTA-CHAMPADANGA NL (SER)	393.46	1,026.00	181.48	633.00
201	RAILWAYS	SCR	MUNEERABAD-MAHABOBNAGAR(NL),SCR	218.24	645.00	309.19	427.00
202	RAILWAYS	NFR	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	1,500.00	4,996.19	3,410.06	3,496.00
203	RAILWAYS	NER	KANPUR-KASGANJ-MATHURA(GC),NER	677.97	1,651.54	1,621.40	974.00
204	RAILWAYS	SWR	HUBLI-ANKOLA(NL),SWR	227.00	2,135.00	116.82	1,908.00
205	RAILWAYS	SCR	NANDYAL-YERRAGUNTALA(NL),SCR	155.74	883.00	755.50	727.00
206	RAILWAYS	SR	KARUR-SALEM(NL),SR	155.55	800.00	800.66	645.00
207	RAILWAYS	NR	NANGALDAM-TALWARA(NL),NR	450.00	2,100.00	391.95	1,650.00
208	RAILWAYS	SWR	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	295.00	1,289.92	1,006.03	995.00
209	RAILWAYS	M RTP	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	495.44	1,781.98	408.79	1,287.00
210	RAILWAYS	RVNL	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	304.00	968.60	150.78	665.00
211	RAILWAYS	NR	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	19,565.00	10,658.34	17,065.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
212	RAILWAYS	SCR	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	124.43	925.30	712.02	801.00
213	RAILWAYS	WR	VIRAMGAM-BHILDI(WR),GC	155.66	548.01	201.26	392.00
214	ROAD TRANSPORT AND HIGHWAYS	NHAI	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	157.47	154.57	268.50	111.00
215	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	195.00	195.00	280.30	85.00
216	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC	1,565.00	1,565.00	1,592.00	27.00
217	ROAD TRANSPORT AND HIGHWAYS	NHAI	2 LANING WITH PS AGRA ALIGARH	250.50	250.50	363.40	113.00
218	ROAD TRANSPORT AND HIGHWAYS	NHAI	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION	682.00	682.00	752.70	71.00
219	ROAD TRANSPORT AND HIGHWAYS	NHAI	KRISHNANAGAR-BERHAMPUR	702.16	702.16	726.40	24.00
220	ROAD TRANSPORT AND HIGHWAYS	NHAI	6-LANING OF DHANKUNI-KHARAGPUR SECTION	1,396.18	1,396.18	1,934.00	538.00
221	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF BRAHAMPORE-FARAKA	998.79	998.79	1,610.00	611.00
222	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF FARAKA-RAIGANJ	1,078.84	1,078.84	1,922.00	843.00
223	ROAD TRANSPORT AND HIGHWAYS	NHAI	JAIPUR-REENGUS	267.81	267.81	699.60	432.00
224	ROAD TRANSPORT AND HIGHWAYS	NHAI	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	909.00	909.00	982.90	74.00
225	ROAD TRANSPORT AND HIGHWAYS	NHAI	BHUBANESWAR TO PURI	500.29	500.29	633.30	133.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
226	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANING OF BARHI-HAZARIBAGH	398.00	398.00	462.00	64.00
227	ROAD TRANSPORT AND HIGHWAYS	NHAI	2 LANNING OF MUZAFFARPUR - SONBARSA	511.54	511.54	1,179.00	667.00
228	ROAD TRANSPORT AND HIGHWAYS	NHAI	4-LANNING OF CHAPRA-HAJIPUR	575.00	575.00	835.60	261.00
229	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING WITH PS MOTIHARI-RAXAUL	375.09	375.09	408.10	33.00
230	ROAD TRANSPORT AND HIGHWAYS	NHAI	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	574.00	574.00	991.70	418.00
231	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING WITH PS KHAGARIA-PURNEA	664.00	664.00	776.40	112.00
232	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	1,535.00	1,535.00	2,188.00	653.00
233	ROAD TRANSPORT AND HIGHWAYS	NHAI	BRAHMPUTRA BRIDGE,NH NO-31	217.61	309.56	258.40	92.00
234	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG, NH-54	196.00	363.74	242.10	168.00
235	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	212.00	386.10	127.10	174.00
236	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHARAMTUL TO SONAPUR (AS-19)	200.00	200.00	289.50	90.00
237	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	160.00	160.00	197.60	38.00
238	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI T BIJNI (AS-7)	208.00	208.00	334.80	127.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
239	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI TO BIJNI (AS-6)	225.00	225.00	276.70	52.00
240	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUWAHATI TO NALBARI (AS-5)	198.16	198.16	345.80	148.00
241	ROAD TRANSPORT AND HIGHWAYS	NHAI	SONAPUR TO GUWAHTI (AS-3)	245.00	245.00	491.20	246.00
242	ROAD TRANSPORT AND HIGHWAYS	NHAI	ARMUR TO KADLOOR YELLAREDDY	390.56	390.56	631.70	241.00
243	ROAD TRANSPORT AND HIGHWAYS	NHAI	HAZARIBAGH-RANCHI	625.07	625.07	995.90	371.00
244	ROAD TRANSPORT AND HIGHWAYS	NHAI	TALEGAON-AMRAVATI	567.00	567.00	1,388.00	821.00
245	ROAD TRANSPORT AND HIGHWAYS	NHAI	JAIPUR-TONK-DEOLI	792.06	792.06	1,983.00	1,191.00
246	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	1,108.00	2,288.00	3,466.00	2,358.00
247	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	572.30	572.30	886.90	315.00
248	ROAD TRANSPORT AND HIGHWAYS	NHAI	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	1,693.75	1,693.75	2,762.00	1,068.00
249	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHENNAI-TADA(SIX LANE)	353.37	353.37	446.20	93.00
250	ROAD TRANSPORT AND HIGHWAYS	NHAI	KISHANGARH-AJMER-BEAWER	795.00	795.00	1,133.00	338.00
251	ROAD TRANSPORT AND HIGHWAYS	NHAI	INDORE-DEWAS(NH-3)	325.00	325.00	611.80	287.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
252	ROAD TRANSPORT AND HIGHWAYS	NHAI	BELGAUM-DHARWAD(NH-4)	480.00	480.00	665.80	186.00
253	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANING OF NAGPUR-BETUL	2,498.76	2,498.76	2,786.00	287.00
254	ROAD TRANSPORT AND HIGHWAYS	NHAI	MURADABAD-BAREILY	1,267.00	1,267.00	2,425.00	1,158.00
255	ROAD TRANSPORT AND HIGHWAYS	NHAI	DEVIHALLI-HASSAN	453.00	453.00	808.70	356.00
256	ROAD TRANSPORT AND HIGHWAYS	NHAI	PANIPAT-ROHTAK	807.00	807.00	1,209.43	402.00
257	ROAD TRANSPORT AND HIGHWAYS	NHAI	DEOLI-KOTA	593.00	593.00	761.30	168.00
258	ROAD TRANSPORT AND HIGHWAYS	NHAI	KUNDUPUR-SURATHKAL & MANGLORE	671.00	671.00	1,273.00	602.00
259	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	852.00	852.00	901.60	50.00
260	ROAD TRANSPORT AND HIGHWAYS	NHAI	2-LANNING OF SHILONG BYPASS	226.00	226.00	282.30	56.00
261	ROAD TRANSPORT AND HIGHWAYS	NHAI	JORBAT - BARAPANI	536.00	536.00	759.90	224.00
262	ROAD TRANSPORT AND HIGHWAYS	NHAI	SAMAIKHALI - GANDHIDHAM	805.39	805.39	842.20	37.00
263	ROAD TRANSPORT AND HIGHWAYS	NHAI	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	1,250.00	1,250.00	1,374.00	124.00
264	ROAD TRANSPORT AND HIGHWAYS	NHAI	GHAZIABAD-ALIGARH NH-91	1,141.00	1,141.00	2,445.00	1,304.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
265	ROAD TRANSPORT AND HIGHWAYS	NHAI	ROHTAK-BAWAL	650.00	650.00	1,178.00	528.00
266	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	785.50	785.50	941.00	156.00
267	ROAD TRANSPORT AND HIGHWAYS	NHAI	4 LANNING OF AHMEDABAD TO GODHARA	1,008.50	1,008.50	1,392.00	384.00
268	ROAD TRANSPORT AND HIGHWAYS	NHAI	2 LANNING OF MOKAMA-MUNGER	351.54	351.54	396.60	45.00
269	ROAD TRANSPORT AND HIGHWAYS	NHAI	PUNE-SHOLAPUR,PKG1	1,110.00	1,110.00	1,826.00	716.00
270	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	1,509.10	1,509.10	2,686.00	1,177.00
271	ROAD TRANSPORT AND HIGHWAYS	NHAI	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	940.00	940.00	1,601.00	661.00
272	ROAD TRANSPORT AND HIGHWAYS	NHAI	DELHI/ HARYANA BORDER TO ROHTAK	486.00	486.00	667.10	181.00
273	ROAD TRANSPORT AND HIGHWAYS	NHAI	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	232.45	232.45	317.50	85.00
274	ROAD TRANSPORT AND HIGHWAYS	NHAI	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	557.00	557.00	1,125.00	568.00
275	ROAD TRANSPORT AND HIGHWAYS	NHAI	AGRA-BYPASS(NS-1/UP-1), NH-2,3	348.16	465.50	322.70	117.00
276	ROAD TRANSPORT AND HIGHWAYS	NHAI	CHAMBAL BRIDGE, NH-76 (RJ-5)	275.00	281.31	180.10	6.00
277	ROAD TRANSPORT AND HIGHWAYS	NHAI	NAGAON TO DHARAMTUL (AS-2)	264.72	264.72	315.90	51.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
278	ROAD TRANSPORT AND HIGHWAYS	NHAI	GUWHATI TO NALBARI (AS-4)	175.96	175.96	182.50	7.00
279	ROAD TRANSPORT AND HIGHWAYS	NHAI	NALBARI TO BIJNI (AS-8)	200.00	200.00	281.60	82.00
280	ROAD TRANSPORT AND HIGHWAYS	NHAI	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	251.03	251.03	385.10	134.00
281	ROAD TRANSPORT AND HIGHWAYS	NHAI	KOTA BYPASS,RJ-4, NH-76 (NHAI)	275.00	250.39	285.30	10.00
282	ROAD TRANSPORT AND HIGHWAYS	NHAI	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	550.30	217.00
283	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	237.80	237.80	328.60	91.00
284	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	200.00	200.00	207.60	8.00
285	ROAD TRANSPORT AND HIGHWAYS	NHAI	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	155.00	201.66	191.80	47.00
286	ROAD TRANSPORT AND HIGHWAYS	NHAI	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	280.00	280.00	366.80	87.00
287	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	199.81	385.13	159.20	185.00
288	ROAD TRANSPORT AND HIGHWAYS	NHAI	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	155.04	280.13	173.80	125.00
289	ROAD TRANSPORT AND HIGHWAYS	NHAI	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	230.00	230.00	251.50	22.00
290	SHIPPING AND PORTS	MUMBAI PORT TRU	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	1,228.00	2,098.56	937.28	871.00
291	SHIPPING AND PORTS	PORT TRUST	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	150.00	600.00	0.00	450.00

Detail of Cost Overrun projects							
(All Cost/ Expenditure in Rs. crore)							
Sl.No	Sector	Agency	Project	Original Cost	Anticipated Cost	Cumulative Expenditure	Cost overrun
292	SHIPPING AND PORTS	RVNL	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	245.67	373.22	0.00	128.00
293	STEEL	RINL	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	8,692.00	12,291.00	11,159.76	3,599.00
294	STEEL	RINL	REVAMPING OF SINTER MACHINES - 1 AND 2	343.00	488.40	8.52	145.00
295	URBAN DEVELOPMENT	M RTP	BANGALORE METRO RAIL PROJECT	6,395.00	11,609.00	0.00	5,214.00
296	URBAN DEVELOPMENT	CPWD	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	114.18	173.08	0.00	59.00
			TOTAL	309,944.02	525,008.76	325,137.82	238,736.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	04/2015	70.54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2015	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	01/2015	66.86
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
8	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	03/2015	34.63
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,258.03 -	12,614.83			
	<u>PETROCHEMICALS</u>						
10	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	8,920.00			
	<u>PETROLEUM</u>						
11	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
12	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2015	73.40

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05
14	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	12/2014	17.25
15	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	4,550.40 -	6,638.94	03/2013 -	01/2015	45.90
16	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	08/2010	8,140.00 -	8,752.00	02/2014 -	12/2014	7.52
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
18	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
19	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
20	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	701.00	11/2015 -	11/2016	5.26
21	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
24	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51
25	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
27	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
28	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72
	Total		72,745.78 -	92,727.18			
	<u>POWER</u>						
30	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90
31	KOLDAM HEP (NTPC) - [180100211]	01/2011	4,527.15 -	7,220.00	04/2009 -	06/2015	59.48
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
34	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65

(January 2015)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
35	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	12/2015	21.34
37	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14
39	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
40	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10
41	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
43	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	03/2016	96.59
44	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	842.77	07/2013 -	08/2015	100.18
45	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	09/2010	2,074.86 -	2,348.37	03/2013 -	06/2015	13.18
46	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096	03/2011	2,569.25 -	3,105.51	03/2014 -	06/2015	20.87
47	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH [N18000105	09/2011	1,366.34 -	1,606.38	12/2013 -	04/2015	17.57
48	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	06/2015	16.63
49	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,259.80	07/2006 02/2015	10/2016	241.67
50	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	1,025.28	08/2014 -	03/2015	13.70
51	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) [N18000156	07/2012	296.87 -	1,128.38	- -	03/2015	280.09
52	RAMMAM-III HEPP (3X40 MW) - [N18000178	09/2014	1,381.84 -	1,384.84	09/2019 -	09/2019	0.22
	Total		54,636.73 -	89,439.29			
	<u>RAILWAYS</u>						
53	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96
54	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
55	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
56	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
57	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
58	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
59	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
60	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
61	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91
63	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
64	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
65	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
66	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
67	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
68	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
73	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
74	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
75	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
77	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
78	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
79	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
80	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
81	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
82	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
83	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
84	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
85	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
86	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
87	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
88	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
89	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
90	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
91	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
92	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
93	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
94	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
95	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
96	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
97	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
98	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
99	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
100	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
101	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
102	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	12/2014	104.49
103	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
104	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	-	346.59
105	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
106	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
107	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
108	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
109	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
110	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]	04/2006	378.56 -	791.59	- -	-	109.11
111	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]	03/1997	261.70 -	280.00	02/2006 -	-	6.99
112	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
113	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N220000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
114	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053]	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
115	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
116	BHOPAL BINA 3D LINE DOUBLING - [N220000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
117	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N220000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
118	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
119	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
120	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]	09/2006	125.00 -	490.00	- -	-	292.00
121	TIDIVANAM-NAGARI (NL) - [N220000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
122	NEW B.G. LINE FROM TETELIA TO BYRNIAH (NATIONAL PROJECT), NEFR - [N220000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
123	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
124	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
125	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
126	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
127	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
128	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
129	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
130	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
131	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
132	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45
133	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
134	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
135	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
136	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
137	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
138	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
139	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
140	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
141	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
142	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
143	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
144	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
145	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
146	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
147	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
148	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
149	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
150	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
151	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
152	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
153	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
154	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
155	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
156	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
157	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
158	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
159	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
160	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
161	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
162	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
163	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
164	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
165	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
166	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
167	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
168	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
169	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	888.65	- -	03/2018	252.64
170	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
171	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
172	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
173	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
174	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
175	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
176	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
177	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
178	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
179	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
180	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
181	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
182	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
183	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
184	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
185	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
186	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
187	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
188	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
189	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
190	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
191	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
192	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
193	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
194	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
195	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
196	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
197	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65

(January 2015)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
198	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
199	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
200	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
201	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
202	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
203	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
204	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
205	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
206	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
207	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
208	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
209	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
210	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
211	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
212	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
213	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		83,322.14 -	211725.89			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
214	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10
215	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75
216	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
217	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
218	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	06/2015	85.58
219	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25

(January 2015)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
220	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
221	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
222	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,866.62 -	4961.13			
	<u>SHIPPING AND PORTS</u>						
223	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	2,098.56	12/2010 -	01/2016	70.89
224	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
225	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	3,071.78			
	<u>STEEL</u>						
226	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	04/2015	41.41
227	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		9,035.00 -	12,779.40			
	<u>URBAN DEVELOPMENT</u>						
228	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
229	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	11,782.08			
	Grand Total		261,456.37	476,549.11			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	04/2015	70.54	76
	Total		16,663.00 -	28,139.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2015	15.77	33
	Total		335.61 -	388.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	01/2015	66.86	67
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	03/2015	34.63	36
	Total		7,617.44 -	11,926.14				
	<u>PETROLEUM</u>							
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24
9	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
10	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) [N16000146]	02/2012	666.00 -	701.00	11/2015 -	11/2016	5.26	12
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	02/2015	54.46	40
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72	8

(January 2015)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
16	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2015	73.40	57
17	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51	14
18	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	4,550.40 -	6,638.94	03/2013 -	01/2015	45.90	22
19	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	03/2015	16.05	28
	Total		47,822.86 -	64389.97				
	<u>POWER</u>							
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	06/2015	16.63	10
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,259.80	07/2006 02/2015	10/2016	241.67	123
22	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	842.77	07/2013 -	08/2015	100.18	25
23	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	12/2015	51.10	63
24	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	03/2016	96.59	31
25	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	08/2014 -	03/2015	13.70	7
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76	82
27	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	09/2011	1,366.34 -	1,606.38	12/2013 -	04/2015	17.57	16
28	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	12/2015	21.34	87
30	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	06/2015	13.18	27
31	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31	52
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
33	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	06/2015	20.87	15

(January 2015)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	05/2018	29.14	62
35	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95	10
36	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90	114
37	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
38	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65	99
	Total		42,145.54 -	64406.07				
	<u>RAILWAYS</u>							
39	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
40	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
41	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97	73
42	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20	36
43	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
44	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
45	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
46	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
47	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
48	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
49	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76	96
50	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45	36
51	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
52	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
53	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
54	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98

(January 2015)

Date of Commissioning (Month/Year)								
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
56	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
57	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
58	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
59	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
60	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
61	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
63	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
65	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70	60
	Total		22,454.90 -	78,760.89				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
66	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10	78
67	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68	79
68	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	06/2015	85.58	71
69	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75	74
70	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
71	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
72	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29	84
73	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
74	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40

(January 2015)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		2,866.62	4961.13				
			-					
	<u>SHIPPING AND PORTS</u>							
75	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00	2,098.56	12/2010	01/2016	70.89	61
	Total		1,228.00	2,098.56				
			-					
	<u>STEEL</u>							
76	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00	12,291.00	10/2009	04/2015	41.41	66
	Total		8,692.00	12,291.00				
			-					
	Grand Total		149,825.97	267361.29				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(January 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	02/2015	15.77
	Total		335.61 -	388.53			
	<u>COAL</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,388.61	06/2009 -	01/2015	66.86
3	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
5	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		3,141.15 -	4,783.70			
	<u>PETROCHEMICALS</u>						
6	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	8,920.00			
	<u>PETROLEUM</u>						
7	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	08/2010	8,140.00 -	8,752.00	02/2014 -	12/2014	7.52
8	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
9	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
11	KOTA JOBNER PIPELINE PROJECT - [N16000170]	04/2011	276.26 -	276.27	12/2015 -	03/2015	0.00
12	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
	Total		25,195.31 -	28,880.47			

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
13	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	03/2019	36.90
14	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
15	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
16	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	07/2016	81.76
17	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
18	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
19	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	03/2016	96.59
20	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	842.77	07/2013 -	08/2015	100.18
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,259.80	07/2006 02/2015	10/2016	241.67
22	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) [N18000156]	07/2012	296.87 -	1,128.38	- -	03/2015	280.09
23	RAMMAM-III HEPP (3X40 MW) - [N18000178]	09/2014	1,381.84 -	1,384.84	09/2019 -	09/2019	0.22
	Total		22,939.25 -	42,236.07			
	<u>RAILWAYS</u>						
24	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
25	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
26	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
27	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
28	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
29	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
30	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
31	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
32	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	- -	-	447.91

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
33	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
34	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
35	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
36	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
37	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
38	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
39	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
40	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
41	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
42	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
43	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
44	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
45	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
46	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
47	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
48	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
49	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
50	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
51	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
52	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
53	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
54	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
55	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
56	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
57	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
58	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
59	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
60	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
61	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
62	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
63	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
64	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
65	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
66	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
67	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
68	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
69	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
70	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
71	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
72	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
73	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
74	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
75	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
76	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	810.80	- -	-	0.00
77	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
78	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
79	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
80	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	280.00	02/2006 -	-	6.99
81	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
82	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	- -	03/2012	241.60
83	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
84	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
85	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
86	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
87	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
88	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
89	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
90	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
91	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91
92	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
93	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
94	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
95	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
96	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
97	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
98	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
99	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
100	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45
101	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
102	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
103	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
104	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
105	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
106	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
107	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
108	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
109	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
110	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
111	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
112	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
113	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
114	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
115	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
116	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
117	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
118	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
119	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
120	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
121	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
122	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
123	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
124	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
125	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
126	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
127	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
128	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
129	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
130	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
131	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
132	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
133	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	888.65	- -	03/2018	252.64
134	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
135	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
136	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
137	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
138	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
139	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
140	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
141	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
142	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
143	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
144	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
145	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
146	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
147	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
148	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
149	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
150	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
151	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
152	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
153	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
154	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
155	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
156	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
157	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
158	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
159	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
160	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
161	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
162	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
163	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
164	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
165	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
166	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
167	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
168	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
169	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
170	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
171	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
172	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
173	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
174	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
175	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
176	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
177	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		80,336.76 -	202467.98			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
178	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2015	30.10
179	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	06/2015	92.75
180	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2015	80.68
181	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
182	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	06/2015	85.58
183	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
184	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
185	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,649.01 -	4651.57			
	<u>SHIPPING AND PORTS</u>						
186	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]	11/2007	1,228.00 -	2,098.56	12/2010 -	01/2016	70.89
187	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
188	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	3,071.78			

(January 2015)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>STEEL</u>						
189	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
190	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		148,419.37	307,497.50			

Details of Delayed Projects w.r.t. Original and Revised Schedule

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	ATOMIC ENERGY									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,132.00	12/2008 10/2013	04/2015	76	70.54	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,836.78	09/2010 09/2016	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	5,998.00	12/2015 -	10/2017	22	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,783.00	12/2016 -	05/2018	17	0	
	Total		40,442.00 -	51,918.00	32,749.78					
	CIVIL AVIATION									
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	388.53	292.44	05/2012 -	02/2015	33	15.77	
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28 -	344.28	43.38	03/2014 -	03/2015	12	0	
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	0	
8	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	323.48	01/2011 -	06/2016	65	0	
	Total		1,206.95 -	1,259.87	659.34					
	COAL									
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,111.82	06/2009 03/2013	01/2015	67	66.86	
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 -	741.62	439.43	03/2013 -	03/2015	24	-6.11	
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,866.43	03/2012 05/2014	03/2015	36	34.63	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
12	PURNADIIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	151.27	03/2013 -	03/2015	24	0	
13	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	122.11	10/2014 -	03/2015	5	0	
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30	478.5	
15	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,620.21	03/2014 -	03/2016	24	0	
16	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,595.91	03/2014 -	03/2016	24	0	
17	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44	50.37	
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	8.02	03/2012 -	03/2016	48	0	
19	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	-	03/2014 -	03/2016	24	0	
20	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	46.04	03/2014 -	03/2016	24	0	
21	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0	
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	232.39	03/2012 -	03/2016	48	0	
23	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.80	03/2012 -	03/2016	48	0	
24	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	0	
25	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60	0	
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.09	03/2012 -	03/2016	48	0	
27	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	0	
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.61	03/2010 -	03/2017	84	0	
29	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	109.79	03/2011 -	03/2017	72	-27.57	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72	0	
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	159.57	03/2013 -	03/2017	48	0	
32	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84	0	
33	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	104.48	12/2012 -	03/2017	51	0	
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	171.66	03/2012 -	03/2017	60	0	
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	118.51	03/2013 -	03/2017	48	0	
36	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0	
37	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	61.79	03/2012 -	03/2017	60	0	
38	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	57.52	03/2014 -	03/2017	36	0	
39	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	2.29	07/2016 -	03/2017	8	0	
40	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	0	
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0	
42	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	472.62	12/2015 -	04/2018	28	0	
43	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
44	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
	Total		27,555.48 -	31,685.88	16,665.60					
	STEEL									
45	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	607.17 -	607.17	383.84	12/2011 01/2015	03/2015	39	0	
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,489.55	12/2012 -	03/2015	27	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
47	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,159.76	10/2009 10/2012	04/2015	66	41.41	
48	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,007.37	12/2011 -	05/2015	41	0	
49	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	483.99	09/2013 -	05/2015	20	0	
50	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	353.72	09/2009 05/2012	06/2015	69	-6.25	
51	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	438.26	04/2013 09/2014	06/2015	26	0	
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	119.25	11/2013 -	06/2015	19	0	
53	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	165.14	08/2014 -	06/2015	10	0	
54	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	111.04	09/2014 -	06/2015	9	0	
55	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	356.17	05/2013 01/2015	08/2015	27	0	
56	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	144.40	10/2013 -	08/2015	22	0	
57	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	134.21	12/2014 -	08/2015	8	0	
58	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,996.99	03/2013 -	09/2015	30	0	
59	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	75.67	07/2015 -	03/2016	8	0	
60	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGAR H	01/2010	15,525.00 -	15,525.00	6,012.46	05/2015 12/2016	12/2016	19	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
61	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	110.00	07/2015 -	03/2017	20	0	
	Total		56,370.71 -	59,939.71	41,541.82					
	PETROLEUM									
62	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	01/2015	22	45.9	
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	1,011.80	10/2011 -	02/2015	40	54.46	
64	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,011.15	11/2012 11/2013	03/2015	28	16.05	
65	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	214.78	08/2012 -	03/2015	31	-11.94	
66	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	03/2015	33	-38.7	
67	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	715.05	05/2013 06/2014	03/2015	22	-11.62	
68	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,038.06	12/2014 -	03/2015	3	0	
69	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	162.26	07/2013 -	03/2015	20	0	
70	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	107.05	09/2012 -	04/2015	31	-24.14	
71	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	101.82	03/2014 -	04/2015	13	0	
72	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	352.49	101.09	03/2014 -	04/2015	13	0	
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,886.37	08/2010 03/2012	05/2015	57	73.4	
74	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-18.75	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
75	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5	0	
76	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.40	05/2014 -	05/2015	12	-44.37	
77	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015	110	820.2	
78	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,334.01	12/2012 -	06/2015	30	0	
79	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	122.07	12/2014 06/2015	06/2015	6	0	
80	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	429.00	275.67	06/2011 03/2012	07/2015	49	-7.41	
81	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	906.97	10/2011 -	10/2015	48	67.62	
82	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,352.08	01/2012 -	10/2015	45	70.49	
83	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2015	12	0	
84	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	
85	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	104.64	03/2015 11/2015	11/2015	8	37.72	
86	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	471.19	09/2011 -	12/2015	51	0	
87	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,145.99	08/2015 -	12/2015	4	0	
88	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.67	01/2014 -	12/2015	23	0	
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	245.20	08/2015 -	12/2015	4	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
90	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	64.31	05/2015 -	12/2015	7	0	
91	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,718.31	03/2013 03/2015	03/2016	36	-3.5	
92	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,058.49	09/2012 -	03/2016	42	0	
93	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	534.53	05/2014 -	03/2016	22	0	
94	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.16	03/2015 -	05/2016	14	29.42	
95	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0	
96	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	199.87	10/2014 10/2015	10/2016	24	49.38	
97	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 701.00	701.00	378.54	11/2015 -	11/2016	12	5.26	
98	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.27	02/2016 04/2017	04/2017	14	31.51	
99	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46	-6.92	
100	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0	
101	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	0	
102	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 -	04/2018	23	0	
103	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48	0	
104	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	16.27	01/2013 -	02/2019	73	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		92,391.59	106,938.21	60,178.74					
	POWER									
105	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04	7,341.04	8,306.00	10/2013	03/2015	17	0	
106	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87	1,961.87	1,604.75	05/2014	03/2015	10	0	
107	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85	1,310.85	980.43	02/2015	03/2015	1	0	
108	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16	1,927.16	1,402.67	10/2014	03/2015	5	0	
109	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78	213.78	187.34	03/2014	03/2015	12	0	
110	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	801.40	08/2014	03/2015	7	13.7	
111	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35	1,935.35	1,147.58	12/2014	03/2015	3	0	
112	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80	182.80	94.03	10/2014	03/2015	5	0	
113	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,253.06	12/2013 04/2015	04/2015	16	17.57	
114	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51	2,127.51	2,072.43	07/2014	05/2015	10	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
115	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	802.93	08/2014 -	05/2015	9	0	
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	161.12	04/2015 -	05/2015	1	0	
117	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,407.00	04/2009 -	06/2015	74	59.48	
118	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	953.21	12/2007 12/2009	06/2015	90	0	
119	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,521.57	11/2012 -	06/2015	31	0	
120	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,037.69	08/2012 -	06/2015	34	0	
121	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,709.43	03/2013 -	06/2015	27	13.18	
122	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,600.10	12/2013 -	06/2015	18	0	
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	458.32	07/2013 -	06/2015	23	0	
124	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,655.67	03/2014 -	06/2015	15	20.87	
125	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	91.30	01/2013 -	06/2015	29	0	
126	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,394.76	11/2013 -	06/2015	19	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
127	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,583.46	09/2014 -	06/2015	9	0	
128	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	358.71	11/2013 -	06/2015	19	0	
129	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	321.72	06/2014 -	06/2015	12	0	
130	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,390.96	08/2014 -	06/2015	10	0	
131	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	461.60	02/2014 -	06/2015	16	0	
132	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	252.57	08/2014 -	06/2015	10	16.63	
133	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	466.32	11/2014 -	06/2015	7	0	
134	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,960.41	10/2014 -	06/2015	8	0	
135	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	878.18	11/2014 -	06/2015	7	0	
136	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	842.77	869.41	07/2013 02/2011	08/2015	25	100.18	
137	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 08/2010	12/2015	87	21.34	
138	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	512.79	09/2010 -	12/2015	63	51.1	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
139	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,102.25	01/2015 -	12/2015	11	0	
140	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL, MULTI STATE	02/2010	2,144.00 -	2,144.00	1,964.50	12/2012 -	12/2015	36	0	
141	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	710.74	11/2012 -	12/2015	37	0	
142	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	921.72	01/2015 -	12/2015	11	0	
143	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	3,403.49	06/2015 -	12/2015	6	0	
144	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL, MULTI STATE	06/2012	1,909.24 -	1,909.24	719.23	06/2015 -	12/2015	6	0	
145	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	956.75	08/2013 03/2016	03/2016	31	96.59	
146	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	509.66	425.16	11/2011 -	03/2016	52	0	
147	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	307.17	02/2012 -	03/2016	49	0	
148	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12 -	4,824.12	4,013.88	10/2012 -	03/2016	41	0	
149	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 -	11,130.19	9,902.60	08/2013 -	03/2016	31	0	
150	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,104.52	04/2013 -	03/2016	35	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
151	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	933.03	11/2012 -	03/2016	40	0	
152	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	0	
153	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	57.64	09/2014 -	06/2016	21	0	
154	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,633.27	09/2009 -	07/2016	82	81.76	
155	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 -	1,259.80	733.11	07/2006 12/2015	10/2016	123	241.67	
156	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,841.20	01/2016 -	11/2016	10	50.95	
157	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,569.00	09/2016 -	02/2017	5	0	
158	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,561.01	12/2009 03/2017	03/2017	87	86.39	
159	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	4,982.00	09/2011 -	03/2017	66	54.25	
160	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	6,644.00	01/2017 -	03/2017	2	0	
161	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	328.00	12/2016 -	05/2017	5	0	
162	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,944.00	11/2016 -	08/2017	9	0	
163	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,586.00	12/2009 10/2014	03/2018	99	73.65	
164	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,079.08	07/2010 02/2016	05/2018	94	79.77	
165	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,348.00	03/2013 -	05/2018	62	29.14	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	571.03	07/2014 11/2018	11/2018	52	50.31	
167	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,828.46	09/2009 -	03/2019	114	36.9	
	Total		165,762.16 -	190,715.54	125,751.31					
	RAILWAYS									
168	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	19	-.01	
169	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73	466.97	
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96	160.76	
171	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	59.2	
172	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	0	
173	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	
174	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	367.76	
175	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	16.41	
176	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	408.79	03/2004 12/2010	03/2016	144	259.68	
177	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	657.06	03/2013 -	03/2016	36	81.45	
178	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
179	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	
180	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	
181	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	
182	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	134.30	03/2016 -	06/2016	3	0	
183	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
184	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	
185	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	55.61	04/2016 -	03/2017	11	0	
186	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	
187	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	
188	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	
189	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	
190	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
191	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	
192	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
193	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	1,815.37	03/2014 03/2019	03/2019	60	28.7	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
194	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	
195	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	
196	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	
197	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	
198	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	
	Total		25,945.26 -	82,251.23	36,462.77					
	ROAD TRANSPORT AND HIGHWAYS									
199	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	01/2015	75	0	
200	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	01/2015	81	0	
201	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	01/2015	59	0	
202	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	02/2015	89	-1.84	
203	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	02/2015	80	0	
204	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	02/2015	80	0	
205	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	02/2015	20	0	
206	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18	0	
207	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	02/2015	13	0	
208	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	02/2015	31	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
209	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78	30.1	
210	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	03/2015	78	0	
211	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015	84	0	
212	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90	82.12	
213	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5	
214	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27	0	
215	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26	0	
216	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	0	
217	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	0	
218	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	03/2015	15	0	
219	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	0	
220	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	0	
221	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	0	
222	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10	0	
223	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25	0	
224	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	03/2015	19	0	
225	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2015	9	0	
226	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
227	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5	0	
228	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8	0	
229	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	250.50	363.40	10/2014 -	03/2015	5	0	
230	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	03/2015	8	0	
231	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6	0	
232	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	03/2015	5	0	
233	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	03/2015	6	0	
234	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 04/2015	04/2015	84	0	
235	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82	0	
236	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	04/2015	20	0	
237	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79	-8.95	
238	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	05/2015	24	0	
239	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	0	
240	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	0	
241	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
242	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13	0	
243	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74	92.75	
244	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	06/2015	79	0	
245	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	80.68	
246	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74	0	
247	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	06/2015	86	0	
248	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 06/2015	06/2015	85	0	
249	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	06/2015	71	85.58	
250	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	33.7	
251	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61	0	
252	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	06/2015	33	0	
253	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0	
254	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	06/2015	26	0	
255	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19	0	
256	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	0	
257	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22	0	
258	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0	
259	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
260	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	08/2015	24	0	
261	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87	0	
262	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40	0	
263	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26	0	
264	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	0	
265	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0	
266	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13	0	
267	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	0	
268	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
269	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	0	
270	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	0	
271	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2015	82	0	
272	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0	
273	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	12/2015	63	0	
274	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	0	
275	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	0	
276	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	0	
277	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
278	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21	0	
279	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	0	
280	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0	
281	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0	
282	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27	0	
283	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	0	
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	0	
285	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17	0	
286	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	0	
287	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0	
288	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	42.25	
289	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0	
290	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	0	
291	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	0	
292	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0	
293	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	0	
294	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
295	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	0	
296	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	0	
297	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0	
298	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
299	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2016	22	0	
300	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	2.29	
	Total		71,897.83 -	73,964.83	73,834.21					
	SHIPPING AND PORTS									
301	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	937.28	12/2010 09/2012	01/2016	61	70.89	
	Total		1,228.00 -	2,098.56	937.28					
	TELECOMMUNICATIONS									
302	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74	0	
303	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	50.93	10/2010 11/2015	09/2015	59	0	
	Total		720.81 -	720.81	246.87					
	URBAN DEVELOPMENT									
304	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
305	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0	
306	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	0	
307	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	
308	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	0	
309	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	0	
310	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	0	
311	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
312	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	0	
313	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	
314	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
315	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8	0	

(January 2015) All Cost/ Expenditure in Rs. crore										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
316	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	0	
317	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	0	
	Total		43,553.53 -	43,553.53	1,081.72					
	Grand Total		527,074.32	645,046.17	390,109.44					

List of projects original without Date of Commissioning

(January 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	15.42	-	09/2018	-	0/0
	Total		314.61	314.61	15.42				0/0
	<u>POWER</u>								
2	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87	1,128.38	298.09	-	03/2015	-	1/17
	Total		296.87	1,128.38	298.09				1/17
	<u>RAILWAYS</u>								
3	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16	260.16	240.21	-	01/2015	-	0/0
4	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97	1,651.54	1,621.40	-	03/2015	-	0/0
5	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24	645.00	309.19	-	03/2015	-	0/0
6	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42	844.00	798.87	-	03/2015	70(R1)	0/0
7	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70	3,700.00	3,198.30	-	03/2015	-	0/0
8	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17	914.98	846.18	-	03/2015	-	0/0
9	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00	951.24	619.87	-	03/2015	-	0/0
10	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74	203.00	227.84	-	03/2015	-	0/0
11	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23	1,072.51	888.87	-	06/2015	-	0/0
12	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71	744.71	576.86	-	03/2016	-	0/1
13	RAMGANJMONDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92	1,225.90	257.59	-	03/2017	-	0/0
14	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0

(January 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
16	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
17	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	-	0/0
18	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	48(R3)	0/0
19	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 252.00	888.65	-	- -	03/2018	-	0/0
20	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
21	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
22	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
23	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
24	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR, MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
25	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
26	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
27	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
28	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
29	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
30	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	- -	03/2019	-	0/0
31	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
32	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
33	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
Total			16,338.85	32,415.45	12,082.05				0/1

(January 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
34	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00	480.00	665.80	-	03/2015	-	2/2
35	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00	671.00	1,273.00	-	06/2015	-	2/3
	Total		1,151.00	1,151.00	1,938.80				4/5
	Grand Total		18,101.33	35,009.44	14,334.36				5/23

Details of Projects Without Milestones w.r.t. Original Schedule

			(January 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	02/2015	0/0
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	02/2015	0/0
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	03/2015	0/0
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	06/2016	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	-	09/2018	0/0
7	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-	0/0
	Total		2,599.56 -			0/0
	<u>COAL</u>					
8	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
9	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	04/2017	0/0
10	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018	0/0
11	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49 -	03/2020 -	03/2020	0/0
12	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16 -	03/2020 -	03/2020	0/0
13	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	03/2021 -	03/2021	0/0
14	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA	09/2014	266.23 -	03/2021 -	03/2021	0/0
15	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-	0/0
	Total		4,423.57 -			0/0
	<u>FERTILISERS</u>					
16	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0

			(January 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>MINES</u>					
17	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JHCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	09/2017	0/0
	Total		1,856.00 -			0/0
	<u>STEEL</u>					
18	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	07/2015 -	03/2016	0/0
19	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	09/2016 -	09/2016	0/0
20	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	10/2016	0/0
	Total		1,500.73 -			0/0
	<u>PETROLEUM</u>					
21	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	12/2014	0/0
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	02/2015	0/0
23	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	07/2013 -	03/2015	0/0
24	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	09/2012 -	04/2015	0/0
25	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
26	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	04/2015 -	04/2015	0/0
27	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
28	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49 -	03/2014 -	04/2015	0/0
29	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	04/2006 04/2016	06/2015	0/0
30	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	08/2015	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	10/2015	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	10/2015	0/0
33	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	10/2014 -	10/2015	0/0
34	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 11/2015	11/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	12/2015	0/0
36	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	01/2016 -	01/2016	0/0
37	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 -	02/2016	0/0
38	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	02/2016	0/0
39	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0
40	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	03/2013 -	06/2016	0/0
41	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	07/2016 -	07/2016	0/0
42	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	10/2014 10/2015	10/2016	0/0
43	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
44	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	01/2017 -	01/2017	0/0
45	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
46	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 4,619.94	02/2016 04/2017	04/2017	0/0
47	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 -	05/2017 -	05/2017	0/0
48	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	09/2017 -	09/2017	0/0
49	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
50	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	12/2014 -	12/2017	0/0
51	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	04/2015 -	12/2017	0/0
52	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	05/2016 -	04/2018	0/0
53	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	12/2014 -	12/2018	0/0
54	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	12/2018 -	12/2018	0/0
55	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	01/2013 -	02/2019	0/0
56	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
57	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
	Total		70,701.91 -			0/0

			(January 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	POWER					
58	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	06/2015 -	12/2015	0/0
59	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
60	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	03/2016 -	05/2016	0/0
61	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0
62	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0
63	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	08/2016 -	08/2016	0/0
64	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
65	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	02/2017 -	02/2017	0/0
66	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	02/2017 -	02/2017	0/0
67	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	04/2017 -	04/2017	0/0
68	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	07/2017	0/0
69	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	10/2017 -	10/2017	0/0
70	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	11/2017 -	11/2017	0/0
71	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	03/2018	0/0
72	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	03/2018 -	03/2018	0/0
73	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	04/2018 -	04/2018	0/0
74	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	05/2018 -	05/2018	0/0
75	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
76	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		37,215.44 -			0/0
	RAILWAYS					
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
78	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
79	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
80	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
81	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
82	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
83	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
84	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
85	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
86	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2014	0/0
87	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
88	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
89	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
90	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	10/2014	0/0
91	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
92	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
93	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014	0/0
94	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	12/2014	0/0
95	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
96	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
97	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
98	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015	0/0
99	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
100	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
101	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0
102	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	- -	03/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
103	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2015	0/0
104	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2015	0/0
105	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
106	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
107	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
108	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
109	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015	0/0
110	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23 -	- -	06/2015	0/0
111	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
112	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
113	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
114	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
115	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	03/2004 12/2010	03/2016	0/0
116	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2016	0/0
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
118	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
119	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
120	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
121	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
122	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
123	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	03/2007 -	03/2016	0/0
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	03/2016 -	03/2016	0/0
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
126	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
127	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
128	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
129	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
130	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
131	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0
132	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
133	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
134	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
135	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
136	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	04/2008 03/2014	06/2017	0/0
137	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
138	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
140	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
141	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
143	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	- -	03/2018	0/0
144	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
145	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
146	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0
147	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
148	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
149	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
150	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0

			(January 2015)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
151	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	11/2002 -	12/2018	0/0
152	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANTPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
153	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
154	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
155	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
156	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	03/2014 03/2019	03/2019	0/0
157	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
158	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
159	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
160	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	03/1998 -	12/2019	0/0
161	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
162	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
163	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
164	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
165	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
166	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
167	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
168	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
169	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
170	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
171	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
172	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
173	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
174	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
175	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
176	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00	07/2012 -	-	0/0
177	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
178	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
179	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
180	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-	0/0
181	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
182	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
183	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
184	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
185	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-	0/0
186	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
187	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
188	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0
189	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
190	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
191	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-	0/0
192	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-	0/0
193	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
194	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
195	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
196	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
197	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
198	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
199	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-	0/0
200	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
201	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-	0/0
202	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
203	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
204	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-	0/0
205	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-	0/0
206	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
207	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
208	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
209	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-	0/0
210	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
211	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
212	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
213	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-	0/0
214	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
215	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
216	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
217	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
218	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
219	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
220	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
221	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
222	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
223	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
224	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
225	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
226	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
227	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
228	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
229	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
230	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
231	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
232	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
233	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
234	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
235	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
236	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
237	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-	0/0
238	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
239	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
240	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
241	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
242	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
243	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0
244	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
245	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
246	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
247	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
248	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
249	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
250	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
251	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
252	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
253	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
254	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
255	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
256	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
257	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
258	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
259	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
260	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0
261	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-	0/0
262	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-	0/0
263	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-	0/0
264	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-	0/0
265	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-	0/0
266	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-	0/0
267	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-	0/0
268	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-	0/0
269	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-	0/0
270	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
271	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
272	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
273	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
274	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
275	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
276	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
277	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
278	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
279	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
280	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
281	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
282	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
283	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
284	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
285	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
286	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
287	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
288	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
289	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
290	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
291	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
292	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
293	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
294	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
295	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
296	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
297	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
298	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
299	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
300	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
301	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
302	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
303	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
304	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
305	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
306	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
307	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
308	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
309	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0
310	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
311	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
312	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
313	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
314	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
315	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
316	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
317	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
318	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
319	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
320	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
321	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
322	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
323	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
324	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
325	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
326	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
327	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
328	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
329	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
330	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
331	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
332	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
333	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
334	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
335	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
336	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
337	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
338	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
339	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
340	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
341	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
342	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
343	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
344	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
345	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
346	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
347	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
348	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
349	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
350	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
351	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
352	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
353	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
354	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
355	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
356	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
357	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-	0/0
358	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
359	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-	0/0
360	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
361	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-	0/0
362	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
363	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
364	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-	0/0
	Total		163,062.32 -			0/0
	ROAD TRANSPORT AND HIGHWAYS					

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
365	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0
366	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
367	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
368	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
369	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
370	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
371	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
372	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
373	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
374	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
375	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2014	0/0
376	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015	0/0
377	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2015	0/0
378	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	01/2015	0/0
379	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	02/2015	0/0
380	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	02/2015	0/0
381	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	02/2015	0/0
382	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	02/2015	0/0
383	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0
384	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	02/2015	0/0
385	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	02/2015	0/0
386	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	03/2015	0/0
387	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	03/2015	0/0
388	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 03/2015	03/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
389	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	09/2007 -	03/2015	0/0
390	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	03/2015	0/0
391	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	03/2015	0/0
392	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	03/2015	0/0
393	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2015	0/0
394	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	12/2013 -	03/2015	0/0
395	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	03/2015	0/0
396	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	03/2015	0/0
397	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2015	0/0
398	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
399	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	05/2014 -	03/2015	0/0
400	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	03/2015	0/0
401	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	03/2015	0/0
402	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2015	0/0
403	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	03/2015	0/0
404	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2015	0/0
405	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	03/2015	0/0
406	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	10/2014 -	03/2015	0/0
407	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	07/2014 -	03/2015	0/0
408	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	03/2015	0/0
409	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	03/2015	0/0
410	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	04/2008 04/2015	04/2015	0/0
411	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	06/2008 04/2015	04/2015	0/0
412	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	04/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
413	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
414	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	05/2015	0/0
415	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	05/2015	0/0
416	TWO LANNING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2015	0/0
417	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2015	0/0
418	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	05/2015	0/0
419	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	05/2015	0/0
420	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	06/2015	0/0
421	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	06/2015	0/0
422	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	06/2015	0/0
423	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	06/2015	0/0
424	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 04/2015	06/2015	0/0
425	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 06/2015	06/2015	0/0
426	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	06/2015	0/0
427	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	06/2015	0/0
428	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	06/2015	0/0
429	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2015	0/0
430	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	06/2015	0/0
431	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	06/2015	0/0
432	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2015	0/0
433	4-LANNING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	06/2015	0/0
434	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
435	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
436	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	08/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
437	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	08/2015	0/0
438	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
439	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	09/2015	0/0
440	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	09/2015	0/0
441	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	09/2015	0/0
442	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	09/2015	0/0
443	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
444	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	10/2015	0/0
445	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
446	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
447	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	11/2015	0/0
448	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	11/2015	0/0
449	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
450	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
451	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2015	0/0
452	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	12/2015	0/0
453	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2015	0/0
454	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	12/2015	0/0
455	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2015	0/0
456	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2015	0/0
457	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	12/2015	0/0
458	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2015	0/0
459	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2015	0/0
460	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
461	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2015	0/0
462	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	12/2015	0/0
463	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2015	0/0
464	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
465	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
466	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	12/2015	0/0
467	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2015	0/0
468	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2015	0/0
469	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
470	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2016	0/0
471	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	03/2016	0/0
472	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	04/2016	0/0
473	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
474	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
475	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
476	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	08/2016	0/0
477	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
478	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
479	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2016	0/0
480	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
481	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
482	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2016	0/0
483	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	02/2017	0/0
484	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
485	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
486	NALBARI TO BIJUNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
487	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N240000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
488	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N240000235]NHAI, TELANGANA	04/2014	1,123.17 -	- -	-	0/0
	Total		90,436.35 -			0/0
	SHIPPING AND PORTS					
489	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	01/2016	0/0
490	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
491	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	03/2012 -	-	0/0
492	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-	0/0
493	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST, GUJARAT	02/2011	830.00 -	05/2013 -	-	0/0
494	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
	Total		5,158.07 -			0/0
	TELECOMMUNICATIONS					
495	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL, ASSAM	06/2007	336.81 -	01/2009 -	03/2015	0/0
496	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 -	07/2015	0/0
497	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	10/2010 11/2015	09/2015	0/0
	Total		14,054.81 -			0/0
	URBAN DEVELOPMENT					
498	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD, DELHI	01/2010	162.90 -	07/2012 -	07/2012	0/0
499	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD, BIHAR	02/2012	171.10 -	09/2014 -	09/2014	0/0
500	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD, BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014	0/0
501	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD, MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014	0/0
502	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 -	03/2012 -	01/2015	0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
503	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
504	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	06/2012 -	05/2015	0/0
505	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	08/2015	0/0
506	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	08/2015	0/0
507	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	10/2015	0/0
508	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	05/2013 -	10/2015	0/0
509	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
510	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	01/2016	0/0
511	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
512	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	12/2014 -	04/2016	0/0
513	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	05/2016	0/0
514	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 -	09/2016	0/0
515	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	12/2014 -	12/2016	0/0
516	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	09/2015 -	12/2016	0/0
517	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	03/2017	0/0
518	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	07/2017 -	07/2017	0/0
519	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	07/2017	0/0
520	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
521	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
522	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-	0/0
523	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-	0/0
524	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
525	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		113,536.00 -			0/0

			(January 2015)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Grand Total		504,742.55			0/0

List of Projects on schedule w.r.t. Latest Schedule

(January 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	ATOMIC ENERGY						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	9/2003	3,492.00 -	5,677.00	4,836.78	09/2010 09/2016	09/2016
	Total		3,492.00 -	5,677.00	4,836.78		
	COAL						
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	6/2008	7,612.33 -	1,188.31	756.49	03/2023 03/2023	03/2023
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	325.23	03/2015 -	03/2015
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	185.26	03/2017 -	03/2017
5	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
6	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	71.67	03/2015 -	03/2015
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
9	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	68.67	03/2016 -	03/2016
10	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026
11	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	-	03/2019 -	03/2019
12	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
13	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	109.65	03/2018 -	03/2018
14	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
15	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
16	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
17	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	98.45	03/2020 -	03/2020
18	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	430.14	68.25	03/2016 -	03/2016
19	GOKUL - [N06000120]	11/2014	267.67 -	267.67	7.33	03/2018 -	03/2018

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	7.14	03/2021 -	03/2021
21	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	-	03/2020 -	03/2020
22	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021
23	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
24	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
25	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
26	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) [N06000091]	6/2011	1,131.28 -	1,131.28	46.30	03/2018 -	03/2018
27	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.90	03/2016 -	03/2016
28	PENGANGA OC - [N06000066]	10/2008	441.82 -	441.82	42.32	03/2020 -	03/2020
29	PELMA OCP(10.00MTY) - [N06000045]	7/2008	1,624.59 -	1,624.59	-	03/2023 03/2023	03/2023
30	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	750.68	03/2016 -	03/2016
	Total		28,169.97 -	21,374.00	2,897.42		
	DUMMY SECTOR						
31	TEST DUMMY - [N35000004]	1/2014	200.00 -	200.00	15.00	03/2018 -	03/2018
	Total		200.00 -	200.00	15.00		
	FERTILISERS						
32	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	0.79	11/2016 -	11/2016
	Total		197.79 -	197.79	.79		
	MINES						
33	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	PETROLEUM						
34	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,334.97	05/2015 -	05/2015

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	260.98	04/2015 -	04/2015
36	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	104.64	03/2015 11/2015	11/2015
37	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	-	12/2016 -	12/2016
38	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	1.94	02/2016 02/2016	02/2016
39	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	7.89	01/2017 -	01/2017
40	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,706.47	110.18	05/2017 -	05/2017
41	RESID UPGRADATION PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	383.78	11/2015 -	11/2015
42	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
43	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	7.60	07/2016 -	07/2016
44	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
45	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	11.10	02/2016 -	02/2016
46	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	80.42	09/2017 -	09/2017
47	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
48	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 -	04/2016
49	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.76	01/2016 -	01/2016
50	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
51	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
52	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.36	04/2015 -	04/2015
53	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	0.27	02/2016 04/2017	04/2017
54	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	4,831.09	05/2016 -	05/2016
55	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	360.03	08/2015 -	08/2015
56	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	122.07	12/2014 06/2015	06/2015

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	39.33	07/2016 -	07/2016
58	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	879.16	11/2015 -	11/2015
	Total		62,852.21 -	66,337.62	10,772.90		
	POWER						
59	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	3,561.01	12/2009 03/2017	03/2017
60	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	346.65	12/2015 -	12/2015
61	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
62	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
63	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	26.80	08/2016 -	08/2016
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	4.20	06/2016 -	06/2016
66	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	3.07	04/2016 -	04/2016
67	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	186.80	05/2016 -	05/2016
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	118.89	03/2016 -	03/2016
69	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	2,137.00	09/2017 -	09/2017
70	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
71	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
72	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
73	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
74	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	440.60	03/2018 -	03/2018

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
75	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
76	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	22.00	10/2016 -	10/2016
77	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
78	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
79	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	-	05/2018 -	05/2018
80	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
81	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	-	10/2017 -	10/2017
82	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
83	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	-	04/2018 -	04/2018
84	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,384.84	77.00	09/2019 -	09/2019
85	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	1,960.00	02/2019 -	02/2019
86	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,124.00	08/2018 -	08/2018
87	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	529.00	03/2019 -	03/2019
88	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
89	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	0.95	06/2015 -	06/2015
90	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	956.75	08/2013 03/2016	03/2016
91	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,548.00	08/2015 -	08/2015
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	513.59	03/2015 -	03/2015
93	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,135.00	06/2017 -	06/2017
94	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,606.38	1,253.06	12/2013 04/2015	04/2015

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,745.08	571.03	07/2014 11/2018	11/2018
	Total		108,252.80 -	112,460.78	18,515.40		
	RAILWAYS						
96	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
97	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
98	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	234.71	137.01	03/2015 -	03/2015
99	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	4/2010	423.66 -	423.66	250.37	03/2017 -	03/2017
100	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
101	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	29.10	03/2015 -	03/2015
102	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	36.31	03/2016 -	03/2016
103	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR- BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	4.66	02/2019 -	02/2019
104	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,619.02	480.06	03/2016 -	03/2016
105	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	86.31	03/2015 -	03/2015
106	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
107	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.03	02/2020 -	02/2020
108	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135]	3/2013	4,874.58 -	4,874.58	1,741.00	03/2016 -	03/2016
109	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	478.77	03/2016 -	03/2016
110	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	6,821.29	1,815.37	03/2014 03/2019	03/2019
	Total		22,761.25 -	31,742.26	5,495.88		
	ROAD TRANSPORT AND HIGHWAYS						
111	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	182.50	04/2008 04/2015	04/2015

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
112	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
113	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	177.78	09/2016 -	09/2016
114	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
115	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
116	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.40	11/2015 -	11/2015
117	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2015
118	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
119	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	590.90	08/2015 -	08/2015
120	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	345.80	04/2008 01/2015	01/2015
121	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	160.00	197.60	05/2008 06/2015	06/2015
122	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
123	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	06/2015
124	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015
125	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	03/2015
	Total		14,313.78 -	14,405.73	5,661.28		
	STEEL						
126	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	181.17	06/2015 -	06/2015
127	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	21.05	05/2016 -	05/2016
128	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	64.41	04/2016 -	04/2016
129	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	8.28	04/2015 -	04/2015
130	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	6,012.46	05/2015 12/2016	12/2016
131	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	35.15	07/2016 -	07/2016

(January 2015)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
132	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	8.52	10/2016 -	10/2016
133	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	-	09/2016 -	09/2016
	Total		18,579.32 -	18,724.72	6,331.04		
	TELECOMMUNICATIONS						
134	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	360.00	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	360.00		
	URBAN DEVELOPMENT						
135	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
136	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
137	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	0.08	09/2016 -	09/2016
138	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
139	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	2.04	03/2017 -	03/2017
140	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	421.28	11/2019 -	11/2019
141	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	688.45	07/2017 -	07/2017
142	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		84,825.70 -	84,825.70	9,811.34		
	Grand Total		358,834.82	371,135.60	64,697.83		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(January 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	PETROLEUM						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,439.48	04/2006 04/2016	06/2015
	Total		429.82 -	3,955.21	3,439.48		
	CIVIL AVIATION						
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II [N04000070	2/2011	452.00	452.00	377.99	03/2015 -	02/2015
	Total		452.00 -	452.00	377.99		
	POWER						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144	9/2012	1,508.74	1,508.74	473.88	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	473.88		
	PETROLEUM						
4	KOTA JOBNER PIPELINE PROJECT - [N16000170	4/2011	276.26 -	276.27	209.97	12/2015 -	03/2015
5	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	117.87	09/2016 -	12/2015
	Total		418.12 -	508.27	327.84		
	POWER						
6	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154	10/2013	1,315.90	1,315.90	264.87	11/2016 -	03/2016
7	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52	1,364.52	66.14	05/2016 -	04/2016
	Total		2,680.42 -	2,680.42	331.01		
	TELECOMMUNICATIONS						
8	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096	10/2009	384.00 -	384.00	50.93	10/2010 11/2015	09/2015
	Total		384.00 -	384.00	50.93		

(January 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	Grand Total		5,873.10	9,488.64	5,001.13		

List of projects without Date of Commissioning

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		626.00 -		
	<u>COAL</u>				
2	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
4	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	-
	Total		1,056.69 -		
	<u>PETROCHEMICALS</u>				
5	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
6	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	12/2013 03/2014	12/2014
7	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	12/2014
8	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
9	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		9,599.43 -		
	<u>POWER</u>				
10	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
11	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
12	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
	Total		8,251.11 -		
	RAILWAYS				
14	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
15	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
16	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
17	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012
18	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012
19	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
20	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
21	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
23	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2014
24	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
25	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
26	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	10/2014
28	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
29	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014
30	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014
31	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	12/2014
32	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
33	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
34	VIRAMGAM-BHILD(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
35	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
36	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
37	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
38	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
39	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
40	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
41	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
42	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
43	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
44	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
45	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
46	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
47	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
48	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
51	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
52	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
53	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
54	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
55	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
56	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
58	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
59	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
61	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
62	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
63	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
64	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
65	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
66	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
67	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
68	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
69	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
70	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
71	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
72	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
73	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
74	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
75	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
76	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
77	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
78	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-
79	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
80	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
81	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
82	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
83	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
84	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
86	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
87	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
88	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
89	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
90	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
91	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
92	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
93	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
94	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
95	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
96	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
97	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
98	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
99	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
100	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
101	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
102	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
103	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
104	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
105	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
106	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
107	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
108	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
110	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
111	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
112	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
113	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
114	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
115	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
116	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
117	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
118	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
119	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
120	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
121	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
122	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
123	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
124	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
125	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
126	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
127	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
128	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
129	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
130	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
131	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
132	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-
133	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
134	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
135	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
136	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
137	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
138	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
139	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
140	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-
141	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
142	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
143	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
144	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
145	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
146	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
147	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
148	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
149	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
150	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
151	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
152	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
153	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
154	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
155	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
156	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
157	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
158	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
159	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
160	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
161	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
162	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
163	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
164	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
165	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
166	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
167	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
168	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
169	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
170	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
171	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
172	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
173	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
174	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
175	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
176	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
177	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
178	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
179	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
180	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
181	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
182	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
183	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
184	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
185	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
186	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
187	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
188	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
189	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
190	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
191	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
192	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
193	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
194	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
195	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
196	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
197	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
198	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
199	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
200	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
201	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
202	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
203	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
204	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
205	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
206	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
207	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
208	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
209	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
210	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
211	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
212	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
213	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
214	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
215	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
216	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
217	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
218	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
219	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
220	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
221	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
222	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
223	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
224	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
225	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
226	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
227	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
228	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
229	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
	Total		105,516.67 -		

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	ROAD TRANSPORT AND HIGHWAYS				
230	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
231	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
232	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
233	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013
234	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
235	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
236	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
237	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
238	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
239	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
240	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
241	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
242	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
243	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
244	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	12/2014
245	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2014
246	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
247	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
248	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
249	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
250	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
251	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		15,475.56 -		

(January 2015)					
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	SHIPPING AND PORTS				
252	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
253	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
254	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
255	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-
256	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		3,930.07 -		
	URBAN DEVELOPMENT				
257	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	07/2012
258	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	09/2014
259	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
260	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41- 43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
261	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
262	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
263	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
264	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
265	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		10,415.77 -		
	Grand Total		160,331.91		

List of Delayed Projects w.r.t. Latest Schedule

(January 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 22,462.00	22,462.00	18,132.00	12/2008 10/2013	04/2015	76	18
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,998.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,783.00	12/2016 -	05/2018	17	-
	Total		36,950.00 -	46,241.00	27,913.00				
	CIVIL AVIATION								
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	388.53	292.44	05/2012 -	02/2015	33	-
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	43.38	03/2014 -	03/2015	12	-
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	09/2015	6	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	323.48	01/2011 -	06/2016	65	-
	Total		1,206.95 -	1,259.87	659.34				
	COAL								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,388.61	3,111.82	06/2009 03/2013	01/2015	67	22
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	439.43	03/2013 -	03/2015	24	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,866.43	03/2012 05/2014	03/2015	36	10
11	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	151.27	03/2013 -	03/2015	24	-
12	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	122.11	10/2014 -	03/2015	5	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,228.77	03/2013 09/2012	09/2015	30	36
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,620.21	03/2014 -	03/2016	24	-
15	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,595.91	03/2014 -	03/2016	24	-
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	46.55	07/2012 -	03/2016	44	-
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	8.02	03/2012 -	03/2016	48	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	-	03/2014 -	03/2016	24	-
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	46.04	03/2014 -	03/2016	24	-
20	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
21	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	232.39	03/2012 -	03/2016	48	-
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.80	03/2012 -	03/2016	48	-
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	-
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.60	03/2011 -	03/2016	60	-
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	145.09	03/2012 -	03/2016	48	-
26	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2016	9	-
27	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	131.61	03/2010 -	03/2017	84	-
28	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	109.79	03/2011 -	03/2017	72	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.71	03/2011 -	03/2017	72	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	159.57	03/2013 -	03/2017	48	-
31	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	147.63	03/2010 -	03/2017	84	-
32	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.48	12/2012 -	03/2017	51	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	171.66	03/2012 -	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.53	118.51	03/2013 -	03/2017	48	-
35	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	-
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	61.79	03/2012 -	03/2017	60	-
37	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	57.52	03/2014 -	03/2017	36	-
38	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.29	07/2016 -	03/2017	8	-
39	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	0.03	03/2015 -	03/2018	36	-
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	-
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	472.62	12/2015 -	04/2018	28	-
42	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
43	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		27,555.48	31,685.88	16,665.60				
	STEEL								
44	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	607.17	607.17	383.84	12/2011 01/2015	03/2015	39	2
45	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00	2,875.00	2,489.55	12/2012	03/2015	27	-
46	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,159.76	10/2009 10/2012	04/2015	66	30
47	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00	6,325.00	5,007.37	12/2011	05/2015	41	-
48	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00	677.00	483.99	09/2013	05/2015	20	-
49	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00	450.00	353.72	09/2009 05/2012	06/2015	69	37
50	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00	572.00	438.26	04/2013 09/2014	06/2015	26	9
51	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55	254.55	119.25	11/2013	06/2015	19	-
52	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	165.14	08/2014	06/2015	10	-
53	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48	160.48	111.04	09/2014	06/2015	9	-
54	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55	898.55	356.17	05/2013 01/2015	08/2015	27	7
55	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	144.40	10/2013	08/2015	22	-
56	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09	237.09	134.21	12/2014	08/2015	8	-
57	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	13,996.99	03/2013	09/2015	30	-
58	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73	877.73	75.67	07/2015	03/2016	8	-
59	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16	404.16	110.00	07/2015	03/2017	20	-
	Total		40,845.71	44,414.71	35,529.36				
	PETROLEUM								
60	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC, MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	01/2015	22	2
61	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	1,011.80	10/2011	02/2015	40	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	PARADIP REFINERY PROJECT - [N16000058]JOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,011.15	11/2012 11/2013	03/2015	28	16
63	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	214.78	08/2012 -	03/2015	31	-
64	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	03/2015	33	-
65	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	715.05	05/2013 06/2014	03/2015	22	9
66	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,038.06	12/2014 -	03/2015	3	-
67	MARKETING TERMINAL AT PARADEEP - [N16000168]JOCL, ODISHA	07/2009	199.75 -	199.75	162.26	07/2013 -	03/2015	20	-
68	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	107.05	09/2012 -	04/2015	31	-
69	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	101.82	03/2014 -	04/2015	13	-
70	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC, MAHARASHTRA	01/2012	352.49 -	352.49	101.09	03/2014 -	04/2015	13	-
71	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	5,633.44	5,886.37	08/2010 03/2012	05/2015	57	38
72	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-
73	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 -	600.17	249.01	12/2014 -	05/2015	5	-
74	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC, MULTI STATE	04/2012	2,547.26 -	1,417.00	1,401.40	05/2014 -	05/2015	12	-
75	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,915.00	1,334.01	12/2012 -	06/2015	30	-
76	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	429.00	275.67	06/2011 03/2012	07/2015	49	40
77	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	906.97	10/2011 -	10/2015	48	-
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,352.08	01/2012 -	10/2015	45	-
79	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2015	12	-
80	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	471.19	09/2011 -	12/2015	51	-
81	DE-BOTTLENECKING OF SMPL - [N16000089]JOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,145.99	08/2015 -	12/2015	4	-
82	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.67	01/2014 -	12/2015	23	-
83	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]JOCL, MULTI STATE	08/2011	586.00 -	586.00	245.20	08/2015 -	12/2015	4	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
84	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	64.31	05/2015 -	12/2015	7	-
85	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,718.31	03/2013 03/2015	03/2016	36	12
86	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,058.49	09/2012 -	03/2016	42	-
87	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	534.53	05/2014 -	03/2016	22	-
88	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 -	2,665.65	605.16	03/2015 -	05/2016	14	-
89	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
90	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	199.87	10/2014 10/2015	10/2016	24	12
91	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 701.00	701.00	378.54	11/2015 -	11/2016	12	-
92	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	188.89	2.00	01/2014 -	11/2017	46	-
93	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	-
94	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	-
95	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	9.72	05/2016 -	04/2018	23	-
96	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,040.60	12/2014 -	12/2018	48	-
97	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	16.27	01/2013 -	02/2019	73	-
	Total		87,028.35 -	96,668.40	56,512.28				
	POWER								
98	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,306.00	10/2013 -	03/2015	17	-
99	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,604.75	05/2014 -	03/2015	10	-
100	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	980.43	02/2015 -	03/2015	1	-
101	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,402.67	10/2014 -	03/2015	5	-
102	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	187.34	03/2014 -	03/2015	12	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
103	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	801.40	08/2014 -	03/2015	7	-
104	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	08/2012	1,935.35 -	1,935.35	1,147.58	12/2014 -	03/2015	3	-
105	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	94.03	10/2014 -	03/2015	5	-
106	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,072.43	07/2014 -	05/2015	10	-
107	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	802.93	08/2014 -	05/2015	9	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	161.12	04/2015 -	05/2015	1	-
109	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	01/2011	4,527.15 7,220.00	7,220.00	6,407.00	04/2009 -	06/2015	74	-
110	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 -	1,007.16	953.21	12/2007 12/2009	06/2015	90	66
111	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,521.57	11/2012 -	06/2015	31	-
112	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,037.69	08/2012 -	06/2015	34	-
113	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,709.43	03/2013 -	06/2015	27	-
114	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,600.10	12/2013 -	06/2015	18	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	458.32	07/2013 -	06/2015	23	-
116	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,655.67	03/2014 -	06/2015	15	-
117	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	91.30	01/2013 -	06/2015	29	-
118	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,394.76	11/2013 -	06/2015	19	-
119	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,583.46	09/2014 -	06/2015	9	-
120	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	358.71	11/2013 -	06/2015	19	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
121	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	321.72	06/2014 -	06/2015	12	-
122	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,390.96	08/2014 -	06/2015	10	-
123	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	461.60	02/2014 -	06/2015	16	-
124	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	252.57	08/2014 -	06/2015	10	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	466.32	11/2014 -	06/2015	7	-
126	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,960.41	10/2014 -	06/2015	8	-
127	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	878.18	11/2014 -	06/2015	7	-
128	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	842.77	869.41	07/2013 02/2011	08/2015	25	54
129	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,881.55	09/2008 08/2010	12/2015	87	64
130	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	512.79	09/2010 -	12/2015	63	-
131	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,102.25	01/2015 -	12/2015	11	-
132	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,964.50	12/2012 -	12/2015	36	-
133	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	710.74	11/2012 -	12/2015	37	-
134	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	921.72	01/2015 -	12/2015	11	-
135	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	3,403.49	06/2015 -	12/2015	6	-
136	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	719.23	06/2015 -	12/2015	6	-
137	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	425.16	11/2011 -	03/2016	52	-
138	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	307.17	02/2012 -	03/2016	49	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
139	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,013.88	10/2012 -	03/2016	41	-
140	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,902.60	08/2013 -	03/2016	31	-
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,104.52	04/2013 -	03/2016	35	-
142	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	933.03	11/2012 -	03/2016	40	-
143	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	05/2016	2	-
144	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	57.64	09/2014 -	06/2016	21	-
145	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,633.27	09/2009 -	07/2016	82	-
146	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 -	1,259.80	733.11	07/2006 12/2015	10/2016	123	10
147	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,841.20	01/2016 -	11/2016	10	-
148	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,569.00	09/2016 -	02/2017	5	-
149	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	4,982.00	09/2011 -	03/2017	66	-
150	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	6,644.00	01/2017 -	03/2017	2	-
151	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	328.00	12/2016 -	05/2017	5	-
152	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	3,944.00	11/2016 -	08/2017	9	-
153	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,586.00	12/2009 10/2014	03/2018	99	41
154	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,079.08	07/2010 02/2016	05/2018	94	27
155	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,348.00	03/2013 -	05/2018	62	-
156	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,828.46	09/2009 -	03/2019	114	-
	Total		158,833.35 -	179,581.75	119,409.46				
	RAILWAYS								
157	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	19	-
158	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	73	-
159	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	96	96

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	15
161	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	33	-
162	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	-
163	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	36
164	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	798.47	03/2010 -	12/2015	69	-
165	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	408.79	03/2004 12/2010	03/2016	144	63
166	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	657.06	03/2013 -	03/2016	36	-
167	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
168	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
169	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
170	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
171	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	134.30	03/2016 -	06/2016	3	-
172	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
173	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	55.61	04/2016 -	03/2017	11	-
174	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
175	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
176	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
177	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
178	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
179	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
180	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
181	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
182	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
183	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
184	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		19,470.26 -	70,891.98	34,216.25				
	ROAD TRANSPORT AND HIGHWAYS								
185	RAJMARG CHORHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	385.10	10/2008 -	01/2015	75	-
186	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	01/2015	59	-
187	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	268.50	09/2007 03/2014	02/2015	89	11
188	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	02/2015	80	-
189	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	02/2015	80	-
190	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	381.50	06/2013 -	02/2015	20	-
191	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	02/2015	18	-
192	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	759.90	01/2014 -	02/2015	13	-
193	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	616.50	07/2012 -	02/2015	31	-
194	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	03/2015	78	-
195	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	03/2015	78	-
196	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	386.10	127.10	09/2007 -	03/2015	90	-
197	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	-
198	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	03/2015	27	-
199	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	03/2015	26	-
200	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2015	21	-
201	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	03/2015	15	-
202	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	03/2015	15	-
203	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2015	11	-
204	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	03/2015	14	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
205	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	03/2015	19	-
206	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	03/2015	10	-
207	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2015	25	-
208	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	03/2015	19	-
209	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2015	9	-
210	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,934.00	09/2014 -	03/2015	6	-
211	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2015	5	-
212	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	03/2015	8	-
213	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	250.50	363.40	10/2014 -	03/2015	5	-
214	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	358.30	07/2014 -	03/2015	8	-
215	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	03/2015	6	-
216	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,592.00	10/2014 -	03/2015	5	-
217	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	03/2015	6	-
218	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	04/2015	20	-
219	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	285.30	10/2008 -	05/2015	79	-
220	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	05/2015	24	-
221	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	-
222	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	05/2015	12	-
223	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	-
224	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	05/2015	13	-
225	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	06/2015	74	-
226	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	06/2015	79	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
227	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	06/2015	79	-
228	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	06/2015	74	-
229	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.80	04/2008 04/2015	06/2015	86	2
230	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	242.10	07/2009 -	06/2015	71	-
231	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	-
232	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	06/2015	61	-
233	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,686.00	09/2012 -	06/2015	33	-
234	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
235	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	06/2015	26	-
236	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	06/2015	19	-
237	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	942.90	07/2013 -	06/2015	23	-
238	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	06/2015	22	-
239	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	-
240	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	08/2015	86	-
241	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	08/2015	24	-
242	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	09/2015	87	-
243	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	09/2015	40	-
244	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	09/2015	26	-
245	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	462.00	02/2014 -	09/2015	19	-
246	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	-
247	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	10/2015	13	-
248	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	-
249	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	-
250	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	752.70	10/2013 -	11/2015	25	-
251	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
252	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	280.00	366.80	02/2009 -	12/2015	82	-
253	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
254	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	12/2015	63	-
255	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	-
256	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	-
257	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	-
258	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	-
259	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	12/2015	21	-
260	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	-
261	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	-
262	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	-
263	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2015	27	-
264	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	-
265	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	141.30	01/2014 -	12/2015	23	-
266	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	12/2015	17	-
267	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	-
268	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	-
269	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	-
270	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	-
271	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	-
272	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	-
273	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	-
274	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
275	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
276	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	-
277	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	-
278	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
279	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2016	22	-
280	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	-
	Total		70,676.10 -	72,651.15	72,082.01				
	SHIPPING AND PORTS								
281	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,098.56	937.28	12/2010 09/2012	01/2016	61	40
	Total		1,228.00 -	2,098.56	937.28				
	TELECOMMUNICATIONS								
282	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	195.94	01/2009 -	03/2015	74	-
	Total		336.81 -	336.81	195.94				
	URBAN DEVELOPMENT								
283	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	93.74	03/2012 -	01/2015	34	-
284	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	-
285	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	17.60	06/2012 -	05/2015	35	-
286	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	-
287	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	315.00	53.96	06/2015 -	08/2015	2	-
288	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	15.60	11/2014 -	10/2015	11	-
289	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	101.52	05/2013 -	10/2015	29	-
290	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	-

(January 2015)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
291	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	103.45	08/2014 -	01/2016	17	-
292	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
293	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	-
294	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 -	14,600.00	-	12/2015 -	08/2016	8	-
295	CONSTRUCTION OF CENTRAL ACADEMY FOR PUBLIC TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	10.64	12/2014 -	12/2016	24	-
296	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	12/2016	15	-
	Total		43,553.53 -	43,553.53	1,081.72				
	Grand Total		487,684.54	589,383.64	365,202.24				
