

दलनह; {k= dh ifj;k t ukvk
CENTRAL SECTOR PROJECTS

**₹150 djkM vkj vf/kd ykxr okyh
(₹ 150 Crore and above)**

**363oh ¶Yk'k fj ikVl@363rd Flash Report
t uojh] 2016@January, 2016**



Hkkjr ljdkj / Government of India

lkf[; dh vkj dk; Øe dk; kUo; u e=ky ;

Ministry of Statistics and Programme Implementation

**vk/kkjh ljpuk vkj ifj;k t uk i=ck/ku iHkkx
Infrastructure and Project Monitoring Division**

l jnkj iV;y Hkou] lln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / New Delhi-110001

oc lkbV / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

	Pages
Executive Summary Hindi	1-23
Executive Summary English	24-41
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-2016	42-46
Month wise List of Deleted Projects Costing Rs. 150 crore and above during 2015-2016	47-48
Summary of projects	49-64
Graphical Presentation of All Projects	65-76
Sector wise Analysis of Projects	77-130
Sector wise Graph	131-142
Annexures	143-143
Status of central sector projects costing Rs.150 Crore and above	144-144
List of projects in which expenditure is more than approved cost	145-153
Details of Projects Ahead of Schedule w.r.t. Original Schedule	154-154
Details of On Schedule Projects w.r.t. Original Schedule	155-167
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	168-179
Details of Delayed Projects w.r.t. Original and Revised Schedule	180-208
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	209-213
Details of Projects Without Date of Commissioning	214-233
Details of projects without original Date of Commissioning	234-236
Details of projects without Milestones w.r.t. original schedule	237-270
List of Projects Ahead of Schedule w.r.t. Latest Schedule	271-272
List of Projects on schedule w.r.t. Latest Schedule	273-288
List of ongoing projects having cost overrun w.r.t. to revised schedule	289-298
List of Delayed Projects w.r.t. Latest Schedule	299-314
Details of Central Sector Projects Showing Time overruns of 6 Months and More	315-329
Details of Central Sector Projects Showing Cost overruns of More Than Rs. 100 Crore	330-338
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More and cost overruns of Rs. 100 Crore and above	339-343
Details of 20 Railways Projects	344-345

कार्यकारी सारांश

1. जनवरी, 2016 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1063 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जनवरी 2016 के दौरान, 6 परियोजनाओं (इस्पात क्षेत्र में 3 परियोजनाएं तथा कोयला, विद्युत तथा शहरी विकास क्षेत्र प्रत्येक में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 1063 परियोजनाओं में से, 346 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 53 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 53 परियोजनाओं में से, 13 परियोजनाएं ₹ 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	सड़क परिवहन एवं राजमार्ग	411	132	19	0
2.	रेलवे	297	31	0	0
3.	विद्युत	111	59	14	7
4.	कोयला	86	44	1	0
5.	पेट्रोलियम	62	36	9	4
6.	इस्पात	33	17	6	0
7.	शहरी विकास	30	12	2	0
8.	स्वास्थ्य और परिवार कल्याण	9	3	0	0
9.	पोत परिवहन एवं पत्तन	8	3	0	0
10.	नागर विमानन	4	1	0	0
11.	परमाणु ऊर्जा	4	4	2	2
12.	खान	3	1	0	0
13.	उर्वरक	1	0	0	0
14.	दूरसंचार	2	2	0	0
15.	पेट्रोरसायन	1	0	0	0
16.	भारी उद्योग	1	1	0	0
कुल		1063	346	53	13

3. 1063 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹ 11,78,671.50 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹ 13,95,087.12 करोड़ होने की संभावना है, जो ₹ 2,16,415.62 करोड़

(मूल लागत का 18.36%) की समय लागत वृद्धि को दर्शाता है। जनवरी, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹ 5,52,163.36 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 39.58% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(31.01.2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	लागत वृद्धि (%)
	परमाणु ऊर्जा				
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनी, 500 मेगावाट)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	70.54
	नागर विमानन				
3	विभिन्न हवाई अड्डों पर सं.56 एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
	कोयला				
1	हिंगुला ओसी-II विस्तार चरण-III (15 एमटीवाई)	11/2008	479.53	479.63	0.02
2	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	12.97
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	16.86
4	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	87.58
5	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
	उर्वरक				
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	5.89
	भारी उद्योग				
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
	पेट्रोरसायन				
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	82.49
	पेट्रोलियम				
1	एमएच उत्तर पुनर्विकास चरण III	06/2014	5706.47	5813.25	1.87
2	गमजी पुनर्विकास परियोजना	05/2015	1671.22	1881.22	12.57
3	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	16.02
4	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	16.05
5	कोच्ची में एलपीजी टर्मिनल	10/2015	607.06	714.25	17.66

	विद्युत				
1	एस्सार पावर गुजरात लिमिटेड की कनेक्टिविटी के लिए पारेषण प्रणाली	12/2011	552.44	609.44	10.32
2	दक्षिणी क्षेत्र की प्रणाली को मजबूत बनाना - XIV	12/2011	297.33	346.79	16.63
3	कुडनकुलम एपीपी ट्रांस प्रणाली (पीजीसीआईएल)	05/2005	1779.29	2187.32	22.93
4	पूर्वोत्तर उत्तर पश्चिमी इंटरकनेक्टर परियोजना-I	02/2009	11130.19	13762.80	23.65
5	छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए डबल्यूआर के उत्तर/पश्चिम भाग में प्रणाली को मजबूत बनाने	12/2011	1746.65	2228.71	27.60
	रेलवे				
1	जयपुर - रिंगुस - चुरु और सीकर - लोहारू गेज रूपांतरण (एनडब्ल्यूआर)	04/2008	653.19	653.55	0.06
2	कल्याण-कसारा तीसरी लाइन	04/2011	277.70	279.70	0.72
3	नालिया से वयोर (डब्ल्यू आर) तक विस्तार के साथ भूज नालिया जीसी	04/2008	318.24	321.62	1.06
4	न्यू कूच बिहार-गुमानी टोपी पैच दोहरीकरण परियोजना	04/2012	283.55	288.81	1.86
5	व्हाइट फील्ड-कोलार एनएल	04/2011	341.05	348.85	2.29
	सड़क परिवहन एवं पत्तन				
1	चंबल पुल, राष्ट्रीय राजमार्ग 76 (आरजे 5)	12/2003	275.00	281.31	2.29
2	ईपीसी एमओ पर पेव्ड शोल्डर के साथ दो लेन, राष्ट्रीय राजमार्ग 226 ई के उन्नयन और पुनर्विकास, 0-1 से 66-20 तक	03/2015	157.18	161.70	2.88
3	81/0 किमी. से 203/0 किमी. में पुलिया को चौड़ा करने तथा पुनर्निर्माण सहित पेव्ड शोल्डर के निर्माण	03/2015	258.97	268.92	3.84
4	एनएच 71 (नई एनएच 52) के पंजाब / हरियाणा सीमा सेक्शन से डोंगल कल्याण के पेव्ड शोल्डर के साथ 4 लेनिंग	11/2014	573.96	605.00	5.41
5	121/0 से 165/00 किमी. (विजयवाड़ा-जगदलपुर-रूद्रमपुर) तक एनएच 221 के पुनर्वास और उन्नयन	10/2014	295.47	313.27	6.02
	पोत परिवहन एवं पत्तन				
1	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	5.66
2	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	66.82

3	मुंबई में बीओटी आधार पर अपतटीय कंटेनर बर्थ के निर्माण और कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	82.72
4	एन्नोर मनाली एक्सप्रेस मार्ग, एफ / हे स्पेशल पर्पज व्हीकल (एसपीवी)	10/2002	150.00	600.00	300.00
	इस्पात				
1	प्रधानमंत्री ग्राम सड़क योजना के तहत-झारखंड पंचवर्षीय रखरखाव के साथ ग्रामीण सड़कों का निर्माण	12/2007	253.92	254.00	0.03
2	गुलबर्गा में पैरामेडिकल और संबद्ध स्वास्थ्य संस्थान का निर्माण	07/2011	324.87	325.00	0.04
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत झारखंड पंचवर्षीय में ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	12.04
4	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत झारखंड पंचवर्षीय में ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	173.00	15.54
5	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत झारखंड पंचवर्षीय में ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	207.00	17.96
	शहरी विकास				
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	13845.01	116.50

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. पूर्ण रूप से अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.01.2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	सीओआर (रु.करोड़ में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	22462.00	9291.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर भाविनि), 500 एमडब्ल्यूई(	09/2003	3492.00	5677.00	2185.00
	नागर विमानन				
1	विभिन्न हवाई अड्डों पर सं. 56 फायर निविदाओं की आपूर्ति एयरफील्ड	10/2012	217.60	244.10	26.50

	कोयला				
1	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
2	निगाही ओसी विस्तार परियोजना 10 एमटीवाई से 15 एमटीवाई, सिंगरौली	10/2007	259.40	486.57	227.17
3	रामागुंडम ओसी-II विस्तार	12/2009	418.97	489.62	70.65
4	मनुगुरु का आरएफआर ओसी परियोजना	11/2012	430.45	486.27	55.82
5	हिंगुला ओसी-II विस्तार फेज-III(15 एमटीवाई)	11/2008	479.53	479.63	0.10
	उर्वरक				
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	11.65
	भारी उद्योग				
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
	पेट्रोरसायन				
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	9965.00	4504.39
	पेट्रोलियम				
1	पारादीप रिफाइनरी परियोजना	02/2009	29777.00	34555.00	4778.00
2	समेकित रिफाइनरी विस्तार परियोजना	03/2012	14225.00	16504.00	2279.00
3	वशिष्टा तथा एस-1 क्षेत्रों का समेकित विकास	05/2013	4124.35	4941.49	817.14
4	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
5	बी-127 क्षेत्रों के एकीकृत विकास	12/2011	2059.63	2665.65	606.02
	विद्युत				
1	सुबनसिरी लोअर एचईपी (8X250 मेगावाट) एनएचपीसी	09/2003	6285.33	18063.89	11778.56
2	बाढ़ एसटीपीपी (3X660मेगावाट) एनटीपीसी	02/2005	8692.97	15095.67	6402.70
3	रघुनाथपुर थर्मल पावर स्टेशन फेज-I	04/2007	4122.00	9606.82	5484.82
4	कामेंग जल विद्युत परियोजना (नीपको)	09/2002	3919.59	8398.76	4479.17
5	पार्वती एचईपी (4x200 मेवा (. (एनएचपीसी)II	12/2004	2496.90	6085.84	3588.94
	रेलवे				
1	उधमपुर-श्रीनगर-बारामूला एनएल, एनआर	03/1995	2500.00	20000.00	17500.00
2	जिरिबाम से इम्फाल (तुपुई)(एनएल)(एनईएफआर)	04/2003	727.56	6570.75	5843.19

3	लुमडिंग -सिलचर-जिरिबाम, बदरपुर-कुमारघाट राष्ट्रीय परियोजना- बराईग्राम	04/1996	1676.31	5500.00	3823.69
4	बोगीबिल तथा लिंक लाइन पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	4996.19	3496.19
5	ललितपुर-सतना-रीवा-सिंगरौली एनएल, (एनसीआर)	09/1998	247.66	3500.00	3252.34
सड़क परिवहन एवं पत्तन					
1	पानीपत जालंधर 6 लेन, (96 किमी. 387.1 किमी.)	05/2009	1108.00	2288.00	1180.00
2	मैबंग से लुमडिंग (एएस-25) 83.400 किमी से .111.000 किमी	12/2003	199.81	385.13	185.32
3	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	331.23	135.23
4	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी से .126.450 किमी-एनएच .54	12/2003	155.04	280.13	125.09
5	एलडब्ल्यूई एस के तहत एनएच-202 पर अप्रोच रोड सहित वेंकटपुरम के समीप गोदावरी नदी पुल का निर्माण	03/2011	218.31	339.82	121.51
पोत परिवहन एवं पत्तन					
1	एन्नोर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल (एसपीवी)	10/2002	150.00	600.00	450.00
2	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	669.46	303.07
3	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	409.83	164.16
4	कामराजार पोर्ट लिमिटेड में कोयला बर्थ-4 के निर्माण	02/2015	244.50	258.33	13.83
	इस्पात				
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल के निर्माण	05/2005	768.88	1060.00	291.12
2	सिंटर मंशीन -1 और 2 का सुधार	12/2009	343.00	488.40	145.40
3	प्रधानमंत्री ग्राम सड़क योजना चरण-VIII के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	10/2011	175.49	207.00	31.51
4	प्रधानमंत्री ग्राम सड़क योजना चरण-VI के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	12/2007	202.61	227.00	24.39

5	प्रधानमंत्री ग्राम सड़क योजना चरण-V के तहत ग्रामीण सड़कों का निर्माण तथा रखरखाव	03/2007	149.73	173.00	23.27
	शहरी विकास				
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	13845.01	7450.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 1063 परियोजनाओं में से, 7 परियोजनाएं समय से पहले चल रही हैं, 253 समय पर तथा 346 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या में 310 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा, 35 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 422 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 346 विलंबित परियोजनाओं में से, 61 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 73 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 141 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 71 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम समयवृद्धि (टीओआर) वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(31.01.2016 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	05/2016	89
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर भाविनि), 500 एमडब्ल्यूई(	09/2003	09/2010	09/2016	72
3	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	12/2019	36
4	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	11/2018	35
	नागर विमानन				
1	पाकयांग सिक्किम) हवाई अड्डा में नए हवाई अड्डे) का निर्माण	01/2009	01/2011	09/2017	80
	कोयला				
1	गेवरा विस्तार ओसीपी (एसईसीएल) (25-35) एमटीवाई	06/2010	03/2014	03/2016	24

2	दीपका विस्तार ओसीपी (एसईसीएल) (20-25) एमटीवाई	12/2009	03/2014	03/2016	24
3	मुराईडीह स्नातकीय टर्नकी परियोजना	02/2011	04/2014	03/2016	23
4	पवन ऊर्जा परियोजना, कलुनीरकुलम, तमिलनाडु	04/2012	10/2014	03/2016	17
5	आरकेपी ओसीपी चरण-I	03/2010	03/2015	03/2016	12
	स्वास्थ्य एवं परिवार कल्याण				
1	एम्स-रायबरेली-हाउसिंग	10/2013	11/2013	03/2016	28
2	एलजीबीआरआईएमएच-तेजपुर, असम	07/2012	12/2014	03/2016	15
3	सफदरजंग अस्पताल का पुनर्विकास और अदर्स -सुपर स्पेशियलिटी ब्लॉक	09/2013	12/2015	03/2016	3
	भारी उद्योग				
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
	खान				
1	सीएपीसी के ओपनकास्ट मौजूद मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	09/2017	04/2020	31
	पेट्रोलियम				
1	2000 एचपी ड्रिलिंग रिग की सं. 2 की खरीद	04/2010	06/2012	01/2016	43
2	पारादीप रिफाइनरी परियोजना	02/2009	11/2012	02/2016	39
3	डब्ल्यूओ-16 क्लस्टर क्षेत्रों के विकास	06/2010	01/2014	01/2016	24
4	माउंडेड बुलेट परियोजना बीपीसीएल	12/2012	12/2014	02/2016	14
5	एसएमपीएल का डीबोटलनेकिंग	12/2009	08/2015	03/2016	7
	विद्युत				
1	उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम-XIX	02/2009	02/2012	02/2016	48
2	उत्तरी क्षेत्र ट्रांसमिशन सुदृढीकरण स्कीम	03/2010	11/2012	02/2016	39
3	सिक्किम से एनआर/डब्ल्यूआर भाग ख में जनरेशन परियोजनाओं से विद्युत के हस्तांतरण के लिए पारेषण प्रणाली	05/2010	01/2013	02/2016	37
4	उत्तरी क्षेत्र प्रणाली सुदृढीकरण स्कीम -XXI	08/2010	04/2013	02/2016	34
5	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	07/2013	01/2016	30
	रेलवे				
1	मुंगेर में रेल-सह-सड़क पुल (एनएल), ईसीआर	04/2002	03/2009	03/2016	84
2	लुंमडिंग-सिलचर-जिरिबम, बदरपुर-बरायग्राम कुमारघाट-राष्ट्रीय परियोजना	04/1996	03/2009	03/2016	84
3	खुर्दा-मेरठ-सहारनपुर और गाजियाबाद-मेरठ का विद्युतीकरण	02/2008	03/2012	03/2016	48
4	कटाखल से भैरवी	04/1998	12/2012	03/2016	39

5	धनगोवापोजी-राजखरश्वान तीसरी लाइन दोहरीकरण	04/2010	12/2015	03/2016	3
	सड़क परिवहन एवं पत्तन				
1	ग्वालियर-शिवपुरी के चार लेन	05/2013	11/2015	01/2016	2
2	होसर- कृष्णागिरी के राष्ट्रीय राजमार्ग 7 की छह लेनिंग, 33.130 किमी. से 93.00 किमी.	06/2011	12/2013	01/2016	25
3	समाख्याली - गांधीधाम	09/2010	03/2013	01/2016	34
4	गुडगांव - कोटपुतली - जयपुर (छह लेन)	02/2008	10/2011	01/2016	51
5	गुवाहाटी नलबाड़ी (एएस 5)	12/2003	04/2008	01/2016	93
	पोत परिवहन एवं पत्तन				
1	एन्नोर मनाली एक्सप्रेस वे एफ/ओ स्पेशल व्हीकल (एसपीवी)	10/2002	03/2006	03/2016	120
2	कोचीन पोर्ट ट्रस्ट पर बल्लापारम में आईसीटी की रेल कनेक्टिविटी	03/2007	04/2009	08/2016	88
3	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	12/2010	01/2016	61
	इस्पात				
1	भिलाई इस्पात संयंत्र के विस्तार	08/2010	03/2013	06/2016	39
2	अन्य संबद्ध सुविधाओं के साथ 45 एमवीए सैफ टी की स्थापना	12/2011	10/2013	03/2016	29
3	गुलबर्गा में मेडिकल कॉलेज के निर्माण और अस्पताल	05/2005	02/2014	03/2016	25
4	कोक ओवन बैटरी-9 बसपा एटी, भिलाई, छत्तीसगढ़ की ठंड मरम्मत	07/2012	08/2014	01/2016	17
5	गुलबर्गा में पैरामेडिकल और संबद्ध स्वास्थ्य संस्थान के निर्माण	07/2011	12/2015	03/2016	3
	दूरसंचार				
1	इंटेलिजेंट फाइबर ऑप्टिक सी के भाग क, पैकेज एफ तथा जी, स्पेक्ट्रम (एनएफएस) ओएफएस लाइंग परियोजना के लिए नेटवर्क	09/2014	09/2014	03/2017	30
2	स्पेक्ट्रम के लिए नेटवर्क	03/2012	07/2015	03/2017	20
	शहरी विकास				
1	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी प.बं. में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	03/2016	45
2	संसदीय सौध संसद भवन परिसर नई दिल्ली में भवन के विस्तार हेतु निर्माण कार्य	05/2009	05/2013	06/2016	37
3	प्रगति मैदान से सटे भूमि पर भारत के उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	01/2016	17
4	कमांड में आईआईटी मंडी के लिए चरण I के तहत विभिन्न भवन	11/2012	11/2014	03/2016	16

5	प्लॉट नं. 4 सेक्टर 10 द्वारका नई दिल्ली पर पीएनबी के प्रधान कार्यालय भवन का निर्माण	05/2012	12/2014	04/2016	16
---	---	---------	---------	---------	----

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

6. अप्रैल 2015 में, इस मंत्रालय की निगरानी पर चल रहे 758 परियोजनाओं में से, 231 परियोजनाओं के संबंध में लागतवृद्धि तथा 323 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है; जबकि जनवरी 2016 के दौरान, 1063 परियोजनाओं में से 240 परियोजनाओं के संबंध में लागतवृद्धि तथा 346 परियोजनाओं के संबंध में समयवृद्धि की सूचना प्राप्त हुई है। अप्रैल 2015 की तुलना में, लागतवृद्धि दर्शाने वाले परियोजनाओं की संख्या 30.47% से घटकर 22.58% हो गई, जबकि समयवृद्धि दर्शाने वाले परियोजनाओं के संबंध में 42.61% से घटकर 32.55% हो गई है।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.01.2016 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा का निर्माण	01/2009	309.46	309.46	412.95	01/2011	09/2017
2	नई अंतरराष्ट्रीय टर्मिनल भवन का	05/2010	335.61	318.00	305.01	05/2012	03/2015

	निर्माण						
3	विभिन्न हवाई अड्डों पर सं. 56 एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	वीएसआई एयरपोर्ट पर नई एकीकृत टर्मिनल भवन का निर्माण	10/2013	314.61	314.61	21.76	एन.ए.	09/2018
कोयला							
1	मदननगर ओसीपी	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
उर्वरक							
1	न्यू सेवेज ट्रीटमेंट प्लांट पैकेज, आरसीएफ थ्रोम्बे	10/2014	197.79	209.44	49.27	11/2016	11/2016
स्वास्थ्य एवं परिवार कल्याण							
1	एलजीबीआरआईए मएच	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	एलएचएमसी-अस्पताल	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	सफदरगंज एसएसबी	09/2013	444.70	444.70	268.07	12/2015	03/2016
4	रायबरेली हाउसिंग	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	सफदरगंज अस्पताल, नई दिल्ली पुनर्विकास और अन्य इमरजेंसी ब्लॉक	11/2013	196.70	196.70	157.61	01/2016	01/2016
भारी उद्योग							
1	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
खान							
1	मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1176.00	4.59	09/2017	04/2020
2	डब्ल्यूपीपीएमएच	12/2015	355.13	355.13	0.00	11/2016	11/2016

3	डब्ल्यूपीपीआरजे	12/2015	344.50	344.50	0.00	11/2016	11/2016
पेट्रोलियम							
1	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	1074.73	10/2011	03/2016
2	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1447.43	01/2012	05/2016
3	एन्नोर में नई विपणन टर्मिनल	11/2006	171.83	171.83	0.00	एन.ए.	एन.ए.
4	12 ऑफशोर सप्लाई वेजेल्स का निर्माण	06/2007	736.65	736.65	499.19	09/2011	10/2016
5	सं. बीस फीडर गैस पाइपलाइन	03/2009	228.64	214.19	140.71	12/2016	12/2016
विद्युत							
1	सुबनसिरी लोअर एच.ई.पी (8x250 मेवा.) (एनएचपीसी)	09/2003	6285.33	18063.89	7969.14	09/2010	एन.ए.
2	बीटीपीएस-ए	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	आरटीपीएस चरण- I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	नॉर्थ ईआर में फाइबर ऑप्टिक संचार प्रणाली का स्थापना	03/2012	198.63	198.63	94.63	09/2014	06/2016
5	उआरटीडीएसएम चरण- I	01/2014	374.63	374.63	16.20	04/2016	11/2016
रेलवे							
1	हावड़ा-आमता-चंपादंगा एनएल (एसईआर)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	नांगलडैम-तलवारा (एनएल), एनआर	03/1981	450.00	2100.00	391.95	07/2012	एन.ए.
3	एकलाखी-बलूरघाट सहित जी से नई बीजी रेलवे लाइन	04/1983	36.80	1336.57	255.55	एन.ए.	03/2019

4	तामलुक दीघा, लाइन दोहरीकरण (एसईआर)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	गुना-इटावा वाया शिवपुर-ग्वालियर- भिंड एनएल, (एनसीआर)	04/1986	158.77	608.02	602.10	03/1994	03/2015
सड़क परिवहन एवं पत्तन							
1	मधुगिरि-मूलबगल (400.330 किमी. से 483.151) - एलओटी-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	अनीशाबाद- औरंगाबाद-- हरिहरगंज (0.000 किमी. 62.000 किमी.)- एलओटी	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	अनीशाबाद- औरंगाबाद-- हरिहरगंज (62.000 किमी. से 154.625 किमी.)- एलओटी	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	बख्तियारपुर- मोकामा	01/1991	1167.45	1167.45	0.00	एन.ए.	एन.ए.
5	बंकुरा-पुरुलिया (0.000 किमी. से 84.000 किमी.)	01/1991	322.00	322.00	0.00	03/2018	03/2018
पोत परिवहन एवं पत्तन							
1	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	03/2016
2	सेतुसमुंद्रम शिप चैनल प्रोजेक्ट	06/2005	2427.40	2427.40	841.02	10/2008	एन.ए.
3	ऑफशोर कंटेनर बर्थ का निर्माण तथा कंटेनर	01/2007	366.39	669.46	415.80	12/2010	01/2016

	टर्मिनल का विकास						
4	कोचीन पोर्ट ट्रस्ट के वल्लारपदम में आईसीटीटी के लिए रेल संपर्क	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	आरओआरओ-II	09/2015	210.00	210.00	0.00	01/2018	01/2018
इस्पात							
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल	05/2005	768.88	1060.00	1070.97	02/2014	03/2016
2	बैगमती का सिंचाई कार्य	10/2005	956.00	956.00	648.16	03/2015	03/2017
3	ग्रामीण सड़क के अंतर्गत निर्माण और प्रबंधन	03/2007	149.73	173.00	175.94	12/2015	03/2017
4	ग्रामीण सड़क के अंतर्गत निर्माण और प्रबंधन	12/2007	202.61	227.00	195.51	12/2016	12/2016
5	गिरीडीह में सड़क और पुल का निर्माण, कोडरमा	12/2007	200.00	200.00	126.15	03/2018	03/2018
दूरसंचार							
1	विक्षेपण का नेटवर्क	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
शहरी विकास							
1	सैन्य एम में शादी आवास के निर्माण	08/2005	191.24	191.24	0.00	08/2007	एन.ए.
2	सीवरेज परियोजना	08/2007	246.90	246.90	0.00	एन.ए.	एन.ए.
3	संसद भवन एनेक्सी के लिए भवन विस्तार कार्य	05/2009	261.85	261.85	168.00	05/2013	06/2016
4	एनआईटी कालिकट केरल के लिए मेगा छात्रावास का निर्माण	01/2010	165.23	165.23	0.00	10/2012	एन.ए.

5	आईआईटी हौज खास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	162.90	162.90	160.00	07/2012	12/2015
---	---	---------	--------	--------	--------	---------	---------

एन.ए. : उपलब्ध नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

9. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं। बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31-01-2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	21077.00
2	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	0.00	5150.14
नागर विमानन					
1	विभिन्न हवाई अड्डों पर सं.56 एयरफील्ड फायर निविदाओं की आपूर्ति	01/2009	309.46	0.00	412.95
कोयला					
1	अनंत ओसी विस्तार चरण -III (15.0 एमटीवाई)	08/2008	207.28	0.00	207.70
2	रामगुंडम ओसी -II विस्तार	12/2009	418.97	0.00	453.18
पेट्रोरसायन					
1	असम गैस क्रैकर प्रोजेक्ट	04/2006	5460.61	8920.00	9175.15
पेट्रोलियम					
1	कोरबा में टीओपी मार्केटिंग	01/2011	141.86	0.00	164.35
विद्युत					
1	पार्वती एचईपी (4x200 मेवा.) (एनएचपीसी) II	09/2002	3919.59	0.00	5398.46
2	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7969.14

3	तीस्ता लो डैम एचईपी, स्टेज IV (4X40 मेगावाट) (एनएचपीसी)	09/2005	1061.38	0.00	1956.52
4	किशनगंगा जलविद्युत परियोजना (3X110 मेगावाट)	01/2009	3642.04	0.00	4402.95
5	उत्तर क्षेत्र प्रणाली को मजबूत बनाने की स्कीम-VII	02/2009	509.66	0.00	528.56
रेलवे					
1	सेगजोल-इटाहर (एनएल) एनईएफआर सहित इकलाखी-बालुरघाट के लिए नई बीजी रेलवे लाइन	04/1983	36.80	36.38	255.55
2	वीरमगाम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	155.66	0.00	201.26
3	पेदापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	12/1994	124.43	0.00	712.02
4	ऊधमपुर-श्रीनगर-बारामूला (एनएल), एन.आर.	03/1995	2500.00	0.00	10722.72
5	कटक - बैरंग (एलडी)	04/1995	127.13	0.00	193.37
सड़क परिवहन एवं पत्तन					
1	हरंगार्जों से मैबंग (एस 23), 126.450 किमी. से 140.700 किमी.	12/2003	280.00	0.00	392.60
2	धरमतुल से सोनापुर, 205-183 किमी. (एस 20)	12/2003	160.00	0.00	197.40
3	गुवाहाटी नलबाड़ी (एस 5)	12/2003	198.16	0.00	242.40
4	नलबाड़ी से बिजनी (एस-7)	12/2003	208.00	230.00	295.20
5	असम पश्चिम बंगाल सीमा (एनएच 31.सी) (1) के बिजनी (एनएचएआई)	12/2003	195.00	0.00	278.96
पोत परिवहन एवं पत्तन					
1	मुंबई में ऑफशोर कंटेनर बर्थ का निर्माण तथा बीओटी आधार पर कंटेनर टर्मिनल का विकास	01/2007	366.39	0.00	415.80
इस्पात					
1	गुलबर्गा में मेडिकल कॉलेज और अस्पताल का निर्माण	05/2005	768.88	1060.00	1070.97
1	पीएमजीएसवाई चरण V के तहत ग्रामीण सड़क का निर्माण तथा प्रबंधन	03/2007	149.73	173.00	175.94
शहरी विकास					
1	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	13525.81

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

10. शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (31.01.2016 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	नई अंतर्राष्ट्रीय टर्मिनल बिल्डिंग का निर्माण (गोवा)	05/2010	05/2012	एन.ए.	03/2015
2	विभिन्न हवाई अड्डों पर सं. 56 एयरफील्ड फायर टैंडर की आपूर्ति	10/2012	03/2015	एन.ए.	09/2015
कोयला					
1	झल्लाराम शाफ्ट परियोजना	09/2007	03/2013	एन.ए.	एन.ए.
स्वास्थ्य एवं परिवार कल्याण					
1	एलएचएमसी नई दिल्ली पुनर्विकास	02/2013	11/2013	एन.ए.	11/2014
पेट्रोसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	12/2013	12/2015
पेट्रोलियम					
1	एन्नोर में नई मार्केटिंग टर्मिनल	11/2006	एन.ए.	एन.ए.	एन.ए.
2	कोची-कूटनद-बंगलौर-मंगलौर पाइपलाइन परियोजना	06/2009	12/2012	एन.ए.	06/2015
3	एक ईटीपी और तीन ईटीपी सह वाटर इंजेक्शन संयंत्रों का निर्माण (डब्ल्यूआईपी)	06/2010	01/2014	एन.ए.	एन.ए.
4	टाटा नगर और राची डिपो से खूंटी का रिसाइलमेंट	04/2011	05/2015	एन.ए.	एन.ए.

	(झारखंड)				
5	एन्नोर-त्रिची मदुरै एलपीजी पाइनपलाइन	05/2013	एन.ए.	एन.ए.	एन.ए.
विद्युत					
1	सुबनसिरि लोअर एचईपी (8X250 मेगावाट) (एनएचपीसी)	09/2003	09/2010	एन.ए.	एन.ए.
2	एसआर का प्रणाली सुदृढीकरण XII	02/2010	06/2012	एन.ए.	एन.ए.
3	आंध्र प्रदेश भाग-क1 की वेमगिरि क्षेत्र में आईएसजीएस परियोजनाओं से संबंधित सामान्य प्रणाली	03/2012	06/2014	एन.ए.	एन.ए.
रेलवे					
1	हावड़ा-अमटा-चम्पादंगा एनएल (एसईआर)	04/1974	03/2007	03/2007	03/2015
2	नांगल बांध-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.ए.	एन.ए.
3	गुना-इटावा वाया शिवपुरी-ग्वालियर -भिंड एनएल , (एनसीआर)	04/1986	03/1994	एन.ए.	03/2015
4	नामखाना-चंद्रनगर, काकद्वीप-बुदाखली और चंद्र नाग के लिए लक्ष्मीकांतपुर-नामखाना के बाद एमएम	04/1987	एन.ए.	एन.ए.	एन.ए.
5	वीरमगाम-भिल्डी (डब्ल्यू आर), जीसी	04/1990	एन.ए.	03/2010	एन.ए.
सड़क परिवहन एवं पत्तन					
1	एनएच 66 के टिंडीवनम अनुभाग के लिए पांडिचेरी	01/1991	01/2008	एन.ए.	एन.ए.
2	पुनर्वास और 2 लाइन्स -2 पेव्ड शोल्डर विन्यास और मजबूत बनाने ओ के साथ लेन करने के लिए उन्नयन	01/1991	04/2014	एन.ए.	एन.ए.
3	पेव्ड शोल्डर के साथ 2 लेन का उन्नयन तथा पुनर्विकास, बिरपुर-बिहपुर	01/1991	एन.ए.	एन.ए.	एन.ए.

	के विन्यास तथा सुदृढीकरण,				
4	ईपीसी आधार पर एनएच 37 की नगांव बाईपास की सीमा से रांगगारा तक 4 लेनिंग (278.60 किमी से 297.00 किमी.)	01/1991	एन.ए.	एन.ए.	एन.ए.
5	4 लेन का किलोमीटर एनएच 52 के 264.10 किमी से राष्ट्रीय राजमार्ग 52क के 20.37 किमी तक गोहपुर से होलोंगी तक 4 लाइनिंग	01/1991	एन.ए.	एन.ए.	एन.ए.
पोत परिवहन एवं पत्तन					
1	सेतुसमुंद्रम शिप चैनल परियोजना	06/2005	10/2008	एन.ए.	एन.ए.
इस्पात					
1	7.0 एमटीपीए कुमारस्वामी लौह अयस्क खदान परियोजना (एनएमडीसी)	02/2011	05/2013	01/2015	08/2015
2	1.2 एमटीपीए पेलेट संयंत्र परियोजना, डोनिमलई (एनएमडीसी)	04/2011	04/2013	09/2014	06/2015
3	नेशनल इंस्टिट्यूट ऑफ फार्मास्यूटिकल एजुकेशन एंड रिसर्च के लिए परिसर और भवन का निर्माण	01/2013	एन.ए.	एन.ए.	एन.ए.
4	राजीव गांधी के अंतर्गत इनडोर खेल हॉल के लिए तेलंगाना में 123 ब्लोको तथा आंध्र प्रदेश में 167 ब्लोको का निर्माण	07/2014	01/1999	एन.ए.	एन.ए.
शहरी विकास					
1	रक्षा मंत्रालय में सैन्य स्टेशन मामुन पंजाब में विवाहित आवासीय के निर्माण	08/2005	08/2007	एन.ए.	एन.ए.
2	मूसी के दक्षिण पर पुरानी शहरी क्षेत्र में सीवरेज	08/2007	एन.ए.	एन.ए.	एन.ए.

	प्रणाली को मजबूत बनाना तथा पुनर्वास (2 जोन में)				
3	आईआईटी हौज खास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	12/2015	12/2015
4	एनआईटी कालीकट केरल के लिए मेगा छात्रावास द्वितीय का निर्माण	01/2010	10/2012	एन.ए.	एन.ए.
5	नागपुर महाराष्ट्र में राष्ट्रीय फायर सर्विसेज कॉलेज के उन्नयन	06/2010	03/2012	एन.ए.	एन.ए.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार कार्य शुरू करने की संशोधित समय-सारणी को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

11. अतिरिक्त विलंब का क्षेत्र-वार ब्योरा निम्नानुसार है:-

i) **परमाणु ऊर्जा क्षेत्र में,** सभी 4 परियोजनाएं विलंबित हैं । माह के दौरान 2 परियोजनाएं 'काकरापार परमाणु ऊर्जा परियोजना-3 तथा 4, एनपीसीआईएल' तथा 'राजस्थान परमाणु ऊर्जा परियोजना-7 तथा 8 (2X700 मेवा), एनपीसीआईएल' में क्रमशः प्रमुख उपस्करों की आपूर्ति तथा सिविल कार्यों में धीमी प्रगति के कारण क्रमशः 13 माह तथा 19 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

ii) **कोयला क्षेत्र में,** 86 परियोजनाओं में से 44 परियोजनाएं विलंबित हैं । माह के दौरान एक परियोजनाओं 'कुल्दा ओसीपी, एमसीएल' में कोयला निकासी समस्या के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iii) **पेट्रोलियम क्षेत्र में,** 62 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं । माह के दौरान, 9 परियोजनाओं के संबंध में 1-10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 9 परियोजनाओं में से 4 मेगा परियोजनाएं हैं। दो परियोजनाएं 'पारादीप रिफाइनरी परियोजना, आईओसीएल' तथा 'सीपीसीएल में माउंडेड बुलेट परियोजना, सीपीसीएल' के संबंध में क्रमशः उपस्करों की आपूर्ति में विलंब तथा बुलेट व वेल्डिंग की संस्थापना के कारण प्रत्येक में 1 माह के विलंब की सूचना प्राप्त हुई है । दो परियोजनाएं 'पारादीप-रायपुर-रांची पाइपलाइन, आईओसीएल' तथा 'गुजरात रिफाइनरी में ईटीपी के लिए रिवर्स ऑस्मोसिस संयंत्र, आईओसीएल' के संबंध में क्रमशः ठीकेदार के खराब प्रदर्शन तथा ठीकेदार द्वारा धीमी प्रगति के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएं 'कोचीन में एलपीजी टर्मिनल, आईओसीएल' तथा 'रेसिड उन्नयन परियोजना, सीपीसीएल' के संबंध में क्रमशः गांव के लोगों द्वारा किए गए हड़ताल तथा कार्य क्षेत्र में परिवर्तन के कारण प्रत्येक में 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । दो परियोजनाएं 'चेन्नई पोर्ट से मनाली रिफाइनरी तक नए

कच्चे तेल की पाइपलाइन परियोजना, सीपीसीएल' तथा 'पारादीप एलपीजी आयात सुविधा, आईओसीएल' के संबंध में क्रमशः निविदा में खराब प्रतिक्रिया तथा सांविधिक अनुमतियों के प्राप्त न होने के कारण प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'सी-26 कलस्टर क्षेत्रों का विकास, ओएनजीसी' में निविदा पुनः जारी करने के कारण 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

iv) **विद्युत क्षेत्र में**, 111 परियोजनाओं में से, 59 परियोजनाएं विलंबित हैं। माह के दौरान 14 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 14 परियोजनाओं में से, 7 परियोजनाएं मेगा परियोजनाएं हैं। तीन परियोजनाएं 'उत्तरी क्षेत्र की पारेषण का प्रणाली सुदृढीकरण योजना, पीजीसीआईएल', 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XXI, पीजीसीआईएल' तथा 'कृष्णापटनम यूएमपीपी भाग ख से संबद्ध ट्रांसमिशन प्रणाली-पार्ट बी, पीजीसीआईएल' में गंभीर आरओडब्ल्यू समस्या के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'झारखंड तथा पश्चिम बंगाल- भाग-क2 में चरण-I जेनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' तथा 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XXVIII, पीजीसीआईएल' में भूमि अधिग्रहण में विलंब के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'पूर्वी क्षेत्र को सुदृढ करने की योजना-V, पीजीसीआईएल' तथा 'पूर्वी क्षेत्र को सुदृढ करने की योजना-III, पीजीसीआईएल' में क्रमशः भूमि अधिग्रहण में विलंब तथा आरओडब्ल्यू समस्या के क्रमशः 2 तथा 3 माह के विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'तीस्ता लो डैम एचईपी, चरण-IV (4X40मेगावाट), एनएचपीसी' तथा 'पश्चिम बंगाल में एनआर भाग में पूलिंग स्टेशन के विकास तथा विद्युत के हस्तांतरण के लिए पारेषण प्रणाली, पीजीसीआईएल' में क्रमशः स्थानीय अवरोधों तथा वन संबंधी अनुमति न मिलने के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'उत्तरी क्षेत्र प्रणाली सुदृढीकरण योजना-XXV, पीजीसीआईएल' तथा 'दक्षिणी क्षेत्र प्रणाली का सुदृढीकरण -XIV, पीजीसीआईएल' में गंभीर आरओडब्ल्यू समस्या के कारण क्रमशः 3 तथा 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'पश्चिमी क्षेत्र प्रणाली सुदृढीकरण योजना-V, पीजीसीआईएल' में गंभीर आरओडब्ल्यू समस्या तथा वन संबंधी अनुमति न मिलने के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'कुडगी टीपीएस से विद्युत की निकासी के लिए आवश्यक पारेषण से जुड़ी उप-स्टेशन विस्तार कार्य, पीजीसीआईएल' में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'जैसलमेर (राजस्थान) के लखमाना में विंड पावर परियोजना 50 मेगावाट, एनएचपीसी' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

v) **इस्पात क्षेत्र में**, 33 परियोजनाओं में से 17 परियोजनाएं विलंबित हैं। माह के दौरान 6 परियोजनाओं के संबंध में 2-15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजना 'ब्लास्ट फरनेस कटेगरी-2- 1 पूंजी मरम्मत, आरआईएनएल' तथा 'एनएलसीपी के अंतर्गत मेघालय से शिलांग कला व संस्कृति का प्रदर्शन करने के लिए अंतर्राष्ट्रीय केन्द्र का निर्माण, एचएससीएल' में क्रमशः घरों से धूल निकासी का आदेश देने में विलंब तथा अपर्याप्त योजना ढांचा के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। एक परियोजना 'चरण XII के अंतर्गत ग्रामीण सड़क विकास प्राधिकरण का निर्माण, एचएससीएल' में केन्द्र सरकार द्वारा निधि जारी करने में हुए विलंब के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजना 'पीएमजीएसवाई चरण VIII के अंतर्गत ग्रामीण सड़क का निर्माण तथा रख-रखाव, एचएससीएल' तथा 'पीएमजीएसवाई चरण V

के अंतर्गत ग्रामीण सड़क का निर्माण तथा रख-रखाव, एचएससीएल' में केन्द्र सरकार द्वारा निधि जारी करने में हुए विलंब के कारण 7 माह तथा 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। एक परियोजना 'गुलबर्ग में पैरामेडिकल तथा संबद्ध स्वास्थ्य संस्थान का निर्माण, एचएससीएल' में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vi) **शहरी विकास क्षेत्र में**, 30 परियोजनाओं में से, 12 परियोजनाएं विलंबित हैं। माह के दौरान 2 परियोजनाओं के संबंध में 4-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'हरिनघंटा कल्याणी नादिया में आईआईएसईआर कोलकाता के स्थायी परिसर का निर्माण, सीपीडब्ल्यूडी' में कार्यों की धीमी प्रगति के कारण 4 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना 'आईएसएम धनबाद में 2000 लड़कों के छात्रावास (1000 डबल बेड वाले कमरे), सीपीडब्ल्यूडी' में 12 माह की अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vii) **सड़क परिवहन एवं राजमार्ग क्षेत्र में**, 411 परियोजनाओं में से, 132 परियोजनाएं विलंबित हैं। माह के दौरान 19 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। चार परियोजनाएं 'गुवाहाटी से नलवारी (एस-4), एनएचआई', धरमपुर से सोनपुर, 205-183 (एस-20), एनएचआई', 'ब्रह्मपुत्र पुल, एनएस सं. 31, एनएचआई' तथा 'पिंपलगांव-नासिक-गोंडे, एनएच-3 (एनएचडीपी-चरण-III), एनएचआई' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। चार परियोजनाएं 'गंगा पुल से रामदेवी क्रॉसिंग, चरण-II, एनएच-25, 75-80.00 किमी., एनएचआई', 'कोटा बाड़पास, आरजे-4, एनएच-76, एनएचआई', 'मोकामा-मुंगेर की दो लेनिंग करना, एनएचआई', 'पीएस-खगड़िया-पूर्णिया के साथ दो लेनिंग, एनएचआई' तथा 'पटना-बख्तजारपुर 181.3 से 231.95 किमी., एनएचआई' में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'सोनपुर से गुवाहाटी (एस-3) एनएचआई' तथा 'निंबी जोधा-देगाना-मेरता सिटी सेक्शन के पीएस सहित दो लेन का चौड़ीकरण तथा सुदृढ़ीकरण, एनएचआई' में क्रमशः 3 माह तथा 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'पेव्ड शोल्डर को 4 लेनिंग करते हुए राष्ट्रीय राजमार्ग-79 के चित्तौड़गढ़ निमुच म.प्र. सीमा, 183 000 से 221 400 किमी., पीडब्ल्यूडी' तथा 'एनएच-232 के रायबरेली-बांदा सेक्शन के पेव्ड शोल्डर की दो लेनिंग, एनएचआई' में क्रमशः 7 तथा 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, दो परियोजनाएं 'कृष्णागिरी-टिंडीवनम (अनुमोदित लंबाई 170 किमी.) की दो लेनिंग, एनएचआई' तथा 'टांडा-रायबरेली के पेव्ड शोल्डर के साथ दो लेनिंग, एनएचआई' में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। दो परियोजनाएं 'एनएच-125 के सितारगंज-तनकुर सेक्शन के पेव्ड शोल्डर के साथ दो लेनिंग, एनएचआई' में क्रमशः 12 तथा 21 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, दो परियोजनाएं 'अंबाला-कैथल-पैकेज 1 की चार लेनिंग, एनएचआई' तथा 'पीएस पैकेज 2 के साथ हिस्सार-देबवली सेक्शन की चार लेनिंग, एनएचआई' में क्रमशः 24 तथा 28 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

12. रेल मंत्रालय ने 1 जनवरी, 2015 से इस मंत्रालय को रेलवे द्वारा कार्यान्वित की जा रही सभी जारी (297) परियोजनाओं पर मासिक स्थिति रिपोर्टें प्रस्तुत करने की परंपरा को समाप्त कर दिया है। रेल मंत्रालय ने अपनी 20 परियोजनाओं के संबंध में नवीनतम जानकारी प्रदान की है, केवल इन्हीं परियोजनाओं को सां. और कार्य. कार्या. मंत्रालय स्तर पर निगरानी के लिए पहचान किया गया है। अतः

उपलब्ध सूचना/आंकड़े का (जनवरी 2015 की स्थिति के अनुसार) रेलवे क्षेत्र की सभी परियोजनाओं के संबंध में उपयोग किया गया है ।

13. सड़क परिवहन एवं राजमार्ग मंत्रालय (एमओआरटीएच) तथा भारतीय राष्ट्रीय राजमार्ग प्राधिकरण (एनएचएआई) ने जून, 2015 से अपनी परियोजनाओं संबंधी आंकड़े प्रदान करना बंद कर दिया है । तथापि, एमओआरटीएच व एनएचएआई ने फरवरी 2016 माह (रिपोर्टिंग माह दिसंबर, 2015) से अपनी सभी चल रही परियोजनाओं को स्वैच्छिक रूप से फिर से अद्यतन करना शुरू किया है । एमओआरटीएच तथा एनएचएआई दोनों ने रिपोर्टिंग माह दिसंबर, 2015 के दौरान सड़क के अंतर्गत 251 नई परियोजनाओं को शामिल किया है । यह मंत्रालय एनएचएआई के द्वारा दी गई जानकारी के अनुसार पीपीपी/बीओटी परियोजनाओं को अलग-अलग रूप से वर्गीकृत कर रहा है ।

14. दिनांक 31.01.2016 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹ 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।

15. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for January 2016 contains information on the status of the 1063 Central Sector Infrastructure Projects costing ₹150 crore and above. During January 2016, 6 projects (3 projects in Steel and 1 project each in Coal, Power and Urban Development sector) have reported completion.

2. During the reference month, out of 1063 projects, 346 projects are delayed with respect to original schedule and 53 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 53 projects, 13 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	411	132	19	0
2	RAILWAYS	297	31	0	0
3	POWER	111	59	14	7
4	COAL	86	44	1	0
5	PETROLEUM	62	36	9	4
6	STEEL	33	17	6	0
7	URBAN DEVELOPMENT	30	12	2	0
8	HEALTH AND FAMILY WELFARE	9	3	0	0
9	SHIPPING AND PORTS	8	3	0	0
10	CIVIL AVIATION	4	1	0	0
11	ATOMIC ENERGY	4	4	2	2
12	MINES	3	1	0	0
13	FERTILISERS	1	0	0	0
14	TELECOMMUNICATIONS	2	2	0	0
15	PETROCHEMICALS	1	0	0	0
16	HEAVY INDUSTRIES	1	1	0	0
Total		1063	346	53	13

3. Total original cost of implementation of the 1063 projects was ₹11,78,671.50 crore and their anticipated completion cost is likely to be ₹13,95,087.12 crore, which reflects overall cost overruns of ₹2,16,415.62 crore (18.36% of original cost). The expenditure incurred on these projects till

January 2016 is ₹5,52,163.36 crore, which is 39.58% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 31-01-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	70.54
	CIVIL AVIATION				
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
	COAL				
1	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.02
2	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	12.97
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	16.86
4	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
5	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	82.49
	PETROLEUM				
1	MH NORTH REDEVELOPMENT PHASE III	06/2014	5706.47	5813.25	1.87
2	GAMJI REDEVELOPMENT PROJECT	05/2015	1671.22	1881.22	12.57
3	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	16.02
4	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	16.05
5	LPG TERMINAL AT KOCHI	10/2015	607.06	714.25	17.66
	POWER				
1	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	12/2011	552.44	609.44	10.32
2	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	297.33	346.79	16.63
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	1779.29	2187.32	22.93
4	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	11130.19	13762.80	23.65
5	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	12/2011	1746.65	2228.71	27.60
	RAILWAYS				
1	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)	04/2008	653.19	653.55	0.06
2	KALYAN-KASARA 3RD LINE	04/2011	277.70	279.70	0.72
3	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	04/2008	318.24	321.62	1.06
4	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	04/2012	283.55	288.81	1.86
5	WHITE FIELD-KOLAR NL	04/2011	341.05	348.85	2.29

ROAD TRANSPORT AND HIGHWAYS					
1	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	275.00	281.31	2.29
2	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	03/2015	157.18	161.70	2.88
3	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	03/2015	258.97	268.92	3.84
4	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	573.96	605.00	5.41
5	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	295.47	313.27	6.02
SHIPPING AND PORTS					
1	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	5.66
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	66.82
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
4	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
STEEL					
1	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND	12/2007	253.92	254.00	0.03
2	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	324.87	325.00	0.04
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	15.54
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	207.00	17.96
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	13845.01	116.50

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 31-01-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	22462.00	9291.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
CIVIL AVIATION					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50

	COAL				
1	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	489.62	70.65
4	RFR OF MANUGURU OC PROJECT	11/2012	430.45	486.27	55.82
5	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	479.63	0.10
	FERTILISERS				
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2109.30
	PETROCHEMICALS				
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9965.00	4504.39
	PETROLEUM				
1	PARADIP REFINERY PROJECT	02/2009	29777.00	34555.00	4778.00
2	INTEGRATED REFINERY EXPANSION PROJECT	03/2012	14225.00	16504.00	2279.00
3	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4124.35	4941.49	817.14
4	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
5	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
	POWER				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	11778.56
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4122.00	9606.82	5484.82
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.76	4479.17
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6085.84	3588.94
	RAILWAYS				
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	6570.75	5843.19
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	5500.00	3823.69
4	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	4996.19	3496.19
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	3500.00	3252.34
	ROAD TRANSPORT AND HIGHWAYS				
1	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
2	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
3	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	331.23	135.23
4	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
5	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	03/2011	218.31	339.82	121.51
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	409.83	164.16
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.33	13.83

	STEEL				
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	291.12
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	207.00	31.51
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	23.27
	URBAN DEVELOPMENT				
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	13845.01	7450.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1063 projects, 7 projects are ahead of schedule, 253 are on schedule and 346 are delayed with respect to their original schedule. However, the number of delayed projects decreases to 310 if delay is calculated on the basis of latest schedule of completion. Further, 35 projects have been sanctioned without original commissioning schedule date and for 422 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 346 delayed projects, 61 projects have overall delay in the range of 1 to 12 months, 73 projects have delay in the range of 13 to 24 months, 141 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 31-01-2016)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
	ATOMIC ENERGY				
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	05/2016	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	09/2016	72
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2019	36
4	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11/2018	35
	CIVIL AVIATION				
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2017	80
	COAL				
1	GEVRA EXPANSION OCP (SECL) (25-35) MTY	06/2010	03/2014	03/2016	24
2	DIPKA EXPANSION OCP (SECL) (20-25) MTY	12/2009	03/2014	03/2016	24
3	MURAI DIH UG TURN-KEY PROJECT	02/2011	04/2014	03/2016	23
4	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	04/2012	10/2014	03/2016	17
5	RKP OCP PHASE-I	03/2010	03/2015	03/2016	12
	HEALTH AND FAMILY WELFARE				
1	AIIMS-RAEBARELI-HOUSING	10/2013	11/2013	03/2016	28
2	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	03/2016	15
3	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND	09/2013	12/2015	03/2016	3

	OTHERS -SUPER SPECIALITY BLOCK				
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	12/2017	75
	MINES				
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	09/2017	04/2020	31
	PETROLEUM				
1	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	04/2010	06/2012	01/2016	43
2	PARADIP REFINERY PROJECT	02/2009	11/2012	02/2016	39
3	DEVELOPMENT OF WO-16 CLUSTER FIELDS	06/2010	01/2014	01/2016	24
4	MOUNDED BULLET PROJECT AT CPCL	12/2012	12/2014	02/2016	14
5	DE-BOTTLENECKING OF SMPL	12/2009	08/2015	03/2016	7
	POWER				
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	02/2009	02/2012	02/2016	48
2	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	03/2010	11/2012	02/2016	39
3	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	05/2010	01/2013	02/2016	37
4	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	08/2010	04/2013	02/2016	34
5	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	01/2016	30
	RAILWAYS				
1	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	04/2002	03/2009	03/2016	84
2	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	03/2009	03/2016	84
3	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	02/2008	03/2012	03/2016	48
4	KATAKHAL TO BHAIRABI	04/1998	12/2012	03/2016	39
5	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	04/2010	12/2015	03/2016	3
	ROAD TRANSPORT AND HIGHWAYS				
1	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	11/2015	01/2016	2
2	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	06/2011	12/2013	01/2016	25
3	SAMAIKHALI - GANDHIDHAM	09/2010	03/2013	01/2016	34
4	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	10/2011	01/2016	51
5	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	01/2016	93
	SHIPPING AND PORTS				
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	03/2016	120
2	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	08/2016	88
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	01/2016	61
	STEEL				
1	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	06/2016	39
2	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	12/2011	10/2013	03/2016	29
3	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	03/2016	25
4	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	07/2012	08/2014	01/2016	17
5	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	07/2011	12/2015	03/2016	3
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	09/2014	09/2014	03/2017	30

2	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2017	20
	URBAN DEVELOPMENT				
1	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	06/2012	03/2016	45
2	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	05/2013	06/2016	37
3	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	01/2016	17
4	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	03/2016	16
5	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	05/2012	12/2014	04/2016	16

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2015, out of 758 projects on the monitor of this Ministry, 231 projects reported cost overruns and 323 projects reported time overruns; while during January 2016, out of 1063 projects, 240 projects reported cost overruns and 346 projects reported time overruns. In comparison to April 2015, number of **projects** reporting **cost overruns** has gone **down** from **30.47%** to **22.58%** whereas **projects** reporting **time overruns** have **decreased** from **42.61%** to **32.55%**.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

8. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 31-01-2016)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIR	01/2009	309.46	309.46	412.95	01/2011	09/2017

2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	318.00	305.01	05/2012	03/2015
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	30.74	03/2015	09/2015
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRP	10/2013	314.61	314.61	21.76	N.A.	09/2018
COAL							
1	MADANNAGAR OCP	10/2015	1875.32	1875.32	0.00	03/2024	03/2024
FERTILISERS							
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	49.27	11/2016	11/2016
HEALTH AND FAMILY WELFARE							
1	LGBRIMH	07/2012	175.57	175.57	106.20	12/2014	03/2016
2	LHMC - HOSPITAL	02/2013	414.11	414.11	210.91	11/2013	11/2014
3	SAFDARJUNG SSB	09/2013	444.70	444.70	268.07	12/2015	03/2016
4	RAEBARELI-HOUSING	10/2013	159.50	159.50	118.95	11/2013	03/2016
5	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	11/2013	196.70	196.70	157.61	01/2016	01/2016
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
1	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MIN	09/2011	1856.00	1176.00	4.59	09/2017	04/2020
2	WPPMH	12/2015	355.13	355.13	0.00	11/2016	11/2016
3	WPPRJ	12/2015	344.50	344.50	0.00	11/2016	11/2016
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	1074.73	10/2011	03/2016
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1447.43	01/2012	05/2016

3	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	171.83	0.00	N.A.	N.A.
4	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	736.65	499.19	09/2011	10/2016
5	TWENTY NOS. FEEDER GAS LINES	03/2009	228.64	214.19	140.71	12/2016	12/2016
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	18063.89	7969.14	09/2010	N.A.
2	BTPS-A	08/2006	2313.00	4237.67	3088.00	12/2011	03/2016
3	RTPS PH-I	04/2007	4122.00	9606.82	1353.36	02/2011	01/2017
4	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	03/2012	198.63	198.63	94.63	09/2014	06/2016
5	URTD SM PHASE-I	01/2014	374.63	374.63	16.20	04/2016	11/2016
RAILWAYS							
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	181.48	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	391.95	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING G	04/1983	36.80	1336.57	255.55	N.A.	03/2019
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	1428.00	466.36	06/2005	12/2019
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	158.77	608.02	602.10	03/1994	03/2015
ROAD TRANSPORT AND HIGHWAYS							
1	"MADHUGIRI-MULBAGAL (KM 400.330 TO KM 483.151) - LOT-II"	01/1991	219.40	219.40	0.00	01/2018	01/2018
2	ANISABAD-AURANGABAD-HARIHARGANJ (KM 0.000 TO KM 62.000)- LOT	01/1991	282.41	282.41	0.00	08/2016	08/2016
3	ANISABAD-AURANGABAD-HARIHARGANJ (KM 62.000 TO KM 154.625) -	01/1991	358.22	358.22	0.00	10/2016	10/2016
4	BAKHTIYARPUR - MOKAMA	01/1991	1167.45	1167.45	0.00	N.A.	N.A.
5	BANKUARA-PURULIA (KM 0.000 TO KM 84.000)	01/1991	322.00	322.00	0.00	03/2018	03/2018

SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	03/2016
2	SETHUSAMUDR AM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	841.02	10/2008	N.A.
3	CONSTRUCTIO N OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF	01/2007	366.39	669.46	415.80	12/2010	01/2016
4	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	409.83	366.20	04/2009	08/2016
5	RORO-II	09/2015	210.00	210.00	0.00	01/2018	01/2018
STEEL							
1	MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97	02/2014	03/2016
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	648.16	03/2015	03/2017
3	CONSTRUCTIO N AND MAINTAINANCE OF RURAL ROAD UNDER	03/2007	149.73	173.00	175.94	12/2015	03/2017
4	CONSTRUCTIO N AND MAINTAINANCE OF RURAL ROAD UNDER	12/2007	202.61	227.00	195.51	12/2016	12/2016
5	CONSTRUCTIO N OF ROAD AND BRIDGE IN GIRIDHI, KODERM	12/2007	200.00	200.00	126.15	03/2018	03/2018
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	13334.00	1360.00	07/2015	03/2017
URBAN DEVELOPMENT							
1	CONSTRUCTIO N OF MARRIED ACCOMODATIO N AT MILITARY M	08/2005	191.24	191.24	0.00	08/2007	N.A.
2	SEWEWRAGE PROJECT	08/2007	246.90	246.90	0.00	N.A.	N.A.
3	CONSTRUCTIO N OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEX	05/2009	261.85	261.85	168.00	05/2013	06/2016
4	CONSTRUCTIO N OF MEGA HOSTEL II FOR NIT CALICUT KER	01/2010	165.23	165.23	0.00	10/2012	N.A.

5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	160.00	07/2012	12/2015
---	---	---------	--------	--------	--------	---------	---------

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 31-01-2016)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	21077.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5150.14
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	01/2009	309.46	0.00	412.95
COAL					
1	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	207.70
2	RAMAGUNDAM OC-II EXTENSION	12/2009	418.97	0.00	453.18
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	8920.00	9175.15
PETROLEUM					
1	MARKETING TOP AT KORBA	01/2011	141.86	0.00	164.35
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5398.46
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7969.14
3	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1956.52
4	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	4402.95
5	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	02/2009	509.66	0.00	528.56
RAILWAYS					
1	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	36.38	255.55
2	VIRAMGAM-BHILDI(WR),GC	04/1990	155.66	0.00	201.26
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	124.43	0.00	712.02
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	0.00	10722.72
5	CUTTACK - BARANG (LD)	04/1995	127.13	0.00	193.37

ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	392.60
2	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12/2003	160.00	0.00	197.40
3	GUWAHATI TO NALBARI (AS-5)	12/2003	198.16	0.00	242.40
4	NALBARI T BIJINI (AS-7)	12/2003	208.00	230.00	295.20
5	BIJINI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	195.00	0.00	278.96
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	415.80
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1060.00	1070.97
1	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	175.94
URBAN DEVELOPMENT					
1	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	13525.81

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 31-01-2016)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	N.A.	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	N.A.	09/2015
COAL					
1	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.A.	N.A.
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	11/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	12/2013	12/2015
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.A.	N.A.	N.A.
2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	06/2009	12/2012	N.A.	06/2015

3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	N.A.	N.A.
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.A.	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	SYSTEM STRENGTHENING XII OF SR	02/2010	06/2012	N.A.	N.A.
3	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.A.	N.A.
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	03/2015
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	N.A.	03/2015
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.A.	03/2010	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	PONDICHERRY TO TINDIVANAM SECTION OF NH-66	01/1991	01/2008	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
4	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	01/1991	N.A.	N.A.	N.A.
5	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	01/1991	N.A.	N.A.	N.A.

SHIPPING AND PORTS					
1	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
STEEL					
1	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	02/2011	05/2013	01/2015	08/2015
2	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	04/2011	04/2013	09/2014	06/2015
3	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(	01/2013	N.A.	N.A.	N.A.
4	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA	07/2014	01/1999	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.A.	N.A.
2	REHABILITATION AND STRENGTHENING OF SEWWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN	08/2007	N.A.	N.A.	N.A.
3	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	12/2015	12/2015
4	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
5	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The Sector-wise details of additional delays are as under:-

- i) In the **Atomic Energy Sector**, All 4 projects are delayed. During the month 2 projects 'Kakrapar Atomic Power Project - 3 and 4, NPCIL' and 'Rajasthan Atomic Power Project -7 and 8 (2X700 MW), NPCIL' have reported additional delay of 13 months and 19 months respectively due to delay in supply of major equipments and slow progress in civil works respectively.
- ii) In the **Coal Sector**, out of 86 projects, 44 projects are delayed. During the month one project 'Kulda OCP, MCL' has reported additional delay of 12 months due to Coal evacuation problem

- iii) In the **Petroleum Sector**, out of 62 projects, 36 projects are delayed. During the month, 9 projects have reported additional delays in the range of 1-10 months. Out of 9 projects, 4 projects are mega projects. Two projects 'Paradip Refinery Project IOCL' and 'Mounded Bullet Project at CPCL' have reported additional delay of 1 month each due to delay in delivery of equipment and erection of bullets & welding respectively. Two projects 'Paradip-Raipur- Ranchi Pipeline IOCL' and 'Reverse Osmosis Plant for ETP at Gujarat Refinery, IOCL' have reported additional delay of 2 months each due to poor performance of contractor and slow progress by contractor respectively. Two projects 'LPG Terminal at Kochi, IOCL' and 'Resid Upgradation Project CPCL' have reported additional delay of 4 months each due to agitation by villagers and change in scope of work respectively. Two projects 'New Crude Oil Pipeline Project from Chennai Port to Manali Refinery, CPCL' and 'Paradip LPG Import Facility, IOCL' have reported additional delay of 5 months each due to poor response to tendering and due to non-receiving of statutory clearances respectively. The project 'Development of C-26 Cluster Fields, ONGC' has reported additional delay of 10 months due to retendering.
- iv) In the **Power Sector**, out of 111 projects, 59 projects are delayed. During the month, 14 projects have reported additional delay in the range of 1-6 months. Out of 14 projects, 7 are mega projects. Three projects 'Northern Region Transmission Strengthening Scheme, PGCIL', 'Northern Region System Strengthening Scheme-XXI PGCIL' and 'Transmission System Associated With Krishnapatnam UMPP-Part B PGCIL' have reported additional delay of 1 month each due to severe RoW problem. Two projects 'Transmission System for Phase-I Generation Projects in Jharkhand and West Bengal-Part-A2, PGCIL' and 'Northern Region System Strengthening Scheme-XXVIII, PGCIL' have reported additional delay of 1 month each due to delay in land acquisition. Two projects 'Eastern Region Strengthening Scheme-V PGCIL' and 'Eastern Region Strengthening Scheme-III PGCIL' have reported additional delay of 2 months and 3 months respectively due to delay in land acquisition and RoW problem respectively. Two projects 'Teesta Low Dam HEP, Stage-IV (4X40 MW), NHPC' and 'Transmission System for Development of Pooling Station in NR Part of West Bengal and Transfer of Power PGCIL' have reported additional delay of 3 months each due to local disturbance and non-receiving of forest clearance respectively. Two projects 'Northern Region System Strengthening scheme-XXV, PGCIL' and 'System Strengthening of Southern Region-XIV PGCIL' have reported additional delay of 3 months and 4 months respectively due to severe RoW problem. The project 'Western Region Strengthening Scheme-V, PGCIL' has reported additional delay of 6 months due to severe RoW problem and non-receiving

of forest clearance. The project 'Sub-Station Extension Works Associated With Transmission System Required For Evacuation of Power From Kudgi TPS PGCIL' has reported additional delay of 5 months and the project 'Wind Power Project at Lakhmana in Jaisalmer (Rajasthan) 50MW, NHPC' has reported additional delay of 1 month (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

- v) In the **Steel Sector**, out of 33 projects, 17 projects are delayed. During the month, 6 projects have reported additional delay in the range of 2-15 months. Two projects 'Blast Furnace-2 Category-1 Capital Repairs, RINL' and 'Construction of International Centre for Performing Arts and Culture, Shilong in Megalaya Under NLCP, HSCL' have reported additional delay of 2 months each due to delay in ordering of stock house dust extraction and inadequate plan outlay respectively. One project 'Construction of Rural Road Development Authority under Phase-XII, HSCL' has reported additional delay of 3 months each due to delay in release of fund by Central Government. Two project 'Construction and Maintenance of Rural Road Under PMGSY Phase VIII, HSCL' and 'Construction and Maintenance of Rural Road Under PMGSY Phase V HSCL' have reported additional delay of 7 months and 15 months due to delay in release of fund by Central Government. One project 'Construction of Paramedical and Allied Health Institute at Gulbarga, HSCL' has reported additional delay of 3 months (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- vi) In the **Urban Development Sector**, out of 30 projects, 12 projects are delayed. During the month, 2 projects have reported additional delay in the range of 4-12 months. The project 'Construction of Permanent Campus of IISER Kolkata at Haringhanta Kalyani Nadia, CPWD' has reported additional delay of 4 months due to slow progress of works. The project '2000 Boys Hostel (1000 Dounle Bedded Room) at ISM Dhanbad, CPWD' has reported additional delay of 12 months (however, no specific reason has been reported by the project implementing agency for the delay in these projects).
- vii) In the **Road Transport & Highways Sector**, out of 411 projects, 132 projects are delayed. During the month, 19 projects have reported additional delay in the range of 1-24 months. Four projects 'Guwhati to Nalbari (AS-4) NHAI', 'Dharamtul to Sonapur, km 205-183 (AS-20), NHAI', 'Brahmputra Bridge, NH no-31 NHAI' and 'Pimpalgaon-Nasik-Gonde, NH-3 (NHDP-Phase-III) NHAI' have reported additional delay of 1 month, Five projects 'Ganga Bridge to Ramdevi Crossing Ph.II NH-25, km.75-80.06 ,NHAI', 'Kota Bypass, RJ-4, NH-76, NHAI', '2 Lanning of

Mokama-Munger, NHAI', '2-Lanning With PS Khagaria-Purnea NHAI' and 'Patna-Baktzarpur km.181.3 to km.231.95, NHAI' projects have reported additional delay of 2 months, Two projects 'Sonapur to Guwahti (AS-3)NHAI' and 'Widening and Strengthening to 2-Lane With PS of Nimbi Jodha-Degana-Merta City Section NHAI' have reported additional delay of 3 months and 5 months respectively, two projects 'NH 79 of Chittorgarh Nee much MP Border km 183 000 to km 221 400 by Four Laning With Paved Shoulder, PWD' and '2-Laning With Paved Shoulders of Raebareli - Banda Section of NH-232, NHAI' have reported additional delay of 7 months and 8 months respectively, Two projects '2-Laning of Krishnagiri-Tindivanam (Approved Length 170 km), NHAI' and '2-Laning With Paved Shoulders of Tanda-Raebareli, NHAI' have reported additional delay of 9 months, Two projects '2 Laning With Paved Shoulder of Sitarganj - Tanakur Section of NH-125, NHAI' and '2-Laning With Paved Shoulder of Muzaffarpur-Barauni, NHAI' have reported additional delay of 12 months and 21 month respectively, Two projects '4 Laning of Ambala - Kaithal - Package -1 NHAI' and 'Four Laning of Hisar - Dabwali Section With PS-Package -2 NHAI' have reported additional delay of 24 months and 28 months respectively (however, no specific reason has been reported by the project implementing agency for the delay in these projects).

12. Ministry of Railways has **discontinued** the practice of furnishing monthly status reports on all its on-going (297) projects to this Ministry w.e.f 1st January 2015. The Ministry of Railways have provided latest information of their 20 projects only which have been identified to be monitored at MoSPI level. Therefore, the available information/data (**as on January 2015**) has been used in respect of remaining projects of Railways sector.

13. Ministry of Road Transport & Highways (MoRTH) & National Highways Authority of India (NHAI) had stopped providing data on their project w.e.f. June 2015. However, MoRTH & NHAI have voluntarily resumed updating of all their on-going projects from the month of February 2016 (Reporting month December 2015). Both MoRTH and NHAI have added 251 new projects under Road sector during reporting month of December 2015. This Ministry is separately classifying PPP/BOT projects as per information given by NHAI.


14. The status as on 31.01.2016 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

15. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	411	19
2	RAILWAYS	297	0
3	POWER	111	14
4	COAL	86	1
5	PETROLEUM	62	9
6	STEEL	33	6
7	URBAN DEVELOPMENT	30	2
8	HEALTH AND FAMILY WELFARE	9	0
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	2
11	CIVIL AVIATION	4	0
12	MINES	3	0
13	TELECOMMUNICATIONS	2	0
14	FERTILISERS	1	0
15	PETROCHEMICALS	1	0
16	HEAVY INDUSTRY	1	0
	Total	1063	53

Sectoral break up of on-going infrastructure projects

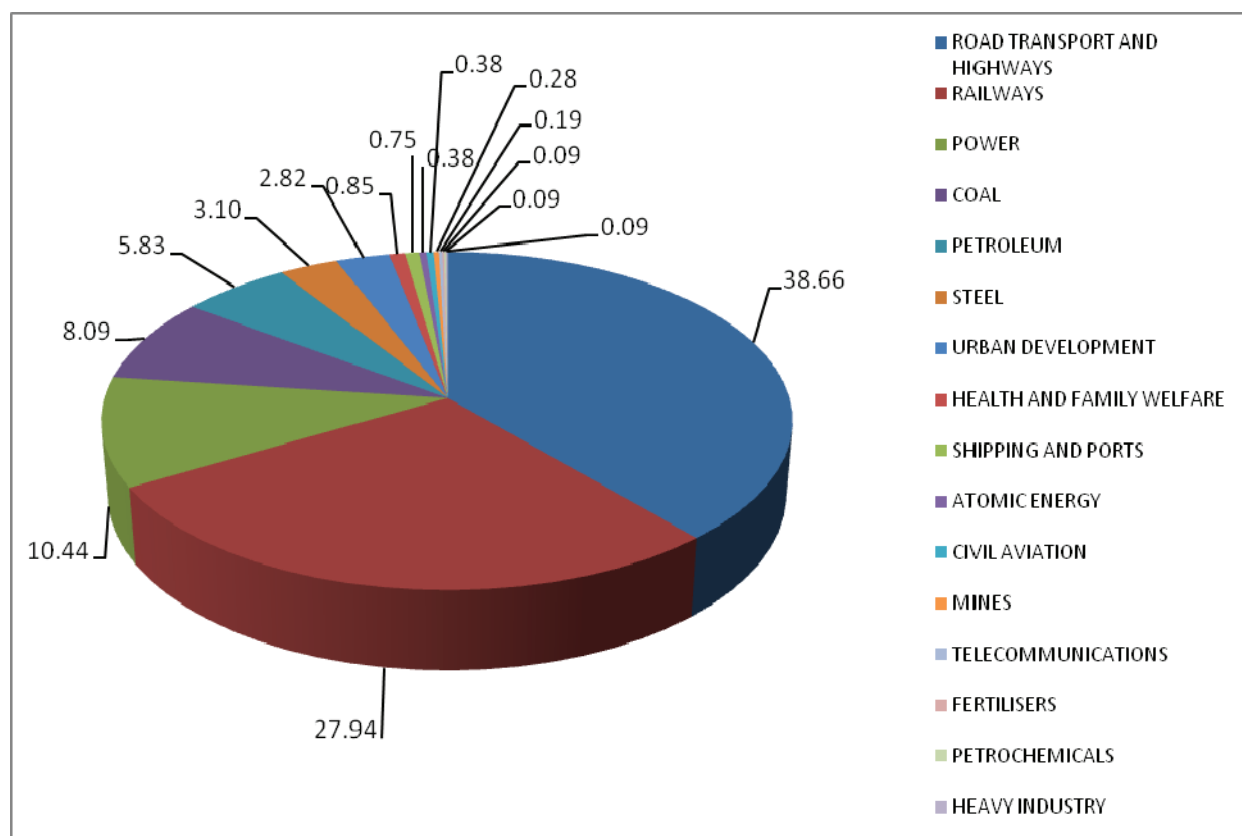

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00
	May,2015			
	<u>PETROLEUM</u>			
3	DEVELOPMENT OF B-193 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000033]	3,248.78	08/2010	5,933.42
4	DEVELOPMENT OF CLUSTER-7 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000104]	4,550.40	03/2013	2,583.55
5	PIPELINE REPLACEMENT PROJECT-3 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000137]	2,547.26	05/2014	1,412.08
	<u>POWER</u>			
6	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000127]	901.77	08/2014	945.20
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000136]	803.34	03/2015	593.19
	<u>TELECOMMUNICATIONS</u>			
8	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000062]	336.81	01/2009	199.37
	June,2015			
	<u>STEEL</u>			
9	EXPANSION OF DURGAPUR STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000074]	2,875.00	12/2012	2,640.00
10	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000075]	254.55	11/2013	135.89
	<u>POWER</u>			
11	KOLDAM HEP (NTPC) (NATIONAL THERMAL POWER CORPORATION) - [180100211]	4,527.15	04/2009	6,622.00

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000105]	1,366.34	12/2013	1,320.96
	<u>RAILWAYS</u>			
13	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) (NORTH EASTERN RAILWAY) - [220100255]	863.23	-	888.87
14	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR (NORTH EAST FRONTIER RAILWAY) - [220100315]	915.70	-	3,198.30
	July,2015			
	<u>STEEL</u>			
15	AUGMENTATION OF IRON ORE STORAGE IN RMHP (RASTRIYA ISPAT NIGAM LIMITED) - [N12000053]	480.00	09/2009	388.52
	<u>PETROLEUM</u>			
16	SURAT PARADIP PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000163]	10,281.00	04/2015	1.49
	<u>POWER</u>			
17	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000130]	1,263.26	11/2014	1,131.58
	August,2015			
	<u>CIVIL AVIATION</u>			
18	GAGAN PROJECT (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000065]	626.00	06/2013	483.53
	<u>COAL</u>			
19	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) (NEYVELI LIGNITE CORPORATION) - [060100087]	2,030.78	06/2009	3,215.91
20	TUTICORIN THERMAL POWER PROJECT- 2X500 MW (NEYVELI LIGNITE CORPORATION) - [N06000047]	4,904.54	03/2012	6,426.43
	<u>PETROLEUM</u>			
21	DEVELOPMENT OF G1 AND GS-15 (ONGCL) (OIL & NATURAL GAS CORPORATION LIMITED) - [160100231]	429.82	04/2006	3,439.38
22	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000098]	288.04	08/2012	229.16
23	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000123]	331.20	08/2013	190.04
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000156]	672.00	10/2011	1,082.12

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>POWER</u>			
25	BARH STPP STAGE -II (NATIONAL THERMAL POWER CORPORATION) - [N18000047]	7,341.04	10/2013	8,962.00
26	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000076]	4,672.99	11/2012	3,769.57
27	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000096]	2,569.25	03/2014	2,876.57
28	VINDHYACHAL STPP STAGE-V (NATIONAL THERMAL POWER CORPORATION) - [N18000134]	3,180.40	08/2015	2,042.00
	September,2015			
	<u>STEEL</u>			
29	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000018]	607.17	12/2011	394.89
30	EXPANSION OF BOKARO STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000055]	6,325.00	12/2011	5,256.65
	<u>PETROLEUM</u>			
31	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000132]	5,608.40	05/2015	4,457.47
	<u>POWER</u>			
32	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000124]	213.78	03/2014	204.54
33	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000154]	1,315.90	10/2016	632.97
34	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000156]	296.87	12/2014	318.66
	October,2015			
	<u>CIVIL AVIATION</u>			
35	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000070]	452.00	03/2015	449.41
	<u>STEEL</u>			
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) (RASTRIYA ISPAT NIGAM LIMITED) - [120100067]	8,692.00	10/2009	11,483.12
37	CAPTIVE POWER PLANT - 2 (RASTRIYA ISPAT NIGAM LIMITED) - [N12000087]	677.00	09/2013	537.19

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
38	102 MW WIND POWER PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000119]	1,106.00	06/2012	437.69
	<u>POWER</u>			
39	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) (POWER GRID CORPORATION OF INDIA LIMITED) - [180100246]	588.25	12/2007	1,020.81
40	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000093]	2,743.19	12/2013	2,827.00
	<u>URBAN DEVELOPMENT</u>			
41	FARIDABAD EXTENSION (DELHI METRO RAIL CORPORATION LTD) - [N28000057]	2,494.00	09/2014	1,311.53
	November, 2015			
	<u>POWER</u>			
42	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID (POWER GRID CORPORATION OF INDIA LIMITED) - [N16000144]	1,508.74	03/2015	1,211.48
	December, 2015			
	<u>CIVIL AVIATION</u>			
43	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS (AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000072]	344.28	03/2014	80.60
	<u>COAL</u>			
44	CHURCHA ROUG(1.35MTY) (SOUTH-EASTERN COAL FIELDS LIMITED) - [N06000046]	462.35	03/2014	497.01
	<u>PETROLEUM</u>			
45	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000142]	1,419.00	12/2014	1,291.63
46	REWARI KANPUR PIPELINE PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000145]	1,210.64	11/2015	1,249.03
47	MARKETING TERMINAL AT PARADEEP (INDIAN OIL CORPORATION LIMITED) - [N16000168]	199.75	07/2013	211.72
48	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000182]	429.06	10/2014	439.02
	<u>POWER</u>			
49	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000160]	243.53	08/2016	185.63

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>SHIPPING AND PORTS</u>			
50	ACQUISITION OF TWO (2) NOS OF 317000 DWT VLCC'S FROM JIANGSU RONGSHENG HEAVY INDUSTRIES CO.LTD.,CHIN(SHIPPING CRP. OF INDIA) - [N25000064]	994.82	11/2013	427.54
	<u>TELECOMMUNICATIONS</u>			
51	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS (BHARAT SANCHAR NIGAM LIMITED) - [N26000096]	384.00	10/2010	74.74
	January,2016			
	<u>COAL</u>			
52	BLOCK-B OCP NCL (3.5 MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000009]	746.04	03/2015	550.32
	<u>STEEL</u>			
53	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000079]	237.09	12/2014	221.88
54	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000080]	313.05	06/2015	319.91
55	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000082]	160.48	09/2014	143.89
	<u>POWER</u>			
56	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000087]	2,074.86	03/2013	1,975.94
	<u>URBAN DEVELOPMENT</u>			
57	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000078]	2,727.89	03/2010	0.01

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2015			
	<u>PETROLEUM</u>			
1	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000103]	723.64	03/2013	.00
2	AHMEDABAD REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000120]	1,916.10	12/2014	1,160.14
3	MEHESANA REDEVELOPMENT PROJECT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000121]	3,823.00	04/2015	1,076.57
4	ANKLESWAR REDEVELOPMENT (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000122]	2,189.63	12/2014	1,034.30
5	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	.47
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000181]	2,913.10	05/2016	13.86
	June,2015			
7	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	122.87
	<u>TELECOMMUNICATIONS</u>			
8	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES (BHARAT SANCHAR NIGAM LIMITED) - [N26000065]	1,077.00	03/2009	.00
	August,2015			
	<u>SHIPPING AND PORTS</u>			
9	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21
10	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	October,2015			
	<u>PETROLEUM</u>			
11	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>SHIPPING AND PORTS</u>			
12	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 (PORT TRUST) - [N25000050]	277.00	03/2012	.21

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS(PORT TRUST) - [N25000060]	830.00	05/2013	.00
	December,2015			
	<u>PETROLEUM</u>			
14	INTEGRATED DEVELOPMENT OF BASSEIN FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000160]	3,513.07	02/2016	667.40
15	IMPROVED OIL RECOVERY OF B-173A FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000185]	352.49	03/2014	.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
16	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000270]	297.78	02/2015	37.72
17	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN(PUBLIC WORKS DEPT OF STATE) - [N24000271]	297.78	02/2015	37.72
18	REHABILITATION & UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN T(PUBLIC WORKS DEPT OF STATE) - [N24000285]	297.78	02/2015	37.72
19	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(PUBLIC WORKS DEPT OF STATE) - [N24000400]	282.41	08/2016	.00
	<u>SHIPPING AND PORTS</u>			
20	CONSTRUCTION AND DEVELOPMENT OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL (MUMBAI PORT TRUST) - [N25000016]	1,228.00	12/2010	1,038.00


Summary of projects in the Flash Report for the month of January, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1059
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects Added in Current Month	10
Number of Projects in Current Month	1063


Brief Analysis

Project Status with respect to Original Schedule: Out of 1063 projects, 7 projects are ahead of schedule, 253 projects are on schedule 346 projects are delayed. 422 projects do not have fixed dates of commissioning. 35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

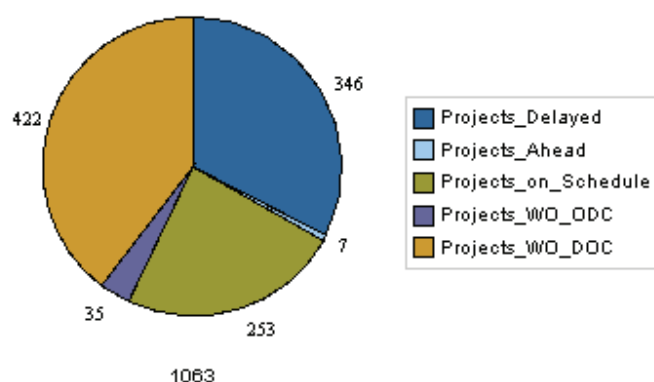

Investment Scenario

Total original cost of implementation of 1063 projects when sanctioned, was of the order of Rs. 1178671.5 crore but this was subsequently revised to Rs. 1395087.12 crore implying a cost overrun of 18.4%. The expenditure incurred on these projects till January, 2016 is Rs. 552163.36 crore, which is 39.6% of the revised cost of the projects.

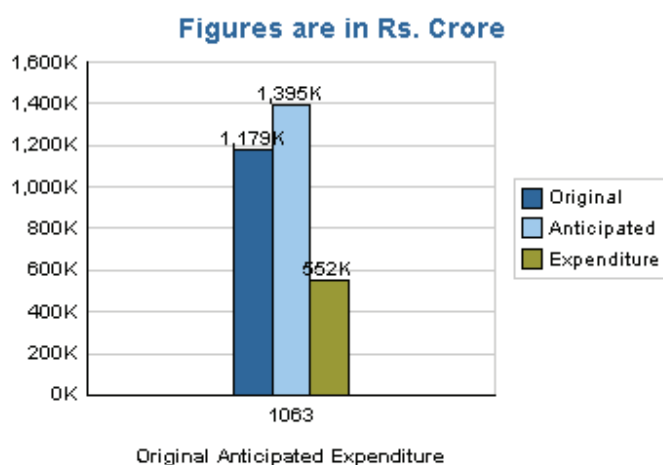

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1059
No of Projects Completed/Dropped/Frozen in Current Month	6
No of Projects added in Current Month	10
No of Projects in Current Month	1063

Project status

Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	346	7	253	35	422	1063	32.55
Latest Approved (Date)	310	9	287	35	422	1063	29.16

Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	932	9,50,592.09	10,50,339.16	3,57,377.16	34.00	99,747.07	10.50
Project with Revision in Cost	131	3,03,153.74	3,44,747.96	1,94,786.20	56.50	41,594.22	13.70
Total	1,063	12,53,745.83	13,95,087.12	5,52,163.36	39.58	141341.29	11.27
Original Cost of All Projects							
Original Cost	1063	11,78,671.50	13,95,087.12	5,52,163.36	39.58	2,16,415.62	18.36

Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	346	584,806.34	707,516.53	407,155.09	57.50	122,710.19	21.00
Latest Approved (RCE)	310	526,296.19	590,459.53	362,600.39	61.40	64,163.34	12.20

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	53	91,993.65	98,489.70	69,835.86	70.90	6,496.05	7.10
Total	53	91,993.65	98,489.70	69,835.86	70.91	6496.05	7.06

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	68.87
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	86	60,889.41	62,002.14	1.83	5	1,800.69	3,170.48	76.07
4	FERTILISERS	1	197.79	209.44	5.89	1	197.79	209.44	5.89
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	33	53,859.49	54,375.39	0.96	7	2,218.50	2,734.40	23.25
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	62	130,718.16	140,226.81	7.27	16	63,409.10	74,805.00	17.97
9	POWER	111	304,580.02	353,098.54	15.93	22	61,522.84	110,104.97	78.97
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	297	172,717.67	301,331.54	74.46	161	82,833.35	214,601.52	159.08
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,608.22	0.98	18	5,171.67	7,634.21	47.62
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	4	1,006.56	1,937.62	92.50
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	30	134,055.93	141,505.81	5.56	1	6,395.00	13,845.01	116.50
Total		1063	1,178,671.50	1,395,087.12	18.36	240	248,614.71	471,218.05	89.54

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	5	1,263.14	3,108.40	146.09
2	ARUNACHAL PRADESH	14	11,758.70	28,030.85	138.38	5	9,616.85	25,889.00	169.20
3	ASSAM	50	28,795.71	44,499.05	54.53	14	15,918.17	31,722.22	99.28
4	BIHAR	64	57,872.84	72,327.53	24.98	15	13,737.73	28,920.47	110.52
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	0.00
6	GUJARAT	30	30,410.18	31,464.82	3.47	6	3,425.92	4,607.88	34.50
7	HARYANA	20	13,986.73	15,957.35	14.09	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,966.47	11,365.75	128.85
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	2	6,142.04	25,751.47	319.27
10	KARNATAKA	41	71,364.99	88,854.89	24.51	19	14,794.54	32,290.60	118.26
11	KERALA	16	25,825.82	30,300.97	17.33	8	17,335.36	21,810.51	25.82
12	MADHYA PRADESH	51	53,839.16	55,730.39	3.51	5	2,404.35	5,184.88	115.65
13	MAHARASHTRA	71	113,215.47	121,988.42	7.75	12	17,419.89	27,446.77	57.56
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	1	4,083.02	5,307.90	30.00
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	325.27
17	NAGALAND	3	6,420.00	8,757.12	36.40	2	5,124.00	7,461.12	45.61
18	ODISHA	47	71,450.12	80,688.91	12.93	13	33,644.42	42,904.55	27.52
19	PUNJAB	23	11,714.51	11,718.51	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	58	39,924.61	40,467.55	1.36	7	2,884.16	3,512.63	21.79
21	SIKKIM	5	2,149.08	4,999.32	132.63	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	57	68,769.74	88,418.98	28.57	21	23,753.56	43,402.80	82.72
23	TRIPURA	9	3,776.07	7,486.36	98.26	7	2,909.18	6,619.47	127.54
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	8	2,576.25	6,510.63	152.72
25	WEST BENGAL	45	49,327.99	62,739.51	27.19	13	8,617.64	24,280.63	181.76
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	16	49,963.05	49,963.05	0.00	0	0.00	0.00	0.00
28	CHHATISGARH	41	88,369.18	89,646.53	1.45	5	3,343.98	4,621.63	38.21
29	JHARKHAND	44	41,826.84	44,389.67	6.13	7	3,739.10	6,343.67	69.66
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	3	4,855.31	7,155.13	47.37
31	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	0.00	0	0.00	0.00	0.00
32	TELANGANA	31	11,908.91	14,943.51	25.48	9	2,836.21	5,870.81	106.99
33	MULTI STATE	176	188,850.62	220,269.11	16.64	43	37,960.80	69,957.24	84.29
Total		1063	1,178,671.50	1,395,087.12	18.36	240	248,614.71	471,218.05	89.54

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	86	60,889.41	62,002.14	1.83	44	26,217.62	27,539.15	3 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	33	53,859.49	54,375.39	0.96	17	40,121.06	40,612.49	2 - 39
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	62	130,718.16	140,226.81	7.27	36	76,753.21	84,335.99	1 - 71
9	POWER	111	304,580.02	353,098.54	15.93	59	161,177.43	197,765.42	2 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	3	779.77	779.77	3 - 28
12	RAILWAYS	297	172,717.67	301,331.54	74.46	31	37,310.20	91,038.32	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,608.22	0.98	132	93,364.12	95,190.05	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61 - 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	30	134,055.93	141,505.81	5.56	12	88,550.24	96,000.12	8 - 60
Total		1063	1,178,671.50	1,395,087.12	18.36	346	584,806.34	707,516.53	

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	47	21,226.93	23,061.97	8.64	18	9,281.00	9,426.40	5 - 39
2	ARUNACHAL PRADESH	14	11,758.70	28,030.85	138.38	2	3,070.89	7,348.11	35 - 78
3	ASSAM	50	28,795.71	44,499.05	54.53	25	15,059.37	25,717.56	15 - 138
4	BIHAR	64	57,872.84	72,327.53	24.98	17	25,531.79	35,287.78	5 - 90
5	GOA	8	3,925.48	3,907.87	-0.45	0	0.00	0.00	-
6	GUJARAT	30	30,410.18	31,464.82	3.47	10	19,719.19	19,699.50	3 - 42
7	HARYANA	20	13,986.73	15,957.35	14.09	5	3,130.20	4,310.20	14 - 69
8	HIMACHAL PRADESH	5	8,088.55	14,487.83	79.12	2	4,190.42	8,669.59	16 - 111
9	JAMMU AND KASHMIR	9	25,620.25	45,229.68	76.54	6	13,202.50	32,811.93	10 - 181
10	KARNATAKA	41	71,364.99	88,854.89	24.51	11	51,309.27	59,717.48	2 - 60
11	KERALA	16	25,825.82	30,300.97	17.33	4	2,462.73	3,434.08	4 - 88
12	MADHYA PRADESH	51	53,839.16	55,730.39	3.51	11	7,987.62	7,797.59	2 - 87
13	MAHARASHTRA	71	113,215.47	121,988.42	7.75	21	40,712.64	45,798.11	1 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	6	6,970.03	8,194.91	17.57	2	687.33	687.33	2 - 29
16	MIZORAM	6	2,188.16	5,402.06	146.88	2	988.06	4,201.96	47 - 123
17	NAGALAND	3	6,420.00	8,757.12	36.40	1	850.00	2,973.42	60 - 60
18	ODISHA	47	71,450.12	80,688.91	12.93	16	36,085.96	41,288.42	4 - 91
19	PUNJAB	23	11,714.51	11,718.51	0.03	0	0.00	0.00	-
20	RAJASTHAN	58	39,924.61	40,467.55	1.36	14	21,464.28	21,505.47	4 - 89
21	SIKKIM	5	2,149.08	4,999.32	132.63	2	1,648.94	4,499.46	51 - 80
22	TAMIL NADU	57	68,769.74	88,418.98	28.57	20	52,247.00	64,581.03	5 - 120
23	TRIPURA	9	3,776.07	7,486.36	98.26	5	2,454.57	5,505.82	7 - 108
24	UTTAR PRADESH	60	52,378.07	56,264.19	7.42	17	18,880.35	18,982.73	7 - 102
25	WEST BENGAL	45	49,327.99	62,739.51	27.19	17	31,897.56	40,299.35	3 - 177
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	1	6,086.08	6,086.08	10 - 10
27	DELHI	16	49,963.05	49,963.05	0.00	5	40,580.86	40,580.86	3 - 37
28	CHHATISGARH	41	88,369.18	89,646.53	1.45	17	57,227.38	57,770.08	7 - 93
29	JHARKHAND	44	41,826.84	44,389.67	6.13	18	8,850.62	11,048.85	3 - 104
30	UTTARAKHAND	6	9,352.40	11,651.71	24.59	4	7,605.57	9,794.74	33 - 78
31	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	0.00	0	0.00	0.00	-
32	TELANGANA	31	11,908.91	14,943.51	25.48	13	4,422.52	5,748.91	8 - 132
33	MULTI STATE	176	188,850.62	220,269.11	16.64	59	96,444.08	105,372.94	1 - 261
Total		1063	1,178,671.50	1,395,087.12	18.36	346	584,806.34	707,516.53	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	4	40,442.00	51,918.00	35 - 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	309.46	309.46	80 - 80
3	COAL	86	60,889.41	62,002.14	1.83	41	18,820.84	19,915.20	3 - 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	-
5	MINES	3	2,555.63	1,875.63	-26.61	1	1,856.00	1,176.00	31 - 31
6	STEEL	33	53,859.49	54,375.39	0.96	16	24,596.06	25,087.49	2 - 39
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	62	130,718.16	140,226.81	7.27	22	53,540.22	59,401.27	1 - 71
9	POWER	111	304,580.02	353,098.54	15.93	51	141,833.18	167,744.05	2 - 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	3	779.77	779.77	3 - 28
12	RAILWAYS	297	172,717.67	301,331.54	74.46	29	31,160.20	80,078.86	3 - 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,608.22	0.98	126	92,094.39	93,828.37	1 - 138
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61 - 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	20 - 30
16	URBAN DEVELOPMENT	30	134,055.93	141,505.81	5.56	10	61,919.29	69,369.30	8 - 60
Total		1063	1,178,671.50	1,395,087.12	18.36	310	485,276.64	590,459.53	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	44,541.00	51,918.00	16.56	2	20,762.00	28,139.00	35.53
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	1	217.60	244.10	12.18
3	COAL	86	61,931.69	62,002.14	0.11	2	898.50	969.25	7.87
4	FERTILISERS	1	209.44	209.44	0.00	0	0.00	0.00	0.00
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0.00
6	STEEL	33	54,229.99	54,375.39	0.27	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,965.00	11.72	1	8,920.00	9,965.00	11.72
8	PETROLEUM	62	137,522.60	140,226.81	1.97	5	15,900.77	18,756.55	17.96
9	POWER	111	332,674.70	353,098.54	6.14	7	28,130.34	48,554.18	72.60
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0.00
12	RAILWAYS	297	197,803.64	301,331.54	52.34	150	83,693.36	190,591.39	127.73
13	ROAD TRANSPORT AND HIGHWAYS	411	248,924.94	250,608.22	0.68	13	3,887.63	5,884.15	51.36
14	SHIPPING AND PORTS	8	4,258.80	5,048.81	18.55	4	1,147.61	1,937.62	68.84
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	30	139,269.80	141,505.81	1.61	1	11,609.00	13,845.01	19.26
Total		1063	1,253,745.83	1,395,087.12	11.27	188	177,227.81	323,201.95	82.37

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	0	0.00	0.00	0- 0
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	86	60,889.41	62,002.14	1.83	1	259.40	486.57	60- 60
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	33	53,859.49	54,375.39	0.96	0	0.00	0.00	0- 0
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	62	130,718.16	140,226.81	7.27	6	8,628.64	10,878.98	4- 35
9	POWER	111	304,580.02	353,098.54	15.93	6	18,370.80	28,404.36	35- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	297	172,717.67	301,331.54	74.46	1	5,300.00	7,986.04	60- 60
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,608.22	0.98	2	425.61	517.56	77- 105
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	30	134,055.93	141,505.81	5.56	0	0.00	0.00	0- 0
Total		1063	1178671.5	1395087.12	18.36	16	32984.45	48273.51	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	51,918.00	28.38	2	16,663.00	28,139.00	72- 89
2	CIVIL AVIATION	4	1,177.28	1,186.17	0.76	0	0.00	0.00	0- 0
3	COAL	86	60,889.41	62,002.14	1.83	5	1,800.69	3,170.48	24- 132
4	FERTILISERS	1	197.79	209.44	5.89	0	0.00	0.00	0- 0
5	MINES	3	2,555.63	1,875.63	-26.61	0	0.00	0.00	0- 0
6	STEEL	33	53,859.49	54,375.39	0.96	5	1,761.97	2,253.40	3- 25
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	62	130,718.16	140,226.81	7.27	11	41,311.99	49,923.98	4- 53
9	POWER	111	304,580.02	353,098.54	15.93	20	54,750.02	91,401.62	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	0.00	0	0.00	0.00	0- 0
12	RAILWAYS	297	172,717.67	301,331.54	74.46	26	22,458.31	77,795.14	3- 261
13	ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	250,608.22	0.98	8	2,586.46	4,438.02	55- 90
14	SHIPPING AND PORTS	8	4,117.75	5,048.81	22.61	3	762.06	1,679.29	61- 120
15	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	30	134,055.93	141,505.81	5.56	1	6,395.00	13,845.01	60- 60
Total		1063	1178671.5	1395087.12	18.36	82	150207.5	276473.24	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>COAL</u>						
1	BLOCK-B OCP NCL (3.5 MTY)	06/2011	746.04	03/2015	535.10	03/2016	550.32
	<u>POWER</u>						
2	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	09/2010	2,074.86	03/2013	2,348.37	01/2016	1,975.94
	<u>STEEL</u>						
3	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	10/2012	160.48	09/2014	160.48	01/2016	143.89
4	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B	11/2012	313.05	06/2015	313.05	01/2016	319.91
5	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	06/2012	237.09	12/2014	237.09	01/2016	221.88
	<u>URBAN DEVELOPMENT</u>						
6	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	2,727.89	03/2010	2,727.89	01/2016	.01

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	DIESEL HYDROTREATOR	7/2015	1,031.37	1/2018	1,031.37	1/2018
2	50 MW 10 PERSENT WIND ENERGY POWER PROJECT	11/2015	500.00	3/2017	500.00	3/2017
3	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	310.00	3/2013	370.00	10/2016
	<u>POWER</u>					
4	KHARGONE STPP STAGE I (1320 MW)	3/2015	9,870.51	9/2019	9,870.51	9/2019
5	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	305.04	3/2017	305.04	3/2017
6	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A)	1/2016	244.19	7/2018	244.19	7/2018
7	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	1,455.47	7/2018	1,455.47	7/2018
8	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM	1/2016	162.11	5/2018	162.11	5/2018
9	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS	1/2016	207.88	7/2018	207.88	7/2018
10	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS	1/2016	187.04	6/2018	187.04	6/2018

Milestones (Cumulative due & achieved)

Total	3862
Achieved up to month	1771


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 NPCIL	11,459.00	11,459.00	12/2015	10/2017	11/2018	13
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) NPCIL	12,320.00	12,320.00	12/2016	05/2018	12/2019	19
	<u>COAL</u>						
3	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2016	03/2017	12
	<u>STEEL</u>						
4	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS RINL	877.73	877.73	07/2015	06/2016	08/2016	2
5	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP HSCL	151.33	151.33	09/2017	09/2017	11/2017	2
6	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA HSCL	324.87	325.00	12/2015	12/2015	03/2016	3
7	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII HSCL	787.29	787.29	12/2016	12/2016	03/2017	3
8	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII HSCL	175.49	207.00	12/2016	12/2016	07/2017	7
9	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V HSCL	149.73	173.00	12/2015	12/2015	03/2017	15
	<u>PETROLEUM</u>						
10	PARADIP REFINERY PROJECT IOCL	29,777.00	34,555.00	11/2012	01/2016	02/2016	1
11	MOUNDED BULLET PROJECT AT CPCL	279.00	279.00	12/2014	01/2016	02/2016	1
12	PARADIP-RAIPUR- RANCHI PIPELINE IOCL	1,793.00	1,793.00	09/2012	03/2016	05/2016	2
13	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY IOCL	160.00	160.00	02/2016	03/2016	05/2016	2
14	LPG TERMINAL AT KOCHI IOCL	607.06	714.25	10/2017	10/2017	02/2018	4

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
15	RESID UPGRADATION PROJECT CPCL	3,110.36	3,110.36	11/2015	07/2016	11/2016	4
16	PARADIP LPG IMPORT FACILITY IOCL	690.00	690.00	07/2018	07/2018	12/2018	5
17	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY CPCL	257.87	257.87	11/2016	11/2016	04/2017	5
18	DEVELOPMENT OF C-26 CLUSTER FIELDS ONGC	2,592.17	2,592.17	05/2014	05/2016	03/2017	10
	<u>POWER</u>						
19	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	01/2016	02/2016	1
20	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI PGCIL	1,677.57	1,677.57	04/2013	01/2016	02/2016	1
21	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 PGCIL	2,422.66	2,422.66	08/2014	02/2016	03/2016	1
22	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,927.16	10/2014	02/2016	03/2016	1
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	05/2015	02/2016	03/2016	1
24	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW NHPC	302.49	302.49	02/2016	01/2016	02/2016	1
25	EASTERN REGION STRENGTHENING SCHEME-V PGCIL	1,364.52	1,364.52	04/2016	04/2016	06/2016	2
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) NHPC	1,061.38	2,193.08	09/2009	06/2016	09/2016	3
27	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER PGCIL	4,404.57	4,404.57	01/2015	12/2016	03/2017	3
28	EASTERN REGION STRENGTHENING SCHEME-III PGCIL	1,272.80	1,272.80	11/2012	12/2016	03/2017	3
29	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV PGCIL	680.69	680.69	03/2016	03/2016	06/2016	3
30	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	02/2016	06/2016	4
31	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS PGCIL	167.40	167.40	12/2015	12/2015	05/2016	5


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	738.48	09/2010	06/2016	12/2016	6
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
33	GUWHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	07/2016	08/2016	1
34	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	07/2016	08/2016	1
35	BRAHMPUTRA BRIDGE, NH NO-31 NHAI	217.61	309.56	04/2010	08/2016	09/2016	1
36	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) NHAI	940.00	940.00	07/2012	03/2016	04/2016	1
37	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	01/2016	03/2016	2
38	KOTA BYPASS, RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	01/2016	03/2016	2
39	2 LANNING OF MOKAMA-MUNGER NHAI	351.54	351.54	05/2013	01/2016	03/2016	2
40	2-LANNING WITH PS KHAGARIA-PURNEA NHAI	664.00	664.00	02/2014	01/2016	03/2016	2
41	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 NHAI	574.00	574.00	03/2014	01/2016	03/2016	2
42	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	04/2016	07/2016	3
43	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION NHAI	368.15	368.15	01/2016	01/2016	06/2016	5
44	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A PWD	511.00	511.00	10/2013	03/2013	10/2013	7
45	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 NHAI	351.34	351.34	01/2016	01/2016	09/2016	8
46	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) NHAI	624.00	624.00	04/2014	03/2016	12/2016	9
47	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI NHAI	495.78	495.78	01/2016	01/2016	10/2016	9
48	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 NHAI	368.73	368.73	09/2016	09/2016	09/2017	12
49	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI NHAI	356.40	356.40	07/2014	03/2016	12/2017	21

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
50	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 NHAI	602.95	602.95	06/2016	06/2016	06/2018	24
51	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 NHAI	867.66	867.66	11/2015	01/2016	05/2018	28
	URBAN DEVELOPMENT						
52	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	09/2015	12/2016	04/2017	4
53	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD CPWD	171.86	171.86	03/2016	05/2016	05/2017	12

Graphical Presentation of All Projects w.r.t. Original Schedule

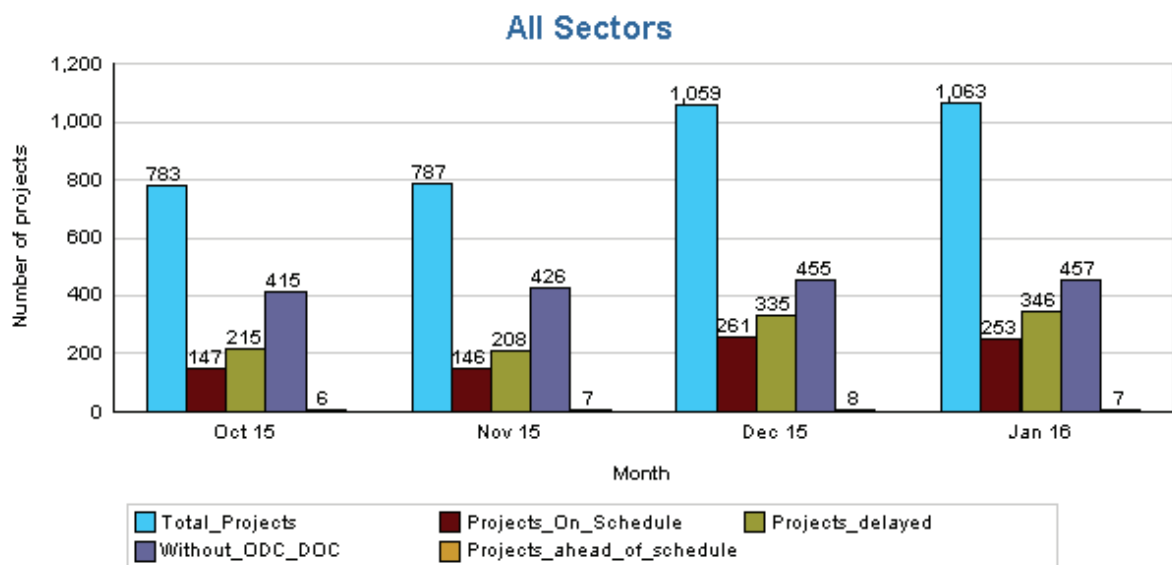


Break-up of 346 Delayed projects in January 2016

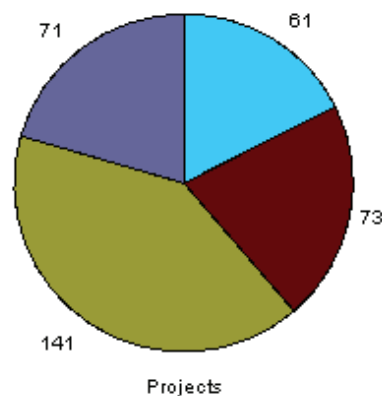


Delay in Months: ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

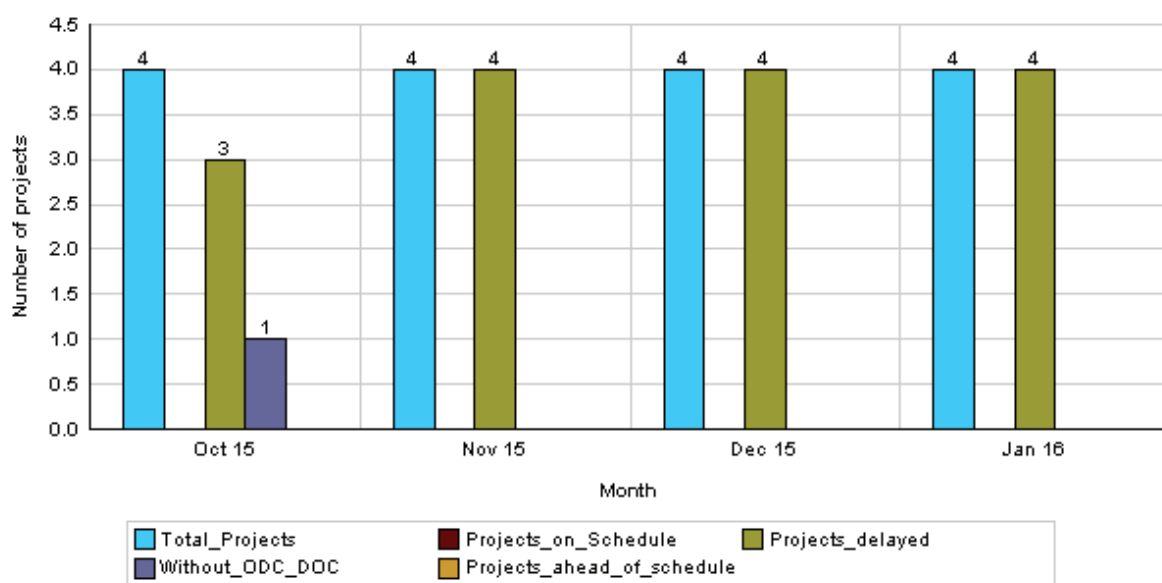


Break-up of 4 Delayed projects in January 2016

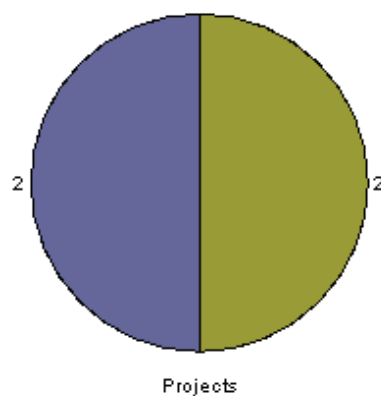


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of CIVIL AVIATION Sector

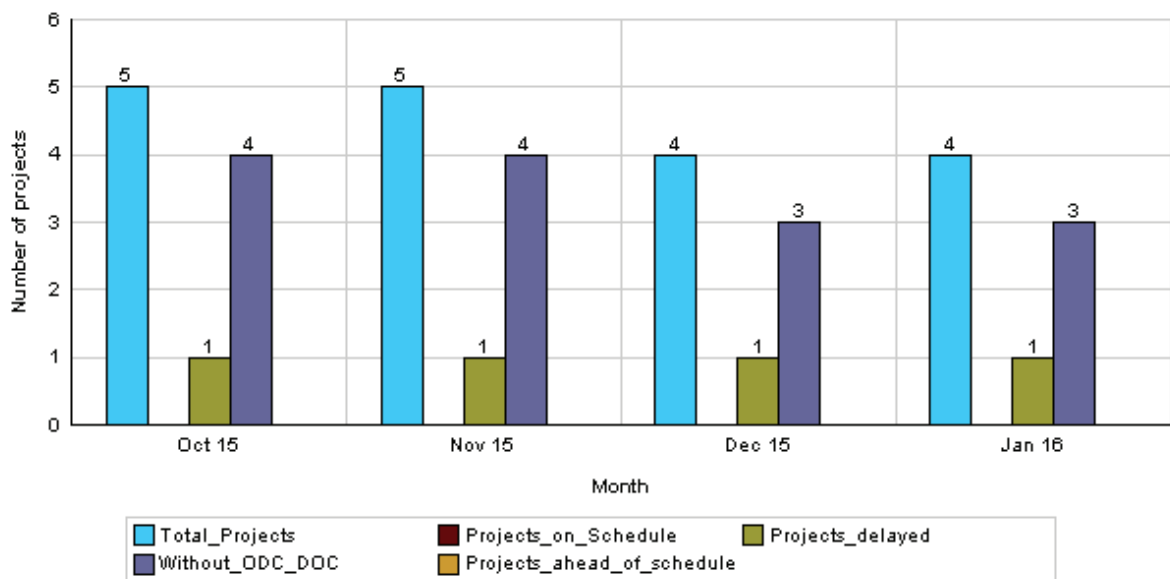


Break-up of 1 Delayed projects in January 2016

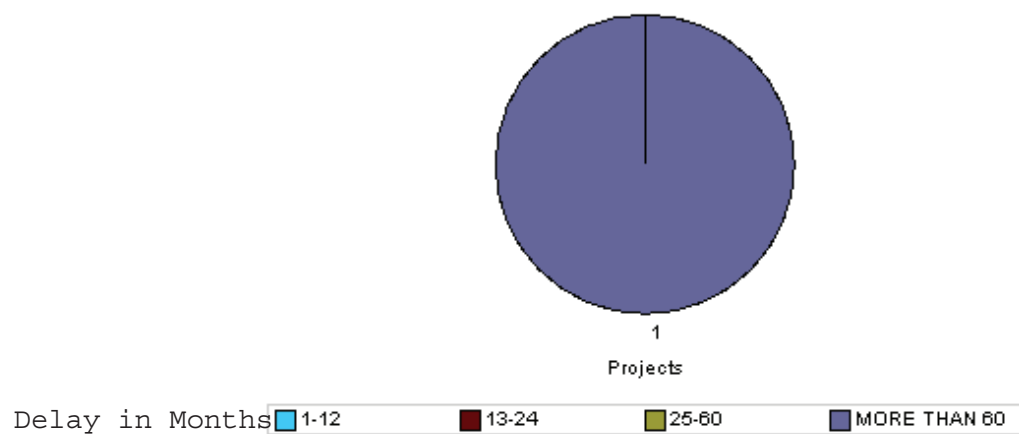

Graphical Presentation of COAL Sector

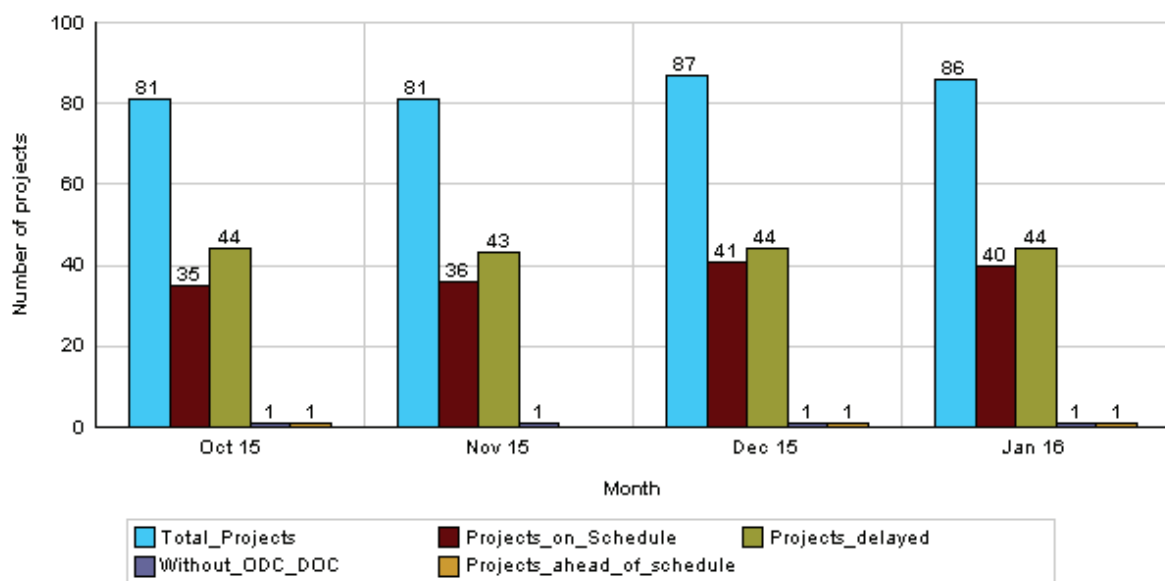


Break-up of 44 Delayed projects in January 2016

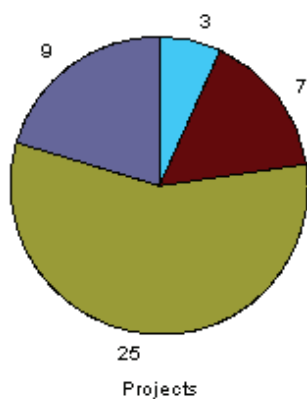


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of STEEL Sector

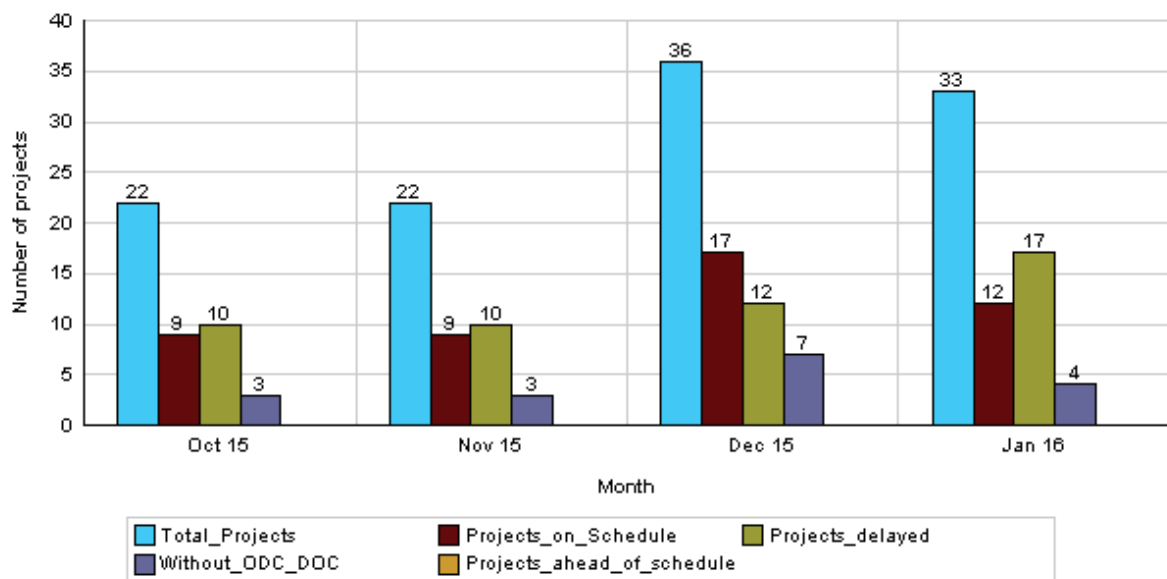


Break-up of 17 Delayed projects in January 2016

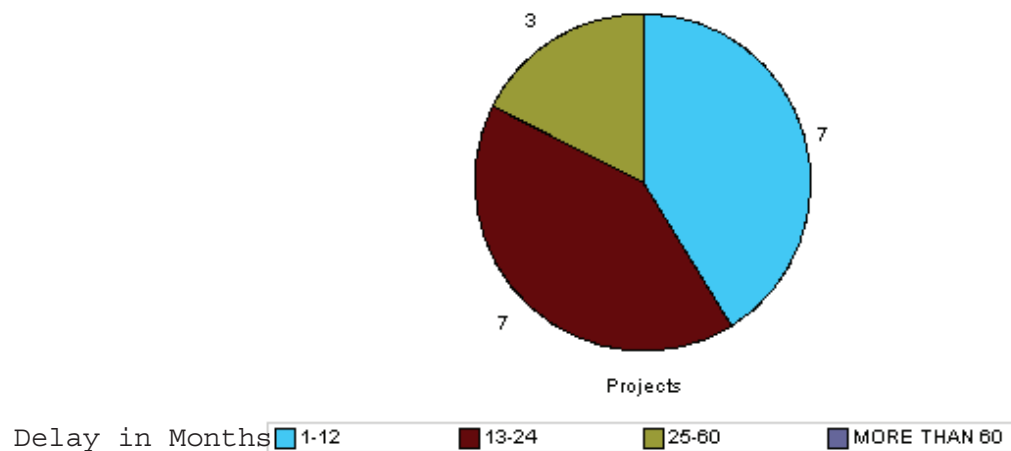

Graphical Presentation of PETROLEUM Sector

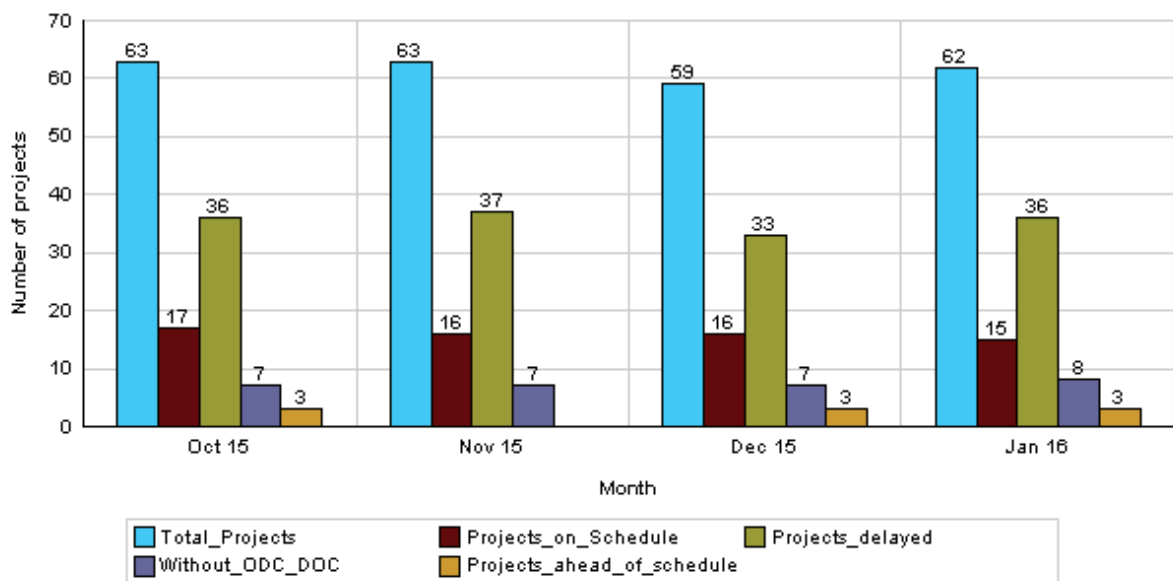


Break-up of 36 Delayed projects in January 2016

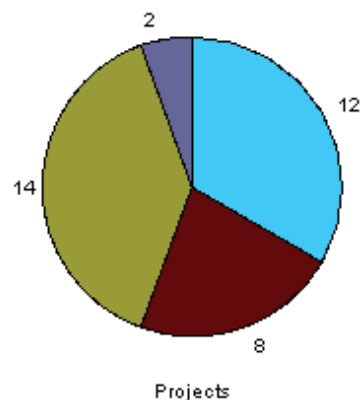


Delay in Months: 1-12, 13-24, 25-60, MORE THAN 60


Graphical Presentation of POWER Sector

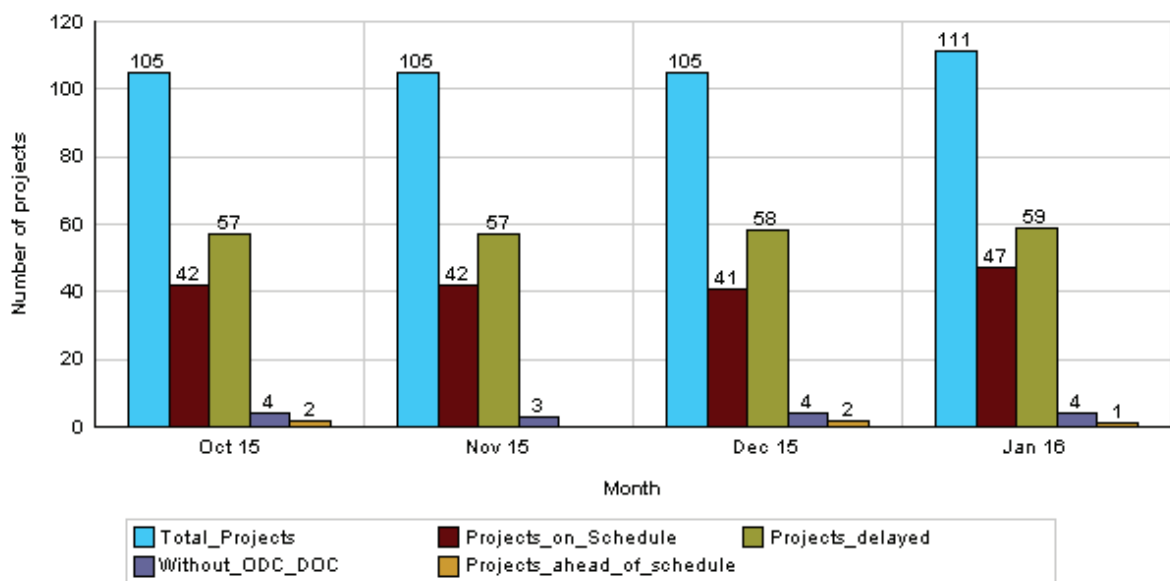


Break-up of 59 Delayed projects in January 2016

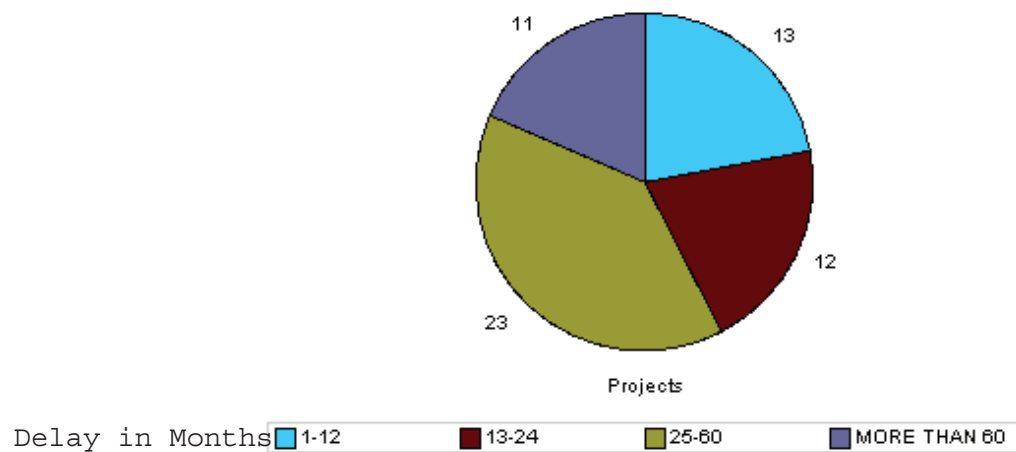

Graphical Presentation of RAILWAYS Sector

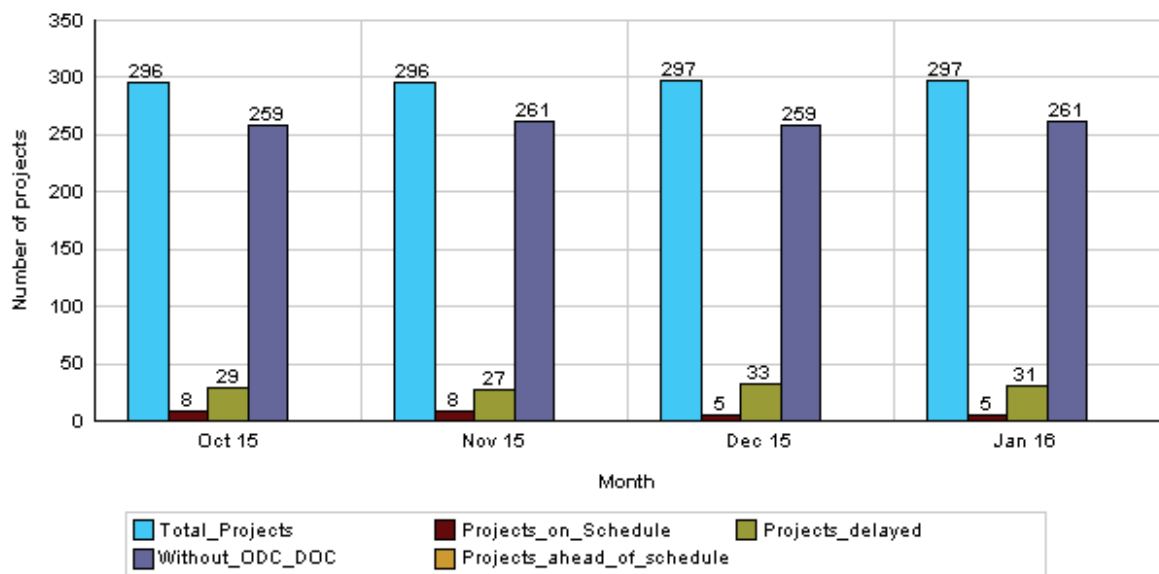


Break-up of 31 Delayed projects in January 2016

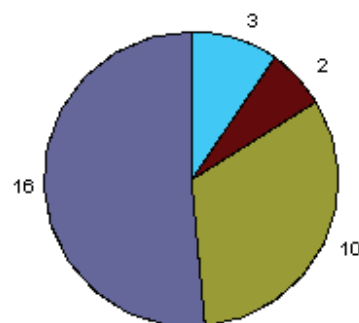


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

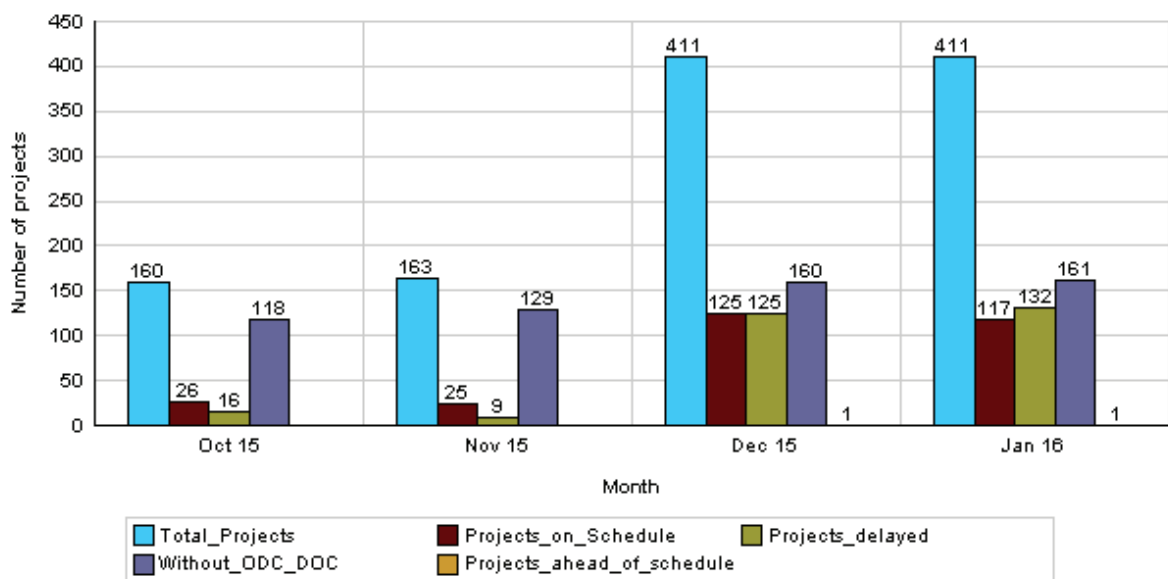


Break-up of 132 Delayed projects in January 2016

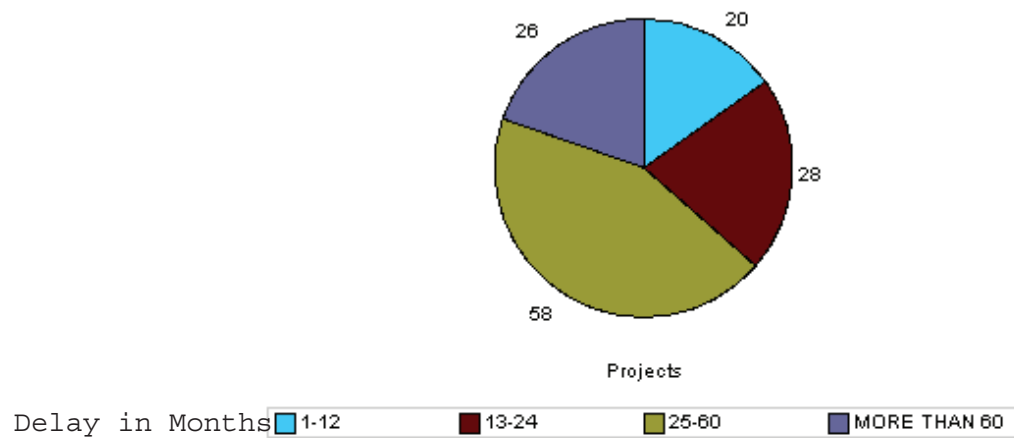


Graphical Presentation of SHIPPING AND PORTS Sector

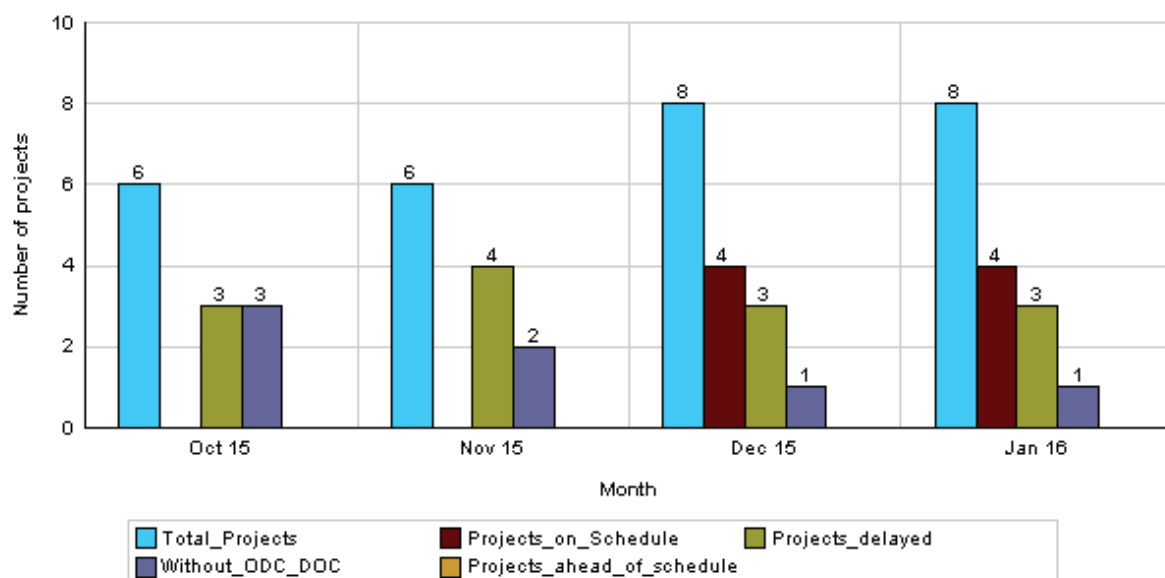


Break-up of 3 Delayed projects in January 2016

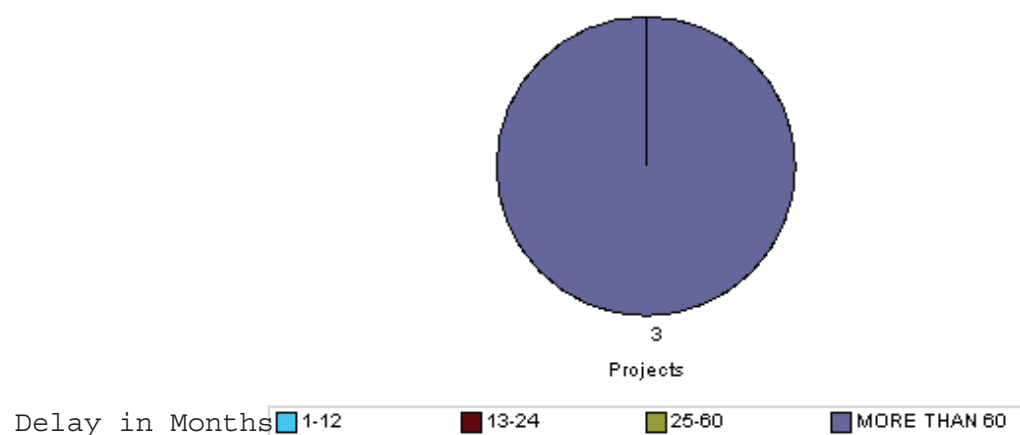


Graphical Presentation of SHIPPING AND PORTS Sector

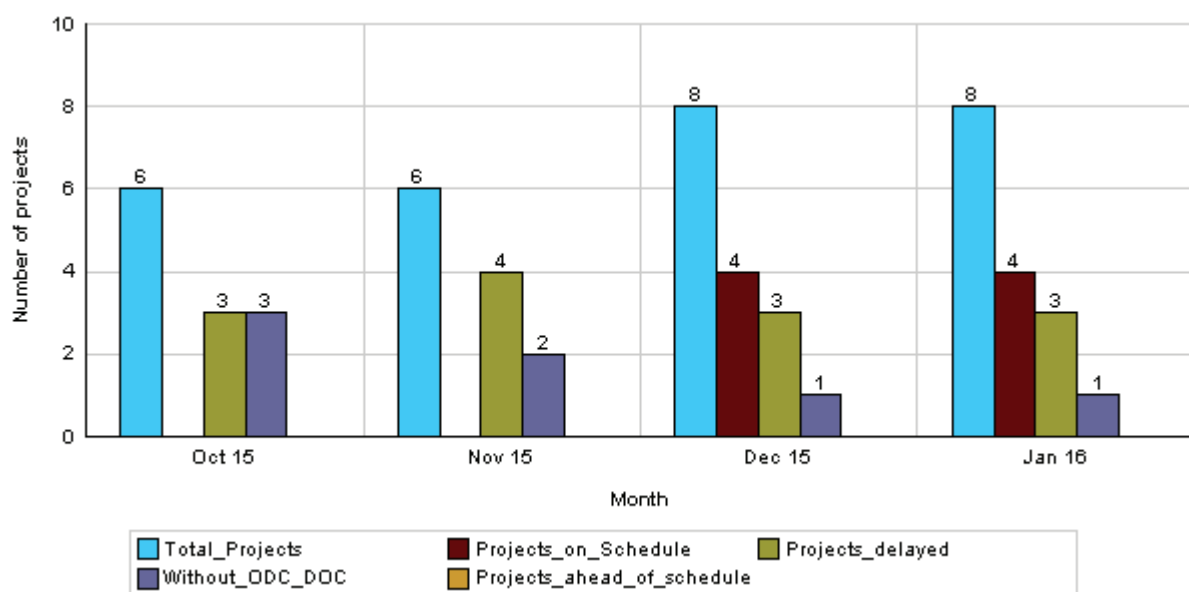


Break-up of 3 Delayed projects in January 2016

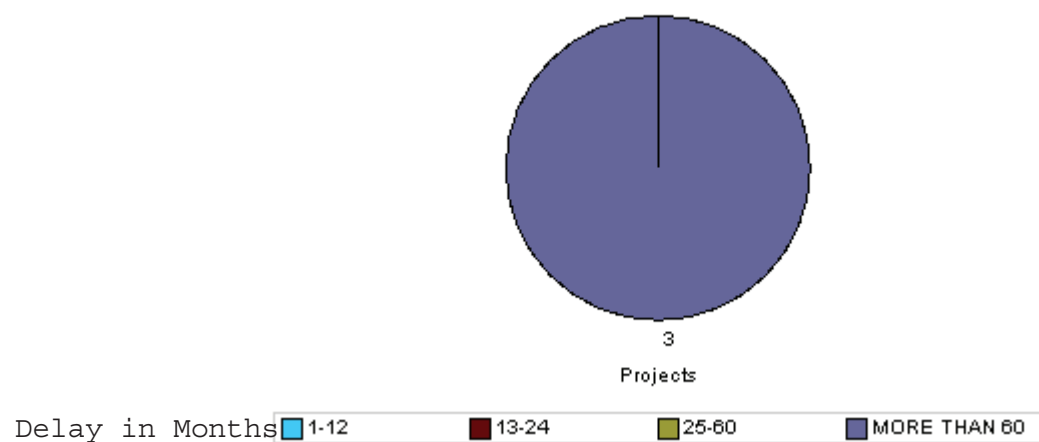

Graphical Presentation of URBAN DEVELOPMENT Sector

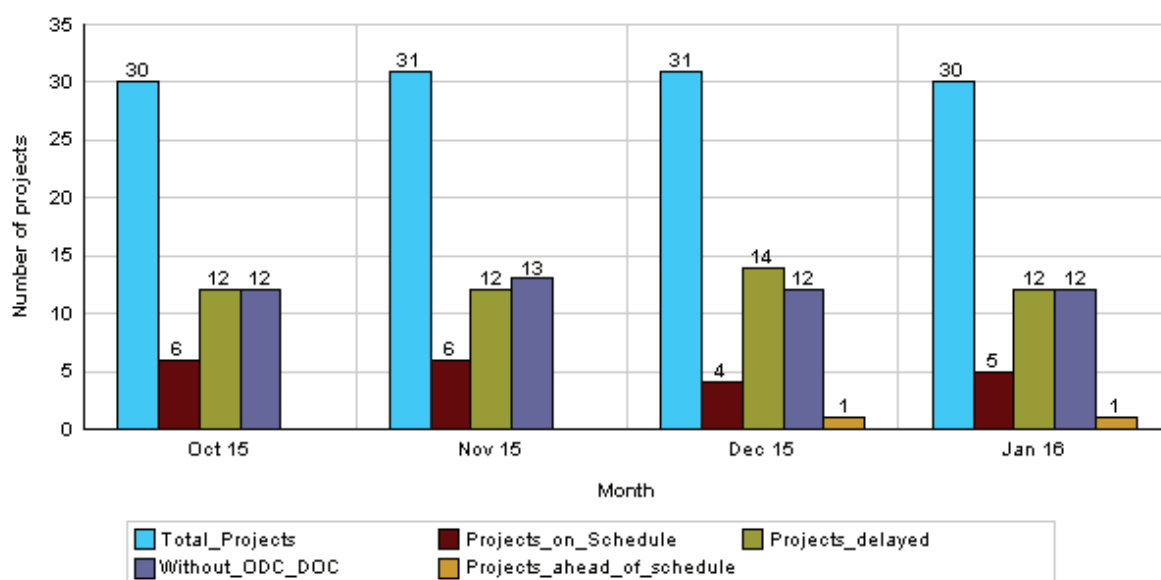

Break-up of 12 Delayed projects in January 2016

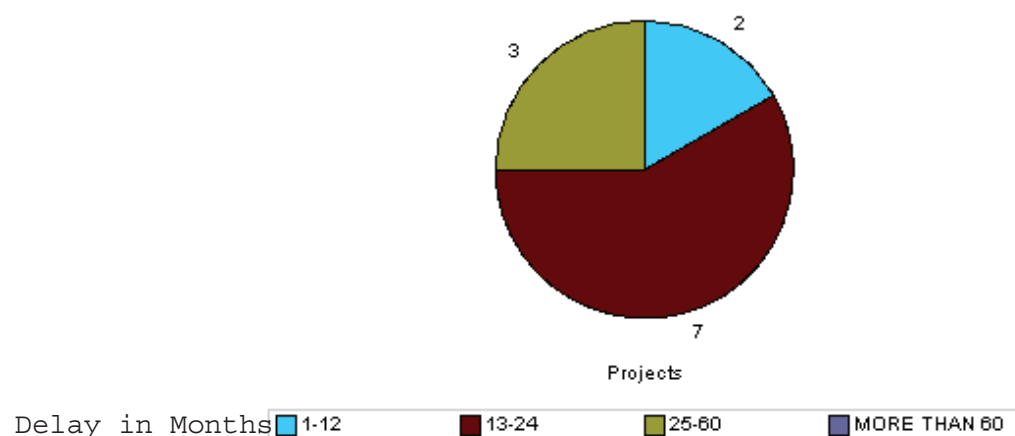

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	44,541.00	51,918.00	39,455.14
CIVIL AVIATION	4	1,177.28	1,177.28	1,186.17	770.46
COAL	86	60,889.41	61,931.69	62,002.14	15,107.97
FERTILISERS	1	197.79	209.44	209.44	49.27
MINES	3	2,555.63	2,555.63	1,875.63	4.59
STEEL	33	53,859.49	54,229.99	54,375.39	30,205.18
PETROCHEMICALS	1	5,460.61	8,920.00	9,965.00	9,175.15
PETROLEUM	62	130,718.16	137,522.60	140,226.81	67,676.67
POWER	111	304,580.02	332,674.70	353,098.54	172,691.27
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
HEALTH AND FAMILY WELFARE	9	2,563.15	2,563.15	2,563.15	946.44
RAILWAYS	297	172,717.67	197,803.64	301,331.54	92,996.30
ROAD TRANSPORT AND HIGHWAYS	411	248,173.44	248,924.94	250,608.22	68,392.18
SHIPPING AND PORTS	8	4,117.75	4,258.80	5,048.81	1,826.73
TELECOMMUNICATIONS	2	15,445.17	15,445.17	15,345.17	2,720.00
URBAN DEVELOPMENT	30	134,055.93	139,269.80	141,505.81	50,146.01
Grand total	1063	1,178,671.50	1,253,745.83	1,395,087.12	552,163.36

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details

(January 2016)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU , .	12/2001	13,171.00 17,270.00	22,462.00	21,077.00	12/2008 10/2013	05/2016	89(O) 31(R)	54/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVNI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU , .	09/2003	3,492.00 -	5,677.00	5,150.14	09/2010 -	09/2016	72(O) -	12/88
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT , .	10/2009	11,459.00 -	11,459.00	7,715.00	12/2015 10/2016	11/2018	35(O) 25(R)	41/70
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN , .	10/2009	12,320.00 -	12,320.00	5,513.00	12/2016 03/2017	12/2019	36(O) 33(R)	29/69
	Total		40,442.00 -	51,918.00	39,455.14				136/329
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA , .	05/2010	335.61 -	318.00	305.01	05/2012 -	03/2015	-	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM , .	01/2009	309.46 -	309.46	412.95	01/2011 06/2016	09/2017	80(O) 15(R)	0/0
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE , .	10/2012	217.60 -	244.10	30.74	03/2015 -	09/2015	-	0/0
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS , .	10/2013	314.61 -	314.61	21.76	- -	09/2018	- -	0/0
	Total		1,177.28 -	1,186.17	770.46				0/0
	COAL								
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA , .	09/2007	467.78 -	467.78	2.85	03/2013 -	-	-	6/83
10	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA , .	01/2005	302.96 -	302.96	302.68	03/2010 -	03/2017	84(O) -	8/10
11	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH , .	06/2010	2,675.67 -	2,675.67	1,990.05	03/2014 -	03/2016	24(O) -	11/16
12	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH , .	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24(O) -	11/13
13	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL,JHARKHAND , .	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72(O) -	2/5
14	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH , .	06/2011	789.88 741.62	741.62	503.51	03/2013 -	03/2016	36(O) -	2/5
15	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH , .	08/2013	7,612.33 7,612.33	7,612.33	798.52	03/2023 03/2023	03/2023	0(O) 0(R)	1/17
16	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH , .	12/2009	1,352.04 1,143.54	1,143.54	809.04	03/2016 -	03/2016	0(O) -	4/6
17	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND , .	08/2008	706.40 -	706.40	78.06	07/2012 -	03/2021	104(O) -	1/3

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA , .	12/2009	212.34 1,228.39	1,228.39	866.79	03/2013 09/2012	03/2016	36(O) 42(R)	21/22
19	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA , .	10/2006	249.03 -	249.03	78.69	03/2012 -	03/2018	72(O) -	30/42
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL , .	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72(O) -	9/15
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH , .	10/2007	259.40 486.57	486.57	81.23	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA , .	12/2007	490.10 -	490.10	204.99	03/2017 -	03/2017	0(O) -	11/11
23	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA , .	12/2007	457.77 -	457.77	209.57	03/2013 -	03/2017	48(O) -	8/9
24	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA , .	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	2/13
25	TALABIRA OCP - [N06000043]MCL,ODISHA , .	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
26	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA , .	12/2007	172.08 -	172.08	151.26	03/2010 -	03/2017	84(O) -	2/4
27	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH , .	11/2014	1,624.59 1,624.59	1,624.59	5.43	03/2023 03/2023	03/2023	0(O) 0(R)	1/10
28	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA , .	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51(O) -	11/44
29	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH , .	08/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023	0(O) -	1/9
30	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA , .	09/2014	441.82 -	441.82	141.07	03/2020 -	03/2020	0(O) -	5/13
31	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA , .	08/2008	207.28 -	207.28	207.70	03/2012 -	03/2017	60(O) -	4/5
32	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA , .	11/2008	479.53 -	479.63	185.34	03/2013 -	03/2017	48(O) -	4/8
33	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH , .	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60(O) -	1/6
34	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH , .	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72(O) -	1/7
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA , .	12/2009	418.97 -	489.62	453.18	03/2012 -	03/2023	132(O) -	0/2
36	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA , .	03/2010	209.78 -	209.78	81.11	03/2015 -	03/2016	12(O) -	8/31
37	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA , .	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48(O) -	5/6
38	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH , .	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48(O) -	4/7
39	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH , .	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016	0(O) -	3/7
40	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND , .	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60(O) -	0/3
41	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND , .	12/2007	179.87 -	179.87	92.95	03/2012 -	03/2017	60(O) -	3/3
42	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND , .	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48(O) -	4/4

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND , .	08/2008	264.68 -	264.68 -	146.05 -	03/2012 -	03/2016 -	48(O) -	2/4
44	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND , .	12/2009	510.85 -	510.85 -	224.65 -	03/2016 -	03/2016 -	0(O) -	2/4
45	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND , .	06/2009	162.46 -	162.46 -	70.20 -	03/2014 -	03/2017 -	36(O) -	3/4
46	KISTARAM OCP - [N06000089]SCCL,TELANGANA , .	11/2010	242.29 -	242.29 -	8.03 -	03/2015 -	03/2018 -	36(O) -	0/5
47	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH , .	06/2011	1,131.28 1,131.28	1,131.28 -	148.45 -	03/2018 -	03/2018 -	0(O) -	6/9
48	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA , .	07/2011	162.76 -	162.76 -	1.31 -	03/2015 -	03/2018 -	36(O) -	4/29
49	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA , .	07/2011	447.06 -	447.06 -	77.44 -	03/2015 -	03/2018 -	36(O) -	4/13
50	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND , .	02/2011	339.88 -	339.88 -	12.06 -	04/2014 -	03/2016 -	23(O) -	4/7
51	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH , .	04/2012	258.56 -	258.56 -	96.39 -	03/2016 -	03/2018 -	24(O) -	3/6
52	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA , .	06/2012	365.01 -	365.01 -	6.56 -	06/2015 -	03/2017 -	21(O) -	18/51
53	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA , .	07/2012	417.33 -	417.33 -	15.14 -	07/2016 -	03/2017 -	8(O) -	6/28
54	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA , .	11/2012	430.45 486.27	486.27 -	93.51 -	03/2016 -	03/2018 -	24(O) -	7/39
55	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND , .	02/2012	858.11 -	858.11 -	108.58 -	03/2020 -	03/2020 -	0(O) -	3/3
56	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH , .	12/2013	610.63 -	610.33 -	- -	03/2022 -	03/2022 -	0(O) -	1/7
57	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND , .	02/2014	555.52 -	555.52 -	3.52 -	03/2021 -	03/2017 -	-48(O) -	0/2
58	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU , .	04/2012	364.75 -	364.75 -	191.25 -	10/2014 -	03/2016 -	17(O) -	8/10
59	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH , .	05/2014	164.49 -	164.49 -	76.43 -	03/2020 -	03/2020 -	0(O) -	2/6
60	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA , .	05/2014	479.15 -	479.15 -	10.44 -	03/2019 -	03/2019 -	0(O) -	1/9
61	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA , .	05/2014	3,756.36 -	3,756.36 -	620.94 -	03/2026 -	03/2026 -	0(O) -	3/15
62	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA , .	05/2014	337.66 -	337.66 -	0.74 -	03/2019 -	03/2019 -	0(O) -	2/6
63	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA , .	06/2014	289.03 -	289.03 -	- -	03/2018 -	03/2018 -	0(O) -	1/5
64	GARJANBAHAL OCP - [N06000117]MCL,ODISHA , .	11/2014	1,375.38 -	1,375.38 -	179.10 -	03/2021 -	03/2021 -	0(O) -	1/9
65	DINESH OCP - [N06000118]WCL,MAHARASHTRA , .	11/2014	611.16 -	611.16 -	199.31 -	03/2020 -	03/2020 -	0(O) -	3/15
66	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA , .	09/2014	266.23 -	266.23 -	98.63 -	03/2021 -	03/2021 -	0(O) -	4/14
67	GOKUL - [N06000120]WCL,MAHARASHTRA , .	11/2014	267.67 -	267.67 -	185.72 -	03/2018 -	03/2018 -	0(O) -	2/8

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
68	BHANEAGON OC - [N06000121]WCL,MAHARASHTRA , .	02/2015	187.94 -	187.94 -	51.51 -	03/2023 -	03/2023 -	0(O) -	6/11
69	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH , .	02/2015	481.60 -	481.60 -	-	03/2023 -	03/2023 -	0(O) -	0/7
70	AMERA OC RCE - [N06000123]SECL,CHHATISGARH , .	02/2015	335.97 -	335.97 -	34.09 -	03/2018 -	03/2018 -	0(O) -	1/4
71	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH , .	12/2014	357.80 -	357.80 -	113.00 -	03/2021 -	03/2021 -	0(O) -	0/7
72	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH , .	12/2014	371.04 -	371.04 -	29.15 -	03/2021 -	03/2021 -	0(O) -	0/6
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA , .	05/2015	295.56 -	295.56 -	72.99 -	03/2019 -	03/2019 -	0(O) -	4/14
74	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA , .	05/2015	397.09 -	397.09 -	0.05 -	03/2019 -	03/2019 -	0(O) -	5/18
75	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA , .	06/2015	205.49 -	205.49 -	1.37 -	03/2020 -	03/2020 -	0(O) -	4/12
76	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA , .	06/2015	483.69 -	483.69 -	46.94 -	03/2021 -	03/2021 -	0(O) -	3/9
77	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA , .	08/2015	727.28 -	727.28 -	61.37 -	03/2025 -	03/2025 -	0(O) -	3/13
78	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA , .	08/2015	288.90 -	288.90 -	-	03/2023 -	03/2023 -	0(O) -	3/15
79	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH , .	07/2015	231.92 -	231.92 -	-	03/2022 -	03/2022 -	0(O) -	0/6
80	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH , .	07/2015	316.10 -	316.10 -	16.87 -	03/2020 -	03/2020 -	0(O) -	0/5
81	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH , .	02/2015	916.24 -	916.24 -	-	03/2023 -	03/2023 -	0(O) -	0/8
82	MALACHUA OPENCAS PROJECT - [N06000139]SECL,MADHYA PRADESH , .	10/2015	488.33 -	488.33 -	-	03/2023 -	03/2023 -	0(O) -	0/8
83	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH , .	10/2015	1,875.32 -	1,875.32 -	-	03/2024 -	03/2024 -	0(O) -	0/0
84	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA , .	11/2015	277.65 -	277.65 -	-	03/2021 -	03/2021 -	0(O) -	0/9
85	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA , .	11/2015	498.42 -	498.42 -	-	03/2018 -	03/2018 -	0(O) -	1/9
86	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND , .	10/2015	359.69 -	359.69 -	6.49 -	03/2022 -	03/2022 -	0(O) -	0/24
87	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU , .	06/2011	5,907.11 -	5,907.11 -	1,373.77 -	12/2015 04/2018	04/2018	28(O) 0(R)	11/35
88	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND , .	08/2011	1,230.27 -	1,230.27 -	47.76 -	04/2015 04/2019	04/2019	48(O) 0(R)	2/11
89	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND , .	08/2011	988.35 -	988.35 -	45.26 -	04/2017 -	04/2017 -	0(O) -	0/2
90	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL , .	08/2012	1,055.05 -	1,055.05 -	202.22 -	03/2018 -	06/2018 -	3(O) -	1/15
91	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU , .	04/2013	1,458.17 -	1,458.17 -	14.59 -	06/2015 -	08/2019 -	50(O) -	1/7
92	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND , .	09/2009	153.82 -	153.82 -	70.92 -	03/2014 -	09/2016 -	30(O) -	1/9
93	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND , .	08/2010	289.45 -	289.45 -	99.75 -	05/2014 -	10/2016 -	29(O) -	0/8

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND , .	10/2012	269.82 -	269.82	68.57	04/2014 -	11/2016	31(O) -	0/10
	Total		60,889.41 -	62,002.14	15,107.97				323/1041
	<u>FERTILISERS</u>								
95	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA , .	10/2014	197.79 209.44	209.44	49.27	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	209.44	49.27				0/0
	<u>MINES</u>								
96	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH , .	09/2011	1,856.00 -	1,176.00	4.59	09/2017 -	04/2020	31(O) -	0/0
97	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 -	355.13	-	11/2016 -	11/2016	0(O) -	0/0
98	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 -	344.50	-	11/2016 -	11/2016	0(O) -	0/0
	Total		2,555.63 -	1,875.63	4.59				0/0
	<u>STEEL</u>								
99	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH , .	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
100	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT , .	01/2013	175.00 -	175.00	-	- -	-	-	0/0
101	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH , .	07/2012	332.65 -	332.65	229.64	08/2014 11/2015	01/2016	17(O) 2(R)	4/5
102	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA , .	12/2011	187.33 -	187.33	173.07	10/2013 12/2015	03/2016	29(O) 3(R)	2/5
103	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND , .	03/2015	255.19 -	255.19	22.05	03/2018 -	03/2018	0(O) -	0/0
104	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA , .	03/2007	149.73 173.00	173.00	175.94	12/2015 -	03/2017	15(O) -	0/0
105	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA , .	05/2005	768.88 1,060.00	1,060.00	1,070.97	02/2014 -	03/2016	25(O) -	0/0
106	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA , .	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN , .	05/2015	189.00 -	189.00	-	03/2017 -	03/2017	0(O) -	0/0
108	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR , .	10/2005	956.00 -	956.00	648.16	03/2015 -	03/2017	24(O) -	0/0
109	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND , .	12/2007	200.00 -	200.00	126.15	03/2018 -	03/2018	0(O) -	0/0
110	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND , .	02/2014	787.29 -	787.29	241.53	12/2016 -	03/2017	3(O) -	0/0
111	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA , .	04/2015	3,127.30 -	3,127.30	297.93	04/2018 -	04/2018	0(O) -	0/0
112	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND , .	04/2013	170.00 -	170.00	88.91	04/2018 -	04/2018	0(O) -	0/0
113	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND , .	10/2013	245.67 -	245.67	98.57	05/2016 -	05/2016	0(O) -	1/3
114	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH , .	08/2010	17,265.00 -	17,265.00	15,516.00	03/2013 03/2016	06/2016	39(O) 3(R)	32/35
115	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA , .	04/2011	572.00 -	572.00	485.35	04/2013 09/2014	06/2015	-	18/19
116	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH , .	05/2012	404.16 -	404.16	265.95	07/2015 -	06/2017	23(O) -	0/1
117	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH , .	12/2009	343.00 -	488.40	38.17	10/2016 -	06/2017	8(O) -	0/0
118	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND , .	12/2007	253.92 254.00	254.00	193.97	06/2016 -	06/2016	0(O) -	0/0
119	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA , .	10/2011	175.49 207.00	207.00	131.77	12/2016 -	07/2017	7(O) -	0/0
120	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA , .	02/2011	898.55 -	898.55	410.53	05/2013 01/2015	08/2015	-	19/20
121	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA , .	06/2014	708.91 -	708.91	295.30	04/2016 -	08/2016	4(O) -	2/2
122	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH , .	07/2011	877.73 -	877.73	399.56	07/2015 -	08/2016	13(O) -	2/2
123	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH , .	12/2009	280.00 -	280.00	26.55	09/2016 -	09/2016	0(O) -	1/1
124	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND , .	02/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017	0(O) -	0/0
125	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND , .	03/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017	0(O) -	0/0
126	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA , .	04/2014	151.33 -	151.33	4.84	09/2017 -	11/2017	2(O) -	0/0
127	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH , .	04/2014	188.93 -	188.93	60.23	04/2015 -	12/2016	20(O) -	2/3

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH, .	01/2010	15,525.00	15,525.00	8,493.78	05/2015 12/2016	12/2016	19(O) 0(R)	32/81
129	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH, .	07/2011	974.76	974.76	220.37	07/2016 -	12/2016	5(O) -	0/1
130	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND, .	05/2015	1,154.18	1,154.18	28.20	12/2017 -	12/2017	0(O) -	0/0
131	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA, .	12/2007	202.61 227.00	227.00	195.51	12/2016 -	12/2016	0(O) -	0/0
	Total		53,859.49	54,375.39	30,205.18				115/178
	<u>PETROCHEMICALS</u>								
132	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM, .	04/2006	5,460.61 8,920.00	9,965.00	9,175.15	04/2012 12/2013	12/2015	-	21/26
	Total		5,460.61	9,965.00	9,175.15				21/26
	<u>PETROLEUM</u>								
133	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU, .	05/2013	711.00	711.00	7.70	- -	-	-	0/0
134	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU, .	11/2006	171.83	171.83	-	- -	-	-	0/0
135	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE, .	01/2015	1,823.00	1,823.00	1.34	- -	-	-	0/0
136	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE, .	01/2015	2,321.00	2,321.00	2.04	- -	-	-	0/0
137	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE, .	02/2015	890.00	890.00	1.80	- -	-	-	0/0
138	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE, .	06/2010	2,523.00 2,523.00	2,523.00	1,792.85	01/2014 12/2015	01/2016	24(O) 1(R)	4/13
139	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE, .	04/2010	270.00	251.66	-	06/2012 -	01/2016	43(O) -	0/0
140	DIESEL HYDROTREATOR - [N16000207]NRL, ASSAM, Central Sector Projects	07/2015	1,031.37	1,031.37	12.72	01/2018 -	01/2018	0(O) -	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA, .	02/2009	29,777.00 34,555.00	34,555.00	31,052.90	11/2012 11/2013	02/2016	39(O) 27(R)	96/100
142	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU, .	12/2012	279.00	279.00	186.98	12/2014 -	02/2016	14(O) -	57/58
143	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA, .	10/2015	607.06 714.25	714.25	73.79	10/2017 02/2018	02/2018	4(O) 0(R)	21/48
144	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM, .	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48(O) 12(R)	5/15
145	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA, .	12/2009	1,584.00	1,584.00	1,399.90	08/2015 -	03/2016	7(O) -	3/12
146	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE, .	12/2009	463.32	463.32	321.64	06/2011 03/2012	03/2016	57(O) 48(R)	13/20

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
147	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT, .	03/2009	317.64 -	240.95	127.08	09/2012 03/2016	03/2016	42(O) 0(R)	0/5
148	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA, .	03/2012	2,592.17 2,592.17	2,592.17	832.22	05/2014 03/2017	03/2017	34(O) 0(R)	0/21
149	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE, .	08/2011	586.00 -	586.00	419.10	08/2015 -	03/2016	7(O) -	3/12
150	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE, .	12/2009	309.81 462.79	462.79	264.14	10/2014 03/2017	03/2017	29(O) 0(R)	28/40
151	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA, .	01/2006	732.00 1,227.00	1,227.00	1,074.73	10/2011 -	03/2016	53(O) -	0/0
152	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE, .	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
153	MARKETING TOP AT KORBA - [N16000186]IOCL, CHHATISGARH, .	01/2011	141.86 -	232.00	164.35	09/2016 -	03/2016	-6(O) -	0/12
154	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC, MAHARASHTRA, .	11/2014	6,068.80 -	6,068.80	648.01	04/2019 -	03/2019	-1(O) -	0/0
155	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC, D & N HAVELI, .	08/2014	6,086.08 -	6,086.08	592.92	05/2019 03/2020	03/2020	10(O) 0(R)	0/0
156	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL, ODISHA, .	03/2014	238.50 -	238.50	1.07	03/2017 -	03/2017	0(O) -	0/0
157	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA, .	08/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019	0(O) -	0/0
158	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL, GUJARAT, Central Sector Projects	11/2015	500.00 -	500.00	-	03/2017 -	03/2017	0(O) -	0/0
159	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA, .	03/2011	861.79 1,256.72	1,256.72	995.12	05/2013 04/2016	04/2016	35(O) 0(R)	1/5
160	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU, .	05/2015	257.87 -	257.87	34.80	11/2016 -	04/2017	5(O) -	9/22
161	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE, .	08/2009	1,793.00 -	1,793.00	1,294.55	09/2012 -	05/2016	44(O) -	6/7
162	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA, .	12/2011	2,059.63 2,665.65	2,665.65	1,323.77	03/2015 05/2016	05/2016	14(O) 0(R)	0/17
163	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE, .	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17(O) 12(R)	0/8
164	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE, .	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26(O) 0(R)	0/3
165	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA, .	03/2012	14,225.00 -	16,504.00	10,044.66	05/2016 -	05/2016	0(O) -	0/30
166	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA, .	03/2013	1,138.50 686.58	686.58	563.49	04/2015 05/2016	05/2016	13(O) 0(R)	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA, .	01/2006	993.00 1,693.00	1,693.00	1,447.43	01/2012 -	05/2016	52(O) -	0/0
168	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE, .	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
169	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC, MAHARASHTRA, .	06/2014	5,706.47 5,813.25	5,813.25	2,689.65	05/2017 05/2017	05/2017	0(O) 0(R)	6/16

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
170	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT , .	12/2011	160.00 -	160.00	38.16	02/2016 02/2016	05/2016	3(O) 3(R)	0/0
171	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA , .	02/2015	2,899.93 2,098.43	2,098.43	641.31	05/2017 -	05/2017	0(O) -	0/0
172	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE , .	06/2009	2,915.00 -	2,915.00	1,381.31	12/2012 -	06/2015	-	7/14
173	CHINCHINADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH , .	07/2014	419.04 -	419.04	326.09	01/2017 -	06/2016	-7(O) -	11/16
174	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT , .	09/2011	202.25 -	160.16	69.23	07/2016 -	07/2016	0(O) -	5/12
175	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR , .	04/2013	480.00 -	480.00	141.59	02/2016 -	07/2016	5(O) -	5/6
176	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM , .	02/2014	163.88 -	163.88	58.18	07/2016 -	07/2016	0(O) -	4/6
177	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM , .	09/2012	871.35 -	1,200.00	537.65	03/2015 11/2015	08/2016	17(O) 9(R)	0/5
178	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA , .	03/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017	0(O) -	0/0
179	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE , .	06/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016	61(O) 0(R)	0/0
180	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN , .	11/2011	310.00 -	370.00	0.37	03/2013 -	10/2016	43(O) -	0/0
181	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA , .	02/2012	666.00 838.08	838.08	572.18	11/2015 11/2016	11/2016	12(O) 0(R)	25/29
182	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU , .	02/2011	3,110.36 -	3,110.36	1,395.63	11/2015 07/2016	11/2016	12(O) 4(R)	45/52
183	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT , .	05/2015	1,671.22 1,881.22	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
184	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE , .	07/2009	3,957.00 3,561.00	3,561.00	26.81	01/2013 -	12/2018	71(O) -	11/38
185	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE , .	02/2011	913.00 -	913.00	480.22	08/2015 -	12/2016	16(O) -	0/0
186	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE , .	05/2013	4,124.35 4,941.49	4,941.49	549.78	04/2016 12/2017	12/2017	20(O) 0(R)	0/6
187	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL , .	03/2014	3,076.00 -	3,076.00	188.44	09/2017 03/2018	12/2017	3(O) -3(R)	0/0
188	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE , .	03/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018	0(O) -	3/8
189	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM , .	03/2009	228.64 -	214.19	140.71	12/2016 -	12/2016	0(O) -	0/0
190	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE , .	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5(O) -	1/39
191	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE , .	10/2011	725.00 -	725.00	130.00	11/2016 -	12/2016	1(O) -	0/14
192	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA , .	05/2015	2,443.00 -	2,443.00	-	12/2017 -	12/2017	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
193	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM , .	06/2010	202.94 -	202.94	2.95	01/2014 -	-	-	0/2
194	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND , .	04/2011	191.96 -	191.96	103.14	05/2015 -	-	-	0/12
	Total		130,718.16 -	140,226.81	67,676.67				369/728
	<u>POWER</u>								
195	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA , .	07/2009	421.01 1,007.57	1,007.57	958.83	07/2013 01/2016	01/2016	30(O) 0(R)	25/26
196	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , .	01/2013	12,964.60 -	12,964.60	4,914.20	01/2018 -	01/2018	0(O) -	23/25
197	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL , .	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71(O) -	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE , .	02/2009	410.29 -	410.29	362.37	02/2012 -	02/2016	48(O) -	7/10
199	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE , .	03/2010	965.58 -	965.58	766.14	11/2012 -	02/2016	39(O) -	7/10
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE , .	08/2010	1,677.57 -	1,677.57	1,447.42	04/2013 -	02/2016	34(O) -	9/11
201	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-A - [N18000098]PGCIL,MULTI STATE , .	05/2010	250.03 -	250.03	187.20	01/2013 -	02/2016	37(O) -	10/15
202	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE , .	08/2014	288.49 -	288.49	67.20	02/2017 -	02/2017	0(O) -	0/12
203	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND , .	02/2014	14,366.58 -	14,366.58	2,349.00	02/2019 -	02/2019	0(O) -	10/12
204	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH , .	05/2011	195.42 -	195.42	51.09	02/2014 -	02/2018	48(O) -	1/1
205	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN , .	02/2015	302.49 302.00	302.49	234.18	02/2016 -	02/2016	0(O) -	0/1
206	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM , .	01/2008	4,375.35 6,749.18	6,749.18	5,719.00	09/2011 -	03/2017	66(O) -	17/37
207	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL , .	04/2010	4,404.57 -	4,404.57	2,405.85	01/2015 -	03/2017	26(O) -	8/16
208	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE , .	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43(O) -	3/5
209	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE , .	03/2011	1,585.12 -	1,585.12	1,578.86	11/2013 -	03/2016	28(O) -	8/12
210	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE , .	07/2010	1,272.80 -	1,272.80	1,244.23	11/2012 -	03/2017	52(O) -	8/13
211	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND , .	10/2011	558.26 -	558.26	529.11	11/2013 -	03/2016	28(O) -	8/12

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
212	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE , .	12/2011	2,422.66 -	2,422.66	2,372.26	08/2014 -	03/2016	19(O) -	9/14
213	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT , .	12/2011	552.44 609.44	609.44	579.80	02/2014 03/2016	03/2016	25(O) 0(R)	8/10
214	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UPPP-PART B - [N18000122]PGCIL,MULTI STATE , .	02/2012	1,927.16 -	1,927.16	1,585.67	10/2014 -	03/2016	17(O) -	5/7
215	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA , .	01/2012	15,166.19 -	15,166.19	10,171.00	01/2017 -	03/2017	2(O) -	30/39
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE , .	09/2012	524.40 -	524.40	323.52	05/2015 -	03/2016	10(O) -	8/12
217	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE , .	03/2014	155.57 -	155.57	5.40	03/2016 -	03/2016	0(O) -	1/6
218	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE , .	06/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018	0(O) -	8/12
219	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH , .	08/2014	188.75 -	188.75	71.50	02/2017 -	03/2016	-11(O) -	0/2
220	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH , .	09/2014	9,188.98 -	9,188.98	1,000.00	03/2019 -	03/2019	0(O) -	14/15
221	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE , .	01/2015	268.80 -	268.80	22.60	03/2018 -	03/2018	0(O) -	0/3
222	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE , .	03/2015	197.40 -	197.40	-	03/2018 -	03/2018	0(O) -	0/0
223	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH , .	03/2015	550.06 -	550.06	15.60	03/2018 -	03/2018	0(O) -	0/3
224	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR , .	03/2010	3,984.03 -	3,984.03	3,178.09	01/2013 -	03/2016	38(O) -	0/1
225	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND , .	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51(O) -	0/0
226	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH , .	01/2016	305.04 -	305.04	-	03/2017 -	03/2017	0(O) -	0/0
227	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE , .	06/2014	400.47 -	400.47	45.19	04/2017 -	04/2017	0(O) -	0/3
228	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR , .	10/2014	8,112.12 -	8,112.12	120.00	04/2020 -	04/2020	0(O) -	0/0
229	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE , .	12/2014	6,517.36 -	6,517.36	301.90	04/2018 -	04/2018	0(O) -	3/12
230	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE , .	04/2015	3,705.61 -	3,705.61	194.60	04/2018 -	04/2018	0(O) -	4/9

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
231	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE , .	04/2015	1,479.30 -	1,479.30	78.90	04/2017 -	04/2017	0(O) -	2/8
232	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR , .	02/2005	8,692.97 15,095.67	15,095.67	11,183.00	01/2011 10/2014	05/2018	88(O) 43(R)	27/48
233	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE , .	09/2013	1,575.30 -	1,575.30	709.90	05/2016 -	05/2016	0(O) -	8/13
234	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA , .	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5(O) -	6/8
235	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE , .	01/2015	3,662.02 -	3,662.02	338.80	05/2018 -	05/2018	0(O) -	0/5
236	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI , .	03/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017	0(O) -	0/9
237	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH , .	05/2015	312.94 -	312.94	16.10	05/2016 -	05/2016	0(O) -	0/0
238	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU , .	01/2016	162.11 -	162.11	-	05/2018 -	05/2018	0(O) -	0/0
239	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH , .	12/2004	2,496.90 6,085.84	6,085.84	4,362.53	12/2009 06/2016	06/2016	78(O) 0(R)	16/27
240	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE , .	02/2009	509.66 -	509.66	528.56	11/2011 -	06/2016	55(O) -	8/11
241	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE , .	07/2010	752.64 689.03	689.03	548.12	07/2013 11/2015	06/2016	35(O) 7(R)	7/9
242	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH , .	05/2011	1,961.87 -	1,961.87	1,798.15	05/2014 -	06/2016	25(O) -	8/12
243	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU , .	09/2011	1,940.13 -	1,940.13	1,938.06	09/2014 -	06/2016	21(O) -	8/13
244	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH , .	11/2011	2,127.51 -	2,127.51	2,319.63	07/2014 -	06/2016	23(O) -	6/8
245	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE , .	12/2011	297.33 346.79	346.79	303.37	08/2014 06/2015	06/2016	22(O) 12(R)	8/10
246	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH , .	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22(O) 6(R)	7/11
247	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH , .	01/2012	1,422.85 -	1,422.85	1,391.42	01/2015 -	06/2016	17(O) -	9/11
248	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE , .	03/2012	198.63 -	198.63	94.63	09/2014 -	06/2016	21(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
249	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH, . .	03/2012	9,569.76 -	9,569.76 -	5,724.59 -	06/2015 -	06/2016 -	12(O) -	21/30
250	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE, . .	11/2011	723.63 -	723.63 -	587.42 -	11/2014 -	06/2016 -	19(O) -	7/10
251	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE, . .	02/2012	3,201.44 -	3,201.44 -	2,996.11 -	10/2014 -	06/2016 -	20(O) -	8/17
252	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATTISGARH, . .	12/2012	11,846.00 -	11,846.00 -	5,564.00 -	06/2017 -	06/2017 -	0(O) -	22/40
253	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE, . .	09/2013	680.69 -	680.69 -	459.89 -	03/2016 -	06/2016 -	3(O) -	10/12
254	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE, . .	10/2013	1,364.52 -	1,364.52 -	434.44 -	04/2016 -	06/2016 -	2(O) -	8/12
255	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL, MULTI STATE, . .	02/2014	539.82 -	539.82 -	111.90 -	06/2016 -	06/2016 -	0(O) -	8/11
256	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL, MULTI STATE, . .	02/2014	908.08 -	908.08 -	135.50 -	06/2016 -	06/2016 -	0(O) -	9/18
257	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE, . .	02/2014	196.58 -	196.58 -	21.50 -	02/2016 -	06/2016 -	4(O) -	7/17
258	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL, ODISHA, . .	01/2016	187.04 -	187.04 -	-	06/2018 -	06/2018 -	0(O) -	0/0
259	PARE HYDRO ELECTRIC PROJECT - [N18000045]NPEPCO, ARUNACHAL PRADESH, . .	12/2008	573.99 - 1,262.27 -	1,262.27 -	1,093.23 -	08/2013 07/2016	07/2016 -	35(O) 0(R)	29/38
260	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL, MULTI STATE, . .	05/2014	303.07 -	303.07 -	19.70 -	07/2016 -	07/2016 -	0(O) -	2/9
261	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL, MULTI STATE, . .	01/2015	203.28 -	203.28 -	18.38 -	07/2017 -	07/2017 -	0(O) -	0/5
262	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI, . .	05/2015	780.33 -	780.33 -	0.90 -	07/2017 -	07/2017 -	0(O) -	0/0
263	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE, . .	07/2015	2,247.37 -	2,247.37 -	16.00 -	07/2018 -	07/2018 -	0(O) -	0/0
264	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL, GUJARAT, . .	01/2016	244.19 -	244.19 -	-	07/2018 -	07/2018 -	0(O) -	0/0
265	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE, . .	01/2016	1,455.47 -	1,455.47 -	-	07/2018 -	07/2018 -	0(O) -	0/0
266	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH, . .	01/2016	207.88 -	207.88 -	-	07/2018 -	07/2018 -	0(O) -	0/0
267	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA, . .	03/2012	9,395.18 -	9,395.18 -	5,881.00 -	11/2016 -	08/2017 -	9(O) -	26/28
268	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND, . .	07/2012	1,527.00 -	1,527.00 -	143.00 -	08/2017 -	08/2017 -	0(O) -	0/9
269	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART - C - [N18000143]PGCIL, MULTI STATE, . .	03/2013	514.20 -	514.20 -	335.10 -	06/2015 -	08/2016 -	14(O) -	7/10

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
270	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE , .	06/2012	1,909.24 -	1,909.24	1,016.53	06/2015 -	08/2016	14(O) -	3/5
271	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE , .	05/2014	829.98 -	829.98	83.30	08/2016 -	08/2016	0(O) -	1/4
272	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA , .	02/2014	12,532.44 -	12,532.44	2,500.00	08/2018 -	08/2018	0(O) -	17/17
273	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC,WEST BENGAL , .	09/2005	1,061.38 -	2,193.08	1,956.52	09/2009 -	09/2016	84(O) -	3/6
274	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND , .	07/2006	1,657.00 2,978.86	2,978.86	1,603.73	02/2016 09/2019	09/2019	43(O) 0(R)	10/21
275	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH , .	03/2013	11,638.55 -	11,638.55	4,856.00	09/2017 -	09/2017	0(O) -	20/41
276	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL , .	09/2014	1,381.84 -	1,381.84	157.00	09/2019 -	09/2019	0(O) -	3/4
277	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE , .	03/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017	0(O) -	0/0
278	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR , .	01/2007	5,353.00 -	5,353.00	5,298.06	05/2014 -	09/2017	40(O) -	0/4
279	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , .	04/2012	9,750.89 -	9,750.89	4,529.23	12/2016 -	09/2017	9(O) -	25/28
280	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH , .	03/2015	9,870.51 -	9,870.51	-	09/2019 -	09/2019	0(O) -	0/6
281	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM , .	07/1998	368.72 1,381.71	1,381.71	951.92	07/2006 10/2016	10/2016	123(O) 0(R)	5/13
282	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT , .	02/2014	378.71 -	378.71	113.30	10/2016 -	10/2016	0(O) -	8/11
283	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE , .	01/2015	871.62 -	871.62	3.10	10/2017 -	10/2017	0(O) -	0/5
284	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT , .	10/2015	315.00 -	315.00	-	10/2016 -	10/2016	0(O) -	0/1
285	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR , .	01/2009	3,642.04 -	5,751.47	4,402.95	01/2016 -	11/2016	10(O) -	7/9
286	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE , .	01/2014	374.63 -	374.63	16.20	04/2016 -	11/2016	7(O) -	0/0
287	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE , .	05/2014	522.29 -	522.29	49.40	11/2016 -	11/2016	0(O) -	2/12
288	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL, MULTI STATE , .	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/3
289	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN , .	07/2015	307.18 -	307.18	7.40	11/2017 -	11/2017	0(O) -	0/0
290	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH , .	09/2002	3,919.59 -	8,398.76	5,398.46	09/2009 -	12/2018	111(O) -	2/3
291	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU , .	05/2005	1,779.29 2,187.32	2,187.32	1,903.55	11/2008 01/2016	12/2016	97(O) 11(R)	20/22
292	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND , .	11/2006	2,978.48 3,846.30	3,846.30	2,699.00	03/2013 -	12/2018	69(O) -	2/15

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA , .	12/2007	477.69 738.48	738.48	579.39	09/2010 01/2016	12/2016	75(O) 11(R)	4/8
294	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND , .	08/2008	2,491.58 -	2,491.58	789.89	06/2013 -	12/2019	78(O) -	5/8
295	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE , .	10/2008	4,824.12 -	4,824.12	4,237.58	10/2012 -	12/2016	50(O) -	7/11
296	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE , .	02/2009	11,130.19 13,762.80	13,762.80	11,463.30	08/2013 12/2017	12/2017	52(O) 0(R)	17/26
297	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE , .	02/2010	2,144.00 2,932.88	2,932.88	2,283.80	12/2012 12/2016	12/2016	48(O) 0(R)	11/23
298	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA , .	03/2012	7,921.47 -	7,921.47	4,904.00	09/2016 -	12/2016	3(O) -	28/34
299	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE , .	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12(O) -	15/18
300	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH , .	07/2013	3,363.12 -	3,363.12	1,018.00	12/2016 -	12/2016	0(O) -	16/18
301	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]JSVNL,BIHAR , .	05/2015	436.68 -	436.68	436.56	12/2016 -	12/2016	0(O) -	0/1
302	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH , .	09/2003	6,285.33 -	18,063.89	7,969.14	09/2010 -	-	-	0/0
303	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE , .	02/2010	232.34 -	232.34	213.69	06/2012 -	-	-	1/4
304	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE , .	10/2011	487.49 639.46	639.46	434.22	06/2014 03/2016	-	-	10/12
305	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH , .	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
	Total		304,580.02 -	353,098.54	172,691.27				771/1248
	<u>HEAVY INDUSTRY</u>								
306	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE , .	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
307	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI , .	11/2013	196.70 -	196.70	157.61	01/2016 -	01/2016	0(O) -	0/0
308	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI , .	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3(O) -	0/0
309	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH , .	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
310	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM , .	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15(O) -	0/0
311	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA , .	09/2014	505.58 -	505.58	9.74	03/2018 -	03/2018	0(O) -	0/0
312	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI , .	12/2013	204.44 -	204.44	25.67	05/2017 -	05/2017	0(O) -	0/0
313	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI , .	08/2014	293.65 -	293.65	49.24	05/2017 -	05/2017	0(O) -	0/0
314	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL , .	12/2014	168.90 -	168.90	0.05	05/2017 -	05/2017	0(O) -	0/0
315	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI , .	02/2013	414.11 -	414.11	210.91	11/2013 -	11/2014	-	0/0
	Total		2,563.15 -	2,563.15	946.44				0/0
	<u>RAILWAYS</u>								
316	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE , .	09/1998	247.66 3,500.00	3,500.00	1,007.95	05/2008 -	-	-	0/0
317	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT , .	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
318	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE , .	04/2012	1,054.35 2,200.00	2,200.00	51.67	-	-	-	0/0
319	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]UTTAR PRADESH , .	04/1997	836.26 -	1,072.51	-	-	-	-	0/0
320	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL , .	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
321	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE , .	04/2006	96.16 -	260.16	240.21	-	01/2015	-	0/0
322	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA , .	12/1994	124.43 -	925.30	712.02	-	02/2014	-	0/0
323	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE , .	02/1996	240.00 -	579.37	599.40	-	02/2012	-	0/0
324	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE , .	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
325	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE , .	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
326	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE , .	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
327	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL , .	04/1983	36.80 36.38	1,336.57	255.55	-	03/2019	-	0/0
328	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA , .	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144(O) -	0/0
329	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH , .	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
330	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH , .	03/1997	677.97 1,062.36	1,651.54	1,621.40	-	03/2018	-	0/0
331	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE , .	04/1997	218.24 236.41	645.00	309.19	-	03/2015	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
332	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL , .	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
333	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR , .	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
334	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA , .	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
335	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE , .	04/1999	744.71 -	744.71	576.86	- -	03/2016	- -	1/1
336	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE , .	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0
337	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR , .	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
338	KODERMA GIRIDH (NL), ECR - [220100306]ECR, JHARKHAND , .	04/1996	768.87 -	768.87	682.31	- 03/2010	03/2010	-	0/0
339	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR , .	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84(O) -	0/0
340	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH , .	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
341	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH , .	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	- -	0/0
342	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU , .	09/2006	343.17 -	914.98	846.18	- -	03/2016	- -	0/0
343	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM , .	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	- -	0/0
344	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR , .	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	- -	0/0
345	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA , .	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
346	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH , .	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
347	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA , .	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
348	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM , .	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
349	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR , .	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
350	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM , .	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
351	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN , .	04/2008	829.74 -	829.74	96.76	03/2015 -	03/2015	-	0/0
352	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND , .	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
353	KATAKHAL TO BHAIRABI - [N22000126]NFR, ASSAM , .	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
354	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM , .	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND , .	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
356	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE , .	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	- -	0/0
357	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL , .	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	- -	0/0
358	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA , .	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108(O) -	0/0
359	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA , .	04/2012	252.00 -	886.65	-	- -	03/2018	- -	0/0
360	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND , .	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	- -	0/0
361	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL , .	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	- -	0/0
362	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL , .	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	- -	0/0
363	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU , .	04/2007	247.00 -	951.24	619.87	- -	03/2015	- -	0/0
364	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA , .	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
365	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE , .	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	- -	0/0
366	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE , .	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	- -	0/0
367	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE , .	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	- -	0/0
368	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE , .	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	- -	0/0
369	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM , .	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	- -	0/0
370	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM , .	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	- -	0/0
371	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA , .	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11(O) -	0/0
372	PLASSEY-JAGANJ DOUBLING - [N22000220]ER,MULTI STATE , .	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	- -	0/0
373	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE , .	04/2011	299.60 -	299.60	-	03/2017 -	03/2017	0(O) -	0/0
374	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE , .	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	- -	0/0
375	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE , .	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
376	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE , .	04/2007	98.74 -	203.00	227.84	- -	03/2015	- -	0/0
377	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH , PPP (BOT)	03/2012	1,503.71 -	1,503.71	175.26	- -	03/2020	- -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH , .	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
379	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA , .	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86(O) 86(R)	0/0
380	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM , .	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110(O) 66(R)	0/0
381	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH , .	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	-	0/0
382	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU , .	04/2006	495.74 -	495.74	315.66	06/2013 06/2013	06/2013	-	0/0
383	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH , .	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87(O) -	0/0
384	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL , .	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3(O) -	0/0
385	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL , .	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27(O) -	0/0
386	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA , .	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
387	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA , .	07/1998	125.00 -	480.00	3.51	07/2008 -	07/2008	-	0/0
388	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA , .	04/2007	482.00 -	874.57	730.11	03/2013 -	09/2015	-	0/0
389	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL , .	04/1999	207.52 -	207.52	223.44	12/2012 -	09/2015	-	0/0
390	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA , .	04/2010	203.40 -	203.40	153.29	- -	09/2015	-	0/0
391	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH , .	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	-	0/0
392	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA , .	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
393	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA , .	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91(O) 91(R)	0/0
394	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL , .	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
395	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR , .	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181(O) -	0/0
396	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE , .	02/1997	386.30 -	1,544.40	-	03/1998 -	12/2019	261(O) -	0/0
397	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND , .	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	-	0/0
398	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL , .	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
399	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA , .	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
400	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR , .	04/2001	624.47 -	2,921.00	2,521.72	10/2007 12/2012	12/2015	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
401	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH , .	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93(O) -	0/0
402	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL , .	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
403	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL , .	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57(O) -	0/0
404	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL , .	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33(O) -	0/0
405	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE , .	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	- -	0/0
406	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA , .	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
407	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND , .	04/2012	258.20 315.13	365.00	2.52	- -	12/2017	- -	0/0
408	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA , .	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21(O) -	0/0
409	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA , .	03/2012	155.81 -	155.81	18.25	- -	12/2016	- -	0/0
410	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND , .	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0
411	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE , .	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
412	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL, RVNL - [220100149]RVNL,CHHATISGARH , .	04/1995	304.00 -	631.78	238.82	12/2012 -	-	-	0/0
413	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND , .	04/1995	900.05 -	900.05	853.83	12/2011 12/2010	-	-	0/0
414	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA , .	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
415	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA , .	02/1997	295.00 -	1,289.92	1,092.98	- -	-	-	0/0
416	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN , .	02/1997	410.08 -	410.08	297.58	- -	-	-	0/0
417	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE , .	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
418	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU , .	02/1997	155.55 -	800.00	800.70	- -	-	-	0/0
419	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA , .	04/1997	227.00 997.58	2,135.00	117.24	- -	-	-	0/0
420	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND , .	03/1999	2,957.21 -	2,957.21	1,966.90	07/2005 -	-	-	0/0
421	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR , .	04/1997	501.69 501.69	1,043.56	819.19	03/2012 -	-	-	0/0
422	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA , .	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
423	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR , .	04/1997	162.87 -	541.00	158.58	- -	-	-	0/0
424	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE , .	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
425	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU , .	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
426	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE , .	03/1998	280.00 -	1,122.00	889.95	- -	-	-	0/6
427	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH , .	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
428	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL , .	03/2000	1,049.69 3,385.14	3,404.92	3,551.53	12/2006 -	-	-	0/0
429	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE , .	04/1998	92.63 -	270.00	376.18	02/2011 02/2011	-	-	0/0
430	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL , .	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
431	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE , .	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
432	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA , .	04/1996	138.00 -	1,382.78	2.81	- -	-	-	0/0
433	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA , .	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
434	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA , .	04/1996	301.64 -	1,185.64	577.84	- 09/2009	-	-	0/0
435	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR , .	04/2003	528.65 -	324.66	227.03	- -	-	-	0/0
436	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR , .	04/2002	322.95 -	341.41	325.36	03/2012 -	-	-	0/0
437	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND , .	04/2002	459.91 -	418.17	260.67	- -	-	-	0/0
438	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR , .	04/2001	406.92 -	339.00	204.83	- -	-	-	0/0
439	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR , .	04/2003	218.19 -	343.00	216.17	- -	-	-	0/0
440	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE , .	04/2005	230.03 -	230.03	172.58	- -	-	-	0/0
441	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA , .	04/1998	183.23 -	1,202.70	185.46	02/2015 -	-	-	0/0
442	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA , .	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
443	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH , .	04/2003	136.62 -	360.00	357.91	12/2007 03/2010	-	-	0/0
444	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR , .	04/1996	332.92 332.92	477.88	498.37	03/2012 -	-	-	0/0
445	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA , .	04/2006	378.56 -	791.59	5.41	- -	-	-	0/0
446	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND , .	03/1997	261.70 -	360.00	253.92	02/2006 -	-	-	0/0
447	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH , .	07/2006	743.00 -	732.81	770.18	03/2008 06/2008	-	-	0/0
448	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU , .	09/2007	404.19 -	1,383.45	457.88	- -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
449	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE , .	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
450	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU , .	09/2006	125.00 -	490.00	67.57	-	-	-	0/0
451	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU , .	09/2006	456.00 -	1,080.00	194.61	-	-	-	0/0
452	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH , .	04/2006	325.00 2,434.00	2,434.00	419.45	03/2010 -	-	-	0/0
453	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL , .	04/2007	1,106.62 -	1,106.62	244.99	12/2010 -	-	-	0/0
454	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL , .	04/2010	2,298.42 -	1,655.68	38.46	03/2014 -	-	-	0/0
455	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN , PPP (BOT)	04/2008	653.19 -	653.55	258.78	03/2014 -	-	-	0/0
456	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN , .	04/2008	516.23 732.06	516.23	597.72	03/2014 -	-	-	0/0
457	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND , .	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
458	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL , .	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0
459	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL , .	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
460	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH , .	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
461	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT , .	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
462	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT , .	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
463	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT , .	04/2008	318.24 -	321.62	2.91	03/2012 -	-	-	0/0
464	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT , .	04/2006	117.36 196.95	196.95	198.83	03/2011 -	-	-	0/0
465	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH , .	03/2013	307.00 -	307.00	-	-	-	-	0/0
466	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE , .	03/2007	243.78 -	243.78	30.05	-	-	-	0/0
467	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH , .	03/2008	195.64 -	195.64	94.11	-	-	-	0/0
468	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH , .	03/2012	199.75 -	199.75	76.08	-	-	-	0/0
469	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE , .	03/2013	295.00 -	494.92	4.22	-	-	-	0/0
470	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH , .	03/2013	643.00 -	643.00	-	-	-	-	0/0
471	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN , .	04/2012	246.08 -	246.08	4.20	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
472	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE , .	04/2007	1,347.26 -	1,347.26 -	164.55 -	- -	- -	- -	0/0
473	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE , .	04/2007	1,640.04 -	1,640.04 -	187.84 -	- -	- -	- -	0/0
474	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT , .	04/2012	567.18 -	567.18 -	31.99 -	- -	- -	- -	0/0
475	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT , .	04/2012	376.59 -	376.59 -	4.58 -	- -	- -	- -	0/0
476	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT , .	04/2011	439.88 -	439.88 -	0.78 -	- -	- -	- -	0/0
477	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT , .	04/1994	320.66 913.48	913.48 -	457.67 -	- -	- -	- -	0/0
478	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT , .	04/2011	446.00 -	685.17 -	206.59 -	- -	- -	- -	0/0
479	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT , .	04/2010	279.40 -	279.40 -	249.02 -	- -	- -	- -	0/0
480	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE , .	04/2011	2,082.75 -	3,500.00 -	54.23 -	- -	- -	- -	0/0
481	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN , .	04/2013	236.93 -	262.00 -	0.41 -	- -	- -	- -	0/0
482	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN , .	04/2013	822.00 -	822.00 -	- -	- -	- -	- -	0/0
483	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN , .	04/2013	323.00 -	323.00 -	- -	- -	- -	- -	0/0
484	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN , .	04/2013	456.00 -	855.16 -	557.82 -	- -	- -	- -	0/0
485	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN , .	04/2010	739.65 -	872.22 -	794.11 -	- -	- -	- -	0/0
486	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN , .	04/2011	239.73 -	179.32 -	75.76 -	- -	- -	- -	0/0
487	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN , .	04/2011	213.39 -	218.39 -	23.63 -	- -	- -	- -	0/0
488	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN , .	04/2012	288.97 -	288.97 -	1.09 -	- -	- -	- -	0/0
489	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN , .	04/2013	242.09 -	242.09 -	0.39 -	- -	- -	- -	0/0
490	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL , .	04/2010	267.37 -	434.00 -	35.90 -	- -	- -	- -	0/0
491	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL , .	04/2011	289.64 -	760.00 -	0.09 -	- -	- -	- -	0/0
492	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR , .	04/2008	490.80 -	490.80 -	0.39 -	- -	- -	- -	0/0
493	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR , .	04/2008	620.57 -	620.57 -	- -	- -	- -	- -	0/0
494	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR , .	04/2008	445.25 -	445.25 -	1.14 -	- -	- -	- -	0/0
495	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE , .	04/2008	415.67 -	415.67 -	14.00 -	- -	- -	- -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
496	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR , .	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
497	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR , .	04/1999	175.69 -	325.00	259.31	- -	-	-	0/0
498	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR , .	04/2006	285.07 -	378.56	111.87	- -	-	-	0/0
499	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR , .	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
500	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR , .	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
501	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR , .	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
502	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR , .	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
503	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR , .	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
504	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR , .	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
505	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR , .	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
506	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR , .	04/2004	372.14 -	355.81	294.07	- -	-	-	0/0
507	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR , .	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
508	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR , .	04/2013	213.01 -	367.17	17.19	- -	-	-	0/0
509	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU , .	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
510	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE , .	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0
511	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU , .	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
512	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU , .	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
513	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU , .	04/1998	271.24 -	520.00	462.69	- -	-	-	0/0
514	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE , .	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
515	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE , .	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
516	KUMBALAM-TURAVUR - [N22000191]SR,KERALA , .	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
517	ERODE-PALANI - [N22000199]SR,TAMIL NADU , .	04/2008	288.57 -	603.22	1.64	- -	-	-	0/0
518	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU , .	04/2008	164.41 -	450.00	16.97	- -	-	-	0/0
519	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA , .	04/2006	191.72 -	222.95	112.40	- -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
520	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA , .	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
521	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL , .	04/2009	573.78 -	573.78	166.89	-	-	-	0/0
522	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE , .	04/2011	601.43 -	800.00	0.69	-	-	-	0/0
523	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE , .	04/1987	406.99 -	406.99	141.55	-	-	-	0/0
524	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE , .	04/2007	450.00 -	450.00	7.91	-	-	-	0/0
525	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE , .	04/2010	172.03 -	172.03	5.86	-	-	-	0/0
526	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE , .	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
527	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE , .	04/2011	288.35 -	288.35	9.60	-	-	-	0/0
528	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE , .	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
529	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE , .	04/2000	157.17 -	157.17	76.90	-	-	-	0/0
530	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONG WITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE , .	04/2001	923.52 -	923.52	208.10	-	-	-	0/0
531	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE , .	04/2005	595.91 -	595.91	89.60	-	-	-	0/0
532	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE , .	04/2010	174.56 -	174.56	63.08	-	-	-	0/0
533	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE , .	04/2010	277.28 -	277.28	67.82	-	-	-	0/0
534	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE , .	04/2010	296.44 -	296.44	4.55	-	-	-	0/0
535	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE , .	04/2010	157.94 -	157.94	43.34	-	-	-	0/0
536	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA , .	04/2008	499.30 -	2,501.05	84.11	-	-	-	0/0
537	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA , .	04/2011	277.70 -	279.70	4.73	-	-	-	0/0
538	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE , .	04/2007	450.55 -	450.55	13.53	-	-	-	0/0
539	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE , .	04/2010	365.17 -	365.17	1.35	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
540	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE , .	04/2011	267.09 -	267.09	1.50	-	-	-	0/0
541	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE , .	04/2011	193.44 -	193.44	53.01	-	-	-	0/0
542	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE , .	04/2011	175.80 -	175.80	1.46	-	-	-	0/0
543	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE , .	04/2010	494.54 -	494.54	31.20	-	-	-	0/0
544	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE , .	04/2000	297.47 -	297.47	51.82	-	-	-	0/0
545	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA & CHAND - [N22000242]ER,MULTI STATE , .	04/2003	337.96 -	337.96	61.36	-	-	-	0/0
546	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE , .	04/2009	493.96 -	493.96	121.27	-	-	-	0/0
547	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA , .	04/2011	184.06 -	184.06	15.23	-	-	-	0/0
548	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE , .	04/2010	268.52 -	268.52	78.81	-	-	-	0/0
549	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE , .	04/2011	166.89 -	166.89	0.02	-	-	-	0/0
550	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA , .	04/2012	297.85 -	297.85	7.17	-	-	-	0/0
551	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA , .	04/2011	913.00 -	1,801.01	1.47	-	-	-	0/0
552	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA , .	04/2007	179.65 -	1,350.91	380.62	-	-	-	0/0
553	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA , .	04/2010	377.93 -	986.30	100.76	-	-	-	0/0
554	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA , .	04/2013	1,112.00 -	1,112.00	-	-	-	-	0/0
555	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE , .	04/2013	723.00 -	723.00	-	-	-	-	0/0
556	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE , .	04/2008	184.26 -	2,000.00	17.32	-	-	-	0/0
557	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE , .	04/2012	923.23 -	923.23	1.01	-	-	-	0/0
558	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH , .	04/2011	283.54 -	283.54	0.31	-	-	-	0/0
559	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH , .	04/2012	377.44 -	377.44	7.50	-	-	-	0/0
560	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB , .	04/2009	396.04 -	369.00	188.93	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
561	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI , .	04/1999	156.65 -	156.65	53.00	- -	-	-	0/0
562	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH , .	04/2013	654.00 -	654.00	-	- -	-	-	0/0
563	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE , .	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
564	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA , .	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
565	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH , .	04/2008	1,046.88 -	2,966.99	40.80	- -	-	-	0/0
566	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE , .	04/2007	336.91 -	336.91	144.25	- -	-	-	0/0
567	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA , .	04/2013	558.00 -	692.43	-	- -	-	-	0/0
568	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE , .	04/2013	296.00 -	466.65	-	- -	-	-	0/0
569	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA , .	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0
570	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE , .	04/2007	970.34 -	1,743.00	359.06	- -	-	-	0/0
571	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA , .	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
572	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI , .	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
573	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH , .	04/2013	829.00 -	829.00	-	- -	-	-	0/0
574	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA , .	04/2011	390.60 -	390.60	4.69	- -	-	-	0/0
575	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH , .	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
576	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE , .	04/2010	337.49 -	337.50	0.21	- -	-	-	0/0
577	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE , .	04/2008	2,050.00 -	2,050.00	194.45	- -	-	-	0/0
578	HARIDWAR-LAKSAR - [N22000289]NR,UTARAKHAND , .	04/2012	219.83 -	329.97	2.38	- -	-	-	0/0
579	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE , .	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
580	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE , .	04/2008	162.96 -	162.96	143.62	- -	-	-	0/0
581	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA , .	04/2013	400.00 -	400.00	-	- -	-	-	0/0
582	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE , .	04/2013	876.00 -	876.00	-	- -	-	-	0/0
583	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH , .	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0
584	QADIAN-BEAS - [N22000295]NR,PUNJAB , .	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
585	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE , .	04/2007	328.14 -	328.14	0.31	- -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
586	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA , .	04/2010	2,127.00 -	2,127.00	325.00	-	-	-	0/0
587	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA , .	04/2011	146.75 -	167.50	0.32	-	-	-	0/0
588	GADAG-WADI NL - [N22000299]SWR,KARNATAKA , .	04/2013	1,117.00 -	1,922.00	1.89	-	-	-	0/0
589	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA , .	04/2013	327.25 -	367.77	-	-	-	-	0/0
590	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE , .	04/2012	250.93 -	250.93	0.14	-	-	-	0/0
591	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL , .	04/2012	255.64 -	255.64	-	-	-	-	0/0
592	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU , .	04/1999	460.94 -	1,030.00	-	01/1999 -	-	-	0/0
593	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE , .	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
594	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE , .	04/2008	466.48 -	800.00	0.83	01/1999 -	-	-	0/0
595	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA , .	04/2012	285.57 -	279.54	1.38	01/1999 -	-	-	0/0
596	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL , .	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
597	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA , .	03/2011	679.27 -	1,111.99	60.31	-	-	-	0/0
598	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA , .	03/2013	858.67 -	837.33	1.15	-	-	-	0/0
599	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA , .	03/2006	201.00 -	230.00	218.67	-	-	-	0/0
600	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA , .	03/2011	165.16 -	234.71	137.01	03/2015 -	-	-	0/0
601	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH , .	04/2014	182.92 -	197.73	-	-	-	-	0/0
602	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU , .	04/2011	190.10 -	190.10	33.19	-	-	-	0/0
603	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA , .	03/2015	1,900.00 -	1,900.00	-	-	-	-	0/0
604	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE , .	05/2015	600.00 -	600.00	-	-	-	-	0/0
605	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE , .	03/2015	1,830.00 -	1,830.00	-	-	-	-	0/0
606	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE , .	05/2015	860.43 -	860.43	-	-	-	-	0/0
607	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR , .	05/2015	380.00 -	380.00	-	-	-	-	0/0
608	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN , .	05/2015	873.71 -	873.71	-	-	-	-	0/0
609	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA , .	05/2015	400.00 -	400.00	-	-	-	-	0/0
610	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA , .	03/2015	960.00 -	960.00	-	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
611	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE , .	03/2015	1,618.00 -	1,618.00	-	-	-	-	0/0
612	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE , .	05/2015	720.00 -	720.00	-	-	-	-	0/0
	Total		172,717.67 -	301,331.54	92,996.30				1/7
	ROAD TRANSPORT AND HIGHWAYS								
613	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM , .	12/2003	157.47 -	157.47	-	09/2007 -	-	-	0/0
614	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR , .	12/2003	300.00 -	300.00	-	10/2008 -	-	-	0/0
615	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH , .	12/2003	251.03 -	251.03	-	10/2008 -	-	-	0/0
616	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL , .	12/2003	225.00 -	225.00	-	07/2008 -	-	-	0/0
617	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
618	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM , .	12/2003	200.00 -	200.00	-	06/2008 -	-	-	0/0
619	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	-	12/2009 -	-	-	0/0
620	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA , .	03/2005	557.00 -	557.00	932.30	02/2010 -	-	-	0/0
621	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	-	08/2011 -	-	-	2/2
622	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH , .	05/2009	572.30 -	572.30	761.40	10/2011 -	-	-	0/0
623	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA , .	09/2010	946.00 -	946.00	-	-	-	-	3/3
624	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU , PPP (BOT)	09/2010	1,655.00 -	1,655.00	-	09/2013 -	-	-	0/0
625	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	-	11/2013 -	-	-	0/0
626	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND , .	08/2010	625.07 -	625.07	-	01/2013 -	-	-	0/0
627	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA , PPP (BOT)	09/2010	671.00 -	671.00	-	-	-	-	2/3
628	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA , .	04/2011	807.00 -	807.00	-	10/2014 -	-	-	0/0
629	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA , .	12/2010	453.00 -	453.00	487.90	-	-	-	1/1
630	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA , .	12/2010	480.00 -	480.00	438.00	-	-	-	2/2
631	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA , .	11/2010	680.00 -	680.00	-	-	-	-	2/2
632	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT , PPP (BOT)	03/2011	785.50 -	785.50	-	08/2013 -	-	-	0/3

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
633	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA , .	02/2011	226.00 -	226.00 -	-	02/2014 -	-	-	0/0
634	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR , .	12/2011	325.51 -	325.00 -	160.20	05/2014 -	-	-	0/0
635	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH , .	10/2011	209.00 -	209.00 -	-	01/2013 -	-	-	0/0
636	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA , .	11/2011	909.00 -	909.00 -	844.10	05/2014 -	-	-	0/0
637	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH , .	07/1999	635.90 -	635.90 -	-	07/2012 -	-	-	0/0
638	FOUR LANNING OF WALAYAR-VADAKKANANCHERRY SECTION - [N24000214]NHAI,KERALA , .	04/2011	682.00 -	682.00 -	34.81	10/2013 -	-	-	0/0
639	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH , .	10/2012	250.50 -	250.50 -	-	10/2014 -	-	-	0/0
640	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH , .	09/2013	606.00 -	606.00 -	-	-	-	-	0/0
641	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA , .	04/2014	1,123.17 -	1,123.17 -	-	-	-	-	0/0
642	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA , .	03/2011	218.31 -	339.82 -	282.02	12/2015 -	-	-	0/3
643	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33 -	298.33 -	-	-	-	-	0/4
644	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05 -	-	-	-	-	0/4
645	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16 -	-	-	-	-	0/4
646	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12 -	-	02/2015 -	-	-	0/4
647	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH , .	01/2014	361.30 -	361.30 -	-	07/2014 -	07/2014	-	0/1
648	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00 -	-	-	-	-	0/1
649	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00 -	-	-	-	-	0/4
650	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43 -	-	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
651	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	-	- -	-	-	0/0
652	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	50.94	- -	-	-	0/0
653	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	-	- -	-	-	0/0
654	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	20.70	03/2015 -	-	-	0/0
655	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	5.26	03/2015 -	-	-	0/0
656	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	10.14	03/2015 -	-	-	0/0
657	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	12/2015 -	12/2015	-	0/0
658	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	111.73	12/2012 -	-	-	0/0
659	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	96.04	- -	-	-	0/0
660	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
661	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	8.89	03/2015 -	-	-	0/0
662	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	15.50	- -	-	-	0/0
663	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	29.39	- -	-	-	0/0
664	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	256.48	- -	-	-	0/0
665	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	198.10	- -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
666	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	-	-	-	0/0
667	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	27.00	01/2015 -	-	-	0/0
668	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	15.17	01/2015 -	-	-	0/0
669	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
670	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	171.16	04/2014 -	-	-	0/0
671	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	131.09	03/2015 -	-	-	0/0
672	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM , ITEM RATE	08/2010	186.96 -	186.96	132.80	-	-	-	0/0
673	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	219.50	03/2011 -	-	-	0/0
674	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	140.75	02/2012 -	-	-	0/0
675	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	122.00	10/2010 -	-	-	0/0
676	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	4.39	03/2011 -	-	-	0/0
677	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	12.66	05/2012 -	-	-	0/0
678	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	7.19	08/2013 -	-	-	0/0
679	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
680	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	49.42	02/2013 -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
681	WIDENING OF 2(TWO) LANE OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
682	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	20.80	08/2015 -	08/2015	-	0/0
683	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 161.70	161.70	2.55	07/2015 -	07/2015	-	0/0
684	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 158.35	154.14	2.55	08/2015 -	08/2015	-	0/0
685	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
686	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	-	- -	-	-	0/0
687	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	45.64	- -	-	-	0/0
688	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	25.87	- -	-	-	0/0
689	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	89.68	- -	-	-	0/0
690	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	-	02/2015 -	-	-	0/0
691	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	-	05/2015 -	05/2015	-	0/0
692	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
693	CONST. OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	-	- -	-	-	0/0
694	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	51.28	- -	-	-	0/0
695	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	12.08	- -	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
696	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16	264.16	-	-	-	-	0/0
697	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02	847.02	299.55	-	-	-	0/0
698	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48	1,494.48	2,090.00	02/2011	02/2011	-	0/0
699	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24	889.24	388.43	-	-	-	0/0
700	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80	257.00	-	05/2015	-	-	0/0
701	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20	470.20	7.97	02/2011	02/2011	-	0/0
702	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38	578.38	-	-	-	-	0/0
703	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83	789.83	72.79	-	-	-	0/0
704	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21	333.21	-	11/2015	11/2015	-	0/0
705	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00	165.00	135.01	09/2010	09/2010	-	0/0
706	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00	201.00	-	09/2010	09/2010	-	0/0
707	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18	2,288.18	-	-	-	-	0/0
708	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA , .	07/2015	1,282.94	1,282.94	-	-	-	-	0/0
709	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	01/1991	225.02	225.02	-	-	-	-	0/0
710	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	01/1991	223.30	223.30	-	-	-	-	0/0
711	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01	520.01	-	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
712	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA , .	09/2015	414.51 -	414.00	-	-	-	-	0/0
713	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH , .	06/2015	583.79 -	583.79	-	-	-	-	0/0
714	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL , .	10/2015	531.13 -	531.13	-	-	-	-	0/0
715	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH,WEST BENGAL , .	10/2015	361.15 -	361.15	-	-	-	-	0/0
716	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	01/1991	289.99 -	289.99	-	-	-	-	0/0
717	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,885.74 -	1,885.74	-	-	-	-	0/0
718	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA , .	10/2015	593.26 -	593.26	-	-	-	-	0/0
719	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA , .	12/2015	649.50 -	649.50	-	-	-	-	0/0
720	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	-	-	-	-	0/0
721	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	-	02/2015	-	-	0/0
722	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	-	-	-	0/0
723	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA , .	08/2015	505.00 -	505.00	-	-	-	-	0/0
724	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	-	-	-	-	0/0
725	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,012.90 -	1,012.90	-	-	-	-	0/0
726	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA , .	06/2015	845.24 -	845.24	-	-	-	-	0/0
727	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU , .	01/1991	285.00 -	285.00	-	01/2008	-	-	0/0
728	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH , .	03/2015	795.76 -	795.76	-	-	-	-	0/0
729	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH , .	03/2015	794.30 -	794.30	-	-	-	-	0/0
730	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013	-	-	0/0
731	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA , .	09/2005	168.00 -	168.00	-	06/2006	-	-	0/0

Sector Wise Details									
(January 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
732	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR , .	08/2015	556.07 -	556.07	-	-	-	-	0/0
733	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS , .	09/2015	273.06 -	273.06	-	-	-	-	0/0
734	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR , .	12/2015	1,041.10 -	1,041.10	-	-	-	-	0/0
735	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR , .	08/2015	814.04 -	814.04	-	-	-	-	0/0
736	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA , .	12/2015	752.28 -	752.28	-	-	-	-	0/0
737	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL , .	12/2015	1,423.96 -	1,423.96	-	-	-	-	0/0
738	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH , .	03/2015	928.83 -	928.83	-	-	-	-	0/0
739	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	01/1991	1,388.00 -	1,388.00	-	-	-	-	0/0
740	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH , .	12/2015	596.67 -	596.67	-	-	-	-	0/0
741	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR , .	08/2015	322.09 -	322.09	-	-	-	-	0/0
742	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH , .	12/2015	509.13 -	509.13	-	-	-	-	0/0
743	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH , .	03/2015	810.22 -	810.22	-	-	-	-	0/0
744	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	-	-	-	-	0/0
745	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR , .	01/1991	642.41 -	642.41	-	-	-	-	0/0
746	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR , .	01/1991	1,167.45 -	1,167.45	-	-	-	-	0/0
747	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH , .	12/2015	726.67 -	726.67	-	-	-	-	0/0
748	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	-	-	-	0/0
749	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	-	-	-	-	0/0
750	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	-	-	-	-	0/0
751	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA , .	12/2015	479.20 -	479.20	-	-	-	-	0/0
752	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR , .	08/2015	399.54 -	399.54	-	-	-	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
753	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR , .	01/1991	478.35 -	478.35 -	-	-	-	-	0/0
754	TWO LANING WITH PS OF CHHAPRA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN , .	08/2015	275.90 -	275.90 -	-	-	-	-	0/0
755	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR , .	08/2015	516.13 -	516.13 -	16.60	-	-	-	0/0
756	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB , EPC	06/2015	892.17 -	892.17 -	14.70	-	-	-	0/0
757	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD, PUNJAB , EPC	06/2015	899.21 -	899.21 -	13.13	-	-	-	0/0
758	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00 -	-	07/2008 -	-	-	0/0
759	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH, UTTAR PRADESH , EPC	12/2014	207.88 -	207.88 -	-	-	-	-	0/0
760	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD, BIHAR , EPC	01/1991	154.62 -	154.62 -	-	-	-	-	0/0
761	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD, BIHAR , EPC	01/1991	319.68 -	319.68 -	-	-	-	-	0/0
762	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM , .	12/2003	198.16 -	198.16 -	242.40	04/2008 01/2016	01/2016	93(O) 0(R)	0/0
763	NALBARI T BIJINI (AS-7) - [N24000048]NHAI, ASSAM , .	12/2003	208.00 230.00	208.00	295.20	04/2008 01/2017	01/2017	105(O) 0(R)	0/0
764	SIX LANNING OF HOSUR - KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU , PPP (BOT)	06/2011	535.00 -	535.00 -	-	12/2013 -	01/2016	25(O) -	0/0
765	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT , PPP (BOT)	09/2010	805.39 -	805.39 -	-	03/2013 -	01/2016	34(O) -	0/0
766	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI, RAJASTHAN , .	01/2014	177.32 -	177.32 -	86.65	01/2016 -	01/2016	0(O) -	0/0
767	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA , EPC	03/2015	153.21 -	153.21 -	-	01/2017 -	01/2017	0(O) -	0/0
768	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL, ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82 -	-	01/2019 -	01/2019	0(O) -	0/0
769	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB , .	01/2014	523.85 -	523.85 -	54.84	01/2016 -	01/2016	0(O) -	0/0
770	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU , .	07/2014	401.11 -	401.11 -	-	01/2017 -	01/2017	0(O) -	0/0
771	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH , .	06/2014	301.04 -	301.04 -	31.28	01/2016 -	01/2016	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
772	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
773	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
774	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2016 -	01/2016	0(O) -	0/0
775	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	-	10/2011 -	01/2016	51(O) -	0/0
776	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	876.68	-	01/2018	-	0/0
777	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,055.00	-	11/2015 -	01/2016	2(O) -	0/0
778	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH , PPP (BOT)	03/2015	830.36 -	830.36	-	01/2019 -	01/2016	-36(O) -	0/0
779	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018	0(O) -	0/0
780	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM , .	12/2003	264.72 -	264.72	-	06/2008 -	02/2016	92(O) -	0/0
781	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	-	05/2010 -	02/2016	69(O) -	0/0
782	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	-	09/2012 -	02/2016	41(O) -	2/3
783	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN , PPP (BOT)	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38(O) -	0/0
784	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31(O) -	0/0
785	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN , PPP (ANNUITY)	03/2012	333.51 -	333.51	271.60	09/2014 -	02/2016	17(O) -	0/0
786	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(O) -	0/0
787	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH .	02/2015	241.61 -	241.61	23.83	02/2017 -	02/2017	0(O) -	0/1
788	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017	0(O) -	0/0
789	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24(O) -	0/1

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
790	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN , .	08/2015	538.08 -	538.08 -	-	02/2018 -	02/2018	0(O) -	0/0
791	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA , .	08/2015	723.54 -	723.54 -	124.59	02/2018 -	02/2018	0(O) -	0/0
792	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN , .	08/2015	482.27 -	482.27 -	-	02/2018 -	02/2018	0(O) -	0/0
793	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80 -	-	02/2016 -	02/2016	0(O) -	0/0
794	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22 -	106.61	02/2018 -	02/2018	0(O) -	0/0
795	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31 -	-	02/2018 -	02/2018	0(O) -	0/0
796	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN , PPP (BOT)	03/2012	914.50 -	914.50 -	1,097.62	10/2015 -	02/2016	4(O) -	0/0
797	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH , .	12/2003	155.00 -	201.66 -	240.22	09/2008 -	03/2016	90(O) -	0/0
798	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM , .	12/2003	280.00 -	361.00 -	392.60	02/2009 -	03/2016	85(O) -	0/0
799	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM , .	12/2003	199.81 -	385.13 -	-	04/2009 -	03/2016	83(O) -	0/0
800	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM , .	12/2003	167.64 -	167.64 -	-	11/2008 -	03/2016	88(O) -	0/0
801	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM , .	12/2003	155.04 -	280.13 -	-	11/2008 -	03/2016	88(O) -	0/0
802	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM , .	12/2003	200.00 -	200.00 -	-	04/2009 -	03/2016	83(O) -	0/0
803	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM , .	12/2003	195.00 -	195.00 -	278.96	06/2008 -	03/2016	93(O) -	0/0
804	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM , .	12/2003	237.80 -	237.80 -	374.10	06/2008 -	03/2016	93(O) -	0/0
805	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR , .	12/2003	332.94 -	332.94 -	-	09/2008 -	03/2016	90(O) -	0/0
806	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN , .	12/2003	275.00 -	250.39 -	273.26	10/2008 -	03/2016	89(O) -	0/0
807	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM , .	12/2003	196.00 -	331.23 -	300.46	07/2009 -	03/2016	80(O) -	0/0
808	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH , .	12/2003	348.16 -	348.16 -	322.70	09/2007 -	03/2016	102(O) -	0/0
809	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN , PPP (BOT)	11/2009	795.00 -	795.00 -	1,607.78	05/2012 -	03/2016	46(O) -	0/0
810	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00 -	-	04/2013 -	03/2016	35(O) -	0/0
811	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00 -	-	08/2012 -	03/2017	55(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
812	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33(O) -	0/0
813	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19(O) -	0/0
814	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	03/2016	34(O) -	0/0
815	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28(O) -	0/0
816	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	-	08/2013 -	03/2017	43(O) -	0/0
817	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29(O) -	0/0
818	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	609.00	02/2014 -	03/2016	25(O) -	0/0
819	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	760.20	03/2014 -	03/2016	24(O) -	0/0
820	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR , .	10/2011	375.09 -	375.09	348.00	04/2014 -	03/2016	23(O) -	0/0
821	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	544.08	11/2013 -	03/2016	28(O) -	0/0
822	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND , .	02/2012	398.00 -	398.00	-	02/2014 -	03/2016	25(O) -	0/0
823	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA , PPP (BOT)	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26(O) -	0/0
824	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31(O) -	0/0
825	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN , .	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37(O) -	0/0
826	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN , PPP (BOT)	12/2011	2,388.51 -	2,388.00	2,301.00	06/2014 -	03/2016	21(O) -	0/0
827	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE , PPP (BOT)	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21(O) -	0/0
828	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA , PPP (BOT)	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17(O) -	0/0
829	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE , .	12/2011	942.69 -	942.69	229.16	06/2014 -	03/2016	21(O) -	0/0
830	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE , PPP (BOT)	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7(O) -	0/0
831	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU , PPP (BOT)	06/2013	1,287.95 -	1,287.95	-	11/2015 -	03/2017	16(O) -	0/0
832	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN , .	03/2014	240.10 -	240.10	144.69	03/2016 -	03/2016	0(O) -	0/0
833	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	-	03/2016 -	03/2016	0(O) -	0/4
834	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	-	03/2016 -	03/2016	0(O) -	0/4

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
835	YAN TO NIRMAL SEREABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	-	03/2016 -	03/2016	0(0) -	1/4
836	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	03/2016	0(0) -	0/4
837	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	50.85	03/2016 -	03/2016	0(0) -	1/4
838	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	03/2015	829.00 -	829.00	-	03/2018 -	03/2018	0(0) -	0/4
839	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018	0(0) -	0/4
840	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	31.64	03/2016 -	03/2016	0(0) -	0/0
841	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR , .	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88(0) -	0/0
842	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN , .	09/2015	567.51 -	567.51	42.79	03/2018 -	03/2018	0(0) -	0/0
843	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	-	03/2017 -	03/2017	0(0) -	0/0
844	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017	0(0) -	0/0
845	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	-	03/2018 -	03/2018	0(0) -	0/0
846	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , EPC	01/1991	322.00 -	322.00	-	03/2018 -	03/2018	0(0) -	0/0
847	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	-	03/2017 -	03/2017	0(0) -	0/0
848	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	-	03/2017 -	03/2017	0(0) -	0/0
849	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH , .	09/2015	768.56 -	768.56	-	03/2018 -	03/2018	0(0) -	0/0
850	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH , .	09/2015	664.53 -	664.53	-	03/2018 -	03/2018	0(0) -	0/0
851	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH , .	09/2015	789.31 -	789.31	-	03/2018 -	03/2018	0(0) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
852	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,HARYANA , .	09/2015	788.51 -	788.51	-	03/2018 -	03/2018	0(O) -	0/0
853	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH , .	09/2015	785.78 -	785.78	-	03/2018 -	03/2018	0(O) -	0/0
854	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	-	03/2018 -	03/2018	0(O) -	0/0
855	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH , .	09/2015	934.46 -	934.46	-	03/2018 -	03/2018	0(O) -	0/0
856	FOUR LANING OF ORISSA/CHHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATTISGARH , .	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7(O) -	0/0
857	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH , .	06/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016	0(O) -	0/0
858	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7(O) -	0/0
859	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA , .	02/2010	650.00 -	650.00	813.91	-	03/2016	-	0/0
860	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31(O) -	0/0
861	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM , .	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016	94(O) 0(R)	0/0
862	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE , .	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67(O) -	0/0
863	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,409.36	07/2012 -	04/2016	45(O) -	3/3
864	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,004.62	07/2013 -	04/2016	33(O) -	0/0
865	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32(O) -	0/0
866	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	504.51	03/2014 -	04/2017	37(O) -	0/0
867	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	822.96	04/2015 -	04/2016	12(O) -	0/0
868	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79	584.72	04/2016 -	04/2016	0(O) -	0/0
869	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	36.02	-	04/2018	-	0/1
870	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	49.78	04/2017 -	04/2017	0(O) -	0/3
871	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN , .	10/2014	206.12 -	206.12	102.21	04/2017 -	04/2017	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
872	JODHPUR - BARMER SECTION OF PACKAGE - I - [N24000354]NHAI,RAJASTHAN , .	10/2014	264.72 -	264.72	83.61	04/2017 -	04/2017	0(O) -	0/0
873	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA , .	10/2015	562.34 -	562.34	-	04/2018 -	04/2018	0(O) -	0/0
874	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12(O) -	0/0
875	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	-	04/2018 -	04/2018	0(O) -	0/0
876	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN , .	12/2003	275.00 -	281.31	149.27	02/2010 -	05/2017	87(O) -	0/0
877	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
878	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE , PPP (BOT)	02/2011	580.43 -	580.43	221.98	08/2013 -	05/2017	45(O) -	0/0
879	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,287.44	09/2014 -	05/2016	20(O) -	0/0
880	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	461.94	06/2015 -	05/2017	23(O) -	0/0
881	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN , .	01/2014	158.04 -	158.04	85.68	12/2015 -	05/2016	5(O) -	0/0
882	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	0/4
883	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018	0(O) -	0/4
884	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	-	05/2018 -	05/2018	0(O) -	0/4
885	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN , .	11/2014	279.14 -	279.14	52.40	05/2017 -	05/2017	0(O) -	0/0
886	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH , .	05/2015	261.09 -	261.09	-	05/2017 -	05/2017	0(O) -	0/0
887	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	-	05/2017 -	05/2017	0(O) -	0/0
888	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017	0(O) -	0/0
889	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	-	05/2017 -	05/2017	0(O) -	0/0
890	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	-	05/2016 -	05/2016	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
891	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA , .	01/1991	229.41 -	229.41 -	-	05/2018 -	05/2018 -	0(O) -	0/0
892	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83 -	13.17	04/2015 -	05/2016 -	13(O) -	0/0
893	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08 -	28.86	05/2018 -	05/2018 -	0(O) -	0/4
894	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH , .	02/2015	327.32 -	327.32 -	-	05/2017 -	05/2017 -	0(O) -	0/0
895	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH , .	11/2015	867.66 -	867.66 -	18.68	11/2015 -	05/2018 -	30(O) -	0/0
896	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU , PPP (BOT)	04/2009	353.37 -	353.37 -	-	10/2011 -	06/2016 -	56(O) -	0/0
897	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00 -	3,619.94	11/2011 -	06/2016 -	55(O) -	0/0
898	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA , .	02/2010	390.56 -	390.56 -	-	02/2012 -	06/2013 -	-	0/0
899	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00 -	863.58	03/2013 -	06/2016 -	39(O) -	0/0
900	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00 -	-	07/2015 -	06/2016 -	11(O) -	0/0
901	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76 -	-	07/2013 -	06/2016 -	35(O) -	0/0
902	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50 -	-	06/2013 -	06/2016 -	36(O) -	0/3
903	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU , .	06/2011	600.00 -	600.00 -	-	06/2013 -	06/2016 -	36(O) -	0/0
904	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88 -	-	07/2013 -	06/2016 -	35(O) -	0/0
905	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00 -	-	01/2014 -	06/2016 -	29(O) -	0/0
906	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00 -	2,478.63	05/2014 -	06/2016 -	25(O) -	0/0
907	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70 -	-	06/2014 -	06/2016 -	24(O) -	0/0
908	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00 -	893.90	03/2013 -	06/2016 -	39(O) -	0/0
909	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00 -	1,840.00	09/2015 -	06/2016 -	9(O) -	0/0
910	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24 -	-	12/2015 -	06/2016 -	6(O) -	0/3

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
911	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21(O) -	0/3
912	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN , .	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5(O) -	0/0
913	REHABILITATION AND UPGRADE OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA , EPC	01/2014	446.77 -	446.77	-	- -	06/2017	- -	0/4
914	REHABILITATION AND UPGRADE OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD, ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24(O) -	0/4
915	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL, ASSAM , EPC	10/2014	437.39 -	437.39	-	06/2018 -	06/2018	0(O) -	0/4
916	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM , EPC	10/2014	463.49 -	463.49	-	06/2018 -	06/2018	0(O) -	0/4
917	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL, ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	-	06/2018 -	06/2018	0(O) -	0/0
918	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH, RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
919	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]NHAI, TAMIL NADU , .	12/2014	451.58 -	451.58	-	06/2017 -	06/2017	0(O) -	0/0
920	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI, UTTAR PRADESH , PPP (ANNUITY)	06/2014	569.38 -	569.38	344.00	06/2016 -	06/2016	0(O) -	0/0
921	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA , .	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24(O) -	0/0
922	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]DORTH, HARYANA , PPP (BOT)	03/2013	959.25 -	959.25	-	06/2016 -	06/2016	0(O) -	0/0
923	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH , .	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24(O) -	0/0
924	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL , .	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018	0(O) -	0/0
925	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR , .	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
926	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	-	06/2018 -	06/2018	0(O) -	0/0
927	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH , .	01/2016	815.28 -	815.28	-	06/2018 -	06/2018	0(O) -	0/0
928	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH , .	01/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018	0(O) -	0/0
929	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH , .	12/2015	667.00 -	667.00	-	06/2018 -	06/2018	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
930	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM , .	12/2003	245.00 -	245.00	214.17	03/2008 07/2016	07/2016	100(O) 0(R)	0/0
931	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE , PPP (BOT)	02/2011	998.79 -	998.79	-	08/2013 -	07/2017	47(O) -	0/0
932	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND , .	11/2011	478.51 -	478.00	277.06	10/2013 -	07/2016	33(O) -	0/0
933	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	-	07/2016 -	07/2016	0(O) -	0/0
934	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24(O) -	0/1
935	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	-	07/2017 -	07/2017	0(O) -	0/0
936	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN , .	07/2015	455.60 -	455.60	13.25	07/2017 -	07/2017	0(O) -	0/0
937	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA , .	01/2016	574.28 -	574.28	-	07/2018 -	07/2018	0(O) -	0/0
938	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	-	07/2017 -	07/2017	0(O) -	0/0
939	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB , .	09/2014	479.00 -	479.00	347.60	- -	07/2016	- -	0/0
940	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH , .	06/2016	667.00 -	667.00	-	07/2018 -	07/2018	0(O) -	0/0
941	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	-	07/2018 -	07/2018	0(O) -	0/0
942	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM , .	12/2003	175.96 -	175.96	304.17	04/2008 08/2016	08/2016	100(O) 0(R)	0/0
943	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM , .	12/2003	160.00 -	160.00	197.40	05/2008 07/2016	08/2016	99(O) 1(R)	0/0
944	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	1,050.90	05/2013 -	08/2016	39(O) -	0/0
945	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE , PPP (BOT)	02/2011	1,078.84 -	1,078.84	-	08/2013 -	08/2016	36(O) -	0/0
946	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH , .	01/2013	373.47 -	373.47	358.30	07/2014 -	08/2015	-	0/0
947	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,267.57	02/2014 -	08/2016	30(O) -	2/2
948	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23(O) -	0/4
949	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT , .	03/2014	503.16 -	503.16	-	08/2016 -	08/2016	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
950	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH, BIHAR , ITEM RATE	01/1991	282.41 -	282.41 -	-	08/2016 -	08/2016	0(O) -	0/0
951	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD, MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15 -	-	09/2015 -	08/2016	11(O) -	0/0
952	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07 -	229.01	08/2016 -	08/2016	0(O) -	0/0
953	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI, MADHYA PRADESH , PPP (BOT)	02/2012	912.00 -	912.00 -	-	08/2016 -	08/2016	0(O) -	0/0
954	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01 -	-	08/2016 -	08/2016	0(O) -	0/0
955	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA , .	04/2010	1,170.52 -	1,170.52 -	1,579.15	06/2012 -	08/2016	50(O) -	0/0
956	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD, MADHYA PRADESH , EPC	03/2015	511.83 -	511.83 -	-	08/2017 -	08/2017	0(O) -	0/0
957	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM , .	12/2003	217.61 309.56	309.56	370.66	04/2010 09/2016	09/2016	77(O) 0(R)	0/0
958	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00 -	-	05/2013 -	09/2016	40(O) -	0/0
959	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36 -	211.68	01/2014 -	09/2016	32(O) -	0/0
960	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60 -	-	09/2016 -	09/2016	0(O) -	0/0
961	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA , EPC	01/2014	255.75 348.00	348.43	-	09/2017 -	09/2017	0(O) -	0/0
962	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA , .	05/2015	709.00 -	709.00 -	-	09/2017 -	09/2017	0(O) -	0/0
963	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI, JHARKHAND , .	09/2015	341.61 -	341.61 -	69.55	09/2017 -	09/2017	0(O) -	0/0
964	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN , .	09/2014	425.19 -	425.19 -	167.91	09/2016 -	09/2016	0(O) -	0/0
965	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH , .	04/2014	351.34 -	351.34 -	132.64	01/2016 -	09/2016	8(O) -	0/0
966	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH , .	09/2015	368.73 -	368.73 -	50.37	09/2016 -	09/2017	12(O) -	0/0
967	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD, MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48 -	-	08/2015 -	09/2016	13(O) -	0/0
968	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI, HARYANA , .	12/2012	438.75 -	438.75 -	-	09/2016 -	09/2016	0(O) -	0/0
969	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00 -	994.21	-	09/2016	-	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
970	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00 -	-	09/2014 -	10/2016	25(O) -	0/0
971	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30 -	-	- -	10/2017	- -	0/4
972	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45 -	-	10/2015 -	10/2017	24(O) -	0/0
973	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16 -	19.72	10/2018 -	10/2018	0(O) -	0/4
974	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74 -	87.30	10/2016 -	10/2016	0(O) -	0/0
975	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH , .	04/2014	495.78 -	495.78 -	159.73	01/2016 -	10/2016	9(O) -	0/0
976	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN , .	01/1991	269.26 -	269.26 -	-	10/2016 -	10/2016	0(O) -	0/0
977	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04 -	-	10/2016 -	10/2016	0(O) -	0/0
978	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63 -	-	10/2017 -	10/2017	0(O) -	0/0
979	REHABILITATION AND UPGRADE TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22 -	-	10/2016 -	10/2016	0(O) -	0/0
980	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45 -	-	10/2016 -	10/2016	0(O) -	0/0
981	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80 -	-	10/2016 -	10/2016	0(O) -	0/0
982	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04 -	157.22	10/2010 -	10/2010	-	0/0
983	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN , .	10/2015	597.00 -	597.00 -	-	10/2017 -	10/2017	0(O) -	0/0
984	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00 -	-	10/2013 -	10/2013	-	0/0
985	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79 -	1,202.43	11/2016 -	11/2016	0(O) -	0/0
986	REHABILITATION AND UPGRADE OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA , EPC	06/2014	260.39 -	260.39 -	-	11/2016 -	11/2016	0(O) -	0/4

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
987	REHABILITATION AND UPGRADATION OF NH-222(61) FROM KM 161.570 TO 211.00 - [N24000255]NHDP, MAHARASHTRA , EPC	12/2013	220.72 -	220.72	-	11/2016 -	11/2016	0(O) -	0/4
988	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA , EPC	01/2014	267.16 352.00	352.05	-	11/2017 -	11/2017	0(O) -	0/0
989	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD, ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24(O) -	0/4
990	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD, ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	-	11/2014 -	11/2016	24(O) -	0/4
991	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL, ASSAM , EPC	03/2015	168.39 -	168.39	-	11/2018 -	11/2018	0(O) -	0/4
992	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM , EPC	10/2014	588.95 -	588.95	-	11/2018 -	11/2018	0(O) -	0/4
993	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA , EPC	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24(O) -	0/0
994	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA , EPC	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24(O) -	0/0
995	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU , .	05/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017	0(O) -	0/0
996	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU , .	11/2014	563.92 -	563.92	-	11/2016 -	11/2016	0(O) -	0/0
997	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA , EPC	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017	0(O) -	0/0
998	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM , .	12/2003	230.00 -	230.00	202.97	06/2005 -	12/2016	138(O) -	0/0
999	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM , .	12/2003	212.00 -	212.00	102.85	09/2007 -	12/2016	111(O) -	0/0
1000	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA , .	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49(O) -	0/0
1001	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39(O) -	0/0
1002	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,742.94	03/2013 -	12/2016	45(O) -	0/0
1003	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	879.98	02/2013 -	12/2016	46(O) -	0/0
1004	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	-	12/2013 -	12/2016	36(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1005	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00 -	-	05/2013 -	12/2016	43(O) -	0/0
1006	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00 -	604.50	07/2013 -	12/2016	41(O) -	0/0
1007	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA , PPP (BOT)	07/2011	586.00 -	586.00 -	-	01/2014 -	12/2016	35(O) -	0/0
1008	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00 -	425.65	09/2013 -	12/2016	39(O) -	0/0
1009	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR , PPP (BOT)	07/2012	356.40 -	356.40 -	344.00	07/2014 -	12/2017	41(O) -	0/0
1010	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE , PPP (ANNUITY)	04/2012	624.00 -	624.00 -	343.75	04/2014 -	12/2016	32(O) -	0/0
1011	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00 -	278.17	02/2015 -	12/2017	34(O) -	0/0
1012	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25 -	-	10/2015 -	12/2016	14(O) -	0/0
1013	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	244.30 -	-	12/2016 -	12/2016	0(O) -	0/4
1014	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH , .	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12(O) -	0/2
1015	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH , .	07/2015	333.21 -	333.21 -	-	12/2015 -	12/2016	12(O) -	0/0
1016	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU , .	06/2015	563.92 -	563.92 -	-	12/2017 -	12/2017	0(O) -	0/0
1017	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA , .	06/2015	996.37 -	996.37 -	-	12/2017 -	12/2017	0(O) -	0/0
1018	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02 -	-	12/2017 -	12/2017	0(O) -	0/0
1019	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04 -	-	11/2016 -	12/2016	1(O) -	0/0
1020	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB , .	12/2015	239.23 -	239.23 -	-	12/2017 -	12/2017	0(O) -	0/0
1021	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR , .	12/2015	2,136.97 -	2,136.97 -	-	12/2018 -	12/2018	0(O) -	0/0
1022	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB , .	10/2015	447.29 -	447.29 -	-	12/2017 -	12/2017	0(O) -	0/0
1023	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR , .	08/2015	854.80 -	854.80 -	-	-	-	-	0/0
	Total		248,173.44 -	250,608.22 -	68,392.18				21/167
	SHIPPING AND PORTS								

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1024	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	841.02	10/2008 -	-	-	0/0
1025	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	415.80	12/2010 -	01/2016	61(O) -	0/0
1026	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU , .	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1027	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120(O) 2(R)	0/0
1028	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU , .	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017	0(O) -	0/1
1029	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017	0(O) -	0/2
1030	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA , .	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88(O) 77(R)	0/0
1031	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017	0(O) -	0/1
	Total		4,117.75 -	5,048.81	1,826.73				0/4
	<u>TELECOMMUNICATIONS</u>								
1032	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE , .	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20(O) -	0/0
1033	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30(O) -	0/70
	Total		15,445.17 -	15,345.17	2,720.00				0/70
	<u>URBAN DEVELOPMENT</u>								
1034	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI , .	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17(O) -	0/0
1035	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,KARNATAKA , .	02/2014	26,405.14 26,405.01	26,405.01	217.54	02/2019 03/2020	03/2020	13(O) 0(R)	0/0
1036	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL , .	01/2009	225.81 -	225.81	138.38	06/2012 03/2016	03/2016	45(O) 0(R)	10/16
1037	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH , .	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16(O) -	0/0
1038	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH , .	06/2014	157.84 -	157.84	30.67	03/2017 -	03/2017	0(O) -	0/0

Sector Wise Details									
(January 2016)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1039	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA , .	08/2014	8,680.00 -	8,680.00	74.92	03/2018 -	03/2018	0(O) -	0/0
1040	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL , .	02/2014	156.57 -	156.57	24.34	09/2015 07/2016	04/2017	19(O) 9(R)	0/7
1041	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI , .	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
1042	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND , .	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14(O) -	0/6
1043	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA , .	05/2006	6,395.00 11,609.00	13,845.01	13,525.81	06/2011 12/2015	06/2016	60(O) 6(R)	3/3
1044	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI , .	05/2009	261.85 -	261.85	168.00	05/2013 10/2015	06/2016	37(O) 8(R)	0/0
1045	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA , .	07/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017	-1(O) -	0/0
1046	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI , .	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
1047	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU , .	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8(O) -	1/24
1048	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU , .	04/2014	332.72 -	332.72	78.89	09/2016 -	09/2016	0(O) -	0/0
1049	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI , .	06/2012	4,264.00 -	4,264.00	1,055.27	11/2019 -	11/2019	0(O) -	0/7
1050	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI , .	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9(O) -	0/0
1051	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH , .	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/1
1052	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI , .	01/2010	162.90 -	162.90	160.00	07/2012 12/2015	12/2015	-	0/0
1053	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA , .	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1054	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR , .	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
1055	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA , .	11/2012	238.43 -	238.43	-	02/2015 -	-	-	0/0
1056	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA , .	02/2011	241.33 -	241.33	70.64	11/2014 -	-	-	0/0
1057	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB , .	08/2005	191.24 -	191.24	-	08/2007 -	-	-	0/0
1058	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARAstra - [N28000073]CPWD,MAHARASHTRA , .	06/2010	205.00 -	205.00	-	03/2012 -	-	-	0/0

Sector Wise Details									
(January 2016)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1059	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA , .	12/2012	315.00 -	315.00	3.11	06/2015 -	-	-	0/0
1060	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA , .	01/2010	165.23 -	165.23	-	10/2012 -	-	-	0/0
1061	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH , .	08/2007	246.90 -	246.90	-	-	-	-	0/0
1062	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB , .	02/2014	388.00 -	388.00	-	01/2015 -	-	-	0/0
1063	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU , .	12/2015	209.00 -	209.00	-	-	-	-	0/0
	Total		134,055.93 -	141,505.81	50,146.01				14/64
	Grand Total		1,178,671.50	1,395,087.12	552,163.36				1771/3862


Summary of projects in the Flash Report for the month of January, 2016

Project Implementation - Current Status:

Number of Projects in Previous Month	1059
Number of Projects completed/dropped/frozen in Current Month	6
Number of Projects Added in Current Month	10
Number of Projects in Current Month	1063


Brief Analysis

Project Status with respect to Original Schedule: Out of 1063 projects, 7 projects are ahead of schedule, 253 projects are on schedule 346 projects are delayed. 422 projects do not have fixed dates of commissioning. 35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

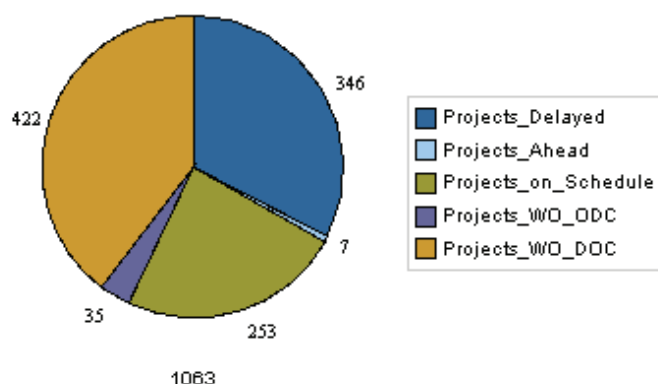

Investment Scenario

Total original cost of implementation of 1063 projects when sanctioned, was of the order of Rs. 1178671.5 crore but this was subsequently revised to Rs. 1395087.12 crore implying a cost overrun of 18.4%. The expenditure incurred on these projects till January, 2016 is Rs. 552163.36 crore, which is 39.6% of the revised cost of the projects.

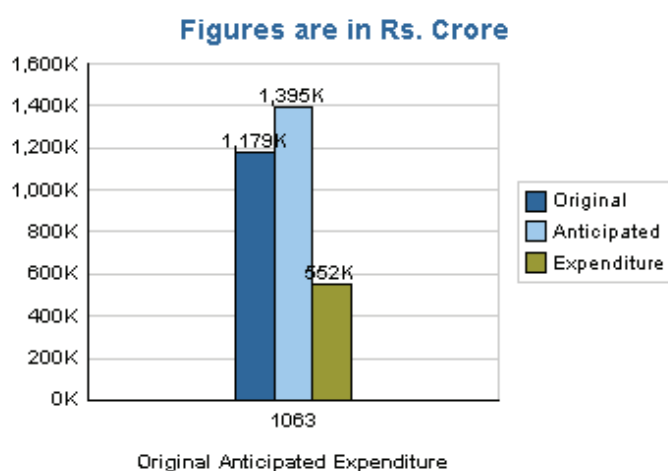

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

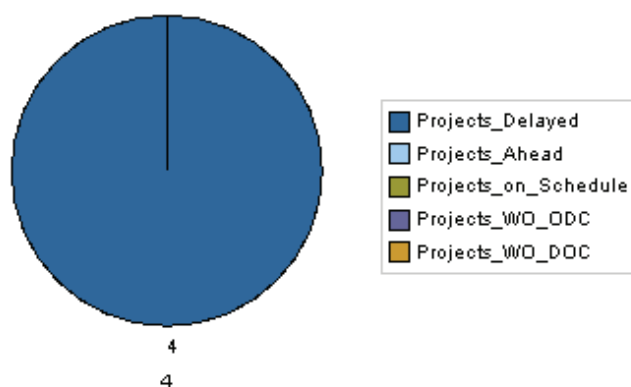

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 51918 crore implying a cost overrun of 28.4%. The expenditure incurred on these projects till January, 2016 is Rs. 39455.14 crore, which is 76% of the revised cost of the projects.

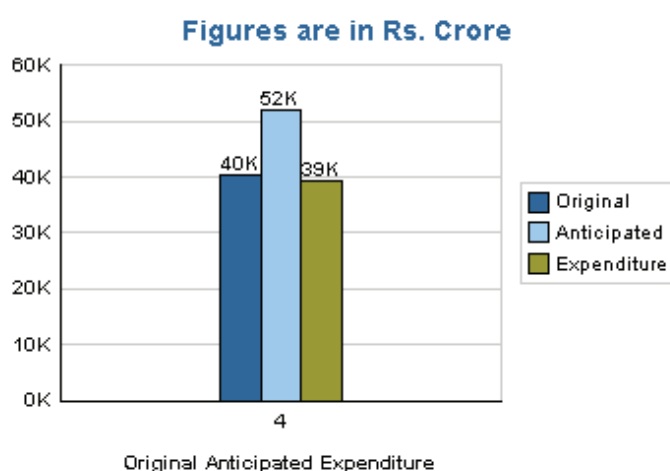

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	4
Number of Projects Delayed	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is delayed. 2 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

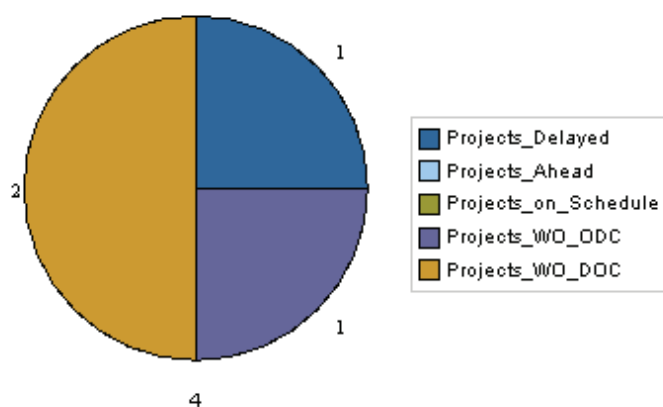

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1186.17 crore implying a cost overrun of .8%. The expenditure incurred on these projects till January, 2016 is Rs. 770.46 crore, which is 65% of the revised cost of the projects.

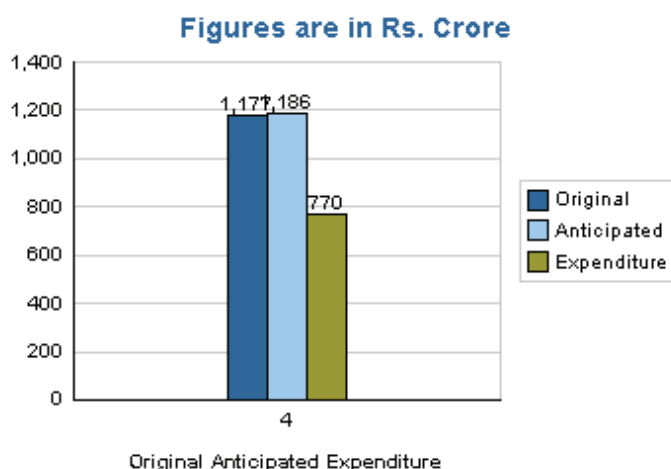

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	86
Number of Projects On Schedule	40
Number of Projects Delayed	44
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 86 projects, 1 project is ahead of schedule, 40 projects are on schedule 44 projects are delayed. 1 project does not have fixed dates of commissioning.

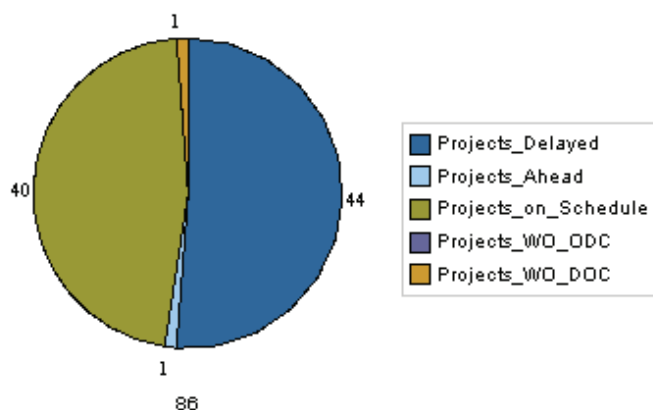

Investment Scenario

Total original cost of implementation of 86 projects when sanctioned, was of the order of Rs. 60889.41 crore but this was subsequently anticipated to Rs. 62002.14 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till January, 2016 is Rs. 15107.97 crore, which is 24.4% of the revised cost of the projects.

Figures are in Rs. Crore

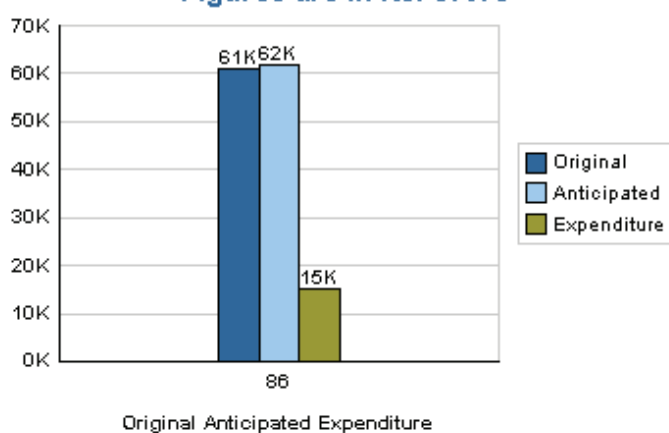

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	33
Number of Projects On Schedule	12
Number of Projects Delayed	17

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 33 projects, 12 projects are on schedule 17 projects are delayed. 4 projects do not have fixed dates of commissioning.

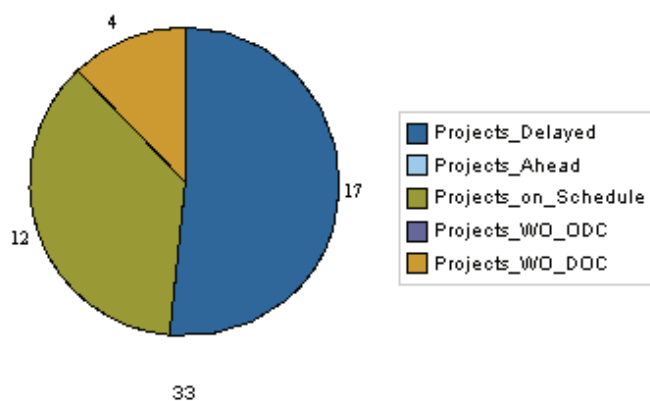

Investment Scenario

Total original cost of implementation of 33 projects when sanctioned, was of the order of Rs. 53859.49 crore but this was subsequently anticipated to Rs. 54375.39 crore implying a cost overrun of 1%. The expenditure incurred on these projects till January, 2016 is Rs. 30205.18 crore, which is 55.5% of the revised cost of the projects.

Figures are in Rs. Crore

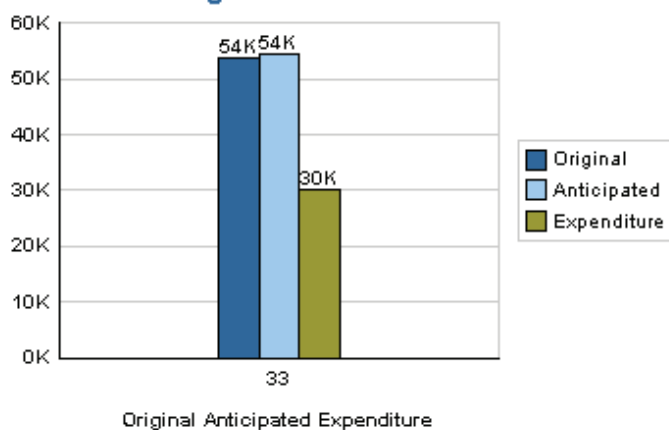

Sector wise current status of projects on the Flash Report

PETROLEUM


Current Status:

Number of Projects	62
Number of Projects On Schedule	15
Number of Projects Delayed	36
Number of Projects Ahead	3

Number of Projects Without Date Of Commissioning	8
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 62 projects, 3 projects are ahead of schedule, 15 projects are on schedule 36 projects are delayed. 8 projects do not have fixed dates of commissioning.

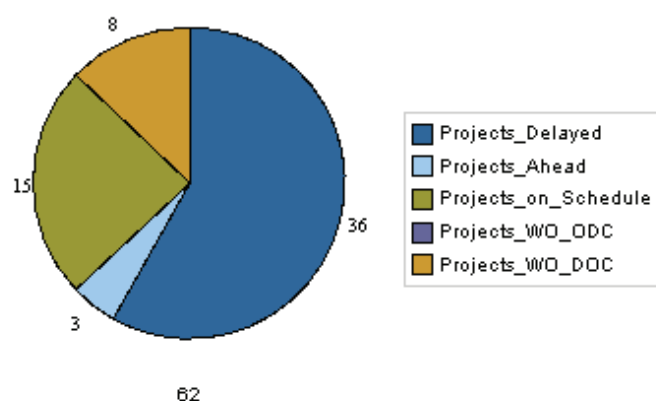

Investment Scenario

Total original cost of implementation of 62 projects when sanctioned, was of the order of Rs. 130718.16 crore but this was subsequently anticipated to Rs. 140226.81 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till January, 2016 is Rs. 67676.67 crore, which is 48.3% of the revised cost of the projects.

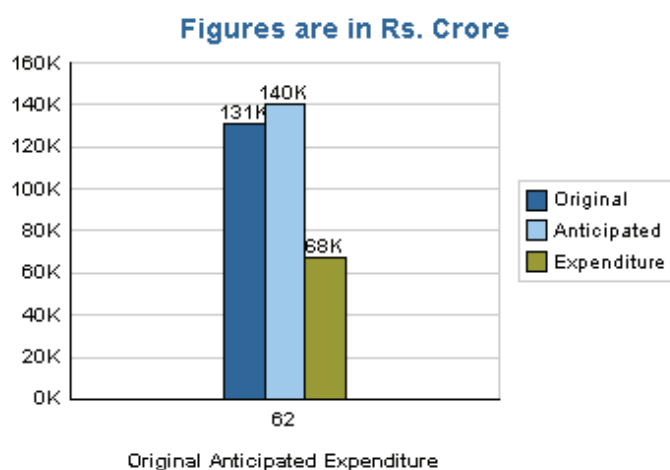

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	111
Number of Projects On Schedule	47
Number of Projects Delayed	59
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning	4
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 111 projects, 1 project is ahead of schedule, 47 projects are on schedule 59 projects are delayed. 4 projects do not have fixed dates of commissioning.

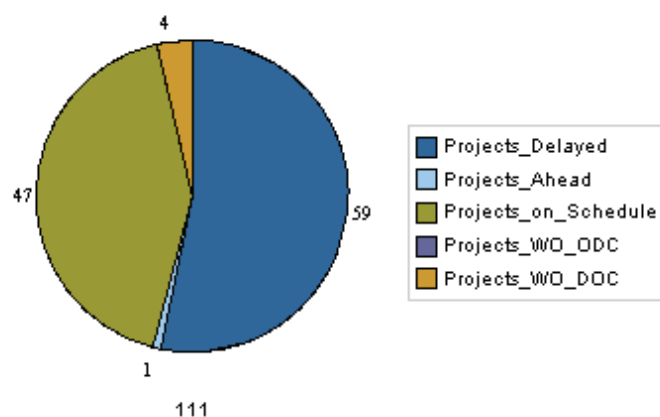

Investment Scenario

Total original cost of implementation of 111 projects when sanctioned, was of the order of Rs. 304580.02 crore but this was subsequently anticipated to Rs. 353098.54 crore implying a cost overrun of 15.9%. The expenditure incurred on these projects till January, 2016 is Rs. 172691.27 crore, which is 48.9% of the revised cost of the projects.

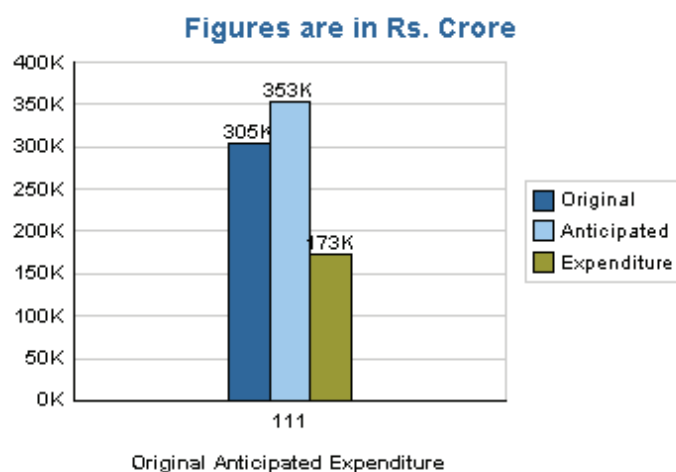

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	297
Number of Projects On Schedule	5
Number of Projects Delayed	31
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	234


Brief Analysis

Project Status with respect to Original Schedule: Out of 297 projects, 5 projects are on schedule 31 projects are delayed. 234 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

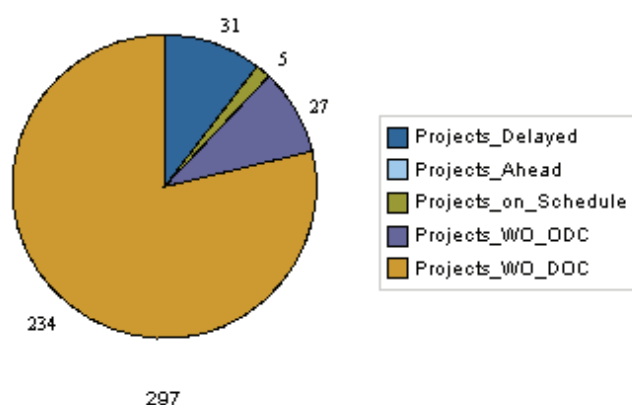

Investment Scenario

Total original cost of implementation of 297 projects when sanctioned, was of the order of Rs. 172717.67 crore but this was subsequently anticipated to Rs. 301331.54 crore implying a cost overrun of 74.5%. The expenditure incurred on these projects till January, 2016 is Rs. 92996.3 crore, which is 30.9% of the revised cost of the projects.

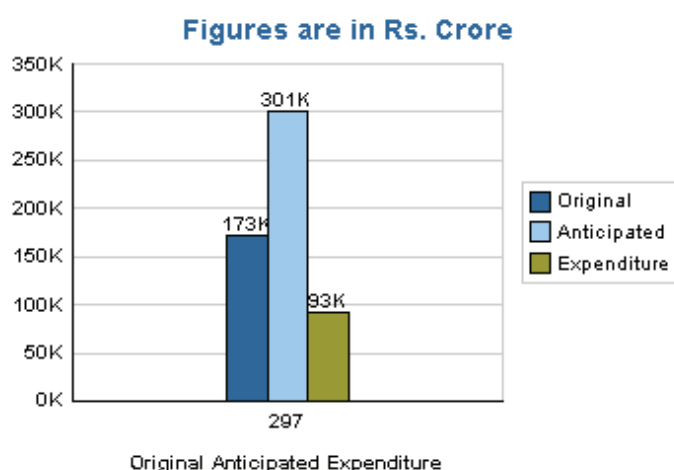

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	411
Number of Projects On Schedule	117
Number of Projects Delayed	132
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	7
Number of Projects Without Date Of Commissioning	154

Brief Analysis


Project Status with respect to Original Schedule: Out of 411 projects, 1 project is ahead of schedule, 117 projects are on schedule 132 projects are delayed. 154 projects do not have fixed dates of commissioning. 7 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

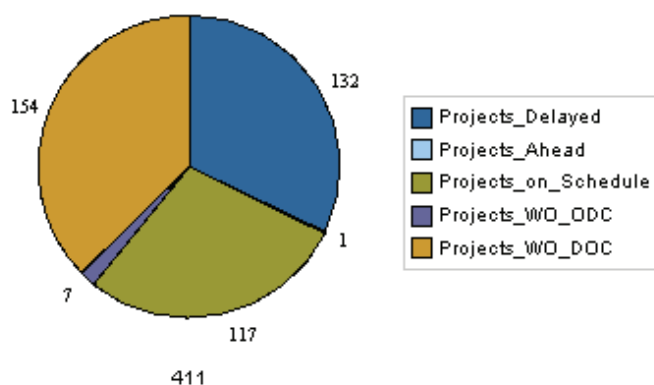

Investment Scenario

Total original cost of implementation of 411 projects when sanctioned, was of the order of Rs. 248173.44 crore but this was subsequently anticipated to Rs. 250608.22 crore implying a cost overrun of 1%. The expenditure incurred on these projects till January, 2016 is Rs. 68392.18 crore, which is 27.3% of the revised cost of the projects.

Figures are in Rs. Crore

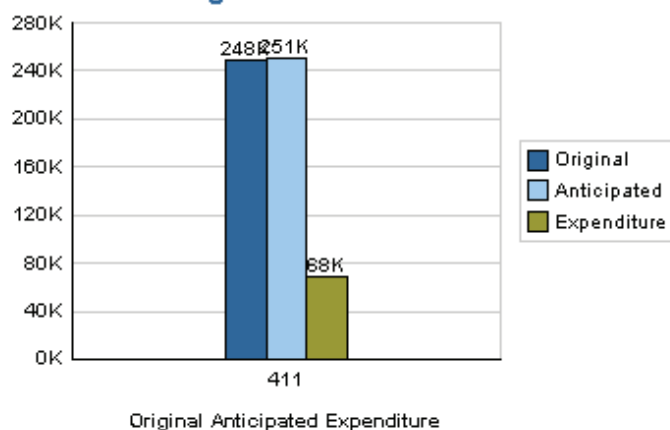

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 3 projects are delayed. 1 project does not have fixed dates of commissioning.

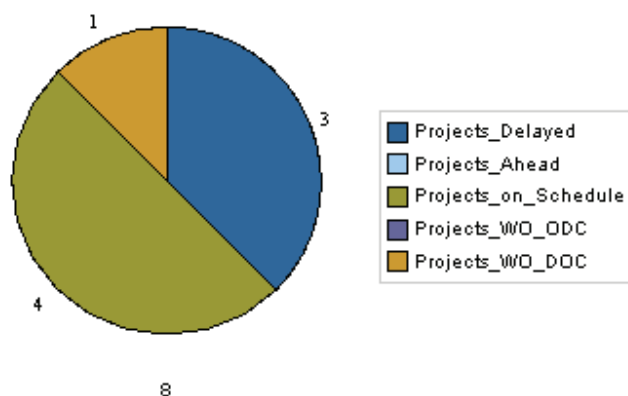

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5048.81 crore implying a cost overrun of 22.6%. The expenditure incurred on these projects till January, 2016 is Rs. 1826.73 crore, which is 36.2% of the revised cost of the projects.

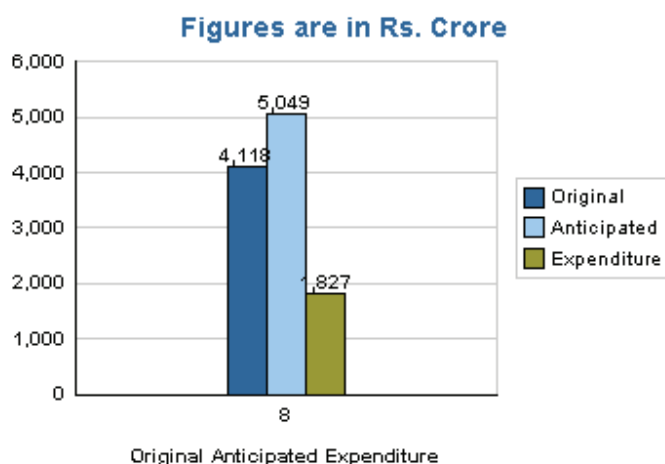

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	2
Number of Projects Delayed	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.

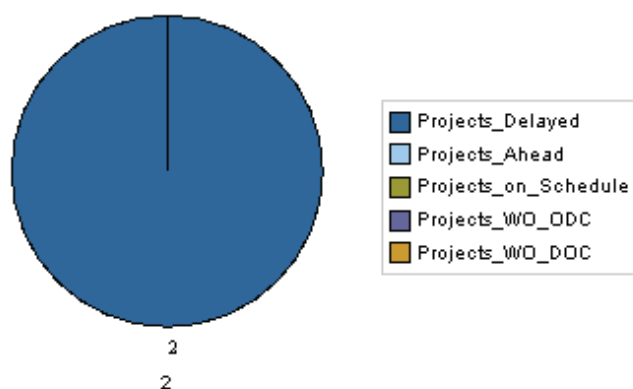

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 15445.17 crore but this was subsequently anticipated to Rs. 15345.17 cr. The expenditure incurred on these projects till January, 2016 is Rs. 2720 crore, which is 17.7% of the revised cost of the projects.

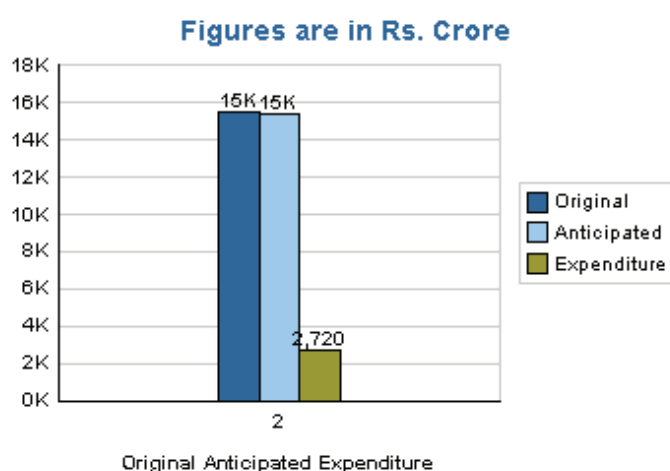

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	5
Number of Projects Delayed	12
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning	12
--	----


Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 1 project is ahead of schedule, 5 projects are on schedule 12 projects are delayed. 12 projects do not have fixed dates of commissioning.

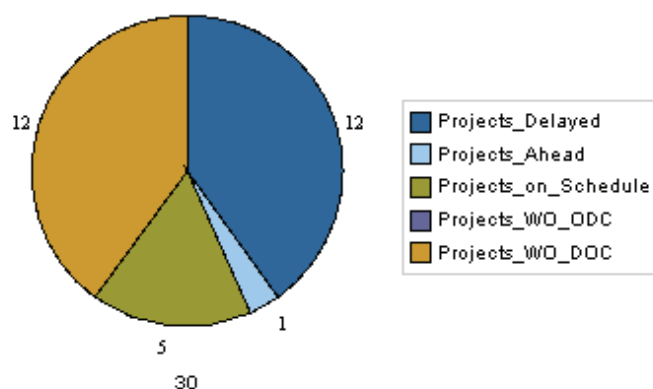

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 134055.93 crore but this was subsequently anticipated to Rs. 141505.81 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till January, 2016 is Rs. 50146.01 crore, which is 35.4% of the revised cost of the projects.

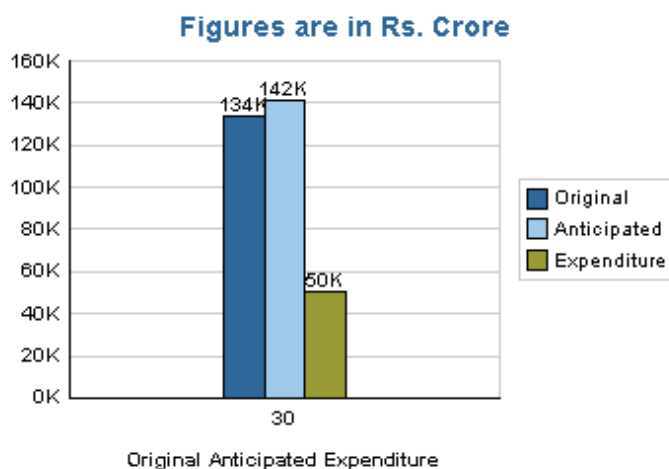

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	2	587.67	587.67	21.76
2	ANDHRA PRADESH	47	21,226.93	23,061.97	8,055.13
3	ARUNACHAL PRADESH	14	11,758.7	28,030.85	13,766.29
4	ASSAM	50	28,795.71	44,499.05	30,778.63
5	BIHAR	64	57,872.84	72,327.53	39,051.73
6	CHHATISGARH	41	88,369.18	89,646.53	48,862.1
7	D & N HAVELI	1	6,086.08	6,086.08	592.92
8	DELHI	16	49,963.05	49,963.05	22,324.03
9	GOA	8	3,925.48	3,907.87	341.03
10	GUJARAT	30	30,410.18	31,464.82	10,934.24
11	HARYANA	20	13,986.73	15,957.35	6,919
12	HIMACHAL PRADESH	5	8,088.55	14,487.83	6,699.38
13	JAMMU AND KASHMIR	9	25,620.25	45,229.68	15,245.67
14	JHARKHAND	44	41,826.84	44,389.67	12,863.37
15	KARNATAKA	41	71,364.99	88,854.89	32,518.66
16	KERALA	16	25,825.82	30,300.97	15,714.94
17	MADHYA PRADESH	51	53,839.16	55,730.39	7,688.39
18	MAHARASHTRA	71	1,13,215.47	1,21,988.42	35,135.6
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	6	6,970.03	8,194.91	2,102.63
21	MIZORAM	6	2,188.16	5,402.06	1,782.75
22	MULTI STATE	176	1,88,850.62	2,20,269.11	71,310.3
23	NAGALAND	3	6,420	8,757.12	10.44
24	ODISHA	47	71,450.12	80,688.91	40,006.62
25	PUNJAB	23	11,714.51	11,718.51	2,032.74
26	RAJASTHAN	58	39,924.61	40,467.55	19,972.57
27	SIKKIM	5	2,149.08	4,999.32	558.12
28	TAMIL NADU	57	68,769.74	88,418.98	51,758.7
29	TELANGANA	31	11,908.91	14,943.51	3,061.89
30	TRIPURA	9	3,776.07	7,486.36	3,401.21
31	UTTAR PRADESH	60	52,378.07	56,264.19	19,111.14
32	UTTARAKHAND	6	9,352.4	11,651.71	5,515.06
33	WEST BENGAL	45	49,327.99	62,739.51	21,238.33
TOTAL		1,063	11,78,671.5	13,95,087.12	5,52,163.36

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	21,077
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	5,150.14
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,398.46
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,969.14
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,956.52
6	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	RAILWAYS	03/1995	2,500	-	10,722.72
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	RAILWAYS	02/1997	295	-	1,092.98
12	KARUR-SALEM (NL) , SR	RAILWAYS	02/1997	155.55	-	800.7
13	NANDYAL-YERRAGUNTALA (NL) , SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR KASGANJ MATHURA (GC) NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
16	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
17	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	819.19
18	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
19	KATIHAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
20	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
21	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
22	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
23	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
24	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
25	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,551.53
26	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	376.18
27	JIND-SONEPAT (NL) , NR	RAILWAYS	01/2004	238.56	-	639.77
28	HARIDASPUR-PARADEEP (NL)	RAILWAYS	04/1996	301.64	-	577.84

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	RAJATGARH-BARANG(LD) , ECR	RAILWAYS	04/1999	166.16	-	349.36
30	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
31	KOSI BRIDGE (NL) , ECR	RAILWAYS	04/2002	322.95	-	325.36
32	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,521.72
33	ETAWAH-MAINPURI (NL) ,NCR	RAILWAYS	04/1997	120	245.39	249.33
34	SUKINDA ROAD - ANGUL (NL) (ECOR)	RAILWAYS	04/1998	183.23	-	185.46
35	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
36	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	322.75
37	RAICHUR-GUNTAKAL(DL) (SCR)	RAILWAYS	04/2003	136.62	-	357.91
38	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	240.22
39	HARANGAJO TO MAIBANG (AS-23) , KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	392.6
40	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	278.96
41	BIJNI TO ASSAM /WB.BORDER (NH-31.C) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	374.1
42	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	412.95

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	ANANTA OC EXPANSION PH-III (15.0 MTY)	COAL	08/2008	207.28	-	207.7
44	RAMAGUNDAM OC-II EXTENSION	COAL	12/2009	418.97	-	453.18
45	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	STEEL	03/2007	149.73	173	175.94
46	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	STEEL	05/2005	768.88	1060	1,070.97
47	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	8920	9,175.15
48	MARKETING TOP AT KORBA	PETROLEUM	01/2011	141.86	-	164.35
49	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	4,402.95
50	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	POWER	02/2009	509.66	-	528.56
51	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,319.63
52	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	498.37
53	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RAILWAYS	07/2006	743	-	770.18
54	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RAILWAYS	09/2006	324.9	-	351.79
55	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	896.75
56	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
58	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
59	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
60	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
61	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	730.11
62	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
63	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
64	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,769.59
65	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.82
66	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.11
67	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	259.31
68	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56
69	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
70	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	1,047.1
72	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
73	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
74	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
75	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
76	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	380.62
77	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
78	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	304.17
79	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
80	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	311.13
81	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	295.2
82	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.4
83	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196	-	300.46
84	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	370.66

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	932.3
86	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	284.69
87	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,409.36
88	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,607.78
89	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	761.4
90	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,619.94
91	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
92	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	863.58
93	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	1,004.62
94	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	487.9
95	MURADABAD-BAREILLY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
96	PUNE-SATARA (NH-4)	ROAD TRANSPORT AND HIGHWAYS	10/2010	1,724.55	-	1,742.94
97	PATNA-MUZZAFFARPUR	ROAD TRANSPORT AND HIGHWAYS	08/2010	671.3	-	879.98
98	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	830.97

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	1,911.64
100	SIX LANNING OF NELLORE- CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,478.63
101	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	760.2
102	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	604.5
103	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	544.08
104	PUNE-SHOLAPUR, PKG-II	ROAD TRANSPORT AND HIGHWAYS	09/2011	835	-	1,684
105	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
106	MUZAFFARNAGAR-HARIDWAR	ROAD TRANSPORT AND HIGHWAYS	09/2011	754	-	893.9
107	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	2,287.44
108	ETAWAH CHAKERI	ROAD TRANSPORT AND HIGHWAYS	03/2013	1,573	-	1,840
109	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LWE S	ROAD TRANSPORT AND HIGHWAYS	03/2011	218.31	-	282.02
110	KOTWA TO DEWAPUR (LMNHP-10)	ROAD TRANSPORT AND HIGHWAYS	11/2005	240	-	295.38
111	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,494.48	-	2,090
112	4 LANING OF GOMTI CHAURAHA - UDAIPUR	ROAD TRANSPORT AND HIGHWAYS	03/2012	914.5	-	1,097.62

Annexure - II

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,170.52	-	1,579.15
114	ROHTAK - BAWAL (APPROVED LENGTH 97 KM)	ROAD TRANSPORT AND HIGHWAYS	02/2010	650	-	813.91
115	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	SHIPPING AND PORTS	01/2007	366.39	-	415.8
116	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6,395	11609	13,525.81

Annexure - III

Details of Projects Ahead of Schedule w.r.t. Original Schedule

(January 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
2	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	71.50	02/2017 -	03/2016
	Total		188.75 -	188.75	71.50		
	<u>PETROLEUM</u>						
3	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	164.35	09/2016 -	03/2016
4	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	326.09	01/2017 -	06/2016
	Total		560.90 -	651.04	490.44		
	<u>URBAN DEVELOPMENT</u>						
5	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						
6	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	648.01	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	648.01		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
7	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]	3/2015	830.36	830.36	-	01/2019 -	01/2016
	Total		830.36 -	830.36	.00		
	Grand Total		13,386.12	13,476.26	3,776.42		

Annexure - IV

Details of On Schedule Projects w.r.t. Original Schedule

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
2	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.65	03/2016 -	03/2016
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
4	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	179.10	03/2021 -	03/2021
5	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
6	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
7	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	204.99	03/2017 -	03/2017
8	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	61.37	03/2025 -	03/2025
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.94	03/2026 -	03/2026
10	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	46.94	03/2021 -	03/2021
11	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
12	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
13	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	98.63	03/2021 -	03/2021
14	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
15	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
16	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
17	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	141.07	03/2020 -	03/2020
18	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	798.52	03/2023 03/2023	03/2023
19	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
20	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.58	03/2020 -	03/2020
21	GOKUL - [N06000120]	11/2014	267.67 -	267.67	185.72	03/2018 -	03/2018
22	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.44	03/2019 -	03/2019
24	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
25	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
27	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
28	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	72.99	03/2019 -	03/2019
29	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
30	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
31	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019
32	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
33	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
34	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	51.51	03/2023 -	03/2023
35	KHADIA EXPANSION OPENCAS PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	148.45	03/2018 -	03/2018
36	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	199.31	03/2020 -	03/2020
37	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016
38	DURGAPUR OPENCAS PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
39	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
40	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	809.04	03/2016 -	03/2016
	Total		33,648.49 -	33,439.69	4,417.59		
	<u>FERTILISERS</u>						
41	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	49.27	11/2016 -	11/2016
	Total		197.79 -	209.44	49.27		
	<u>HEALTH AND FAMILY WELFARE</u>						
42	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70 -	196.70	157.61	01/2016 -	01/2016
43	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	9.74	03/2018 -	03/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	168.90	0.05	05/2017 -	05/2017
45	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	293.65	49.24	05/2017 -	05/2017
46	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	204.44	25.67	05/2017 -	05/2017
	Total		1,369.27 -	1,369.27	242.31		
	<u>MINES</u>						
47	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]	12/2015	355.13 -	355.13	-	11/2016 -	11/2016
48	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]	12/2015	344.50 -	344.50	-	11/2016 -	11/2016
	Total		699.63 -	699.63	.00		
	<u>PETROLEUM</u>						
49	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	641.31	05/2017 -	05/2017
50	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	-	12/2017 -	12/2017
51	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	12.72	01/2018 -	01/2018
52	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	500.00	-	03/2017 -	03/2017
53	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 -	03/2019
54	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
55	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017
56	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	69.23	07/2016 -	07/2016
57	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	10,044.66	05/2016 -	05/2016
58	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	140.71	12/2016 -	12/2016
59	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018
60	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,689.65	05/2017 05/2017	05/2017
61	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
62	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	58.18	07/2016 -	07/2016
63	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		38,108.52	39,944.25	14,379.05		
	<u>POWER</u>						
64	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00	1,527.00	143.00	08/2017	08/2017
65	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12	3,363.12	1,018.00	12/2016	12/2016
66	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28	203.28	18.38	07/2017	07/2017
67	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18	307.18	7.40	11/2017	11/2017
68	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47	1,455.47	-	07/2018	07/2018
69	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME - PART B - [N18000196]	4/2015	3,705.61	3,705.61	194.60	04/2018	04/2018
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08	908.08	135.50	06/2016	06/2016
71	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06	550.06	15.60	03/2018	03/2018
72	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71	378.71	113.30	10/2016	10/2016
73	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07	303.07	19.70	07/2016	07/2016
74	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11	162.11	-	05/2018	05/2018
75	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37	2,247.37	16.00	07/2018	07/2018
76	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00	11,846.00	5,564.00	06/2017	06/2017
77	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68	436.68	436.56	12/2016	12/2016
78	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98	829.98	83.30	08/2016	08/2016
79	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98	9,188.98	1,000.00	03/2019	03/2019
80	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88	207.88	-	07/2018	07/2018
81	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80	268.80	22.60	03/2018	03/2018
82	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55	11,638.55	4,856.00	09/2017	09/2017
83	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84	1,381.84	157.00	09/2019	09/2019
84	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04	187.04	-	06/2018	06/2018
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82	539.82	111.90	06/2016	06/2016

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	3.10	10/2017 -	10/2017
87	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
88	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	120.00	04/2020 -	04/2020
89	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
90	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	67.20	02/2017 -	02/2017
91	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	4,914.20	01/2018 -	01/2018
92	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	78.90	04/2017 -	04/2017
93	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	5.40	03/2016 -	03/2016
94	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04 -	305.04	-	03/2017 -	03/2017
95	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]	2/2015	302.49 302.00	302.49	234.18	02/2016 -	02/2016
96	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,500.00	08/2018 -	08/2018
97	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
98	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
99	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	49.40	11/2016 -	11/2016
100	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	709.90	05/2016 -	05/2016
101	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	338.80	05/2018 -	05/2018
102	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016
103	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	-	09/2019 -	09/2019
104	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,349.00	02/2019 -	02/2019
105	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	-	07/2018 -	07/2018
106	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	0.90	07/2017 -	07/2017
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	03/2018 -	03/2018
108	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	301.90	04/2018 -	04/2018
109	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	16.10	05/2016 -	05/2016

(January 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
110	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
	Total		136,002.24 -	136,002.24	26,351.81		
	<u>RAILWAYS</u>						
111	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
112	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
113	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
114	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
115	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
	Total		2,670.53 -	6,808.36	172.17		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
116	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
117	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338	10/2014	206.12 -	206.12	102.21	04/2017 -	04/2017
118	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
119	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
120	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
121	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	52.40	05/2017 -	05/2017
122	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
123	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349	5/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017
124	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342	5/2015	709.00 -	709.00	-	09/2017 -	09/2017
125	2-LANING WITH PS SITARGANJ BAREILLY SECTION - [N24000364	6/2014	301.04 -	301.04	31.28	01/2016 -	01/2016
126	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	-	12/2017 -	12/2017
127	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	-	02/2018 -	02/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
128	JALANDHAR - AMRITSAR - [N24000351]	1/2014	523.85 -	523.85	54.84	01/2016 -	01/2016
129	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
130	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	83.61	04/2017 -	04/2017
131	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	13.25	07/2017 -	07/2017
132	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	23.83	02/2017 -	02/2017
133	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
134	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
135	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
136	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
137	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
138	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000446]	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
139	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	-	02/2018 -	02/2018
140	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
141	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
142	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	144.69	03/2016 -	03/2016
143	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
144	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
145	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]	3/2013	959.25 -	959.25	-	06/2016 -	06/2016
146	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	229.01	08/2016 -	08/2016
147	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	1,202.43	11/2016 -	11/2016
148	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	-	04/2018 -	04/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464	3/2015	830.36 -	830.36	-	01/2016 -	01/2016
150	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
151	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
152	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
153	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
154	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
155	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
156	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
157	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
158	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
159	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
160	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
161	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
162	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
163	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	244.30	-	12/2016 -	12/2016
164	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
165	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
166	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
167	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
168	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019

(January 2016)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
169	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
170	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
171	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
172	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
173	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
174	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
175	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	-	09/2017 -	09/2017
176	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
177	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
178	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
179	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
180	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
181	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
182	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
183	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
184	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
185	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
186	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
187	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	3/2015	829.00 -	829.00	-	03/2018 -	03/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
188	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
189	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
191	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
192	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	-	11/2017 -	11/2017
193	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
194	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016
195	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
196	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
197	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	10/2014	463.49 -	463.49	-	06/2018 -	06/2018
198	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
199	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
200	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
201	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
202	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
203	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
204	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
205	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
206	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	10/2014	437.39 -	437.39	-	06/2018 -	06/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
207	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
208	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
209	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]	6/2014	569.38 -	569.38	344.00	06/2016 -	06/2016
210	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	584.72	04/2016 -	04/2016
211	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018
212	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	-	07/2017 -	07/2017
213	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
214	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	-	08/2016 -	08/2016
215	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
216	VADODARA-SURAT SECTION - [N24000361]	3/2014	503.16 -	503.16	-	08/2016 -	08/2016
217	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	-	05/2017 -	05/2017
218	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
219	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	167.91	09/2016 -	09/2016
220	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92 -	563.92	-	11/2016 -	11/2016
221	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	69.55	09/2017 -	09/2017
222	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
223	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
225	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
226	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
227	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
228	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
229	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
230	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	124.59	02/2018 -	02/2018

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
231	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
232	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	-	01/2017 -	01/2017
	Total		63,412.44 -	63,640.03	4,855.27		
	<u>SHIPPING AND PORTS</u>						
233	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017
234	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017
235	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
236	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017
	Total		928.29 -	942.12	63.91		
	<u>STEEL</u>						
237	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017
238	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109	12/2007	253.92 254.00	254.00	193.97	06/2016 -	06/2016
239	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	195.51	12/2016 -	12/2016
240	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
241	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
242	TURBO BLOWER - 5 - [N12000092	12/2009	280.00 -	280.00	26.55	09/2016 -	09/2016
243	REBUILDING OF COB-7 AT BSL - [N12000083	10/2013	245.67 -	245.67	98.57	05/2016 -	05/2016
244	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096	5/2015	1,154.18 -	1,154.18	28.20	12/2017 -	12/2017
245	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	297.93	04/2018 -	04/2018
246	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
247	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	126.15	03/2018 -	03/2018
248	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
	Total		11,860.88 -	11,885.35	1,080.45		

						(January 2016)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>URBAN DEVELOPMENT</u>						
249	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	4/2014	332.72 -	332.72	78.89	09/2016 -	09/2016
250	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017
251	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,264.00	1,055.27	11/2019 -	11/2019
252	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
253	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	74.92	03/2018 -	03/2018
	Total		14,653.77 -	14,653.77	1,239.75		
	Grand Total		303,551.85	309,594.15	52,851.58		

Annexure - V

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
6	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2016	478.50
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,800.69 -	3,170.48			
	<u>FERTILISERS</u>						
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	11/2016	5.89
	Total		197.79 -	209.44			
	<u>HEAVY INDUSTRY</u>						
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>PETROCHEMICALS</u>						
11	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49
14	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	02/2018	17.66
15	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81
16	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	03/2016	63.54
17	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
18	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
19	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83
20	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2016	16.05
21	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
22	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
23	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08	11/2015 -	11/2016	25.84
24	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2017	49.38
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	03/2016	67.62
26	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
27	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	10/2016	19.35
	Total		63,409.10 -	74,805.00			
	<u>POWER</u>						
28	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
29	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
30	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63
31	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2016	54.59
32	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
33	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79
34	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
35	BONGAIGAON THERMAL POWER PROJECT - [N18000041	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
36	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
37	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06
38	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	6,085.84	12/2009 06/2016	06/2016	143.74
39	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
40	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	-	31.17
41	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91
42	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
43	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	06/2016	16.63
44	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60
45	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93
47	BARH STPP(3X660MW) NTPC - [180100242	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
48	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
49	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32
	Total		61,522.84 -	110,104.97			
	<u>RAILWAYS</u>						
50	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
52	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40
53	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
54	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
55	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
56	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
57	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
58	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
59	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
60	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
61	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
62	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
63	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	3,040.00	03/2009 -	03/2016	230.08
64	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
65	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
66	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
67	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
68	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	-	556.39
69	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
70	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
71	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
72	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	360.00	12/2007 03/2010	-	163.50
73	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	360.00	02/2006 -	-	37.56

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
74	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
75	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
76	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	03/2016	166.63
77	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	490.00	- -	-	292.00
78	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
79	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
80	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
82	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
83	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
84	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
85	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
86	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
87	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
88	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
89	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
90	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
91	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
92	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
93	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
94	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
95	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
96	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
97	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18 -	- -	- -	100.76
98	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99 -	- -	- -	183.41
99	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43 -	- -	- -	24.09
100	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65 -	- -	- -	57.65
101	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47 -	- -	- -	47.93
102	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00 -	- -	- -	79.63
103	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85 -	- -	- -	2.29
104	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50 -	- -	- -	0.00
105	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97 -	- -	- -	50.10
106	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50 -	- -	- -	14.14
107	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00 -	- -	- -	72.07
108	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77 -	- -	- -	12.38
109	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00 -	01/1999 -	- -	123.46
110	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00 -	01/1999 -	- -	71.50
111	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00 -	01/1999 -	- -	53.96
112	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00 -	- -	- -	447.91
113	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98 -	03/2004 -	03/2016 -	259.68
114	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19 -	04/2008 12/2011	06/2017 -	233.08
115	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	3,500.00 -	05/2008 -	- -	1,313.23
116	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56 -	03/2012 -	- -	108.01
117	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015 -	300.67
118	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00 -	- -	- -	232.17
119	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34 -	12/2008 -	03/2018 -	245.34
120	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25 -	- -	- -	324.33

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
121	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
122	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
123	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
124	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
126	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
127	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
129	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
130	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
131	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
132	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
133	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
134	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
135	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
136	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
137	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	2,434.00	03/2010 -	-	648.92
138	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
139	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
140	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
141	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
142	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
143	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
144	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
145	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
146	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
147	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
148	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
149	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345	04/1997	836.26 -	1,072.51	- -	-	28.25
150	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
151	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
152	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
153	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
154	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	-	1.06
155	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	679.27 -	1,111.99	- -	-	63.70
156	JHARSUGUDA-RENGALI DOUBLING - [N22000317	03/2006	201.00 -	230.00	- -	-	14.43
157	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
158	DELANG-PURI DOUBLING - [N22000320	03/2011	165.16 -	234.71	03/2015 -	-	42.11
159	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321	04/2014	182.92 -	197.73	- -	-	8.10
160	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
161	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
162	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
163	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
164	CHHAPRA-BALLIA UP - [N22000134	03/2013	295.00 -	494.92	- -	-	67.77
165	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	913.48	- -	-	184.87
166	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	446.00 -	685.17	- -	-	53.63

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
167	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
168	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
169	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
170	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
171	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
172	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
173	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
174	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
175	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
176	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
177	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
178	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
179	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
180	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
181	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
182	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
183	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
184	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
185	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
186	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
187	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
188	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
189	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	-	-	91.71
190	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	-	-	55.74
191	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	-	-	28.14
192	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	-	03/2019	154.33
193	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007	03/2016	38.80
194	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	-	03/2018	251.85
195	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	-	03/2020	5.00
196	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	-	03/2018	110.44
197	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	-	03/2018	1.86
198	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	-	-	109.04
199	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	-	-	173.71
200	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	-	03/2015	285.12
201	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	-	-	16.29
202	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	-	03/2020	30.00
203	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	-	03/2018	180.56
204	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	03/2017	63.25
205	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	-	03/2018	162.68
206	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	-	03/2018	216.06
207	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	-	03/2018	45.17
208	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	-	03/2019	47.95
209	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016	12/2017	29.06
210	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	-	-	33.02
	Total		82,833.35 -	214,601.52			

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	ROAD TRANSPORT AND HIGHWAYS						
211	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93
212	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
213	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
214	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
215	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2016	106.50
216	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41
217	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
218	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84
219	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	161.70	07/2015 -	-	2.88
220	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25
221	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2016	30.10
222	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
223	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
224	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
225	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
226	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
227	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
228	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		5,171.67 -	7,634.21			
	SHIPPING AND PORTS						

(January 2016)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
229	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	03/2016	300.00
230	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
231	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
232	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
233	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	12/2016	12.04
234	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 207.00	207.00	12/2016 -	07/2017	17.96
235	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,060.00	1,060.00	02/2014 -	03/2016	37.86
236	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	07/2011	324.87 325.00	325.00	12/2015 -	03/2016	0.04
237	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 254.00	254.00	06/2016 -	06/2016	0.03
238	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
239	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	173.00	12/2015 -	03/2017	15.54
	Total		2,218.50 -	2,734.40			
	<u>URBAN DEVELOPMENT</u>						
240	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	13,845.01	06/2011 -	06/2016	116.50
	Total		6,395.00 -	13,845.01			
	Grand Total		248,614.71	471,218.05			

Annexure - VI

Details of Delayed Projects w.r.t. Original Schedule

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,077.00	12/2008 10/2013	05/2016	89	70.54	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,150.14	09/2010 -	09/2016	72	62.57	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	7,715.00	12/2015 10/2016	11/2018	35	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,513.00	12/2016 03/2017	12/2019	36	0	
	Total		40,442.00 -	51,918.00	39,455.14					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	412.95	01/2011 06/2016	09/2017	80	0	Terminal Building work stopped by local residents demanding compensation citing damages to their properties.
	Total		309.46 -	309.46	412.95					
	<u>COAL</u>									
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,990.05	03/2014 -	03/2016	24	0	
7	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24	0	
8	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	503.51	03/2013 -	03/2016	36	-6.11	
9	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	866.79	03/2013 09/2012	03/2016	36	478.5	
10	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	81.11	03/2015 -	03/2016	12	0	
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48	0	
12	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL, JHARKHAND	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
13	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	0	
14	MURADIH UG TURN-KEY PROJECT - [N06000096]JCL,JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23	0	
15	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]JCL,TAMIL NADU	04/2012	364.75 -	364.75	191.25	10/2014 -	03/2016	17	0	
16	RAJMAHAL OC EXP. - [N06000056]JCL,JHARKHAND	09/2009	153.82 -	153.82	70.92	03/2014 -	09/2016	30	0	Delay/ non issuance of 'Patta' for land/plots allotted to PAFs shifted and being shifted in the area acquired under CBA Act.
17	MADHUBAND NLW WASHERY - [N06000126]JCL,JHARKHAND	08/2010	289.45 -	289.45	99.75	05/2014 -	10/2016	29	0	
18	PATHERDIH NLW WASHERY - [N06000127]JCL,JHARKHAND	10/2012	269.82 -	269.82	68.57	04/2014 -	11/2016	31	0	
19	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.68	03/2010 -	03/2017	84	0	
20	ASHOK EXPN OCP CCL (10 MTY) - [060100096]JCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	0	
21	JHANJRA R-VI SEAM PSLW - [N06000020]JCL,WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	0	Processing of FC stage-I and stage-II was delayed by State Forest Deptt. and State Govt.
22	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]JCL,MADHYA PRADESH	10/2007	259.40 486.57	486.57	81.23	03/2012 03/2018	03/2017	60	87.58	
23	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	209.57	03/2013 -	03/2017	48	0	
24	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	151.26	03/2010 -	03/2017	84	0	
25	KAKATIYA LONGWALL - [N06000048]JCL,TELANGANA	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51	0	
26	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	207.70	03/2012 -	03/2017	60	0	
27	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	185.34	03/2013 -	03/2017	48	.02	
28	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND	12/2007	179.87 -	179.87	92.95	03/2012 -	03/2017	60	0	Authentication of village potanga, Court cases
29	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	0	Verification of authenticated land
30	KARMA OCP (1.0MTY) - [N06000088]JCL,JHARKHAND	06/2009	162.46 -	162.46	70.20	03/2014 -	03/2017	36	0	Authentication of land of village

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
31	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	0	
32	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	15.14	07/2016 -	03/2017	8	0	Aquisition of non forest land and R&R
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	78.69	03/2012 -	03/2018	72	0	
34	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48	0	
35	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	8.03	03/2015 -	03/2018	36	0	
36	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	
37	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	77.44	03/2015 -	03/2018	36	0	
38	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24	0	
39	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2018	24	12.97	
40	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	1,373.77	12/2015 04/2018	04/2018	28	0	
41	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	202.22	03/2018 -	06/2018	3	0	
42	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019	48	0	
43	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 -	1,458.17	14.59	06/2015 -	08/2019	50	0	
44	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	0	
45	JAGANNATHPOR OCP (3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	0	
46	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	0	
47	MAGADH OC 20 MTY (CCL) - [N06000015]CCCL, JHARKHAND	08/2008	706.40 -	706.40	78.06	07/2012 -	03/2021	104	0	
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0	
49	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	489.62	453.18	03/2012 -	03/2023	132	16.86	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		26,217.62 -	27,539.15	10,684.01					
	<u>MINES</u>									
50	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	1,176.00	4.59	09/2017 -	04/2020	31	-36.64	Delay in grant of statutory clearances i.e. environmental clearance, clearance from standing committee of NBWL.
	Total		1,856.00 -	1,176.00	4.59					
	<u>STEEL</u>									
51	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	229.64	08/2014 11/2015	01/2016	17	0	
52	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	173.07	10/2013 12/2015	03/2016	29	0	
53	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	1,060.00	1,070.97	02/2014 -	03/2016	25	37.86	
54	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015 -	03/2016	3	.04	
55	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	15,516.00	03/2013 03/2016	06/2016	39	0	
56	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	295.30	04/2016 -	08/2016	4	0	
57	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	399.56	07/2015 -	08/2016	13	0	
58	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	60.23	04/2015 -	12/2016	20	0	
59	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	8,493.78	05/2015 12/2016	12/2016	19	0	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
60	3RD CONVERTER AND 4TH CASTER - [N12000088]JRLN, ANDHRA PRADESH	07/2011	974.76 -	974.76	220.37	07/2016 -	12/2016	5	0	
61	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	173.00	175.94	12/2015 -	03/2017	15	15.54	
62	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	648.16	03/2015 -	03/2017	24	0	
63	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	241.53	12/2016 -	03/2017	3	0	
64	SMS-1 CONVERTERS REVAMPING - [N12000090]JRLN, ANDHRA PRADESH	05/2012	404.16 -	404.16	265.95	07/2015 -	06/2017	23	0	
65	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]JRLN, ANDHRA PRADESH	12/2009	343.00 -	488.40	38.17	10/2016 -	06/2017	8	42.39	
66	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 207.00	207.00	131.77	12/2016 -	07/2017	7	17.96	
67	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	4.84	09/2017 -	11/2017	2	0	
	Total		40,121.06 -	40,612.49	28,228.85					
	PETROLEUM									
68	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,792.85	01/2014 12/2015	01/2016	24	0	
69	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	251.66	-	06/2012 -	01/2016	43	-6.79	
70	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 34,555.00	34,555.00	31,052.90	11/2012 11/2013	02/2016	39	16.05	
71	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	279.00	186.98	12/2014 -	02/2016	14	0	
72	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL, MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,399.90	08/2015 -	03/2016	7	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
73	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	463.32	321.64	06/2011 03/2012	03/2016	57	0	
74	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	317.64 -	240.95	127.08	09/2012 03/2016	03/2016	42	-24.14	
75	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, MULTI STATE	08/2011	586.00 -	586.00	419.10	08/2015 -	03/2016	7	0	
76	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,074.73	10/2011 -	03/2016	53	67.62	issues faced with local elements in the RoU.
77	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	995.12	05/2013 04/2016	04/2016	35	45.83	
78	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,294.55	09/2012 -	05/2016	44	0	
79	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC, MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,323.77	03/2015 05/2016	05/2016	14	29.42	
80	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC, MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	0	
81	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	131.19	03/2014 05/2016	05/2016	26	0	
82	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 686.58	686.58	563.49	04/2015 05/2016	05/2016	13	-39.69	
83	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,447.43	01/2012 -	05/2016	52	70.49	Progress is slow due to heavy rains during the period, RoU issue
84	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL, GUJARAT	12/2011	160.00 -	160.00	38.16	02/2016 02/2016	05/2016	3	0	
85	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL, BIHAR	04/2013	480.00 -	480.00	141.59	02/2016 -	07/2016	5	0	
86	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	537.65	03/2015 11/2015	08/2016	17	37.72	space constraint in few locations, obstructions, retendering, poor performance of contractor, torrential rain, delay in award

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
87	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016	61	0	
88	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	370.00	0.37	03/2013 -	10/2016	43	19.35	
89	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	838.08	572.18	11/2015 11/2016	11/2016	12	25.84	
90	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,395.63	11/2015 07/2016	11/2016	12	0	
91	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	480.22	08/2015 -	12/2016	16	0	
92	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	130.00	11/2016 -	12/2016	1	0	
93	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48	-3.5	
94	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	832.22	05/2014 03/2017	03/2017	34	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
5	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	264.14	10/2014 03/2017	03/2017	29	49.38	1.ROU: As per the recent amendment in LARR Act April 2015 issued by GOI, the compensation under P & MP Act.1963 as well as 12 other acts listed schedule 4 of the LARR act has to be as per schedule 1 of the act. Govt. of Maharashtra has issued Gazette Notification on 26.05.2015 only finalizing Multiplication factor. CA has prepared the award compensation for land and tree for village-Sawale, Taluka- Maval Dist. Pune and Varne village Distt. Raighad. Award is passed and the amount is transferred to CA account. Award distribution is in progress for both the villages. However pipeline works had been stopped for almost one month by villagers and political interference. Villagers are demanding more compensation for ROU. Discussion with local authority and villagers is on for resolving the issue. 2. SH55 in Pune District (13.5 kms): After obtaining Permission from PWD authorities, works stopped by local villagers at Pimple Jagtap, Khed Taluk, Pune District. They are opposing the pipeline laying along SH 55 stating that a) Existing SH55 road is not acquired by PWD Dept b) Pipeline laying on the new 4 lane road is not acceptable as this portion is yet to be acquired by PWD. Requested assistance from State Govt. / PWD authorities to provide the suitable documents confirming the ownership of ROU.
96	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	34.80	11/2016 -	04/2017	5	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
97	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017	25	0	
98	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,941.49	4,941.49	549.78	04/2016 12/2017	12/2017	20	19.81	
99	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	3,076.00	188.44	09/2017 03/2018	12/2017	3	0	
100	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 714.25	714.25	73.79	10/2017 02/2018	02/2018	4	17.66	
101	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	26.81	01/2013 -	12/2018	71	-10.01	
102	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	0	
103	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	6,086.08	592.92	05/2019 03/2020	03/2020	10	0	
	Total		76,753.21 -	84,335.99	50,658.89					
	POWER									
104	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,007.57	1,007.57	958.83	07/2013 01/2016	01/2016	30	139.32	
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	362.37	02/2012 -	02/2016	48	0	Severe ROW problem resolved. Balance work under progress.
106	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	766.14	11/2012 -	02/2016	39	0	Severe ROW problem in western UP.
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,447.42	04/2013 -	02/2016	34	0	Severe ROW problem in western UP.
108	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	187.20	01/2013 -	02/2016	37	0	Delayed land acquisition.
109	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43	0	Contractual problem.
110	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,578.86	11/2013 -	03/2016	28	0	Delayed land acquisition & severe ROW problem.

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
111	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	529.11	11/2013 -	03/2016	28	0	Delay in land acquisition for Chandwa S/stn. & huge forest involvement.Repeated stoppage of work by extremists affecting progress.
112	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	2,372.26	08/2014 -	03/2016	19	0	Delay in land acquisition for sub station & ROW problem.
113	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 609.44	609.44	579.80	02/2014 03/2016	03/2016	25	10.32	Severe ROW problem & non-readiness of Gantry tower at Essar Power Yard.
114	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,585.67	10/2014 -	03/2016	17	0	Severe ROW problem.
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	323.52	05/2015 -	03/2016	10	0	Delay in land acquisition for Varanasi s/stn.
116	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	3,178.09	01/2013 -	03/2016	38	0	- Delay in completion of Project due to delay in land acquisition of Ash Dyke and ROU of MUW corridor. - Non performance of civil, Swyd, CHP, AHP agencies
117	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	83.21	- Shifting of old switch yard. Frequent interruption due to labour unrest aggravated delay in completion of the work. - Space constraint to facilitate construction activity to preserve heritage old power house building of Bokaro -A. -Contractual issues. - Delay in construction of 400 KV BTPS - KTPS transmission line by PGCIL due to forest land clearance.
118	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
119	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]NNEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,085.84	6,085.84	4,362.53	12/2009 06/2016	06/2016	78	143.74	
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	509.66	528.56	11/2011 -	06/2016	55	0	Severe ROW problem in western UP.
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 689.03	689.03	548.12	07/2013 11/2015	06/2016	35	-8.45	Delay in forest clearance & snow bound area.
122	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,798.15	05/2014 -	06/2016	25	0	Delayed land acquisition for Champa S/stn.
123	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,938.06	09/2014 -	06/2016	21	0	Contractual issues & severe ROW problem in Karnataka.
124	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	2,319.63	07/2014 -	06/2016	23	0	Severe ROW problem & forest clearance awaited.
125	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL, MULTI STATE	12/2011	297.33 346.79	346.79	303.37	08/2014 06/2015	06/2016	22	16.63	Severe ROW problem in Karnataka.
126	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL, CHHATTISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22	27.6	Forest clearance awaited.
127	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,391.42	01/2015 -	06/2016	17	0	Forest clearance awaited.
128	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	94.63	09/2014 -	06/2016	21	0	Severe ROW problem are being encountered.

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
129	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76	9,569.76	5,724.59	06/2015	06/2016	12	0	Delay in land acquisition of Champa HVDC terminal & forest clearance awaited.
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63	723.63	587.42	11/2014	06/2016	19	0	Delay in forest clearance & severe ROW problem.
131	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44	3,201.44	2,996.11	10/2014	06/2016	20	0	Final forest clearance awaited. Permission to work obtained in Jan 16.
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE	09/2013	680.69	680.69	459.89	03/2016	06/2016	3	0	Severe ROW problem at Bhiwari end & non-readiness of bay at Jaipur (RRVPLN).
133	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL, MULTI STATE	10/2013	1,364.52	1,364.52	434.44	04/2016	06/2016	2	0	Delayed land acquisition & ROW problem in Jharkhand.
134	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL, MULTI STATE	02/2014	196.58	196.58	21.50	02/2016	06/2016	4	0	Completion delay due to delay in manufacturing of Reactors by M/s BHEL.
135	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,262.27	1,262.27	1,093.23	08/2013 07/2016	07/2016	35	119.91	
136	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL, MULTI STATE	03/2013	514.20	514.20	335.10	06/2015	08/2016	14	0	
137	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL, MULTI STATE	06/2012	1,909.24	1,909.24	1,016.53	06/2015	08/2016	14	0	Contractual issue.
138	TEESTA LOW DAM HEP, STAGE-IV (4x40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38	2,193.08	1,956.52	09/2009	09/2016	84	106.63	1. Initial delay in handing over of forest land & start of work 2. Bandh/ closure by locals, political outfits like GJMM and its effect 3. Due to inordinate delay and extended stay, BOQ rates become unworkable and resulted in cash deficit of Civil Contractor. 4. Delay in award of E&M contract due to clarification regarding participation of Chinese firm

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
139	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	951.92	07/2006 10/2016	10/2016	123	274.73	
140	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,751.47	4,402.95	01/2016 -	11/2016	10	57.92	Rehabilitation & Resettlement Plan is pending for approval with J&K State Govt.
141	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	16.20	04/2016 -	11/2016	7	0	Non- availability of PMU test lab worldwide and delay in amendment of Stnd. IEEE C37.118. design challenges.
142	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,903.55	11/2008 01/2016	12/2016	97	22.93	Severe ROW problem in Kerala.
143	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	579.39	09/2010 01/2016	12/2016	75	54.59	Severe ROW problem & forest clearance awaited.
144	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,237.58	10/2012 -	12/2016	50	0	Severe ROW problem & forest clearance awaited.
145	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,283.80	12/2012 12/2016	12/2016	48	36.79	Contractual issues & forest clearance awaited.
146	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	4,904.00	09/2016 -	12/2016	3	0	- Delay in supplies & slow progress in erection activities of Steam Generator (M/s BHEL). - Slow progress of work in Main Plant civil Package (M/s IVRCL)
147	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,043.56	12/2015 -	12/2016	12	0	Huge forest involvement & severe ROW problem.
148	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.00	9,606.82	1,353.36	02/2011 -	01/2017	71	133.06	- Frequent local issues/ resistance by land losers. - Supply of defective equipments and delay in replacement of same by RIL. - Dismantling and reconstruction of MDBFP Foundation. - Damage of imported insulation material and delay in its replacement.

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
149	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,719.00	09/2011 -	03/2017	66	54.25	-Inadequate deployment of manpower & resources by M/s BHEL and its sub-agencies have affected the erection/commissioning progress of U#1
150	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	2,405.85	01/2015 -	03/2017	26	0	Gen. project delayed. Forest clearance awaited.
151	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80 -	1,272.80	1,244.23	11/2012 -	03/2017	52	0	Delay in land acquisition & ROW problem.
152	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19 -	15,166.19	10,171.00	01/2017 -	03/2017	2	0	- NGT issue – work stopped from 17.03.14 to 01.04.14 - Work stoppage due to agitation against the project (5.07.14 to 22.07.14) - Delay in supply of Generator Stator of U#2 & 3 (M/s Toshiba)
153	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18 -	9,395.18	5,881.00	11/2016 -	08/2017	9	0	- Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
154	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	5,353.00	5,298.06	05/2014 -	09/2017	40	0	- Delay in balance land acquisition - Law & order problem
155	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	4,529.23	12/2016 -	09/2017	9	0	Delay of 12 months in Engg. & supplies by BGR which has led to a consequent delay of 12 months in erection.
156	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	11,463.30	08/2013 12/2017	12/2017	52	23.65	Gen. project delayed & law & order problem in NER.
157	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42 -	195.42	51.09	02/2014 -	02/2018	48	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
158	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	11,183.00	01/2011 10/2014	05/2018	88	73.65	- Non performance of Russian agency M/s TPE & M/s PM. - TPE stopped work from Oct'2013 and the contract of M/s TPE was terminated on 14.01.15. - Award of balance works on "as is where is basis in done in Jan'16. Schedule for U#1 commissioning is 16 months i.e. May'17 and subsequent units at 6 months interval.
159	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.76	5,398.46	09/2009 -	12/2018	111	114.28	1. Initial delay in start of Dam works due to delay in Revised Forest clearance 2. Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3. Back hill slope failure of Power House three times, 4. Ban on use of aggregates by Hon'ble High Court, Shimla
160	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,699.00	03/2013 -	12/2018	69	29.14	- Unprecedented flood in Uttarakhand during Aug'12 and Jun'13 damaging cofferdam and approach roads. TBM stuck up thrice & L&T Alpine JV did not perform leading to termination of contract. - Head Race Tunnel (HRT) Package is under retender. NIT done in May'15, Price bid opened in Nov'15.
161	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL, UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,603.73	02/2016 09/2019	09/2019	43	79.77	1. 4.67 Ha. land diversion case for dumping area at Village Chopra. 2. Cash flow problem with the contractor.
162	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58 -	2,491.58	789.89	06/2013 -	12/2019	78	0	Post Award: 1. Minor hindrances by local villagers.
	Total		161,177.43 -	197,765.42	137,606.94					

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>HEAVY INDUSTRY</u>									
163	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	122.78	NATRIIP is a temporary organization is the major hurdle of the project. NATRIIP is first of its kind of project for which no train manpower was available in the country.
	Total		1,718.00 -	3,827.30	.00					
	<u>HEALTH AND FAMILY WELFARE</u>									
164	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS - SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3	0	Fund Constraints.
165	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28	0	Local disturbances.
166	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15	0	i) Delay in issuance of labour licence from labour Deptt. ii) Frequent bandhs and heavy rain iii) Obstruction of work by locals. iv) Difficulty in procurement of sand and aggregates due to ban of forest produce.
	Total		779.77 -	779.77	493.22					
	<u>RAILWAYS</u>									
167	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]JMRT,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	259.68	
168	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR,BIHAR	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84	230.08	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
169	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	60.77	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defrozed and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015 (Meerut-Saharanpur).
170	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	
171	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	228.1	
172	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	
173	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	38.8	
174	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	95.9	Contractual issues
175	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
176	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	138.61	Contractual issues
177	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	
178	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	0	
179	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	233.08	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
180	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	38.24	
181	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]JNR,JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	700	
182	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	18.66	Contractual issue, land aquisition, non finalisation of alignment of flyover at Bilaspur
183	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	29.06	land aquisition & hurdle clearances like drains etc. by GHMC authorities.
184	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
185	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems. State Govt. has been requested to expedite handing over of land to Railways for early commissioning of the line.
186	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance of 9.94 Hect Trishna Wild life Sanctuary.
187	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	
188	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	0	
189	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-28.09	Non-handing over of land of Joka Depot
190	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	
191	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,443.62	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
192	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,544.40	-	03/1998 -	12/2019	261	299.79	
193	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
194	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	In Kanthi-Egra section land acquisition is kept in abeyance due to insufficient funds and no interest showing by the State Govt.
195	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected work progress in Rongchong and Kalimpong (West Bengal).
196	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-20	land aquisition problem
	Total		37,310.20 -	91,038.32	38,971.83					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
198	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2016	01/2016	93	0	
199	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	01/2016	25	0	
200	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	-	03/2013 -	01/2016	34	0	
201	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH, RAJASTHAN	02/2008	1,673.70 -	1,673.70	-	10/2011 -	01/2016	51	0	
202	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH, MADHYA PRADESH	05/2013	1,055.00 -	1,055.00	-	11/2015 -	01/2016	2	0	
203	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	02/2016	92	0	
204	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	-	05/2010 -	02/2016	69	0	
205	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	1,509.10	-	09/2012 -	02/2016	41	0	
206	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	02/2016	38	0	
207	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	02/2016	17	0	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
208	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH, RAJASTHAN	03/2012	914.50 -	914.50	1,097.62	10/2015 -	02/2016	4	0	
209	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	240.22	09/2008 -	03/2016	90	30.1	
210	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	392.60	02/2009 -	03/2016	85	28.93	
211	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	-	04/2009 -	03/2016	83	92.75	
212	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	-	11/2008 -	03/2016	88	0	
213	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	-	11/2008 -	03/2016	88	80.68	
214	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	-	04/2009 -	03/2016	83	0	
215	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	195.00	278.96	06/2008 -	03/2016	93	0	
216	BIJUNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	374.10	06/2008 -	03/2016	93	0	
217	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	-	09/2008 -	03/2016	90	0	
218	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	273.26	10/2008 -	03/2016	89	-8.95	
219	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	331.23	300.46	07/2009 -	03/2016	80	68.99	
220	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	348.16	322.70	09/2007 -	03/2016	102	0	
221	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,607.78	05/2012 -	03/2016	46	0	
222	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	-	04/2013 -	03/2016	35	0	
223	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	03/2016	33	0	
224	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	03/2016	19	0	
225	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	351.54	329.40	05/2013 -	03/2016	34	0	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
226	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	830.97	11/2013 -	03/2016	28	0	
227	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	0	
228	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	609.00	02/2014 -	03/2016	25	0	
229	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	760.20	03/2014 -	03/2016	24	0	
230	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	348.00	04/2014 -	03/2016	23	0	
231	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	544.08	11/2013 -	03/2016	28	0	
232	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	-	02/2014 -	03/2016	25	0	
233	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	0	
234	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31	0	
235	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37	0	
236	BEAWARE PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,301.00	06/2014 -	03/2016	21	-02	
237	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21	0	
238	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17	0	
239	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	229.16	06/2014 -	03/2016	21	0	
240	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	0	
241	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88	0	
242	FOUR LANING OF ORISSA/CHATTISHGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7	0	
243	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
244	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016	94	0	
245	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67	0	
246	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,409.36	07/2012 -	04/2016	45	0	
247	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,004.62	07/2013 -	04/2016	33	0	
248	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32	0	
249	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	822.96	04/2015 -	04/2016	12	0	
250	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	0	
251	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	0	
252	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,287.44	09/2014 -	05/2016	20	0	
253	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN	01/2014	158.04 -	158.04	85.68	12/2015 -	05/2016	5	0	
254	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	0	
255	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI, TAMIL NADU	04/2009	353.37 -	353.37	-	10/2011 -	06/2016	56	0	
256	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,619.94	11/2011 -	06/2016	55	106.5	
257	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, TAMIL NADU	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39	0	
258	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	0	
259	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35	0	

(January 2016)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
260	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	06/2016	36	0	
261	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	-	06/2013 -	06/2016	36	0	
262	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35	0	
263	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29	0	
264	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,478.63	05/2014 -	06/2016	25	0	
265	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24	0	
266	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	893.90	03/2013 -	06/2016	39	0	
267	ETAHAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,840.00	09/2015 -	06/2016	9	0	
268	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	-	12/2015 -	06/2016	6	0	
269	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21	0	
270	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI, RAJASTHAN	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5	0	
271	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD, ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	0	
272	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	214.17	03/2008 07/2016	07/2016	100	0	
273	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	277.06	10/2013 -	07/2016	33	-11	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
274	REHABILITATION AND UPGRADE OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]P.W.D, ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	0	
275	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	304.17	04/2008 08/2016	08/2016	100	0	
276	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	197.40	05/2008 07/2016	08/2016	99	0	
277	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,050.90	05/2013 -	08/2016	39	0	
278	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	-	08/2013 -	08/2016	36	0	
279	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,267.57	02/2014 -	08/2016	30	0	
280	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]P.W.D, MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	0	
281	FOUR LANING FROM MP-MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	1,579.15	06/2012 -	08/2016	50	0	
282	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, ASSAM	12/2003	217.61 309.56	309.56	370.66	04/2010 09/2016	09/2016	77	42.25	
283	INDORE-DEWAS (NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40	0	
284	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	211.68	01/2014 -	09/2016	32	0	
285	2-LANING WITH PAVED SHOULDERS OF RAIBAREILI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	132.64	01/2016 -	09/2016	8	0	
286	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]P.W.D, MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	0	
287	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
288	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	159.73	01/2016 -	10/2016	9	0	
289	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	0	
290	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	-	11/2014 -	11/2016	24	0	
291	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	202.97	06/2005 -	12/2016	138	0	
292	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	102.85	09/2007 -	12/2016	111	0	
293	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	0	
294	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	0	
295	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,742.94	03/2013 -	12/2016	45	0	
296	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	879.98	02/2013 -	12/2016	46	0	
297	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	-	12/2013 -	12/2016	36	0	
298	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	-	05/2013 -	12/2016	43	0	
299	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.50	07/2013 -	12/2016	41	0	
300	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35	0	
301	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	425.65	09/2013 -	12/2016	39	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
302	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00	624.00	343.75	04/2014	12/2016	32	0	
303	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25	283.25	-	10/2015	12/2016	14	0	
304	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275.622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21	333.21	14.12	12/2015	12/2016	12	0	
305	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21	333.21	-	12/2015	12/2016	12	0	
306	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04	923.04	-	11/2016	12/2016	1	0	
307	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	208.00	295.20	04/2008	01/2017	105	0	
308	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16	702.16	391.77	07/2014	02/2017	31	0	
309	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55	251.55	-	02/2015	02/2017	24	0	
310	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00	617.00	-	08/2012	03/2017	55	0	
311	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00	485.00	-	08/2013	03/2017	43	0	
312	WALAJPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95	1,287.95	-	11/2015	03/2017	16	0	
313	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00	2,848.00	504.51	03/2014	04/2017	37	0	
314	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00	281.31	149.27	02/2010	05/2017	87	2.29	
315	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43	580.43	221.98	08/2013	05/2017	45	0	
316	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00	1,479.00	461.94	06/2015	05/2017	23	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
317	REHABILITATION AND UPGRADE OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD, ANDHRA PRADESH	02/2015	224.83	224.83	-	05/2015	05/2017	24	0	
318	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79	998.79	-	08/2013	07/2017	47	0	
319	REHABILITATION AND UPGRADE OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01	309.01	-	09/2015	08/2017	23	0	
320	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73	368.73	50.37	09/2016	09/2017	12	0	
321	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45	271.45	-	10/2015	10/2017	24	0	
322	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67	165.67	2.43	11/2015	11/2017	24	0	
323	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12	159.12	2.43	11/2015	11/2017	24	0	
324	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40	356.40	344.00	07/2014	12/2017	41	0	
325	BARSAAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00	867.00	278.17	02/2015	12/2017	34	0	
326	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD, ODISHA	12/2011	191.08	191.08	42.58	08/2015	03/2018	31	0	
327	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI, MADHYA PRADESH	11/2015	867.66	867.66	18.68	11/2015	05/2018	30	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
328	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	0	
329	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	0	
	Total		93,364.12 -	95,190.05	50,887.31					
	<u>SHIPPING AND PORTS</u>									
330	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	415.80	12/2010 -	01/2016	61	82.72	
331	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120	300	Relocating of fishing stalls for a length about 300m in fishing harbour.
332	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	66.82	
	Total		762.06 -	1,679.29	921.80					
	<u>TELECOMMUNICATIONS</u>									
333	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	0	
334	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-4.74	
	Total		15,445.17 -	15,345.17	2,720.00					
	<u>URBAN DEVELOPMENT</u>									
335	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17	0	
336	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD,WEST BENGAL	01/2009	225.81 -	225.81	138.38	06/2012 03/2016	03/2016	45	0	

(January 2016)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
337	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16	0	
338	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	
339	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 11,609.00	13,845.01	13,525.81	06/2011 12/2015	06/2016	60	116.5	Difficult geological condition , slow progress to avoid damages to structure in densely populated area
340	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	168.00	05/2013 10/2015	06/2016	37	0	
341	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8	0	
342	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9	0	Rehabilitation & Resettlement, Land acquisition and Delay in technical approval from M/o Railways delays the project.
343	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	
344	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	24.34	09/2015 07/2016	04/2017	19	0	
345	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	0	
346	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 26,405.01	26,405.01	217.54	02/2019 03/2020	03/2020	13	0	
	Total		88,550.24 -	96,000.12	46,109.56					
	Grand Total		584,806.34	707,516.53	407,155.09					

Annexure - VII

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(January 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00 -	09/2010 -	09/2016	62.57	72
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00 -	12/2008 -	05/2016	70.54	89
	Total		16,663.00 -	28,139.00 -				
	<u>COAL</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39 -	03/2013 -	03/2016	478.50	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57 -	03/2012 -	03/2017	87.58	60
5	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62 -	03/2012 -	03/2023	16.86	132
6	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27 -	03/2016 -	03/2018	12.97	24
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63 -	03/2013 -	03/2017	0.02	48
	Total		1,800.69 -	3,170.48 -				
	<u>HEAVY INDUSTRY</u>							
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30 -	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30 -				
	<u>PETROLEUM</u>							
9	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79 -	10/2014 -	03/2017	49.38	29
10	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00 -	03/2013 -	10/2016	19.35	43
11	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25 -	10/2017 -	02/2018	17.66	4
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.08 -	11/2015 -	11/2016	25.84	12
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00 -	10/2011 -	03/2016	67.62	53

(January 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
14	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	04/2016	45.83	35
15	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72	17
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	05/2016	70.49	52
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
18	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35 -	4,941.49	04/2016 -	12/2017	19.81	20
19	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2016	16.05	39
	Total		41,311.99 -	49,923.98				
	<u>POWER</u>							
20	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	06/2016	16.63	22
21	TUJRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
22	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.57	07/2013 -	01/2016	139.32	30
23	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2016	54.59	75
24	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32	25
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	08/2013 -	07/2016	119.91	35
26	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63	84
27	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
28	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	06/2016	27.60	22
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2016	22.93	97
30	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	12/2016	36.79	48
31	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21	51
32	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,085.84	12/2009 06/2016	06/2016	143.74	78
33	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14	69

(January 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92	10
35	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28	111
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06	71
37	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25	66
38	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
39	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		54,750.02 -	91,401.62				
	<u>RAILWAYS</u>							
40	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62	177
41	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61	91
42	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44	21
43	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90	86
44	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77	48
45	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
46	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
47	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
48	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66	93
49	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
50	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
51	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
52	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
53	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21

(January 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
54	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
56	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
57	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
59	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
60	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	3,040.00	03/2009 -	03/2016	230.08	84
61	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
62	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
63	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
65	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		22,458.31 -	77,795.14				
	ROAD TRANSPORT AND HIGHWAYS							
66	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	03/2016	30.10	90
67	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68	88
68	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99	80
69	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75	83
70	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	09/2016	42.25	77
71	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
72	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93	85
73	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2016	106.50	55

(January 2016)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		2,586.46	4,438.02				
			-					
	<u>SHIPPING AND PORTS</u>							
74	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00	600.00	03/2006	03/2016	300.00	120
75	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67	409.83	04/2009	08/2016	66.82	88
76	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39	669.46	12/2010	01/2016	82.72	61
	Total		762.06	1,679.29				
			-					
	<u>STEEL</u>							
77	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73	173.00	12/2015	03/2017	15.54	15
78	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49	207.00	12/2016	07/2017	17.96	7
79	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]	07/2011	324.87	325.00	12/2015	03/2016	0.04	3
80	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00	488.40	10/2016	06/2017	42.39	8
81	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88	1,060.00	02/2014	03/2016	37.86	25
	Total		1,761.97	2,253.40				
			-					
	<u>URBAN DEVELOPMENT</u>							
82	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	13,845.01	06/2011	06/2016	116.50	60
	Total		6,395.00	13,845.01				
			-					
	Grand Total		150,207.50	276,473.24				

Annexure - VIII

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015
	Total		553.21 -		
	<u>COAL</u>				
3	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		467.78 -		
	<u>STEEL</u>				
4	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	04/2013 09/2014	06/2015
5	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	05/2013 01/2015	08/2015
6	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
7	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
	Total		1,877.55 -		
	<u>PETROCHEMICALS</u>				
8	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	04/2012 12/2013	12/2015
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
9	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	06/2015
10	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
11	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
12	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
13	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
14	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
15	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	01/2014 -	-
16	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
	Total		9,226.73 -		
	<u>POWER</u>				
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
18	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
19	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	06/2014 03/2016	-
20	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		7,211.60 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
21	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014
	Total		414.11 -		
	<u>RAILWAYS</u>				
22	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
23	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
24	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
25	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
26	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
27	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
28	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
29	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
30	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
31	CUTTACK - BARANG (LD) - [220100326]RVNL, ODISHA	04/1995	127.13 -	- 10/2014	10/2014
32	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
33	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	- -	01/2015
34	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
35	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
36	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 236.41	- -	03/2015
37	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
38	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
39	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
40	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR, TAMIL NADU	04/2007	247.00 -	- -	03/2015
41	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
42	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	- -	03/2015
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015
44	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015
45	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015
46	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR, KARNATAKA	04/2010	203.40 -	- -	09/2015
47	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
48	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015
49	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015
50	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-
51	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-
52	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,054.35 2,200.00	- -	-
53	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345], UTTAR PRADESH	04/1997	836.26 -	- -	-
54	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00	03/2010 -	-
55	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
56	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
57	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
59	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
60	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
61	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
62	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
63	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
64	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
65	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-
66	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
67	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
68	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
69	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
70	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
71	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
72	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
73	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
74	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
75	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
76	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
77	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
78	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
79	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
80	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
81	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
82	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
83	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
84	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
85	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
86	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
87	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
88	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
89	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
90	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
91	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
92	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
93	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
94	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
95	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
96	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
98	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-
99	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
100	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
101	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
102	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
103	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
104	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-
105	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
106	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
107	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
108	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
109	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
110	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
111	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-
112	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
113	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
114	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
115	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
116	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
117	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
118	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
119	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
120	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
121	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
122	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
123	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
124	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
125	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
126	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
127	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
128	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
129	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
130	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
131	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
132	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
133	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-
134	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
135	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-
136	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
137	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
138	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-
139	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-
140	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-
141	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-
142	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
143	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
144	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
145	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
146	ARARIA-SUPAUL (NL) - [N22000177]ECR, BIHAR	04/2008	304.41 -	- -	-
147	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
148	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
149	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	-
150	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	470.00 -	- -	-
151	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
152	ATTIPPATTU-PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	446.87 -	- -	-
153	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR, MULTI STATE	04/2008	523.52 -	- -	-
154	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-
155	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR, TAMIL NADU	04/1999	198.68 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
156	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
157	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
158	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
159	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
160	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
161	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
162	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
163	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
164	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
165	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
166	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
167	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
168	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
169	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
170	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
171	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
172	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
173	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
174	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
175	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
176	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
177	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
178	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
179	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
180	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
181	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
182	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
183	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
184	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
185	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
186	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
187	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
188	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
189	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
190	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
191	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
192	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
193	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
194	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
195	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
196	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
197	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
198	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
199	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
200	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
201	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
202	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
203	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
204	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
205	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
206	DELHI-SOHNNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
207	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
208	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
209	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
210	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
211	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
212	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
213	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
214	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
215	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
216	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
217	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
218	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
219	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
220	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
221	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
222	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
223	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
224	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
225	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
226	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
227	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
228	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
229	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
230	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
231	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
232	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
233	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
234	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
235	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
236	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
237	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
238	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
239	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
240	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
241	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
242	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
243	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-
244	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
245	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
246	HUBLI- CHIKKAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-
247	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-
248	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-
249	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-
250	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
251	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
252	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-
253	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-
254	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-
255	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		113,146.06		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
256	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48	02/2011	02/2011
257	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20	02/2011	02/2011
258	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26	05/2015	05/2015
259	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30	07/2014	07/2014
260	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 161.70	07/2015	07/2015
261	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015	08/2015
262	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 158.35	08/2015	08/2015
263	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00	09/2010	09/2010
264	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00	09/2010	09/2010
265	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21	11/2015	11/2015
266	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05	12/2015	12/2015
267	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04	10/2010	10/2010
268	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56	02/2012	06/2013
269	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00	10/2013	10/2013
270	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47	07/2014	08/2015
271	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47	09/2007	-
272	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00	10/2008	-
273	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03	10/2008	-
274	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00	07/2008	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
276	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
277	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
278	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	-
279	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
280	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-
281	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
282	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-
283	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
284	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	-
285	KUNDUPUR-SURATHKAL AND MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	- -	-
286	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	-
287	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	-
288	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	- -	-
289	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	-
290	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	-
291	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-
292	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.51 -	05/2014 -	-
293	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-
294	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-
295	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
296	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
297	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
298	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
299	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
300	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
301	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
302	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-
303	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
304	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
305	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
306	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
307	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
308	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
309	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
310	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
311	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
312	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
313	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
314	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
315	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
316	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
317	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	03/2015 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
318	REHABILITATION AND UPGRADE OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
319	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
320	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
321	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
322	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
323	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
324	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
325	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
326	REHABILITATION AND UPGRADE TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
327	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
328	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-
329	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
330	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
331	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
332	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
333	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
334	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
335	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
336	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
337	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
338	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
339	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
340	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
341	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
342	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
343	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	02/2015 -	-
344	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
345	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
346	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
347	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
348	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
349	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
350	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
351	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	-
352	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
353	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
354	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-
355	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
356	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	01/1991	225.02 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
357	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	01/1991	223.30 -	- -	-
358	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
359	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	- -	-
360	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI, MADHYA PRADESH	06/2015	583.79 -	- -	-
361	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, WEST BENGAL	10/2015	531.13 -	- -	-
362	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH, WEST BENGAL	10/2015	361.15 -	- -	-
363	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	01/1991	289.99 -	- -	-
364	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	- -	-
365	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	- -	-
366	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI, MAHARASHTRA	12/2015	649.50 -	- -	-
367	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH, GOA	10/2015	936.40 -	- -	-
368	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP, MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
369	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI, HARYANA	07/2015	2,128.72 -	- -	-
370	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	- -	-
371	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI, UTTAR PRADESH	07/2015	1,657.20 -	- -	-
372	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	- -	-
373	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	-
374	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI, TAMIL NADU	01/1991	285.00 -	01/2008 -	-
375	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-
376	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-
377	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD, RAJASTHAN	09/2012	511.00 -	10/2013 -	-
378	NAGPUR - KONDHALI - [N24000472]DORTH, MAHARASHTRA	09/2005	168.00 -	06/2006 -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
379	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
380	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-
381	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	- -	-
382	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH, BIHAR	08/2015	814.04 -	- -	-
383	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	-
384	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, WEST BENGAL	12/2015	1,423.96 -	- -	-
385	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	-
386	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	01/1991	1,388.00 -	- -	-
387	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	- -	-
388	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	- -	-
389	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	- -	-
390	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-
391	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI, MADHYA PRADESH	06/2015	1,583.79 -	- -	-
392	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
393	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	01/1991	1,167.45 -	- -	-
394	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	- -	-
395	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-
396	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH, GOA	12/2015	773.98 -	- -	-
397	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH, GOA	12/2015	819.95 -	- -	-
398	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	- -	-
399	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	- -	-
400	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR	01/1991	478.35 -	- -	-
401	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
402	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
403	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
404	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
405	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
406	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
407	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
408	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
409	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
	Total		85,467.45 -		
	<u>SHIPPING AND PORTS</u>				
410	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
	Total		2,427.40 -		
	<u>URBAN DEVELOPMENT</u>				
411	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 12/2015	12/2015
412	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015
413	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
414	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	02/2015 -	-
415	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	-
416	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	-
417	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	03/2012 -	-
418	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00 -	06/2015 -	-
419	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
420	REHABILITATION AND STRENGTHENING OF SEWEWRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
421	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	01/2015 -	-
422	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
	Total		25,670.13 -		
	Grand Total		251,922.63		

Annexure - IX

Details of Projects Without Original Date of Commissioning

(January 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	CIVIL AVIATION								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	21.76	-	09/2018	-	0/0
	Total		314.61	314.61	21.76				0/0
	RAILWAYS								
2	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71	744.71	576.86	-	03/2016	-	0/1
3	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17	914.98	846.18	-	03/2016	-	0/0
4	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81	155.81	18.25	-	12/2016	-	0/0
5	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92	1,225.90	257.59	-	03/2017	-	0/0
6	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0
7	NEW B.G. LINE FROM TETELIA TO BYRNIAHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00	496.24	213.72	-	03/2017	-	0/0
8	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52	394.28	233.46	-	03/2017	-	0/0
9	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20	365.00	2.52	-	12/2017	-	0/0
10	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER, UTTAR PRADESH	03/1997	677.97	1,651.54	1,621.40	-	03/2018	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92	565.13	2.80	-	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00	886.65	-	-	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77	441.45	85.78	-	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55	288.81	11.74	-	03/2018	-	0/0
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22	679.57	40.41	-	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82	435.58	0.56	-	03/2018	-	0/0

(January 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL & RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.39	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	- -	03/2020	-	0/0
27	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
28	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	175.26	- -	03/2020	-	0/0
	Total		19,590.88 -	30,884.76	5,992.51				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
29	ROHTAK - BAWAL (APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	650.00	813.91	- -	03/2016	-	0/0
30	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	347.60	- -	07/2016	-	0/0
31	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	1,665.00	994.21	- -	09/2016	-	0/0
32	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP, MAHARASHTRA	01/2014	446.77 -	446.77	-	- -	06/2017	-	0/4
33	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP, MAHARASHTRA	03/2015	168.30 -	168.30	-	- -	10/2017	-	0/4
34	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	876.68	- -	01/2018	-	0/0

(January 2016)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
35	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	36.02	- -	04/2018	-	0/1
	Total		5,099.07 -	5,099.07	3,068.42				0/9
	Grand Total		25,004.56	36,298.44	9,082.69				0/10

Annexure - X

Details of Projects Without Milestones w.r.t. Original Schedule

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	03/2015	0/0
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	09/2015	0/0
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 06/2016	09/2017	0/0
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	-	09/2018	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	03/2024 -	03/2024	0/0
	Total		1,875.32 -			0/0
	<u>FERTILISERS</u>					
6	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 -	11/2016	0/0
	Total		197.79 -			0/0
	<u>MINES</u>					
7	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 -	11/2016 -	11/2016	0/0
8	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 -	11/2016 -	11/2016	0/0
9	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL,MADHYA PRADESH	09/2011	1,856.00 -	09/2017 -	04/2020	0/0
	Total		2,555.63 -			0/0
	<u>STEEL</u>					
10	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,060.00	02/2014 -	03/2016	0/0
11	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 325.00	12/2015 -	03/2016	0/0
12	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 254.00	06/2016 -	06/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	12/2016	0/0
14	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
15	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
16	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2017	0/0
17	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	03/2017	0/0
18	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	06/2017	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 207.00	12/2016 -	07/2017	0/0
20	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
21	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	10/2017 -	10/2017	0/0
22	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	11/2017	0/0
23	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	12/2017 -	12/2017	0/0
24	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	03/2018 -	03/2018	0/0
25	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
26	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	04/2018 -	04/2018	0/0
27	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
28	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
29	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
	Total		15,398.80 -			0/0
	<u>PETROLEUM</u>					
30	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	06/2012 -	01/2016	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	03/2016	0/0
32	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 05/2016	05/2016	0/0
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	01/2012 -	05/2016	0/0
34	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	02/2016 02/2016	05/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 10/2016	10/2016	0/0
36	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	10/2016	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	08/2015 -	12/2016	0/0
38	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	12/2016	0/0
39	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 -	03/2017	0/0
40	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	03/2017 -	03/2017	0/0
41	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 2,098.43	05/2017 -	05/2017	0/0
42	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	09/2017 -	09/2017	0/0
43	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00 -	09/2017 03/2018	12/2017	0/0
44	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA	05/2015	2,443.00 -	12/2017 -	12/2017	0/0
45	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 -	03/2019	0/0
46	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 -	03/2019	0/0
47	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 1,881.22	11/2019 -	11/2019	0/0
48	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 03/2020	03/2020	0/0
49	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-	0/0
50	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-	0/0
51	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
52	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
53	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-	0/0
	Total		40,203.59 -			0/0
	<u>POWER</u>					
54	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,139.00	12/2011 -	03/2016	0/0
55	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]PGCIL,ANDHRA PRADESH	05/2015	312.94 -	05/2016 -	05/2016	0/0
56	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	09/2014 -	06/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
57	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	11/2016	0/0
58	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL	04/2007	4,122.00 8,781.00	02/2011 -	01/2017	0/0
59	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 -	03/2017	0/0
60	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
61	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 -	09/2017	0/0
62	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
63	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
64	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
65	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA	01/2016	187.04 -	06/2018 -	06/2018	0/0
66	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
67	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
68	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
69	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
70	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	04/2020	0/0
71	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	Total		28,883.90 -			0/0
	<u>HEAVY INDUSTRY</u>					
72	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
73	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
74	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	01/2016	0/0
75	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	03/2016	0/0
76	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	03/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
77	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
78	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	05/2017	0/0
79	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	05/2017	0/0
80	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	05/2017	0/0
81	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
	Total		2,563.15 -			0/0
	<u>RAILWAYS</u>					
82	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008	0/0
83	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010	0/0
84	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
85	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012	0/0
86	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012	0/0
87	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
88	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013	0/0
89	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014	0/0
90	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]JER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
91	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014	0/0
92	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015	0/0
93	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015	0/0
94	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015	0/0
95	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015	0/0
96	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015	0/0
97	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015	0/0
98	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
99	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
100	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015	0/0
101	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
102	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015	0/0
103	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	06/2015	0/0
104	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	09/2015	0/0
105	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	09/2015	0/0
106	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	09/2015	0/0
107	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
108	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	12/2015	0/0
109	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	10/2007 12/2012	12/2015	0/0
110	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRT,MAHARASHTRA	03/1996	495.44 495.44	03/2004 -	03/2016	0/0
111	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 3,040.00	03/2009 -	03/2016	0/0
112	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2016	0/0
113	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
114	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	12/2012 -	03/2016	0/0
115	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2016	0/0
116	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
117	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
118	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	04/2016	0/0
119	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
120	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	10/2016	0/0
121	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
122	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	12/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
123	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
124	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	03/2017	0/0
125	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	- -	03/2017	0/0
126	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	- -	03/2017	0/0
127	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
128	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
129	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
130	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
131	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	04/2008 12/2011	06/2017	0/0
132	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
133	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2017	0/0
134	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	12/2017	0/0
135	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 315.13	- -	12/2017	0/0
136	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
137	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2018	0/0
138	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	03/2018	0/0
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2018	0/0
140	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2018	0/0
141	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	04/2014 03/2015	03/2018	0/0
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	- 03/2014	03/2018	0/0
143	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	- -	03/2018	0/0
144	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 190.39	- -	03/2018	0/0
145	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 278.21	- -	03/2018	0/0
146	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	- -	03/2018	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
147	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	- -	03/2018	0/0
148	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	- -	03/2018	0/0
149	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	- -	03/2018	0/0
150	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	- -	03/2018	0/0
151	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
153	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
154	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 36.38	- -	03/2019	0/0
155	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	03/2011 03/2014	03/2019	0/0
156	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	- -	03/2019	0/0
157	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0
158	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	- -	03/2019	0/0
159	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 205.31	- -	03/2019	0/0
160	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	- -	03/2019	0/0
161	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
162	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2019	0/0
163	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	12/2019	0/0
164	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	- -	12/2019	0/0
165	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
166	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	12/2015 -	03/2020	0/0
167	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 03/2020	03/2020	0/0
168	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
169	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- 03/2016	03/2020	0/0
170	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
171	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
172	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR, MULTI STATE	09/1998	247.66 3,500.00	05/2008 -	-	0/0
173	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-	0/0
174	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR, MULTI STATE	04/2012	1,054.35 2,200.00	- -	-	0/0
175	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345], UTTAR PRADESH	04/1997	836.26 -	- -	-	0/0
176	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 2,434.00	03/2010 -	-	0/0
177	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	- 03/2010	-	0/0
178	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
179	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-	0/0
180	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 -	- -	-	0/0
181	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	-	0/0
182	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	-	0/0
183	NANGALDAM-TALWARA(NL), NR - [220100188]NR, MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
184	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 -	- -	-	0/0
185	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
186	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	2,957.21 -	07/2005 -	-	0/0
187	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	501.69 501.69	03/2012 -	-	0/0
188	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	550.00 517.70	- -	-	0/0
189	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 -	- -	-	0/0
190	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
191	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	100.00 -	- -	-	0/0
192	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 -	- -	-	0/0
193	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
194	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
195	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-	0/0
196	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
197	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	04/1996	138.00 -	- -	-	0/0
198	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, ODISHA	04/1994	470.21 -	- -	-	0/0
199	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	- 09/2009	-	0/0
200	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, BIHAR	04/2003	528.65 -	- -	-	0/0
201	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
202	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-	0/0
203	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-	0/0
204	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	- -	-	0/0
205	HATHUA-BHATNI (N L) (NER) - [220100319]NER, MULTI STATE	04/2005	230.03 -	- -	-	0/0
206	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	02/2015 -	-	0/0
207	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 -	- -	-	0/0
208	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
209	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
210	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	378.56 -	- -	-	0/0
211	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER, JHARKHAND	03/1997	261.70 -	02/2006 -	-	0/0
212	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
213	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19 -	- -	-	0/0
214	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	-	0/0
215	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 -	- -	-	0/0
216	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 -	- -	-	0/0
217	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-	0/0
218	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
219	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 -	-	0/0
220	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0
221	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
222	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
223	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
224	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
225	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	-	0/0
226	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	-	0/0
227	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
228	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
229	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
230	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
231	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
232	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	-	0/0
233	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-	0/0
234	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
235	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
236	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
237	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
238	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
239	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
240	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
241	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-	0/0
242	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
243	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-	0/0
244	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-	0/0
245	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-	0/0
246	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-	0/0
247	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-	0/0
248	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00 -	- -	-	0/0
249	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	- -	-	0/0
250	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-	0/0
251	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	- -	-	0/0
252	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-	0/0
253	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-	0/0
254	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
255	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
256	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 -	- -	-	0/0
257	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0
258	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-	0/0
259	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-	0/0
260	BIHTA-AURANGABAD (NL) - [N22000170]ECOR, BIHAR	04/2008	326.20 -	- -	-	0/0
261	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR, BIHAR	04/1999	175.69 -	- -	-	0/0
262	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR, BIHAR	04/2006	285.07 -	- -	-	0/0
263	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-	0/0
264	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-	0/0
265	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-	0/0
266	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
267	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
268	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
269	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
270	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
271	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
272	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
273	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
274	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
275	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
276	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
277	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
278	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
279	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
280	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
281	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
282	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
283	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
284	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
285	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
286	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
287	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
288	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
289	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
290	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
291	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
292	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
293	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
294	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
295	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
296	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
297	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
298	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
299	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
300	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-	0/0
301	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
302	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
303	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
304	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
305	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
306	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
307	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
308	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
309	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
310	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
311	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-	0/0
312	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
313	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
314	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
315	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
316	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
317	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
318	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-	0/0
319	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-	0/0
320	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-	0/0
321	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-	0/0
322	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
323	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
324	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
325	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
326	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
327	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
328	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
329	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
330	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
331	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
332	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
333	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
334	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
335	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
336	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
337	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
338	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
339	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
340	BHADRALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-	0/0
341	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-	0/0
342	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
343	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
344	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
345	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
346	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
347	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
348	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
349	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
350	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
351	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
352	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
353	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
354	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
355	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
356	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
357	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
358	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
359	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
360	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
361	SAMBALPUR-TALCHER DOUBLING - [N22000315]JECOR,ODISHA	03/2011	679.27 -	- -	-	0/0
362	BHADRAK - NERGUNDI 3RD LINE - [N22000316]JECOR,ODISHA	03/2013	858.67 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
363	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-	0/0
364	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	-	0/0
365	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
366	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-	0/0
367	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,900.00 -	- -	-	0/0
368	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	-	0/0
369	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 -	- -	-	0/0
370	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	- -	-	0/0
371	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
372	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
373	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA	05/2015	400.00 -	- -	-	0/0
374	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 -	- -	-	0/0
375	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 -	- -	-	0/0
376	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 -	- -	-	0/0
	Total		171,692.96 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
377	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
378	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
379	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0
380	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 161.70	07/2015 -	07/2015	0/0
381	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	08/2015	0/0
382	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 158.35	08/2015 -	08/2015	0/0
383	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
384	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
385	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
386	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	12/2015 -	12/2015	0/0
387	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
388	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
389	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
390	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	08/2015	0/0
391	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2016	01/2016	0/0
392	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	01/2016	0/0
393	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	01/2016	0/0
394	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237]NHAI,RAJASTHAN	01/2014	177.32 -	01/2016 -	01/2016	0/0
395	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	01/2016	0/0
396	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	01/2016	0/0
397	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2016 -	01/2016	0/0
398	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	01/2016	0/0
399	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]DORTH,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	01/2016	0/0
400	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497]NHAI,MADHYA PRADESH	03/2015	830.36 -	01/2019 -	01/2016	0/0
401	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	02/2016	0/0
402	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	02/2016	0/0
403	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	02/2016	0/0
404	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	09/2014 -	02/2016	0/0
405	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
406	4 LANING OF GOMTI CHAURAHA - UDAIPUR - [N24000455]DORTH,RAJASTHAN	03/2012	914.50 -	10/2015 -	02/2016	0/0
407	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	03/2016	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	03/2016	0/0
409	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	03/2016	0/0
410	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	03/2016	0/0
411	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	03/2016	0/0
412	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	03/2016	0/0
413	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	06/2008 -	03/2016	0/0
414	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	06/2008 -	03/2016	0/0
415	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	03/2016	0/0
416	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	03/2016	0/0
417	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	03/2016	0/0
418	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 -	03/2016	0/0
419	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	03/2016	0/0
420	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	03/2016	0/0
421	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	03/2016	0/0
422	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	03/2016	0/0
423	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	03/2016	0/0
424	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	03/2016	0/0
425	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	03/2016	0/0
426	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	03/2016	0/0
427	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	03/2016	0/0
428	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	03/2016	0/0
429	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	03/2016	0/0
430	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	03/2016	0/0
431	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	01/2014 -	03/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2016	0/0
433	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	03/2016	0/0
434	BEAWAR PALI PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.51 -	06/2014 -	03/2016	0/0
435	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	03/2016	0/0
436	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	10/2014 -	03/2016	0/0
437	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	03/2016	0/0
438	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
439	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	03/2016 -	03/2016	0/0
440	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
441	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI,BIHAR	11/2005	240.00 -	11/2008 -	03/2016	0/0
442	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATTISGARH	02/2013	1,232.00 -	08/2015 -	03/2016	0/0
443	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2016	0/0
444	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	03/2016	0/0
445	ROHTAK - BAWAL(APPROVED LENGTH 97 KM) - [N24000525]NHAI,HARYANA	02/2010	650.00 -	- -	03/2016	0/0
446	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 04/2016	04/2016	0/0
447	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	09/2010 -	04/2016	0/0
448	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	04/2016	0/0
449	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	04/2016	0/0
450	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2016	0/0
451	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	04/2016 -	04/2016	0/0
452	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2016	0/0
453	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	05/2016	0/0
454	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2016	0/0
455	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI,RAJASTHAN	01/2014	158.04 -	12/2015 -	05/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
456	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	05/2016	0/0
457	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
458	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	06/2016	0/0
459	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2016	0/0
460	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	06/2016	0/0
461	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
462	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2016	0/0
463	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	06/2016	0/0
464	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	06/2016	0/0
465	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2016	0/0
466	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2016	0/0
467	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2016	0/0
468	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	06/2016	0/0
469	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	06/2016	0/0
470	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	01/2016 -	06/2016	0/0
471	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]NHAI,UTTAR PRADESH	06/2014	569.38 -	06/2016 -	06/2016	0/0
472	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456]DORTH,HARYANA	03/2013	959.25 -	06/2016 -	06/2016	0/0
473	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 07/2016	07/2016	0/0
474	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2016	0/0
475	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016	0/0
476	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	-	07/2016	0/0
477	GUWAHTI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 08/2016	08/2016	0/0
478	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 07/2016	08/2016	0/0
479	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	08/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
480	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	08/2016	0/0
481	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	08/2016	0/0
482	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
483	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
484	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	08/2016	0/0
485	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457]NHAI,MADHYA PRADESH	02/2012	912.00 -	08/2016 -	08/2016	0/0
486	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2016	0/0
487	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	08/2016	0/0
488	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	09/2016	0/0
489	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	09/2016	0/0
490	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2016	0/0
491	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
492	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	09/2016	0/0
493	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	09/2016	0/0
494	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
495	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]NHAI,HARYANA	12/2012	438.75 -	09/2016 -	09/2016	0/0
496	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	09/2016	0/0
497	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2016	0/0
498	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
499	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	10/2016	0/0
500	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
501	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
502	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
503	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
504	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
505	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
506	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	11/2016	0/0
507	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	06/2005 -	12/2016	0/0
508	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	09/2007 -	12/2016	0/0
509	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2016	0/0
510	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
511	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2016	0/0
512	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	12/2016	0/0
513	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2016	0/0
514	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2016	0/0
515	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2016	0/0
516	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
517	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2016	0/0
518	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	04/2014 -	12/2016	0/0
519	4-LANNING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2016	0/0
520	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
521	4-LANNING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	12/2016	0/0
522	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	01/2017	0/0
523	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	01/2017	0/0
524	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	01/2017	0/0
525	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	01/2017	0/0
526	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	02/2017	0/0
527	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	02/2017	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
528	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	02/2017	0/0
529	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	03/2017	0/0
530	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	08/2013 -	03/2017	0/0
531	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	11/2015 -	03/2017	0/0
532	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	03/2017	0/0
533	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD, UTTAR PRADESH	11/2010	305.49 -	03/2017 -	03/2017	0/0
534	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH	10/2013	317.76 -	03/2017 -	03/2017	0/0
535	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	03/2017	0/0
536	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
537	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI, RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
538	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
539	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
540	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	08/2013 -	05/2017	0/0
541	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	06/2015 -	05/2017	0/0
542	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
543	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
544	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
545	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD, ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0
546	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
547	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
548	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH - [N24000340]NHAI, TAMIL NADU	12/2014	451.58 -	06/2017 -	06/2017	0/0
549	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	08/2013 -	07/2017	0/0
550	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
551	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
552	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	07/2017	0/0
553	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
554	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
555	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
556	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
557	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
558	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
559	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	10/2017	0/0
560	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
561	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
562	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
563	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
564	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
565	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0
566	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	12/2017	0/0
567	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
568	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	12/2017	0/0
569	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
570	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
571	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
572	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2017	0/0
573	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
574	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	01/2018	0/0
575	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
576	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
577	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0
578	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
579	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
580	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
581	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
582	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
583	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
584	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
585	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
586	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
587	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,HARYANA	09/2015	788.51 -	03/2018 -	03/2018	0/0
588	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
589	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
590	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
591	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
592	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
593	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
594	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	05/2018	0/0
595	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	11/2015 -	05/2018	0/0
596	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	06/2018	0/0
597	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
598	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
599	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
600	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
601	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHAI, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
602	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
603	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
604	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
605	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
606	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	07/2018	0/0
607	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI, MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
608	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
609	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHAI, ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	01/2019	0/0
610	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
611	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 -	09/2007 -	-	0/0
612	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
613	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	10/2008 -	-	0/0
614	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
615	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
616	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
617	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
618	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, KERALA	03/2005	557.00 -	02/2010 -	-	0/0
619	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	-	0/0
620	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	-	0/0
621	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
622	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	-	0/0
623	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	10/2014 -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
624	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	-	0/0
625	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.51 -	05/2014 -	-	0/0
626	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	01/2013 -	-	0/0
627	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	-	0/0
628	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-	0/0
629	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-	0/0
630	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-	0/0
631	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-	0/0
632	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-	0/0
633	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
634	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
635	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
636	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
637	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
638	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
639	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
640	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
641	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
642	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
643	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	03/2015 -	-	0/0
644	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
645	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
646	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
647	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
648	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
649	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
650	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
651	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
652	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
653	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
654	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000304]PWD,MIZORAM	08/2010	186.96 -	- -	-	0/0
655	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
656	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
657	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
658	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
659	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
660	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
661	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
662	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
663	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
664	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
665	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
666	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
667	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
668	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
669	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	02/2015 -	-	0/0
670	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
671	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
672	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
673	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
674	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
675	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
676	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
677	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	05/2015 -	-	0/0
678	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
679	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
680	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	-	0/0
681	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
682	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM	01/1991	225.02 -	- -	-	0/0
683	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	01/1991	223.30 -	- -	-	0/0
684	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
685	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270 (D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	-	0/0
686	4 LANING OF BIAORA - DEWAS - [N24000434]NHAI,MADHYA PRADESH	06/2015	583.79 -	- -	-	0/0
687	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,WEST BENGAL	10/2015	531.13 -	- -	-	0/0
688	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]DORTH, WEST BENGAL	10/2015	361.15 -	- -	-	0/0
689	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	01/1991	289.99 -	- -	-	0/0
690	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	-	0/0
691	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	-	0/0
692	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	-	0/0
693	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
694	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
695	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
696	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	-	0/0
697	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	-	0/0
698	4 LANING OF GUNA TO BIAORA - [N24000458]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	- -	-	0/0
699	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-	0/0
700	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 - [N24000466]NHAI,TAMIL NADU	01/1991	285.00 -	01/2008 -	-	0/0
701	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
702	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
703	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
704	NAGPUR - KONDHALI - [N24000472]DORTH,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
705	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
706	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,ANDAMAN & NICOBAR ISLANDS	09/2015	273.06 -	- -	-	0/0
707	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-	0/0
708	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]DORTH,BIHAR	08/2015	814.04 -	- -	-	0/0
709	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-	0/0
710	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,WEST BENGAL	12/2015	1,423.96 -	- -	-	0/0
711	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
712	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	01/1991	1,388.00 -	- -	-	0/0
713	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- -	-	0/0
714	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	- -	-	0/0
715	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	- -	-	0/0
716	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
717	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	-	0/0
718	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
719	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	01/1991	1,167.45 -	- -	-	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
720	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	- -	-	0/0
721	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
722	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
723	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
724	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	-	0/0
725	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	-	0/0
726	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
727	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	-	0/0
728	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	-	0/0
729	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
730	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
731	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
732	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
733	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
734	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
735	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
	Total		223,055.64 -			0/0
	<u>SHIPPING AND PORTS</u>					
736	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	01/2016	0/0
737	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 01/2016	03/2016	0/0
738	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	04/2009 03/2010	08/2016	0/0
739	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
740	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
	Total		3,399.46 -			0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>TELECOMMUNICATIONS</u>					
741	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00	07/2015	03/2017	0/0
	Total		13,334.00			0/0
	<u>URBAN DEVELOPMENT</u>					
742	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90	07/2012 12/2015	12/2015	0/0
743	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00	01/2015	12/2015	0/0
744	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30	08/2014	01/2016	0/0
745	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	11/2014	03/2016	0/0
746	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01	12/2014	04/2016	0/0
747	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85	05/2013 10/2015	06/2016	0/0
748	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72	09/2016	09/2016	0/0
749	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00	03/2016	12/2016	0/0
750	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84	03/2017	03/2017	0/0
751	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79	07/2017	06/2017	0/0
752	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21	07/2017	07/2017	0/0
753	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00	03/2018	03/2018	0/0
754	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 26,405.01	02/2019 03/2020	03/2020	0/0
755	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10	09/2014	-	0/0
756	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43	02/2015	-	0/0
757	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33	11/2014	-	0/0
758	CONSTRUCTION OF MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24	08/2007	-	0/0
759	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00	03/2012	-	0/0
760	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASHTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00	06/2015	-	0/0
761	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23	10/2012	-	0/0

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
762	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI (IN ZONE 2 IN - [N28000082]JhNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
763	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD, PUNJAB	02/2014	388.00 -	01/2015 -	-	0/0
764	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	- -	-	0/0
	Total		108,053.82 -			0/0
	Grand Total		614,109.34			0/0

Annexure - XI

List of Projects Ahead of Schedule w.r.t. Latest Schedule

							(January 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	81.23	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	81.23		
	<u>PETROLEUM</u>						
2	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	188.44	09/2017 03/2018	12/2017
	Total		3,076.00 -	3,076.00	188.44		
	<u>COAL</u>						
3	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	3.52	03/2021 -	03/2017
	Total		555.52 -	555.52	3.52		
	<u>POWER</u>						
4	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	71.50	02/2017 -	03/2016
	Total		188.75 -	188.75	71.50		
	<u>PETROLEUM</u>						
5	MARKETING TOP AT KORBA - [N16000186]	1/2011	141.86 -	232.00	164.35	09/2016 -	03/2016
6	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	326.09	01/2017 -	06/2016
	Total		560.90 -	651.04	490.44		
	<u>URBAN DEVELOPMENT</u>						
7	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	2,562.95	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	2,562.95		
	<u>PETROLEUM</u>						

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
8	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197	11/2014	6,068.80 -	6,068.80	648.01	04/2019 -	03/2019
	Total		6,068.80 -	6,068.80	648.01		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
9	FOUR LANING OF SHIVPURI-GUNA SECTION OF NH-3 FROM KM236.00 TO KM 332.100 IN THE STATE OF MADHYA PRAD - [N24000497	3/2015	830.36	830.36	-	01/2019 -	01/2016
	Total		830.36 -	830.36	.00		
	Grand Total		16,721.52	17,038.83	4,046.09		

Annexure - XII

List of Projects on schedule w.r.t. Latest Schedule

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
2	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	224.65	03/2016 -	03/2016
3	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	204.99	03/2017 -	03/2017
5	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	113.00	03/2021 -	03/2021
6	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	148.45	03/2018 -	03/2018
7	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	29.15	03/2021 -	03/2021
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	798.52	03/2023 03/2023	03/2023
9	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	1.37	03/2020 -	03/2020
10	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	46.94	03/2021 -	03/2021
11	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	16.87	03/2020 -	03/2020
12	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
13	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	98.63	03/2021 -	03/2021
14	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	47.76	04/2015 04/2019	04/2019
15	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.49	03/2022 -	03/2022
16	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	-	03/2018 -	03/2018
17	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	141.07	03/2020 -	03/2020
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	620.94	03/2026 -	03/2026
19	KAMPTTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
20	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.43	03/2023 03/2023	03/2023
21	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	0.74	03/2019 -	03/2019

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	76.43	03/2020 -	03/2020
23	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
24	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	51.51	03/2023 -	03/2023
25	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
26	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	108.58	03/2020 -	03/2020
27	GOKUL - [N06000120]	11/2014	267.67 -	267.67	185.72	03/2018 -	03/2018
28	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	1.33	03/2023 -	03/2023
29	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	10.44	03/2019 -	03/2019
30	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	0.05	03/2019 -	03/2019
31	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
32	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	61.37	03/2025 -	03/2025
33	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	199.31	03/2020 -	03/2020
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	1,373.77	12/2015 04/2018	04/2018
35	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	198.59 -	198.59	125.13	03/2016 -	03/2016
36	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
37	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
38	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	809.04	03/2016 -	03/2016
39	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
40	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	72.99	03/2019 -	03/2019
41	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	179.10	03/2021 -	03/2021
42	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	34.09	03/2018 -	03/2018
	Total		40,785.87 -	40,577.07	5,839.12		
	<u>FERTILISERS</u>						
43	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	49.27	11/2016 -	11/2016

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		197.79	209.44	49.27		
			-				
	<u>HEALTH AND FAMILY WELFARE</u>						
44	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005	11/2013	196.70	196.70	157.61	01/2016	01/2016
			-			-	
45	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90	168.90	0.05	05/2017	05/2017
			-			-	
46	AIIMS - OPD(NEW) - [N21000009	8/2014	293.65	293.65	49.24	05/2017	05/2017
			-			-	
47	AIIMS - MOTHER AND CHILD BLOCK - [N21000008	12/2013	204.44	204.44	25.67	05/2017	05/2017
			-			-	
48	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	9/2014	505.58	505.58	9.74	03/2018	03/2018
			-			-	
	Total		1,369.27	1,369.27	242.31		
			-				
	<u>MINES</u>						
49	IMPLEMENTATION OF 50.4 MW WIND POWER PROJECT AT YELLAPUR - [N10000008	12/2015	355.13	355.13	-	11/2016	11/2016
			-			-	
50	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009	12/2015	344.50	344.50	-	11/2016	11/2016
			-			-	
	Total		699.63	699.63	.00		
			-				
	<u>PETROLEUM</u>						
51	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161	3/2013	1,138.50	686.58	563.49	04/2015 05/2016	05/2016
			-				
52	DIESEL HYDROTREATOR - [N16000207	7/2015	1,031.37	1,031.37	12.72	01/2018	01/2018
			-			-	
53	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208	11/2015	500.00	500.00	-	03/2017	03/2017
			-			-	
54	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204	8/2015	2,818.88	2,818.88	-	03/2019	03/2019
			-			-	
55	IOR OF B-173A FIELD - [N16000140	1/2012	352.49	352.49	131.19	03/2014 05/2016	05/2016
			-				
56	CONSTRUCTION OF 6 ETPS - [N16000117	3/2009	317.64	240.95	127.08	09/2012 03/2016	03/2016
			-				
57	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25	160.16	69.23	07/2016	07/2016
			-			-	
58	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	5/2013	4,124.35	4,941.49	549.78	04/2016 12/2017	12/2017
			-				
59	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06	714.25	73.79	10/2017 02/2018	02/2018
			-				

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 05/2017	05/2017
61	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	10,044.66	05/2016 -	05/2016
62	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,323.77	03/2015 05/2016	05/2016
63	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	140.71	12/2016 -	12/2016
64	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	599.26	12/2018 -	12/2018
65	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	832.22	05/2014 03/2017	03/2017
66	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
67	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	111.66	09/2017 -	09/2017
68	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.08	572.18	11/2015 11/2016	11/2016
69	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	995.12	05/2013 04/2016	04/2016
70	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	2,689.65	05/2017 05/2017	05/2017
71	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	1.07	03/2017 -	03/2017
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	736.65	499.19	09/2011 10/2016	10/2016
73	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	-	12/2017 -	12/2017
74	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	58.18	07/2016 -	07/2016
75	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
76	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	264.14	10/2014 03/2017	03/2017
77	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	641.31	05/2017 -	05/2017
78	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	592.92	05/2019 03/2020	03/2020
	Total		58,245.51 -	61,802.97	20,903.92		
	POWER						

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	2/2010	2,144.00 -	2,932.88	2,283.80	12/2012 12/2016	12/2016
80	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017
81	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,018.00	12/2016 -	12/2016
82	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	703.00	03/2018 -	03/2018
83	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	7.40	11/2017 -	11/2017
84	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) - [N18000198]	5/2015	312.94 -	312.94	16.10	05/2016 -	05/2016
85	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	194.60	04/2018 -	04/2018
86	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	49.40	11/2016 -	11/2016
87	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	709.90	05/2016 -	05/2016
88	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	338.80	05/2018 -	05/2018
89	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]	10/2015	315.00 -	315.00	-	10/2016 -	10/2016
90	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	135.50	06/2016 -	06/2016
91	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	-	05/2018 -	05/2018
92	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	16.00	07/2018 -	07/2018
93	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	5,564.00	06/2017 -	06/2017
94	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	609.44	579.80	02/2014 03/2016	03/2016
95	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	5/2015	436.68 -	436.68	436.56	12/2016 -	12/2016
96	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,262.27	1,093.23	08/2013 07/2016	07/2016
97	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	83.30	08/2016 -	08/2016
98	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	301.90	04/2018 -	04/2018

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
99	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47	1,455.47	-	07/2018	07/2018
100	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42	972.42	-	11/2017	11/2017
101	TRIPURA GAS BASED POWER PROJECT - [N18000071]	7/2009	421.01	1,007.57	958.83	07/2013 01/2016	01/2016
102	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49	288.49	67.20	02/2017	02/2017
103	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51	9,870.51	-	09/2019	09/2019
104	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58	14,366.58	2,349.00	02/2019	02/2019
105	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19	244.19	-	07/2018	07/2018
106	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33	780.33	0.90	07/2017	07/2017
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40	197.40	-	03/2018	03/2018
108	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60	12,964.60	4,914.20	01/2018	01/2018
109	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30	1,479.30	78.90	04/2017	04/2017
110	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57	155.57	5.40	03/2016	03/2016
111	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	6,085.84	4,362.53	12/2009 06/2016	06/2016
112	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]	1/2016	305.04	305.04	-	03/2017	03/2017
113	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98	9,188.98	1,000.00	03/2019	03/2019
114	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88	207.88	-	07/2018	07/2018
115	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	1/2015	268.80	268.80	22.60	03/2018	03/2018
116	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55	11,638.55	4,856.00	09/2017	09/2017
117	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84	1,381.84	157.00	09/2019	09/2019
118	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00	2,978.86	1,603.73	02/2016 09/2019	09/2019

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211]	1/2016	187.04 -	187.04	-	06/2018 -	06/2018
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 -	539.82	111.90	06/2016 -	06/2016
121	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRIPUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	3.10	10/2017 -	10/2017
122	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,381.71	951.92	07/2006 10/2016	10/2016
123	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC [N18000167]	6/2014	400.47 -	400.47	45.19	04/2017 -	04/2017
124	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	11,463.30	08/2013 12/2017	12/2017
125	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	120.00	04/2020 -	04/2020
126	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW [N18000203]	2/2015	302.49 302.00	302.49	234.18	02/2016 -	02/2016
127	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	2,500.00	08/2018 -	08/2018
128	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.70	05/2017 -	05/2017
129	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	0.10	09/2017 -	09/2017
130	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	15.60	03/2018 -	03/2018
131	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	113.30	10/2016 -	10/2016
132	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	19.70	07/2016 -	07/2016
133	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	18.38	07/2017 -	07/2017
	Total		155,346.49 -	166,023.61	49,648.95		
	<u>RAILWAYS</u>						
134	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
135	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
137	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	7,986.04	2,443.62	03/2014 03/2019	03/2019
138	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
139	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
140	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	-	03/2017 -	03/2017
	Total		8,820.53 -	17,767.82	2,626.23		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
141	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	-	06/2018 -	06/2018
142	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	370.66	04/2010 09/2016	09/2016
143	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]	2/2015	241.61 -	241.61	23.83	02/2017 -	02/2017
144	FOUR LANING OF VARANASI BYPASS - [N24000356]	5/2015	261.09 -	261.09	-	05/2017 -	05/2017
145	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	208.00	295.20	04/2008 01/2017	01/2017
146	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	-	06/2018 -	06/2018
147	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]	9/2014	425.19 -	425.19	167.91	09/2016 -	09/2016
148	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]	11/2014	563.92 -	563.92	-	11/2016 -	11/2016
149	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]	6/2015	1,012.90 -	1,012.90	-	03/2016 -	03/2016
150	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	-	03/2018 -	03/2018
151	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	-	11/2017 -	11/2017
152	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	-	09/2017 -	09/2017
153	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]	6/2014	301.04 -	301.04	31.28	01/2016 -	01/2016
154	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	-	12/2017 -	12/2017

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	-	02/2018 -	02/2018
156	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	214.17	03/2008 07/2016	07/2016
157	JALANDHAR - AMRITSAR - [N24000351]	1/2014	523.85 -	523.85	54.84	01/2016 -	01/2016
158	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS [N24000357]	9/2015	567.51 -	567.51	42.79	03/2018 -	03/2018
159	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]	10/2014	206.12 -	206.12	102.21	04/2017 -	04/2017
160	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH- - [N24000340]	12/2014	451.58 -	451.58	-	06/2017 -	06/2017
161	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	-	07/2018 -	07/2018
162	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	-	05/2018 -	05/2018
163	4-LANING OF PUNJAB/HARYANA BORDER-JIND - [N24000461]	12/2012	438.75 -	438.75	-	09/2016 -	09/2016
164	FOUR LANING OF CHADIGARH - KHARAR - [N24000503]	10/2015	447.29 -	447.29	-	12/2017 -	12/2017
165	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
166	GUWAHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96 -	175.96	304.17	04/2008 08/2016	08/2016
167	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]	3/2014	240.10 -	240.10	144.69	03/2016 -	03/2016
168	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	-	12/2017 -	12/2017
169	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	-	03/2018 -	03/2018
170	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]	8/2014	187.79 -	187.79	-	07/2016 -	07/2016
171	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]	3/2013	257.80 -	257.80	-	02/2016 -	02/2016
172	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR - [N24000428]	6/2014	569.38 -	569.38	344.00	06/2016 -	06/2016
173	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]	10/2013	677.79 -	677.79	584.72	04/2016 -	04/2016
174	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	830.19	01/2018 -	01/2018
175	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	-	07/2017 -	07/2017
176	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
177	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	-	08/2016 -	08/2016
178	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
179	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]	10/2013	445.89 -	445.89	-	03/2017 -	03/2017
180	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	-	11/2018 -	11/2018
181	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]	10/2013	493.94 -	493.94	-	03/2017 -	03/2017
182	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]	2/2015	377.83 -	377.83	-	07/2017 -	07/2017
183	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	-	03/2017 -	03/2017
184	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	-	05/2017 -	05/2017
185	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]	10/2014	454.89 -	454.89	22.75	05/2018 -	05/2018
186	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]	10/2014	437.39 -	437.39	-	06/2018 -	06/2018
187	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]	1/1991	282.41 -	282.41	-	08/2016 -	08/2016
188	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]	11/2010	305.49 -	305.49	122.11	03/2017 -	03/2017
189	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]	1/1991	208.87 -	208.87	-	05/2016 -	05/2016
190	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]	1/1991	358.22 -	358.22	-	10/2016 -	10/2016
191	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	106.61	02/2018 -	02/2018
192	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	-	03/2018 -	03/2018
193	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]	12/2013	319.80 -	319.80	-	10/2016 -	10/2016
194	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
195	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	3/2015	829.00 -	829.00	-	03/2018 -	03/2018
196	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	49.78	04/2017 -	04/2017
197	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
198	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	-	03/2018 -	03/2018
199	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	19.72	10/2018 -	10/2018
200	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	18.45	03/2018 -	03/2018
201	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255	12/2013	220.72 -	220.72	-	11/2016 -	11/2016
202	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	-	12/2017 -	12/2017
203	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241	12/2013	177.18 -	177.18	-	03/2016 -	03/2016
204	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	-	09/2017 -	09/2017
205	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	-	11/2018 -	11/2018
206	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
207	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242	12/2013	158.65 -	158.65	-	03/2016 -	03/2016
208	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	-	06/2018 -	06/2018
209	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	-	11/2017 -	11/2017
210	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250	6/2014	260.39 -	260.39	-	11/2016 -	11/2016
211	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377	1/2014	397.04 -	397.04	-	10/2016 -	10/2016

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
212	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	-	05/2017 -	05/2017
213	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	15.47	02/2017 -	02/2017
214	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	10/2014	463.49 -	463.49	-	06/2018 -	06/2018
215	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331	1/2014	282.41 -	282.41	31.64	03/2016 -	03/2016
216	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	103.22	05/2017 -	05/2017
217	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403	10/2013	283.45 -	283.45	-	10/2016 -	10/2016
218	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246	10/2014	244.30 -	244.30	-	12/2016 -	12/2016
219	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	-	08/2017 -	08/2017
220	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245	1/2014	270.00 -	270.00	50.85	03/2016 -	03/2016
221	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
222	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	-	06/2018 -	06/2018
223	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	-	01/2019 -	01/2019
224	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	-	10/2017 -	10/2017
225	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYAWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	10.56	11/2017 -	11/2017
226	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336	10/2014	227.74 -	227.74	87.30	10/2016 -	10/2016
227	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	28.86	05/2018 -	05/2018
228	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017

						(January 2016)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
229	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244	1/2014	340.00 -	340.00	-	03/2016 -	03/2016
230	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	-	05/2018 -	05/2018
231	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTON) TO TW - [N24000243	12/2013	244.08 -	244.08	-	03/2016 -	03/2016
232	4 LANING OF OBEDULLAGANJ-BETUL SECTION - [N24000457	2/2012	912.00 -	912.00	-	08/2016 -	08/2016
233	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	-	07/2018 -	07/2018
234	4-LANING OF ROHTAK - HISSAR SECTION - [N24000456	3/2013	959.25 -	959.25	-	06/2016 -	06/2016
235	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426	11/2012	530.07 -	530.07	229.01	08/2016 -	08/2016
236	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,202.43	11/2016 -	11/2016
237	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	-	04/2018 -	04/2018
238	FOUR LANING OF SHIVPURI TO GUNA SECTION OF NH-3 FROM KM 236.00 TO KM 332.100 IN THE STATE OF MADHY - [N24000464	3/2015	830.36 -	830.36	-	01/2016 -	01/2016
239	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	-	03/2018 -	03/2018
240	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
241	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350	6/2015	563.92 -	563.92	-	12/2017 -	12/2017
242	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	-	03/2018 -	03/2018
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369	1/1991	269.26 -	269.26	-	10/2016 -	10/2016
244	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474	2/2015	327.32 -	327.32	-	05/2017 -	05/2017
245	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446	9/2015	788.51 -	788.51	-	03/2018 -	03/2018
246	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	-	02/2018 -	02/2018

							(January 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
247	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	-	10/2017 -	10/2017
248	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	-	06/2018 -	06/2018
249	PADI - DAHOD - [N24000353	11/2014	279.14 -	279.14	52.40	05/2017 -	05/2017
250	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	-	07/2018 -	07/2018
251	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343	9/2015	341.61 -	341.61	69.55	09/2017 -	09/2017
252	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463	12/2015	1,083.00 -	1,083.00	-	06/2018 -	06/2018
253	FOUR LANING OF PARWANOO -SOLAN - [N24000479	9/2015	934.46 -	934.46	-	03/2018 -	03/2018
254	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450	9/2015	785.78 -	785.78	-	03/2018 -	03/2018
255	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347	8/2015	723.54 -	723.54	124.59	02/2018 -	02/2018
256	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER - [N24000237	1/2014	177.32 -	177.32	86.65	01/2016 -	01/2016
257	VADODARA-SURAT SECTION - [N24000361	3/2014	503.16 -	503.16	-	08/2016 -	08/2016
258	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	311.13	06/2008 04/2016	04/2016
259	GUWAHATI TO NALBARI (AS-5) - [N24000046	12/2003	198.16 -	198.16	242.40	04/2008 01/2016	01/2016
260	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	83.61	04/2017 -	04/2017
261	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	13.25	07/2017 -	07/2017
262	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	-	04/2018 -	04/2018
263	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	-	01/2017 -	01/2017
	Total		64,682.17 -	65,001.71	6,593.00		
	SHIPPING AND PORTS						
264	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	9.14	04/2017 -	04/2017
265	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	0.28	12/2017 -	12/2017
266	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018

							(January 2016)
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
267	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]	10/2013	198.94 -	198.94	54.49	06/2017 -	06/2017
	Total		928.29 -	942.12	63.91		
	<u>STEEL</u>						
268	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	2.61	09/2017 -	09/2017
269	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]	12/2007	253.92 254.00	254.00	193.97	06/2016 -	06/2016
270	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	195.51	12/2016 -	12/2016
271	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]	5/2015	189.00 -	189.00	-	03/2017 -	03/2017
272	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	22.05	03/2018 -	03/2018
273	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	26.55	09/2016 -	09/2016
274	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	98.57	05/2016 -	05/2016
275	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]	5/2015	1,154.18 -	1,154.18	28.20	12/2017 -	12/2017
276	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]	3/2015	1,034.01 -	1,034.01	-	10/2017 -	10/2017
277	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	8,493.78	05/2015 12/2016	12/2016
278	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	297.93	04/2018 -	04/2018
279	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	88.91	04/2018 -	04/2018
280	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]	12/2007	200.00 -	200.00	126.15	03/2018 -	03/2018
	Total		27,385.88 -	27,410.35	9,574.23		
	<u>URBAN DEVELOPMENT</u>						
281	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.01	217.54	02/2019 03/2020	03/2020
282	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	4/2014	332.72 -	332.72	78.89	09/2016 -	09/2016
283	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	30.67	03/2017 -	03/2017

(January 2016)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
284	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	1,055.27	11/2019 -	11/2019
285	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
286	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	74.92	03/2018 -	03/2018
287	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]	1/2009	225.81 -	225.81	138.38	06/2012 03/2016	03/2016
	Total		41,284.72 -	41,284.59	1,595.67		
	Grand Total		399,746.15	423,088.58	97,136.61		

Annexure - XIII**List of ongoing projects having cost overrun w.r.t. to revised schedule**

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	09/2016	62.57
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	05/2016	70.54
	Total		16,663.00 -	28,139.00			
	<u>CIVIL AVIATION</u>						
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		217.60 -	244.10			
	<u>COAL</u>						
4	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
5	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2017	0.02
	Total		898.50 -	969.25			
	<u>HEAVY INDUSTRY</u>						
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
7	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,965.00	04/2012 -	12/2015	82.49
	Total		5,460.61 -	9,965.00			
	<u>PETROLEUM</u>						
8	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86 -	232.00	09/2016 -	03/2016	63.54
10	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	08/2016	37.72
12	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	10/2016	19.35
	Total		15,900.77 -	18,756.55			
	<u>POWER</u>						
13	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.76	09/2009 -	12/2018	114.28
14	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	18,063.89	09/2010 -	-	187.40
15	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243	09/2005	1,061.38 -	2,193.08	09/2009 -	09/2016	106.63
16	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203	02/2015	302.49 302.00	302.49	02/2016 -	02/2016	0.00
17	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,237.67	12/2011 -	03/2016	83.21
18	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202	04/2007	4,122.00 8,781.00	9,606.82	02/2011 -	01/2017	133.06
19	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,751.47	01/2016 -	11/2016	57.92
	Total		21,645.83 -	48,554.18			
	<u>RAILWAYS</u>						
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
21	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
22	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
23	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
24	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
26	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
27	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69	3,404.92	12/2006	-	224.37
28	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63	270.00	02/2011	-	191.48
29	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90	2,371.85	03/2005 12/2008	12/2019	2,019.62
30	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56	740.00	03/2012	12/2012	210.19
31	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64	1,185.64	09/2009	-	293.06
32	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	-	03/2017	160.32
33	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19	343.00	-	-	57.20
34	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79	1,101.16	-	03/2017	186.92
35	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23	1,202.70	02/2015	-	556.39
36	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13	225.00	-	10/2014	76.98
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	318.33	03/2009 03/2009	10/2016	138.61
38	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78	810.80	-	-	0.00
39	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62	360.00	12/2007 03/2010	-	163.50
40	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70	360.00	02/2006	-	37.56
41	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20	950.00	03/2010	06/2017	38.24
42	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19	1,383.45	-	-	242.28
43	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17	914.98	-	03/2016	166.63
44	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00	490.00	-	-	292.00
45	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00	1,080.00	-	-	136.84
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10	275.08	03/2012	03/2016	60.77
47	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34	2,820.25	04/2014	03/2018	355.36
48	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012	-	43.54
49	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66	548.01	03/2010	-	252.06

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
50	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	791.59	- -	-	109.11
51	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
52	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
53	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
54	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
55	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
56	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
57	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
58	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
59	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
60	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
61	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
62	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
63	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
64	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
65	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
66	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
67	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
68	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
69	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
70	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
71	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
72	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
73	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
75	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
76	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
77	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,820.00	-	-	447.91
78	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
81	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	-	-	232.17
82	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
83	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	-	-	324.33
84	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
85	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
86	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
87	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
88	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	496.24	-	03/2017	148.12
89	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	827.73	-	03/2019	175.91
90	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
91	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
92	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
93	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
94	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	-	03/2018	99.75
95	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
96	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2018	143.60
97	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
98	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
99	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
100	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
101	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	325.50	02/2009 02/2009	04/2016	95.90
102	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	12/2017	18.66
103	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
104	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
105	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
106	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
107	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
108	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
109	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
110	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
111	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26 -	1,072.51	- -	-	28.25
112	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
113	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
114	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
115	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
116	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
117	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
118	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
120	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	-	42.11
121	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
122	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
123	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
124	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
125	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
126	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
127	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
128	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
129	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
130	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
131	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
132	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
133	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
134	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
135	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
136	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
137	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
138	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
139	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
140	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
141	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
143	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
144	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
145	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
146	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
147	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
148	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
149	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
150	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
151	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
152	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007	03/2016	38.80
153	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
154	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	03/2020	5.00
155	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
156	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
157	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
158	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
159	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
160	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
161	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
164	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,653.55	-	03/2018	216.06
166	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	312.12 -	453.10	-	03/2018	45.17
167	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	-	03/2019	47.95
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
169	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	800.00	-	-	33.02
	Total		76,270.05 -	190,591.39			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
170	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	03/2016	28.93
171	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2016	92.75
172	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	03/2016	80.68
173	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	03/2016	68.99
174	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2016	106.50
175	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2016	30.10
176	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
177	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
178	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
179	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	36.24
180	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	31.78
181	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	0.00
182	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		3,710.66 -	5,884.15			

(January 2016)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
183	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	03/2016	300.00
184	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
185	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	409.83	04/2009 -	08/2016	66.82
186	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	01/2016	82.72
	Total		1,006.56 -	1,937.62			
	<u>STEEL</u>						
187	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	06/2017	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
188	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	13,845.01	06/2011 -	06/2016	116.50
	Total		6,395.00 -	13,845.01			
	Grand Total		150,229.58	323,201.95			

Annexure- XIV

List of Delayed Projects w.r.t. Latest Schedule

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,077.00	12/2008 10/2013	05/2016	89	31
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 -	5,677.00	5,150.14	09/2010 -	09/2016	72	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	7,715.00	12/2015 10/2016	11/2018	35	25
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	5,513.00	12/2016 03/2017	12/2019	36	33
	Total		40,442.00 -	51,918.00	39,455.14				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	412.95	01/2011 06/2016	09/2017	80	15
	Total		309.46 -	309.46	412.95				
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,990.05	03/2014 -	03/2016	24	-
7	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,713.30	03/2014 -	03/2016	24	-
8	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 741.62	741.62	503.51	03/2013 -	03/2016	36	-
9	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	866.79	03/2013 09/2012	03/2016	36	42
10	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	81.11	03/2015 -	03/2016	12	-
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	67.47	03/2012 -	03/2016	48	-
12	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	36.08	03/2011 -	03/2016	60	-
13	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	146.05	03/2012 -	03/2016	48	-
14	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.06	04/2014 -	03/2016	23	-
15	WIND POWER PROJECT, KAZHUNEERKULAM, TAMIL NADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	191.25	10/2014 -	03/2016	17	-
16	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	70.92	03/2014 -	09/2016	30	-
17	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	99.75	05/2014 -	10/2016	29	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	68.57	04/2014 -	11/2016	31	-
19	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL,ODISHA	01/2005	302.96 -	302.96	302.68	03/2010 -	03/2017	84	-
20	ASHOK EXPN OCP CCL (10 MTY) - [N060100096]CCL,JHARKHAND	12/2007	341.63 -	341.63	126.41	03/2011 -	03/2017	72	-
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.18	226.26	03/2011 -	03/2017	72	-
22	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	209.57	03/2013 -	03/2017	48	-
23	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	151.26	03/2010 -	03/2017	84	-
24	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	120.89	12/2012 -	03/2017	51	-
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	207.70	03/2012 -	03/2017	60	-
26	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	185.34	03/2013 -	03/2017	48	-
27	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	92.95	03/2012 -	03/2017	60	-
28	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	150.78	03/2013 -	03/2017	48	-
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	70.20	03/2014 -	03/2017	36	-
30	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21	-
31	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	15.14	07/2016 -	03/2017	8	-
32	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	78.69	03/2012 -	03/2018	72	-
33	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	211.06	03/2014 -	03/2018	48	-
34	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	8.03	03/2015 -	03/2018	36	-
35	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	77.44	03/2015 -	03/2018	36	-
37	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	96.39	03/2016 -	03/2018	24	-
38	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 486.27	486.27	93.51	03/2016 -	03/2018	24	-
39	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	202.22	03/2018 -	06/2018	3	-
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 -	1,458.17	14.59	06/2015 -	08/2019	50	-
41	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48	-
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	24.72	03/2015 -	03/2020	60	-
43	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	0.30	03/2014 -	03/2020	72	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40	706.40	78.06	07/2012	03/2021	104	-
45	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72	-
46	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97	489.62	453.18	03/2012	03/2023	132	-
	Total		18,820.84	19,915.20	9,181.25				
	MINES								
47	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]HCL, MADHYA PRADESH	09/2011	1,856.00	1,176.00	4.59	09/2017	04/2020	31	-
	Total		1,856.00	1,176.00	4.59				
	STEEL								
48	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65	332.65	229.64	08/2014 11/2015	01/2016	17	2
49	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33	187.33	173.07	10/2013 12/2015	03/2016	29	3
50	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA	05/2005	768.88 1,060.00	1,060.00	1,070.97	02/2014	03/2016	25	-
51	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA	07/2011	324.87 325.00	325.00	263.57	12/2015	03/2016	3	-
52	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00	17,265.00	15,516.00	03/2013 03/2016	06/2016	39	3
53	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL, ODISHA	06/2014	708.91	708.91	295.30	04/2016	08/2016	4	-
54	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73	877.73	399.56	07/2015	08/2016	13	-
55	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93	188.93	60.23	04/2015	12/2016	20	-
56	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL, ANDHRA PRADESH	07/2011	974.76	974.76	220.37	07/2016	12/2016	5	-
57	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	173.00	175.94	12/2015	03/2017	15	-
58	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00	956.00	648.16	03/2015	03/2017	24	-
59	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29	787.29	241.53	12/2016	03/2017	3	-
60	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16	404.16	265.95	07/2015	06/2017	23	-
61	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00	488.40	38.17	10/2016	06/2017	8	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCCL,TRIPURA	10/2011	175.49 207.00	207.00	131.77	12/2016 -	07/2017	7	-
63	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCCL,MEGHALAYA	04/2014	151.33 -	151.33	4.84	09/2017 -	11/2017	2	-
	Total		24,596.06 -	25,087.49	19,735.07				
	<u>PETROLEUM</u>								
64	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,792.85	01/2014 12/2015	01/2016	24	1
65	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	251.66	-	06/2012 -	01/2016	43	-
66	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	31,052.90	11/2012 11/2013	02/2016	39	27
67	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	186.98	12/2014 -	02/2016	14	-
68	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,399.90	08/2015 -	03/2016	7	-
69	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	321.64	06/2011 03/2012	03/2016	57	48
70	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	419.10	08/2015 -	03/2016	7	-
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	1,074.73	10/2011 -	03/2016	53	-
72	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,294.55	09/2012 -	05/2016	44	-
73	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.14	12/2014 05/2015	05/2016	17	12
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,447.43	01/2012 -	05/2016	52	-
75	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	38.16	02/2016 02/2016	05/2016	3	3
76	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	141.59	02/2016 -	07/2016	5	-
77	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	537.65	03/2015 11/2015	08/2016	17	9
78	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	370.00	0.37	03/2013 -	10/2016	43	-
79	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	1,395.63	11/2015 07/2016	11/2016	12	4
80	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	480.22	08/2015 -	12/2016	16	-
81	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	725.00	130.00	11/2016 -	12/2016	1	-

(January 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
82	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,795.13	03/2013 03/2016	03/2017	48	12
83	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	34.80	11/2016 -	04/2017	5	-
84	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	3,957.00 3,561.00	3,561.00	26.81	01/2013 -	12/2018	71	-
85	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE	01/2015	690.00 -	690.00	-	07/2018 -	12/2018	5	-
	Total		53,540.22 -	59,401.27	43,945.58				
	POWER								
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	362.37	02/2012 -	02/2016	48	-
87	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	766.14	11/2012 -	02/2016	39	-
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,447.42	04/2013 -	02/2016	34	-
89	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	187.20	01/2013 -	02/2016	37	-
90	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL, MULTI STATE	12/2009	1,216.83 -	1,216.83	1,062.99	08/2012 -	03/2016	43	-
91	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,578.86	11/2013 -	03/2016	28	-
92	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	529.11	11/2013 -	03/2016	28	-
93	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL, MULTI STATE	12/2011	2,422.66 -	2,422.66	2,372.26	08/2014 -	03/2016	19	-
94	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL, MULTI STATE	02/2012	1,927.16 -	1,927.16	1,585.67	10/2014 -	03/2016	17	-
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	323.52	05/2015 -	03/2016	10	-
96	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	3,178.09	01/2013 -	03/2016	38	-
97	BOKARO THERMAL POWER STATION-A - [N18000199]DVC, JHARKHAND	08/2006	2,313.00 4,139.00	4,237.67	3,088.00	12/2011 -	03/2016	51	-
98	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL, KARNATAKA	02/2014	167.40 -	167.40	88.20	12/2015 -	05/2016	5	-

(January 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	528.56	11/2011 -	06/2016	55	-
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	548.12	07/2013 11/2015	06/2016	35	7
101	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,798.15	05/2014 -	06/2016	25	-
102	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,938.06	09/2014 -	06/2016	21	-
103	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,319.63	07/2014 -	06/2016	23	-
104	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	303.37	08/2014 06/2015	06/2016	22	12
105	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,475.53	08/2014 12/2015	06/2016	22	6
106	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,391.42	01/2015 -	06/2016	17	-
107	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	94.63	09/2014 -	06/2016	21	-
108	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	5,724.59	06/2015 -	06/2016	12	-
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	587.42	11/2014 -	06/2016	19	-
110	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,996.11	10/2014 -	06/2016	20	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	459.89	03/2016 -	06/2016	3	-
112	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	434.44	04/2016 -	06/2016	2	-
113	EASTERN REGION STRENGTHENING SCHEME-IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	21.50	02/2016 -	06/2016	4	-
114	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	335.10	06/2015 -	08/2016	14	-
115	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,016.53	06/2015 -	08/2016	14	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38	2,193.08	1,956.52	09/2009	09/2016	84	-
117	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC, JAMMU AND KASHMIR	01/2009	3,642.04	5,751.47	4,402.95	01/2016	11/2016	10	-
118	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63	374.63	16.20	04/2016	11/2016	7	-
119	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU	05/2005	1,779.29	2,187.32	1,903.55	11/2008	12/2016	97	11
120	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69	738.48	579.39	09/2010	12/2016	75	11
121	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, MULTI STATE	10/2008	4,824.12	4,824.12	4,237.58	10/2012	12/2016	50	-
122	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47	7,921.47	4,904.00	09/2016	12/2016	3	-
123	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART-B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88	2,514.88	1,043.56	12/2015	12/2016	12	-
124	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00	9,606.82	1,353.36	02/2011	01/2017	71	-
125	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35	6,749.18	5,719.00	09/2011	03/2017	66	-
126	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	2,405.85	01/2015	03/2017	26	-
127	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80	1,272.80	1,244.23	11/2012	03/2017	52	-
128	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19	15,166.19	10,171.00	01/2017	03/2017	2	-
129	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18	9,395.18	5,881.00	11/2016	08/2017	9	-
130	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00	5,353.00	5,298.06	05/2014	09/2017	40	-
131	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89	9,750.89	4,529.23	12/2016	09/2017	9	-
132	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL, UTTAR PRADESH	05/2011	195.42	195.42	51.09	02/2014	02/2018	48	-
133	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97	15,095.67	11,183.00	01/2011	05/2018	88	43
134	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC, HIMACHAL PRADESH	09/2002	3,919.59	8,398.76	5,398.46	09/2009	12/2018	111	-
135	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48	3,846.30	2,699.00	03/2013	12/2018	69	-
136	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL, UTTARAKHAND	08/2008	2,491.58	2,491.58	789.89	06/2013	12/2019	78	-
	Total		141,833.18	167,744.05	114,309.80				
	HEAVY INDUSTRY								

(January 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N2000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	.00				
	HEALTH AND FAMILY WELFARE								
138	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	444.70	268.07	12/2015 -	03/2016	3	-
139	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	159.50	118.95	11/2013 -	03/2016	28	-
140	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	175.57	106.20	12/2014 -	03/2016	15	-
	Total		779.77 -	779.77	493.22				
	RAILWAYS								
141	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	440.08	03/2004 -	03/2016	144	-
142	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 3,040.00	3,040.00	1,834.31	03/2009 -	03/2016	84	-
143	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	48	27
144	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
145	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,769.59	03/2009 -	03/2016	84	-
146	DANGOPOSI-RAJAKHARWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
147	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	1,242.25	1,047.10	03/2007 -	03/2016	108	-
148	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	325.50	349.36	02/2009 02/2009	04/2016	86	86
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	204.56	03/2016 -	06/2016	3	-
150	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	318.33	322.75	03/2009 03/2009	10/2016	91	91
151	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
152	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.93	04/2016 -	03/2017	11	-
153	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19	4,996.19	4,102.70	04/2008 12/2011	06/2017	110	66
154	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	896.75	03/2010 -	06/2017	87	-
155	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	20,000.00	10,722.72	11/2002 -	12/2017	181	-

(January 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
156	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	351.79	03/2010 -	12/2017	93	-
157	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	135.06	03/2016 -	12/2017	21	-
158	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
159	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
160	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
161	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
162	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,911.65	03/2016 -	06/2018	27	-
163	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,095.20	619.56	03/2016 -	12/2018	33	-
164	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
165	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,544.40	-	03/1998 -	12/2019	261	-
166	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
167	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101
168	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
169	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	878.29	03/2016 -	12/2020	57	-
	Total		31,160.20 -	80,078.86	36,517.77				
	ROAD TRANSPORT AND HIGHWAYS								
170	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	-	12/2013 -	01/2016	25	-
171	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	-	03/2013 -	01/2016	34	-
172	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]DORTH,RAJASTHAN	02/2008	1,673.70 -	1,673.70	-	10/2011 -	01/2016	51	-
173	FOUR LANING OF GWALIOR-SHIPURI - [N24000494]DORTH,MADHYA PRADESH	05/2013	1,055.00 -	1,055.00	-	11/2015 -	01/2016	2	-
174	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	-	06/2008 -	02/2016	92	-
175	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	-	05/2010 -	02/2016	69	-

(January 2016)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10	1,509.10	-	09/2012	02/2016	41	-
177	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06	792.06	1,983.00	12/2012	02/2016	38	-
178	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51	333.51	271.60	09/2014	02/2016	17	-
179	4 LANNING OF GOMTI CHAURAH - UDAIPUR - [N24000455]DORTH, RAJASTHAN	03/2012	914.50	914.50	1,097.62	10/2015	02/2016	4	-
180	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00	201.66	240.22	09/2008	03/2016	90	-
181	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00	361.00	392.60	02/2009	03/2016	85	-
182	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81	385.13	-	04/2009	03/2016	83	-
183	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64	167.64	-	11/2008	03/2016	88	-
184	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04	280.13	-	11/2008	03/2016	88	-
185	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00	200.00	-	04/2009	03/2016	83	-
186	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00	195.00	278.96	06/2008	03/2016	93	-
187	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80	237.80	374.10	06/2008	03/2016	93	-
188	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94	332.94	-	09/2008	03/2016	90	-
189	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00	250.39	273.26	10/2008	03/2016	89	-
190	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00	331.23	300.46	07/2009	03/2016	80	-
191	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16	348.16	322.70	09/2007	03/2016	102	-
192	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00	795.00	1,607.78	05/2012	03/2016	46	-
193	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00	1,175.00	-	04/2013	03/2016	35	-
194	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00	1,267.00	2,425.00	06/2013	03/2016	33	-
195	4 LANNING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76	2,498.76	-	08/2014	03/2016	19	-
196	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54	351.54	329.40	05/2013	03/2016	34	-
197	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00	650.00	830.97	11/2013	03/2016	28	-
198	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00	571.00	-	10/2013	03/2016	29	-
199	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00	664.00	609.00	02/2014	03/2016	25	-
200	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00	574.00	760.20	03/2014	03/2016	24	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
201	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	348.00	04/2014 -	03/2016	23	-
202	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	544.08	11/2013 -	03/2016	28	-
203	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	-	02/2014 -	03/2016	25	-
204	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	1,684.00	01/2014 -	03/2016	26	-
205	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	-	08/2013 -	03/2016	31	-
206	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	03/2016	37	-
207	BEAWAR PALI PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.51 -	2,388.00	2,301.00	06/2014 -	03/2016	21	-
208	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	-	06/2014 -	03/2016	21	-
209	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	484.19	455.26	10/2014 -	03/2016	17	-
210	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	942.69	229.16	06/2014 -	03/2016	21	-
211	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI, MULTI STATE	02/2013	1,232.00 -	1,232.00	927.19	08/2015 -	03/2016	7	-
212	KOTWA TO DEWAPUR (LMNHP-10) - [N24000346]NHAI, BIHAR	11/2005	240.00 -	240.00	295.38	11/2008 -	03/2016	88	-
213	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATISGARH	02/2013	1,232.00 -	1,232.00	-	08/2015 -	03/2016	7	-
214	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH, UTTAR PRADESH	05/2013	164.54 -	164.54	-	08/2015 -	03/2016	7	-
215	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	232.45	284.69	09/2010 -	04/2016	67	-
216	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,409.36	07/2012 -	04/2016	45	-
217	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,004.62	07/2013 -	04/2016	33	-
218	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,911.64	08/2013 -	04/2016	32	-
219	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	1,928.22	822.96	04/2015 -	04/2016	12	-
220	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	381.86 -	381.86	-	04/2015 -	04/2016	12	-
221	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
222	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,287.44	09/2014 -	05/2016	20	-
223	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR - [N24000238]NHAI, RAJASTHAN	01/2014	158.04 -	158.04	85.68	12/2015 -	05/2016	5	-
224	REHABILITATION AND UPGRADEATION OF NH-167 FROM KM 70 - [N24000416]PWD, ANDHRA PRADESH	02/2015	224.83 -	224.83	13.17	04/2015 -	05/2016	13	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
225	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	-	10/2011 -	06/2016	56	-
226	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,619.94	11/2011 -	06/2016	55	-
227	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	863.58	03/2013 -	06/2016	39	-
228	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
229	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2016	35	-
230	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	-	06/2013 -	06/2016	36	-
231	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	-	06/2013 -	06/2016	36	-
232	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	-	07/2013 -	06/2016	35	-
233	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	06/2016	29	-
234	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,478.63	05/2014 -	06/2016	25	-
235	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2016	24	-
236	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	893.90	03/2013 -	06/2016	39	-
237	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,840.00	09/2015 -	06/2016	9	-
238	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	-	12/2015 -	06/2016	6	-
239	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	-	09/2014 -	06/2016	21	-
240	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	184.28	01/2016 -	06/2016	5	-
241	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION) - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	417.61	112.85	06/2014 -	06/2016	24	-
242	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	277.06	10/2013 -	07/2016	33	-
243	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	258.99	64.65	07/2014 -	07/2016	24	-
244	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.40	05/2008 07/2016	08/2016	99	1
245	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	1,050.90	05/2013 -	08/2016	39	-
246	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	-	08/2013 -	08/2016	36	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
247	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,267.57	02/2014 -	08/2016	30	-
248	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	871.15	-	09/2015 -	08/2016	11	-
249	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	1,170.52	1,579.15	06/2012 -	08/2016	50	-
250	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	-	05/2013 -	09/2016	40	-
251	2-LANING WITH PS RAIBARELI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	211.68	01/2014 -	09/2016	32	-
252	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	132.64	01/2016 -	09/2016	8	-
253	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	320.48	-	08/2015 -	09/2016	13	-
254	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	-	09/2014 -	10/2016	25	-
255	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	159.73	01/2016 -	10/2016	9	-
256	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	24	-
257	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	170.21	-	11/2014 -	11/2016	24	-
258	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	202.97	06/2005 -	12/2016	138	-
259	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	102.85	09/2007 -	12/2016	111	-
260	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	30.63	11/2012 -	12/2016	49	-
261	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	-	09/2013 -	12/2016	39	-
262	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,742.94	03/2013 -	12/2016	45	-
263	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	879.98	02/2013 -	12/2016	46	-
264	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	-	12/2013 -	12/2016	36	-
265	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	-	05/2013 -	12/2016	43	-
266	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	604.50	07/2013 -	12/2016	41	-
267	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	-	01/2014 -	12/2016	35	-

(January 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
268	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	425.65	09/2013 -	12/2016	39	-
269	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	343.75	04/2014 -	12/2016	32	-
270	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	-	10/2015 -	12/2016	14	-
271	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	333.21	14.12	12/2015 -	12/2016	12	-
272	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	12	-
273	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	-	11/2016 -	12/2016	1	-
274	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	391.77	07/2014 -	02/2017	31	-
275	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	-	02/2015 -	02/2017	24	-
276	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	-	08/2012 -	03/2017	55	-
277	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	-	08/2013 -	03/2017	43	-
278	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	-	11/2015 -	03/2017	16	-
279	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	504.51	03/2014 -	04/2017	37	-
280	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	149.27	02/2010 -	05/2017	87	-
281	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	221.98	08/2013 -	05/2017	45	-
282	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	461.94	06/2015 -	05/2017	23	-
283	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
284	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	-	08/2013 -	07/2017	47	-
285	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	-	09/2015 -	08/2017	23	-
286	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	50.37	09/2016 -	09/2017	12	-
287	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-

(January 2016)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
288	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	2.43	11/2015 -	11/2017	24	-
289	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	2.43	11/2015 -	11/2017	24	-
290	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	344.00	07/2014 -	12/2017	41	-
291	BARSAAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
292	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	191.08	42.58	08/2015 -	03/2018	31	-
293	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - 2 - [N24000492]NHAI,MADHYA PRADESH	11/2015	867.66 -	867.66	18.68	11/2015 -	05/2018	30	-
294	4 LANING OF AMBALA - KAITHAL - PACKAGE - 1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	-	06/2016 -	06/2018	24	-
295	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE - I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	611.65	-	06/2016 -	06/2018	24	-
	Total		92,094.39 -	93,828.37	49,149.58				
	<u>SHIPPING AND PORTS</u>								
296	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	415.80	12/2010 -	01/2016	61	-
297	ENMORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 01/2016	03/2016	120	2
298	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 373.22	409.83	366.20	04/2009 03/2010	08/2016	88	77
	Total		762.06 -	1,679.29	921.80				
	<u>TELECOMMUNICATIONS</u>								
299	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	13,334.00	1,360.00	07/2015 -	03/2017	20	-
300	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	2,011.17	1,360.00	09/2014 -	03/2017	30	-
	Total		15,445.17 -	15,345.17	2,720.00				
	<u>URBAN DEVELOPMENT</u>								

(January 2016)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
301	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD, DELHI	07/2012	884.30 -	884.30	-	08/2014 -	01/2016	17	-
302	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 -	270.83	57.69	11/2014 -	03/2016	16	-
303	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD, DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	-
304	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 11,609.00	13,845.01	13,525.81	06/2011 12/2015	06/2016	60	6
305	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD, DELHI	05/2009	261.85 -	261.85	168.00	05/2013 10/2015	06/2016	37	8
306	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL, TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	11,786.98	12/2015 -	08/2016	8	-
307	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	38,585.00	20,172.80	03/2016 -	12/2016	9	-
308	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
309	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	24.34	09/2015 07/2016	04/2017	19	9
310	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	12.23	03/2016 -	05/2017	14	-
	Total		61,919.29 -	69,369.30	45,753.64				
	Grand Total		485,276.64	590,459.53	362,600.39				

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2019	12320	36
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2018	11459	35
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	13171	89
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492	72

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2017	309.46	80

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
7	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
8	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
9	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
10	RCE OF INDARAM OCP (1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
11	BAROUD OC EXPANSION (RCE) - 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
12	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
13	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
14	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
15	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
16	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
17	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
18	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2016	209.78	12
19	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
22	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
23	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	03/2016	364.75	17
24	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	36
25	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2016	289.45	29
26	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	11/2016	269.82	31
27	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
28	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
29	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
30	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
31	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	341.63	72
32	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
33	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
34	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
35	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
36	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
37	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
38	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
39	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
40	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
41	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
42	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
43	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	09/2016	153.82	30
45	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
46	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
47	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
48	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	LGBRIMH-TEZPUR, ASSAM	HSCC	07/2012	12/2014	03/2016	175.57	15
50	AIIMS-RAEBARELI-HOUSING	HSCC	10/2013	11/2013	03/2016	159.5	28

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
51	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
52	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	HCL	09/2011	09/2017	04/2020	1856	31

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
53	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	10/2016	310	43
54	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	17
55	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	29
56	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	02/2016	279	14
57	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732	53
58	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	03/2016	586	7
59	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	11/2016	3110.36	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	03/2016	317.64	42
61	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71
62	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	35
63	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	05/2016	1793	44
64	DE-BOTTLENECKING OF SMPL	IOCL	12/2009	08/2015	03/2016	1584	7
65	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	02/2016	29777	39
66	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
67	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	14
68	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	03/2017	2592.17	34
69	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2017	2465.15	48
70	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	05/2016	1138.5	13
71	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	10/2016	736.65	61
72	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	01/2016	2523	24
73	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	01/2016	270	43
74	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993	52
75	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
76	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
77	DAMAN DEVELOPMENT PROJECT	ONGC	08/2014	05/2019	03/2020	6086.08	10
78	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
79	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
80	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
81	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	12/2016	913	16

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
82	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	08/2016	1909.24	14
83	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2016	514.2	14
84	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	12/2016	2514.88	12
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2016	723.63	19
86	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	06/2016	1961.87	25
87	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
88	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
89	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
90	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	03/2016	2422.66	19
91	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	03/2016	558.26	28
92	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
93	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	97
94	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
95	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	06/2016	1422.85	17
96	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
97	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	01/2016	421.01	30
98	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	03/2016	1927.16	17
99	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
100	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2016	9569.76	12
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	06/2016	752.64	35
102	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	02/2016	250.03	37
103	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	03/2017	1272.8	52
104	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
105	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
106	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
107	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
108	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313	51
109	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122	71
110	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
111	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	84
112	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	75
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	02/2016	410.29	48
114	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2016	4824.12	50
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	02/2016	1677.57	34
116	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	02/2016	965.58	39
117	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	03/2016	1585.12	28
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	06/2016	509.66	55
119	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	03/2017	4404.57	26
120	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
121	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
122	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144	48
123	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	11/2016	374.63	7
124	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.9	78
125	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER (MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
126	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43
127	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	06/2016	2127.51	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
128	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	35
129	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	03/2016	552.44	25
130	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	06/2016	297.33	22
131	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	22
132	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	06/2016	3201.44	20
133	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII	PGCIL	09/2012	05/2015	03/2016	524.4	10

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
135	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
136	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	M RTP	04/2012	03/2016	12/2017	632.68	21
137	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
138	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
139	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	06/2018	4874.58	27
140	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
141	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
142	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	ECR	04/2002	03/2009	03/2016	921	84
143	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	91
144	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87
145	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
146	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
148	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
149	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110
151	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733	111
152	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
153	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
154	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
155	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
156	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
157	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
158	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2017	2500	181
159	RAJATGARH-BARANG (LD), ECOR	RVNL	04/1999	02/2009	04/2016	166.16	86
160	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
162	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
163	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
164	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA)	PWD	12/2011	08/2015	03/2018	191.08	31
165	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	MORTH	05/2013	08/2015	03/2016	164.54	7
166	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	08/2016	1170.52	50
167	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	NHAI	11/2015	11/2015	05/2018	867.66	30
168	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	03/2016	1232	7
169	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	DORTH	02/2008	10/2011	01/2016	1673.7	51
170	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
171	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
172	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	12/2016	671.3	46
173	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	03/2016	351.54	34
174	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	06/2016	1008.5	36
175	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2016	650	28
176	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	04/2016	1141	32
177	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	01/2016	535	25
178	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
179	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	06/2016	600	36
180	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
181	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
182	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
183	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	06/2016	1813.76	35
184	4-LANING OF BRAHAMPURE-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
185	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
186	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
187	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2016	1396.18	20
188	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2016	291.36	32
189	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
190	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
191	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	12/2017	356.4	41
192	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2016	953.88	35
193	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2016	374	43

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	03/2017	485	43
195	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	03/2016	571	29
196	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	01/2016	805.39	34
197	BIJNI TO ASSAM /WB.BORDER (NH- 31.C) (NHAI)	NHAI	12/2003	06/2008	03/2016	237.8	93
198	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2016	536	29
199	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
200	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2016	1535	25
201	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	03/2016	664	25
202	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	03/2016	574	24
203	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2016	375.09	23
204	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2016	575	41
205	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	03/2016	511.54	28
206	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	06/2016	1100.7	24
207	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	03/2016	398	25
208	GUJARAT/MAHARASHTRA BORDERSURAT- HAZIRA PORT SECTION	NHAI	03/2010	09/2012	02/2016	1509.1	41
209	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	03/2016	1175	35
210	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP- PHASE-III)	NHAI	03/2005	07/2012	04/2016	940	45
211	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	02/2016	792.06	38
212	CHENNAI-TADA (SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
213	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	03/2016	835	26
214	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
215	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	03/2016	500.29	31
216	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	10/2016	1410	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
217	JAIPUR-REENGUS	NHAI	08/2010	02/2013	03/2016	267.81	37
218	BEAWAR PALI PINDWARA	NHAI	12/2011	06/2014	03/2016	2388.51	21
219	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
220	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	06/2016	754	39
221	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	01/2017	208	105
222	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2016	225	94
223	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	NHAI	12/2003	06/2008	03/2016	195	93
224	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	03/2016	155	90
225	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	03/2016	275	89
226	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
227	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	06/2016	852	39
228	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	08/2016	1585	39
229	4-LANING OF ROHATAK JIND (LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2016	283.25	14
230	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2016	230	138
231	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	03/2016	280	85
232	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	83
233	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	03/2016	167.64	88
234	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	88
235	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	03/2016	200	83
236	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	02/2016	486	69
237	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	03/2016	348.16	102
238	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	08/2016	160	99
239	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	08/2016	175.96	100

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
240	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	03/2016	332.94	90
241	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	12/2016	212	111
242	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196	80
243	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
244	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	03/2016	795	46
245	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108	55
246	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593	33
247	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	06/2016	828	21
248	REENGUS SIKAR	NHAI	03/2012	09/2014	02/2016	333.51	17
249	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
250	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
251	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
252	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	PWD	02/2014	11/2014	11/2016	170.21	24
253	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
254	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	PWD	03/2015	09/2015	08/2017	309.01	23
255	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
256	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	PWD	07/2015	12/2015	12/2016	333.21	12
257	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	PWD	02/2014	06/2014	06/2016	417.61	24
258	GUWAHATI TO NALBARI (AS-5)	NHAI	12/2003	04/2008	01/2016	198.16	93
259	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
260	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49
261	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	PWD	02/2014	07/2014	07/2016	258.99	24
262	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
263	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622 (DESIGN C	PWD	07/2015	12/2015	12/2016	333.21	12
264	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	PWD	01/2014	11/2014	11/2016	195.45	24
265	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
266	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2016	1267	33
267	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2016	2498.76	19
268	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2016	1724.55	45
269	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	09/2016	325	40
270	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	02/2016	264.72	92
271	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	07/2016	245	100
272	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	09/2016	217.61	77
273	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2016	478.51	33
274	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	12/2016	624	32
275	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	05/2017	1479	23
276	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2016	942.69	21
277	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	03/2016	1232	7
278	ETAWAH CHAKERI	NHAI	03/2013	09/2015	06/2016	1573	9
279	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	06/2016	2125.24	6
280	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
281	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	PWD	02/2015	04/2015	05/2016	224.83	13
282	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	NHDP	01/2012	04/2015	04/2016	381.86	12
283	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	PWD	11/2011	09/2015	08/2016	871.15	11
284	SATANA-BELA SECTION OF NH-75 (4L) IN MP	PWD	01/2012	08/2015	09/2016	320.48	13
285	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	10/2016	495.78	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
286	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	12
287	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	09/2016	351.34	8
288	KOTWA TO DEWAPUR (LMNHP-10)	NHAI	11/2005	11/2008	03/2016	240	88
289	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
290	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
291	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	88
292	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	01/2016	366.39	61
293	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	03/2016	150	120

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
294	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	01/2016	332.65	17
295	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	03/2017	149.73	15
296	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343	8
297	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	08/2016	877.73	13
298	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
299	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	06/2017	404.16	23
300	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HSCL	10/2011	12/2016	07/2017	175.49	7
301	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	03/2016	768.88	25
302	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2017	956	24
303	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2016	17265	39
304	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	SAIL	04/2014	04/2015	12/2016	188.93	20
305	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	03/2016	187.33	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XV

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
306	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2017	13334	20
307	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	ITI	09/2014	09/2014	03/2017	2111.17	30

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
308	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
309	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
310	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	01/2016	884.3	17
311	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
312	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	06/2016	261.85	37
313	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	05/2017	171.86	14
314	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	06/2016	6395	60
315	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
316	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	03/2016	270.83	16
317	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	04/2017	156.57	19
318	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	03/2016	225.81	45
319	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291
COAL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17
4	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05
HEAVY INDUSTRY							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3
PETROCHEMICALS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39
PETROLEUM							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
8	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4941.49	817.14
9	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495
12	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.08	172.08
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
16	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.76	4479.17
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	18063.89	11778.56
22	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
23	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
24	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
25	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.57	586.56
26	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
27	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
28	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5751.47	2109.43
29	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
30	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1262.27	688.28
31	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
32	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
33	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6085.84	3588.94
34	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9606.82	5484.82
35	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4237.67	1924.67
36	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
38	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	2193.08	1131.7

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
40	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
41	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
42	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
43	KARUR-SALEM (NL) ,SR	SR	02/1997	N.A.	155.55	800	644.45
44	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
45	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
46	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
47	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
48	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
49	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
50	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95
51	JIND-SONEPAT (NL) ,NR	NR	01/2004	03/2012	238.56	740	501.44
52	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
53	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	3040	2119
54	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
55	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
56	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
57	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
58	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
59	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
60	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
62	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91
63	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	MRTTP	03/1996	03/2004	495.44	1781.98	1286.54
65	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
66	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
67	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
68	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
69	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
70	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
71	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
72	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
73	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
74	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
75	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
76	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTTP	04/2008	03/2014	5300	7986.04	2686.04
77	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
78	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
79	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	496.24	296.24
80	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
81	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
82	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	MRTTP	04/2012	03/2016	632.68	816.55	183.87
83	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
85	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA- NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
86	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
87	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
88	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
89	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
90	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
91	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
92	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
93	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
94	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
95	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
96	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
97	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
98	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
99	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
100	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
101	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
102	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
103	HAIJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
104	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
105	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
106	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
108	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
109	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
110	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
111	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
112	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
113	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
114	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
115	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
116	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
117	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
118	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
119	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
120	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)		04/1997	N.A.	836.26	1072.51	236.25
121	HUBLI-ANKOLA (NL), SWR	SWR	04/1997	N.A.	227	2135	1908
122	RANCHI-LOHARDAGA (GC), SER	SER	04/1997	06/2004	194.07	335	140.93
123	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
124	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
125	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
126	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
127	MUNEERABAD-MAHABOONNAGAR (NL), SCR	SCR	04/1997	N.A.	218.24	645	426.76
128	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
129	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
131	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
132	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
133	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
134	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
135	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
136	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	325.5	159.34
137	DALLI-RAJHARA - RAOGHAT (PART OF DALLI- RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
138	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	2434	2109
139	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	NR	03/2002	06/2007	625.3	847.75	222.45
140	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	20000	17500
141	NANGALDAM-TALWARA (NL) , NR	NR	03/1981	07/2012	450	2100	1650
142	KANPUR KASGANJ MATHURA (GC) NER	NER	03/1997	N.A.	677.97	1651.54	973.57
143	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
144	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
145	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
146	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
147	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
148	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
149	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
150	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	3500	3252.34
151	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
152	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
154	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
155	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
156	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
157	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
158	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
159	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
160	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
161	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
162	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
163	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
164	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
165	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	360	223.38
166	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	318.33	184.92
167	VIRAMGAM-BHILDI (WR) ,GC	WR	04/1990	N.A.	155.66	548.01	392.35
168	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
169	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
170	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
171	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
172	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
173	RAMGANJMUNDI-BHOPAL (NL) ,WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVI

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
174	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
175	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
176	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
177	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
178	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
179	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
180	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
181	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
182	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
183	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1060	291.12
184	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
185	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	6395	13845.01	7450.01

DOA -> Date of Approval

DOC -> date of Commissioning

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	05/2016	1,3171.00	2,2462.00	9291	89
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	09/2016	3492.00	5677.00	2185	72

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	03/2016	212.34	1228.39	1016.05	36
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	08/2016	871.35	1200.00	328.65	17
7	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	03/2016	732.00	1227.00	495	53
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2017	309.81	462.79	152.98	29
9	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4941.49	817.14	20
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	05/2016	993.00	1693.00	700	52
11	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	02/2016	2,9777.00	3,4555.00	4778	39
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT (MOPS)	ONGC	03/2011	05/2013	04/2016	861.79	1256.72	394.93	35
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.08	172.08	12
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	01/2016	421.01	1007.57	586.56	30
16	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	06/2016	1746.65	2228.71	482.06	22
17	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
18	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
19	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
20	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	03/2016	2313.00	4237.67	1924.67	51
21	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	01/2017	4122.00	9606.82	5484.82	71
22	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2016	2496.90	6085.84	3588.94	78
23	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	07/2016	573.99	1262.27	688.28	35
24	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5751.47	2109.43	10
25	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
26	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.76	4479.17	111
27	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	09/2016	1061.38	2193.08	1131.7	84
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2016	477.69	738.48	260.79	75
29	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
30	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	12/2016	2144.00	2932.88	788.88	48

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	BARH STPP (3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88
32	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2016	1779.29	2187.32	408.03	97

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
33	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	MRTP	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
34	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
35	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
36	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	12/2017	2500.00	2,0000.00	17500	181
37	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
38	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
39	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87
40	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
41	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	03/2016	921.00	3040.00	2119	84
42	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	10/2016	133.41	318.33	184.92	91
43	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
44	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.10	275.08	103.98	48
45	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
46	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144
48	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
49	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111
50	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
51	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
52	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
53	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
54	RAJATGARH-BARANG (LD), ECOR	RVNL	04/1999	02/2009	04/2016	166.16	325.50	159.34	86
55	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
56	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2016	1108.00	2288.00	1180	55
57	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2016	196.00	331.23	135.23	80
58	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	03/2016	155.04	280.13	125.09	88
59	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	03/2016	199.81	385.13	185.32	83

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	08/2016	245.67	409.83	164.16	88
61	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND	MUMBAI PORT TRU	01/2007	12/2010	01/2016	366.39	669.46	303.07	61

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure - XVII

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
62	DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMBAI ENMORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	03/2016	150.00	600.00	450	120

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	06/2017	343.00	488.40	145.4	8
64	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	03/2016	768.88	1060.00	291.12	25

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
65	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	06/2016	6395.00	1,3845.01	7450.01	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Annexure- XVIII

**Details of 20 Railways Projects [as identified by Ministry of Railways vide letter
no. 2011/w-1 /Genl / MoSPI dated 28/10/2015] to be monitored at MoSPI level**

			(January 2016)			
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>RAILWAYS</u>					
1	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 - 2,921.00	10/2007 12/2012	12/2015	0/0
2	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 3,040.00 3,040.00	03/2009 -	03/2016	0/0
3	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 - 5,500.00	03/2009 -	03/2016	0/0
4	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 - 1,242.25	03/2007 -	03/2016	0/0
5	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,996.19 4,996.19	04/2008 12/2011	06/2017	0/0
6	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 - 20,000.00	11/2002 -	12/2017	0/0
7	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36 1,651.54	- - -	03/2018	0/0
8	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 - 1,143.60	- - -	03/2018	0/0
9	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 - 1,544.40	03/1998 -	12/2019	0/0
10	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 3,500.00 3,500.00	05/2008 -	-	0/0
11	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 - 1,266.89	- -	-	0/0
12	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 2,200.00 2,200.00	- -	-	0/0
13	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345],UTTAR PRADESH	04/1997	836.26 - 1,072.51	- -	-	0/0
14	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 2,434.00 2,434.00	03/2010 -	-	0/0

			(January 2016)			
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	2,957.21 - 2,957.21	07/2005 -	-	0/0
16	HARIDASPUR-PARADEEP (NL) - [220100285] RVNL, ODISHA	04/1996	301.64 - 1,185.64	- 09/2009	-	0/0
17	SUKINDA ROAD - ANGUL (NL) (ECOR) - [220100325] RVNL, ODISHA	04/1998	183.23 - 1,202.70	02/2015 -	-	0/0
18	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189] SR, MULTI STATE	04/2008	822.39 - 1,280.83	- -	-	0/0
19	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297] SWR, KARNATAKA	04/2010	2,127.00 - 2,127.00	- -	-	0/0
20	SAMBALPUR-TALCHER DOUBLING - [N22000315] ECR, ODISHA	03/2011	679.27 - 1,111.99	- -	-	0/0
	Total		20,808.52 -			0/0
	Grand Total		20,808.52			0/0
