

**375th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
January 2017**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
Executive summary Hindi	1-3
Executive summary English	4-7
Month wise List of Completed Projects Costing Rs.150 crore and above during 2016-2017	8-13
Month wise List of Deleted Projects Costing Rs.150 crore and above during 2016-2017	14-16
Summary of Projects (Rs 150 crore and above)	17-27
Month wise List of projects dropped/Frozen during current month	28-28
List of projects added during current month & Milestone Summary	29-30
List of projects reporting additional delay during current month	31-34
Sector wise Analysis of Projects (Rs 150 crore and above)	35-35
Sector wise Summary of Mega Projects (Rs 1000 crore and above)	36-46
Graphical Presentation of all Projects w.r.t. Original Scheduled	47-63
Sector wise analysis of all ongoing Projects	64-124
Graphical Sector wise analysis of Projects	125-142
Annexure	143-143
Status of Central Sector Projects costing Rs. 150 crore and above	144-144
List of Projects (Rs. 150 crore and above) in which Expenditure is More than Approved Cost	145-152
Details of Projects (Rs. 150 crore and above) Ahead of Schedule w.r.t. Original Schedule	153-153
Details of On Schedule Projects (Rs. 150 crore and above) w.r.t. Original Schedule	154-168
Details of Ongoing Projects (Rs. 150 crore and above) having Cost Overruns w.r.t. to Original Schedule	169-184
Details of Delayed Projects (Rs. 150 crore and above) w.r.t. Original Schedule	185-218
Details of Ongoing Projects (Rs. 150 crore and above) having Time and Cost Overruns w.r.t. Original Schedule	219-224
Details of Projects (Rs. 150 crore and above) Without Date of Commissioning	225-247
Details of Projects (Rs. 150 crore and above) Without Original Date of Commissioning	248-255
Details of Projects (Rs. 150 crore and above) Without Milestones w.r.t. Original Schedule	256-294
List of Projects (Rs. 150 crore and above) Ahead of Schedule w.r.t. Latest Schedule	295-296
List of Projects (Rs. 150 crore and above) on schedule w.r.t. Latest Schedule	297-317
List of ongoing projects (Rs. 150 crore and above) having cost overrun w.r.t. to latest schedule	318-328
List of Delayed Projects (Rs. 150 crore and above) w.r.t. Latest Schedule	329-343
Details of Central Sector Projects (Rs. 150 crore and above) showing Time Overruns of 6 Months and more	344-358
Details of Central Sector Projects (Rs. 150 crore and above) showing Cost Overruns of more than Rs 100 crore	359-369
Details of Central Sector Projects Showing Time Overrun of 6 Months and more and Cost Overrun of Rs.100 Crore and above	370-375
Details of Ongoing Projects (Rs.150 crore and above) Under -Public Private Partnership Mode	376-380

1. जनवरी, 2016 की बड़ी परियोजनाओं से संबंधित फ्लैश रिपोर्ट में ₹150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 1201 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है।

2. **केन्द्रीय क्षेत्र परियोजनाओं** (150 करोड़ रु. और उससे अधिक लागत वाली) के कार्यान्वयन स्थिति नीचे दिया गया है:

(i) संदर्भाधीन माह के दौरान, 61 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। 61 परियोजनाओं में से, 20 मेगा परियोजनाएं 1000 करोड़ और उससे अधिक लागत वाली हैं।

(ii) 1201 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹15,28,249.27 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹16,99,285.76 करोड़ होने की संभावना है, जो ₹1,71,036.49 करोड़ (मूल लागत का 11.19%) की समग्र लागत वृद्धि को दर्शाता है। जनवरी, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹7,08,958.70 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 41.72% है।

(iii) इसके अतिरिक्त, 1201 परियोजनाओं में से, 2 परियोजनाओं के संबंध में समापन की सूचना दी गई है तथा 20 नई परियोजनाएं आरंभ की गई हैं। 8 परियोजनाएं समय से पहले चल रही हैं, 286 समय पर हैं, 329 विलंबित हैं, 293 परियोजनाएं लागत वृद्धि दर्शाती हैं तथा 95 परियोजनाएं अपनी मूल परियोजना समय-अवधि की तुलना में समय तथा लागत वृद्धि दोनों दर्शाती हैं। तथापि, यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है तो विलंबित परियोजनाओं की संख्या में 271 तक की कमी हो जाती है। 578 परियोजनाओं के लिए जहां शुरू करने की मूल/अनुमानित तारीख सूचित नहीं किया गया है, सभी संबंधित से निवेदन है कि शुरू करने की मूल/अनुमानित तारीख प्रदान करें ताकि इन परियोजनाओं की समापन तथा लक्षित तारीख समान रूप से निगरानी की जा सके।

(iv) 329 विलंबित परियोजनाओं में से, 62 परियोजनाओं में 1 से 12 माह तक का विलंब है, 66 परियोजनाओं में 13 से 24 महीने तक का विलंब है, 123 परियोजनाओं में 25 से 60 माह तक का विलंब है तथा 78 परियोजनाओं में 61 माह और उससे अधिक का विलंब है।

(v) 329 विलंबित परियोजनाओं में से, 95 परियोजनाओं में लागत वृद्धि हुई है। इनमें से 59 परियोजनाओं की लागत संशोधित की जा चुकी है तथा 36 परियोजनाओं की लागत अभी संशोधित नहीं की गई है। इन 59 परियोजनाओं में से, जिनकी लागत संशोधित की गई है, 13 परियोजनाओं की अनुमानित लागत संशोधित लागत से पुनः अधिक हो चुकी है। 329 विलंबित परियोजनाओं में से, 166 परियोजनाओं ने कोई उपलब्धि प्रदान नहीं की है तथा 102 परियोजनाओं के मामले में उपलब्धि के पूर्ण होने की तारीख पहले ही समाप्त हो चुकी है।

(vi) उपर्युक्त के अलावा जहां 198 परियोजनाएं हैं जो समय पर चल रही हैं, लेकिन लागतवृद्धि नहीं दर्शा रही है। इनमें से 99 परियोजनाओं की लागत संशोधित की जा चुकी है। 99 परियोजनाओं, जिनकी लागत संशोधित की जा चुकी है, इनमें से 41 परियोजनाओं की अनुमानित लागत संशोधित लागत से पुनः अधिक हो चुकी है। इन 198 परियोजनाओं में से, 128 परियोजनाओं ने कोई उपलब्धि प्रदान नहीं की है तथा 5 परियोजनाओं के मामले में उपलब्धि के पूर्ण होने की तारीख पहले ही समाप्त हो चुकी है।

(vii) चालू माह में, 311 परियोजनाएं 6 माह से अधिक की समयवृद्धि दर्शा रही हैं; 219 परियोजनाएं ₹100 करोड़ से अधिक की लागतवृद्धि दर्शा रही हैं तथा 74 परियोजनाएं 6 माह से अधिक की समयवृद्धि और ₹100 करोड़ से अधिक की लागत वृद्धि दोनों दर्शा रही हैं। इसके अतिरिक्त, 158 परियोजनाओं के मामले में अनुमोदित लागत से अधिक व्यय हो चुका है तथा 852 परियोजनाओं ने उपलब्धियां सूचित नहीं की हैं। संबंधित सचिवों से इन परियोजनाओं की समय-सीमा और लागत निर्धारित करने के लिए पुनरीक्षा करने का अनुरोध किया गया है।

3. केन्द्रीय क्षेत्र मेगा परियोजनाओं (1000 करोड़ रु. और उससे अधिक लागत वाली) के कार्यान्वयन स्थिति नीचे दिया गया है:-

(i) संदर्भाधीन माह के दौरान, 1201 परियोजनाओं में से 353 परियोजनाएं **मेगा** परियोजनाएं हैं। 353 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹11,79,239.09 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹13,23,133.31 करोड़ होने की संभावना है, जो ₹1,43,894.22 करोड़ (मूल लागत का 12.20%) की समग्र लागत वृद्धि को दर्शाता है। जनवरी, 2016 तक इन परियोजनाओं पर किया गया व्यय ₹5,84,199.11 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 44.15% है।

(ii) इसके अलावा 127 मेगा परियोजनाओं में से, 51 परियोजनाएं लागतवृद्धि दर्शाती हैं। इनमें से, 32 परियोजनाएं जिनकी लागत संशोधित की जा चुकी है तथा 19 परियोजनाओं की लागत अभी संशोधित नहीं की गई है। इन 32 परियोजनाओं में से, जिनकी लागत संशोधित की गई है, 9 परियोजनाओं की अनुमानित लागत संशोधित लागत से पुनः अधिक हो चुकी है। 127 विलंबित परियोजनाओं में से, 59 परियोजनाओं ने कोई उपलब्धि प्रदान नहीं की है तथा 52 परियोजनाओं के मामले में उपलब्धि के पूर्ण होने की तारीख पहले ही समाप्त हो चुकी है।

(iii) उपर्युक्त के अलावा जहां 64 मेगा परियोजनाएं हैं जो समय पर चल रही हैं, लेकिन लागतवृद्धि नहीं दर्शा रही है। इनमें से 39 परियोजनाओं की लागत संशोधित की जा चुकी है। 39 परियोजनाओं, जिनकी लागत संशोधित की जा चुकी है, इनमें से 16 परियोजनाओं की अनुमानित लागत संशोधित लागत से पुनः अधिक हो चुकी है। इन 64 परियोजनाओं में से, 30 परियोजनाओं ने कोई उपलब्धि प्रदान नहीं की है तथा 3 परियोजनाओं के मामले में उपलब्धि के पूर्ण होने की तारीख पहले ही समाप्त हो चुकी है।

(iv) चालू माह में, 123 मेगा परियोजनाएं 6 माह से अधिक की समयवृद्धि दर्शा रही हैं; 114 मेगा परियोजनाएं 100 करोड़ रु. से अधिक की लागतवृद्धि दर्शा रही हैं तथा 50 मेगा परियोजनाएं 6 माह से अधिक की समयवृद्धि और 100 करोड़ रु. से अधिक की लागत वृद्धि दोनों दर्शा रही हैं। इसके अतिरिक्त, 65 मेगा परियोजनाओं के मामले में अनुमोदित लागत से अधिक व्यय हो चुका है तथा 230 मेगा परियोजनाओं ने उपलब्धियां सूचित नहीं की हैं। संबंधित सचिवों से इन परियोजनाओं की समय-सीमा और लागत निर्धारित करने के लिए पुनरीक्षा करने का अनुरोध किया गया है।

4. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रमिकों की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय संबंधी मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

5. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया जाता है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं।

6. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं।

7. रेल मंत्रालय ने मंत्रालय के ओसीएमएस पर ₹500 करोड़ और उससे अधिक लागत वाली चालू परियोजनाओं के संबंध में अद्यतन सूचना प्रदान की है। ₹500 करोड़ से कम लागत वाली परियोजनाओं के संबंध में वर्तमान और नवीनतम अद्यतन सूचना सूचित की गई है और प्राप्त हुई है।

8. दिनांक 31.01.2017 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹150 करोड़ तथा अधिक लागत वाली परियोजनाओं से संबंधित स्थिति www.cspm.gov.in/publication पर उपलब्ध रिपोर्ट में सूचित की गई है।

9. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for January 2016 contains information on the status of the 1201 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. The implementation status of **Central Sector Projects (costing Rs 150 crore and above)** may be summarized as below:-

(i). During the reference month, 61 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 61 projects, 20 are **Mega** Projects costing ₹1000 crore and above.

(ii). Total original cost of implementation of the 1201 projects was ₹15,28,249.27 crore and their anticipated completion cost is likely to be ₹16,99,285.76 crore, which reflects overall cost overruns of ₹1,71,036.49 crore (11.19% of original cost). The expenditure incurred on these projects till January 2016 is ₹7,08,958.70 crore, which is 41.72% of the anticipated cost of the projects.

(iii). Out of the 1201 projects, 2 projects have reported completion and 20 new projects have been started. Of these 8 projects are ahead of schedule, 286 are on schedule and 329 are delayed, 293 projects are showing cost overrun and 95 projects are showing both time and cost overrun with respect to original implementation schedules. However, the number of delayed projects decreases to 271 if delay is calculated with reference to latest revised schedules of completion. For 578 projects, where original/anticipated commissioning date has not been reported, all concerned have been requested to provide the original/anticipated commissioning date so that these projects can be monitored for completion vis-a-vis the targeted dates.

(iv). Out of 329 delayed projects, 62 projects have overall delay in the range of 1 to 12 months, 66 projects have delay in the range of 13 to 24 months, 123 projects have delay in the range of 25 to 60 months and 78 projects have delay of 61 months and above.

(v). Further, out of the 329 delayed projects, 95 projects have cost overruns. Out of these, the cost for 59 projects has been revised and for 36 projects the cost has not yet been revised. Of the 59 projects where cost has been revised, the anticipated cost of 13 projects has again exceeded the revised cost. Out of 329 delayed projects, 166 projects have not provided any milestones and in 102 cases the dates of completion of the milestones have already lapsed.

(vi). In addition to above there are 198 projects which though are on schedule but are having cost overruns. Of these, the cost for 99 projects has since been revised. Of the 99 projects where cost has been revised, the anticipated cost of 41 projects has exceeded even the revised costs. Out of these 198 projects, 128 projects have not provided any milestones and for 5 projects the completion date of milestone(s) has already lapsed.

(vii). In the current month, there are 311 projects showing time overruns of more than 6 months; 219 projects showing cost overruns of more than ₹100 crore and 74 projects showing both time overruns of more than 6 months and cost overruns of more than ₹100 crore. Further, expenditure has exceeded the approved cost in 158 projects and in 852 projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimates.

3. The implementation status of **Central Sector Mega Projects** (costing Rs 1000 crore and above) may be summaries as below:-

(i) During the reference month out of 1201 projects 353 are **mega** projects. Total original cost of implementation of these 353 projects was ₹11,79,239.09 crore and their anticipated completion cost is likely to be ₹13,23,133.31crore, which reflects overall cost overruns of ₹1,43,894.22 crore (12.20% of original cost). The expenditure incurred on these projects till January 2016 is ₹ 5,84,199.11 crore, which is 44.15% of the anticipated cost of the projects.

(ii). Further, out of the 127 delayed mega projects, 51 projects have cost overruns. Out of these, the cost for 32 projects has been revised and for 19 projects the cost has not yet been revised. Of the 32 projects where cost has been revised, the anticipated cost of 9 projects has again exceeded the revised cost. Out of 127 delayed projects, 59 projects have not provided any milestones and in 52 cases the dates of completion of the milestones have already lapsed.

(iii). In addition to above there are 64 mega projects which though are on schedule but are having cost overruns. Of these, the cost for 39 projects has since been revised. Of the 39 projects where cost has been revised, the anticipated cost of 16 projects has exceeded even the revised costs. Out of these 64 projects, 30 projects have not provided any milestones and for 3 projects the completion date of milestone(s) has already lapsed.

(iv). In the current month, there are 123 mega projects showing time overruns of more than 6 months; 114 mega projects showing cost overruns of more than Rs.100 crore and 50 mega projects showing both time overruns of more than 6 months and cost overruns of more than Rs.100 crore. Further, expenditure has exceeded the approved cost in 65 mega projects and in 230 mega projects milestones have not been reported. Concerned secretaries have been requested to take a review of these projects to fix time lines and cost estimate.

4. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

5. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones.

6. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported.


7. Ministry of Railways have provided the latest information of all its ongoing projects costing ₹500 crore and above on the OCMS of this Ministry. The recent and latest updated information in respect of projects costing below ₹500 crore is reported as and when received.

8. The status as on 31.01.2017 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report available at www.cspm.gov.in/publication.

9. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	451	19
2	RAILWAYS	347	2
3	POWER	121	22
4	PETROLEUM	89	5
5	COAL	87	6
6	STEEL	33	3
7	URBAN DEVELOPMENT	31	2
8	HEALTH AND FAMILY WELFARE	13	1
9	SHIPPING AND PORTS	8	0
10	ATOMIC ENERGY	4	0
11	CIVIL AVIATION	4	1
12	MINES	4	0
13	TELECOMMUNICATIONS	3	0
14	FERTILISERS	2	0
15	DEFENCE PRODUCTION	2	0
16	PETROCHEMICALS	1	0
17	HEAVY INDUSTRY	1	0
	Total	1201	61

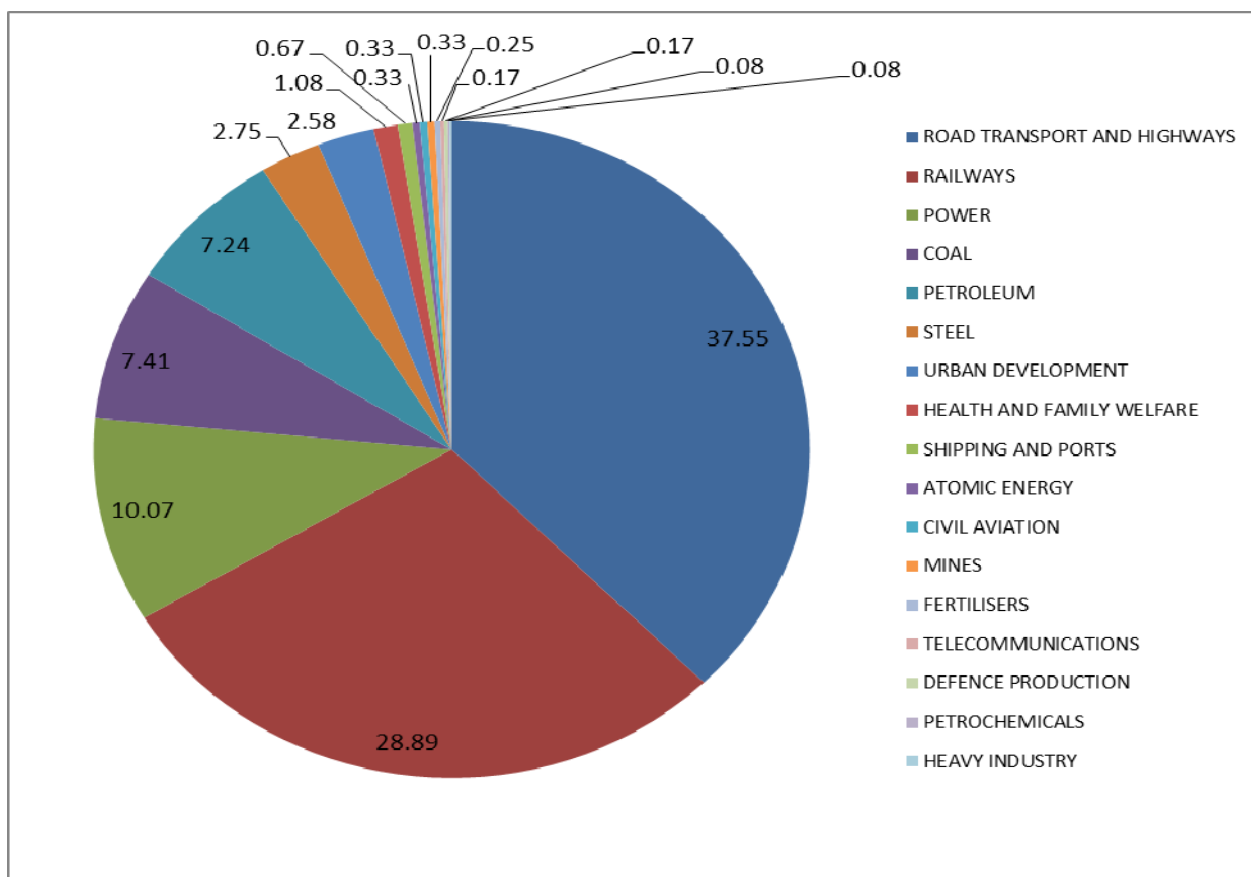

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2016			
	<u>COAL</u>			
1	KRISHNASHILA (NCL) (4MTY) (NORTHERN COAL FIELDS LIMITED) - [N06000007]	789.88	03/2013	511.19
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) (NORTHERN COAL FIELDS LIMITED) - [N06000010]	1,352.04	03/2016	848.99
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100207]	157.47	09/2007	238.50
4	KOTA BYPASS,RJ-4, NH-76 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106297]	275.00	10/2008	184.63
5	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106304]	251.03	10/2008	326.30
6	SILIGURI TO ISLAMPUR (WB-7) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000028]	225.00	07/2008	191.00
7	NALBARI TO BIJNI (AS-8) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000035]	200.00	06/2008	281.60
8	GUWAHATI TO NALBARI (AS-5) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000046]	198.16	04/2008	242.40
9	DHARAMTUL TO SONAPUR (AS-19) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000051]	200.00	06/2008	289.50
10	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000107]	557.00	02/2010	932.30
11	KISHANGARH-AJMER-BEAWER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000128]	795.00	05/2012	1,512.11
12	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000132]	572.30	10/2011	761.40
13	JAIPUR-TONK-DEOLI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000135]	792.06	12/2012	1,983.00
14	HAZARIBAGH-RANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000141]	625.07	01/2013	995.90
15	ARMUR TO KADLOOR YELLAREDDY (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000143]	390.56	02/2012	631.60
16	PANIPAT-ROHTAK (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000151]	807.00	10/2014	1,209.43
17	DEVIHALLI-HASSAN (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000152]	453.00	-	487.90
18	BELGAUM-DHARWAD(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000158]	480.00	-	438.00
19	UGRADATION OF HYDERABAD-BANGALORE SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000160]	680.00	-	188.40
20	2-LANNING OF SHILONG BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000181]	226.00	02/2014	282.30
21	BHOPAL-SANCHI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000192]	209.00	01/2013	11.28

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2016-2017

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
22	PUNE-SHOLAPUR,PKG-II PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000193]	835.00	01/2014	1,684.00
23	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000196]	909.00	05/2014	844.10
24	LUCKNOW-RAIBAREILI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000207]	635.90	07/2012	616.50
25	NAGPUR-WAINGANGA BRIDGE PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000210]	484.19	10/2014	458.86
26	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000214]	682.00	10/2013	34.81
27	2 LANING WITH PS AGRA ALIGARH (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000220]	250.50	10/2014	65.30
28	2 LANING WITH PS KANPUR KABRAI (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000221]	373.47	07/2014	358.30
29	2-LANING WITH PS OF JHALAWAR-RAJASTHAN-MP. BORDER (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000237]	177.32	01/2016	86.50
30	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD ITEM RATE(PUBLIC WORKS DEPT OF STATE) - [N24000304]	186.96	-	132.80
31	2-LANING WITH PAVED SHOULDER OF RAEBARELI TO JAUNPUR PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000428]	569.38	06/2016	737.59
32	PONDICHERRY TO TINDIVANAM SECTION OF NH-66 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000466]	285.00	01/2008	285.00
	May,2016			
	<u>STEEL</u>			
33	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000072]	572.00	04/2013	451.58
34	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) (NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)) - [N12000073]	898.55	05/2013	379.57
	<u>PETROLEUM</u>			
35	MOUNDED BULLET PROJECT AT CPCL (CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000154]	279.00	12/2014	190.86
	<u>URBAN DEVELOPMENT</u>			
36	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000061]	225.81	06/2012	143.72
37	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000063]	171.10	09/2014	192.24
	June,2016			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2016-2017

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
38	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000108]	232.45	09/2010	343.71
	July,2016			
	<u>PETROLEUM</u>			
39	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000183]	2,476.82	12/2018	982.92
	<u>POWER</u>			
40	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000056]	410.29	02/2012	390.87
41	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000083]	965.58	11/2012	791.84
42	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000095]	1,677.57	04/2013	1,487.22
43	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000104]	558.26	11/2013	629.41
44	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000113]	2,422.66	08/2014	2,497.86
45	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP- PART B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000122]	1,927.16	10/2014	1,642.57
46	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK IN ANANTPUR DISTRICT, ANDHRA PRADESH- PART A (PHASE-I) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000198]	312.94	05/2016	109.00
	<u>RAILWAYS</u>			
47	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR (EAST CENTRAL RAILWAYS) - [220100307]	921.00	03/2009	1,649.05
48	PATNA GANGA BRIDGE (NL), ECR (EAST CENTRAL RAILWAYS) - [220100308]	624.47	10/2007	3,104.92
49	CONSTRUCTION OF STEEL SUPERSTRUCTURE AND OTHER ANCILLARY WORKS OF RAIL CUM ROAD BRIDGE. FABRICATION (EAST CENTRAL RAILWAYS) - [N22000342]	1,191.31	06/2012	1,296.95
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
50	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106221]	155.00	09/2008	248.73
51	4 LANNING OF GODHARA TO GUJARAT/MP BORDER PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000168]	785.50	08/2013	923.28
52	JAIPUR-REENGUS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000198]	267.81	02/2013	699.60
53	BEAWAR PALI PINDWARA PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000199]	2,388.51	06/2014	2,490.61
54	REENGUS SIKAR PPP (ANNUITY)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000227]	333.51	09/2014	226.96

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2016-2017

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
55	2-LANING WITH PS LAMBIA-JAITRAN-RAIPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000238]	158.04	12/2015	129.37
56	4 LANING OF GOMTI CHAURAHA - UDAIPUR EPC(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000455]	914.50	10/2015	1,128.25
57	4-LANING OF ROHTAK - HISSAR SECTION PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000456]	959.25	06/2016	1,229.40
	August,2016			
	<u>POWER</u>			
58	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100243]	1,061.38	09/2009	2,048.42
	<u>RAILWAYS</u>			
59	CUTTACK - BARANG (LD) (RAIL VIKAS NIGAM LTD.) - [220100326]	127.13	-	237.96
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
60	GUWHATI TO NALBARI (AS-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000038]	175.96	04/2008	309.01
61	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000171]	535.00	12/2013	924.70
	September,2016			
	<u>COAL</u>			
62	ASHOK EXPN OCP CCL (10 MTY) (CENTRAL COAL FIELDS LIMITED) - [060100096]	341.63	03/2011	241.62
	<u>PETROLEUM</u>			
63	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG (OIL INDIA LIMITED) - [N16000165]	270.00	06/2012	172.53
	<u>RAILWAYS</u>			
64	BANKURA - DAMODAR (GC) (SER) (SOUTH EASTERN RAILWAY) - [220100277]	111.90	03/2005	195.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
65	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106290]	195.00	06/2008	294.65
66	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106294]	332.94	09/2008	518.85
67	NAGAON TO DHARAMTUL (AS-2) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000042]	264.72	06/2008	322.50
	October,2016			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2016-2017

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>COAL</u>			
68	ADRIYALA SHAFT PROJECT (SINGARENI COLLIERIES COMPANY LIMITED) - [N06000016]	212.34	03/2013	1,237.34
	<u>PETROLEUM</u>			
69	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE (INDIAN STRATEGIC PETROLEUM RESERVES LTD) - [N16000157]	732.00	10/2011	1,172.10
70	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000191]	160.00	02/2016	129.36
71	BULK PETROLEUM OIL AND LUBRICANT (POL) DEPOT AT IMPHAL, MANIPUR Central Sector Projects(INDIAN OIL CORPORATION LIMITED) - [N16000215]	103.02	07/2016	124.29
	<u>TELECOMMUNICATIONS</u>			
72	GSM/UMTS IN KARNATAKA LOT 1 (2G+3G) (BHARAT SANCHAR NIGAM LIMITED) - [N26000104]	154.12	08/2016	84.75
	November,2016			
	<u>STEEL</u>			
73	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000076]	187.33	10/2013	183.07
	<u>PETROLEUM</u>			
74	LPG MARKETING TERMINAL, PARADIP (INDIAN OIL CORPORATION LIMITED) - [N16000174]	158.91	03/2015	127.44
	<u>POWER</u>			
75	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000098]	250.03	01/2013	309.70
76	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000129]	3,201.44	10/2014	3,500.21
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000135]	524.40	05/2015	368.42
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000152]	680.69	03/2016	551.69
79	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000161]	167.40	12/2015	121.30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
80	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000211]	356.40	07/2014	352.00
	December,2016			

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2016-2017

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	<u>STEEL</u>			
81	UPGRADATION OF BLAST FURNACE-1 AT RSP (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000084]	708.91	04/2016	574.88
	<u>PETROLEUM</u>			
82	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) (GAS AUTHORITY OF INDIA LIMITED) - [N16000093]	463.32	06/2011	415.56
83	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE (GAS AUTHORITY OF INDIA LIMITED) - [N16000190]	419.04	01/2017	378.59
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
84	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106293]	237.80	06/2008	422.84
85	AGRA-BYPASS(NS-1/UP-1), NH-2,3 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000098]	348.16	09/2007	426.93
	<u>TELECOMMUNICATIONS</u>			
86	INSTALLATION AND COMMISSIONING OF GSM UP (E) 2G+3G (BHARAT SANCHAR NIGAM LIMITED) - [N26000103]	174.39	04/2015	118.14
	January,2017			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
87	SAMAIKHALI - GANDHIDHAM PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000179]	805.39	03/2013	1,408.40
	<u>URBAN DEVELOPMENT</u>			
88	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000069]	261.85	05/2013	235.00

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	May,2016			
	<u>URBAN DEVELOPMENT</u>			
1	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000066]	238.43	02/2015	0.00
	July,2016			
	<u>PETROLEUM</u>			
2	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT (GAS AUTHORITY OF INDIA LIMITED) - [N16000129]	2,915.00	12/2012	1,381.86
	August,2016			
	<u>COAL</u>			
3	GOPAL PRASAD OCP (15MTY) (MAHANADI COAL FIELDS LIMITED) - [N06000042]	395.87	03/2015	76.74
4	TALABIRA OCP (MAHANADI COAL FIELDS LIMITED) - [N06000043]	447.72	03/2016	52.36
	September,2016			
	<u>PETROLEUM</u>			
5	CONSTRUCTION OF COASTAL POL TERMINAL AT ENNORE (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000219]	393.00	04/2018	0.00
6	LPG STORAGE TERMINAL AT PALAKKAD, KERALA (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000220]	184.00	12/2017	12.43
7	LPG IMPORT TERMINAL AT HALDIA, WEST BENGAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000221]	694.00	10/2018	57.19
	<u>RAILWAYS</u>			
8	AKOLA-KHANDWA GC AKOLA-AKOT (SOUTH CENTRAL RAILWAY) - [N22000263]	184.26	-	17.32
9	MUDKHED-PARBHANI (SOUTH CENTRAL RAILWAY) - [N22000283]	390.60	-	2.11
10	AKKANAPET-MEDAK (SOUTH CENTRAL RAILWAY) - [N22000285]	153.00	-	0.00
11	KAKINADA-PITHAPURAM (SOUTH CENTRAL RAILWAY) - [N22000314]	215.06	-	0.01
12	MANOHARABAD-KOTAPALLI (SOUTH CENTRAL RAILWAY) - [N22000357]	1,160.47	-	0.00
13	SECUNDERABAD-MOHABOONNAGAR (RAIL VIKAS NIGAM LTD.) - [N22000371]	728.10	-	0.00

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
14	VIRAMGAM BHILDI (WESTERN RAILWAY) - [N22000391]	237.13	03/2018	25.05
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
15	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106226]	230.00	06/2005	203.60
16	CHENNAI-TADA(SIX LANE) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000129]	353.37	10/2011	365.08
17	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000139]	1,655.00	09/2013	641.78
18	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000228]	1,287.95	11/2015	757.57
19	2 LANING WITH PAVED SHOULDER OF KARAIKUDI - RAMANATHAPURAM SECTION OF NH-210 INCLUDING 500 M ON SH-(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000340]	451.58	06/2017	28.00
	October,2016			
	<u>RAILWAYS</u>			
20	VIRAMGAM-BHILDI(WR),GC (WESTERN RAILWAY) - [220100062]	155.66	-	278.93
21	INDORE-DEWAS-UJJAIN(80 KM) DL (WESTERN RAILWAY) - [N22000375]	600.00	-	0.00
22	BHILDI VIRAMGAM WITH NEW MM FOR MSH-TRAH GAUGE CONVERSION PROJECT (WESTERN RAILWAY) - [N22000384]	153.82	03/2019	12.60
23	INDORE DEWAS UJJAIN (80 KM) (WESTERN RAILWAY) - [N22000393]	600.00	-	0.00
	November,2016			
	<u>COAL</u>			
24	JALLARAM SHAFT PROJECT (SINGARENI COLLIERS COMPANY LIMITED) - [N06000025]	467.78	03/2013	2.85
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
25	4 LANING OF OBEDULLAGANJ-BETUL SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000457]	912.00	08/2016	120.43
	January,2017			
	<u>MINES</u>			
26	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC(HINDUSTAN COPPER LIMITED) - [N10000007]	1,856.00	09/2017	32.18

Month wise List of Deleted Projects Costing Rs.150 crore and above during				
2016-2017				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	<u>PETROLEUM</u>			
27	NEW MARKETING TERMINAL AT ENNORE (INDIAN OIL CORPORATION LIMITED) - [N16000178]	171.83	-	0.00


Summary of projects in the Flash Report for the month of January, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1186
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects degradation from the status of project during the current month	1
Number of Projects Added in Current Month	20
Number of Projects in Current Month	1201

Brief Analysis

Project Status with respect to Original Schedule: Out of 1201 projects, 8 projects are ahead of schedule, 286 projects are on schedule 329 projects are delayed. 447 projects do not have fixed dates of commissioning. 131 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

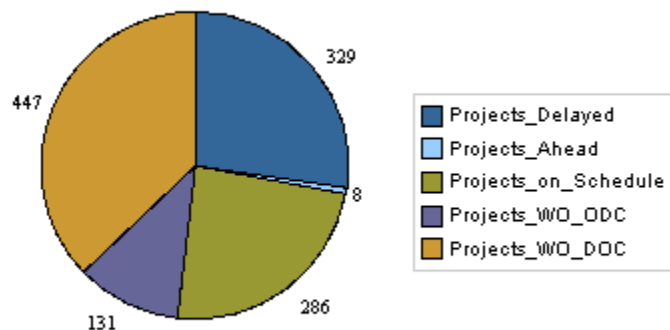


Total No Of Project's:- 1201

Investment Scenario

Total original cost of implementation of 1201 projects when sanctioned, was of the order of Rs. 1528249.27 crore but this was subsequently revised to Rs. 1699285.76 crore implying a cost overrun of 11.2%. The expenditure incurred on these projects till January, 2017 is Rs. 708958.7 crore, which is 41.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

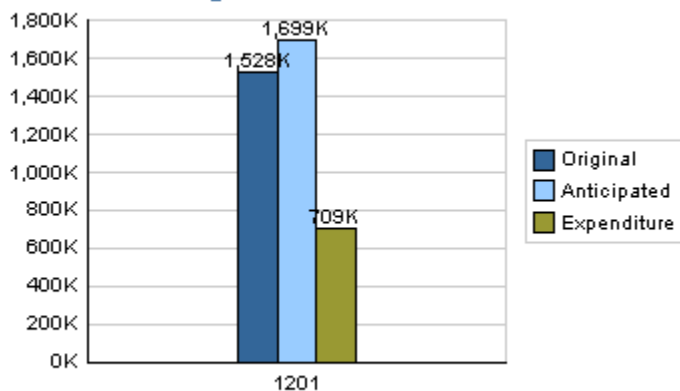

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	1186
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	20
No of Projects degraded from the status of Major Project during the Current Month	1
No of Projects in Current Month	1201

Project status						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	329 (27.39%)	8 (.67%)	286 (23.81%)	131 (10.91%)	447 (37.22%)	1201
Latest Approved (Date)	270 (22.48%)	10 (.83%)	376 (31.31%)	97 (8.08%)	447 (37.22%)	1201

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	973	12,78,106.26	13,26,362.76	4,74,535.59	35.80	48,256.50	3.80
Project with Revision in Cost	228	3,46,987.83	3,72,923.00	2,34,423.11	62.90	25,935.17	7.50
Total	1,201	16,25,094.09	16,99,285.76	7,08,958.70	41.72	74,191.67	4.57
Original Cost of All Projects							
Original Cost	1,201	15,28,249.27	16,99,285.76	7,08,958.70	41.72	1,71,036.49	11.19

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	329	5,41,128.98	6,68,709.03	4,69,321.34	70.20	1,27,580.05	23.60
Latest Approved (RCE)	271	4,00,629.50	4,67,778.41	3,44,273.43	73.60	67,148.91	16.80

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	61	88,427.97	95,502.76	68,546.57	71.80	7,074.79	8.00

Extent of cost overrun in projects with respect to original schedule (Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	3	841.67	1,238.96	47.20
3	COAL	87	85,632.34	85,544.13	-0.10	5	1,740.78	2,401.68	37.97
4	FERTILISERS	2	680.64	703.44	3.35	2	680.64	703.44	3.35
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	33	56,967.14	57,180.82	0.38	5	1,639.71	2,211.39	34.86
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
8	PETROLEUM	89	1,85,636.77	1,86,447.26	0.44	16	19,926.04	23,588.86	18.38
9	POWER	121	3,34,690.29	3,83,881.20	14.70	28	77,525.40	1,26,779.92	63.53
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
12	RAILWAYS	347	3,51,974.29	4,40,707.90	25.21	195	1,02,528.07	2,51,670.51	145.47
13	ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,96,459.23	1.51	26	10,168.08	14,892.59	46.46
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	5	1,205.50	2,172.77	80.24
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	1,40,978.94	1,49,046.42	5.72	3	6,986.35	15,234.21	118.06
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1201	15,28,249.27	16,99,285.76	11.19	293	2,47,280.55	4,83,357.63	95.47

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	54	94,347.36	98,047.72	3.92	7	2,289.68	6,870.97	200.08
2	ARUNACHAL PRADESH	20	13,401.94	29,214.96	117.99	5	9,616.85	25,429.87	164.43
3	ASSAM	50	39,028.48	57,069.66	46.23	16	20,421.11	38,638.86	89.21
4	BIHAR	75	67,446.38	80,514.59	19.38	15	13,203.03	26,617.48	101.60
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	0.00
6	GUJARAT	45	39,313.44	43,025.13	9.44	11	6,598.07	10,510.61	59.30
7	HARYANA	21	13,724.68	15,697.80	14.38	3	1,633.56	3,653.00	123.62
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	2	4,966.47	11,365.74	128.85
9	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	2	6,142.04	25,348.17	312.70
10	KARNATAKA	44	76,696.44	94,581.65	23.32	20	15,069.07	34,118.06	126.41
11	KERALA	19	33,504.08	35,120.13	4.82	6	2,117.36	3,733.41	76.32
12	MADHYA PRADESH	52	53,511.21	57,894.21	8.19	7	4,634.35	9,025.89	94.76
13	MAHARASHTRA	100	1,61,202.70	1,70,218.50	5.59	21	25,584.98	37,864.07	47.99
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	1227.45
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	5	2,001.20	6,965.67	248.07	2	988.06	5,952.53	502.45
17	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
18	ODISHA	66	70,255.03	77,749.09	10.67	19	5,832.84	13,375.95	129.32
19	PUNJAB	26	14,507.23	14,511.23	0.03	1	573.96	605.00	5.41
20	RAJASTHAN	65	45,091.11	46,852.62	3.91	14	5,177.36	6,938.87	34.02
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	181.28
22	TAMIL NADU	48	69,394.91	84,085.18	21.17	14	21,296.34	36,735.72	72.50
23	TRIPURA	11	4,400.64	9,459.94	114.97	7	2,909.18	7,968.48	173.91
24	UTTAR PRADESH	79	1,02,641.68	1,06,041.58	3.31	9	3,695.80	7,095.70	91.99
25	WEST BENGAL	53	54,854.77	65,429.70	19.28	18	11,614.34	24,286.59	109.11
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
27	DELHI	17	50,925.07	50,831.89	-0.18	2	353.35	406.17	14.95
28	CHHATISGARH	42	97,016.69	1,00,033.44	3.11	9	9,008.64	12,025.39	33.49
29	JHARKHAND	46	46,319.35	49,550.69	6.98	8	8,623.19	11,854.53	37.47
30	UTTARAKHAND	11	16,558.99	18,940.91	14.38	4	4,997.76	7,380.19	47.67
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	40.28
32	TELANGANA	34	24,623.00	27,006.92	9.68	8	2,623.87	5,096.00	94.22
33	MULTI STATE	168	2,70,141.26	2,51,399.99	-6.94	57	49,685.16	86,722.83	74.54
Total		1201	15,28,249.27	16,99,285.76	11.19	293	2,47,280.55	4,83,357.63	95.47

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	4	40,442.00	52,241.00	47 - 98
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	2	624.07	994.86	21 - 83
3	COAL	87	85,632.34	85,544.13	-0.10	39	20,323.21	20,235.00	6 - 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	10 - 10
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	33	56,967.14	57,180.82	0.38	14	39,587.34	39,814.56	3 - 51
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	89	1,85,636.77	1,86,447.26	0.44	36	48,623.45	48,918.77	1 - 71
9	POWER	121	3,34,690.29	3,83,881.20	14.70	60	1,94,433.24	2,26,076.70	3 - 134
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	3	666.99	666.99	1 - 2
12	RAILWAYS	347	3,51,974.29	4,40,707.90	25.21	39	41,337.66	1,10,020.72	11 - 261
13	ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,96,459.23	1.51	108	85,025.35	89,137.26	1 - 114
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	1	366.39	669.46	96 - 96
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	2	15,445.17	15,345.17	26 - 30
16	URBAN DEVELOPMENT	31	1,40,978.94	1,49,046.42	5.72	19	52,338.32	60,551.80	3 - 70
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1201	15,28,249.27	16,99,285.76	11.19	329	5,41,128.98	6,68,709.03	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	54	94,347.36	98,047.72	3.92	14	7,149.07	9,187.71	3 - 144
2	ARUNACHAL PRADESH	20	13,401.94	29,214.96	117.99	2	3,070.89	7,517.72	45 - 94
3	ASSAM	50	39,028.48	57,069.66	46.23	20	13,935.84	26,113.65	15 - 122
4	BIHAR	75	67,446.38	80,514.59	19.38	12	32,270.88	38,673.58	1 - 88
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	-
6	GUJARAT	45	39,313.44	43,025.13	9.44	14	22,318.48	23,923.31	6 - 84
7	HARYANA	21	13,724.68	15,697.80	14.38	5	3,130.20	4,310.20	24 - 82
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	3	6,107.21	10,586.37	15 - 111
9	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	7	21,314.62	40,520.75	20 - 193
10	KARNATAKA	44	76,696.44	94,581.65	23.32	6	49,946.13	57,956.14	6 - 70
11	KERALA	19	33,504.08	35,120.13	4.82	5	1,727.29	1,834.48	6 - 55
12	MADHYA PRADESH	52	53,511.21	57,894.21	8.19	9	5,189.43	6,249.53	5 - 87
13	MAHARASHTRA	100	1,61,202.70	1,70,218.50	5.59	26	54,111.28	58,925.62	5 - 258
14	MANIPUR	2	944.25	9,874.69	945.77	2	944.25	9,874.69	33 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	536.00	536.00	41 - 41
16	MIZORAM	5	2,001.20	6,965.67	248.07	2	988.06	5,952.53	71 - 134
17	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
18	ODISHA	66	70,255.03	77,749.09	10.67	21	10,474.51	11,905.39	5 - 108
19	PUNJAB	26	14,507.23	14,511.23	0.03	3	1,359.14	1,359.14	3 - 16
20	RAJASTHAN	65	45,091.11	46,852.62	3.91	13	19,245.95	19,446.99	7 - 87
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	51 - 83
22	TAMIL NADU	48	69,394.91	84,085.18	21.17	18	50,869.35	62,327.27	1 - 118
23	TRIPURA	11	4,400.64	9,459.94	114.97	4	1,341.17	4,060.65	3 - 72
24	UTTAR PRADESH	79	1,02,641.68	1,06,041.58	3.31	14	21,308.86	22,565.39	3 - 84
25	WEST BENGAL	53	54,854.77	65,429.70	19.28	15	26,518.30	25,368.98	2 - 75
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
27	DELHI	17	50,925.07	50,831.89	-0.18	4	2,122.31	2,122.31	1 - 27
28	CHHATISGARH	42	97,016.69	1,00,033.44	3.11	15	62,311.05	64,317.05	3 - 93
29	JHARKHAND	46	46,319.35	49,550.69	6.98	22	26,600.00	28,935.78	5 - 166
30	UTTARAKHAND	11	16,558.99	18,940.91	14.38	4	7,605.57	9,794.74	43 - 78
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	34	24,623.00	27,006.92	9.68	13	5,476.78	5,787.12	6 - 132
33	MULTI STATE	168	2,70,141.26	2,51,399.99	-6.94	51	80,342.81	1,00,476.39	3 - 261
Total		1201	15,28,249.27	16,99,285.76	11.19	329	5,41,128.98	6,68,709.03	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	4	40,442.00	52,241.00	47 - 98
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	2	624.07	994.86	21 - 83
3	COAL	87	85,632.34	85,544.13	-0.10	34	12,181.35	12,307.92	6 - 132
4	FERTILISERS	2	680.64	703.44	3.35	0	0.00	0.00	-
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	-
6	STEEL	33	56,967.14	57,180.82	0.38	12	23,886.85	24,082.85	3 - 51
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
8	PETROLEUM	89	1,85,636.77	1,86,447.26	0.44	10	5,730.17	6,031.12	1 - 41
9	POWER	121	3,34,690.29	3,83,881.20	14.70	47	1,08,022.57	1,20,636.57	3 - 118
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	3	666.99	666.99	1 - 2
12	RAILWAYS	347	3,51,974.29	4,40,707.90	25.21	34	35,633.78	94,326.00	0 - 261
13	ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,96,459.23	1.51	108	85,025.35	89,137.26	1 - 114
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	1	2,111.17	2,011.17	30 - 30
16	URBAN DEVELOPMENT	31	1,40,978.94	1,49,046.42	5.72	14	50,966.89	59,072.37	3 - 70
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1201	15,28,249.27	16,99,285.76	11.19	270	3,67,009.19	4,65,335.41	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	2	22,947.00	28,462.00	24.03
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	3	841.67	1,238.96	47.20
3	COAL	87	85,417.56	85,544.13	0.15	3	1,328.95	1,455.52	9.52
4	FERTILISERS	2	703.44	703.44	0.00	0	0.00	0.00	0.00
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0.00
6	STEEL	33	57,348.11	57,180.82	-0.29	3	1,586.97	1,777.68	12.02
7	PETROCHEMICALS	1	9,965.00	9,965.00	0.00	0	0.00	0.00	0.00
8	PETROLEUM	89	1,86,788.89	1,86,447.26	-0.18	4	4,166.57	5,731.47	37.56
9	POWER	121	3,68,166.09	3,83,881.20	4.27	6	27,068.67	45,428.78	67.83
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	1	196.70	209.00	6.25
12	RAILWAYS	347	3,92,738.06	4,40,707.90	12.21	155	1,06,373.10	2,10,422.08	97.82
13	ROAD TRANSPORT AND HIGHWAYS	451	2,93,990.78	2,96,459.23	0.84	16	8,945.86	11,935.63	33.42
14	SHIPPING AND PORTS	8	4,434.32	5,085.02	14.67	4	852.61	1,503.31	76.32
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	31	1,49,192.42	1,49,046.42	-0.10	0	0.00	0.00	0.00
17	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1201	16,25,094.09	16,99,285.76	4.57	198	1,76,026.10	3,11,991.73	77.24

[^] - Cost Overrun = Anticipated Cost minus Latest Approved Cost.

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	85- 98
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	2	624.07	994.86	21- 83
3	COAL	87	85,632.34	85,544.13	-0.10	3	1,328.95	1,455.52	24- 132
4	FERTILISERS	2	680.64	703.44	3.35	0	0.00	0.00	0- 0
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	33	56,967.14	57,180.82	0.38	2	492.73	664.34	14- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	89	1,85,636.77	1,86,447.26	0.44	0	0.00	0.00	0- 0
9	POWER	121	3,34,690.29	3,83,881.20	14.70	3	9,874.63	18,548.56	24- 111
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
12	RAILWAYS	347	3,51,974.29	4,40,707.90	25.21	21	16,096.94	73,232.90	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,96,459.23	1.51	9	5,952.95	9,972.54	16- 99
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	1,40,978.94	1,49,046.42	5.72	0	0.00	0.00	0- 0
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1201	15,28,249.27	16,99,285.76	11.19	43	52,751.27	1,37,158.02	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	85- 98
2	CIVIL AVIATION	4	1,177.28	1,556.96	32.25	2	624.07	994.86	21- 83
3	COAL	87	85,632.34	85,544.13	-0.10	5	1,740.78	2,401.68	24- 132
4	FERTILISERS	2	680.64	703.44	3.35	1	197.79	209.44	10- 10
5	MINES	4	6,773.63	6,773.63	0.00	0	0.00	0.00	0- 0
6	STEEL	33	56,967.14	57,180.82	0.38	4	870.83	1,098.05	3- 15
7	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
8	PETROLEUM	89	1,85,636.77	1,86,447.26	0.44	11	15,547.82	17,745.69	5- 70
9	POWER	121	3,34,690.29	3,83,881.20	14.70	22	59,944.79	91,651.86	24- 134
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	HEALTH AND FAMILY WELFARE	13	3,637.08	3,649.38	0.34	0	0.00	0.00	0- 0
12	RAILWAYS	347	3,51,974.29	4,40,707.90	25.21	29	25,134.44	94,733.90	21- 261
13	ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,96,459.23	1.51	14	7,016.33	11,129.10	9- 99
14	SHIPPING AND PORTS	8	4,117.75	5,085.02	23.49	1	366.39	669.46	96- 96
15	TELECOMMUNICATIONS	3	15,863.43	15,763.43	-0.63	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	31	1,40,978.94	1,49,046.42	5.72	3	6,986.35	15,234.21	21- 70
17	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1201	15,28,249.27	16,99,285.76	11.19	95	1,36,810.59	2,68,157.55	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

State-Wise Position of Central Sector Projects costing Rs. 150 crore and above showing Both Time and Cost Overruns

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	54	94,347.36	98,047.72	3.92	3	1,241.74	3,280.38	14 - 144
2	ARUNACHAL PRADESH	20	13,401.94	29,214.96	117.99	2	3,070.89	7,517.72	45 - 94
3	ASSAM	50	39,028.48	57,069.66	46.23	10	9,674.41	21,957.93	26 - 122
4	BIHAR	75	67,446.38	80,514.59	19.38	1	8,692.97	15,095.67	88 - 88
5	GOA	10	4,379.12	4,361.51	-0.40	0	0.00	0.00	-
6	GUJARAT	45	39,313.44	43,025.13	9.44	2	1,827.34	3,559.49	54 - 84
7	HARYANA	21	13,724.68	15,697.80	14.38	1	1,108.00	2,288.00	69 - 69
8	HIMACHAL PRADESH	12	12,531.81	18,931.08	51.06	1	3,919.59	8,398.75	111 - 111
9	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	2	6,142.04	25,348.17	24 - 193
10	KARNATAKA	44	76,696.44	94,581.65	23.32	1	6,395.00	14,405.01	70 - 70
11	KERALA	19	33,504.08	35,120.13	4.82	1	607.06	714.25	10 - 10
12	MADHYA PRADESH	52	53,511.21	57,894.21	8.19	4	3,176.60	4,244.44	16 - 87
13	MAHARASHTRA	100	1,61,202.70	1,70,218.50	5.59	10	16,369.54	22,328.58	10 - 258
14	MANIPUR	2	944.25	9,874.69	945.77	1	727.56	9,658.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	5	2,001.20	6,965.67	248.07	2	988.06	5,952.53	71 - 134
17	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
18	ODISHA	66	70,255.03	77,749.09	10.67	8	1,808.10	3,239.33	9 - 96
19	PUNJAB	26	14,507.23	14,511.23	0.03	0	0.00	0.00	-
20	RAJASTHAN	65	45,091.11	46,852.62	3.91	4	1,588.21	1,789.25	28 - 87
21	SIKKIM	5	2,149.08	5,138.08	139.08	2	1,648.94	4,638.22	51 - 83
22	TAMIL NADU	48	69,394.91	84,085.18	21.17	3	18,442.29	30,649.32	85 - 118
23	TRIPURA	11	4,400.64	9,459.94	114.97	4	1,341.17	4,060.65	3 - 72
24	UTTAR PRADESH	79	1,02,641.68	1,06,041.58	3.31	1	325.00	1,581.53	84 - 84
25	WEST BENGAL	53	54,854.77	65,429.70	19.28	0	0.00	0.00	-
26	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
27	DELHI	17	50,925.07	50,831.89	-0.18	0	0.00	0.00	-
28	CHHATISGARH	42	97,016.69	1,00,033.44	3.11	6	5,916.20	7,922.20	5 - 93
29	JHARKHAND	46	46,319.35	49,550.69	6.98	3	3,474.75	5,810.53	62 - 166
30	UTTARAKHAND	11	16,558.99	18,940.91	14.38	2	4,635.48	6,825.16	43 - 75
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
32	TELANGANA	34	24,623.00	27,006.92	9.68	3	1,482.10	1,792.44	21 - 132
33	MULTI STATE	168	2,70,141.26	2,51,399.99	-6.94	16	31,042.94	51,658.67	15 - 261
Total		1201	15,28,249.27	16,99,285.76	11.19	95	1,36,810.59	2,68,157.55	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

<u>List of projects completed/dropped/Frozen during current month</u>							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>MINES</u>						
1	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC	09/2011	1,856.00	09/2017	1,176.00	04/2020	32.18
	<u>PETROLEUM</u>						
2	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	N.A.	171.83	N.A.	0.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
3	SAMAIKHIALI - GANDHIDHAM PPP (BOT)	09/2010	805.39	03/2013	805.39	11/2016	1,408.40
	<u>URBAN DEVELOPMENT</u>						
4	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	05/2009	261.85	05/2013	261.85	12/2016	235.00

(All Cost in Rs. Crore)

List of projects added					(January 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	NEYVELI SOLAR POWER PROJECT 130 MW	5/2016	687.28	6/2017	687.28	6/2017
2	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	17,237.00	11/2021	17,237.00	11/2021
	<u>MINES</u>					
3	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	5,540.00	4/2021	5,540.00	4/2021
4	UTKAL D AND E COAL MINE PROJECT	5/2016	534.00	1/2020	534.00	1/2020
	<u>PETROLEUM</u>					
5	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY	7/2015	822.66	11/2018	822.66	11/2018
6	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	1,945.00	/	1,945.00	-
7	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	151.00	/	151.00	-
8	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	1,021.00	/	1,021.00	-
9	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	4,497.00	/	4,497.00	-
10	BSVI UP GRADATION	9/2016	1,810.00	12/2019	1,810.00	12/2019
11	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	135.00	3/2019	170.70	3/2019
12	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	224.00	4/2019	207.25	4/2019
13	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	324.00	/	324.00	-
14	BRANCH PIPELINE FROM PATNA TO MOTIHARI & BAITALPUR ON BKPL	5/2016	664.00	/	664.00	-
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
15	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	450.68	/	450.68	-
16	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	1,251.11	/	1,251.11	-
17	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	244.90	/	244.90	-

List of projects added					(January 2017)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>TELECOMMUNICATIONS</u>					
18	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	418.26	6/2017	418.26	6/2017
	<u>URBAN DEVELOPMENT</u>					
19	CONSTRUCTION OC 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY EPC	5/2011	164.00	1/2018	164.00	1/2018
20	CONSTRUCTION OF 1003 NOS (900 NOS TYPE II 54 NOS TYPE III 33 NOS TYPE IV 16 NOS TYPE V) FAMILY QUAR	5/2016	164.30	1/2018	164.30	1/2018

Milestones (Cumulative due & achieved)

Total	3875
Achieved up to month	1946

List of projects reporting additional delays (January 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI	309.46	553.53	01/2011	09/2017	12/2017	3
	<u>COAL</u>						
2	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU NLC	364.75	364.75	10/2014	01/2017	06/2017	5
3	RAJMAHAL OC EXP. ECL	153.82	153.82	03/2014	03/2017	12/2017	9
4	MURAI DIH UG TURN-KEY PROJECT BCCL	339.88	339.88	04/2014	03/2017	10/2018	19
5	CHURI BENTI UG (0.81 MTY) CCL	163.51	163.51	03/2011	03/2018	03/2020	24
6	NORTH URIMARI OCP (3.0 MTY) CCL	179.87	179.87	03/2012	03/2017	03/2019	24
7	KARMA OCP (1.0MTY) CCL	162.46	162.46	03/2014	03/2017	03/2019	24
	<u>STEEL</u>						
8	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT SAIL	1,154.18	1,154.18	12/2017	12/2017	05/2018	5
9	REBUILDING OF COB-7 AT BSL SAIL	245.67	245.67	05/2016	03/2017	10/2017	7
10	NEW SINTER PLANT AT BOKARO STEEL PLANT SAIL	1,034.01	1,034.01	10/2017	10/2017	07/2018	9
	<u>PETROLEUM</u>						
11	RESID UPGRADATION PROJECT CPCL	3,110.36	3,110.36	11/2015	02/2017	03/2017	1
12	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY IOCL	3,076.00	3,076.00	09/2017	03/2018	06/2018	3
13	LPG TERMINAL AT KOCHI IOCL	607.06	714.25	10/2017	02/2018	08/2018	6
14	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY IOCL	931.00	931.00	07/2017	07/2017	02/2018	7
15	POLYPROPYLENE PLANT AT PARADIP REFINERY IOCL	3,150.00	3,150.00	09/2017	03/2018	12/2018	9

List of projects reporting additional delays (January 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>POWER</u>						
16	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV PGCIL	723.63	723.63	11/2014	05/2017	06/2017	1
17	MOUDA STPP STAGE 2 NTPC	7,921.47	7,921.47	09/2016	01/2017	02/2017	1
18	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B PGCIL	155.57	155.57	03/2016	05/2017	06/2017	1
19	BOKARO THERMAL POWER STATION-A DVC	2,313.00	4,366.64	12/2011	01/2017	02/2017	1
20	EASTERN REGION STRENGTHENING SCHEME-III PGCIL	1,272.80	1,731.10	11/2012	10/2017	12/2017	2
21	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	9,569.76	9,569.76	06/2015	04/2017	06/2017	2
22	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 PGCIL	378.71	378.71	10/2016	02/2017	04/2017	2
23	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,187.32	11/2008	06/2018	09/2018	3
24	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION PGCIL	303.07	303.07	07/2016	03/2017	06/2017	3
25	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	522.29	11/2016	03/2017	06/2017	3
26	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E PGCIL	972.42	972.42	11/2017	01/2017	04/2017	3
27	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII PGCIL	908.08	908.08	06/2016	05/2017	09/2017	4
28	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. PGCIL	2,144.00	2,932.88	12/2012	09/2017	02/2018	5
29	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID PGCIL	288.49	288.49	02/2017	04/2017	09/2017	5
30	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	738.48	09/2010	06/2017	12/2017	6
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	06/2017	12/2017	6
32	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH PGCIL	1,746.65	2,228.71	08/2014	06/2017	12/2017	6


List of projects reporting additional delays							
(January 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
33	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	2,514.88	12/2015	06/2017	12/2017	6
34	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	5,071.94	10/2012	06/2017	02/2018	8
35	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) PGCIL	305.04	305.04	03/2017	03/2017	12/2017	9
36	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C PGCIL	514.20	514.20	06/2015	01/2017	12/2017	11
37	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A PGCIL	1,479.30	1,479.30	04/2017	04/2017	12/2018	20
	<u>HEALTH AND FAMILY WELFARE</u>						
38	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK HSCC	444.70	444.70	12/2015	06/2016	07/2016	1
	<u>RAILWAYS</u>						
39	HATHUA-BHATNI (N L) (NER) NER	230.03	230.03	N.A.	02/2017	03/2017	1
40	NEW BG LINE FROM BYRNIHAT TO SHILLONG NFR	4,083.02	6,000.00	N.A.	03/2020	03/2021	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
41	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	01/2017	02/2017	1
42	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 NHAI	563.92	563.92	11/2016	04/2017	05/2017	1
43	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	01/2017	03/2017	2
44	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	309.56	04/2010	12/2016	02/2017	2
45	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI PPP (BOT)	852.00	852.00	03/2013	02/2017	04/2017	2
46	2 LANNING OF MOKAMA-MUNGER NHAI PPP (ANNUITY)	351.54	351.54	05/2013	12/2016	02/2017	2
47	KANDLA - MUNDRA PORT NHAI PPP (BOT)	953.88	953.88	07/2013	02/2017	04/2017	2
48	AHMEDABAD TO VADODARA SECTION NHAI PPP (BOT)	2,125.24	2,125.24	12/2015	12/2016	02/2017	2
49	2-LANING WITH PS BHILWARA-LODPURA SECTION NHAI	240.10	240.10	03/2016	01/2017	03/2017	2

List of projects reporting additional delays							
(January 2017)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
50	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 NHAI	197.69	197.69	N.A.	05/2018	07/2018	2
51	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 NHAI	244.00	244.00	N.A.	05/2018	07/2018	2
52	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 NHAI PPP (BOT)	1,693.75	1,693.75	08/2011	12/2016	03/2017	3
53	FOUR LANING OF CHANDIGARH - KHARAR NHAI	447.29	447.29	12/2017	12/2018	04/2019	4
54	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR NHAI	563.92	563.92	12/2017	12/2017	06/2018	6
55	KRISHNANAGAR-BERHAMPUR NHAI PPP (ANNUITY)	702.16	702.16	07/2014	02/2017	09/2017	7
56	RANCHI-RARGA-JAMSETHPUR NHAI PPP (ANNUITY)	1,479.00	1,479.00	06/2015	05/2017	12/2017	7
57	PATNA-MUZZAFFARPUR NHAI PPP (ANNUITY)	671.30	671.30	02/2013	12/2016	09/2017	9
58	4-LANNING OF CHAPRA-HAJIPUR NHAI PPP (ANNUITY)	575.00	575.00	07/2013	12/2016	09/2017	9
59	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	06/2016	06/2017	12
	<u>URBAN DEVELOPMENT</u>						
60	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA CPWD	205.00	170.62	03/2012	03/2017	10/2017	7
61	CHENNAI METRO RAIL LTD (PHASE 1) CMRL	14,600.00	14,600.00	12/2015	08/2016	12/2017	16

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	467,26.00	52,241.00	43,936.82
CIVIL AVIATION	4	1,177.28	11,77.28	1,556.96	909.38
COAL	87	85,632.34	854,17.56	85,544.13	16,510.71
FERTILISERS	2	680.64	7,03.44	703.44	141.17
MINES	4	6,773.63	67,73.63	6,773.63	606.08
STEEL	33	56,967.14	573,48.11	57,180.82	35,073.50
PETROCHEMICALS	1	5,460.61	99,65.00	9,965.00	9,895.57
PETROLEUM	89	1,85,636.77	1,867,88.89	1,86,447.26	54,194.71
POWER	121	3,34,690.29	3,681,66.09	3,83,881.20	2,14,784.64
HEAVY INDUSTRY	1	1,718.00	17,18.00	3,827.30	2,289.00
HEALTH AND FAMILY WELFARE	13	3,637.08	36,37.08	3,649.38	1,569.94
RAILWAYS	347	3,51,974.29	3,927,38.06	4,40,707.90	1,29,314.65
ROAD TRANSPORT AND HIGHWAYS	451	2,92,045.44	2,939,90.78	2,96,459.23	1,29,331.46
SHIPPING AND PORTS	8	4,117.75	44,34.32	5,085.02	2,122.39
TELECOMMUNICATIONS	3	15,863.43	158,63.43	15,763.43	5,533.11
URBAN DEVELOPMENT	31	1,40,978.94	1,491,92.42	1,49,046.42	62,722.90
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	22.67
Grand total	1201	15,28,249.27	16,25,094.09	16,99,285.76	7,08,958.70

SECTORWISE SUMMARY OF MEGA PROJECTS **(Costing Rs 1000 crore & above)**

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	124	1
2	ROAD TRANSPORT AND HIGHWAYS	87	3
3	POWER	64	10
4	PETROLEUM	37	3
5	COAL	12	0
6	URBAN DEVELOPMENT	10	1
7	STEEL	9	2
8	ATOMIC ENERGY	4	0
9	TELECOMMUNICATIONS	2	0
10	MINES	1	0
11	PETROCHEMICALS	1	0
12	HEAVY INDUSTRY	1	0
13	SHIPPING AND PORTS	1	0
	Total	353	20

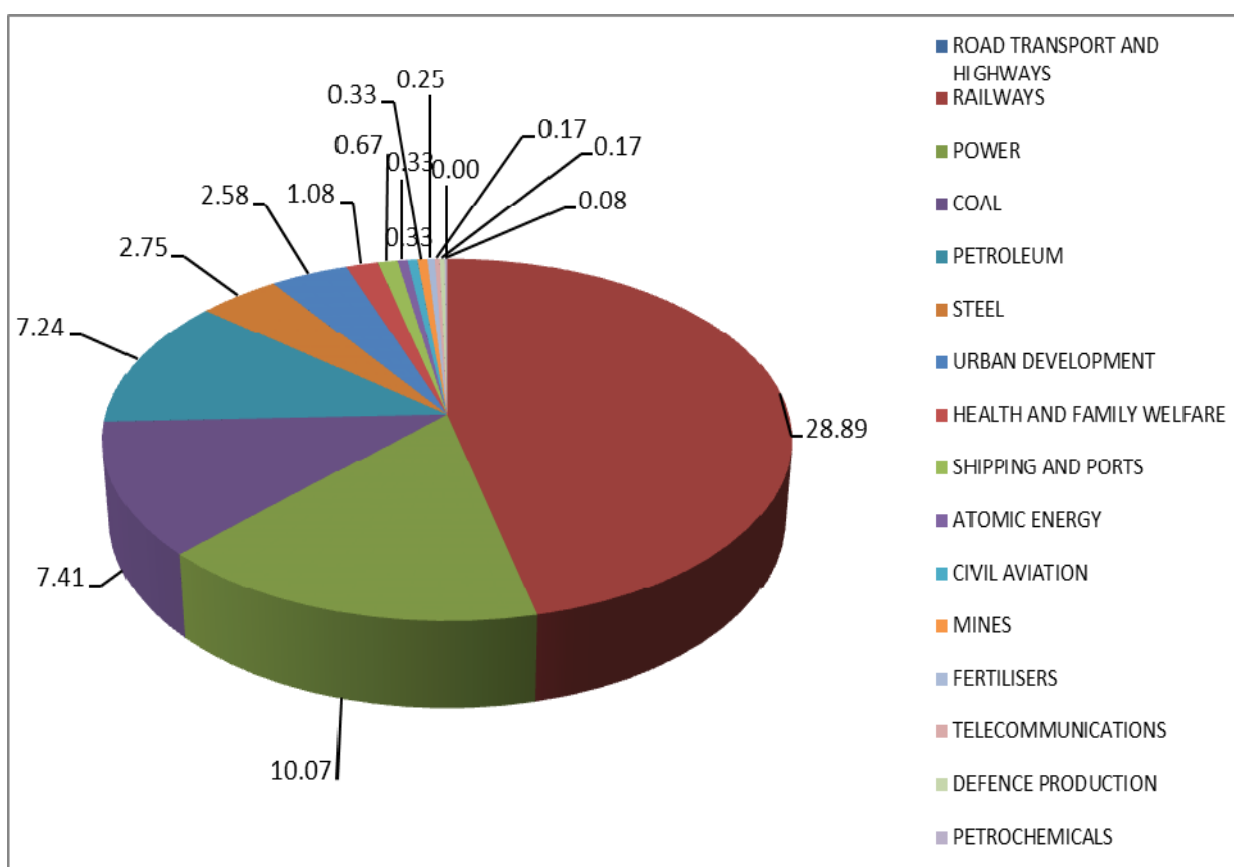

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	343
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects added in Current Month	7
No of Projects elevated to the status of Mega Projects	4
No of Projects in Current Month	353

Project status						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	127 (35.98%)	2 (.57%)	76 (21.53%)	49 (13.88%)	99 (28.05%)	353
Latest Approved (Date)	99 (28.05%)	1 (.28%)	125 (35.41%)	29 (8.22%)	99 (28.05%)	353

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	265	9,75,747.46	10,09,267.67	3,78,104.21	37.50	33,520.21	3.40
Project with Revision in Cost	88	2,90,550.71	3,13,865.64	2,06,094.90	65.70	23,314.93	8.00
Total	353	12,66,298.17	13,23,133.31	5,84,199.11	44.15	56,835.14	4.49
Original Cost of All Projects							
Original Cost	353	11,79,239.09	13,23,133.31	5,84,199.11	44.15	1,43,894.22	12.20

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	127	4,59,601.40	5,82,812.99	4,10,634.96	70.50	1,23,211.59	26.80
Latest Approved (RCE)	99	3,30,488.68	3,95,474.75	2,92,684.68	74.00	64,986.07	19.70

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	20	71,070.83	77,426.54	56,114.51	72.50	6,355.71	8.90

Extent of cost overrun in mega projects with respect to original schedule (Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	70.81
2	COAL	12	55,807.73	55,807.73	0.00	0	0.00	0.00	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,164.22	48,150.68	-0.03	1	768.88	1,113.34	44.80
5	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	1	5,460.61	9,965.00	82.49
6	PETROLEUM	37	1,63,425.41	1,64,217.77	0.48	8	17,200.81	20,099.33	16.85
7	POWER	64	3,10,182.04	3,58,917.34	15.71	24	75,710.45	1,24,445.75	64.37
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
9	RAILWAYS	124	2,67,244.11	3,31,960.87	24.22	73	66,397.99	1,88,933.42	184.55
10	ROAD TRANSPORT AND HIGHWAYS	87	1,27,988.26	1,31,474.90	2.72	4	4,847.10	8,333.74	71.93
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	10	1,35,394.14	1,43,258.15	5.81	1	6,395.00	14,405.01	125.25
Total		353	11,79,239.09	13,23,133.31	12.20	115	1,95,161.84	3,99,584.89	104.75

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Extent of cost overrun in mega projects with respect to original schedule (State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	15	81,246.20	83,396.38	2.65	2	1,073.00	3,950.18	268.14
2	ARUNACHAL PRADESH	3	9,356.22	24,952.87	166.70	3	9,356.22	24,952.87	166.70
3	ASSAM	10	26,494.46	42,658.76	61.01	6	18,183.62	34,434.18	89.37
4	BIHAR	14	41,018.97	52,350.17	27.62	5	10,666.26	21,997.46	106.23
5	GUJARAT	10	23,129.07	25,658.99	10.94	3	3,626.32	6,156.24	69.77
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	2	4,966.47	11,365.74	128.85
8	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	2	6,142.04	25,348.17	312.70
9	KARNATAKA	19	64,551.91	81,159.34	25.73	10	11,268.95	28,635.38	154.11
10	KERALA	5	27,824.08	28,840.08	3.65	1	550.00	1,566.00	184.73
11	MADHYA PRADESH	13	34,706.96	38,608.53	11.24	5	3,687.75	7,589.32	105.80
12	MAHARASHTRA	40	1,35,688.04	1,43,802.40	5.98	12	22,396.31	33,013.10	47.40
13	MANIPUR	1	727.56	9,658.00	1227.45	1	727.56	9,658.00	1227.45
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	2	988.06	5,952.53	502.45	2	988.06	5,952.53	502.45
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	22	52,872.91	59,328.36	12.21	5	2,445.13	8,900.58	264.01
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	6	18,795.04	18,795.04	0.00	0	0.00	0.00	0.00
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	12	54,400.40	67,268.43	23.65	4	19,281.29	32,149.32	66.74
22	TRIPURA	3	2,129.35	6,386.31	199.92	3	2,129.35	6,386.31	199.92
23	UTTAR PRADESH	29	79,695.68	82,189.63	3.13	3	1,839.23	4,333.18	135.60
24	WEST BENGAL	21	42,248.95	50,670.49	19.93	6	8,544.64	18,693.83	118.78
25	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	0.00
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	0.00
27	CHHATISGARH	14	86,451.85	88,561.21	2.44	5	8,085.45	10,194.81	26.09
28	JHARKHAND	10	33,188.25	35,781.77	7.81	3	7,451.01	10,044.53	34.81
29	UTTARAKHAND	6	14,392.36	16,582.04	15.21	2	4,635.48	6,825.16	47.24
30	TELANGANA	6	14,904.53	16,572.01	11.19	2	502.99	2,170.47	331.51
31	MULTI STATE	60	2,24,201.30	2,00,281.44	-10.67	24	39,234.21	69,894.84	78.15
Total		353	11,79,239.09	13,23,133.31	12.20	115	1,95,161.84	3,99,584.89	104.75

[^] - Cost Overrun = Anticipated Cost minus Original Cost

Extent of time overrun in mega projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	4	40,442.00	52,241.00	47 - 98
2	COAL	12	55,807.73	55,807.73	0.00	3	8,192.43	8,192.43	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	4	34,978.19	34,978.19	5 - 51
5	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
6	PETROLEUM	37	1,63,425.41	1,64,217.77	0.48	13	39,413.09	39,679.95	9 - 71
7	POWER	64	3,10,182.04	3,58,917.34	15.71	39	1,85,241.95	2,16,486.80	3 - 134
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
9	RAILWAYS	124	2,67,244.11	3,31,960.87	24.22	23	34,267.90	1,00,662.83	27 - 261
10	ROAD TRANSPORT AND HIGHWAYS	87	1,27,988.26	1,31,474.90	2.72	34	51,283.32	54,769.96	6 - 71
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	2	15,445.17	15,345.17	26 - 30
13	URBAN DEVELOPMENT	10	1,35,394.14	1,43,258.15	5.81	4	48,619.35	56,629.36	5 - 70
Total		353	11,79,239.09	13,23,133.31	12.20	127	4,59,601.40	5,82,812.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in mega projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	15	81,246.20	83,396.38	2.65	2	2,328.00	3,410.00	49 - 144
2	ARUNACHAL PRADESH	3	9,356.22	24,952.87	166.70	2	3,070.89	7,517.72	45 - 94
3	ASSAM	10	26,494.46	42,658.76	61.01	5	10,888.16	22,328.07	26 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	3	27,010.57	33,413.27	5 - 88
5	GUJARAT	10	23,129.07	25,658.99	10.94	5	17,491.46	19,220.23	14 - 54
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	69 - 69
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	2	5,836.38	10,315.54	15 - 111
8	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	7	21,314.62	40,520.75	20 - 193
9	KARNATAKA	19	64,551.91	81,159.34	25.73	4	49,621.34	57,631.35	6 - 70
10	KERALA	5	27,824.08	28,840.08	3.65	0	0.00	0.00	-
11	MADHYA PRADESH	13	34,706.96	38,608.53	11.24	3	3,242.90	3,820.77	16 - 47
12	MAHARASHTRA	40	1,35,688.04	1,43,802.40	5.98	13	46,014.24	50,436.15	5 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,952.53	502.45	2	988.06	5,952.53	71 - 134
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	22	52,872.91	59,328.36	12.21	4	5,790.23	6,809.70	15 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	6	18,795.04	18,795.04	0.00	2	13,993.70	13,993.70	48 - 71
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	12	54,400.40	67,268.43	23.65	8	45,249.89	57,456.92	16 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	29	79,695.68	82,189.63	3.13	7	18,466.01	19,722.54	3 - 84
24	WEST BENGAL	21	42,248.95	50,670.49	19.93	8	22,750.71	21,665.80	6 - 57
25	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,316.73	-0.32	1	1,219.21	1,219.21	5 - 5
27	CHHATISGARH	14	86,451.85	88,561.21	2.44	8	60,734.77	62,161.16	3 - 51
28	JHARKHAND	10	33,188.25	35,781.77	7.81	7	22,477.09	24,756.57	5 - 99
29	UTTARAKHAND	6	14,392.36	16,582.04	15.21	3	7,127.06	9,316.74	43 - 78
30	TELANGANA	6	14,904.53	16,572.01	11.19	1	1,266.60	1,266.60	6 - 6
31	MULTI STATE	60	2,24,201.30	2,00,281.44	-10.67	25	67,881.13	87,395.98	3 - 261
Total		353	11,79,239.09	13,23,133.31	12.20	127	4,59,601.40	5,82,812.99	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of time overrun in mega projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost Overrun^ (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	4	40,442.00	52,241.00	47 - 98
2	COAL	12	55,807.73	55,807.73	0.00	2	2,285.32	2,285.32	6 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	9	48,164.22	48,150.68	-0.03	3	19,453.19	19,453.19	5 - 51
5	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	-
6	PETROLEUM	37	1,63,425.41	1,64,217.77	0.48	1	3,110.36	3,110.36	16 - 16
7	POWER	64	3,10,182.04	3,58,917.34	15.71	26	98,831.28	1,11,046.67	3 - 118
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
9	RAILWAYS	124	2,67,244.11	3,31,960.87	24.22	22	29,682.94	87,657.42	0 - 261
10	ROAD TRANSPORT AND HIGHWAYS	87	1,27,988.26	1,31,474.90	2.72	34	51,283.32	54,769.96	6 - 71
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	1	2,111.17	2,011.17	30 - 30
13	URBAN DEVELOPMENT	10	1,35,394.14	1,43,258.15	5.81	4	48,619.35	56,629.36	5 - 70
Total		353	11,79,239.09	13,23,133.31	12.20	98	2,97,536.93	3,93,031.75	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Extent of cost overrun in mega projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.00	52,241.00	11.80	2	22,947.00	28,462.00	24.03
2	COAL	12	55,807.73	55,807.73	0.00	0	0.00	0.00	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	9	48,466.31	48,150.68	-0.65	1	1,070.97	1,113.34	3.96
5	PETROCHEMICALS	1	9,965.00	9,965.00	0.00	0	0.00	0.00	0.00
6	PETROLEUM	37	1,64,277.02	1,64,217.77	-0.04	3	3,959.57	5,524.22	39.52
7	POWER	64	3,43,202.72	3,58,917.34	4.58	5	26,766.67	45,126.29	68.59
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
9	RAILWAYS	124	3,00,056.97	3,31,960.87	10.63	54	73,211.14	1,60,120.69	118.71
10	ROAD TRANSPORT AND HIGHWAYS	87	1,29,261.70	1,31,474.90	1.71	4	6,120.54	8,333.74	36.16
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0.00
13	URBAN DEVELOPMENT	10	1,43,404.15	1,43,258.15	-0.10	0	0.00	0.00	0.00
Total		353	12,66,298.17	13,23,133.31	4.49	70	1,35,793.89	2,52,507.58	85.95

[^] - Cost Overrun = Anticipated Cost minus Latest Approved Cost

Extent of time & cost overrun in mega projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	85- 98
2	COAL	12	55,807.73	55,807.73	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
6	PETROLEUM	37	1,63,425.41	1,64,217.77	0.48	0	0.00	0.00	0- 0
7	POWER	64	3,10,182.04	3,58,917.34	15.71	3	9,874.63	18,548.56	24- 111
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
9	RAILWAYS	124	2,67,244.11	3,31,960.87	24.22	14	13,572.65	69,600.33	34- 261
10	ROAD TRANSPORT AND HIGHWAYS	87	1,27,988.26	1,31,474.90	2.72	4	4,847.10	8,333.74	16- 69
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	10	1,35,394.14	1,43,258.15	5.81	0	0.00	0.00	0- 0
Total		353	11,79,239.09	13,23,133.31	12.20	24	46,675.38	1,28,771.93	

\$- Time overrun = Anticipated Date of Commissioning minus latest schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus latest approved Cost

Extent of time & cost overrun in mega projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	52,241.00	29.18	2	16,663.00	28,462.00	85- 98
2	COAL	12	55,807.73	55,807.73	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	9	48,164.22	48,150.68	-0.03	0	0.00	0.00	0- 0
5	PETROCHEMICALS	1	5,460.61	9,965.00	82.49	0	0.00	0.00	0- 0
6	PETROLEUM	37	1,63,425.41	1,64,217.77	0.48	5	13,623.59	15,195.11	12- 48
7	POWER	64	3,10,182.04	3,58,917.34	15.71	19	58,682.28	89,927.13	24- 134
8	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
9	RAILWAYS	124	2,67,244.11	3,31,960.87	24.22	19	21,138.21	88,618.05	34- 261
10	ROAD TRANSPORT AND HIGHWAYS	87	1,27,988.26	1,31,474.90	2.72	4	4,847.10	8,333.74	16- 69
11	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
12	TELECOMMUNICATIONS	2	15,445.17	15,345.17	-0.65	0	0.00	0.00	0- 0
13	URBAN DEVELOPMENT	10	1,35,394.14	1,43,258.15	5.81	1	6,395.00	14,405.01	70- 70
Total		353	11,79,239.09	13,23,133.31	12.20	51	1,23,067.18	2,48,768.34	

\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

State-Wise Position of Central Sector Projects costing Rs.1000 crore and above showing Both Time and Cost Overruns


(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost Overrun^ (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	15	81,246.20	83,396.38	2.65	1	743.00	1,825.00	144 - 144
2	ARUNACHAL PRADESH	3	9,356.22	24,952.87	166.70	2	3,070.89	7,517.72	45 - 94
3	ASSAM	10	26,494.46	42,658.76	61.01	4	8,423.01	19,949.18	26 - 122
4	BIHAR	14	41,018.97	52,350.17	27.62	1	8,692.97	15,095.67	88 - 88
5	GUJARAT	10	23,129.07	25,658.99	10.94	1	1,509.10	3,237.87	54 - 54
6	HARYANA	4	5,634.39	6,814.39	20.94	1	1,108.00	2,288.00	69 - 69
7	HIMACHAL PRADESH	5	9,740.15	16,139.42	65.70	1	3,919.59	8,398.75	111 - 111
8	JAMMU AND KASHMIR	10	27,408.66	46,614.79	70.07	2	6,142.04	25,348.17	24 - 193
9	KARNATAKA	19	64,551.91	81,159.34	25.73	1	6,395.00	14,405.01	70 - 70
10	KERALA	5	27,824.08	28,840.08	3.65	0	0.00	0.00	-
11	MADHYA PRADESH	13	34,706.96	38,608.53	11.24	2	2,230.00	2,807.87	16 - 47
12	MAHARASHTRA	40	1,35,688.04	1,43,802.40	5.98	5	14,423.33	19,503.64	12 - 192
13	MANIPUR	1	727.56	9,658.00	1,227.45	1	727.56	9,658.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	2	988.06	5,952.53	502.45	2	988.06	5,952.53	71 - 134
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	22	52,872.91	59,328.36	12.21	1	183.23	1,202.70	58 - 58
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	6	18,795.04	18,795.04	0.00	0	0.00	0.00	-
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	12	54,400.40	67,268.43	23.65	3	18,442.29	30,649.32	85 - 118
22	TRIPURA	3	2,129.35	6,386.31	199.92	1	813.34	3,451.00	72 - 72
23	UTTAR PRADESH	29	79,695.68	82,189.63	3.13	1	325.00	1,581.53	84 - 84
24	WEST BENGAL	21	42,248.95	50,670.49	19.93	0	0.00	0.00	-
25	D & N HAVELI	1	6,086.08	6,086.08	0.00	0	0.00	0.00	-
26	DELHI	4	45,462.73	45,316.73	-0.32	0	0.00	0.00	-
27	CHHATISGARH	14	86,451.85	88,561.21	2.44	3	5,297.01	6,723.40	26 - 40
28	JHARKHAND	10	33,188.25	35,781.77	7.81	2	3,213.05	5,492.53	62 - 99
29	UTTARAKHAND	6	14,392.36	16,582.04	15.21	2	4,635.48	6,825.16	43 - 75
30	TELANGANA	6	14,904.53	16,572.01	11.19	0	0.00	0.00	-
31	MULTI STATE	60	2,24,201.30	2,00,281.44	-10.67	12	29,595.75	49,770.60	20 - 261
	Total	353	11,79,239.09	13,23,133.31	12.20	51	1,23,067.18	2,48,768.34	


\$- Time overrun = Anticipated Date of Commissioning minus Original schedule Date of Commissioning

^ - Cost Overrun = Anticipated Cost minus Original Cost.

Graphical Presentation of All Projects w.r.t. Original Schedule

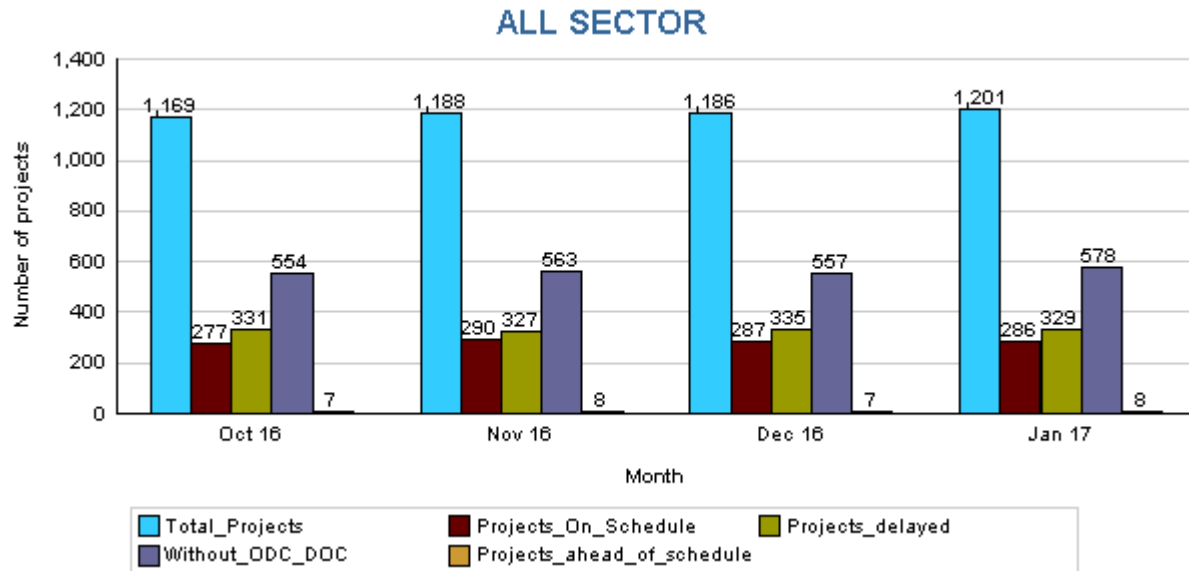


Break-up of 329 Delayed projects in January 2017

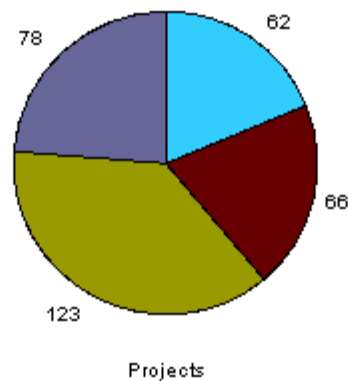


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

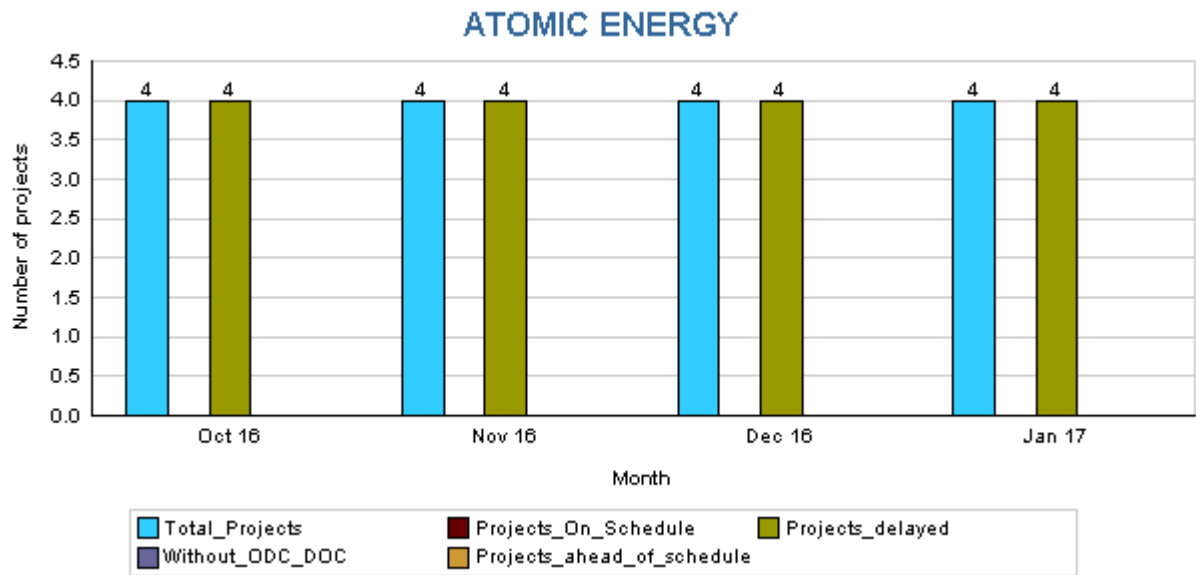


Break-up of 4 Delayed projects in January 2017

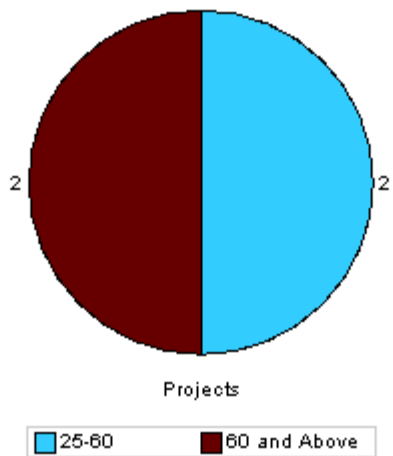


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

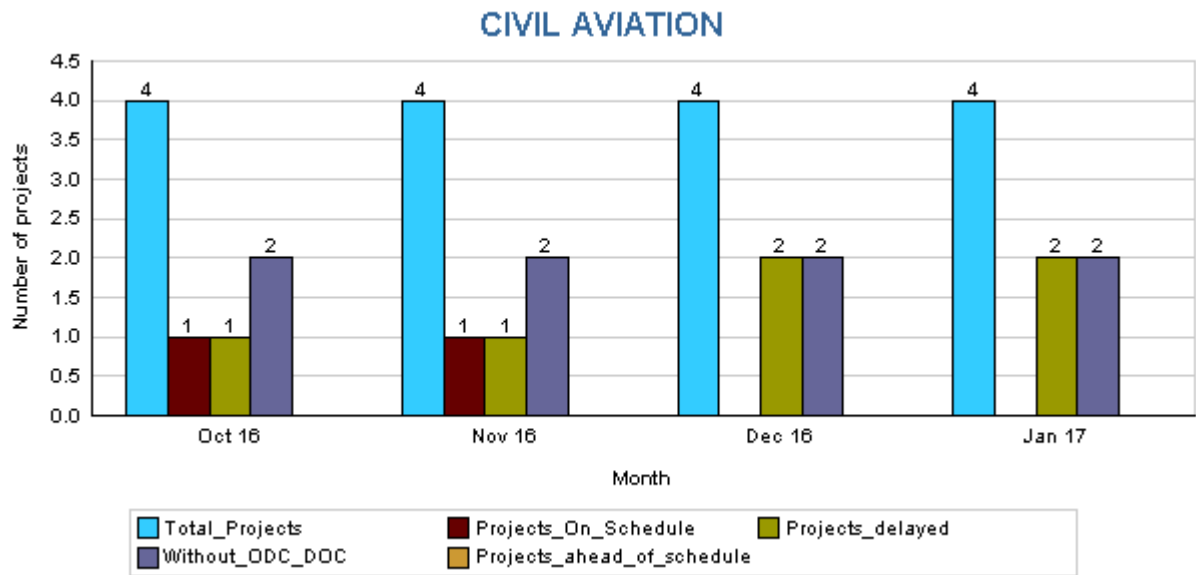


Break-up of 2 Delayed projects in January 2017

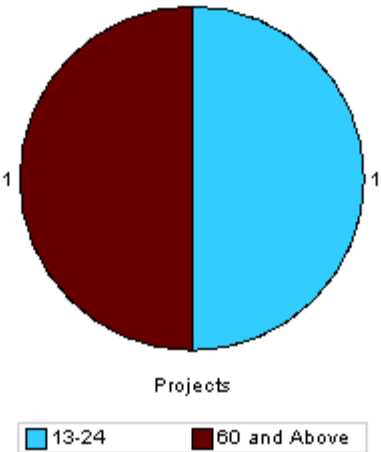


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

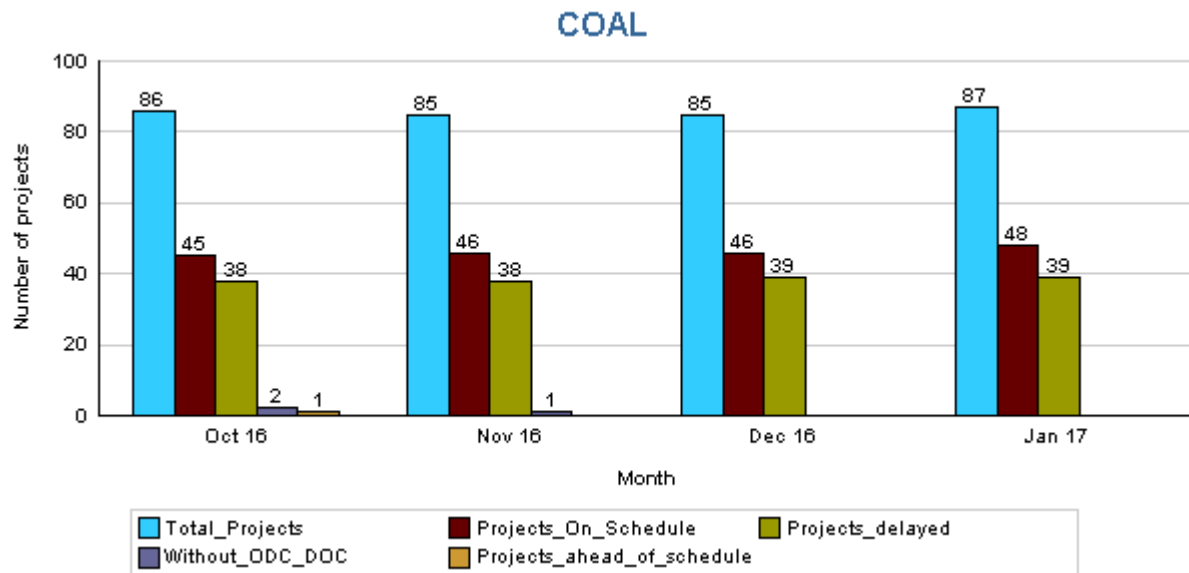


Break-up of 39 Delayed projects in January 2017

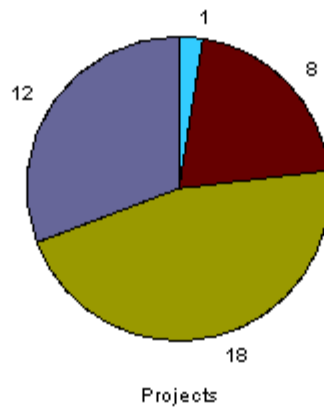


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

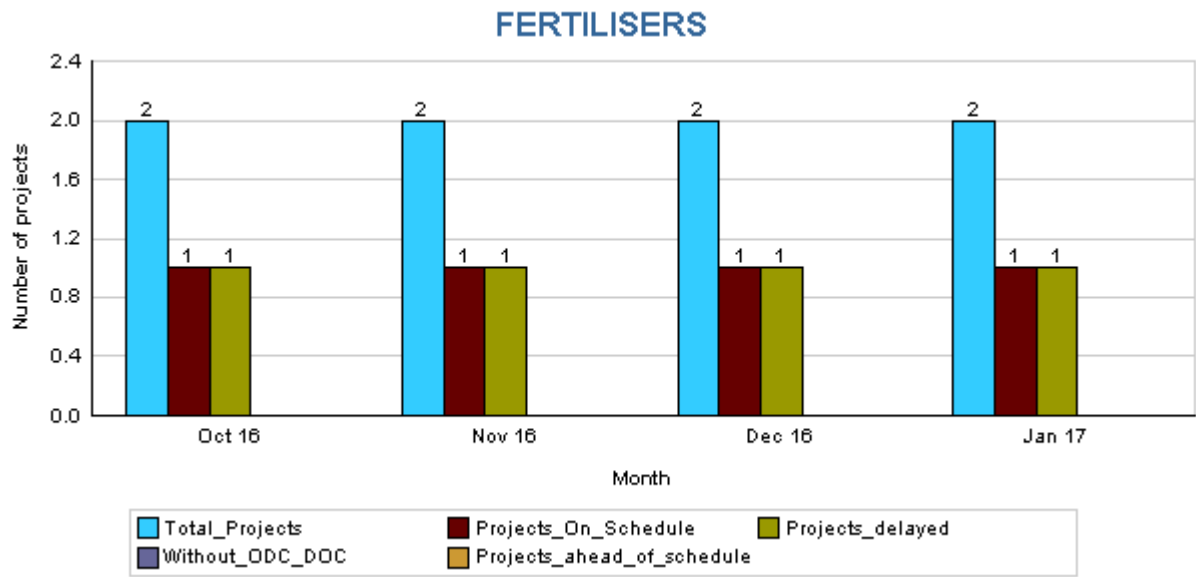


Break-up of 1 Delayed projects in January 2017

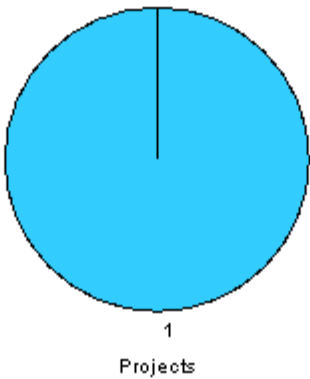

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

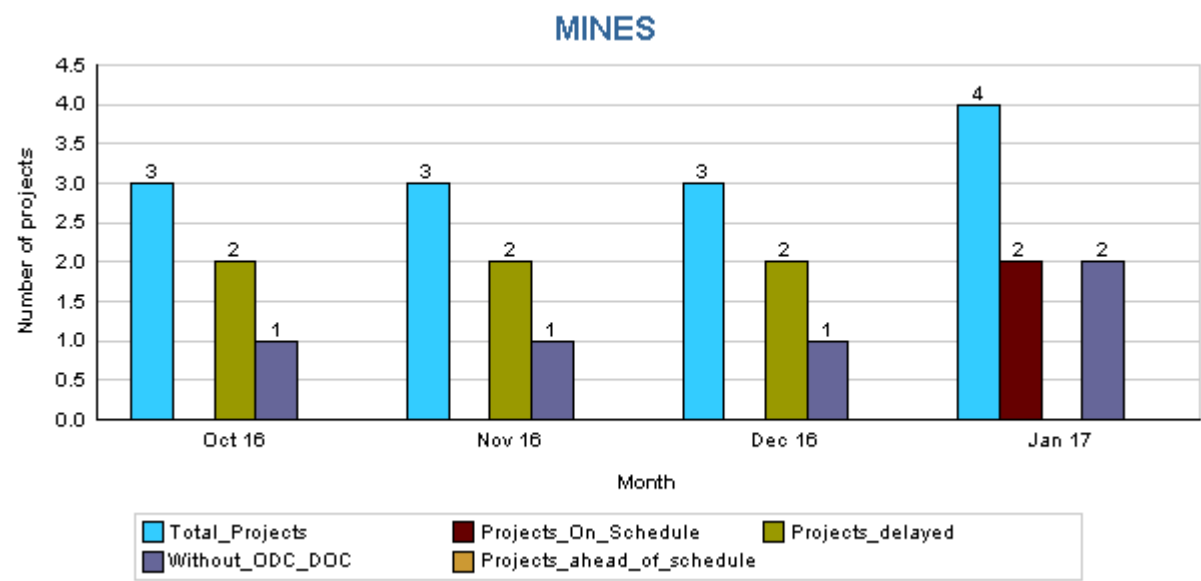


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

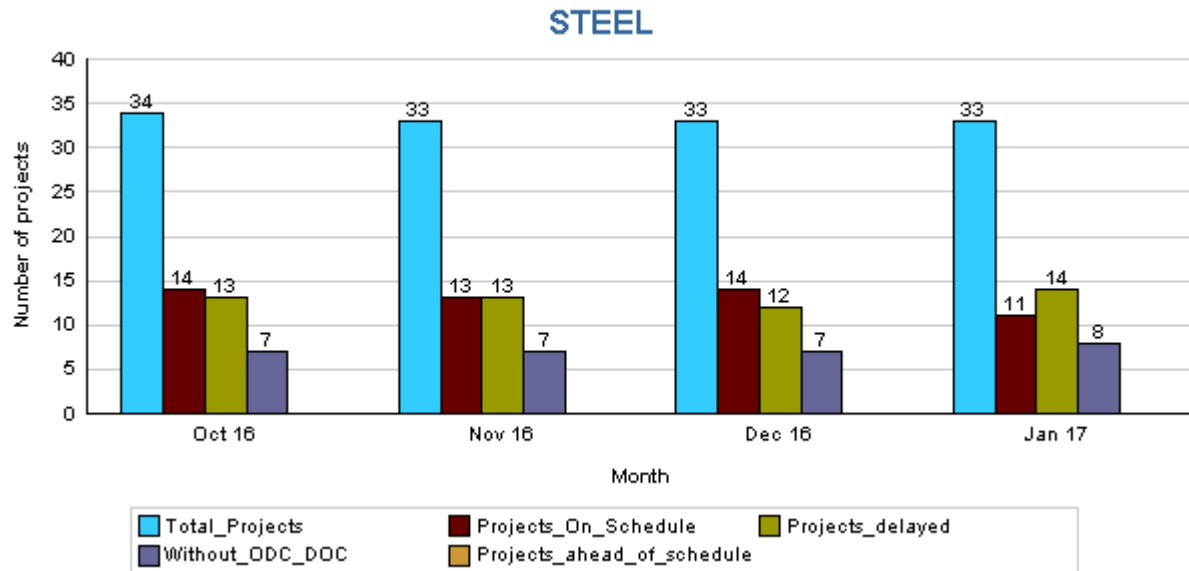


Break-up of 14 Delayed projects in January 2017

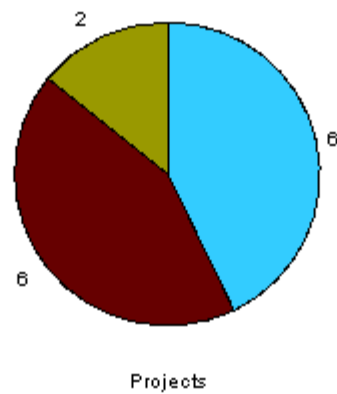

Delay in Months




**Graphical Presentation of All Projects
w.r.t. Original Schedule**

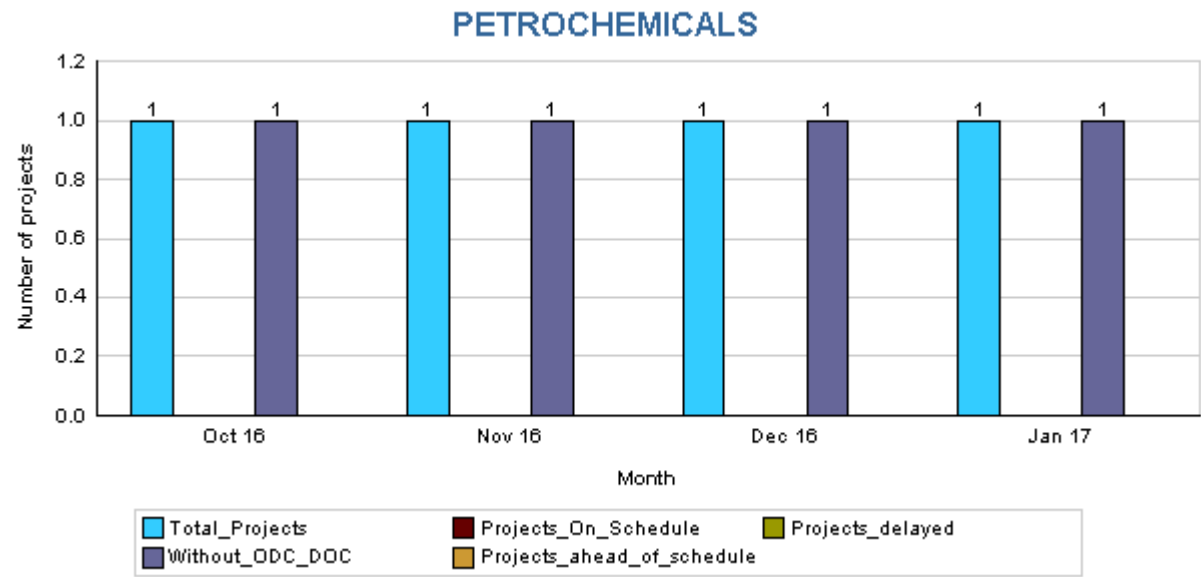


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

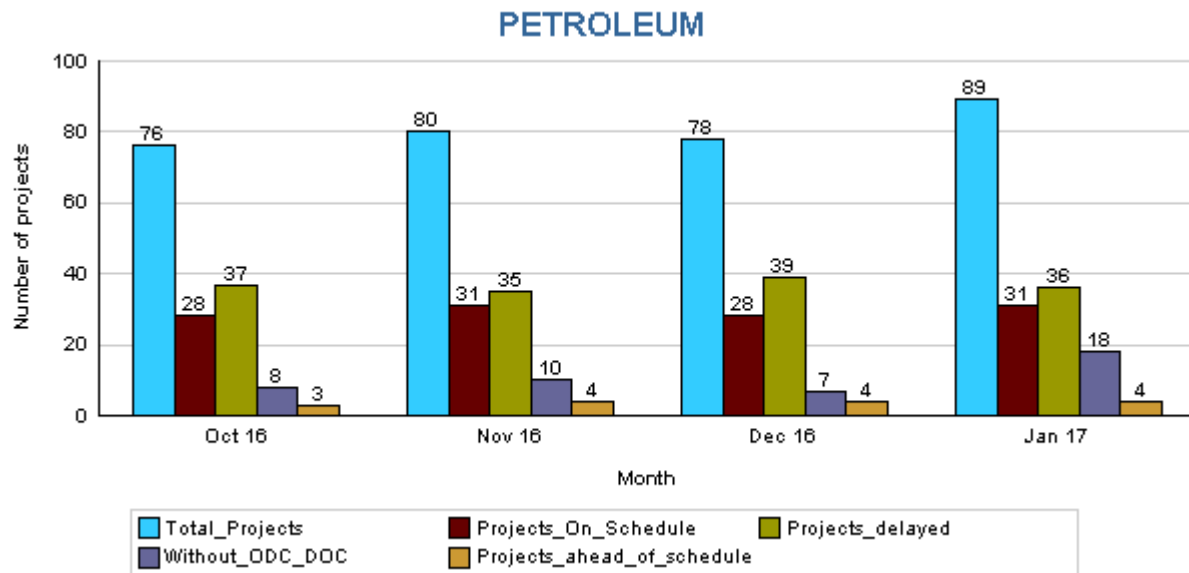


Break-up of 36 Delayed projects in January 2017

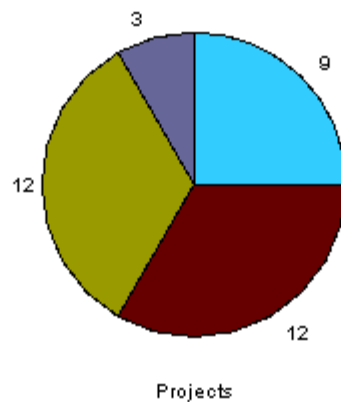


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Original Schedule

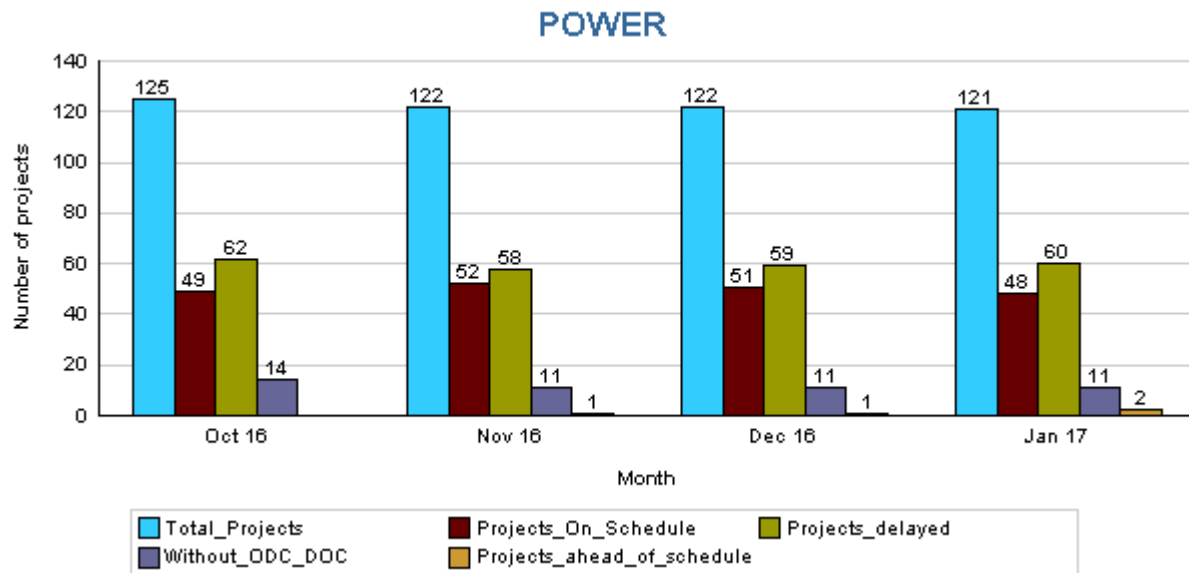


Break-up of 60 Delayed projects in January 2017

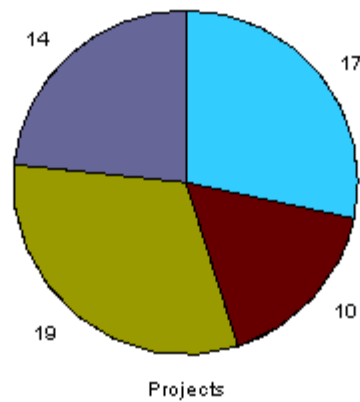


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

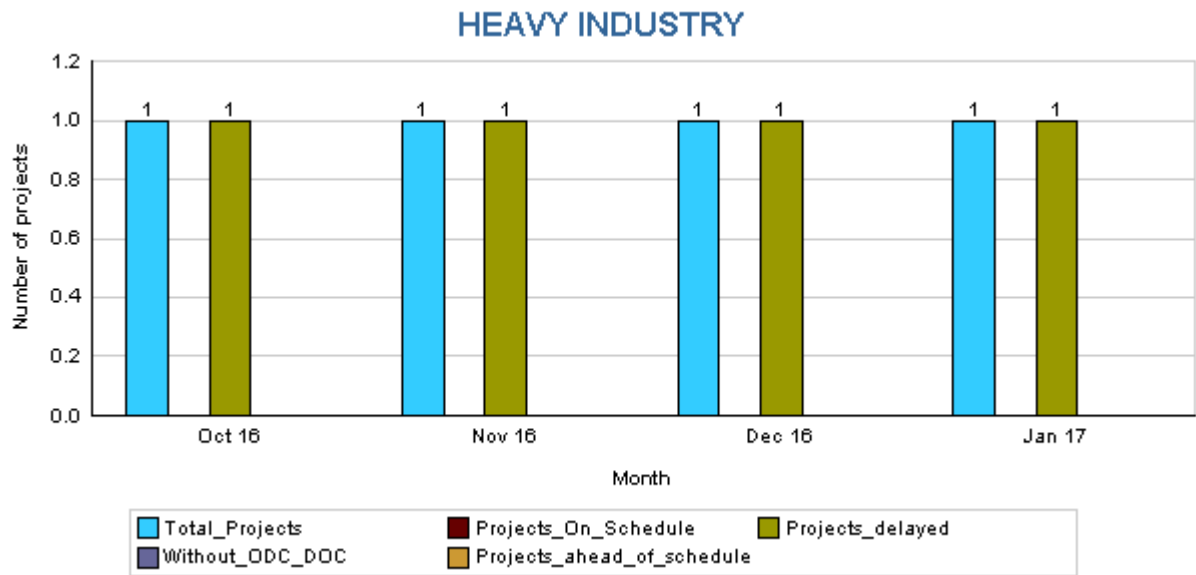


Break-up of 1 Delayed projects in January 2017

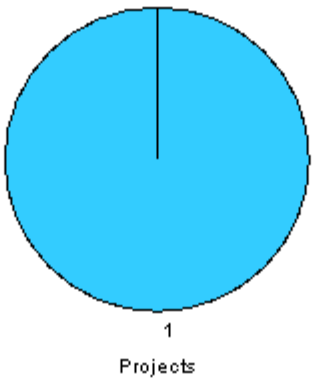


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

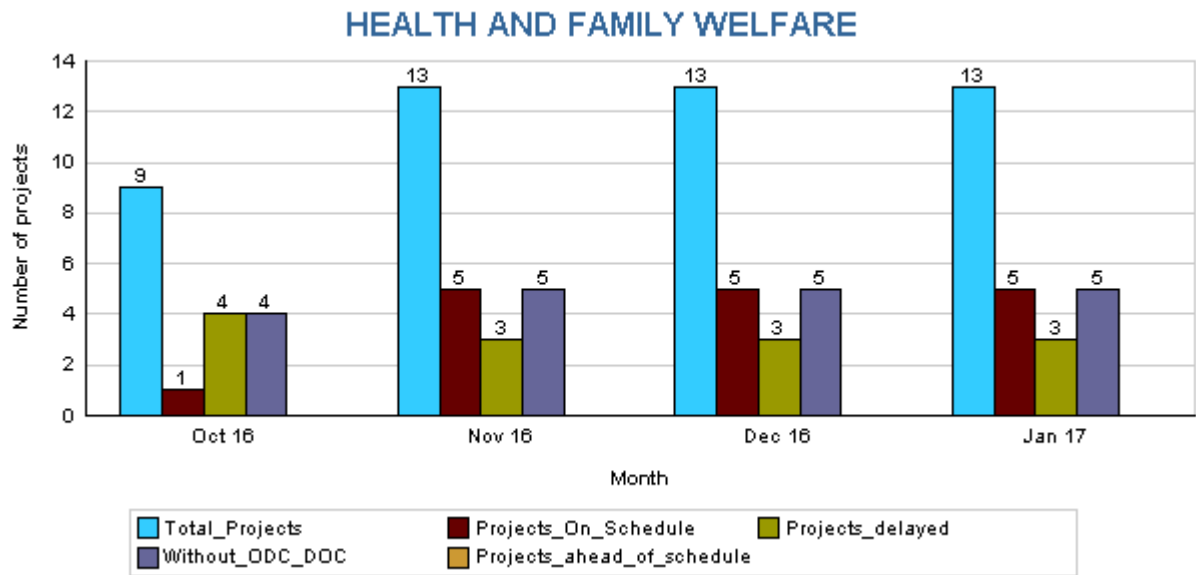


Break-up of 3 Delayed projects in January 2017

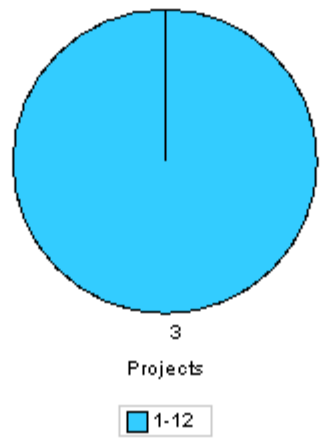


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

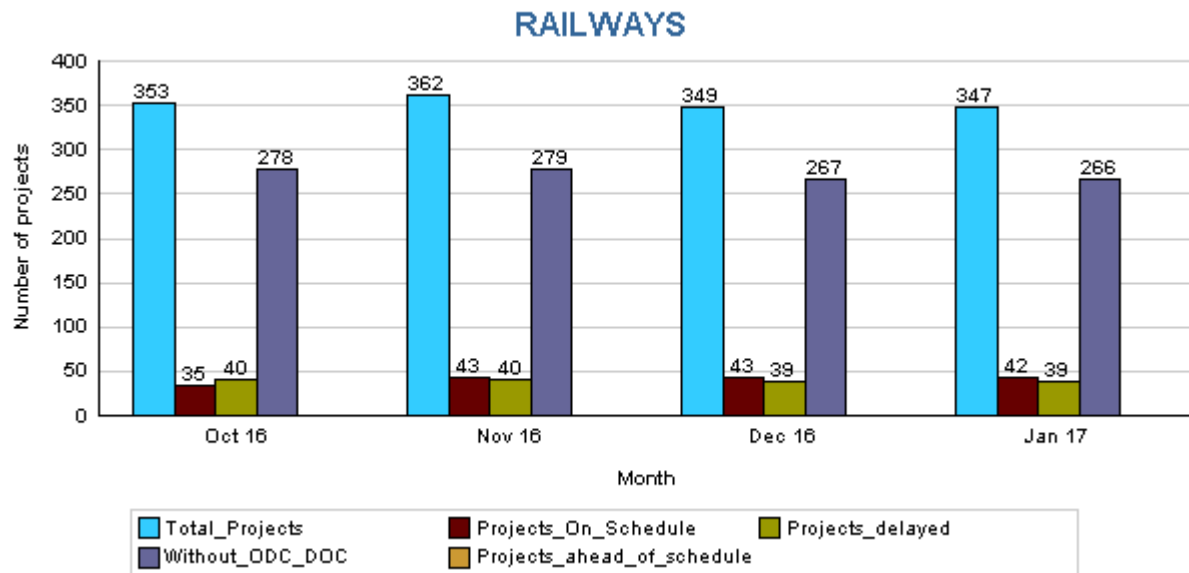


Break-up of 39 Delayed projects in January 2017

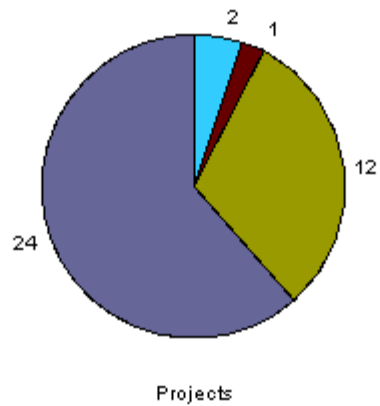


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

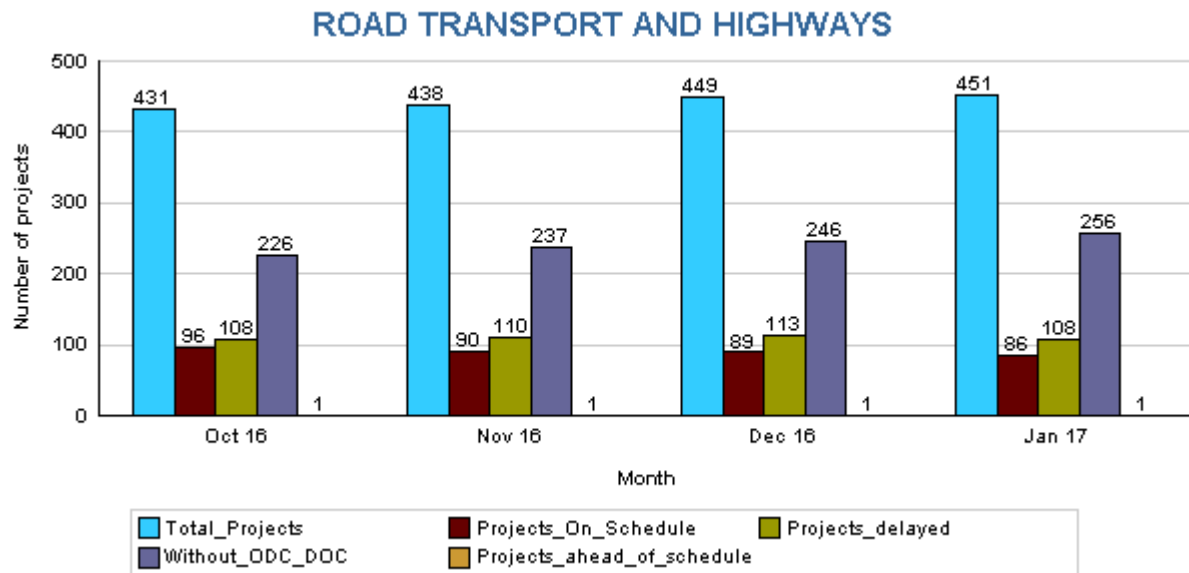


Break-up of 108 Delayed projects in January 2017

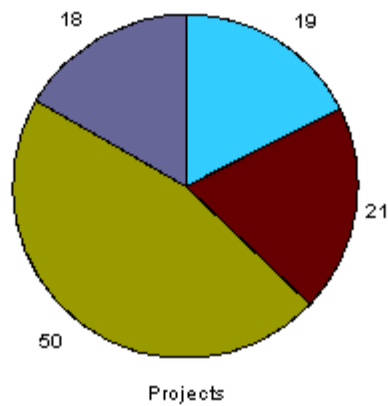


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

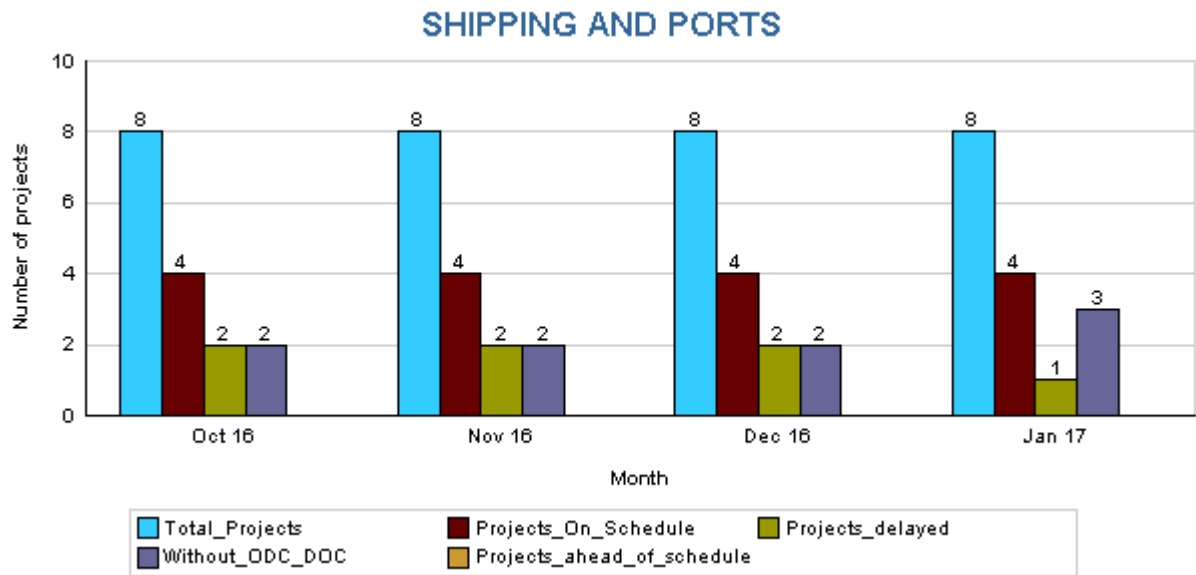


Break-up of 1 Delayed projects in January 2017

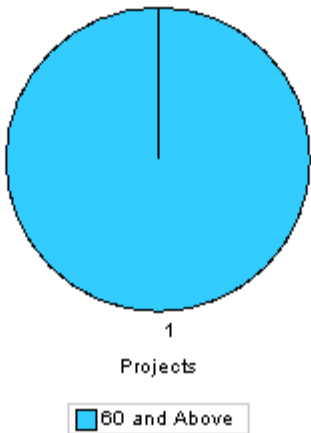

Graphical Presentation of All Projects w.r.t. Original Schedule

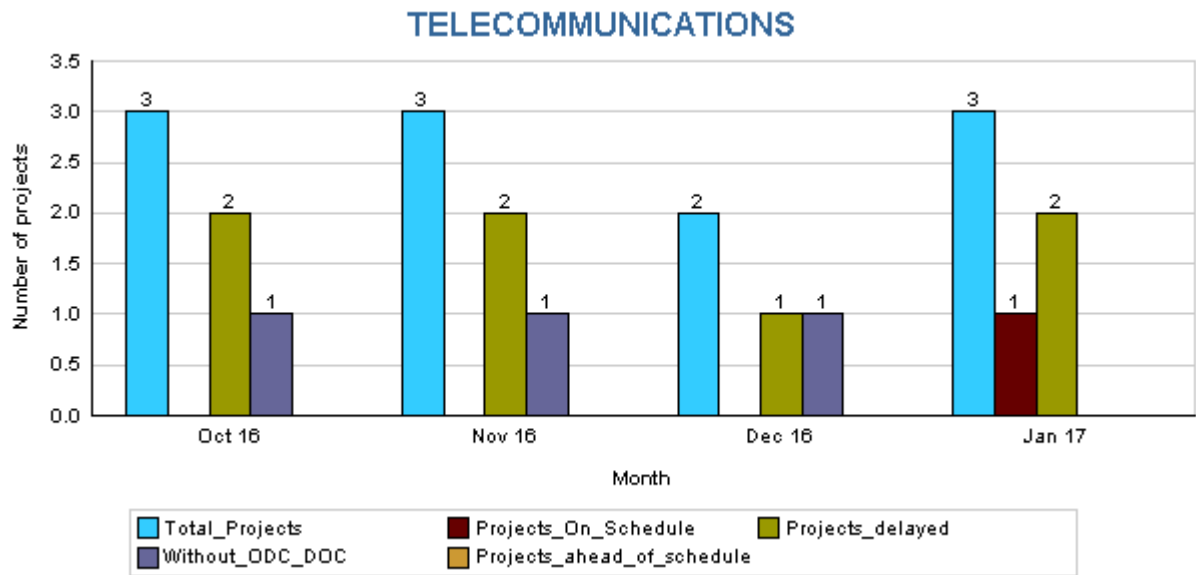


Break-up of 2 Delayed projects in January 2017

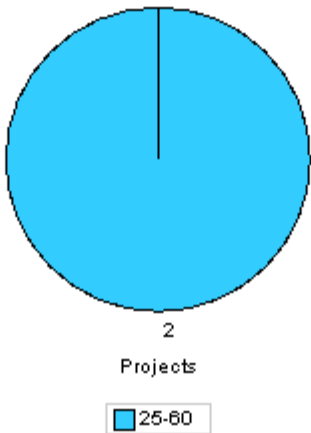


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

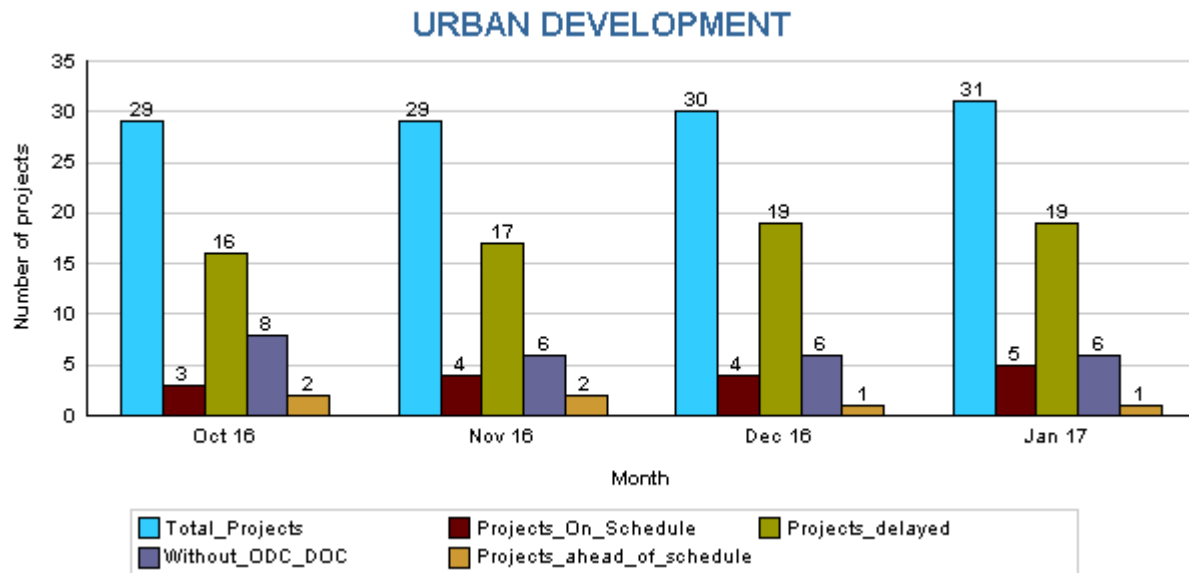

Break-up of 19 Delayed projects in January 2017

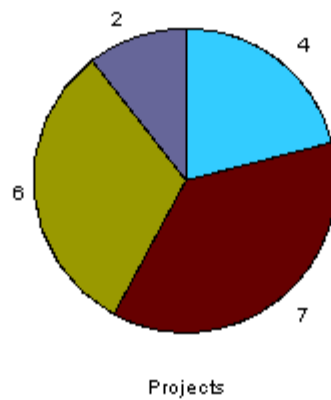

Delay in Months



List of ongoing Projects Costing Rs. 150 Crore and above.									
						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU ,	12/2001	13,171.00 17,270.00	22,462.00	21,994.00	12/2008 10/2013	02/2017	98(O) 40(R)	98/102
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,000.00	5,356.82	09/2010 09/2016	10/2017	85(O) 13(R)	80/87
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 -	11,459.00	9,417.00	12/2015 11/2016	11/2019	47(O) 36(R)	43/70
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	7,169.00	12/2016 03/2017	12/2020	48(O) 45(R)	30/68
	Total		40,442.00 -	52,241.00	43,936.82				251/327
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA ,	05/2010	335.61 -	318.00	305.59	05/2012 -	-	-	0/0
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE ,	10/2012	217.60 -	244.10	122.73	03/2015 -	03/2015	-	0/0
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS ,	10/2013	314.61 -	441.33	26.35	09/2018 -	06/2020	21(O) -	0/0
8	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	454.71	01/2011 -	12/2017	83(O) -	0/0
	Total		1,177.28 -	1,556.96	909.38				0/0
	<u>COAL</u>								
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	321.95	03/2010 -	03/2017	84(O) -	9/10
10	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,158.41	03/2023 -	03/2023	0(O) -	11/16
11	KUMMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 7,612.33	7,612.33	929.15	03/2023 03/2023	03/2023	0(O) 0(R)	2/18
12	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	80.61	07/2012 03/2017	03/2021	104(O) 48(R)	1/3
13	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 -	249.03	125.78	03/2012 -	03/2018	72(O) -	32/42
14	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	203.87	03/2022 -	03/2022	0(O) -	5/9
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 486.57	486.57	250.31	03/2012 03/2018	03/2017	60(O) -12(R)	1/1
16	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	185.94	03/2010 -	03/2019	108(O) -	3/4
17	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 1,624.59	1,624.59	5.70	03/2023 03/2023	03/2023	0(O) 0(R)	1/10

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	122.29	12/2012 -	03/2017	51(O) -	11/44
19	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	1,186.64	26.79	03/2023 -	03/2023	0(O) -	2/10
20	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	160.89	03/2020 -	03/2020	0(O) -	3/11
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	215.34	03/2012 -	03/2019	84(O) -	3/5
22	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.63	188.68	03/2013 -	03/2019	72(O) -	5/8
23	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.59	459.59	53.25	03/2015 03/2020	03/2020	60(O) 0(R)	1/7
24	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	4.76	03/2014 -	03/2020	72(O) -	1/7
25	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132(O) -	0/2
26	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	95.92	03/2015 -	03/2017	24(O) -	8/31
27	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	176.64	03/2012 -	03/2017	60(O) -	5/6
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	198.64	03/2014 -	03/2018	48(O) -	0/2
29	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	166.21	03/2016 -	03/2018	24(O) -	4/7
30	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2020	108(O) -	0/2
31	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	96.78	03/2012 -	03/2019	84(O) -	0/2
32	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND ,	07/2008	210.98 -	210.98	153.82	03/2013 -	03/2018	60(O) -	1/3
33	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	148.00	03/2012 -	03/2018	72(O) -	1/3
34	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	225.57	03/2016 -	03/2018	24(O) -	2/3
35	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2019	60(O) -	1/2
36	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	242.29	.09	03/2015 -	03/2018	36(O) -	0/5
37	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 1,131.28	1,131.28	377.37	03/2018 -	03/2018	0(O) -	6/9
38	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36(O) -	4/29
39	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	447.06	246.83	03/2015 -	03/2018	36(O) -	5/13
40	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	133.99	03/2016 -	03/2018	24(O) -	3/6
41	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	45.47	06/2015 -	03/2017	21(O) -	24/36
42	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	417.33	35.41	07/2016 -	03/2018	20(O) -	16/28

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	486.27	121.04	03/2016 -	03/2018	24(O) -	31/39
44	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	111.09	03/2020 -	03/2020	0(O) -	4/4
45	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	-	03/2022 -	03/2022	0(O) -	1/7
46	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.36	03/2021 -	03/2021	0(O) -	0/2
47	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	94.56	03/2020 -	03/2020	0(O) -	3/6
48	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	19.07	03/2019 -	03/2019	0(O) -	1/9
49	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	637.53	03/2026 -	03/2026	0(O) -	3/15
50	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	2.03	03/2019 -	03/2019	0(O) -	3/6
51	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	-	03/2018 -	03/2018	0(O) -	1/5
52	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	338.01	03/2021 -	03/2021	0(O) -	1/9
53	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	290.81	03/2020 -	03/2020	0(O) -	2/8
54	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	114.50	03/2021 -	03/2021	0(O) -	4/12
55	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	179.27	03/2018 -	03/2018	0(O) -	3/7
56	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 -	187.94	71.66	03/2023 -	03/2023	0(O) -	6/10
57	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	-	03/2023 -	03/2023	0(O) -	0/7
58	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	42.57	03/2018 -	03/2018	0(O) -	1/5
59	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	112.25	03/2021 -	03/2021	0(O) -	1/7
60	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	28.88	03/2021 -	03/2021	0(O) -	1/6
61	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	87.32	03/2019 -	03/2019	0(O) -	9/13
62	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	397.09	2.40	03/2019 -	03/2019	0(O) -	6/18
63	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	68.09	03/2020 -	03/2020	0(O) -	3/10
64	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	63.42	03/2021 -	03/2021	0(O) -	2/6
65	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	88.50	03/2025 -	03/2025	0(O) -	3/13
66	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 -	288.90	-	03/2023 -	03/2023	0(O) -	2/10
67	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	-	03/2022 -	03/2022	0(O) -	0/6
68	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	18.31	03/2020 -	03/2020	0(O) -	0/5

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
69	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	-	03/2023 -	03/2023	0(O) -	1/9
70	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	-	03/2023 -	03/2023	0(O) -	0/3
71	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024	0(O) -	0/2
72	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 -	277.65	-	03/2021 -	03/2021	0(O) -	2/6
73	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	10.87	03/2020 -	03/2020	0(O) -	2/6
74	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	6.68	03/2022 -	03/2022	0(O) -	0/21
75	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	-	03/2018 -	03/2018	0(O) -	0/9
76	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	-	03/2020 -	03/2020	0(O) -	1/17
77	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	108.75	03/2021 -	03/2021	0(O) -	0/2
78	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	16.97	03/2019 -	03/2019	0(O) -	1/9
79	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	112.48	03/2019 -	03/2019	0(O) -	1/8
80	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 -	5,907.11	3,328.28	12/2015 04/2018	04/2018	28(O) 0(R)	13/35
81	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	145.11	04/2015 -	04/2019	48(O) -	1/6
82	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	04/2017	0(O) -	1/3
83	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	221.58	03/2017 -	05/2018	14(O) -	11/11
84	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU ,	04/2012	364.75 -	364.75	252.03	10/2014 06/2017	06/2017	32(O) 0(R)	8/10
85	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU ,	05/2016	687.28 -	687.28	91.73	06/2017 -	06/2017	0(O) -	0/0
86	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	101.20	04/2014 -	08/2017	40(O) -	0/10
87	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	156.53	06/2015 08/2019	08/2019	50(O) 0(R)	2/7
88	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	269.36	03/2018 -	09/2018	6(O) -	7/15
89	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	135.47	05/2014 -	09/2017	40(O) -	0/8
90	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	2.57	09/2019 -	09/2019	0(O) -	0/0
91	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54(O) -	4/7
92	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	310.50	03/2013 -	11/2018	68(O) -	8/9

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
93	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.00	795.95	11/2021 -	11/2021	0(O) -	0/0
94	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	90.82	03/2014 -	12/2017	45(O) -	4/6
95	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	75.10	12/2019 -	12/2019	0(O) -	0/0
	Total		85,632.34 -	85,544.13	16,510.71				329/858
	FERTILISERS								
96	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	79.51	11/2016 09/2017	09/2017	10(O) 0(R)	0/0
97	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 494.00	494.00	61.66	12/2017 -	12/2017	0(O) -	0/1
	Total		680.64 -	703.44	141.17				0/1
	MINES								
98	UTKAL D AND E COAL MINE PROJECT - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	34.50	01/2020 -	01/2020	0(O) -	0/1
99	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 -	5,540.00	.88	04/2021 -	04/2021	0(O) -	0/1
100	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN , PPP (ANNUITY)	12/2015	344.50 -	344.50	309.64	11/2016 -	09/2016	-	0/1
101	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA , Private	12/2015	355.13 355.13	355.13	261.06	11/2016 12/2016	12/2016	-	0/1
	Total		6,773.63 -	6,773.63	606.08				0/4
	STEEL								
102	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	-	01/1999 -	-	-	0/0
103	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH ,	07/2011	877.73 -	877.73	700.36	07/2015 -	02/2017	19(O) -	2/2
104	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH ,	12/2009	280.00 -	280.00	95.81	09/2016 -	03/2017	6(O) -	1/1
105	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND ,	03/2015	255.19 -	255.19	115.57	03/2018 -	03/2018	0(O) -	0/1
106	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	179.14	12/2015 -	03/2017	15(O) -	0/0
107	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	203.43	12/2016 -	03/2017	3(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,118.64	02/2014 03/2016	03/2016	-	0/0
109	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	19.75	03/2017 -	03/2017	0(O) -	0/0
110	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	657.66	03/2015 -	03/2017	24(O) -	0/0
111	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	140.40	03/2018 -	03/2018	0(O) -	0/0
112	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	03/2016	-	0/0
113	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	466.13	04/2018 -	04/2018	0(O) -	0/2
114	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	270.78	12/2015 -	04/2016	-	0/0
115	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	93.66	04/2018 -	04/2018	0(O) -	0/0
116	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH ,	07/2011	974.76 -	974.76	451.53	07/2016 -	05/2017	10(O) -	1/1
117	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH ,	05/2012	404.16 -	404.16	380.93	07/2015 -	05/2017	22(O) -	0/1
118	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	221.73	12/2017 -	05/2018	5(O) -	1/2
119	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH ,	08/2010	17,265.00 -	17,265.00	17,033.59	03/2013 -	06/2017	51(O) -	34/37
120	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	198.97	06/2016 -	06/2016	-	0/0
121	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	15.17	06/2020 -	06/2020	0(O) -	2/12
122	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	11.13	06/2019 -	06/2019	0(O) -	0/0
123	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	116.00	10/2017 -	07/2018	9(O) -	0/2
124	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	146.51	12/2016 07/2017	07/2017	7(O) 0(R)	0/0
125	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	24.02	09/2017 -	09/2017	0(O) -	0/0
126	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	35.73	09/2017 -	09/2017	0(O) -	0/0
127	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	39.27	09/2018 -	09/2018	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
128	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND ,	10/2013	245.67 -	245.67	182.95	05/2016 -	10/2017	17(O) -	1/3
129	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	10,986.26	05/2015 12/2017	12/2017	31(O) 0(R)	48/85
130	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	142.68	10/2016 -	12/2017	14(O) -	0/0
131	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	12/2017	- -	0/0
132	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	389.20	12/2016 -	12/2016	-	0/0
133	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	349.35	12/2017 -	12/2017	0(O) -	0/0
134	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	107.02	04/2015 -	-	-	3/4
	Total		56,967.14 -	57,180.82	35,073.50				93/153
	PETROCHEMICALS								
135	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM ,	04/2006	5,460.61 9,965.00	9,965.00	9,895.57	04/2012 12/2015	01/2016	-	26/26
	Total		5,460.61 -	9,965.00	9,895.57				26/26
	PETROLEUM								
136	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	10.91	- -	-	-	0/0
137	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	8.72	- -	-	-	0/0
138	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	20.44	- -	-	-	0/0
139	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	890.00	16.29	- -	-	-	0/0
140	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	-	- -	-	-	0/0
141	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	-	- -	-	-	0/0
142	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	-	- -	-	-	0/0
143	BRANCH PIPELINE FROM PATNA TO MOTIHARI & BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	-	- -	-	-	0/0
144	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	-	- -	-	-	0/0
145	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	-	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
146	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	144.96	01/2018 -	01/2018	0(O) -	39/61
147	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 370.00	370.00	325.80	03/2013 01/2017	01/2017	46(O) 0(R)	0/24
148	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM ,	06/2012	150.00 -	150.00	140.02	07/2014 09/2017	01/2017	30(O) -8(R)	0/12
149	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	.53	01/2019 -	01/2019	0(O) -	0/13
150	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH ,	01/2011	141.86 222.81	222.81	189.51	09/2016 -	02/2017	5(O) -	0/12
151	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU ,	05/2015	257.87 -	257.87	88.97	11/2016 -	02/2018	15(O) -	17/22
152	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	306.51	02/2020 -	02/2020	0(O) -	0/0
153	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.01	02/2017 -	02/2017	0(O) -	0/0
154	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT ,	02/2016	931.00 -	931.00	63.30	07/2017 02/2018	02/2018	7(O) 0(R)	0/0
155	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 2,378.89	2,378.89	1,882.07	03/2013 03/2018	03/2018	60(O) 0(R)	5/15
156	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA ,	12/2009	1,584.00 -	1,584.00	1,554.08	03/2017 -	03/2017	0(O) -	3/12
157	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT ,	03/2009	317.64 -	240.95	159.43	09/2012 03/2017	03/2017	54(O) 0(R)	2/5
158	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,130.70	03/2015 03/2018	03/2018	36(O) 0(R)	0/17
159	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE ,	04/2012	600.17 600.17	600.17	375.76	12/2014 03/2018	03/2018	39(O) 0(R)	0/8
160	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	681.49	- -	03/2018	- -	0/0
161	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE ,	08/2011	586.00 -	586.00	529.25	08/2015 -	03/2017	19(O) -	3/12
162	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 462.79	462.79	318.90	10/2014 03/2017	03/2018	41(O) 12(R)	28/40
163	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA ,	03/2013	1,138.50 686.58	686.58	671.29	04/2015 03/2017	03/2017	23(O) 0(R)	0/0
164	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,338.88	11/2015 12/2016	03/2017	16(O) 3(R)	49/52
165	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM ,	03/2009	228.64 -	209.19	142.22	12/2016 -	03/2018	15(O) -	0/0
166	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 -	6,068.80	2,765.05	04/2019 03/2019	03/2019	-1(O) 0(R)	0/0
167	50 MW 10 PERSENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT , Central Sector Projects	11/2015	500.00 435.00	435.00	57.81	03/2017 -	03/2017	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
168	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 -	3,961.54	2,468.50	12/2017 03/2019	03/2019	15(O) 0(R)	0/0
169	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	84.91	03/2018 -	03/2018	0(O) -	14/22
170	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION(GUJARAT,RAJASTH - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	9.94	03/2020 -	03/2020	0(O) -	2/24
171	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 -	658.62	-	03/2023 -	03/2023	0(O) -	0/0
172	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 -	390.52	-	03/2019 -	03/2019	0(O) -	0/0
173	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 171.00	170.70	33.30	03/2019 -	03/2019	0(O) -	0/0
174	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,190.69	210.27	04/2018 04/2018	04/2018	0(O) 0(R)	0/0
175	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU ,	08/2014	393.00 -	393.00	118.59	04/2018 -	04/2018	0(O) -	0/0
176	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	327.78	2.40	04/2018 -	04/2018	0(O) -	8/20
177	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	24.54	04/2019 -	04/2019	0(O) -	0/0
178	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,057.18	05/2013 05/2017	05/2017	48(O) 0(R)	1/5
179	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE ,	04/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017	25(O) 0(R)	0/5
180	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA ,	06/2014	5,706.47 5,813.25	5,813.25	5,088.83	05/2017 05/2018	05/2018	12(O) 0(R)	7/16
181	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 -	6,086.08	1,763.35	05/2019 05/2019	05/2019	0(O) 0(R)	0/0
182	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,098.43	1,237.43	05/2017 -	05/2017	0(O) -	0/0
183	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020	14(O) 0(R)	0/0
184	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU , Central Sector Projects	02/2016	367.11 -	367.11	103.03	04/2017 -	05/2017	1(O) -	19/22
185	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	830.93	03/2015 05/2017	05/2017	26(O) 0(R)	0/5
186	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	736.65	533.16	09/2011 06/2017	06/2017	69(O) 0(R)	0/0
187	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT ,	09/2011	202.25 -	160.16	99.51	07/2016 06/2018	06/2018	23(O) 0(R)	5/12

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 439.03	439.03	5.87	03/2017 -	06/2018	15(O) -	0/0
189	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL ,	03/2014	3,076.00 -	3,076.00	892.55	09/2017 06/2018	06/2018	9(O) 0(R)	3/7
190	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	133.65	05/2015 -	06/2017	25(O) -	0/12
191	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH , Central Sector Projects	03/2009	181.02 -	173.28	108.85	01/2017 06/2017	06/2017	5(O) 0(R)	0/0
192	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA ,	05/2016	215.38 -	215.38	108.03	06/2017 06/2017	06/2017	0(O) 0(R)	0/0
193	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	128.56	06/2020 -	06/2020	0(O) -	0/0
194	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020	0(O) -	0/0
195	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 714.25	714.25	144.74	10/2017 08/2018	08/2018	10(O) 0(R)	21/52
196	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	36.47	07/2018 11/2019	08/2019	13(O) -3(R)	1/38
197	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 -	4,588.29	626.25	08/2018 -	08/2018	0(O) -	0/0
198	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	110.36	09/2018 09/2018	09/2018	0(O) 0(R)	0/0
199	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL ,	08/2014	190.45 -	190.45	-	09/2017 -	09/2017	0(O) -	0/0
200	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	3.42	09/2019 -	09/2019	0(O) -	0/0
201	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA ,	02/2012	666.00 838.08	768.25	672.65	11/2015 11/2016	10/2016	-	29/29
202	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA ,	03/2014	238.50 -	238.50	111.81	03/2017 10/2017	10/2017	7(O) 0(R)	4/6
203	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL ,	03/2015	694.00 -	694.00	72.21	10/2018 -	10/2018	0(O) -	0/0
204	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	341.70	2.95	01/2014 11/2019	11/2019	70(O) 0(R)	0/2
205	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019	0(O) -	0/0
206	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	48.72	11/2019 -	11/2019	0(O) -	0/0
207	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	-	11/2018 -	11/2018	0(O) -	0/0
208	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	07/2009	3,957.00 3,561.00	3,397.00	456.75	01/2013 12/2018	12/2018	71(O) 0(R)	20/37
209	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,701.29	12/2016 -	12/2016	-	6/7

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA ,	03/2012	2,592.17 2,592.17	2,592.17	1,869.67	05/2014 12/2017	12/2017	43(O) 0(R)	0/21
211	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE ,	01/2012	352.49 -	352.49	351.78	03/2014 12/2016	12/2016	-	3/3
212	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KARNATAKA ,	01/2006	993.00 1,693.00	1,693.00	1,502.70	01/2012 -	12/2016	-	0/0
213	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE ,	05/2013	4,124.35 4,259.49	4,259.49	2,122.24	04/2016 12/2017	12/2017	20(O) 0(R)	0/3
214	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR ,	04/2013	480.00 -	422.00	330.25	02/2016 12/2016	12/2016	-	6/6
215	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	515.65	09/2017 12/2018	12/2018	15(O) 0(R)	2/6
216	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE ,	10/2011	725.00 -	725.00	513.75	11/2016 -	12/2016	-	0/12
217	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA ,	05/2015	2,443.00 1,417.00	2,443.00	616.11	12/2017 06/2017	12/2017	0(O) 6(R)	0/0
218	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 247.52	247.52	-	02/2019 -	12/2018	-2(O) -	1/10
219	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA ,	02/2015	184.00 -	184.00	46.02	06/2017 -	12/2017	6(O) -	0/0
220	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	21.71	05/2019 -	12/2018	-5(O) -	1/13
221	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	1,427.94	105.76	12/2018 -	12/2018	0(O) -	9/21
222	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	8.43	08/2019 -	12/2018	-8(O) -	1/13
223	BSVI UP GRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	8.95	12/2019 -	12/2019	0(O) -	0/0
224	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA ,	03/2012	16,504.00 -	16,504.00	13,214.81	05/2016 -	-	-	0/16
	Total		1,85,636.77 -	1,86,447.26	54,194.71				309/750
	POWER								
225	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,HIMACHAL PRADESH ,	12/2005	358.42 -	358.42	-	12/2008 09/2010	-	-	0/15
226	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 1,078.31	1,078.31	986.33	07/2013 -	-	-	25/26
227	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH ,	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	11/20
228	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR ,	01/2009	3,642.04 -	5,783.17	4,800.42	01/2016 -	01/2018	24(O) -	5/6
229	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE ,	02/2009	509.66 -	509.66	635.96	11/2011 -	01/2017	62(O) -	11/11

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
230	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE ,	12/2009	1,216.83 1,428.87	1,428.87	1,092.09	08/2012 09/2016	01/2017	53(O) 4(R)	5/5
231	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE ,	06/2012	1,909.24 -	1,909.24	1,265.03	06/2015 -	01/2017	19(O) -	5/5
232	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	696.27	04/2020 -	01/2023	33(O) -	0/0
233	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	25.80	01/2018 -	01/2018	0(O) -	0/0
234	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	16.00	01/2019 -	01/2019	0(O) -	0/0
235	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,420.88	10/2012 03/2017	02/2018	64(O) 11(R)	8/11
236	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,431.10	12/2012 12/2016	02/2018	62(O) 14(R)	12/23
237	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	6,102.00	09/2016 01/2017	02/2017	5(O) 1(R)	38/41
238	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH ,	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	2/2
239	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	14,366.58	3,934.00	02/2019 02/2020	02/2020	12(O) 0(R)	14/18
240	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 -	195.42	100.27	02/2014 -	02/2018	48(O) -	2/3
241	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND ,	08/2006	2,313.00 4,138.41	4,366.64	3,820.69	12/2011 03/2016	02/2017	62(O) 11(R)	13/14
242	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	.30	02/2019 -	02/2019	0(O) -	0/0
243	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	1.00	02/2019 -	02/2019	0(O) -	0/0
244	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE ,	07/2010	752.64 689.03	689.03	605.02	07/2013 11/2015	03/2017	44(O) 16(R)	7/9
245	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE ,	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	03/2016	-	11/12
246	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 -	1,940.13	2,281.56	09/2014 -	03/2017	30(O) -	10/13
247	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT ,	12/2011	552.44 609.44	609.44	501.60	02/2014 03/2016	03/2016	-	10/10
248	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH ,	01/2012	1,422.85 1,875.13	1,875.13	1,721.72	01/2015 06/2016	03/2017	26(O) 9(R)	9/11
249	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE ,	09/2013	1,575.30 -	1,575.30	1,235.60	05/2016 -	03/2017	10(O) -	10/13

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
250	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	998.10	03/2018 -	03/2018	0(O) -	8/12
251	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	1,880.00	12/2016 03/2017	03/2017	3(O) 0(R)	22/26
252	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	2,172.00	03/2019 -	03/2019	0(O) -	17/20
253	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 -	268.80	103.30	03/2018 -	03/2018	0(O) -	0/3
254	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	26.70	03/2018 -	03/2018	0(O) -	0/0
255	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH ,	03/2015	550.06 -	550.06	-	03/2018 -	03/2018	0(O) -	0/3
256	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR ,	03/2010	3,984.03 -	3,984.03	3,413.45	01/2013 -	03/2016	-	1/1
257	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC,WEST BENGAL ,	04/2007	4,122.00 8,781.30	9,142.58	8,524.99	02/2011 -	03/2016	-	26/26
258	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	5.90	03/2019 -	03/2019	0(O) -	0/0
259	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	-	03/2019 -	03/2019	0(O) -	0/0
260	KANDORNA AND BHANWAD WIND FARM - [N18000234]THDCIL,GUJARAT ,	11/2016	415.49 -	415.49	24.00	03/2017 -	03/2017	0(O) -	0/2
261	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT ,	02/2014	378.71 -	378.71	245.30	10/2016 -	04/2017	6(O) -	8/11
262	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE ,	06/2014	400.47 -	400.47	232.10	04/2017 -	04/2017	0(O) -	1/3
263	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE ,	11/2014	972.42 -	972.42	686.90	11/2017 -	04/2017	-7(O) -	1/3
264	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE ,	12/2014	6,517.36 -	6,517.36	1,688.20	04/2018 -	04/2018	0(O) -	3/12
265	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	-	04/2018 -	04/2018	0(O) -	4/9
266	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	7.10	04/2018 -	04/2018	0(O) -	0/0
267	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	14.60	04/2019 -	04/2019	0(O) -	0/0
268	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	12,694.00	01/2011 05/2018	05/2018	88(O) 0(R)	26/47

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
269	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH ,	12/2008	573.99 1,337.76	1,337.76	1,341.09	08/2013 05/2017	05/2017	45(O) 0(R)	31/38
270	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE ,	03/2012	198.63 -	198.63	120.73	09/2014 -	05/2017	32(O) -	0/0
271	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE ,	01/2015	3,662.02 -	3,662.02	1,668.70	05/2018 -	05/2018	0(O) -	0/5
272	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	1.90	05/2017 -	05/2017	0(O) -	2/9
273	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL,TAMIL NADU ,	01/2016	162.11 -	162.11	15.10	05/2018 -	05/2018	0(O) -	0/0
274	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL,TRIPURA ,	05/2016	409.19 -	409.19	25.20	05/2018 -	05/2018	0(O) -	0/0
275	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	161.60	05/2019 -	05/2019	0(O) -	0/0
276	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 3,846.30	3,846.30	3,053.00	03/2013 06/2019	06/2019	75(O) 0(R)	3/15
277	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM ,	01/2008	4,375.35 6,749.18	6,749.18	6,405.00	09/2011 06/2017	06/2017	69(O) 0(R)	28/37
278	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE ,	02/2010	232.34 -	232.34	237.09	06/2012 -	06/2017	60(O) -	1/4
279	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH ,	11/2011	2,127.51 2,619.56	2,619.56	2,525.03	07/2014 06/2016	06/2017	35(O) 12(R)	6/8
280	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH ,	03/2012	9,569.76 -	9,569.76	6,707.99	06/2015 -	06/2017	24(O) -	21/30
281	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE ,	11/2011	723.63 -	723.63	687.82	11/2014 -	06/2017	31(O) -	7/10
282	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,364.52	1,050.44	04/2016 -	06/2017	14(O) -	8/12
283	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	352.50	06/2016 -	06/2017	12(O) -	8/11
284	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE ,	05/2014	829.98 -	829.98	337.20	08/2016 -	06/2017	10(O) -	2/4
285	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE ,	05/2014	303.07 -	303.07	182.30	07/2016 -	06/2017	11(O) -	5/9
286	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 -	522.29	311.90	11/2016 -	06/2017	7(O) -	5/12
287	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 -	155.57	69.60	03/2016 -	06/2017	15(O) -	2/6
288	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 -	196.58	78.70	02/2016 -	06/2017	16(O) -	7/17
289	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	12,964.60	8,189.41	01/2018 -	06/2018	5(O) -	26/31

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
290	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	6.10	06/2018 -	06/2018	0(O) -	0/0
291	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 -	790.13	48.50	06/2019 -	06/2019	0(O) -	0/0
292	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	15,166.19	12,777.00	01/2017 07/2017	07/2017	6(O) 0(R)	38/46
293	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	203.28	93.30	07/2017 -	07/2017	0(O) -	0/5
294	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	1.00	07/2017 -	07/2017	0(O) -	0/0
295	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	129.50	07/2018 -	07/2018	0(O) -	0/0
296	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL,GUJARAT ,	01/2016	244.19 -	244.19	38.10	07/2018 -	07/2018	0(O) -	0/0
297	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	104.80	07/2018 -	07/2018	0(O) -	0/0
298	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL,ANDHRA PRADESH ,	01/2016	207.88 -	207.88	4.90	07/2018 -	07/2018	0(O) -	0/0
299	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	590.00	07/2020 -	07/2020	0(O) -	10/10
300	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	-	07/2018 -	07/2018	0(O) -	0/0
301	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	7,337.00	11/2016 08/2017	08/2017	9(O) 0(R)	29/36
302	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017	0(O) -	0/9
303	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	12,532.44	4,863.00	08/2018 -	08/2018	0(O) -	21/25
304	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	1,919.35	11/2008 12/2016	09/2018	118(O) 21(R)	20/22
305	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	2,978.86	2,068.02	02/2016 09/2019	09/2019	43(O) 0(R)	15/23
306	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM ,	07/1998	368.72 1,352.53	1,352.53	1,137.81	07/2006 09/2017	09/2017	134(O) 0(R)	6/13
307	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	11,846.00	7,539.00	06/2017 09/2017	09/2017	3(O) 0(R)	26/40
308	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	11,638.55	6,888.00	09/2017 -	09/2017	0(O) -	22/41
309	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXII - [N18000159]PGCIL,MULTI STATE ,	02/2014	908.08 -	908.08	559.10	06/2016 -	09/2017	15(O) -	12/18
310	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 -	288.49	171.20	02/2017 -	09/2017	7(O) -	2/12
311	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	234.00	09/2019 -	09/2019	0(O) -	5/6
312	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 7,998.00	5,353.00	6,266.92	05/2014 03/2017	09/2017	40(O) 6(R)	1/4

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
313	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	6,117.37	12/2016 -	09/2017	9(O) -	27/34
314	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	9,870.51	2,209.00	09/2019 -	09/2019	0(O) -	16/16
315	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL,ODISHA ,	01/2016	187.04 -	187.04	20.80	06/2018 -	09/2017	-9(O) -	0/0
316	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	1,788.41	476.46	09/2017 -	09/2017	0(O) -	0/0
317	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	5,331.03	12/2009 10/2017	10/2017	94(O) 0(R)	16/30
318	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	94.10	10/2017 -	10/2017	0(O) -	0/5
319	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL,GUJARAT ,	10/2015	315.00 -	315.00	283.58	10/2016 -	10/2016	-	2/2
320	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	73.10	11/2017 -	11/2017	0(O) -	0/0
321	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	-	11/2018 -	11/2018	0(O) -	0/0
322	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	8.40	11/2019 -	11/2019	0(O) -	0/0
323	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	8.00	11/2018 -	11/2018	0(O) -	0/0
324	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	-	11/2017 -	11/2017	0(O) -	0/8
325	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,086.47	09/2009 -	12/2018	111(O) -	2/3
326	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	634.29	09/2010 12/2016	12/2017	87(O) 12(R)	4/8
327	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	2,491.58	1,016.89	06/2013 -	12/2019	78(O) -	7/11
328	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,137.80	08/2013 12/2017	12/2017	52(O) 0(R)	19/26
329	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL ,	04/2010	4,404.57 -	4,404.57	3,261.45	01/2015 -	12/2017	35(O) -	8/16
330	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,358.23	11/2012 12/2016	12/2017	61(O) 12(R)	10/13
331	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH ,	05/2011	1,961.87 2,310.58	2,310.58	1,886.05	05/2014 06/2016	12/2016	-	12/12
332	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	475.32	06/2014 03/2016	12/2017	42(O) 21(R)	10/12
333	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 346.79	346.79	339.27	08/2014 06/2015	12/2017	40(O) 30(R)	8/10
334	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH ,	12/2011	1,746.65 2,228.71	2,228.71	1,822.73	08/2014 12/2015	12/2017	40(O) 24(R)	7/11

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
335	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 -	514.20	489.20	06/2015 -	12/2017	30(O) -	7/10
336	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 -	2,514.88	1,663.25	12/2015 -	12/2017	24(O) -	15/18
337	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	51.90	04/2016 -	12/2017	20(O) -	0/0
338	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	137.20	09/2017 -	12/2017	3(O) -	0/0
339	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE ,	04/2015	1,479.30 -	1,479.30	383.60	04/2017 -	12/2018	20(O) -	2/8
340	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	41.20	03/2017 -	12/2017	9(O) -	0/0
341	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	67.10	12/2018 -	12/2018	0(O) -	0/0
342	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	-	12/2018 -	12/2018	0(O) -	0/0
343	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	17,435.15	8,795.49	09/2010 -	-	-	0/0
344	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC,RAJASTHAN ,	02/2015	302.49 302.00	302.49	290.89	02/2016 -	-	-	1/1
345	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	1,892.86	10/2017 -	10/2017	0(O) -	0/0
	Total		3,34,690.29 -	3,83,881.20	2,14,784.64				867/1268
	HEAVY INDUSTRY								
346	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75(O) -	0/0
	Total		1,718.00 -	3,827.30	2,289.00				0/0
	HEALTH AND FAMILY WELFARE								
347	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	210.92	11/2013 -	11/2014	-	0/0
348	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	03/2016	-	0/0
349	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI ,	11/2013	196.70 -	209.00	209.00	01/2016 -	01/2016	-	0/0
350	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	9.00	02/2018 -	02/2018	0(O) -	0/0
351	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	505.58	140.00	03/2018 -	03/2018	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
352	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	-	05/2018 -	05/2018	0(O) -	0/0
353	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	97.00	05/2017 -	06/2017	1(O) -	0/0
354	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	159.00	05/2017 -	06/2017	1(O) -	0/0
355	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI ,	09/2013	444.70 -	444.70	410.30	12/2015 -	07/2016	-	0/0
356	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	168.90	38.00	05/2017 -	07/2017	2(O) -	0/0
357	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	312.99	25.00	08/2018 -	08/2018	0(O) -	0/0
358	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	19.00	09/2018 -	09/2018	0(O) -	0/0
359	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH ,	10/2013	159.50 -	159.50	139.22	11/2013 -	10/2016	-	0/0
	Total		3,637.08 -	3,649.38	1,569.94				0/0
	<u>RAILWAYS</u>								
360	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 -	631.78	350.76	12/2012 -	-	-	0/0
361	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	532.98	- -	-	-	0/0
362	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	780.98	327.28	- -	-	-	0/0
363	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	527.54	07/2012 -	-	-	0/0
364	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 774.90	870.00	848.70	- -	-	-	0/0
365	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	130.11	- -	-	-	0/0
366	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.43	03/2007 03/2007	-	-	0/0
367	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND ,	04/1997	194.07 -	335.00	226.39	06/2004 -	-	-	0/0
368	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 458.26	480.00	3.49	07/2008 -	-	-	0/0
369	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	891.01	03/2012 -	-	-	0/0
370	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	452.71	12/2009 -	-	-	0/0
371	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	198.17	- -	-	-	0/0
372	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 781.02	876.10	842.81	06/2007 -	-	-	0/0
373	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	100.00 535.13	712.82	621.08	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
374	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE ,	04/1998	92.63 228.08	350.00	320.04	02/2011 -	-	-	0/0
375	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 724.89	973.33	622.55	12/2012 12/2012	-	-	0/0
376	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	4.49	- -	-	-	0/0
377	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	376.05	- -	-	-	0/0
378	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	230.92	- -	-	-	0/0
379	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	208.40	.15	- -	-	-	0/0
380	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH ,	04/2003	136.62 -	376.00	373.73	12/2007 03/2010	-	-	0/0
381	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	465.97	12/2010 -	-	-	3/7
382	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA ,	04/2007	482.00 874.57	874.57	929.12	03/2013 -	-	-	0/0
383	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	1,655.68	38.79	03/2014 -	-	-	0/0
384	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN ,	04/2008	516.23 732.06	735.00	728.06	03/2014 -	-	-	0/0
385	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 167.73	167.73	220.45	03/2012 -	-	-	0/0
386	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL ,	04/2009	533.38 -	533.38	135.06	12/2011 -	-	-	0/0
387	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL ,	04/2009	611.03 -	611.03	147.38	12/2011 -	-	-	0/0
388	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL ,	04/1999	207.52 334.87	334.87	320.65	12/2012 06/2016	-	-	0/0
389	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	307.00	-	- -	-	-	0/0
390	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	243.78	51.49	- -	-	-	0/0
391	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	494.92	53.79	- -	-	-	0/0
392	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	643.00	-	- -	-	-	0/0
393	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	431.00	8.59	- -	-	-	0/0
394	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	324.15	- -	-	-	0/0
395	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	845.68	1.56	- -	-	-	0/0
396	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	3,500.00	169.23	- -	-	-	0/1

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
397	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	276.89	13.20	- -	-	-	0/0
398	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	822.00	-	- -	-	-	0/1
399	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	323.00	-	- -	-	-	0/0
400	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN ,	04/2011	239.73 -	257.78	71.34	- -	-	-	0/0
401	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 218.39	272.99	36.81	- -	-	-	0/0
402	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	369.08	79.96	- -	-	-	0/0
403	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	293.68	27.61	- -	-	-	0/0
404	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 -	434.00	38.65	- -	-	-	0/0
405	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 -	1,009.00	7.88	- -	-	-	0/0
406	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
407	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	583.00	331.69	12/2015 -	-	-	0/0
408	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	490.80 633.87	490.80	.39	- -	-	-	0/0
409	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	-	- -	-	-	0/0
410	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	-	- -	-	-	0/0
411	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 549.75	549.75	14.65	- -	-	-	0/0
412	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
413	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
414	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
415	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
416	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	523.52	2.26	- -	-	-	0/0
417	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 1,500.00	1,500.00	.29	- -	-	-	0/0
418	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	346.15	155.87	- -	-	-	0/0
419	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	5.39	- -	-	-	0/0
420	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 603.22	603.22	1.64	- -	-	-	0/0
421	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	342.85	280.75	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	4.21	- -	-	-	0/0
423	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 268.52	268.52	.67	- -	-	-	0/0
424	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 800.00	800.00	39.27	- -	-	-	0/0
425	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 319.58	319.58	142.62	- -	-	-	0/0
426	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 290.85	290.85	9.31	- -	-	-	0/0
427	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 260.60	260.60	6.93	- -	-	-	0/0
428	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 1,130.13	1,130.13	57.15	- -	-	-	0/0
429	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 234.41	234.41	215.68	03/2015 -	-	-	0/0
430	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 238.36	238.36	162.26	- -	-	-	0/0
431	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	241.26	- -	-	-	0/0
432	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 595.91	595.91	103.62	- -	-	-	0/0
433	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 104.80	160.97	56.80	- -	-	-	0/0
434	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 198.88	198.88	22.77	- -	-	-	0/0
435	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	17.33	- -	-	-	0/0
436	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.37	- -	-	-	0/0
437	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	193.30	- -	-	-	0/0
438	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 186.64	186.64	178.20	- -	-	-	0/0
439	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 173.91	173.91	57.85	- -	-	-	0/0
440	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 370.81	369.69	32.00	- -	-	-	0/0
441	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 131.47	153.02	52.01	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
442	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 79.39	186.89	65.39	- -	-	-	0/0
443	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 681.68	681.68	137.94	- -	-	-	0/0
444	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	-	-	0/0
445	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE ,	04/2006	96.16 260.16	280.00	272.97	- -	-	-	0/0
446	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 1,801.00	1,801.01	2.09	- 06/2016	-	-	0/0
447	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	633.24	- -	-	-	0/1
448	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	247.04	- -	-	-	0/1
449	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	1,112.00	.36	- -	-	-	0/1
450	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 -	2,200.00	123.86	- -	-	-	0/0
451	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	923.23	1.37	- -	-	-	0/1
452	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	759.41	.51	- -	-	-	0/0
453	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	272.92	- -	-	-	0/0
454	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	199.35	- -	-	-	0/0
455	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 197.17	197.17	60.76	- -	-	-	0/0
456	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.70	- -	-	-	0/0
457	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	2,966.99	7.08	- -	-	-	0/0
458	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.67	- -	-	-	0/0
459	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	-	- -	-	-	0/0
460	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 466.65	466.65	-	- -	-	-	0/0
461	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 832.47	832.47	.94	- -	-	-	0/0
462	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 1,714.49	1,714.49	560.85	- 06/2014	-	-	0/2
463	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 348.85	348.85	.35	- -	-	-	0/0
464	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	3.19	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
465	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.48	- -	-	-	0/1
466	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	1,313.48	30.51	- -	-	-	0/1
467	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 -	792.01	1.13	- -	-	-	0/1
468	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,050.00	269.63	- -	-	-	0/1
469	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	62.75	- -	-	-	0/0
470	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	287.51	- -	-	-	0/0
471	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	154.28	- -	-	-	0/0
472	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	-	- -	-	-	0/0
473	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	-	- -	-	-	0/0
474	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
475	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
476	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	94.96	- -	-	-	0/0
477	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 1,922.00	1,922.00	2.65	- -	-	-	0/0
478	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	-	- -	-	-	0/0
479	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 259.23	259.23	23.83	- -	-	-	0/0
480	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 272.20	272.20	2.33	- -	-	-	0/0
481	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	750.00	-	01/1999 -	-	-	0/0
482	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	1.51	01/1999 -	-	-	0/0
483	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 -	426.00	-	01/1999 -	-	-	0/0
484	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA ,	04/2010	203.40 203.40	273.84	272.67	- -	-	-	0/0
485	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	-	- -	-	-	0/0
486	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	873.71	-	- -	-	-	0/0
487	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	236.82	- -	-	-	0/0
488	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH ,	04/1997	836.26 1,072.52	1,072.52	1,058.25	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	81,459.00 -	28,181.00	-	-	-	-	0/0
490	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	2,750.00	-	-	-	-	0/0
491	KONDAPALLI-KOTHAGUEDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	.36	-	-	-	0/1
492	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.04	-	-	-	0/0
493	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 3,631.00	3,631.00	-	-	-	-	0/0
494	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,246.26	-	-	-	-	0/0
495	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	-	-	-	-	0/0
496	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.54	07/2014 -	-	-	0/0
497	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	556.31 -	612.00	-	-	-	-	0/0
498	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	900.00	-	-	-	-	0/0
499	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,000.00	-	-	-	-	0/0
500	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	2,335.67	.05	-	-	-	0/0
501	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA ,	02/1997	295.00 1,289.92	1,289.92	1,391.30	-	01/2017	-	0/1
502	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA ,	01/2004	238.56 717.15	740.00	742.57	03/2012 01/2016	01/2016	-	0/0
503	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.30	03/2011 -	01/2011	-	0/0
504	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 608.02	634.48	631.43	03/1994 02/2016	02/2016	-	0/0
505	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	849.98	-	02/2017	-	1/1
506	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA ,	04/1999	166.16 -	370.00	363.32	02/2009 02/2009	02/2017	96(O) 96(R)	0/1
507	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	340.00	344.04	03/2009 03/2009	02/2017	95(O) 95(R)	1/1
508	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 926.23	1,010.00	983.96	-	03/2017	-	0/0
509	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	557.65	03/2004 03/2020	03/2020	192(O) 0(R)	0/0
510	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 1,125.89	1,125.89	1,035.41	12/2011 03/2020	03/2020	99(O) 0(R)	0/0
511	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 372.09	525.00	557.98	-	03/2019	-	0/0
512	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 4,327.28	6,093.31	1,271.49	05/2008 03/2023	03/2023	178(O) 0(R)	0/4

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
513	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 1,045.20	2,125.18	90.93	- -	03/2021	- -	0/0
514	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,010.00	2,419.18	12/2008 -	03/2019	123(O) -	0/0
515	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 1,319.33	1,319.33	794.39	- 12/2009	03/2019	- 111(R)	0/0
516	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,185.64	772.88	- 09/2009	03/2019	- 114(R)	0/0
517	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 4,454.18	9,658.00	5,918.56	03/2011 -	03/2020	108(O) -	0/0
518	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 1,849.60	2,650.00	377.44	- 03/2023	03/2023	- 0(R)	0/0
519	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	230.24	- -	03/2017	- -	0/0
520	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	- -	0/0
521	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 1,160.47	1,160.47	3.66	- -	03/2022	- -	0/1
522	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,825.00	1,154.14	03/2008 06/2008	03/2020	144(O) 141(R)	0/0
523	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	780.00	363.52	- -	03/2019	- -	0/0
524	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,145.00	363.12	- -	03/2020	- -	0/0
525	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	690.91	03/2010 -	03/2017	84(O) -	0/0
526	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
527	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 236.37	275.08	141.55	03/2012 12/2013	03/2016	-	0/0
528	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,451.00	1,936.18	03/2014 -	03/2020	72(O) -	0/0
529	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 2,393.48	4,600.00	1,023.83	04/2014 -	03/2020	71(O) -	0/0
530	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51(O) -	0/0
531	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	829.74	280.08	03/2015 -	03/2019	48(O) -	0/0
532	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 658.07	658.07	523.26	03/2014 03/2019	03/2019	60(O) 0(R)	0/0
533	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL ,	04/2004	293.74 155.56	229.33	141.72	12/2010 03/2017	03/2017	75(O) 0(R)	0/0
534	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 -	385.60	49.69	03/2013 -	03/2020	84(O) -	0/0
535	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	58.86	03/2012 -	03/2019	84(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
536	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	171.69	03/2015 -	03/2020	60(O) -	0/0
537	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM ,	04/1998	227.90 -	509.00	352.77	12/2012 -	03/2016	-	0/0
538	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM ,	04/1996	1,676.31 -	7,000.00	6,630.23	03/2009 -	03/2017	96(O) -	0/0
539	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	362.55	- 03/2022	03/2022	- 0(R)	0/0
540	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	177.28	- -	03/2020	- -	0/0
541	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	399.63	19.72	- -	03/2019	- -	0/0
542	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	446.00 -	1,037.15	711.78	- -	03/2019	- -	0/0
543	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN ,	04/2010	739.65 -	872.22	812.05	- -	03/2017	- -	0/1
544	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	- -	0/0
545	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE ,	04/2008	822.39 -	1,480.83	1,551.40	- -	03/2018	- -	0/1
546	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 -	1,857.00	1,363.36	03/2007 -	03/2016	-	0/0
547	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 972.52	972.52	99.11	- -	03/2019	- -	1/1
548	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	- -	0/0
549	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL ,	04/2011	209.77 -	445.00	461.09	- -	03/2018	- -	0/0
550	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55 -	330.00	129.05	- -	03/2018	- -	0/0
551	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	27.27	- -	03/2021	- -	0/0
552	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 210.00	394.28	148.33	- -	03/2017	- -	0/0
553	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	.79	- -	03/2019	- -	0/0
554	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,078.13	- -	03/2018	- -	0/0
555	AMBARİ FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	508.00	380.01	- -	03/2019	- -	0/0
556	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	33.20	- -	03/2019	- -	0/0
557	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11(O) -	0/0
558	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 332.14	332.14	169.99	- 03/2019	03/2019	- 0(R)	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 2,491.43	2,491.43	331.52	- 03/2023	03/2023	- 0(R)	0/0
560	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	85.63	- 03/2021	03/2021	- 0(R)	0/0
561	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.11	03/2017 -	03/2017	0(O) -	0/0
562	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 579.03	720.59	528.58	03/2017 -	03/2017	0(O) -	0/0
563	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	102.10	- 03/2019	03/2019	- 0(R)	0/0
564	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	28.59	- 03/2022	03/2022	- 0(R)	0/0
565	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE ,	04/2007	98.74 203.00	381.39	338.87	- 03/2017	03/2017	- 0(R)	0/0
566	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	701.23	- -	03/2019	- -	0/1
567	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	283.43	- -	03/2020	- -	0/0
568	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,111.99	1,579.27	352.12	- 03/2020	03/2021	- 12(R)	0/0
569	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 -	810.28	7.55	- -	03/2021	- -	0/0
570	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	356.19	- 03/2020	03/2020	- 0(R)	0/1
571	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	112.11	- -	03/2020	- -	0/0
572	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU ,	04/2011	190.10 -	355.96	240.92	- -	03/2019	- -	0/0
573	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	226.10	- 03/2020	03/2020	- 0(R)	0/5
574	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	124.02	- -	03/2020	- -	0/0
575	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	176.03	- 11/2015	03/2020	- 52(R)	0/2
576	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022	0(O) -	0/0
577	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	-	- 03/2024	03/2024	- 0(R)	0/0
578	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	2,425.00	-	- 03/2024	03/2024	- 0(R)	0/0
579	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	5.90	- 03/2022	03/2022	- 0(R)	0/0
580	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 -	2,449.91	-	- 03/2023	03/2023	- 0(R)	0/0
581	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	1.17	- 03/2023	03/2023	- 0(R)	0/0
582	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	-	- 03/2023	03/2023	- 0(R)	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
583	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 -	1,035.16	-	- 03/2022	03/2022	- 0(R)	0/0
584	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 -	637.95	-	- 03/2022	03/2022	- 0(R)	0/0
585	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	11.08	- 03/2021	03/2021	- 0(R)	0/0
586	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	10.00	03/2020 -	03/2020	0(O) -	0/6
587	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	16.01	03/2021 -	03/2021	0(O) -	0/0
588	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	2.89	03/2021 -	03/2021	0(O) -	0/0
589	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	5.92	03/2021 -	03/2021	0(O) -	0/0
590	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	701.61	6.15	03/2021 -	03/2021	0(O) -	0/0
591	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	5.65	03/2021 -	03/2021	0(O) -	0/0
592	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,232.32	4.04	- -	03/2021	- -	0/0
593	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	870.96	.02	- -	03/2021	- -	0/0
594	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	3.48	- -	03/2021	- -	0/0
595	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	-	03/2021 -	03/2021	0(O) -	3/3
596	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	969.83	31.23	03/2020 -	03/2020	0(O) -	0/0
597	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	108.73	03/2021 -	03/2021	0(O) -	0/0
598	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	927.01	599.94	03/2019 -	03/2019	0(O) -	0/0
599	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,514.45	1,024.69	03/2020 -	03/2020	0(O) -	0/0
600	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	960.18	580.79	03/2020 -	03/2020	0(O) -	0/0
601	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	513.66	03/2020 -	03/2020	0(O) -	0/0
602	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	722.82	03/2019 -	03/2019	0(O) -	0/0
603	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 2,478.23	2,478.23	.04	03/2022 03/2022	03/2022	0(O) 0(R)	0/1
604	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 582.13	582.13	-	03/2020 03/2020	03/2020	0(O) 0(R)	0/1
605	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	4.01	03/2020 -	03/2020	0(O) -	0/0
606	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
607	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12(O) -	0/0
608	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	358.87	03/2018 -	03/2018	0(O) -	0/0
609	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	168.12	03/2019 -	03/2019	0(O) -	0/0
610	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN ,	04/2012	471.82 -	471.82	18.81	03/2019 -	03/2019	0(O) -	0/0
611	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	293.89	03/2018 -	03/2018	0(O) -	0/0
612	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	127.56	03/2018 -	03/2018	0(O) -	0/0
613	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	170.54	03/2019 -	03/2019	0(O) -	0/0
614	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	65.39	03/2019 -	03/2019	0(O) -	0/0
615	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	217.84	03/2019 -	03/2019	0(O) -	0/0
616	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE ,	04/2006	614.54 -	613.00	515.46	-	04/2014	-	0/0
617	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM ,	04/2003	4,300.00 -	4,520.00	4,272.46	-	05/2015	-	0/0
618	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM ,	04/2007	180.09 -	180.00	155.12	-	05/2011	-	0/0
619	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	1,500.00 -	5,000.00	4,464.70	04/2008 12/2011	06/2018	122(O) 78(R)	0/0
620	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,004.90	674.28	- 06/2021	06/2021	- 0(R)	0/0
621	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	343.00	267.31	-	06/2017	-	0/0
622	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	310.45	- 03/2021	06/2022	- 15(R)	0/0
623	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH ,	09/2007	687.20 -	950.00	963.74	03/2010 -	06/2017	87(O) -	0/0
624	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	06/2016	-	0/0
625	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	195.64	317.83	-	06/2017	-	0/0
626	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27(O) -	0/0
627	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE ,	04/2007	313.24 -	554.70	461.48	01/1999 06/2017	06/2017	221(O) 0(R)	0/0
628	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA ,	03/2011	165.16 -	234.71	223.63	03/2015 -	07/2015	-	0/0
629	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE ,	04/1992	315.64 -	315.00	310.73	-	08/2014	-	0/0
630	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 -	355.00	325.37	-	09/2015	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
631	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	620.00	-	- -	09/2019	- -	0/0
632	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 245.39	245.39	210.67	12/2008 -	10/2015	-	0/0
633	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE ,	12/2006	170.00 -	436.00	438.63	03/2011 -	10/2011	-	0/0
634	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA ,	03/2006	201.00 230.00	230.00	246.93	- 10/2015	10/2015	-	0/0
635	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	-	06/2005 -	11/2015	-	0/0
636	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]JER,MULTI STATE ,	04/2010	157.94 157.94	157.94	48.72	- -	11/2018	- -	0/0
637	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.23	680.93	06/1999 12/2020	12/2020	258(O) 0(R)	0/0
638	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	19,565.00	14,922.23	11/2002 -	12/2018	193(O) -	0/0
639	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	1,040.88	- 12/2020	12/2020	- 0(R)	0/0
640	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 1,160.54	1,776.81	1,181.00	03/1998 -	12/2019	261(O) -	0/0
641	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 843.45	966.98	924.00	02/2009 12/2017	12/2017	106(O) 0(R)	0/0
642	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH ,	03/1997	677.97 1,595.40	1,679.13	1,741.68	- -	12/2016	-	0/0
643	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.70	294.14	02/2015 -	12/2019	58(O) -	0/0
644	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	318.00	299.61	02/2006 -	12/2019	166(O) -	0/1
645	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	516.40	441.77	03/2010 -	12/2017	93(O) -	0/3
646	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	3,161.58	1,212.65	03/2016 -	12/2020	57(O) -	0/0
647	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 -	2,619.00	685.23	03/2016 -	12/2018	33(O) -	0/0
648	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 1,030.29	1,030.29	664.87	03/2012 -	12/2016	-	0/0
649	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 -	1,389.62	1,641.30	03/2014 -	12/2017	45(O) -	0/0
650	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	199.75	201.23	- -	12/2017	- -	0/0
651	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	1.52	- -	12/2020	- -	0/0
652	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,266.89	191.18	- -	12/2020	- -	0/0
653	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
654	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 855.16	860.00	566.46	- -	12/2018	- -	0/0
655	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46(O) 0(R)	0/0
656	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	12/2016	-	0/0
657	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL,WEST BENGAL ,	04/2010	171.02 -	235.00	230.26	06/2013 -	12/2016	-	0/0
658	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	51.09	- -	12/2017	- -	0/0
659	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	464.49	- 12/2018	12/2018	- 0(R)	0/0
660	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	325.99	03/2016 -	12/2017	21(O) -	0/0
661	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 266.00	266.00	104.21	- -	12/2012	-	0/0
662	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	209.00	58.31	12/2016 -	12/2016	-	0/0
663	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 678.54	678.54	.75	- 12/2018	12/2018	- 0(R)	0/38
664	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.23	12/2020 -	12/2020	0(O) -	0/1
665	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.12	12/2020 -	12/2020	0(O) -	1/1
666	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020	0(O) -	1/1
667	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM ,	04/2003	971.22 -	966.27	834.11	- -	12/2009	-	0/0
668	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	763.18 1,013.50	1,428.00	480.27	12/2021 -	12/2021	0(O) -	0/0
669	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 604.04	939.00	183.98	12/2021 -	12/2021	0(O) -	0/0
670	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	943.60	-	12/2024 -	12/2024	0(O) -	0/0
671	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	728.10	.34	12/2024 -	12/2024	0(O) -	0/0
672	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025	0(O) -	0/0
673	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	4,295.30	157.32	12/2026 -	12/2026	0(O) -	0/0
674	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.14	12/2025 -	12/2025	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
675	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	652.02	12/2020 -	12/2020	0(O) -	0/0
676	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.65	558.06	12/2020 -	12/2020	0(O) -	0/0
677	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	.20	12/2021 -	12/2021	0(O) -	0/0
678	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL ,	04/1983	36.80 274.41	614.00	259.27	- -	-	-	0/0
679	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	782.83	12/2010 -	-	-	0/0
680	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
681	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA ,	02/1998	242.42 369.70	1,542.41	1,025.78	- 05/2009	-	-	0/1
682	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.61	- -	-	-	0/6
683	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MTP, WEST BENGAL ,	03/2000	1,049.69 3,385.14	3,404.92	3,544.30	12/2006 -	-	-	0/0
684	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	320.39	03/2012 -	-	-	0/0
685	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
686	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 332.92	477.88	495.40	03/2012 -	-	-	0/0
687	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	- -	-	-	0/0
688	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
689	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
690	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
691	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	.19	- -	-	-	0/0
692	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
693	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
694	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	- -	-	-	0/0
695	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
696	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
697	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	26.06	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
698	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	44.38	- -	-	-	0/0
699	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
700	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	-	- -	-	-	0/0
701	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
702	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.32	- -	-	-	0/0
703	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	-	- -	-	-	0/0
704	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	-	- -	-	-	0/0
705	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR,HARYANA ,	05/2015	400.00 -	400.00	-	- -	-	-	0/0
706	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	483.83	03/2003 -	-	-	0/0
	Total		3,51,974.29 -	4,40,707.90	1,29,314.65				11/104
	ROAD TRANSPORT AND HIGHWAYS								
707	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	-	-	0/0
708	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA , PPP (BOT)	11/2009	567.00 -	567.00	1,055.94	11/2013 -	-	-	0/0
709	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	316.63	06/2013 -	-	-	0/0
710	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
711	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	104.19	03/2016 -	-	-	3/4
712	YAN TO NIRMAL SERE REHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
713	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	-	03/2016 -	-	-	0/2
714	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
715	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD, TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
716	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA , EPC	03/2015	298.33 -	298.33	32.92	- -	-	-	0/4
717	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	32.86	- -	-	-	0/4
718	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	55.73	- -	-	-	0/4
719	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	-	02/2015 -	-	-	0/4
720	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 200.69	207.40	192.97	07/2014 -	-	-	0/1
721	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	-	- -	-	-	0/1
722	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	-	- -	-	-	0/4
723	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	-	- -	-	-	0/0
724	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.05	- -	-	-	0/0
725	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.31	156.26	69.34	- 03/2013	-	-	0/0
726	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	-	12/2012 -	-	-	0/0
727	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	-	- -	-	-	0/0
728	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	-	12/2015 -	-	-	0/0
729	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	49.93	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
730	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	50.74	- -	-	-	0/0
731	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	77.55	- -	-	-	0/0
732	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
733	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	217.74	- -	-	-	0/0
734	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	-	- -	-	-	0/0
735	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	59.97	01/2015 -	-	-	0/0
736	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	53.14	01/2015 -	-	-	0/0
737	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	-	05/2014 -	-	-	0/0
738	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	-	04/2014 -	-	-	0/0
739	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
740	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	-	03/2011 -	-	-	0/0
741	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
742	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	-	10/2010 -	-	-	0/0
743	TWO LANING OF LALPUL - MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2011 -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
744	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	-	05/2012 -	-	-	0/0
745	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	-	08/2013 -	-	-	0/0
746	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	-	08/2013 -	-	-	0/0
747	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
748	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	-	02/2011 -	-	-	0/0
749	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 268.92	268.92	-	08/2015 -	-	-	0/0
750	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	-	07/2015 -	-	-	0/0
751	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	-	- -	-	-	0/0
752	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.53	- -	-	-	0/0
753	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	101.48	- -	-	-	0/0
754	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	96.10	- -	-	-	0/0
755	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.42	- -	-	-	0/0
756	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
757	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	-	- -	-	-	0/0
758	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	27.40	- -	-	-	0/0
759	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.69	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
760	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	267.63	- -	-	-	0/0
761	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	-	- -	-	-	0/0
762	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
763	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
764	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	18.13	- -	-	-	0/0
765	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
766	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	135.20	- -	-	-	0/0
767	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	-	- -	-	-	0/0
768	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	-	- -	-	-	0/0
769	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	56.97	- -	-	-	0/0
770	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
771	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	-	- -	-	-	0/0
772	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	-	- -	-	-	0/0
773	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	-	- -	-	-	0/0
774	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	-	- -	-	-	0/0
775	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	-	- -	-	-	0/0
776	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
777	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	41.76	- -	-	-	0/0
778	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	22.00	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
779	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	-	- -	-	-	0/0
780	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	45.25	- -	-	-	0/0
781	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	42.99	- -	-	-	0/0
782	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.26	07/2008 -	-	-	0/0
783	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	-	- -	-	-	0/0
784	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	-	- -	-	-	0/0
785	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	-	- -	-	-	0/0
786	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	-	03/2014 -	09/2016	-	0/0
787	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	.45	- -	-	-	0/0
788	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	-	- -	-	-	0/0
789	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	-	- -	-	-	0/0
790	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	-	- -	-	-	0/0
791	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	-	- -	-	-	0/0
792	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	-	- -	-	-	0/0
793	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	-	- -	-	-	0/0
794	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	-	- -	-	-	0/0
795	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	-	- -	-	-	0/0
796	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	-	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
797	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	-	- -	-	-	0/0
798	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	-	- -	-	-	0/0
799	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	-	- -	-	-	0/0
800	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	-	- -	-	-	0/0
801	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	-	- -	-	-	0/0
802	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	-	- -	-	-	0/0
803	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	-	- -	-	-	0/0
804	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	-	- -	-	-	0/0
805	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	-	- -	-	-	0/0
806	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	-	- -	-	-	0/0
807	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	-	08/2014 -	08/2014	-	0/0
808	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	56.06	07/2016 -	07/2016	-	0/0
809	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	13.50	07/2016 -	07/2016	-	0/0
810	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	15.90	05/2016 -	05/2016	-	0/0
811	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	-	05/2016 -	05/2016	-	0/0
812	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	-	10/2016 -	10/2016	-	0/0
813	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	-	11/2015 -	11/2015	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
814	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	-	-	-	-	0/0
815	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	-	-	-	-	0/0
816	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	-	06/2019 -	06/2019	0(0) -	0/0
817	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	-	-	-	-	0/0
818	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	-	-	-	-	0/0
819	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	-	-	-	-	0/0
820	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	34.84	-	-	-	0/0
821	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	-	-	-	-	0/0
822	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	-	-	-	-	0/0
823	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	-	-	-	-	0/0
824	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	-	-	-	-	0/0
825	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	-	-	-	-	0/0
826	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	-	-	-	-	0/0
827	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	-	-	-	-	0/0
828	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	-	-	-	-	0/0
829	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	-	-	-	-	0/0
830	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	-	-	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
831	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	-	- -	-	-	0/0
832	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	-	- -	-	-	0/0
833	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	-	- -	-	-	0/0
834	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA ,	09/2016	950.69 -	950.69	-	- -	-	-	0/0
835	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	-	- -	-	-	0/0
836	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI, MULTI STATE ,	09/2016	1,244.10 -	1,244.10	-	- -	-	-	0/0
837	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA ,	09/2016	1,004.67 -	1,004.67	-	- -	-	-	0/0
838	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	-	- -	-	-	0/0
839	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	-	- -	-	-	0/0
840	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA ,	11/2016	400.25 -	400.25	-	- -	-	-	0/0
841	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA ,	11/2016	446.17 -	446.17	-	- -	-	-	0/0
842	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA ,	11/2016	290.73 -	290.73	-	- -	-	-	0/0
843	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA ,	10/2016	1,008.96 -	1,008.96	-	- -	-	-	0/0
844	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	-	- -	-	-	0/0
845	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	-	- -	-	-	0/0
846	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	-	- -	-	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
847	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	-	- -	-	-	0/0
848	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	-	- -	-	-	0/0
849	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	-	- -	-	-	0/0
850	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	-	- -	-	-	0/0
851	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	478.32	05/2013 -	01/2017	44(O) -	0/0
852	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,418.23	07/2013 -	01/2017	42(O) -	0/0
853	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	2,126.85	04/2015 -	01/2017	21(O) -	0/0
854	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN ,	01/2014	368.15 -	368.15	231.79	01/2016 -	01/2017	12(O) -	0/0
855	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	-	01/2017 -	01/2017	0(O) -	0/0
856	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0(O) -	0/4
857	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	31.31	01/2019 -	01/2019	0(O) -	1/4
858	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	269.47	01/2017 -	01/2017	0(O) -	0/0
859	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	-	01/2018 -	01/2018	0(O) -	0/0
860	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	-	01/2017 -	01/2017	0(O) -	0/0
861	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL ,	10/2015	361.15 -	361.15	-	- -	01/2018	- -	0/0
862	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	-	- -	01/2019	- -	0/0
863	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,393.23	07/2017 -	01/2018	6(O) -	0/0
864	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	1,786.45	- -	01/2018	- -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
865	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	315.07	- -	01/2019	- -	0/0
866	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	1,996.84	01/2018 -	01/2018	0(O) -	0/0
867	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	-	01/2016 -	01/2016	-	0/4
868	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	12.60	01/2016 -	01/2016	-	0/4
869	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	-	- -	01/2019	- -	0/0
870	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	442.64	02/2009 -	02/2017	96(O) -	0/0
871	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	204.64	11/2008 -	02/2017	99(O) -	0/0
872	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	316.94	06/2008 06/2016	02/2017	104(O) 8(R)	0/0
873	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 309.56	309.56	436.38	04/2010 09/2016	02/2017	82(O) 5(R)	0/0
874	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	4,554.86	06/2015 -	02/2017	20(O) -	0/0
875	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	02/2017	45(O) -	0/0
876	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,898.25	09/2015 -	02/2017	17(O) -	0/0
877	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	02/2017	14(O) -	0/3
878	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,643.50	11/2016 -	02/2018	15(O) -	0/0
879	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	-	02/2017 -	02/2017	0(O) -	0/1
880	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	46.68	02/2017 -	02/2017	0(O) -	0/1
881	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017	0(O) -	0/0
882	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24(O) -	0/1

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
883	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	129.39	02/2018 -	02/2018	0(O) -	0/0
884	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54	483.45	02/2018 -	02/2018	0(O) -	0/0
885	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	159.09	02/2018 -	02/2018	0(O) -	0/0
886	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	331.09	08/2016 -	02/2017	6(O) -	0/0
887	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	69.06	02/2016 -	02/2016	-	0/0
888	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	-	02/2011 -	02/2011	-	0/0
889	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	-	02/2011 -	02/2011	-	0/0
890	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	-	02/2018 -	02/2018	0(O) -	0/0
891	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	-	02/2018 -	02/2018	0(O) -	0/0
892	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	02/2015	-	0/0
893	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	69.82	-	02/2018	-	0/0
894	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	-	02/2017 -	02/2017	0(O) -	0/0
895	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	299.99	11/2008 -	03/2017	100(O) -	0/0
896	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	266.81	04/2009 -	03/2017	95(O) -	0/0
897	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	03/2017	108(O) 5(R)	0/0
898	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	204.93	05/2008 12/2016	03/2017	106(O) 3(R)	0/0
899	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM ,	12/2003	212.00 -	212.00	125.45	09/2007 -	03/2017	114(O) -	0/0
900	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	403.94	07/2009 -	03/2017	92(O) -	0/0
901	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	472.83	05/2010 -	03/2017	82(O) -	0/0
902	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 2,782.54	3,237.87	3,407.69	09/2012 -	03/2017	54(O) -	2/3
903	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.74	08/2011 -	03/2017	67(O) -	2/2

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
904	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,206.10	04/2013 -	03/2017	47(O) -	0/0
905	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	741.37	08/2012 -	03/2017	55(O) -	0/0
906	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH , PPP (BOT)	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	03/2017	45(O) -	0/0
907	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,503.50	08/2014 -	03/2017	31(O) -	0/0
908	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	1,968.37	03/2013 -	03/2017	48(O) -	0/0
909	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	03/2017	40(O) -	0/0
910	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,972.30	08/2013 -	03/2017	43(O) -	0/0
911	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	654.59	02/2014 -	03/2017	37(O) -	0/0
912	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	901.28	03/2014 -	03/2017	36(O) -	0/0
913	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	534.11	04/2014 -	03/2017	35(O) -	0/0
914	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,802.57	08/2013 -	03/2018	55(O) -	0/0
915	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,718.55	06/2014 -	03/2017	33(O) -	0/0
916	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	398.85	01/2014 -	03/2017	38(O) -	0/0
917	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,266.60	1,084.00	09/2016 -	03/2017	6(O) -	0/0
918	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN , PPP (BOT)	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017	11(O) -	0/0
919	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	178.69	03/2016 -	03/2017	12(O) -	0/0
920	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	-	03/2015 -	03/2015	-	0/0
921	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	-	03/2015 -	03/2015	-	0/0
922	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	-	03/2015 -	03/2015	-	0/0
923	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018	0(O) -	0/4
924	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	-	03/2016 -	03/2016	-	0/0
925	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	155.59	01/2016 -	03/2017	14(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
926	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	54.02	03/2018 -	03/2018	0(O) -	0/0
927	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	304.01	01/2016 -	03/2017	14(O) -	0/0
928	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	414.93	01/2016 -	03/2017	14(O) -	0/0
929	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017	0(O) -	0/0
930	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	-	03/2017 -	03/2017	0(O) -	0/0
931	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	6.33	03/2018 -	03/2018	0(O) -	0/0
932	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL , EPC	01/1991	322.00 -	322.00	66.59	03/2018 -	03/2018	0(O) -	0/0
933	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017	0(O) -	0/0
934	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017	0(O) -	0/0
935	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	509.86	08/2016 -	03/2017	7(O) -	0/0
936	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	170.97	03/2018 -	03/2018	0(O) -	0/0
937	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	155.16	03/2018 -	03/2018	0(O) -	0/0
938	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	-	- -	03/2019	- -	0/0
939	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	208.59	03/2018 -	03/2018	0(O) -	0/0
940	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	29.92	- -	03/2019	- -	0/0
941	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	70.46	03/2018 -	03/2018	0(O) -	0/0
942	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	209.82	03/2018 -	03/2018	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
943	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018	0(O) -	0/0
944	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	83.52	03/2018 -	03/2018	0(O) -	0/0
945	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	1,173.20	08/2015 -	03/2017	19(O) -	0/0
946	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	389.73	- -	03/2017	- -	0/0
947	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,383.55	11/2015 -	03/2017	16(O) -	0/0
948	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	280.36	03/2016 -	03/2019	36(O) -	0/0
949	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,145.48	06/2012 -	03/2018	69(O) -	0/0
950	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,680.00	- -	03/2017	- -	0/0
951	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31(O) -	0/0
952	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	-	- -	03/2019	- -	0/0
953	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) .NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	138.15	- -	03/2018	- -	0/0
954	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	212.33	05/2016 -	03/2017	10(O) -	0/0
955	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	53.85	06/2016 -	03/2017	9(O) -	0/0
956	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	91.92	05/2016 -	03/2017	10(O) -	0/0
957	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU , PPP (BOT)	09/2010	852.00 -	852.00	905.31	03/2013 -	04/2017	49(O) -	0/0
958	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	977.69	07/2013 -	04/2017	45(O) -	0/0
959	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37(O) -	0/0
960	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHUDEAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	84.84	- -	04/2018	- -	0/1

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
961	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	128.93	04/2017 -	04/2017	0(O) -	0/4
962	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN ,	10/2014	206.12 -	206.12	161.60	04/2017 -	04/2017	0(O) -	0/0
963	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	04/2017	7(O) -	0/0
964	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	175.75	04/2017 -	04/2017	0(O) -	0/0
965	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA ,	10/2015	562.34 -	562.34	71.13	04/2018 -	04/2018	0(O) -	0/0
966	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	04/2015	-	0/0
967	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	208.00	04/2018 -	04/2018	0(O) -	0/0
968	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	-	- -	04/2019	- -	0/0
969	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	8.63	- -	04/2018	- -	0/0
970	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	-	- 04/2018	04/2018	- 0(R)	0/0
971	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16(O) -	0/0
972	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	-	- 04/2018	04/2018	- 0(R)	0/0
973	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	-	- -	04/2019	- -	0/0
974	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	155.20	- -	04/2018	- -	0/0
975	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	87.58	04/2018 -	04/2018	0(O) -	0/0
976	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	237.03	04/2009 -	05/2017	97(O) -	0/0
977	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	226.32	02/2010 -	05/2017	87(O) -	0/0
978	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA , PPP (BOT)	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58(O) -	3/3
979	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	769.68	09/2013 -	05/2017	44(O) -	0/0
980	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,567.40	09/2014 -	05/2017	32(O) -	0/0
981	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24(O) -	2/4

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
982	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	45.48	05/2018 -	05/2018	0(O) -	0/4
983	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	43.99	05/2018 -	05/2018	0(O) -	1/4
984	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	157.97	05/2017 -	05/2017	0(O) -	0/0
985	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	41.87	05/2017 -	05/2017	0(O) -	0/0
986	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	185.13	11/2016 -	05/2017	6(O) -	0/0
987	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	205.09	05/2015 -	05/2015	-	0/0
988	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.54	05/2017 -	05/2017	0(O) -	0/0
989	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	-	05/2017 -	05/2017	0(O) -	0/0
990	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	166.22	05/2017 -	05/2017	0(O) -	0/0
991	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 223.00	208.87	219.99	05/2016 -	05/2016	-	0/0
992	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 265.35	229.41	67.86	05/2018 -	05/2018	0(O) -	0/0
993	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	-	04/2015 -	05/2016	-	0/0
994	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	92.86	05/2018 -	05/2018	0(O) -	1/4
995	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	- -	0/0
996	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	44.69	- -	05/2018	- -	0/0
997	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	26.88	- -	05/2018	- -	0/0
998	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	33.72	- -	05/2018	- -	0/0
999	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	54.33	- -	05/2018	- -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1000	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH ,	02/2015	327.32 -	327.32	162.33	05/2017 -	05/2017	0(O) -	0/0
1001	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	413.78	- -	05/2018	- -	0/0
1002	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	-	- 05/2018	05/2018	- 0(R)	0/0
1003	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	104.75	- -	05/2018	- -	0/0
1004	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	-	- -	05/2019	- -	0/0
1005	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	63.82	- -	05/2018	- -	0/0
1006	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	4.54	- -	05/2019	- -	0/0
1007	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 230.00	208.00	316.60	04/2008 01/2017	06/2017	110(O) 5(R)	0/0
1008	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	- -	06/2017	- -	3/3
1009	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,131.46	05/2013 -	06/2017	49(O) -	0/0
1010	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	717.40	01/2014 -	06/2017	41(O) -	0/0
1011	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	552.91	11/2013 -	06/2017	43(O) -	0/0
1012	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA , PPP (BOT)	03/2011	500.29 -	500.29	875.61	08/2013 -	06/2017	46(O) -	0/0
1013	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	2,228.56	09/2014 -	06/2017	33(O) -	0/0
1014	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,281.38	08/2013 -	06/2017	46(O) -	0/0
1015	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	107.87	- -	06/2017	- -	0/4
1016	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	-	06/2014 -	06/2016	-	0/2
1017	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	06/2018	0(O) -	0/4
1018	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	06/2018	0(O) -	0/4
1019	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	80.27	06/2018 -	06/2018	0(O) -	0/3

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1020	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	-	06/2018 -	06/2018	0(O) -	0/0
1021	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	44.40	12/2017 -	06/2018	6(O) -	0/0
1022	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	-	06/2018 -	06/2018	0(O) -	0/0
1023	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	16.61	06/2016 -	06/2018	24(O) -	0/0
1024	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	11.60	06/2016 -	06/2018	24(O) -	0/0
1025	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	23.39	06/2018 -	06/2018	0(O) -	0/0
1026	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	36.07	- -	06/2017	- -	0/0
1027	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	30.21	- -	06/2017	- -	0/0
1028	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019	0(O) -	0/0
1029	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018	0(O) -	0/0
1030	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	13.56	06/2018 -	06/2018	0(O) -	0/0
1031	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	39.63	06/2018 -	06/2018	0(O) -	0/0
1032	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	21.92	07/2018 -	06/2018	-1(O) -	0/0
1033	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	31.96	06/2018 -	06/2018	0(O) -	0/0
1034	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	20.05	- -	06/2017	- -	0/0
1035	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	- -	0/0
1036	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	-	- -	06/2018	- -	0/0
1037	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	-	- -	06/2018	- -	0/0
1038	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	15.98	06/2016 -	06/2016	-	0/0
1039	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	-	06/2019 -	06/2019	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1040	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN , PPP (BOT)	06/2016	725.95 -	725.95	-	06/2019 -	06/2019	0(O) -	0/0
1041	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	-	06/2019 -	06/2019	0(O) -	0/0
1042	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	255.60	05/2017 -	06/2017	1(O) -	0/0
1043	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	35.33	06/2016 -	06/2016	-	0/4
1044	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	-	- -	06/2017	- -	0/0
1045	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	46.64	05/2016 -	06/2017	13(O) -	0/0
1046	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,889.98	07/2015 -	07/2017	24(O) -	0/0
1047	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	68.07	07/2016 -	07/2016	-	0/12
1048	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE-DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	07/2016	-	0/1
1049	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	63.38	07/2017 -	07/2017	0(O) -	0/0
1050	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	141.89	07/2017 -	07/2017	0(O) -	0/0
1051	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	16.61	07/2018 -	07/2018	0(O) -	0/0
1052	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	257.45	07/2018 -	07/2018	0(O) -	0/0
1053	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	-	- -	07/2018	- -	0/0
1054	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	27.95	- -	07/2018	- -	0/0
1055	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	-	- -	07/2018	- -	0/0
1056	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,864.02	11/2011 -	08/2017	69(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1057	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23(O) -	0/4
1058	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	-	08/2015 -	08/2015	-	0/0
1059	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	75.32	08/2016 -	08/2016	-	0/0
1060	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	393.88	09/2015 -	08/2016	-	0/0
1061	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,130.00	08/2016 -	08/2017	12(O) -	0/0
1062	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	312.54	-	08/2018	-	0/0
1063	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	-	08/2015 -	08/2015	-	0/0
1064	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	08/2017	0(O) -	0/0
1065	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	22.18	08/2014 -	08/2014	-	0/0
1066	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	103.80	-	08/2018	-	0/0
1067	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	-	-	08/2018	-	0/0
1068	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	145.03	01/2017 -	08/2017	7(O) -	0/0
1069	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	881.43	02/2013 -	09/2017	55(O) -	0/0
1070	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	621.88	07/2013 -	09/2017	50(O) -	0/0
1071	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	407.21	07/2014 -	09/2017	38(O) -	0/0
1072	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	363.06	06/2014 -	09/2017	39(O) -	0/0
1073	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,856.83	02/2014 -	09/2017	43(O) -	2/2
1074	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017	0(O) -	0/0
1075	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	32.70	09/2017 -	09/2017	0(O) -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1076	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI,JHARKHAND ,	09/2015	341.61 -	341.61	195.07	09/2017 -	09/2017	0(O) -	0/0
1077	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	12(O) -	0/0
1078	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	192.55	08/2015 -	09/2016	-	0/0
1079	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	-	09/2010 -	09/2010	-	0/0
1080	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	-	09/2010 -	09/2010	-	0/0
1081	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,064.23	10/2011 -	09/2017	71(O) -	0/0
1082	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,038.84	07/2013 -	10/2017	51(O) -	0/0
1083	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT , PPP (BOT)	03/2012	828.00 -	828.00	871.49	09/2014 -	10/2017	37(O) -	0/3
1084	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	24.63	- -	10/2017	- -	0/4
1085	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24(O) -	0/0
1086	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	49.00	10/2018 -	10/2018	0(O) -	1/4
1087	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	-	10/2016 -	10/2016	-	0/0
1088	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	218.10	10/2016 -	10/2016	-	0/0
1089	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	17.71	10/2016 -	10/2016	-	0/0
1090	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 251.92	218.63	106.15	10/2017 -	10/2017	0(O) -	0/0
1091	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	200.21	10/2016 -	10/2016	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1092	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	21.03	10/2016 -	10/2016	-	0/0
1093	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	-	10/2016 -	10/2016	-	0/0
1094	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	10/2010	-	0/0
1095	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	206.52	10/2017 -	10/2017	0(O) -	0/0
1096	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1097	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	-	10/2013 -	10/2013	-	0/0
1098	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	-	07/2016 -	10/2016	-	0/0
1099	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	-	- -	10/2018	- -	0/0
1100	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	9.90	10/2016 -	10/2016	-	0/4
1101	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	14.71	10/2017 -	10/2017	0(O) -	0/0
1102	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	69.69	10/2017 -	10/2017	0(O) -	0/0
1103	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,251.64	03/2013 -	11/2017	56(O) -	0/0
1104	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	119.70	11/2016 -	11/2016	-	0/2
1105	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	113.36	11/2016 -	11/2016	-	0/4
1106	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017	0(O) -	0/0
1107	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.22	185.82	214.86	- 11/2014	11/2014	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1108	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	-	11/2014 -	11/2016	-	0/4
1109	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	11/2016	-	0/4
1110	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0(O) -	0/4
1111	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	125.00	11/2018 -	11/2018	0(O) -	0/4
1112	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24(O) -	0/0
1113	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24(O) -	0/0
1114	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	414.31	11/2017 -	11/2017	0(O) -	0/0
1115	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	-	11/2015 -	11/2015	-	0/0
1116	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	405.44	11/2016 -	11/2017	12(O) -	0/0
1117	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	266.74	- -	11/2017	- -	0/0
1118	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	6.35	- -	11/2017	- -	0/0
1119	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	444.03	- -	11/2018	- -	0/0
1120	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	-	11/2017 -	11/2017	0(O) -	0/0
1121	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	136.47	11/2014 -	11/2014	-	0/0
1122	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	-	- -	11/2018	- -	0/0
1123	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL ,	03/2016	229.37 -	229.37	-	- -	11/2018	- -	0/0
1124	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	-	- -	11/2018	- -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1125	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	-	- -	11/2018	- -	0/0
1126	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	-	11/2016 -	11/2016	-	0/0
1127	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5(O) -	0/0
1128	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA , PPP (BOT)	03/2011	359.00 -	359.00	2.74	09/2013 -	12/2016	-	0/0
1129	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT , PPP (BOT)	12/2010	1,008.50 -	1,008.50	1,284.34	06/2013 -	12/2017	54(O) -	0/3
1130	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48(O) -	0/0
1131	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55(O) -	0/0
1132	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52(O) -	0/0
1133	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	623.74	10/2013 -	12/2017	50(O) -	0/0
1134	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	2,962.27	05/2014 -	12/2016	-	0/0
1135	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,492.40	06/2014 -	12/2017	42(O) -	0/0
1136	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA , PPP (BOT)	07/2011	586.00 -	586.00	160.54	01/2014 -	12/2016	-	0/0
1137	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL , PPP (BOT)	02/2011	580.43 -	580.43	279.95	08/2013 -	12/2017	52(O) -	0/0
1138	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	321.08	10/2013 -	12/2017	50(O) -	0/0
1139	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	690.66	06/2015 -	12/2017	30(O) -	0/0
1140	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL , PPP (ANNUITY)	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34(O) -	0/0
1141	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA , PPP (BOT)	10/2013	283.25 -	283.25	182.91	10/2015 -	12/2017	26(O) -	0/0
1142	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	-	12/2016 -	12/2016	-	0/4
1143	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	-	12/2015 -	12/2016	-	0/2
1144	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	-	12/2015 -	12/2016	-	0/0
1145	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	77.11	01/2016 -	12/2016	-	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1146	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA ,	06/2015	996.37 -	996.37	2.18	12/2017 -	12/2017	0(O) -	0/0
1147	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	12/2017	0(O) -	0/0
1148	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	-	12/2018 -	12/2018	0(O) -	0/4
1149	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	-	12/2018 -	12/2018	0(O) -	0/0
1150	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	89.22	12/2017 -	12/2017	0(O) -	0/0
1151	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	356.65	12/2018 -	12/2018	0(O) -	0/0
1152	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	87.51	- -	12/2017	- -	0/0
1153	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	146.28	- -	12/2017	- -	0/0
1154	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	-	12/2016 -	12/2016	- -	0/0
1155	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	12/2016	- -	0/0
1156	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	-	- -	-	- -	0/0
1157	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	-	- -	-	- -	0/0
	Total		2,92,045.44 -	2,96,459.23	1,29,331.46				26/191
	<u>SHIPPING AND PORTS</u>								
1158	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	- -	0/0
1159	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA ,	03/2007	245.67 -	409.83	350.68	04/2009 -	-	- -	0/0
1160	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL,TAMIL NADU ,	09/2015	210.00 -	210.00	-	01/2018 -	01/2018	0(O) -	0/0
1161	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067]KPL,TAMIL NADU ,	12/2014	274.85 -	274.85	-	04/2017 -	04/2017	0(O) -	0/1
1162	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065]KPL,TAMIL NADU , PPP (ANNUITY)	10/2013	198.94 -	235.15	-	06/2017 -	06/2017	0(O) -	0/1
1163	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	525.49	03/2006 03/2016	12/2016	- -	0/0

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1164	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 669.46	669.46	415.01	12/2010 12/2018	12/2018	96(O) 0(R)	0/0
1165	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	258.33	-	12/2017 -	12/2017	0(O) -	0/1
	Total		4,117.75 -	5,085.02	2,122.39				0/3
	<u>TELECOMMUNICATIONS</u>								
1166	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30(O) -	0/70
1167	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	-	06/2017 -	06/2017	0(O) -	0/0
1168	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	13,334.00	5,231.54	07/2015 09/2017	09/2017	26(O) 0(R)	0/0
	Total		15,863.43 -	15,763.43	5,533.11				0/70
	<u>URBAN DEVELOPMENT</u>								
1169	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	-	08/2014 -	-	-	0/0
1170	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	5.00	- -	-	-	0/6
1171	CONSTRUCTION OC 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]MEGA,MADHYA PRADESH , EPC	05/2011	164.00 -	164.00	13.97	01/2018 -	01/2018	0(O) -	0/0
1172	CONSTRUCTION OF 1003 NOS (900 NOS TYPE II 54 NOS TYPE III 33 NOS TYPE IV 16 NOS TYPE V) FAMILY QUAR - [N28000096]CPWD,MADHYA PRADESH ,	05/2016	164.30 -	164.30	9.13	01/2018 -	01/2018	0(O) -	0/0
1173	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	32.86	03/2016 02/2018	02/2018	23(O) 0(R)	1/6
1174	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	1,753.99	02/2019 -	03/2020	13(O) -	0/0
1175	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	80.60	09/2015 03/2017	03/2018	30(O) 12(R)	3/11
1176	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,219.21	12.76	10/2019 -	03/2020	5(O) -	0/0
1177	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARAstra - [N28000074]CPWD,MAHARASHTRA ,	12/2012	315.00 315.00	315.00	258.64	06/2015 08/2016	03/2017	21(O) 7(R)	0/8

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1178	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI ,	05/2012	405.01 405.01	405.01	-	12/2014 03/2017	03/2017	27(O) 0(R)	2/3
1179	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	1,188.76	03/2018 -	03/2018	0(O) -	0/0
1180	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	1,933.60	03/2019 -	03/2019	0(O) -	0/0
1181	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA ,	05/2006	6,395.00 14,405.01	14,405.01	14,282.31	06/2011 12/2015	04/2017	70(O) 16(R)	3/3
1182	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017	54(O) 0(R)	0/1
1183	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI(MOD - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	2.39	- 04/2019	04/2019	- 0(R)	0/2
1184	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH ,	12/2012	188.87 -	188.87	143.39	12/2015 12/2016	06/2017	18(O) 6(R)	0/0
1185	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	332.72	188.26	09/2016 01/2017	06/2017	9(O) 5(R)	0/0
1186	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	67.62	03/2017 -	06/2017	3(O) -	0/5
1187	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017	-1(O) -	0/0
1188	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN , Central Sector Projects	08/2014	350.02 479.87	479.87	233.50	03/2015 03/2017	07/2017	28(O) 4(R)	0/0
1189	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	178.88	05/2017 08/2017	08/2017	3(O) 0(R)	6/12
1190	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASHTRA - [N28000073]CPWD,MAHARASHTRA ,	06/2010	205.00 170.62	170.62	139.57	03/2012 08/2016	10/2017	67(O) 14(R)	7/20
1191	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,118.00	2,087.10	11/2019 -	11/2019	0(O) -	1/7
1192	CONSTRUCTION OF CIVIL STRUCTURES AN OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA ,	07/2015	154.00 -	154.00	33.07	11/2015 -	11/2017	24(O) -	0/0
1193	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI ,	09/2011	38,585.00 -	38,585.00	26,425.53	03/2016 -	12/2016	-	0/0
1194	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 270.83	270.83	98.76	11/2014 05/2017	12/2017	37(O) 7(R)	0/0
1195	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	159.77	03/2016 12/2017	12/2017	21(O) 0(R)	0/0
1196	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 14,600.00	14,600.00	13,305.52	12/2015 -	12/2017	24(O) -	11/24
1197	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	-	0/0
1198	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	51.38	03/2015 10/2017	12/2017	33(O) 2(R)	0/10

List of ongoing Projects Costing Rs. 150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(January 2017)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1199	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	-	- -	-	-	0/0
	Total		1,40,978.94 -	1,49,046.42	62,722.90				34/118
	<u>DEFENCE PRODUCTION</u>								
1200	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	167.69	8.38	05/2018 -	05/2018	0(O) -	0/1
1201	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	285.95	14.29	08/2020 -	08/2020	0(O) -	0/1
	Total		453.64 -	453.64	22.67				0/2
	Grand Total		15,28,249.27	16,99,285.76	7,08,958.70				1946/3875


Summary of projects in the Flash Report for the month of January, 2017

Project Implementation - Current Status:

Number of Projects in Previous Month	1186
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects degradation from the status of project during the current month	1
Number of Projects Added in Current Month	20
Number of Projects in Current Month	1201

Brief Analysis

Project Status with respect to Original Schedule: Out of 1201 projects, 8 projects are ahead of schedule, 286 projects are on schedule 329 projects are delayed. 447 projects do not have fixed dates of commissioning. 131 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

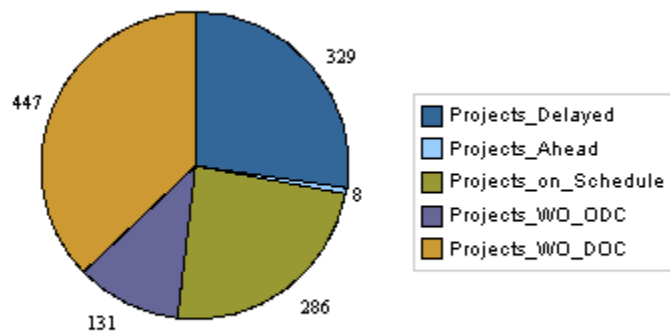


Total No Of Project's:- 1201

Investment Scenario

Total original cost of implementation of 1201 projects when sanctioned, was of the order of Rs. 1528249.27 crore but this was subsequently revised to Rs. 1699285.76 crore implying a cost overrun of 11.2%. The expenditure incurred on these projects till January, 2017 is Rs. 708958.7 crore, which is 41.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

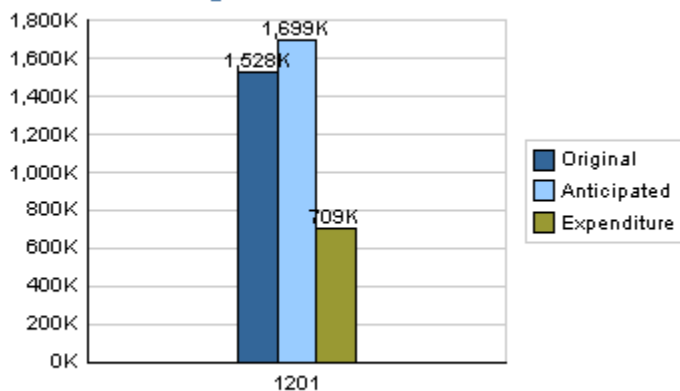

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

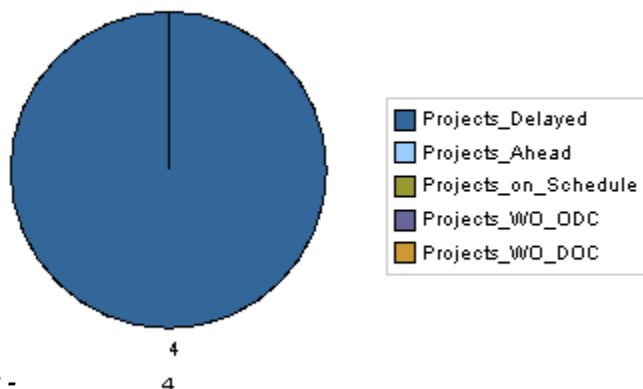


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 52241 crore implying a cost overrun of 29.2%. The expenditure incurred on these projects till January, 2017 is Rs. 43936.82 crore, which is 84.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

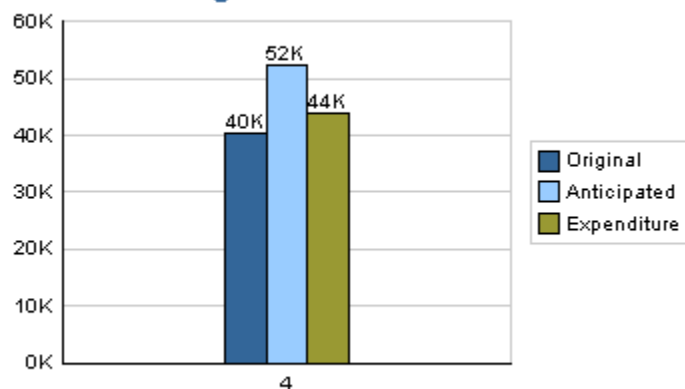

Sector wise current status of projects on the Flash Report

CIVIL AVIATION

Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

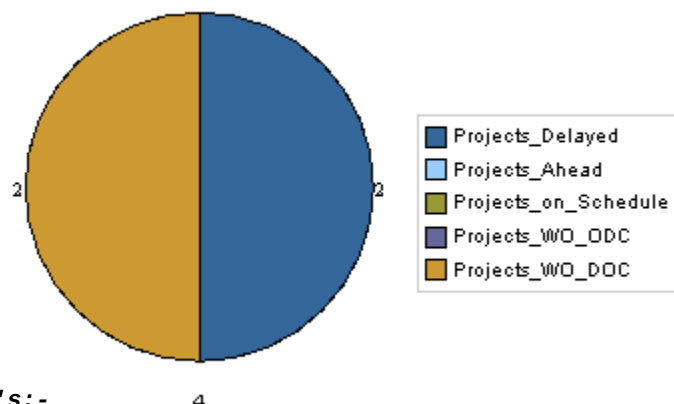


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1177.28 crore but this was subsequently anticipated to Rs. 1556.96 crore implying a cost overrun of 32.3%. The expenditure incurred on these projects till January, 2017 is Rs. 909.38 crore, which is 58.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

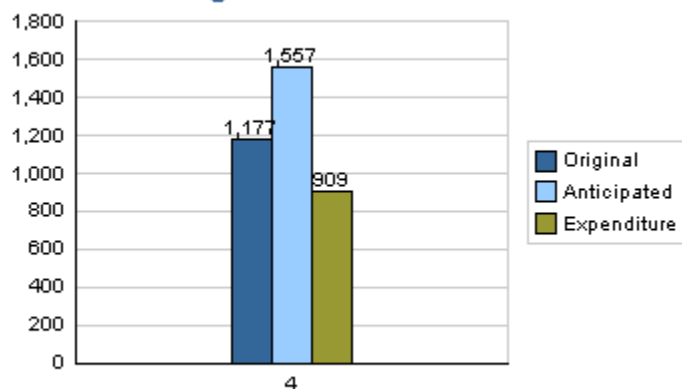

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	87
Number of Projects On Schedule	48
Number of Projects Delayed	39

Brief Analysis

Project Status with respect to Original Schedule: Out of 87 projects, 48 projects are on schedule 39 projects are delayed.

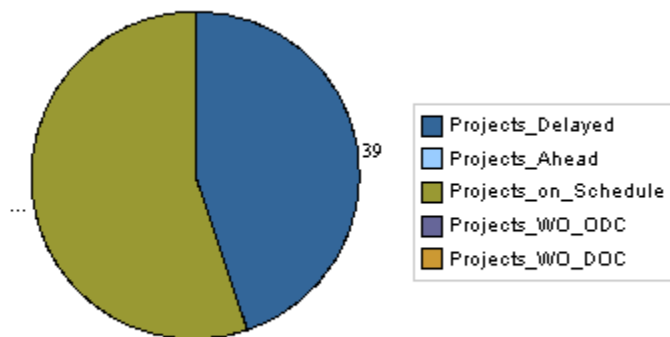


Total No Of Project's:-

87

Investment Scenario

Total original cost of implementation of 87 projects when sanctioned, was of the order of Rs. 85632.34 crore but this was subsequently anticipated to Rs. 85544.13 cr The expenditure incurred on these projects till January, 2017 is Rs. 16510.71 crore, which is 19.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

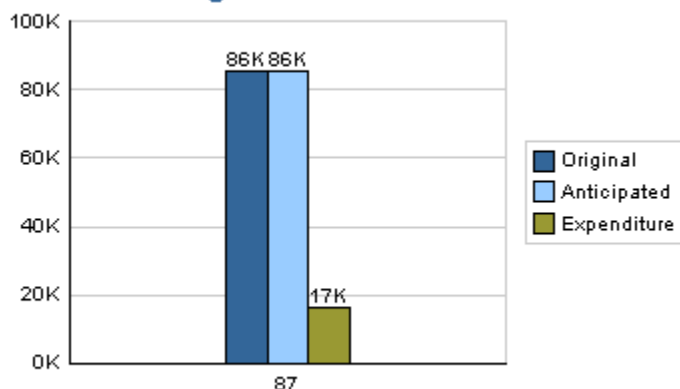

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	2
Number of Projects On Schedule	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project is delayed.

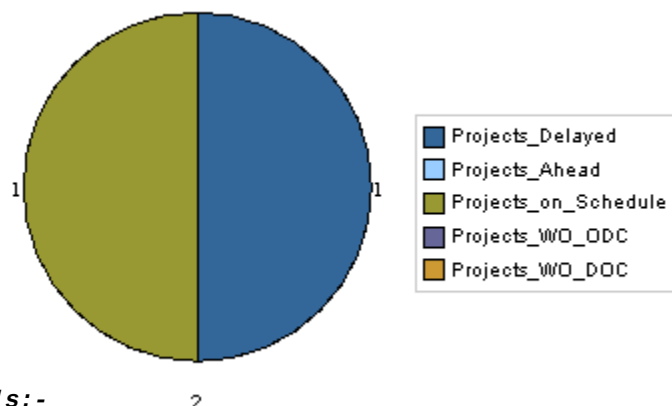


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 680.64 crore but this was subsequently anticipated to Rs. 703.44 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till January, 2017 is Rs. 141.17 crore, which is 20.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

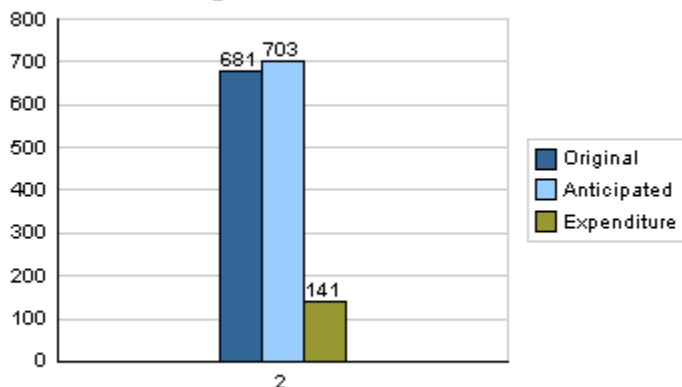

Sector wise current status of projects on the Flash Report

MINES


Current Status:

Number of Projects	4
Number of Projects On Schedule	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule 2 projects do not have fixed dates of commissioning.

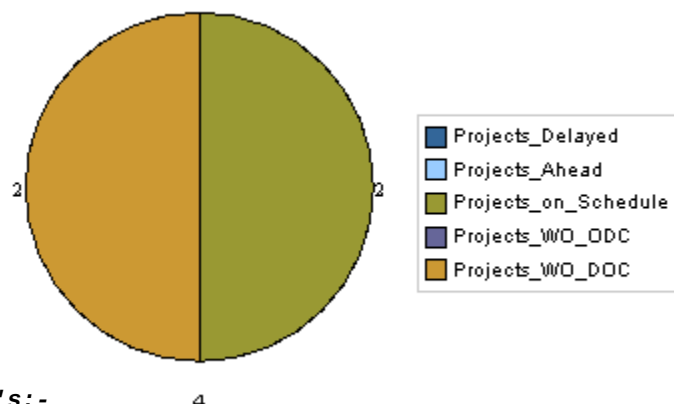


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6773.63 crore but this was subsequently anticipated to Rs. 6773.63 crore The expenditure incurred on these projects till January, 2017 is Rs. 606.08 crore, which is 8.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

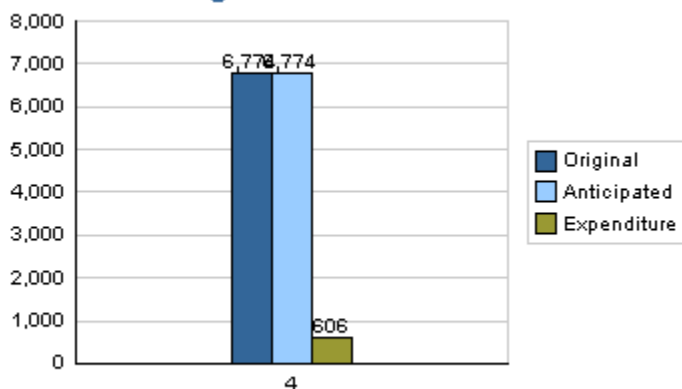

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	33
Number of Projects On Schedule	11
Number of Projects Delayed	14

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 33 projects, 11 projects are on schedule 14 projects are delayed. 7 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

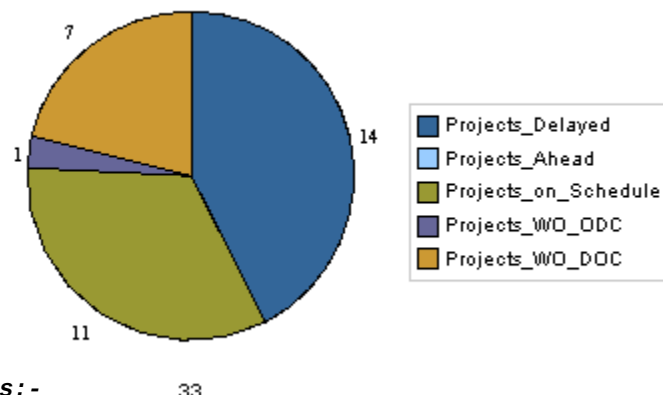


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 33 projects when sanctioned, was of the order of Rs. 56967.14 crore but this was subsequently anticipated to Rs. 57180.82 crore implying a cost overrun of .4%. The expenditure incurred on these projects till January, 2017 is Rs. 35073.5 crore, which is 61.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

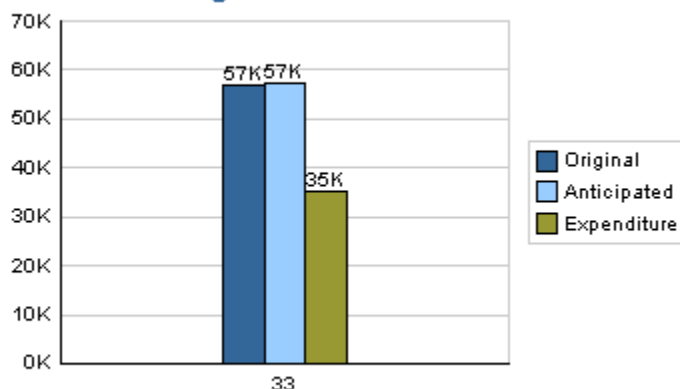

Sector wise current status of projects on the Flash Report

PETROCHEMICALS


Current Status:

Number of Projects 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project does not have fixed dates of commissioning.

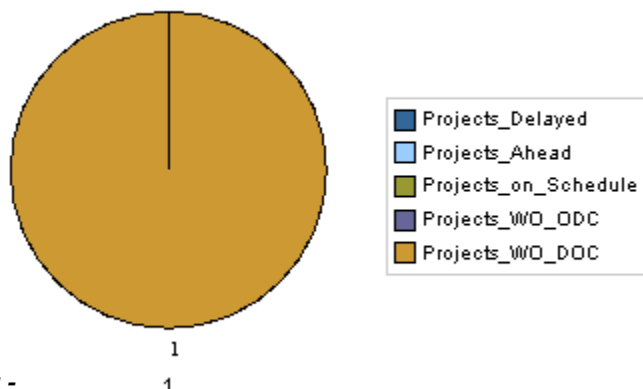


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 5460.61 crore but this was subsequently anticipated to Rs. 9965 crore implying a cost overrun of 82.5%. The expenditure incurred on these projects till January, 2017 is Rs. 9895.57 crore, which is 99.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

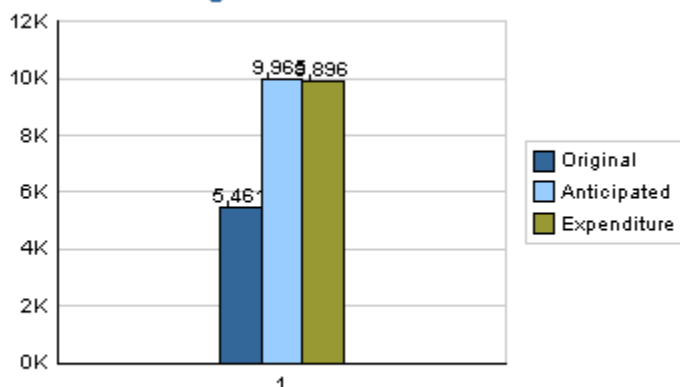

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	89
Number of Projects On Schedule	31
Number of Projects Delayed	36
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	17

Brief Analysis

Project Status with respect to Original Schedule: Out of 89 projects, 4 projects are ahead of schedule, 31 projects are on schedule 36 projects are delayed. 17 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

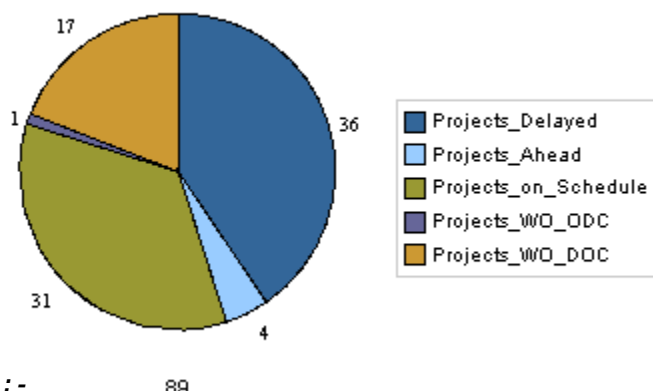


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 89 projects when sanctioned, was of the order of Rs. 185636.77 crore but this was subsequently anticipated to Rs. 186447.26 crore implying a cost overrun of .4%. The expenditure incurred on these projects till January, 2017 is Rs. 54194.71 crore, which is 29.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

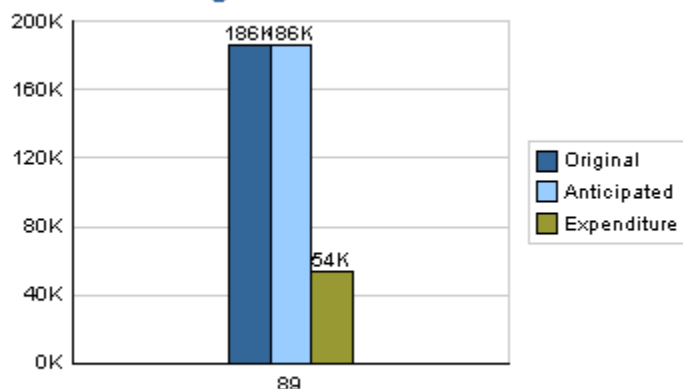

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	121
Number of Projects On Schedule	48
Number of Projects Delayed	60
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 121 projects, 2 projects are ahead of schedule, 48 projects are on schedule 60 projects are delayed. 11 projects do not have fixed dates of commissioning.

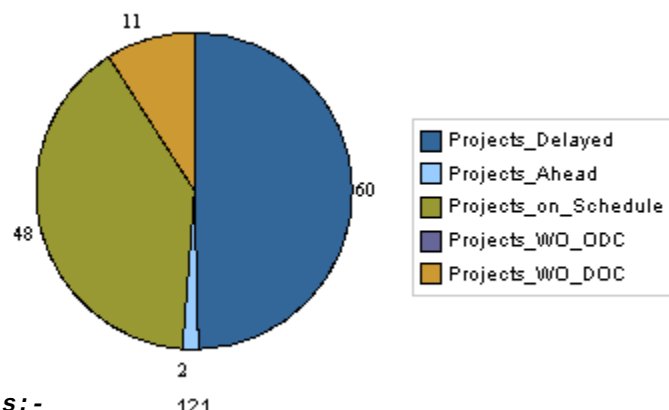


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 121 projects when sanctioned, was of the order of Rs. 334690.29 crore but this was subsequently anticipated to Rs. 383881.2 crore implying a cost overrun of 14.7%. The expenditure incurred on these projects till January, 2017 is Rs. 214784.64 crore, which is 56% of the anticipated cost of the projects.

Figures are in Rs. Crore

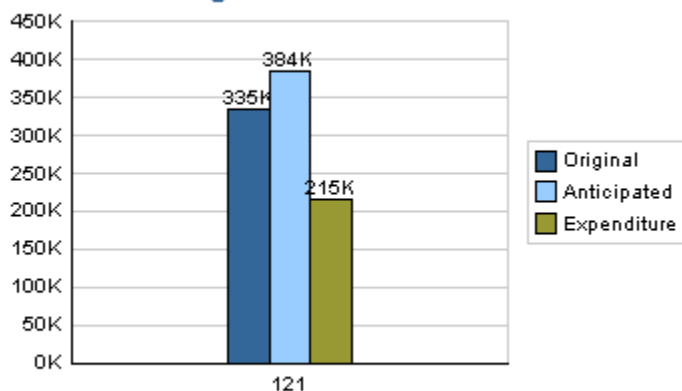

Sector wise current status of projects on the Flash Report


HEAVY INDUSTRY

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1718 crore but this was subsequently anticipated to Rs. 3827.3 crore implying a cost overrun of 122.8%. The expenditure incurred on these projects till January, 2017 is Rs. 2289 crore, which is 59.8% of the anticipated cost of the projects.

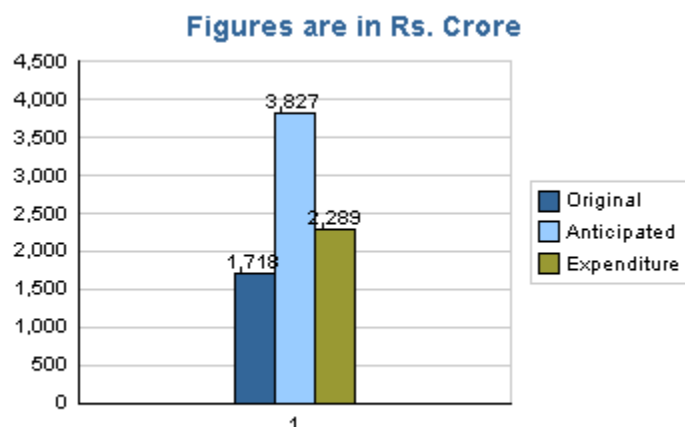

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	13
Number of Projects On Schedule	5
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are on schedule 3 projects are delayed. 5 projects do not have fixed dates of commissioning.

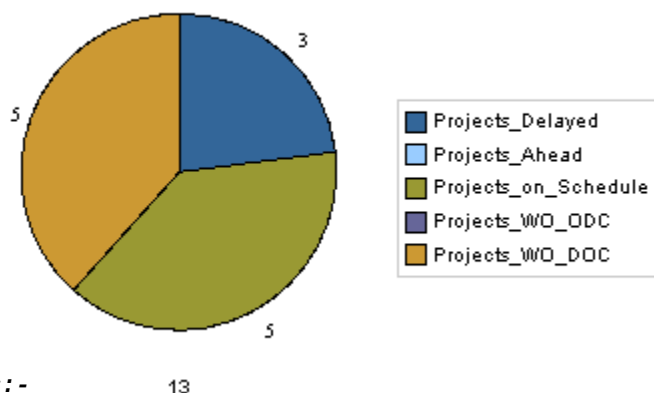


Total No Of Project's:-

13

Investment Scenario

Total original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 3637.08 crore but this was subsequently anticipated to Rs. 3649.38 crore implying a cost overrun of .3%. The expenditure incurred on these projects till January, 2017 is Rs. 1569.94 crore, which is 43% of the anticipated cost of the projects.

Figures are in Rs. Crore

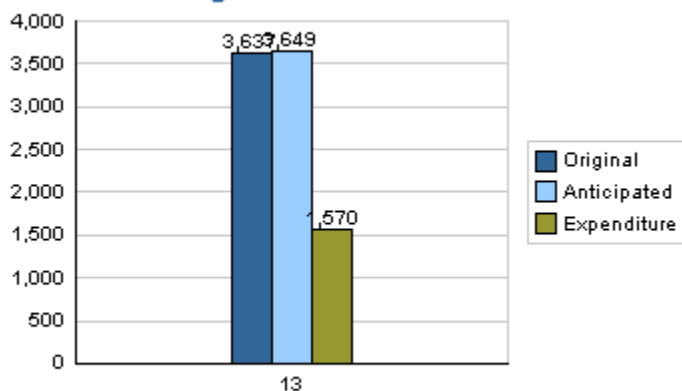

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	347
Number of Projects On Schedule	42
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	72
Number of Projects Without Date Of Commissioning	194

Brief Analysis

Project Status with respect to Original Schedule: Out of 347 projects, 42 projects are on schedule 39 projects are delayed. 194 projects do not have fixed dates of commissioning. 72 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

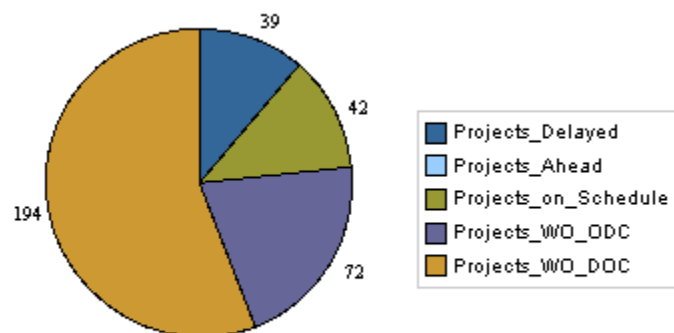


Total No Of Project's:-

347

Investment Scenario

Total original cost of implementation of 347 projects when sanctioned, was of the order of Rs. 351974.29 crore but this was subsequently anticipated to Rs. 440707.9 crore implying a cost overrun of 25.2%. The expenditure incurred on these projects till January, 2017 is Rs. 129314.65 crore, which is 29.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

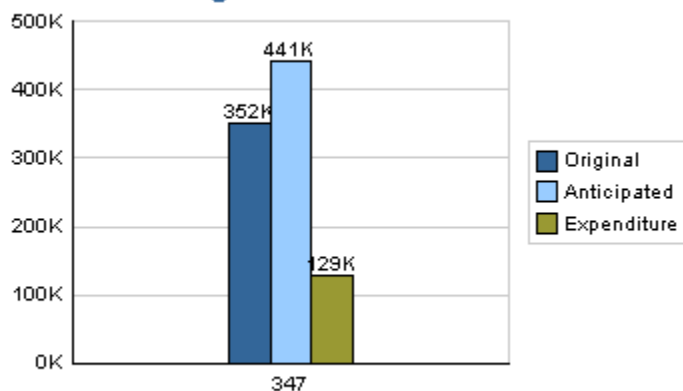

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	451
Number of Projects On Schedule	86
Number of Projects Delayed	108
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	56
Number of Projects Without Date Of Commissioning	200

Brief Analysis

Project Status with respect to Original Schedule: Out of 451 projects, 1 project is ahead of schedule, 86 projects are on schedule 108 projects are delayed. 200 projects do not have fixed dates of commissioning. 56 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

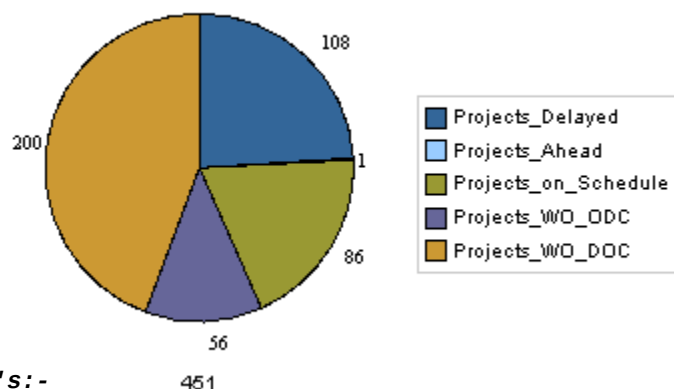

Investment Scenario

Total original cost of implementation of 451 projects when sanctioned, was of the order of Rs. 292045.44 crore but this was subsequently anticipated to Rs. 296459.23 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till January, 2017 is Rs. 129331.46 crore, which is 43.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

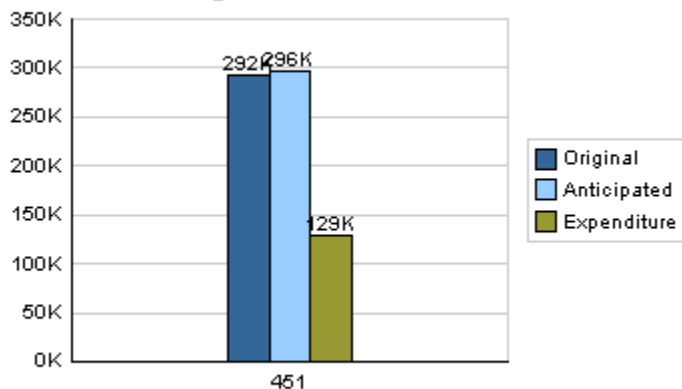

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	8
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 8 projects, 4 projects are on schedule 1 project is delayed. 3 projects do not have fixed dates of commissioning.

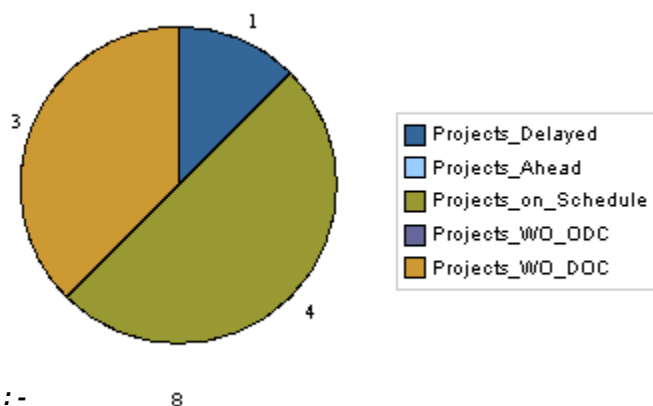


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 4117.75 crore but this was subsequently anticipated to Rs. 5085.02 crore implying a cost overrun of 23.5%. The expenditure incurred on these projects till January, 2017 is Rs. 2122.39 crore, which is 41.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

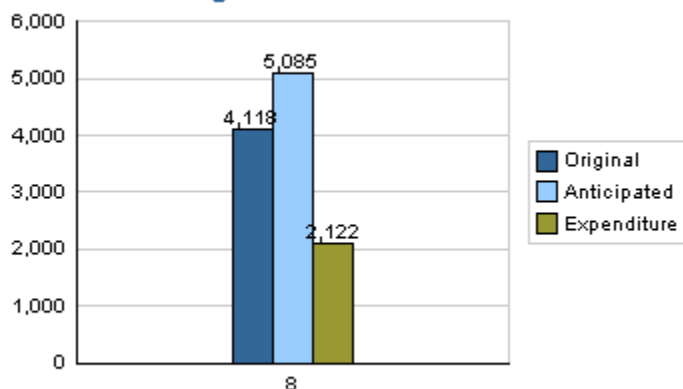

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	3
Number of Projects On Schedule	1
Number of Projects Delayed	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 1 project is on schedule 2 projects are delayed.

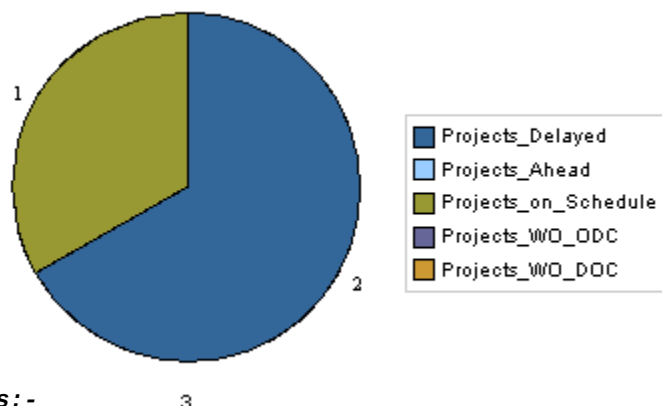


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15863.43 crore but this was subsequently anticipated to Rs. 15763.43 cr The expenditure incurred on these projects till January, 2017 is Rs. 5533.11 crore, which is 35.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

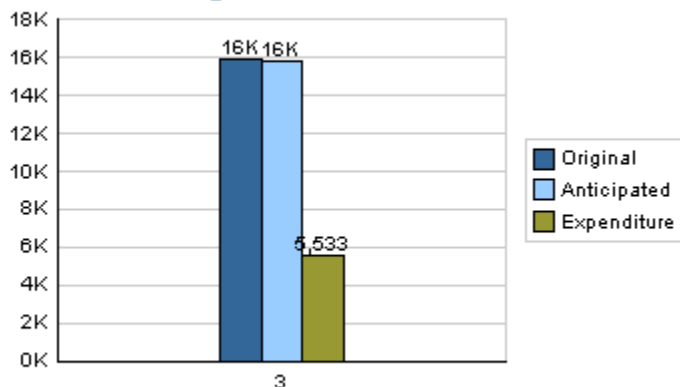

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	31
Number of Projects On Schedule	5
Number of Projects Delayed	19
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 31 projects, 1 project is ahead of schedule, 5 projects are on schedule 19 projects are delayed. 5 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

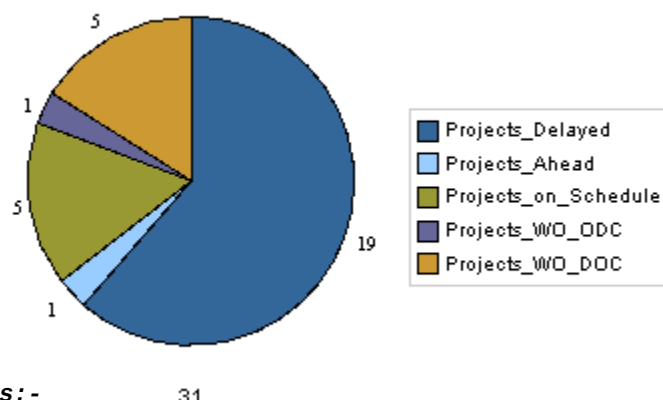


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 31 projects when sanctioned, was of the order of Rs. 140978.94 crore but this was subsequently anticipated to Rs. 149046.42 crore implying a cost overrun of 5.7%. The expenditure incurred on these projects till January, 2017 is Rs. 62722.9 crore, which is 42.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

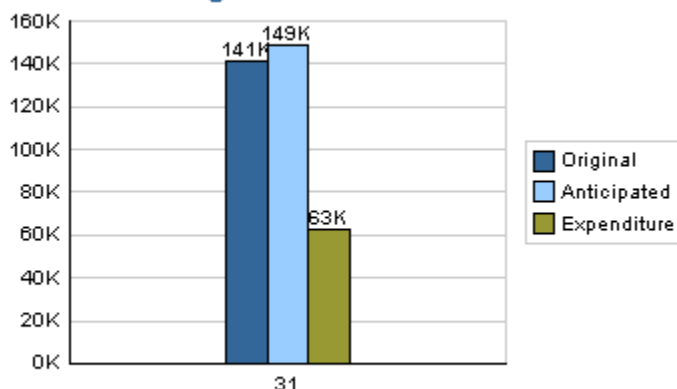

Sector wise current status of projects on the Flash Report


DEFENCE PRODUCTION

Current Status:

Number of Projects	2
Number of Projects On Schedule	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are on schedule

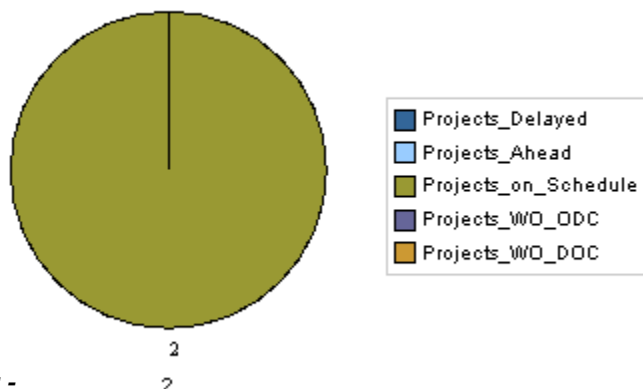


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore. The expenditure incurred on these projects till January, 2017 is Rs. 22.67 crore, which is 5% of the anticipated cost of the projects.

Figures are in Rs. Crore

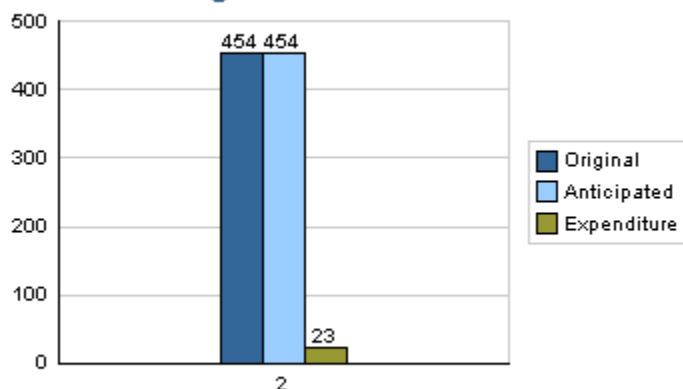

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JANUARY 2017)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	441.33	26.35
2	ANDHRA PRADESH	54	94,347.36	98,047.72	11,603.06
3	ARUNACHAL PRADESH	20	13,401.94	29,214.96	15,942.48
4	ASSAM	50	39,028.48	57,069.66	40,865.67
5	BIHAR	75	67,446.38	80,514.59	42,231.56
6	CHHATISGARH	42	97,016.69	1,00,033.44	57,352.69
7	D & N HAVELI	1	6,086.08	6,086.08	1,763.35
8	DELHI	17	50,925.07	50,831.89	29,819
9	GOA	10	4,379.12	4,361.51	655.34
10	GUJARAT	45	39,313.44	43,025.13	26,264
11	HARYANA	21	13,724.68	15,697.8	9,291.35
12	HIMACHAL PRADESH	12	12,531.81	18,931.08	7,941.04
13	JAMMU AND KASHMIR	10	27,408.66	46,614.79	31,607.5
14	JHARKHAND	46	46,319.35	49,550.69	16,221.51
15	KARNATAKA	44	76,696.44	94,581.65	40,827.69
16	KERALA	19	33,504.08	35,120.13	15,888.01
17	MADHYA PRADESH	52	53,511.21	57,894.21	19,202.89
18	MAHARASHTRA	100	1,61,202.7	1,70,218.5	57,018.32
19	MANIPUR	2	944.25	9,874.69	5,969.94
20	MEGHALAYA	6	7,108.02	9,025	885.15
21	MIZORAM	5	2,001.2	6,965.67	2,292.46
22	MULTI STATE	168	2,70,141.26	2,51,399.99	87,888.14
23	NAGALAND	3	6,420	8,570	171.69
24	ODISHA	66	70,255.03	77,749.09	19,658.21
25	PUNJAB	26	14,507.23	14,511.23	3,346.84
26	RAJASTHAN	65	45,091.11	46,852.62	21,015.18
27	SIKKIM	5	2,149.08	5,138.08	868.39
28	TAMIL NADU	48	69,394.91	84,085.18	60,445.4
29	TELANGANA	34	24,623	27,006.92	5,301.82
30	TRIPURA	11	4,400.64	9,459.94	5,213.12
31	UTTAR PRADESH	79	1,02,641.68	1,06,041.58	29,528.22
32	UTTARAKHAND	11	16,558.99	18,940.91	6,825.21
33	WEST BENGAL	53	54,854.77	65,429.7	35,027.12
TOTAL		1,201	15,28,249.27	16,99,285.76	7,08,958.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	13171	17270	21994
CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	454.71
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
3	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	321.95
4	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	185.94
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	215.34
6	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	418.97	-	481.31
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
7	SAFDARJUNG HOSPITAL, NEW DELHI- REDEVELOPMENT and OTHERS-EMERGENCY BLOCK	HSCC	11/2013	196.7	-	209
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	1718	-	2289
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6086.47
10	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	8795.49
11	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	3642.04	-	4800.42
12	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	573.99	1337.76	1341.09
13	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	509.66	-	635.96
14	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	232.34	-	237.09
15	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	1940.13	-	2281.56

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
16	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	608.02	631.43
17	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	124.43	926.23	983.96
18	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	680.93
19	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	2500	-	14922.23
20	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	304	-	350.76
21	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	532.98
22	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	295	1289.92	1391.3
23	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	1160.54	1181
24	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	527.54
25	KARUR-SALEM(NL), SR	SR	02/1997	155.55	774.9	848.7
26	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	155.74	843.45	924
27	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	677.97	1595.4	1741.68
28	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	-	4464.7
29	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	218.24	372.09	557.98
30	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	194.07	-	226.39
31	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	891.01
32	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	452.71
33	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	782.83
34	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	242.42	369.7	1025.78
35	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	744.71	849.98
36	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	198.17
37	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	781.02	842.81
38	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	100	535.13	621.08

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
39	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.61
40	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	733	-	2419.18
41	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	1049.69	3385.14	3544.3
42	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	92.63	228.08	320.04
43	JIND-SONEPAT (NL),NR	NR	01/2004	238.56	717.15	742.57
44	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	674.28
45	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	301.64	-	772.88
46	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	166.16	-	363.32
47	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	4454.18	5918.56
48	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	267.31
49	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	230.24
50	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	183.23	-	294.14
51	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	344.04
52	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	136.62	-	373.73
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	332.92	495.4
54	GOELKERA-MANOHARPUR,(LD)(SER)	RVNL	03/1997	261.7	-	299.61
55	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	743	-	1154.14
56	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	441.77
57	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	687.2	-	963.74
58	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	170	-	438.63
59	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	363.52
60	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	363.12
61	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	690.91

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
62	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	1936.18
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	482	874.57	929.12
64	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	167.73	220.45
65	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	1389.62	-	1641.3
66	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.3
67	KATAKHAL TO BHAIIRABI	NFR	04/1998	227.9	-	352.77
68	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	1676.31	-	6630.23
69	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	317.83
70	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	201.23
71	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	446	-	711.78
72	VIRAMGAM-SURENDRANAGAR (DL)	WR	04/2010	279.4	-	325.37
73	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	739.65	-	812.05
74	TAMLUK-BASULYA-SUTAHATA DOUBLING	RVNL	04/2010	171.02	-	230.26
75	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	331.69
76	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
77	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	464.49
78	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	822.39	-	1551.4
79	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	-	1363.36
80	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	209.77	-	461.09
81	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	280.75
82	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI	NFR	04/1999	523.17	-	1078.13
83	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	380.01
84	PEN ROHA DOUBLING	CR	04/2007	98.74	203	338.87

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
85	PANVEL PEN DOUBLING	CR	04/2006	96.16	260.16	272.97
86	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	313.24	-	461.48
87	JHARSUGUDA-RENGALI DOUBLING	ECOR	03/2006	201	230	246.93
88	DELANG-PURI DOUBLING	ECOR	03/2011	165.16	-	223.63
89	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	190.1	-	240.92
90	HOSADURGA - CHICKAJAJUR (28.89 KM)	SWR	04/2010	203.4	203.4	272.67
91	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.54

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
92	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	442.64
93	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	237.03
94	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	299.99
95	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	204.64
96	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	200	-	266.81
97	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	316.94
98	NALBARI T BIJNI (AS-7)	NHAI	12/2003	208	230	316.6
99	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	204.93
100	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	403.94
101	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	309.56	436.38
102	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	940	-	1415.36
103	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	2782.54	3407.69
104	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	1693.75	-	2675.74
105	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	1108	-	3864.02
106	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1206.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
107	TALEGAON-AMRAVATI	NHAI	11/2009	567	-	1055.94
108	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	852	-	905.31
109	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2131.46
110	DEOLI-KOTA	NHAI	01/2011	593	-	1038.84
111	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	617	-	741.37
112	MURADABAD-BAREILY	NHAI	04/2010	1267	-	2666.66
113	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	2498.76	-	2503.5
114	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	1968.37
115	INDORE-DEWAS(NH-3)	NHAI	11/2010	325	-	478.32
116	NASHRI- CHANANI	NHAI	05/2011	2159	-	4554.86
117	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2418.23
118	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	881.43
119	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	1008.5	-	1284.34
120	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
121	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1972.3
122	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1328.82
123	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	977.69
124	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	623.74
125	JORBAT - BARAPANI	NHAI	01/2011	536	-	717.4
126	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	2962.27
127	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	901.28
128	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	534.11

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
129	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	621.88
130	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	552.91
131	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1492.4
132	BHUBANESWAR TO PURI	NHAI	03/2011	500.29	-	875.61
133	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	2228.56
134	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1251.64
135	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2281.38
136	4-LANING OF BRAHAMPURE-FARAKA	NHAI	02/2011	998.79	-	1802.57
137	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1718.55
138	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2567.4
139	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	398.85
140	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1898.25
141	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4700.69
142	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	2126.85
143	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	828	-	871.49
144	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1856.83
145	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	NHAI	10/2013	677.79	-	883.59
146	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1393.23
147	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
148	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3064.23
149	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	NHAI	07/2015	1393	-	1786.45
150	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1383.55
151	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	1996.84

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JANUARY 2017)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
152	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2145.48
153	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	1680
154	TRICHY - KARUR	NHAI	03/2007	516	-	761.26

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
155	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	150	-	525.49
156	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	245.67	-	350.68

STEEL

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
157	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	179.14
158	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1118.64

Details of All Central Sector Infrastructure Projects having Ahead of Schedule w.r.t. Original Schedule

Annexure - III

Costing Rs. 150 crore & above						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	686.90	11/2017 -	04/2017
	Total		972.42 -	972.42	686.90		
	<u>URBAN DEVELOPMENT</u>						
2	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	.00		
	<u>PETROLEUM</u>						
3	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	2,765.05	04/2019 03/2019	03/2019
	Total		6,068.80 -	6,068.80	2,765.05		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	21.92	07/2018 -	06/2018
	Total		667.00 -	667.00	21.92		
	<u>POWER</u>						
5	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]	1/2016	187.04 -	187.04	20.80	06/2018 -	09/2017
	Total		187.04 -	187.04	20.80		
	<u>PETROLEUM</u>						
6	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 247.52	247.52	-	02/2019 -	12/2018
7	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	21.71	05/2019 -	12/2018
8	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	8.43	08/2019 -	12/2018
	Total		1,026.52 -	1,026.52	30.14		
	Grand Total		14,103.57	14,103.57	3,524.81		

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Annexure - IV

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	COAL						
1	AMADAND OPENCASE EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	108.75	03/2021 -	03/2021
2	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
3	MALACHUA OPENCASE PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
4	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	42.57	03/2018 -	03/2018
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	338.01	03/2021 -	03/2021
6	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	88.50	03/2025 -	03/2025
7	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	377.37	03/2018 -	03/2018
8	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.88	03/2021 -	03/2021
9	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	637.53	03/2026 -	03/2026
10	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
11	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.68	03/2022 -	03/2022
12	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	10.87	03/2020 -	03/2020
13	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	68.09	03/2020 -	03/2020
14	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	203.87	03/2022 -	03/2022
15	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	160.89	03/2020 -	03/2020
16	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	929.15	03/2023 03/2023	03/2023
17	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	112.25	03/2021 -	03/2021
18	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	112.48	03/2019 -	03/2019
19	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.36	03/2021 -	03/2021
20	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
21	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	87.32	03/2019 -	03/2019

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
22	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	16.97	03/2019 -	03/2019
23	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,158.41	03/2023 -	03/2023
24	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
25	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.70	03/2023 03/2023	03/2023
26	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	2.03	03/2019 -	03/2019
27	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	94.56	03/2020 -	03/2020
28	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	75.10	12/2019 -	12/2019
29	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
30	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.57	09/2019 -	09/2019
31	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	290.81	03/2020 -	03/2020
32	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.00	795.95	11/2021 -	11/2021
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
34	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
35	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
36	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	71.66	03/2023 -	03/2023
37	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
38	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	111.09	03/2020 -	03/2020
39	GOKUL - [N06000120]	11/2014	267.67 -	267.67	179.27	03/2018 -	03/2018
40	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	26.79	03/2023 -	03/2023
41	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	19.07	03/2019 -	03/2019
42	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	2.40	03/2019 -	03/2019
43	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
44	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	5/2016	687.28 -	687.28	91.73	06/2017 -	06/2017
45	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	63.42	03/2021 -	03/2021

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
46	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	18.31	03/2020 -	03/2020
47	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
48	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	114.50	03/2021 -	03/2021
	Total		65,309.13 -	65,309.13	7,503.17		
	<u>DEFENCE PRODUCTION</u>						
49	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	14.29	08/2020 -	08/2020
50	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	167.69	8.38	05/2018 -	05/2018
	Total		453.64 -	453.64	22.67		
	<u>FERTILISERS</u>						
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	61.66	12/2017 -	12/2017
	Total		482.85 -	494.00	61.66		
	<u>HEALTH AND FAMILY WELFARE</u>						
52	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	140.00	03/2018 -	03/2018
53	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	25.00	08/2018 -	08/2018
54	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	-	05/2018 -	05/2018
55	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	19.00	09/2018 -	09/2018
56	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	152.95	9.00	02/2018 -	02/2018
	Total		1,579.51 -	1,579.51	193.00		
	<u>MINES</u>						
57	UTKAL D AND E COAL MINE PROJECT - [N10000011]	5/2016	534.00 -	534.00	34.50	01/2020 -	01/2020
58	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	0.88	04/2021 -	04/2021
	Total		6,074.00 -	6,074.00	35.38		

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	PETROLEUM						
59	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	658.62	-	03/2023 -	03/2023
60	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	0.53	01/2019 -	01/2019
61	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	390.52 -	390.52	-	03/2019 -	03/2019
62	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	-	09/2017 -	09/2017
63	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	24.54	04/2019 -	04/2019
64	DE-BOTTLENECKING OF SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1,554.08	03/2017 -	03/2017
65	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	84.91	03/2018 -	03/2018
66	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	678.00	5.01	02/2017 -	02/2017
67	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	3.42	09/2019 -	09/2019
68	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION(GUJARAT,RAJASTH - [N16000238]	9/2016	1,879.00 -	1,879.00	9.94	03/2020 -	03/2020
69	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
70	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]	5/2015	2,443.00 -	2,443.00	616.11	12/2017 06/2017	12/2017
71	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	118.59	04/2018 -	04/2018
72	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
73	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,237.43	05/2017 -	05/2017
74	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	105.76	12/2018 -	12/2018
75	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	110.36	09/2018 09/2018	09/2018
76	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	306.51	02/2020 -	02/2020
77	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	626.25	08/2018 -	08/2018
78	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]	5/2016	215.38 -	215.38	108.03	06/2017 06/2017	06/2017
79	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	48.72	11/2019 -	11/2019
80	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	128.56	06/2020 -	06/2020

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
81	BSVI UP GRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	8.95	12/2019 -	12/2019
82	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	-	11/2018 -	11/2018
83	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	72.21	10/2018 -	10/2018
84	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	144.96	01/2018 -	01/2018
85	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,190.69	210.27	04/2018 04/2018	04/2018
86	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	435.00	57.81	03/2017 -	03/2017
87	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	33.30	03/2019 -	03/2019
88	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	2.40	04/2018 -	04/2018
89	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	1,763.35	05/2019 05/2019	05/2019
	Total		93,144.51 -	92,498.43	7,382.00		
	<u>POWER</u>						
90	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017
91	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	93.30	07/2017 -	07/2017
92	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	998.10	03/2018 -	03/2018
93	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	73.10	11/2017 -	11/2017
94	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	104.80	07/2018 -	07/2018
95	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	-	12/2018 -	12/2018
96	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	15.10	05/2018 -	05/2018
97	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
98	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	129.50	07/2018 -	07/2018
99	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	8.00	11/2018 -	11/2018
100	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,892.86	10/2017 -	10/2017
101	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	14.60	04/2019 -	04/2019

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
102	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	-	07/2018 -	07/2018
103	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	1,688.20	04/2018 -	04/2018
104	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	25.20	05/2018 -	05/2018
105	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	0.30	02/2019 -	02/2019
106	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) [N18000235]	11/2016	330.00 -	330.00	-	11/2017 -	11/2017
107	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	2,172.00	03/2019 -	03/2019
108	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	4.90	07/2018 -	07/2018
109	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]	1/2014	1,788.41 -	1,788.41	476.46	09/2017 -	09/2017
110	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	103.30	03/2018 -	03/2018
111	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	6,888.00	09/2017 -	09/2017
112	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	234.00	09/2019 -	09/2019
113	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	94.10	10/2017 -	10/2017
114	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	232.10	04/2017 -	04/2017
115	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	590.00	07/2020 -	07/2020
116	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	1.00	02/2019 -	02/2019
117	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	-	03/2019 -	03/2019
118	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	16.00	01/2019 -	01/2019
119	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	7.10	04/2018 -	04/2018
120	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) [N18000221]	4/2016	287.99 -	287.99	6.10	06/2018 -	06/2018
121	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	2,209.00	09/2019 -	09/2019
122	KANDORNA AND BHANWAD WIND FARM - [N18000234]	11/2016	415.49 -	415.49	24.00	03/2017 -	03/2017
123	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	25.80	01/2018 -	01/2018
124	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.13	48.50	06/2019 -	06/2019

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
125	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	38.10	07/2018 -	07/2018
126	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	-	11/2018 -	11/2018
127	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	1.00	07/2017 -	07/2017
128	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	26.70	03/2018 -	03/2018
129	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	4,863.00	08/2018 -	08/2018
130	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.90	05/2017 -	05/2017
131	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	67.10	12/2018 -	12/2018
132	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	1,668.70	05/2018 -	05/2018
133	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	161.60	05/2019 -	05/2019
134	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	-	03/2018 -	03/2018
135	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	8.40	11/2019 -	11/2019
136	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	5.90	03/2019 -	03/2019
137	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	04/2018 -	04/2018
	Total		1,19,003.44 -	1,19,317.48	25,163.82		
	<u>RAILWAYS</u>						
138	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	10.00	03/2020 -	03/2020
139	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	720.59	528.58	03/2017 -	03/2017
140	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
141	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	5.65	03/2021 -	03/2021
142	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]	1/2011	493.17 -	493.17	358.87	03/2018 -	03/2018
143	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	0.23	12/2020 -	12/2020

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
144	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]	5/2014	207.00 -	207.00	127.56	03/2018 -	03/2018
145	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]	10/2013	343.00 -	343.00	217.84	03/2019 -	03/2019
146	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	4.01	03/2020 -	03/2020
147	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	580.79	03/2020 -	03/2020
148	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	16.01	03/2021 -	03/2021
149	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022
150	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	6.15	03/2021 -	03/2021
151	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	927.01	599.94	03/2019 -	03/2019
152	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]	4/2012	471.82 -	471.82	18.81	03/2019 -	03/2019
153	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	728.10	0.34	12/2024 -	12/2024
154	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	558.06	12/2020 -	12/2020
155	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	269.60	1.11	03/2017 -	03/2017
156	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	31.23	03/2020 -	03/2020
157	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.14	12/2025 -	12/2025
158	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	-	03/2021 -	03/2021
159	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	183.98	12/2021 -	12/2021
160	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	168.12	03/2019 -	03/2019
161	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	5.92	03/2021 -	03/2021
162	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	108.73	03/2021 -	03/2021
163	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 03/2020	03/2020
164	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	170.54	03/2019 -	03/2019
165	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,514.45	1,024.69	03/2020 -	03/2020
166	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	722.82	03/2019 -	03/2019

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
167	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	1/2013	387.70 -	387.70	293.89	03/2018 -	03/2018
168	KOTTAVALSA - KORAPUT DOUBLING - [N22000377	4/2015	2,499.71 -	2,499.71	2.89	03/2021 -	03/2021
169	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427	12/2015	174.00 -	174.00	65.39	03/2019 -	03/2019
170	KATNI-BINA 3RD LINE (263 KM) - [N22000415	6/2016	2,478.23 -	2,478.23	0.04	03/2022 03/2022	03/2022
171	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	763.18 -	1,428.00	480.27	12/2021 -	12/2021
172	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350	12/2015	1,491.47 -	1,491.47	0.12	12/2020 -	12/2020
173	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413	3/2012	1,183.25 -	1,183.25	652.02	12/2020 -	12/2020
174	RAIPUR - TITLAGARH - DOUBLING - [N22000411	3/2007	758.09 -	758.09	513.66	03/2020 -	03/2020
175	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
176	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,273.00 1,908.00	1,908.00	0.20	12/2021 -	12/2021
177	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
178	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
179	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	4,295.30	157.32	12/2026 -	12/2026
	Total		51,086.04 -	53,358.09	7,615.92		
	ROAD TRANSPORT AND HIGHWAYS						
180	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	14.71	10/2017 -	10/2017
181	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	269.47	01/2017 -	01/2017
182	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	71.13	04/2018 -	04/2018
183	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499	12/2015	667.00 -	667.00	31.96	06/2018 -	06/2018
184	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632	9/2014	1,684.00 -	1,684.00	-	02/2017 -	02/2017
185	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373	11/2010	305.49 -	305.49	-	03/2017 -	03/2017

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
186	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
187	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
188	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
189	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
190	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	128.93	04/2017 -	04/2017
191	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
192	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018
193	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	49.00	10/2018 -	10/2018
194	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
195	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
196	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	0.02	09/2017 -	09/2017
197	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
198	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	125.00	11/2018 -	11/2018
199	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
200	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327	3/2015	394.00 -	394.00	80.27	06/2018 -	06/2018
201	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	0.02	11/2017 -	11/2017
202	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017

Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
203	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
204	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
205	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
206	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017
207	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
208	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
209	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	31.31	01/2019 -	01/2019
210	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018
211	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
212	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
213	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017
214	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017
215	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
216	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388	11/2013	497.05 -	497.05	0.54	05/2017 -	05/2017
217	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414	1/1991	229.41 -	229.41	67.86	05/2018 -	05/2018
218	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
219	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	41.87	05/2017 -	05/2017
220	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491	1/2016	815.28 -	815.28	13.56	06/2018 -	06/2018
221	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484	12/2015	239.23 -	239.23	89.22	12/2017 -	12/2017
222	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493	1/2016	1,027.53 -	1,027.53	39.63	06/2018 -	06/2018

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
223	TWO LANE WITH PAVED SHOULDERS OF CHAS -RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	195.07	09/2017 -	09/2017
224	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	23.39	06/2018 -	06/2018
225	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	83.52	03/2018 -	03/2018
226	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	209.82	03/2018 -	03/2018
227	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	483.45	02/2018 -	02/2018
228	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	208.59	03/2018 -	03/2018
229	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	414.31	11/2017 -	11/2017
230	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO - 50) - [N24000342]	5/2015	709.00 -	709.00	32.70	09/2017 -	09/2017
231	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]	6/2015	996.37 -	996.37	2.18	12/2017 -	12/2017
232	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]	9/2015	768.56 -	768.56	170.97	03/2018 -	03/2018
233	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]	3/2015	226.31 226.00	226.00	69.69	10/2017 -	10/2017
234	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	162.33	05/2017 -	05/2017
235	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	70.46	03/2018 -	03/2018
236	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]	8/2015	538.08 -	538.08	129.39	02/2018 -	02/2018
237	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]	10/2015	597.00 -	597.00	206.52	10/2017 -	10/2017
238	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	1/2015	326.63 327.00	327.00	87.58	04/2018 -	04/2018
239	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	157.97	05/2017 -	05/2017
240	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	16.61	07/2018 -	07/2018
241	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
242	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,996.84	01/2018 -	01/2018

Details of All Central Sector Infrastructure Projects having On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
243	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
244	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
245	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
246	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	257.45	07/2018 -	07/2018
247	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445	8/2014	822.90 -	822.90	208.00	04/2018 -	04/2018
248	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436	9/2015	664.53 -	664.53	155.16	03/2018 -	03/2018
249	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	356.65	12/2018 -	12/2018
250	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	45.48	05/2018 -	05/2018
251	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	106.15	10/2017 -	10/2017
253	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
254	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	92.86	05/2018 -	05/2018
255	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
256	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
257	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324	3/2015	194.11 -	194.11	43.99	05/2018 -	05/2018
258	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
259	JAISALMER - BARMER - [N24000348	8/2015	482.27 -	482.27	159.09	02/2018 -	02/2018
260	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	54.02	03/2018 -	03/2018
261	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
262	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338	10/2014	206.12 -	206.12	161.60	04/2017 -	04/2017

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
263	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354	10/2014	264.72 -	264.72	175.75	04/2017 -	04/2017
264	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352	7/2015	455.60 -	455.60	141.89	07/2017 -	07/2017
265	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61 -	241.61	46.68	02/2017 -	02/2017
	Total		47,807.08 -	47,969.00	8,465.13		
	SHIPPING AND PORTS						
266	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	-	04/2017 -	04/2017
267	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	-	12/2017 -	12/2017
268	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	-	06/2017 -	06/2017
269	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
	Total		928.29 -	978.33	.00		
	STEEL						
270	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097	2/2014	4,749.00 -	4,749.00	24.02	09/2017 -	09/2017
271	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	140.40	03/2018 -	03/2018
272	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094	4/2015	3,127.30 -	3,127.30	466.13	04/2018 -	04/2018
273	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115	11/2015	818.00 -	818.00	15.17	06/2020 -	06/2020
274	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	1,682.85	39.27	09/2018 -	09/2018
275	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103	4/2014	151.33 -	151.33	35.73	09/2017 -	09/2017
276	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	19.75	03/2017 -	03/2017
277	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	11.13	06/2019 -	06/2019
278	ALTERNATE GAS NETWORK AT BSL - [N12000093	3/2015	255.19 -	255.19	115.57	03/2018 -	03/2018
279	COKE OVEN BATTERY-5 - [N12000117	12/2011	2,858.00 -	2,500.00	349.35	12/2017 -	12/2017

**Details of All Central Sector Infrastructure Projects having On Schedule
Projects w.r.t. Original Schedule**

Costing Rs. 150 crore & above ,						(January 2017)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
280	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112	4/2013	170.00 -	170.00	93.66	04/2018 -	04/2018
	Total		14,463.54 -	14,105.54	1,310.18		
	<u>TELECOMMUNICATIONS</u>						
281	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105	6/2016	418.26 -	418.26	-	06/2017 -	06/2017
	Total		418.26 -	418.26	.00		
	<u>URBAN DEVELOPMENT</u>						
282	CONSTRUCTION OF 1003 NOS (900 NOS TYPE II 54 NOS TYPE III 33 NOS TYPE IV 16 NOS TYPE V) FAMILY QUAR - [N28000096	5/2016	164.30 -	164.30	9.13	01/2018 -	01/2018
283	NAGPUR METRO RAIL - [N28000085	8/2014	8,680.00 -	8,680.00	1,188.76	03/2018 -	03/2018
284	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,118.00	2,087.10	11/2019 -	11/2019
285	CONSTRUCTION OC 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095	5/2011	164.00 -	164.00	13.97	01/2018 -	01/2018
286	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094	1/2016	6,928.00 6,928.00	6,928.00	1,933.60	03/2019 -	03/2019
	Total		20,200.30 -	20,054.30	5,232.56		
	Grand Total		4,20,950.59	4,22,609.71	62,985.49		

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	02/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	12/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071]	10/2012	217.60 -	244.10	03/2015 -	03/2015	12.18
	Total		841.67 -	1,238.96			
	<u>COAL</u>						
6	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2019	.02
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,740.78 -	2,401.68			
	<u>FERTILISERS</u>						
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. [N08000010]	02/2016	482.85 -	494.00	12/2017 -	12/2017	2.31

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		680.64	703.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
13	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]	11/2013	196.70	209.00	01/2016	01/2016	6.25
	Total		196.70	209.00			
	<u>HEAVY INDUSTRY</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00	3,827.30	09/2011	12/2017	122.78
	Total		1,718.00	3,827.30			
	<u>PETROCHEMICALS</u>						
15	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61	9,965.00	04/2012	01/2016	82.49
	Total		5,460.61	9,965.00			
	<u>PETROLEUM</u>						
16	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	439.03	03/2017	06/2018	24.53
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00	1,693.00	01/2012	12/2016	70.49
18	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06	714.25	10/2017	08/2018	17.66
19	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	05/2013	4,124.35	4,259.49	04/2016	12/2017	3.28
20	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86	222.81	09/2016	02/2017	57.06
21	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47	5,813.25	05/2017	05/2018	1.87
22	GAMJI REDEVELOPMENT PROJECT - [N16000202]	05/2015	1,671.22	1,881.22	11/2019	11/2019	12.57
23	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94	341.70	01/2014	11/2019	68.37
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,256.72	05/2013	05/2017	45.83

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
25	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42
26	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	768.25	11/2015 -	10/2016	15.35
27	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	- -	03/2018	45.67
28	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	03/2018	49.38
29	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72
30	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35
31	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	Total		19,926.04 -	23,588.86			
	<u>POWER</u>						
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
33	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
34	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59
35	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14
36	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65
37	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83 -	1,428.87	08/2012 -	01/2017	17.43
38	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79
39	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	05/2011	1,961.87 -	2,310.58	05/2014 -	12/2016	17.77
40	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14
41	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	06/2017	54.25
42	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01
43	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79
44	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	121.80

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
45	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2017	147.51
46	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77
47	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2017	31.17
48	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	06/2017	23.13
49	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	05/2017	133.06
50	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED [N18000114]	12/2011	552.44 -	609.44	02/2014 -	03/2016	10.32
51	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2017	16.63
52	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60
53	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79
54	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93
55	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65
56	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	01/2012	1,422.85 -	1,875.13	01/2015 -	03/2017	31.79
57	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,352.53	07/2006 02/2015	09/2017	266.82
58	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
59	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	Total		77,525.40 -	1,26,779.92			
	RAILWAYS						
60	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	299.62
61	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	- -	-	1,568.48
62	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
63	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	870.00	- -	-	459.31
64	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
65	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	1,542.41	- 05/2009	-	536.26
66	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
67	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
68	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
69	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	350.00	02/2011 -	-	277.85
70	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	- 12/2009	03/2019	10.97
71	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
72	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
73	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
74	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,650.00	- -	03/2023	462.73
75	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	06/2017	57.20
76	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	208.40	- -	-	46.30
77	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
78	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
79	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
80	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	340.00	03/2009 03/2009	02/2017	154.85
81	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	- -	06/2022	137.80
82	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
83	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
84	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
85	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
86	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
87	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
88	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	- -	03/2022	206.55
89	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
90	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	658.07	03/2014 -	03/2019	.75
91	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,030.29	03/2012 -	12/2016	70.85
92	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	01/2011	72.97
93	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	509.00	12/2012 -	03/2016	123.34
94	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,491.43	- -	03/2023	398.98
95	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	- -	03/2021	185.52
96	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
97	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
98	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
99	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	03/2017	70.09
100	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	- -	03/2019	8.18
101	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	- -	03/2022	81.31
102	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	381.39	- -	03/2017	286.26
103	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	280.00	- -	-	191.18
104	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
105	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97

**Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t.
to Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
106	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
107	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,054.35 -	2,200.00	- -	-	108.66
108	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	759.41	- -	-	167.83
109	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
110	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
111	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
112	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
113	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
114	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
115	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,714.49	- -	-	76.69
116	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
117	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	792.01	- -	-	134.68
118	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
119	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
120	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
121	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
122	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
123	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
124	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
125	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
126	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
127	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
128	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	- -	12/2020	341.34
129	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
130	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
131	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
132	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
133	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
134	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
135	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
136	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
137	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
138	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
139	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
140	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2019	290.00
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
143	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
144	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
145	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
146	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
147	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
148	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	-	27.24
149	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
150	KANPUR KASGANJ MATHURA(GC) NER - [220100197]	03/1997	677.97 1,062.36	1,679.13	- -	12/2016	147.67
151	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	02/2017	51.31
152	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	780.98	- -	-	90.45
153	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]	04/2008	516.23 -	735.00	03/2014 -	-	42.38
154	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
155	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
156	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
157	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62
158	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	631.78	12/2012 -	-	107.82
159	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	370.00	02/2009 02/2009	02/2017	122.68
160	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
161	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89
162	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	525.00	- -	03/2019	140.56
163	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	-	284.00
164	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
165	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
166	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	11/2015	155.02
167	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	335.00	06/2004 -	-	72.62
168	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
169	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]	04/1997	836.26 -	1,072.52	- -	-	28.25

**Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t.
to Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
170	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [N220100183]	02/1997	295.00 -	1,289.92	- -	01/2017	337.26
171	BANGLORE - SATYAMANGALAM (NL)(SWR) - [N220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
172	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	-	81.45
173	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [N220100262]	09/1995	100.00 -	712.82	- -	-	612.82
174	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
175	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
176	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	10/2015	14.43
177	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	- -	03/2020	40.44
178	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
179	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
180	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
181	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) [N22000322]	04/2011	190.10 -	355.96	- -	03/2019	87.25
182	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
183	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	04/2010	203.40 -	273.84	- -	-	34.63
184	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	620.00	- -	09/2019	3.33
185	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [N220100106]	12/1994	124.43 -	1,010.00	- -	03/2017	711.70
186	AMRAVATI-NARKHER NL(CR) - [N220100118]	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	29.44
187	ANGAMALI-SABARIMALA (N.L.)(SR) - [N220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
188	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
189	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	431.00	- -	-	75.15
190	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
191	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
192	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
193	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
194	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
195	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	09/2015	27.06
196	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
197	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
198	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	-	16.87
199	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152]	04/2013	456.00 -	860.00	- -	12/2018	88.60
200	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	03/2017	17.92
201	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	- -	-	7.53
202	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	-	27.93
203	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	-	27.72
204	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	-	21.31
205	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
206	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
207	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
208	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
209	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
210	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
211	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40

**Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t.
to Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
212	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
213	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
214	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
215	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
216	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
217	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
218	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
219	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
220	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	12/2018	91.71
221	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
222	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
223	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
224	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	03/2016	107.49
225	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	972.52	- -	03/2019	285.92
226	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	- -	03/2018	112.14
227	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	- -	03/2018	16.38
228	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
229	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
230	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
231	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
232	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
233	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2019	171.38

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
234	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
235	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	- -	03/2019	62.76
236	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
237	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
238	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
239	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
240	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
241	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	03/2019	27.07
242	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	- -	03/2022	101.93
243	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	03/2023	5.33
244	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	03/2023	10.94
245	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	03/2022	21.21
246	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
247	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
248	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	05/2015	5.12
249	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
250	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
251	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
252	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
253	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
254	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		1,02,528.07	2,51,670.51			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
255	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00	361.00	02/2009	02/2017	28.93
256	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81	385.13	04/2009	05/2017	92.75
257	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04	280.13	11/2008	02/2017	80.68
258	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00	331.23	07/2009	03/2017	68.99
259	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00	2,288.00	11/2011	08/2017	106.50
260	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96	605.00	-	-	5.41
261	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307	12/2011	156.63	276.00	02/2012	-	76.21
262	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97	268.92	08/2015	-	3.84
263	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18	162.00	07/2015	-	3.07
264	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61	309.56	04/2010	02/2017	42.25
265	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00	281.31	02/2010	05/2017	2.29
266	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10	3,237.87	09/2012	03/2017	114.56
267	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00	1,206.10	04/2013	03/2017	2.65
268	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47	313.27	02/2017	02/2017	6.02
269	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31	339.82	12/2015	-	55.66
270	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75	348.43	09/2017	09/2017	36.24
271	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16	352.05	11/2017	11/2017	31.78

Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t. to Original Schedule

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
272	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	02/2017	10.82
273	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
274	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	03/2017	51.83
275	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26
276	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640	01/2015	326.63 327.00	327.00	04/2018 -	04/2018	.11
277	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	02/2015	239.91 240.00	240.00	10/2017 -	10/2017	.04
278	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06
279	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02
280	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30
	Total		10,168.08 -	14,892.59			
	<u>SHIPPING AND PORTS</u>						
281	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2016	300.00
282	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
283	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66
284	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
285	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	Total		1,205.50 -	2,172.77			
	<u>STEEL</u>						

**Details of All Central Sector Infrastructure Projects having Cost Overruns w.r.t.
to Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)		
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
286	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	03/2017	12.04
287	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79
288	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	03/2016	44.80
289	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	12/2017	42.39
290	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50
	Total		1,639.71 -	2,211.39			
	URBAN DEVELOPMENT						
291	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	14,405.01	06/2011 -	04/2017	125.25
292	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75
293	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]	08/2014	350.02 -	479.87	03/2015 -	07/2017	37.10
	Total		6,986.35 -	15,234.21			
	Grand Total		2,47,280.55	4,83,357.63			

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Annexure - VI

Costing Rs. 150 crore & above, (January 2017)

						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,994.00	12/2008 10/2013	02/2017	98	70.54	
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,356.82	09/2010 09/2016	10/2017	85	71.82	
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	9,417.00	12/2015 11/2016	11/2019	47	0	
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	7,169.00	12/2016 03/2017	12/2020	48	0	
	Total		40,442.00 -	52,241.00	43,936.82					
	<u>CIVIL AVIATION</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	553.53	454.71	01/2011 -	12/2017	83	78.87	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.35	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	481.06					
	<u>COAL</u>									
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	321.95	03/2010 -	03/2017	84	0	
8	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40 486.57	486.57	250.31	03/2012 03/2018	03/2017	60	87.58	
9	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	122.29	12/2012 -	03/2017	51	0	
10	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	95.92	03/2015 -	03/2017	24	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	176.64	03/2012 -	03/2017	60	0	
12	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	365.01	45.47	06/2015 -	03/2017	21	0	
13	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	252.03	10/2014 06/2017	06/2017	32	0	
14	PATHERDIH NLW WASHERY - [N06000127]BCCL, JHARKHAND	10/2012	269.82 -	269.82	101.20	04/2014 -	08/2017	40	0	
15	MADHUBAND NLW WASHERY - [N06000126]BCCL, JHARKHAND	08/2010	289.45 -	289.45	135.47	05/2014 -	09/2017	40	0	
16	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82 -	153.82	90.82	03/2014 -	12/2017	45	0	Delay/non-issuance of patta for land/plots allotted to PAFs in area acquired under CBA Act & delay in finalisation of pending title cases of land in CBA tribunals and unjustified demand of villagers for giving possession of land acquired under CBA Act.
17	SHANTIKHANI LONGWALL PROJ- SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	249.03	125.78	03/2012 -	03/2018	72	0	
18	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	198.64	03/2014 -	03/2018	48	0	
19	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	166.21	03/2016 -	03/2018	24	0	
20	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98 -	210.98	153.82	03/2013 -	03/2018	60	0	
21	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	148.00	03/2012 -	03/2018	72	0	
22	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	225.57	03/2016 -	03/2018	24	0	
23	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	242.29	.09	03/2015 -	03/2018	36	0	
24	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	0	
25	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06 -	447.06	246.83	03/2015 -	03/2018	36	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
26	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	133.99	03/2016 -	03/2018	24	0	
27	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 -	417.33	35.41	07/2016 -	03/2018	20	0	
28	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	486.27	121.04	03/2016 -	03/2018	24	12.97	
29	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 -	5,907.11	3,328.28	12/2015 04/2018	04/2018	28	0	
30	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	221.58	03/2017 -	05/2018	14	0	
31	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	269.36	03/2018 -	09/2018	6	0	Rehabilitation of PAFs: Process of R&R activity delayed due to disputes among villagers for selection of rehab site.
32	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
33	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	310.50	03/2013 -	11/2018	68	0	
34	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	185.94	03/2010 -	03/2019	108	0	
35	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	215.34	03/2012 -	03/2019	84	0	
36	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.63	188.68	03/2013 -	03/2019	72	.02	
37	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87 -	179.87	96.78	03/2012 -	03/2019	84	0	
38	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2019	60	0	
39	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	145.11	04/2015 -	04/2019	48	0	
40	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	156.53	06/2015 08/2019	08/2019	50	-51.37	
41	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 459.59	459.59	53.25	03/2015 03/2020	03/2020	60	201.51	
42	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	4.76	03/2014 -	03/2020	72	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
43	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2020	108	0	
44	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	80.61	07/2012 03/2017	03/2021	104	0	
45	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	16.86	
	Total		20,323.21 -	20,235.00	9,007.54					
	<u>FERTILISERS</u>									
46	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	79.51	11/2016 09/2017	09/2017	10	5.89	
	Total		197.79 -	209.44	79.51					
	<u>STEEL</u>									
47	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	700.36	07/2015 -	02/2017	19	0	
48	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	95.81	09/2016 -	03/2017	6	0	
49	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	179.14	12/2015 -	03/2017	15	17.5	
50	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	203.43	12/2016 -	03/2017	3	12.04	
51	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	657.66	03/2015 -	03/2017	24	0	
52	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	451.53	07/2016 -	05/2017	10	0	
53	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	380.93	07/2015 -	05/2017	22	0	
54	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	17,033.59	03/2013 -	06/2017	51	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
55	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	206.71	146.51	12/2016 07/2017	07/2017	7	17.79	
56	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	182.95	05/2016 -	10/2017	17	0	
57	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	10,986.26	05/2015 12/2017	12/2017	31	0	
58	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	142.68	10/2016 -	12/2017	14	42.39	
59	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	221.73	12/2017 -	05/2018	5	0	
60	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	116.00	10/2017 -	07/2018	9	0	
	Total		39,587.34 -	39,814.56	31,498.58					
	PETROLEUM									
61	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 370.00	370.00	325.80	03/2013 01/2017	01/2017	46	19.35	
62	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]IOCL,ASSAM	06/2012	150.00 -	150.00	140.02	07/2014 09/2017	01/2017	30	0	
63	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 222.81	222.81	189.51	09/2016 -	02/2017	5	57.06	
64	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	159.43	09/2012 03/2017	03/2017	54	-24.14	Slow progress in civil work and fabrication work Delay in delivery of Nut Shell filters and internal of IGF units
65	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	529.25	08/2015 -	03/2017	19	0	
66	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	671.29	04/2015 03/2017	03/2017	23	-39.69	Financial constraints of contractor Delay in mobilisation of marine spreads by contractor

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
67	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	3,110.36	2,338.88	11/2015 12/2016	03/2017	16	0	Restricted timings for radiography activities
68	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,057.18	05/2013 05/2017	05/2017	48	45.83	Increase in scope of work post-award of contract. •Delay in procurement of steel and fabrication of legs by the contractor. •Slow progress in fabrication – non-structural , E&I erection •Possible impact on balance activities due to fire incident on MOPU. •Financial dispute between consortium partners.
69	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017	25	0	Re-visit of the techno-economics of the project in view of new development.
70	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11 -	367.11	103.03	04/2017 -	05/2017	1	0	Delivery of Reactor at site is expected by end Jan 17 due to delay in approval for erecting temporary bridge across Buckingham canal from PWD due to monsoon. Due to Vardha Cyclone in 12th Dec 16 there was water scarcity in the Refinery for construction and fire fighting activities, hence all project site activities were suspended.
71	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	830.93	03/2015 05/2017	05/2017	26	37.72	Heavy rain in Assam, Refloating of tender. Delay in delivery of critical items due to financial instability Poor participation of vendors bundhs, environmental issues in North East
72	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	533.16	09/2011 06/2017	06/2017	69	0	Delay in preparation of drawings, shortage of skilled manpower, change in delivery location
73	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	133.65	05/2015 -	06/2017	25	0	Delay in land acquisition

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
74	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	173.28	108.85	01/2017 06/2017	06/2017	5	-4.28	ROU, Forest clearance
75	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]IOCL,ODISHA	03/2014	238.50 -	238.50	111.81	03/2017 10/2017	10/2017	7	0	Delay in getting approval
76	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	1,869.67	05/2014 12/2017	12/2017	43	0	Retendering
77	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 4,259.49	4,259.49	2,122.24	04/2016 12/2017	12/2017	20	3.28	Interruption of site-works by villagers .
78	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	184.00	46.02	06/2017 -	12/2017	6	0	
79	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	88.97	11/2016 -	02/2018	15	0	Delay due to poor response to purchase & works tender
80	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	931.00	63.30	07/2017 02/2018	02/2018	7	0	
81	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 2,378.89	2,378.89	1,882.07	03/2013 03/2018	03/2018	60	-3.5	ROU acquisition Delay in forest clearance.Inadequate manpower at -Local problem and court cases by tea gardener.Slow progress in engineering and procurement
82	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,130.70	03/2015 03/2018	03/2018	36	29.42	Non-performance of contractor
83	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	375.76	12/2014 03/2018	03/2018	39	0	non-performance of the contractor
84	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	318.90	10/2014 03/2017	03/2018	41	49.38	delay in getting pipeline permission
85	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	142.22	12/2016 -	03/2018	15	-8.51	
86	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	5,088.83	05/2017 05/2018	05/2018	12	1.87	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
87	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	99.51	07/2016 06/2018	06/2018	23	-20.81	
88	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 439.03	439.03	5.87	03/2017 -	06/2018	15	24.53	
89	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	892.55	09/2017 06/2018	06/2018	9	0	
90	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	714.25	144.74	10/2017 08/2018	08/2018	10	17.66	delay in jetty works, work stopped due to NGT orders, agitation by local people
91	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	3,957.00 3,561.00	3,397.00	456.75	01/2013 12/2018	12/2018	71	-14.15	Award of RoU and crop compensation in Bihar is affected/slow due to non availability of full time CA.
92	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	515.65	09/2017 12/2018	12/2018	15	0	
93	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	3,961.54	2,468.50	12/2017 03/2019	03/2019	15	-14.25	Representation in IEM by one of the bidder.
94	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	36.47	07/2018 11/2019	08/2019	13	0	
95	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	341.70	2.95	01/2014 11/2019	11/2019	70	68.37	
96	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020	14	0	Retendering
	Total		48,623.45 -	48,918.77	24,992.44					
	<u>POWER</u>									
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	635.96	11/2011 -	01/2017	62	0	Project completed. Delayed due to severe ROW problem in western region.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
98	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 1,428.87	1,428.87	1,092.09	08/2012 09/2016	01/2017	53	17.43	
99	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,265.03	06/2015 -	01/2017	19	0	
100	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	6,102.00	09/2016 01/2017	02/2017	5	0	
101	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,366.64	3,820.69	12/2011 03/2016	02/2017	62	88.79	Nil
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	605.02	07/2013 11/2015	03/2017	44	-8.45	Project completed except Kishenpur – New Wanpoo line. ROW problem & Limited working period due to snow-bound area affecting implementation. Work stand still due to disturbance in Kashmir since Jul'16. Further 01 locs. & 1.09 Km stringing under severe ROW problem.
103	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,281.56	09/2014 -	03/2017	30	0	02 out of 03 line completed. Completion of balance line delayed problem being faced in Karnataka on Salem PS – Madhugiri line.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
104	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL, CHHATTISGARH	01/2012	1,422.85 1,875.13	1,875.13	1,721.72	01/2015 06/2016	03/2017	26	31.79	Completion delayed due to delay in forest clearance. (Huge forest involvement 295 Ha.). Final forest clearance obtained in Dec'15. Problem being faced due to involvement of difficult hilly locations. demand by forest dwellers, being resolved with support from State Govt.
105	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL, MULTI STATE	09/2013	1,575.30 -	1,575.30	1,235.60	05/2016 -	03/2017	10	0	Completion delay due to severe ROW problem in Mauda-II – Betul line. Betul – Khandwa line erection completed. Commissioning matching with Mauda-II - Betul line. Khandwa-Indore line commissioned in Dec'16.
106	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	1,880.00	12/2016 03/2017	03/2017	3	0	
107	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL, GUJARAT	02/2014	378.71 -	378.71	245.30	10/2016 -	04/2017	6	0	Gen. proj. delayed. However, contingency arrangement being worked out subject to availability of Sw. Yd. at Kakrapar end which is expected by Apr'17.
108	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO, ARUNACHAL PRADESH	12/2008	573.99 1,337.76	1,337.76	1,341.09	08/2013 05/2017	05/2017	45	133.06	
109	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	120.73	09/2014 -	05/2017	32	0	03 lines are U/c on which OPGW installation if held up. Supply has been completed in packages. Presently there are only 04 lines balance among which 03 are under construction and fourth line is being ROW problem.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
110	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	6,405.00	09/2011 06/2017	06/2017	69	54.25	
111	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	237.09	06/2012 -	06/2017	60	0	S/S almost ready since Jun'12. Line completed except 5 kms near Yelahanka, which was held up due to Severe ROW problem. Land owner are demanding higher compensation. Matter being perused at Distt. / State Govt. level. After support from State Govt., compensation survey by Revenue deptt. completed. Critical due to continuing ROW problem. D.C. order awaited.
112	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 2,619.56	2,619.56	2,525.03	07/2014 06/2016	06/2017	35	23.13	01/02 line & 01/01 S/stn. completed. Balance Aurangabad-Boisor line affected due to delay in forest clearance (Stage-I received in Aug'15). Permission to work received in Oct'15 & severe ROW in routing of line through grape garden area. Critical
113	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	6,707.99	06/2015 -	06/2017	24	0	Implementation affected due to delay in land acquisition of Champa Sub station (land acquired in Apr'13). HVDC line completed. Commissioning matching with HVDC Station. Pole-I alongwith HVDC line expected by Feb'17.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	687.82	11/2014 -	06/2017	31	0	Severe ROW problem in Uttarakhand in Dehradun-Abdullapur line. Final forest clearance received in Apr'16. Delay tree cutting by forest deptt. in Uttarakhand affected stringing. Progress affected of Dulhasti-Kishenpur line, site work affected due to heavy snowfall and disturbance in J&K. ROW problem in Doda distt.
115	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	1,050.44	04/2016 -	06/2017	14	0	Severe ROW problem at Rajarhat end as well as in Jharkhand area. LILO line expected in Mar'17 & main line progressively by Jun'17. Work in Rajarhat area at standstill due to severe ROW.
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	352.50	06/2016 -	06/2017	12	0	Completion delayed due to severe ROW problem at Singrauli end.
117	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	337.20	08/2016 -	06/2017	10	0	02 out of 03 elements completed up to Dec'16. Balance work stopped due to disturbance in Kashmir since Aug'16. Due to disturbance in Kashmir, no work since Jul'16. Minimum 04 working months required for completion.
118	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	182.30	07/2016 -	06/2017	11	0	Down stream 220KV line (GETCO) not ready for commissioning. Completion matching with GETCO associated lines.
119	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	311.90	11/2016 -	06/2017	7	0	Completion delayed due to shifting of transformer delay. However, ICT held up at bridge near Farakka. Permission to cross bridge refused by MoST, W.B. ICT temporally stored at Durgapur.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
120	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	69.60	03/2016 -	06/2017	15	0	03 out of 05 elements completed. Completion delay due to delay in equipment supply(Off-shore). Down stream line delayed. CEA take up with State for readiness of down stream line by Mar'17. Critical
121	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	78.70	02/2016 -	06/2017	16	0	Completion delayed due to delay in manufacturing of Reactors by Vendor. Reactors now under manufacturing & supply under progress. ICT-II yet to be supply for Maithon Sub station.
122	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	12,777.00	01/2017 07/2017	07/2017	6	0	
123	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	7,337.00	11/2016 08/2017	08/2017	9	0	
124	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,352.53	1,352.53	1,137.81	07/2006 09/2017	09/2017	134	266.82	
125	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	7,539.00	06/2017 09/2017	09/2017	3	0	
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	559.10	06/2016 -	09/2017	15	0	02 out of 04 line completed. Progress affected due to severe ROW problem. Land owner demanding compensation as per guidelines of MoP. State Govt. yet to issue notification. Land owner has approached H'ble Court. High court has directed to State to finalise by 31.01.17. Delay in finalisation of compensation.
127	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	171.20	02/2017 -	09/2017	7	0	Completion delayed due to delay in Transformer supply (falter in testing).
128	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	5,353.00	6,266.92	05/2014 03/2017	09/2017	40	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
129	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89	9,750.89	6,117.37	12/2016	09/2017	9	0	
130	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	5,331.03	12/2009 10/2017	10/2017	94	147.51	
131	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	634.29	09/2010 12/2016	12/2017	87	54.59	01/03 line & part of 2nd line completed. Severe ROW problem in balance 02 lines, (400KV D/C Vapi-Navi Mumbai line & LILO at Navi Mumbai). LILO line is being completed using underground cable, however, ROW problem for laying of cable continue. Cable burnt/ damaged by miscreants. Critical. Vapi-Navi Mumbai line now decided to be terminated at Kudus S/stn. Further, its commissioning is linked to readiness of Kudus S/s of MSETCL. Critical.
132	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,137.80	08/2013 12/2017	12/2017	52	23.65	05/08 line compltd. Completion affected due to agitation against Big Dam proj. affecting the construction works in Assam and adverse law & order situation in NER. Lower Subhanshri-B'Chariyali line in almost standstill since Dec'11 due to agitation. Gen. Proj. are also getting delayed. Kameng HEP is ant. in Dec'17 & Lower Subansiri HER is uncertain.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
133	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	3,261.45	01/2015	12/2017	35	0	Gen. Proj. (Punatsangchu-I HEP in Bhutan) getting delayed. Also line getting completed ahead of Gen. Proj. now anticipated in 2017-18. Work slowed down to the extent feasible to match Gen. Forest clearance (Stage-I) obtained for WB in Jun'16. Severe ROW issues affecting progress in the LIL lines. Commissioning matching with HVDC Terminal. Pole-I expected by Mar'17.
134	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL, MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,358.23	11/2012 12/2016	12/2017	61	36.01	07/08 line & 06/07 sub station completed. Completion affected due to delay in land acquisition of Daltonganj (land acquired in May'15) & Change of location of Ultra S/stn. to Pandiabil due to local resistance. Further Daltonganj S/S pkg. re-awarded in May'16. Work under progress. JSEB to ensure matching completion of down-stream system.
135	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, MULTI STATE	10/2011	487.49 639.46	639.46	475.32	06/2014 03/2016	12/2017	42	31.17	Project completed except 400KV Madugiri-Yelhanka line. Severe ROW problem being faced in Karnataka. (Down stream system being executed by State not available). Efforts being made to resolve with the help of State Govt.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
136	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	339.27	08/2014 06/2015	12/2017	40	16.63	Completion delayed due to severe ROW problem in Bengaluru area seeking huge compensation of tower location & corridor. Compensation order issued by State in line with Govt. guidance. Villages-wise compensation rate is to be decided by Distt. Admn. (awaited) for which corridor survey is under progress.
137	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,822.73	08/2014 12/2015	12/2017	40	27.6	01/03 lines completed. Implementation affected due to delay in forest clearance received for Aurangabad – Padghe line & delay in completion Kudus (Padghe) S/stn. being executed by MSETCL. Critical. ROW problem is also being encountered.
138	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	489.20	06/2015 -	12/2017	30	0	765KV bay commissioned alongwith associated line in Jan'17. Balance work under progress.. Commissioning delay due to non-availability of down-stream system, now planned for completion matching with Srikakulam – Garividi line being executed under TBCB (ant. by Dec'17).
139	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,663.25	12/2015 -	12/2017	24	0	Implementation affected due to severe ROW problem in Odisha & Huge Angul-Jharsaguda line. Working permission awaited. Working permission in Jharsaguda–Dharamjaygarh line (Odisha portion) obtained in May'16. Chattisgarh portion, forest clearance awaited. Critical

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
140	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	51.90	04/2016 -	12/2017	20	0	90% Sub station PMU's has been supplied for which installation is under progress. PDC in control center is being installed in WRDLC, Maharashtra SLDC. For balance PDC FAT is scheduled in end of February 2017.
141	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	137.20	09/2017 -	12/2017	3	0	
142	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	41.20	03/2017 -	12/2017	9	0	Completion likely to be delayed due to be delayed in generation Project (anticipated by Nov 17.
143	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,783.17	4,800.42	01/2016 -	01/2018	24	58.79	
144	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,420.88	10/2012 03/2017	02/2018	64	5.14	8 out of 9 lines completed by Dec'16. 1200kV Wardha - Aurangabad affected due to delay in implementation arising out of complexities involved (1200KV tower) & severe ROW problem also being encountered, apart from poor performance by executing agency necessitating termination & re-awarding fresh contracts.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
145	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,431.10	12/2012 12/2016	02/2018	62	36.79	11/17 line & 03/07 S/s completed. Implementing of balance lines affected due to stiff resistance/ local disturbances & geographical constraints in NER. 03 nos. lines terminated & re-tendered due to poor performance by contractor & awarded recently in Jun'16/Nov'16. 03 lines in Arunachal Pradesh affected due to issue arising out of compensation & land ownership disputes. Issue getting resolved with support of state/Distt. Admn.
146	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	100.27	02/2014 -	02/2018	48	0	Arrangement for Power evacuation by UPPTCL (including steps taken to address the time and cost overrun):- a. Power evacuation to be done by UPPTCL. PPA has already been signed. b. Work still not taken up by UPPTCL. May get delayed as construction of transmission line require Forest Clearance. c. Revised Implementation Agreement and Connection Agreement still to be signed with GoUP & UPPTCL respectively on confirmation.
147	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	12,694.00	01/2011 05/2018	05/2018	88	73.65	
148	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	8,189.41	01/2018 -	06/2018	5	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
149	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,919.35	11/2008 12/2016	09/2018	118	22.93	06/07 lines & 02/02 sub station completed ahead of Gen. Proj. Balance 01 line (Edamon-Muvattupuzha line) getting delayed due to prolonged severe ROW problem in Kerala. Revised G.O. issued on 30.07.15 in which compensation to be done on land value, to be finalised by concerned DC with the support of State Govt. Balance survey resumed on 27.07.16. Package being re-tendered for award of balance work.
150	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,086.47	09/2009 -	12/2018	111	114.28	
151	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	383.60	04/2017 -	12/2018	20	0	Work has been slowed-down to match with Generation. (Completion likely to be delayed due to delay in Generation project).
152	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	3,053.00	03/2013 06/2019	06/2019	75	29.14	
153	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	2,068.02	02/2016 09/2019	09/2019	43	79.77	1- Assistance of Dist. Administration to resolve law and order problem causing stoppage of muck dumping since 30.07.16 i.e. more than 06 months at Chopra. 2- Early issuance of GO from GoUK for diversion of 4.668 Ha. land for dumping area at village Chopra. 3- Permission from DM, Tehri for dumping at alternate dumping area at Koti.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
154	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,016.89	06/2013 -	12/2019	78	0	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan'2014. Now the works at various fronts are in progress with intermittent hindrances by villagers. Regular support of Distt. Administration is required for smooth progress of the project works.
155	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	3,934.00	02/2019 02/2020	02/2020	12	0	
156	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	696.27	04/2020 -	01/2023	33	0	
	Total		1,94,433.24 -	2,26,076.70	1,62,734.31					
	HEAVY INDUSTRY									
157	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	122.78	train manpower was not available in the country
	Total		1,718.00 -	3,827.30	2,289.00					
	HEALTH AND FAMILY WELFARE									
158	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	97.00	05/2017 -	06/2017	1	0	
159	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	159.00	05/2017 -	06/2017	1	0	
160	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	38.00	05/2017 -	07/2017	2	0	
	Total		666.99 -	666.99	294.00					
	RAILWAYS									

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
161	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	370.00	363.32	02/2009 02/2009	02/2017	96	122.68	
162	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	344.04	03/2009 03/2009	02/2017	95	154.85	
163	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,581.53	690.91	03/2010 -	03/2017	84	386.62	
164	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 155.56	229.33	141.72	12/2010 03/2017	03/2017	75	-21.93	
165	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,000.00	6,630.23	03/2009 -	03/2017	96	317.58	
166	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	0	
167	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	963.74	03/2010 -	06/2017	87	38.24	
168	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	554.70	461.48	01/1999 06/2017	06/2017	221	77.08	
169	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 843.45	966.98	924.00	02/2009 12/2017	12/2017	106	520.89	
170	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	441.77	03/2010 -	12/2017	93	58.94	
171	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,641.30	03/2014 -	12/2017	45	0	
172	MULTI MODAL TRANSPORT SYSTEM(MMST) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	325.99	03/2016 -	12/2017	21	29.06	
173	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,000.00	4,464.70	04/2008 12/2011	06/2018	122	233.33	
174	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
175	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	14,922.23	11/2002 -	12/2018	193	682.6	
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,619.00	685.23	03/2016 -	12/2018	33	-10.11	
177	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,010.00	2,419.18	12/2008 -	03/2019	123	310.64	
178	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	7,986.04	2,423.55	03/2014 03/2019	03/2019	60	50.68	Fund constraint affecting the progress of projects.
179	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	280.08	03/2015 -	03/2019	48	0	
180	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 658.07	658.07	523.26	03/2014 03/2019	03/2019	60	.75	
181	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	58.86	03/2012 -	03/2019	84	1.06	
182	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	0	
183	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,181.00	03/1998 -	12/2019	261	359.96	
184	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.70	294.14	02/2015 -	12/2019	58	556.39	
185	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	318.00	299.61	02/2006 -	12/2019	166	21.51	
186	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	557.65	03/2004 03/2020	03/2020	192	259.68	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
187	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 1,125.89	1,125.89	1,035.41	12/2011 03/2020	03/2020	99	25.09	Total land acquisition required is 18.0 Hectares, out of which, proposal for 15.2 Hectares is with Government of West Bengal.
188	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 4,454.18	9,658.00	5,918.56	03/2011 -	03/2020	108	1227.45	
189	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,154.14	03/2008 06/2008	03/2020	144	145.63	
190	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,451.00	1,936.18	03/2014 -	03/2020	72	324.3	
191	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 2,393.48	4,600.00	1,023.83	04/2014 -	03/2020	71	642.73	
192	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51	204.95	
193	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	49.69	03/2013 -	03/2020	84	-2.17	
194	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	171.69	03/2015 -	03/2020	60	252.94	
195	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	858.23	680.93	06/1999 12/2020	12/2020	258	29.44	
196	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	1,212.65	03/2016 -	12/2020	57	-20	
197	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
198	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022	46	226.23	
199	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 4,327.28	6,093.31	1,271.49	05/2008 03/2023	03/2023	178	2360.35	
	Total		41,337.66 -	1,10,020.72	57,843.49					

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	ROAD TRANSPORT AND HIGHWAYS									
200	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	478.32	05/2013 -	01/2017	44	0	N.R.
201	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,418.23	07/2013 -	01/2017	42	0	N.R.
202	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	2,126.85	04/2015 -	01/2017	21	0	N.R.
203	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	231.79	01/2016 -	01/2017	12	0	N.R.
204	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	442.64	02/2009 -	02/2017	96	28.93	N.R.
205	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	204.64	11/2008 -	02/2017	99	80.68	N.R.
206	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	316.94	06/2008 06/2016	02/2017	104	0	N.R.
207	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	436.38	04/2010 09/2016	02/2017	82	42.25	N.R.
208	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	4,554.86	06/2015 -	02/2017	20	0	N.R.
209	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	02/2017	45	0	N.R.
210	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,898.25	09/2015 -	02/2017	17	0	N.R.
211	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	02/2017	14	0	N.R.
212	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	0	N.R.
213	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	503.16	331.09	08/2016 -	02/2017	6	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
214	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	299.99	11/2008 -	03/2017	100	0	N.R.
215	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	266.81	04/2009 -	03/2017	95	0	N.R.
216	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	03/2017	108	0	N.R.
217	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	204.93	05/2008 12/2016	03/2017	106	0	N.R.
218	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	125.45	09/2007 -	03/2017	114	0	N.R.
219	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	403.94	07/2009 -	03/2017	92	68.99	N.R.
220	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	472.83	05/2010 -	03/2017	82	0	N.R.
221	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 2,782.54	3,237.87	3,407.69	09/2012 -	03/2017	54	114.56	N.R.
222	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.74	08/2011 -	03/2017	67	0	Delay is on account of land acquisition and Forest Issues.
223	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,206.10	04/2013 -	03/2017	47	2.65	N.R.
224	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	741.37	08/2012 -	03/2017	55	0	N.R.
225	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	03/2017	45	0	N.R.
226	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,503.50	08/2014 -	03/2017	31	0	N.R.
227	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,968.37	03/2013 -	03/2017	48	0	N.R.
228	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	03/2017	40	0	N.R.
229	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,972.30	08/2013 -	03/2017	43	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
230	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	03/2017	37	0	N.R.
231	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	901.28	03/2014 -	03/2017	36	0	N.R.
232	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	375.09	534.11	04/2014 -	03/2017	35	0	N.R.
233	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	1,047.00	1,718.55	06/2014 -	03/2017	33	0	N.R.
234	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	398.85	01/2014 -	03/2017	38	0	N.R.
235	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	1,084.00	09/2016 -	03/2017	6	0	N.R.
236	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI, RAJASTHAN	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017	11	0	N.R.
237	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	240.10	178.69	03/2016 -	03/2017	12	0	N.R.
238	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	523.85	155.59	01/2016 -	03/2017	14	0	N.R.
239	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	351.34	304.01	01/2016 -	03/2017	14	0	N.R.
240	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	495.78	414.93	01/2016 -	03/2017	14	0	N.R.
241	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	530.07	509.86	08/2016 -	03/2017	7	0	N.R.
242	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI, CHHATISGARH	02/2013	1,232.00 -	1,232.00	1,173.20	08/2015 -	03/2017	19	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
243	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,383.55	11/2015 -	03/2017	16	51.83	N.R.
244	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	320.00	212.33	05/2016 -	03/2017	10	.06	N.R.
245	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	53.85	06/2016 -	03/2017	9	.02	N.R.
246	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	163.00	91.92	05/2016 -	03/2017	10	.3	N.R.
247	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	905.31	03/2013 -	04/2017	49	0	N.R.
248	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	977.69	07/2013 -	04/2017	45	0	N.R.
249	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37	0	N.R.
250	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	04/2017	7	0	N.R.
251	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	237.03	04/2009 -	05/2017	97	92.75	N.R.
252	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	226.32	02/2010 -	05/2017	87	2.29	Delay is on account of rehabilitation and corrective action necessitated after construction accident on 24.12.2009.
253	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	0	Delay is on account of i) Court order on cutting of trees ii) Public agitation and stopping of works.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
254	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	769.68	09/2013 -	05/2017	44	0	N.R.
255	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,567.40	09/2014 -	05/2017	32	0	N.R.
256	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	0	N.R.
257	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	185.13	11/2016 -	05/2017	6	0	N.R.
258	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	316.60	04/2008 01/2017	06/2017	110	0	N.R.
259	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,131.46	05/2013 -	06/2017	49	0	N.R.
260	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	717.40	01/2014 -	06/2017	41	0	N.R.
261	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	552.91	11/2013 -	06/2017	43	0	N.R.
262	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	875.61	08/2013 -	06/2017	46	0	N.R.
263	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	2,228.56	09/2014 -	06/2017	33	0	N.R.
264	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,281.38	08/2013 -	06/2017	46	0	N.R.
265	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	255.60	05/2017 -	06/2017	1	0	N.R.
266	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	46.64	05/2016 -	06/2017	13	.26	N.R.
267	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,889.98	07/2015 -	07/2017	24	0	N.R.
268	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,864.02	11/2011 -	08/2017	69	106.5	Delay is on account of Poor performance by contractor.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
269	REHABILITATION AND UPGRADE OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD, ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	0	N.R.
270	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	1,655.01	1,130.00	08/2016 -	08/2017	12	0	N.R.
271	REHABILITATION AND UPGRADE OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH, ODISHA	07/2014	342.05 342.00	342.00	145.03	01/2017 -	08/2017	7	-0.1	N.R.
272	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	881.43	02/2013 -	09/2017	55	0	N.R.
273	4-LANING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	621.88	07/2013 -	09/2017	50	0	N.R.
274	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	407.21	07/2014 -	09/2017	38	0	N.R.
275	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	942.69	363.06	06/2014 -	09/2017	39	0	Delay is on account of Inadequate mobilization of resources by contractor, Forest clearance and Land related issues.
276	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,856.83	02/2014 -	09/2017	43	0	N.R.
277	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	12	0	N.R.
278	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,064.23	10/2011 -	09/2017	71	0	N.R.
279	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	1,038.84	07/2013 -	10/2017	51	0	N.R.
280	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	871.49	09/2014 -	10/2017	37	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
281	REHABILITATION AND UPGRADE OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	0	N.R.
282	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,251.64	03/2013 -	11/2017	56	0	Delay is on account of Poor performance of Contractor and delay in land acquisition.
283	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	0	N.R.
284	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	0	N.R.
285	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	405.44	11/2016 -	11/2017	12	0	N.R.
286	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,284.34	06/2013 -	12/2017	54	0	N.R.
287	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	0	N.R.
288	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	0	N.R.
289	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	0	N.R.
290	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	623.74	10/2013 -	12/2017	50	0	N.R.
291	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,492.40	06/2014 -	12/2017	42	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
292	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, WEST BENGAL	02/2011	580.43 -	580.43	279.95	08/2013 -	12/2017	52	0	N.R.
293	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI, UTTARAKHAND	11/2011	478.51 -	478.00	321.08	10/2013 -	12/2017	50	-11	N.R.
294	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	1,479.00	690.66	06/2015 -	12/2017	30	0	N.R.
295	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	0	N.R.
296	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	182.91	10/2015 -	12/2017	26	0	N.R.
297	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	972.50	1,393.23	07/2017 -	01/2018	6	0	N.R.
298	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,643.50	11/2016 -	02/2018	15	0	N.R.
299	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,802.57	08/2013 -	03/2018	55	0	N.R.
300	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,145.48	06/2012 -	03/2018	69	0	N.R.
301	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA) - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	0	N.R.
302	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	44.40	12/2017 -	06/2018	6	0	N.R.
303	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	16.61	06/2016 -	06/2018	24	0	N.R.
304	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	11.60	06/2016 -	06/2018	24	0	N.R.

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
305	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	N.R.
306	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	280.36	03/2016 -	03/2019	36	0	N.R.
307	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	0	N.R.
	Total		85,025.35 -	89,137.26	99,159.05					
	<u>SHIPPING AND PORTS</u>									
308	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	669.46	415.01	12/2010 12/2018	12/2018	96	82.72	
	Total		366.39 -	669.46	415.01					
	<u>TELECOMMUNICATIONS</u>									
309	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30	-4.74	
310	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	5,231.54	07/2015 09/2017	09/2017	26	0	
	Total		15,445.17 -	15,345.17	5,533.11					
	<u>URBAN DEVELOPMENT</u>									
311	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	315.00	258.64	06/2015 08/2016	03/2017	21	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above, (January 2017)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
312	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 405.01	405.01	-	12/2014 03/2017	03/2017	27	0	
313	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 14,405.01	14,405.01	14,282.31	06/2011 12/2015	04/2017	70	125.25	difficult geological conditions
314	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017	54	0	Mismanagement by agency
315	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	143.39	12/2015 12/2016	06/2017	18	0	due to paucity of fund
316	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	188.26	09/2016 01/2017	06/2017	9	0	Fund problem, mobilization of men and material
317	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	67.62	03/2017 -	06/2017	3	0	Central magazine held up by NSG during execution for clearance from CFEEs. Work of 300m Baffle range, 50m indoor shooting Range held up NSG for certification from TBRL. Swimming pool held by NSG
318	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	233.50	03/2015 03/2017	07/2017	28	37.1	Delay by consultant
319	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	178.88	05/2017 08/2017	08/2017	3	0	
320	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 170.62	170.62	139.57	03/2012 08/2016	10/2017	67	-16.77	Inadequate fund
321	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	33.07	11/2015 -	11/2017	24	0	

**Details of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Original Schedule**

Costing Rs. 150 crore & above,										(January 2017)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
322	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	98.76	11/2014 05/2017	12/2017	37	0	
323	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	349.33	159.77	03/2016 12/2017	12/2017	21	44.75	non availability of sufficient fund and delay in local body approvals.
324	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	13,305.52	12/2015 -	12/2017	24	0	
325	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	51.38	03/2015 10/2017	12/2017	33	0	waterlogging of construction site, frequent bandh, non payment of bills
326	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	32.86	03/2016 02/2018	02/2018	23	0	Fund shortage
327	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	80.60	09/2015 03/2017	03/2018	30	0	
328	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	1,753.99	02/2019 -	03/2020	13	0	land acquisition
329	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	12.76	10/2019 -	03/2020	5	0	
	Total		52,338.32 -	60,551.80	31,057.42					
	Grand Total		5,41,128.98	6,68,709.03	4,69,321.34					

Details of All Central Sector Infrastructure Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

Costing Rs. 150 crore & above, (January 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82	85
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	22,462.00	12/2008 -	02/2017	70.54	98
	Total		16,663.00 -	28,462.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	12/2017	78.87	83
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		624.07 -	994.86				
	<u>COAL</u>							
5	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.59	03/2015 -	03/2020	201.51	60
6	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	03/2017	87.58	60
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
8	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97	24
9	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	479.63	03/2013 -	03/2019	.02	72
	Total		1,740.78 -	2,401.68				
	<u>FERTILISERS</u>							
10	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	11/2016 -	09/2017	5.89	10
	Total		197.79 -	209.44				

**Details of All Central Sector Infrastructure Projects having Time and Cost Overruns
w.r.t Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>HEAVY INDUSTRY</u>							
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROLEUM</u>							
12	MARKETING TOP AT KORBA - [N16000186	01/2011	141.86 -	222.81	09/2016 -	02/2017	57.06	5
13	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	06/2010	202.94 -	341.70	01/2014 -	11/2019	68.37	70
14	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	462.79	10/2014 -	03/2018	49.38	41
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	01/2017	19.35	46
16	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	439.03	03/2017 -	06/2018	24.53	15
17	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	08/2018	17.66	10
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	05/2017	45.83	48
19	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72	26
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2018	29.42	36
21	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	05/2013	4,124.35 -	4,259.49	04/2016 -	12/2017	3.28	20
22	MH NORTH REDEVELOPMENT PHASE III - [N16000188	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2018	1.87	12
	Total		15,547.82 -	17,745.69				
	<u>POWER</u>							
23	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	346.79	08/2014 -	12/2017	16.63	40
24	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	07/1998	368.72 -	1,352.53	07/2006 02/2015	09/2017	266.82	134
25	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2017	54.59	87
26	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	12/2017	31.17	42

**Details of All Central Sector Infrastructure Projects having Time and Cost Overruns
w.r.t Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
27	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	08/2013 -	05/2017	133.06	45
28	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]	12/2009	1,216.83 -	1,428.87	08/2012 -	01/2017	17.43	53
29	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	12/2017	36.01	61
30	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	01/2012	1,422.85 -	1,875.13	01/2015 -	03/2017	31.79	26
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	02/2016 -	09/2019	79.77	43
32	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.71	08/2014 -	12/2017	27.60	40
33	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	09/2018	22.93	118
34	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,619.56	07/2014 -	06/2017	23.13	35
35	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	02/2018	36.79	62
36	BOKARO THERMAL POWER STATION-A - [N18000199]	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	88.79	62
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	10/2017	147.51	94
38	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	06/2019	29.14	75
39	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79	24
40	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28	111
41	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	06/2017	54.25	69
42	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2018	5.14	64
43	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	05/2018	73.65	88
44	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	12/2017	23.65	52
	Total		59,944.79 -	91,651.86				

Details of All Central Sector Infrastructure Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	RAILWAYS							
45	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	02/2017	154.85	95
46	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	520.89	106
47	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	02/2017	122.68	96
48	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39	58
49	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
50	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51	166
51	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
52	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94	93
53	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62	84
54	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68	192
56	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
57	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23	46
58	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06	21
59	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113	04/2008	653.19 -	658.07	03/2014 -	03/2019	.75	60
60	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	29.44	258
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24	87
62	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45	108
63	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64	123
64	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63	144
65	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30	72

Details of All Central Sector Infrastructure Projects having Time and Cost Overruns w.r.t Original Schedule

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
66	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94	60
67	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09	99
68	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98	34
69	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33	122
71	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58	96
72	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
73	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68	60
	Total		25,134.44 -	94,733.90				
	ROAD TRANSPORT AND HIGHWAYS							
74	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	02/2017	80.68	99
75	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	03/2017	.30	10
76	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	03/2017	.02	9
77	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	06/2017	.26	13
78	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2017	68.99	92
79	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2017	92.75	97
80	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	02/2017	42.25	82
81	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29	87
82	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	02/2017	28.93	96
83	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	03/2017	.06	10
84	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	03/2017	51.83	16

**Details of All Central Sector Infrastructure Projects having Time and Cost Overruns
w.r.t Original Schedule**

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
85	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50	69
86	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	03/2017	2.65	47
87	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	03/2017	114.56	54
	Total		7,016.33 -	11,129.10				
	<u>SHIPPING AND PORTS</u>							
88	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	<u>STEEL</u>							
89	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	17.50	15
90	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	07/2017	17.79	7
91	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	03/2017	12.04	3
92	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	12/2017	42.39	14
	Total		870.83 -	1,098.05				
	<u>URBAN DEVELOPMENT</u>							
93	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068	02/2011	241.33 -	349.33	03/2016 -	12/2017	44.75	21
94	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091	08/2014	350.02 -	479.87	03/2015 -	07/2017	37.10	28
95	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	14,405.01	06/2011 -	04/2017	125.25	70
	Total		6,986.35 -	15,234.21				
	Grand Total		1,36,810.59	2,68,157.55				

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-
	Total		553.21 -		
	<u>MINES</u>				
3	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT - [N10000009]NALCO,RAJASTHAN	12/2015	344.50 -	11/2016 -	09/2016
4	Implementation of 50.4 MW Wind Power Project at Jath, Sangli, Maharashtra - [N10000008]NALCO,MAHARASHTRA	12/2015	355.13 355.13	11/2016 12/2016	12/2016
	Total		699.63 -		
	<u>STEEL</u>				
5	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 03/2016	03/2016
6	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016
7	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016
8	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	06/2016
9	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016
10	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
11	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
	Total		2,741.26 -		
	<u>PETROCHEMICALS</u>				
12	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 9,965.00	04/2012 12/2015	01/2016
	Total		5,460.61 -		

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	PETROLEUM				
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.08	11/2015 11/2016	10/2016
14	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 -	12/2016
15	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	03/2014 12/2016	12/2016
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 1,693.00	01/2012 -	12/2016
17	REPLACEMENT OF COKE CHAMBERS - [N16000177]IOCL,BIHAR	04/2013	480.00 -	02/2016 12/2016	12/2016
18	CRU TO ISOMERIZATION (ISOM) - [N16000200]BPCL,MULTI STATE	10/2011	725.00 -	11/2016 -	12/2016
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
20	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	- -	-
21	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	- -	-
22	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
23	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA	05/2016	1,945.00 -	- -	-
24	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	- -	-
25	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	- -	-
26	BRANCH PIPELINE FROM PATNA TO MOTIHARI & BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR	05/2016	664.00 -	- -	-
27	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 -	- -	-
28	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR	09/2015	324.00 -	- -	-
29	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	16,504.00 -	05/2016 -	-
	Total		35,860.49 -		
	POWER				
30	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	11/2013 -	03/2016
31	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 609.44	02/2014 03/2016	03/2016
32	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	01/2013 -	03/2016

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
33	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202]DVC, WEST BENGAL	04/2007	4,122.00 8,781.30	02/2011 -	03/2016
34	PATAN WIND FARM SITE, GUJARAT 50 MW - [N18000204]THDCIL, GUJARAT	10/2015	315.00 -	10/2016 -	10/2016
35	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 2,310.58	05/2014 06/2016	12/2016
36	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI - II HEP - [180100261]PGCIL, HIMACHAL PRADESH	12/2005	358.42 -	12/2008 09/2010	-
37	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 1,078.31	07/2013 -	-
38	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL, ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
39	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
40	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203]NHPC, RAJASTHAN	02/2015	302.49 302.00	02/2016 -	-
	Total		20,094.15 -		
	HEALTH AND FAMILY WELFARE				
41	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57 -	12/2014 -	03/2016
42	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC, DELHI	02/2013	414.11 -	11/2013 -	11/2014
43	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC, DELHI	11/2013	196.70 -	01/2016 -	01/2016
44	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC, DELHI	09/2013	444.70 -	12/2015 -	07/2016
45	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC, UTTAR PRADESH	10/2013	159.50 -	11/2013 -	10/2016
	Total		1,390.58 -		
	RAILWAYS				
46	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR, ASSAM	04/2003	971.22 -	- -	12/2009
47	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011
48	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR, ASSAM	04/2007	180.09 -	- -	05/2011
49	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011
50	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 266.00	- -	12/2012
51	HARMUTI-NAHARLAGUN - [N22000382]NFR, MULTI STATE	04/2006	614.54 -	- -	04/2014

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
52	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	08/2014
53	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	05/2015
54	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015
55	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015
56	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015
57	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 230.00	- 10/2015	10/2015
58	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	11/2015
59	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016
60	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016
61	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016
62	KATAKHAL TO BHAIKABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016
63	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016
65	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,595.40	- -	12/2016
66	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012 -	12/2016
67	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016
68	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016
69	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016
70	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL, CHHATISGARH	04/1995	304.00 -	12/2012 -	-
71	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
72	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
73	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
74	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-
75	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
76	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
77	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-
78	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
80	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
81	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
82	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-
83	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 535.13	- -	-
84	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.08	02/2011 -	-
85	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 724.89	12/2012 12/2012	-
86	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-
87	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
88	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
89	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
90	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
91	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
92	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-
93	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-
94	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
95	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	-
96	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
97	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-
98	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 334.87	12/2012 06/2016	-
99	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
100	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
101	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	- -	-
102	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
103	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
104	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
105	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
106	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
107	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
108	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
109	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
110	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
111	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 218.39	- -	-
112	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
113	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
114	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
115	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
116	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
117	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 -	-
118	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 633.87	- -	-
119	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
120	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
121	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 549.75	- -	-
122	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
123	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
124	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
125	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
126	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
127	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 1,500.00	- -	-
128	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
129	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
130	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 603.22	- -	-
131	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
132	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
133	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 268.52	- -	-
134	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 800.00	- -	-
135	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 319.58	- -	-
136	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 290.85	- -	-
137	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 260.60	- -	-
138	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-
139	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 234.41	03/2015 -	-
140	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 238.36	- -	-
141	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
142	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-
143	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 104.80	- -	-
144	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 198.88	- -	-
145	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
146	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
147	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
148	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 186.64	- -	-
149	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 173.91	- -	-
150	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 370.81	- -	-
151	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 131.47	- -	-
152	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 79.39	- -	-
153	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 681.68	- -	-
154	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
155	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-
156	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 1,801.00	- 06/2016	-
157	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	- -	-
158	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
159	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
160	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
161	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
162	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
163	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
164	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
165	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 197.17	- -	-
166	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
167	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
168	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
169	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-
170	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-
171	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-
172	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 1,714.49	- 06/2014	-
173	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-
174	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
175	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
176	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
177	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
178	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
179	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
180	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
181	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
182	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
183	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
184	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
185	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
186	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
187	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-
188	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
189	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 259.23	- -	-
190	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 272.20	- -	-
191	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
192	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-
193	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
194	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-
195	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-
196	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
197	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-
198	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-
199	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-
200	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-
201	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
202	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
203	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-
204	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-
205	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
206	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
207	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-
208	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-
209	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
210	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	-
211	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	-
212	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	-
213	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
214	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
215	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
216	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
217	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
218	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
219	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
220	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-
221	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
222	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
223	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
224	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
225	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
226	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
227	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
228	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
229	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
230	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
231	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	- -	-
232	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER, MULTI STATE	04/2010	268.52 -	- -	-
233	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	- -	-
234	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	- -	-
235	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	- -	-
236	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
237	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
238	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR, HARYANA	05/2015	400.00 -	- -	-
239	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		1,89,433.00 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
240	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	05/2016
241	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	05/2016
242	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	07/2016
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	07/2016
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	08/2014
245	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	09/2016
246	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	10/2016
247	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	11/2015
248	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010
249	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010
250	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010
251	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011
252	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011
253	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
254	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013
255	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014
257	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014
258	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015
259	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015
260	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015
261	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015
262	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015
263	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015
264	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015
265	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015
266	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015
267	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	01/2016
268	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	01/2016
269	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016
270	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016
271	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016
272	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016
273	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	06/2016
274	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	06/2016
276	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	07/2016
277	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	07/2016
278	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016
279	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016
280	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016
281	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016
282	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016
283	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016
284	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016
285	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016
286	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016
287	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016
288	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	10/2016
289	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	11/2016
290	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	11/2016
291	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	11/2016
292	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	11/2016
293	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
294	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016
295	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	12/2016
296	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016
297	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	12/2016
298	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	12/2016
299	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016
300	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016
301	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016
302	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
303	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-
304	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
305	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
306	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
307	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
308	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
309	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
310	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
311	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
312	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD TO FO - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
313	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
314	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
315	REHABILITATION AND UPGRADEATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 200.69	07/2014 -	-
316	REHABILITATION AND UPGRADEATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
317	REHABILITATION AND UPGRADEATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
318	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
319	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
320	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-
321	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
322	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
323	REHABILITATION AND UPGRADEATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
324	REHABILITATION AND UPGRADEATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
325	REHABILITATION AND UPGRADEATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
326	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
327	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
328	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
329	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
330	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
331	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
332	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
333	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
334	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
335	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
336	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
337	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
338	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
339	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
340	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
341	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
342	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
343	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
344	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-
345	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
346	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
347	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
348	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
349	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
350	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
351	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
352	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
353	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
354	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
355	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
356	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
357	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-
358	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
359	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
360	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
361	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
362	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-
363	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
364	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
365	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
366	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
367	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,					(January 2017)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
368	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
369	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	-
370	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
371	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
372	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
373	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
374	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
375	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
376	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
377	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
378	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
379	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
380	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
381	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
382	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	- -	-
383	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
384	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
385	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
386	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	- -	-
387	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
388	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	- -	-
389	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	- -	-
390	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
391	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
392	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
393	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
394	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
395	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
396	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
397	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
398	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
399	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
400	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
401	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
402	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
403	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
404	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
405	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
406	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
407	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-
408	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-
409	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-
410	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-
411	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-
412	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-
413	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
414	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
415	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
416	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
417	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-
418	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	- -	-
419	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
420	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-
421	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
422	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
423	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	-
424	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-
425	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
426	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI, MAHARASHTRA	11/2016	400.25 -	- -	-
427	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI, MAHARASHTRA	11/2016	446.17 -	- -	-
428	SIX LANNING FROM EXISTING KM 494.410 (DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550 (DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-
429	REHABILITATION AND UPGRADATION TO FOUR LANNING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
430	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-
431	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	-
432	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN (PACKAGE - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	-
433	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-
434	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI, UTTAR PRADESH	01/2017	450.68 -	- -	-
435	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V (PKG VI) REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	- -	-
436	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	- -	-
437	2-LANNING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2016
438	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH	12/2015	291.05 -	- -	-
439	FOUR LANNING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
	Total		1,16,081.87 -		
	SHIPPING AND PORTS				
440	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 03/2016	12/2016
441	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
442	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-
	Total		2,823.07 -		

Details of All Central Sector Infrastructure Projects having Without Date of Commissioning

Costing Rs. 150 crore & above,				(January 2017)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>URBAN DEVELOPMENT</u>				
443	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015
444	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	12/2016
445	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-
446	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CENTRA - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	- -	-
447	REHABILITATION AND STRENGTHENING OF SEWEWAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		63,061.20 -		
	Grand Total		4,38,199.07		

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
1	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	175.00	1.83	- -	12/2017	-	0/0
	Total		175.00 -	175.00	1.83				0/0
	<u>PETROLEUM</u>								
2	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	1,330.00	681.49	- -	03/2018	-	0/0
	Total		913.00 -	1,330.00	681.49				0/0
	<u>RAILWAYS</u>								
3	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 1,289.92	1,289.92	1,391.30	- -	01/2017	-	0/1
4	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	1,126.79	849.98	- -	02/2017	-	0/1
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	1,010.00	983.96	- 03/2017	03/2017	0(R3)	0/0
6	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	230.24	- -	03/2017	-	0/0
7	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	1,101.16	194.91	- -	03/2017	-	0/0
8	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	812.05	- -	03/2017	-	0/1
9	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	148.33	- -	03/2017	-	0/0
10	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	381.39	338.87	- 03/2017	03/2017	0(R3)	0/0
11	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	343.00	267.31	- -	06/2017	-	0/0
12	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	317.83	- -	06/2017	-	0/0
13	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	201.23	- -	12/2017	-	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
14	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	51.09	- -	12/2017	-	0/0
15	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]RVNL,MULTI STATE	04/2008	822.39 -	1,480.83	1,551.40	- -	03/2018	-	0/1
16	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	445.00	461.09	- -	03/2018	-	0/0
17	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	330.00	129.05	- -	03/2018	-	0/0
18	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	1,871.00	1,078.13	- -	03/2018	-	0/0
19	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 157.94	157.94	48.72	- -	11/2018	-	0/0
20	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 855.16	860.00	566.46	- -	12/2018	-	0/0
21	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	464.49	- 12/2018	12/2018	0(R3)	0/0
22	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	720.00 678.54	678.54	.75	- 12/2018	12/2018	0(R3)	0/38
23	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	525.00	557.98	- 03/2019	03/2019	0(R3)	0/0
24	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	794.39	- 12/2009	03/2019	111(R1)	0/0
25	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	772.88	- 09/2009	03/2019	114(R1)	0/0
26	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	780.00	363.52	- -	03/2019	-	0/0
27	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	399.63	19.72	- -	03/2019	-	0/0
28	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	1,037.15	711.78	- -	03/2019	-	0/0
29	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	03/2019	-	0/0
30	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 972.52	972.52	99.11	- -	03/2019	-	1/1
31	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	450.00	.79	- -	03/2019	-	0/0
32	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	508.00	380.01	- -	03/2019	-	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
33	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	398.93	33.20	- -	03/2019	-	0/0
34	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 332.14	332.14	169.99	03/2019	03/2019	0(R3)	0/0
35	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 199.12	199.12	102.10	- 03/2019	03/2019	0(R3)	0/0
36	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL, KARNATAKA	04/2010	2,127.00 -	2,127.00	701.23	- -	03/2019	-	0/1
37	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL, TAMIL NADU	04/2011	190.10 -	355.96	240.92	- -	03/2019	-	0/0
38	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	620.00	-	- -	09/2019	-	0/0
39	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	2,145.00	363.12	- -	03/2020	-	0/0
40	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL, GUJARAT	04/2012	567.18 -	975.62	177.28	- -	03/2020	-	0/0
41	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	03/2020	-	0/0
42	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	283.43	- -	03/2020	-	0/0
43	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 1,160.83	1,160.83	356.19	- 03/2020	03/2020	0(R3)	1/1
44	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	238.03	112.11	- -	03/2020	-	0/0
45	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,900.00 1,141.00	1,141.00	226.10	- 03/2020	03/2020	0(R3)	0/5
46	YELAHANKA-PENKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 860.43	860.43	124.02	- -	03/2020	-	0/0
47	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	176.03	- 11/2015	03/2020	52(R3)	0/2
48	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	514.68 2,271.50	2,271.50	1,040.88	- 12/2020	12/2020	0(R3)	0/0
49	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	376.59 -	644.38	1.52	- -	12/2020	-	0/0
50	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL, GUJARAT	04/2013	1,266.89 -	1,266.89	191.18	- -	12/2020	-	0/0
51	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	330.00 1,045.20	2,125.18	90.93	- -	03/2021	-	0/0
52	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	6,000.00	27.27	- -	03/2021	-	0/0
53	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	277.70 792.89	792.89	85.63	- 03/2021	03/2021	0(R3)	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
54	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	1,579.27	352.12	- 03/2020	03/2021	12(R3)	0/0
55	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	810.28	7.55	- -	03/2021	-	0/0
56	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	11.08	- 03/2021	03/2021	0(R3)	0/0
57	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,232.32	4.04	- -	03/2021	-	0/0
58	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	870.96	.02	- -	03/2021	-	0/0
59	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	3.48	- -	03/2021	-	0/0
60	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	3,004.90	674.28	- 06/2021	06/2021	0(R3)	0/0
61	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N2200032]SCR,TELANGANA	04/2006	378.56 1,160.47	1,160.47	3.66	- -	03/2022	-	0/1
62	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	362.55	- 03/2022	03/2022	0(R3)	0/0
63	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	540.02	28.59	- 03/2022	03/2022	0(R3)	0/0
64	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	1,272.19	5.90	- 03/2022	03/2022	0(R3)	0/0
65	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	1,035.16	-	- 03/2022	03/2022	0(R3)	0/0
66	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	637.95	-	- 03/2022	03/2022	0(R3)	0/0
67	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	310.45	- 03/2021	06/2022	15(R3)	0/0
68	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 1,849.60	2,650.00	377.44	- 03/2023	03/2023	0(R3)	0/0
69	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	2,491.43	331.52	- 03/2023	03/2023	0(R3)	0/0
70	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	2,449.91	-	- 03/2023	03/2023	0(R3)	0/0
71	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	3,627.47	1.17	- 03/2023	03/2023	0(R3)	0/0
72	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	2,081.27	-	- 03/2023	03/2023	0(R3)	0/0
73	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	9,968.00	-	- 03/2024	03/2024	0(R3)	0/0
74	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	2,425.00	-	- 03/2024	03/2024	0(R3)	0/0
	Total		70,117.59 -	98,308.50	20,764.35				2/53

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
75	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	389.73	- -	03/2017	-	0/0
76	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	1,665.00	1,680.00	- -	03/2017	-	0/0
77	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	- -	06/2017	-	3/3
78	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	446.77	107.87	- -	06/2017	-	0/4
79	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	795.76	36.07	- -	06/2017	-	0/0
80	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	30.21	- -	06/2017	-	0/0
81	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	20.05	- -	06/2017	-	0/0
82	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	-	- -	06/2017	-	0/0
83	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	168.30	24.63	- -	10/2017	-	0/4
84	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	845.24	266.74	- -	11/2017	-	0/0
85	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	6.35	- -	11/2017	-	0/0
86	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	928.83	87.51	- -	12/2017	-	0/0
87	TWO LANING WITH PS OF CHHAPRA - GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	854.80	146.28	- -	12/2017	-	0/0
88	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	361.15	-	- -	01/2018	-	0/0
89	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	1,393.00	1,786.45	- -	01/2018	-	0/0
90	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	69.82	- -	02/2018	-	0/0
91	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_ NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	771.18	138.15	- -	03/2018	-	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	297.00	84.84	- -	04/2018	-	0/1
93	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	8.63	- -	04/2018	-	0/0
94	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	509.13	-	- 04/2018	04/2018	0(R3)	0/0
95	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	-	- 04/2018	04/2018	0(R3)	0/0
96	TWO LANING WITH PS OF CHHAPRA - REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	516.13	155.20	- -	04/2018	-	0/0
97	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	414.00	44.69	- -	05/2018	-	0/0
98	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	26.88	- -	05/2018	-	0/0
99	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	33.72	- -	05/2018	-	0/0
100	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	54.33	- -	05/2018	-	0/0
101	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	867.66	413.78	- -	05/2018	-	0/0
102	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	-	- 05/2018	05/2018	0(R3)	0/0
103	TWO LANING WITH PS OF JOWAI - MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	104.75	- -	05/2018	-	0/0
104	UP/HARYANA BORDER - YAMUNA NAGAR - SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	600.85	63.82	- -	05/2018	-	0/0
105	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	676.73	-	- -	06/2018	-	0/0
106	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	-	- -	06/2018	-	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
107	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	197.69	-	-	07/2018	-	0/0
108	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	27.95	-	07/2018	-	0/0
109	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	244.00	-	-	07/2018	-	0/0
110	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	312.54	-	08/2018	-	0/0
111	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	103.80	-	08/2018	-	0/0
112	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	-	-	08/2018	-	0/0
113	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	331.46	-	-	10/2018	-	0/0
114	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	444.03	-	11/2018	-	0/0
115	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	-	-	11/2018	-	0/0
116	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	-	-	11/2018	-	0/0
117	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	-	-	11/2018	-	0/0
118	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	-	-	11/2018	-	0/0
119	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	1,657.20	-	-	01/2019	-	0/0
120	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	315.07	-	01/2019	-	0/0
121	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	227.49	-	-	01/2019	-	0/0
122	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	1,885.74	-	-	03/2019	-	0/0

Details of All Central Sector Infrastructure Projects having Without Original Date of Commissioning

Costing Rs. 150 crore & above (January 2017)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
123	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	29.92	- -	03/2019	-	0/0
124	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	997.15	-	- -	03/2019	-	0/0
125	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	-	- -	04/2019	-	0/0
126	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	-	- -	04/2019	-	0/0
127	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	2,288.18	-	- -	05/2019	-	0/0
128	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	701.12	-	- -	05/2019	-	0/0
129	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	4.54	- -	05/2019	-	0/0
130	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	1,081.57	-	- -	06/2019	-	0/0
	Total		42,464.14 -	42,463.63	7,836.88				3/12
	<u>URBAN DEVELOPMENT</u>								
131	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI(MOD - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	2.39	- 04/2019	04/2019	0(R3)	0/2
	Total		197.33 -	197.33	2.39				0/2
	Grand Total		1,13,867.06	1,42,474.46	29,286.94				5/67

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Annexure - X

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	12/2017	0/0
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 -	05/2012 -	-	0/0
	Total		1,177.28 -			0/0
	<u>COAL</u>					
5	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 -	06/2017 -	06/2017	0/0
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
7	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
8	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	Total		18,960.36 -			0/0
	<u>FERTILISERS</u>					
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	11/2016 09/2017	09/2017	0/0
	Total		197.79 -			0/0
	<u>STEEL</u>					
10	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 03/2016	03/2016	0/0
11	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) IN DIFFER - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	03/2016	0/0
12	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	04/2016	0/0
13	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	06/2016	0/0
14	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	12/2016	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
15	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	03/2017	0/0
16	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	03/2017	0/0
17	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	03/2017	0/0
18	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2017	0/0
19	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 07/2017	07/2017	0/0
20	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	09/2017	0/0
21	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	09/2017	0/0
22	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	10/2016 -	12/2017	0/0
23	CONSTRUCTION OF CAMPUS AND BUILDING FOR NATIONAL INSTITUTE OF PHARMACEUTICAL EDUCATION AND RESEARCH(- [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	12/2017	0/0
24	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	12/2017 -	12/2017	0/0
25	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	03/2018	0/0
26	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	04/2018	0/0
27	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	09/2018 -	09/2018	0/0
28	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	06/2019 -	06/2019	0/0
29	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RAJIV GA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
	Total		14,817.21 -			0/0
	<u>PETROLEUM</u>					
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KARNATAKA	01/2006	993.00 1,693.00	01/2012 -	12/2016	0/0
31	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	02/2017	0/0
32	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	04/2015 03/2017	03/2017	0/0
33	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]OIL,GUJARAT	11/2015	500.00 435.00	03/2017 -	03/2017	0/0
34	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 -	05/2017	0/0
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 06/2017	06/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]ONGC,MADHYA PRADESH	03/2009	181.02 -	01/2017 06/2017	06/2017	0/0
37	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]ONGC,TRIPURA	05/2016	215.38 -	06/2017 06/2017	06/2017	0/0
38	NEW 250 TMTPA LPG PLANT AT PANAGARH - [N16000222]HPCL, WEST BENGAL	08/2014	190.45 -	09/2017 -	09/2017	0/0
39	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205]BPCL,MAHARASHTRA	05/2015	2,443.00 1,417.00	12/2017 06/2017	12/2017	0/0
40	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00 -	06/2017 -	12/2017	0/0
41	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]IOCL,GUJARAT	02/2016	931.00 -	07/2017 02/2018	02/2018	0/0
42	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	- -	03/2018	0/0
43	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	12/2016 -	03/2018	0/0
44	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 04/2018	04/2018	0/0
45	ENNORE TERMINAL - [N16000224]BPCL,TAMIL NADU	08/2014	393.00 -	04/2018 -	04/2018	0/0
46	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 439.03	03/2017 -	06/2018	0/0
47	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 -	08/2018 -	08/2018	0/0
48	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0
49	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 -	10/2018 -	10/2018	0/0
50	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	11/2018 -	11/2018	0/0
51	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 -	04/2019 03/2019	03/2019	0/0
52	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 -	12/2017 03/2019	03/2019	0/0
53	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 -	03/2019 -	03/2019	0/0
54	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 171.00	03/2019 -	03/2019	0/0
55	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA	05/2015	224.00 207.00	04/2019 -	04/2019	0/0
56	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 -	05/2019 05/2019	05/2019	0/0
57	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH	09/2016	407.00 -	09/2019 -	09/2019	0/0
58	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 -	11/2019 -	11/2019	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
59	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM	02/2016	2,582.00 -	11/2019 -	11/2019	0/0
60	BSVI UP GRADATION - [N16000257]MANGALORE REFIN, KARNATAKA	09/2016	1,810.00 1,810.00	12/2019 -	12/2019	0/0
61	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL, KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
62	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC, MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
63	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC, ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 -	06/2020	0/0
64	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH	07/2016	20,928.00 -	07/2020 -	07/2020	0/0
65	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC, JHARKHAND	12/2015	658.62 -	03/2023 -	03/2023	0/0
66	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-	0/0
67	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	- -	-	0/0
68	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE	01/2015	2,321.00 -	- -	-	0/0
69	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL, MULTI STATE	02/2015	890.00 -	- -	-	0/0
70	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL, MAHARASHTRA	05/2016	1,945.00 -	- -	-	0/0
71	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL, HIMACHAL PRADESH	02/2016	151.00 -	- -	-	0/0
72	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL	04/2016	1,021.00 -	- -	-	0/0
73	BRANCH PIPELINE FROM PATNA TO MOTIHARI & BAITALPUR ON BKPL - [N16000252]IOCL, BIHAR	05/2016	664.00 -	- -	-	0/0
74	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL, TAMIL NADU	05/2016	4,497.00 -	- -	-	0/0
75	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL, BIHAR	09/2015	324.00 -	- -	-	0/0
	Total		1,19,977.46 -			0/0
	POWER					
76	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	09/2014 -	05/2017	0/0
77	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL, DELHI	05/2015	780.33 -	07/2017 -	07/2017	0/0
78	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS - [N18000211]PGCIL, ODISHA	01/2016	187.04 -	06/2018 -	09/2017	0/0
79	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]PGCIL, JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
80	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL, RAJASTHAN	07/2015	307.18 -	11/2017 -	11/2017	0/0
81	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	04/2016 -	12/2017	0/0
82	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL, MULTI STATE	03/2015	1,071.24 -	09/2017 -	12/2017	0/0
83	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL, MADHYA PRADESH	01/2016	305.04 -	03/2017 -	12/2017	0/0
84	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 -	01/2018	0/0
85	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL, MULTI STATE	03/2015	197.40 -	03/2018 -	03/2018	0/0
86	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	04/2018 -	04/2018	0/0
87	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]PGCIL, TAMIL NADU	01/2016	162.11 -	05/2018 -	05/2018	0/0
88	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]PGCIL, TRIPURA	05/2016	409.19 -	05/2018 -	05/2018	0/0
89	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL, MADHYA PRADESH	04/2016	287.99 -	06/2018 -	06/2018	0/0
90	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL, MULTI STATE	07/2015	2,247.37 -	07/2018 -	07/2018	0/0
91	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]PGCIL, GUJARAT	01/2016	244.19 -	07/2018 -	07/2018	0/0
92	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	07/2018 -	07/2018	0/0
93	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]PGCIL, ANDHRA PRADESH	01/2016	207.88 -	07/2018 -	07/2018	0/0
94	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	07/2018 -	07/2018	0/0
95	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
96	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
97	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
98	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
99	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
100	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
101	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL, MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
102	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
103	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
104	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
105	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
106	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
107	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
108	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	01/2023	0/0
109	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
110	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	10/2017	0/0
	Total		55,139.82 -			0/0
	<u>HEAVY INDUSTRY</u>					
111	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	12/2017	0/0
	Total		1,718.00 -			0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
112	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2016	0/0
113	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	11/2014	0/0
114	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK - [N21000005]HSCC,DELHI	11/2013	196.70 -	01/2016 -	01/2016	0/0
115	SAFDARJUNG HOSPITAL RE-DEVELOPMENT AND OTHERS -SUPER SPECIALITY BLOCK - [N21000004]HSCC,DELHI	09/2013	444.70 -	12/2015 -	07/2016	0/0
116	AIIMS-RAEBARELI-HOUSING - [N21000006]HSCC,UTTAR PRADESH	10/2013	159.50 -	11/2013 -	10/2016	0/0
117	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	06/2017	0/0
118	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	06/2017	0/0
119	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2017	0/0
120	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	02/2018	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
121	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	03/2018	0/0
122	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	05/2018	0/0
123	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA	07/2016	312.99 -	08/2018 -	08/2018	0/0
124	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	09/2018	0/0
	Total		3,637.08 -			0/0
	RAILWAYS					
125	LUMDING-DIBRUGARH (628 KM) INCL. LINK BRANCH LINES OF HAIBARGAON-MAIRABARI (89 KM) - [N22000385]NFR,ASSAM	04/2003	971.22 -	- -	12/2009	0/0
126	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	01/2011	0/0
127	NEW GUWAHATI-DIGARU-PATCH DOUBLING - [N22000387]NFR,ASSAM	04/2007	180.09 -	- -	05/2011	0/0
128	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	03/2011 -	10/2011	0/0
129	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 266.00	- -	12/2012	0/0
130	HARMUTI-NAHARLAGUN - [N22000382]NFR,MULTI STATE	04/2006	614.54 -	- -	04/2014	0/0
131	DUDHNOI-MENDHIPATHAR - [N22000378]NFR,MULTI STATE	04/1992	315.64 -	- -	08/2014	0/0
132	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]NFR,ASSAM	04/2003	4,300.00 -	- -	05/2015	0/0
133	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	07/2015	0/0
134	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	09/2015	0/0
135	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	12/2008 -	10/2015	0/0
136	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 230.00	- 10/2015	10/2015	0/0
137	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	11/2015	0/0
138	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 717.15	03/2012 01/2016	01/2016	0/0
139	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 02/2016	02/2016	0/0
140	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	03/2012 12/2013	03/2016	0/0
141	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 -	12/2012 -	03/2016	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
142	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2016	0/0
143	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
144	KANPUR KASGANJ MATHURA(GC) NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,595.40	- -	12/2016	0/0
145	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 1,030.29	03/2012 -	12/2016	0/0
146	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2016	0/0
147	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]RVNL, WEST BENGAL	04/2010	171.02 -	06/2013 -	12/2016	0/0
148	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	12/2016	0/0
149	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017	0/0
150	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	03/2017	0/0
151	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	03/2017	0/0
152	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	03/2017	0/0
153	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 155.56	12/2010 03/2017	03/2017	0/0
154	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	03/2009 -	03/2017	0/0
155	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	- -	03/2017	0/0
156	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	03/2017	0/0
157	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
158	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 579.03	03/2017 -	03/2017	0/0
159	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 203.00	- 03/2017	03/2017	0/0
160	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	06/2017	0/0
161	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	06/2017	0/0
162	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	06/2017	0/0
163	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 06/2017	06/2017	0/0
164	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 843.45	02/2009 12/2017	12/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
165	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	12/2017	0/0
166	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	- -	12/2017	0/0
167	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	12/2017	0/0
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2017	0/0
169	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR,WEST BENGAL	04/2011	209.77 -	- -	03/2018	0/0
170	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL	04/2012	283.55 -	- -	03/2018	0/0
171	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
172	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2018	0/0
173	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	03/2018	0/0
174	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
175	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	04/2008 12/2011	06/2018	0/0
176	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	06/2018	0/0
177	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 157.94	- -	11/2018	0/0
178	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	12/2018	0/0
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	03/2016 -	12/2018	0/0
180	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 855.16	- -	12/2018	0/0
181	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- 12/2018	12/2018	0/0
182	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 372.09	- 03/2019	03/2019	0/0
183	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
184	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 1,319.33	- 12/2009	03/2019	0/0
185	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	03/2019	0/0
186	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	- -	03/2019	0/0
187	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,821.29	03/2014 03/2019	03/2019	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
188	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2019	0/0
189	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 658.07	03/2014 03/2019	03/2019	0/0
190	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
191	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	03/2019	0/0
192	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	03/2019	0/0
193	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 -	- -	03/2019	0/0
194	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 -	- -	03/2019	0/0
195	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 -	- -	03/2019	0/0
196	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 -	- -	03/2019	0/0
197	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 332.14	- 03/2019	03/2019	0/0
198	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	- 03/2019	03/2019	0/0
199	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]RVNL,TAMIL NADU	04/2011	190.10 -	- -	03/2019	0/0
200	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2019	0/0
201	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2019	0/0
202	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	03/2019	0/0
203	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
204	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423]CCOI,RAJASTHAN	04/2012	471.82 -	03/2019 -	03/2019	0/0
205	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
206	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	03/2019	0/0
207	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	03/2019	0/0
208	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	- -	09/2019	0/0
209	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,160.54	03/1998 -	12/2019	0/0
210	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	12/2019	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Antici Pated	Milestones Achieved/ Total
1	2	3	4	5	6	7
211	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 03/2020	03/2020	0/0
212	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 1,125.89	12/2011 03/2020	03/2020	0/0
213	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 4,454.18	03/2011 -	03/2020	0/0
214	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
215	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	- -	03/2020	0/0
216	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
217	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 2,393.48	04/2014 -	03/2020	0/0
218	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
219	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2020	0/0
220	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
221	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	- -	03/2020	0/0
222	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	03/2020	0/0
223	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	- -	03/2020	0/0
224	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	03/2020	0/0
225	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	- -	03/2020	0/0
226	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	03/2020	0/0
227	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
228	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
229	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
230	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2020	0/0
231	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
232	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 12/2020	12/2020	0/0
233	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	- 12/2020	12/2020	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
234	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	12/2020	0/0
235	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	- -	12/2020	0/0
236	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	- -	12/2020	0/0
237	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	12/2020	0/0
238	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
239	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,045.20	- -	03/2021	0/0
240	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	- -	03/2021	0/0
241	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	- 03/2021	03/2021	0/0
242	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,111.99	- 03/2020	03/2021	0/0
243	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	03/2021	0/0
244	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	- 03/2021	03/2021	0/0
245	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2021 -	03/2021	0/0
246	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2021 -	03/2021	0/0
247	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2021 -	03/2021	0/0
248	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
249	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2021	0/0
250	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	- -	03/2021	0/0
251	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	- -	03/2021	0/0
252	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	- -	03/2021	0/0
253	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	03/2021	0/0
254	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- 06/2021	06/2021	0/0
255	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 1,013.50	12/2021 -	12/2021	0/0
256	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 604.04	12/2021 -	12/2021	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
257	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
258	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- 03/2022	03/2022	0/0
259	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	- 03/2022	03/2022	0/0
260	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	03/2022	0/0
261	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	- 03/2022	03/2022	0/0
262	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 -	- 03/2022	03/2022	0/0
263	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 -	- 03/2022	03/2022	0/0
264	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	- 03/2021	06/2022	0/0
265	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
266	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	02/2019 12/2022	12/2022	0/0
267	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 1,849.60	- 03/2023	03/2023	0/0
268	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 2,491.43	- 03/2023	03/2023	0/0
269	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 -	- 03/2023	03/2023	0/0
270	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	- 03/2023	03/2023	0/0
271	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	- 03/2023	03/2023	0/0
272	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	- 03/2024	03/2024	0/0
273	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	- 03/2024	03/2024	0/0
274	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
275	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
276	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
277	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	12/2025	0/0
278	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	12/2026	0/0
279	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
280	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
281	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-	0/0
282	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
283	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 774.90	- -	-	0/0
284	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- -	-	0/0
285	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
286	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	06/2004 -	-	0/0
287	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 458.26	07/2008 -	-	0/0
288	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0
289	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
290	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
291	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 781.02	06/2007 -	-	0/0
292	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 535.13	- -	-	0/0
293	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 228.08	02/2011 -	-	0/0
294	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 724.89	12/2012 12/2012	-	0/0
295	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- -	-	0/0
296	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
297	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
298	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
299	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
300	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 874.57	03/2013 -	-	0/0
301	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	-	0/0
302	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
303	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 167.73	03/2012 -	-	0/0
304	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
305	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
306	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 334.87	12/2012 06/2016	-	0/0
307	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
308	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-	0/0
309	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-	0/0
310	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
311	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-	0/0
312	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
313	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-	0/0
314	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	- -	-	0/0
315	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-	0/0
316	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR, RAJASTHAN	04/2011	239.73 -	- -	-	0/0
317	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 218.39	- -	-	0/0
318	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	- -	-	0/0
319	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	- -	-	0/0
320	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
321	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER, MULTI STATE	04/2010	553.63 -	- -	-	0/0
322	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
323	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 -	12/2015 -	-	0/0
324	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	490.80 633.87	- -	-	0/0
325	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
326	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
327	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 549.75	- -	-	0/0
328	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
329	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
330	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
331	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
332	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
333	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 1,500.00	- -	-	0/0
334	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
335	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
336	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 603.22	- -	-	0/0
337	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
338	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
339	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 268.52	- -	-	0/0
340	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 800.00	- -	-	0/0
341	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 319.58	- -	-	0/0
342	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 290.85	- -	-	0/0
343	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 260.60	- -	-	0/0
344	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 1,130.13	- -	-	0/0
345	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 234.41	03/2015 -	-	0/0
346	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 238.36	- -	-	0/0
347	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
348	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 595.91	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
349	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 104.80	- -	-	0/0
350	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 198.88	- -	-	0/0
351	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
352	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
353	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
354	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 186.64	- -	-	0/0
355	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 173.91	- -	-	0/0
356	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 370.81	- -	-	0/0
357	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 131.47	- -	-	0/0
358	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 79.39	- -	-	0/0
359	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 681.68	- -	-	0/0
360	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
361	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 260.16	- -	-	0/0
362	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 1,801.00	- 06/2016	-	0/0
363	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
364	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
365	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
366	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
367	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 197.17	- -	-	0/0
368	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
369	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
370	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
371	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- -	-	0/0

Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule

Costing Rs. 150 crore & above (January 2017)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
372	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 466.65	- -	-	0/0
373	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 832.47	- -	-	0/0
374	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 348.85	- -	-	0/0
375	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
376	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
377	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
378	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
379	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
380	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
381	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
382	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
383	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
384	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 1,922.00	- -	-	0/0
385	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
386	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 259.23	- -	-	0/0
387	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 272.20	- -	-	0/0
388	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
389	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 -	-	0/0
390	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
391	HOSADURGA - CHICKAJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 203.40	- -	-	0/0
392	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- -	-	0/0
393	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
394	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
395	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM) - [N22000345]NER,UTTAR PRADESH	04/1997	836.26 1,072.52	- -	-	0/0
396	DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	81,459.00 -	- -	-	0/0
397	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	- -	-	0/0
398	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
399	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 3,631.00	- -	-	0/0
400	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	-	0/0
401	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
402	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
403	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	556.31 -	- -	-	0/0
404	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
405	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
406	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	- -	-	0/0
407	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	- -	-	0/0
408	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
409	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
410	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-	0/0
411	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
412	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
413	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-	0/0
414	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 -	- -	-	0/0
415	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
416	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
417	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
418	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
419	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
420	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
421	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
422	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
423	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
424	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
425	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	- -	-	0/0
426	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER, MULTI STATE	04/2010	268.52 -	- -	-	0/0
427	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
428	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR, MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
429	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	- -	-	0/0
430	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
431	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
432	ROHTAK - BHIWANI DOUBLING - [N22000331]NWR, HARYANA	05/2015	400.00 -	- -	-	0/0
433	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 -	-	0/0
	Total		3,19,156.24 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
434	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	05/2016	0/0
435	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	05/2016	0/0
436	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
437	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	07/2016	0/0
438	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	07/2016	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
439	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	08/2014	0/0
440	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	09/2016	0/0
441	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	10/2016	0/0
442	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	11/2015	0/0
443	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	09/2010	0/0
444	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	09/2010	0/0
445	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	10/2010	0/0
446	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	02/2011	0/0
447	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	02/2011	0/0
448	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
449	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	10/2013	0/0
450	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	08/2014	0/0
451	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.22	- 11/2014	11/2014	0/0
452	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	11/2014	0/0
453	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	02/2015	0/0
454	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	03/2015	0/0
455	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	03/2015	0/0
456	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	03/2015	0/0
457	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	04/2015	0/0
458	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	05/2015	0/0
459	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	08/2015	0/0
460	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	08/2015	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
461	FOUR LANEING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	11/2015	0/0
462	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	02/2016	0/0
463	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	03/2016	0/0
464	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 223.00	05/2016 -	05/2016	0/0
465	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	05/2016	0/0
466	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	06/2016	0/0
467	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	08/2016	0/0
468	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	08/2016	0/0
469	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	09/2016	0/0
470	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	10/2016	0/0
471	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	10/2016	0/0
472	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	10/2016	0/0
473	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	10/2016	0/0
474	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	10/2016	0/0
475	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	10/2016	0/0
476	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	10/2016	0/0
477	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	11/2016	0/0
478	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	12/2016	0/0
479	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	12/2016	0/0
480	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2016	0/0
481	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	12/2016	0/0
482	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	12/2016	0/0
483	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	12/2016	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
484	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00	05/2013	01/2017	0/0
485	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76	07/2013	01/2017	0/0
486	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22	04/2015	01/2017	0/0
487	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15	01/2016	01/2017	0/0
488	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21	01/2017	01/2017	0/0
489	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11	01/2017	01/2017	0/0
490	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05	01/2017	01/2017	0/0
491	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00	02/2009	02/2017	0/0
492	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04	11/2008	02/2017	0/0
493	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00	06/2008	02/2017	0/0
494	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 09/2016	02/2017	0/0
495	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	06/2015	02/2017	0/0
496	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54	05/2013	02/2017	0/0
497	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00	09/2015	02/2017	0/0
498	REHABILITATION AND UPGADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017	02/2017	0/0
499	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16	08/2016	02/2017	0/0
500	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00	02/2017	02/2017	0/0
501	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64	11/2008	03/2017	0/0
502	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00	04/2009	03/2017	0/0
503	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00	03/2008 10/2016	03/2017	0/0
504	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00	05/2008 12/2016	03/2017	0/0
505	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00	09/2007	03/2017	0/0
506	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00	07/2009	03/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
507	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00	05/2010	03/2017	0/0
508	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00	04/2013	03/2017	0/0
509	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00	08/2012	03/2017	0/0
510	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00	06/2013	03/2017	0/0
511	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76	08/2014	03/2017	0/0
512	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	03/2013	03/2017	0/0
513	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00	11/2013	03/2017	0/0
514	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00	08/2013	03/2017	0/0
515	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00	02/2014	03/2017	0/0
516	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	03/2014	03/2017	0/0
517	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09	04/2014	03/2017	0/0
518	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00	06/2014	03/2017	0/0
519	2-LANNING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36	01/2014	03/2017	0/0
520	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60	09/2016	03/2017	0/0
521	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79	04/2016	03/2017	0/0
522	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10	03/2016	03/2017	0/0
523	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85	01/2016	03/2017	0/0
524	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34	01/2016	03/2017	0/0
525	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78	01/2016	03/2017	0/0
526	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHAI,UTTAR PRADESH	10/2013	445.89	03/2017	03/2017	0/0
527	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]P.W.D,UTTAR PRADESH	11/2010	305.49	03/2017	03/2017	0/0
528	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHAI,UTTAR PRADESH	10/2013	317.76	03/2017	03/2017	0/0
529	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHAI,UTTAR PRADESH	10/2013	493.94	03/2017	03/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
530	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	03/2017	0/0
531	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	03/2017	0/0
532	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2017	0/0
533	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	03/2017	0/0
534	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	03/2017	0/0
535	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	03/2017	0/0
536	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	03/2017	0/0
537	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	03/2017	0/0
538	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	04/2017	0/0
539	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	04/2017	0/0
540	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	04/2017	0/0
541	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338]NHAI,RAJASTHAN	10/2014	206.12 -	04/2017 -	04/2017	0/0
542	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	04/2017	0/0
543	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	04/2017	0/0
544	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	05/2017	0/0
545	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	05/2017	0/0
546	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	05/2017	0/0
547	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2017	0/0
548	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	05/2017	0/0
549	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	05/2017	0/0
550	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	05/2017	0/0
551	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	05/2017	0/0
552	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	05/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
553	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	05/2017	0/0
554	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	05/2017	0/0
555	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2017	06/2017	0/0
556	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	06/2017	0/0
557	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2017	0/0
558	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	06/2017	0/0
559	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	06/2017	0/0
560	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	06/2017	0/0
561	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	06/2017	0/0
562	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	06/2017	0/0
563	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	06/2017	0/0
564	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	06/2017	0/0
565	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2017	0/0
566	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	- -	06/2017	0/0
567	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	06/2017	0/0
568	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	07/2017	0/0
569	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	07/2017	0/0
570	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	07/2017	0/0
571	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	08/2017	0/0
572	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	08/2017	0/0
573	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	08/2017	0/0
574	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	08/2017	0/0
575	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	09/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
576	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 -	09/2017	0/0
577	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	09/2017	0/0
578	PANVEL-INDAPUR - [N24000216]NHAI, MAHARASHTRA	12/2011	942.69 -	06/2014 -	09/2017	0/0
579	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	09/2017 -	09/2017	0/0
580	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	09/2017 -	09/2017	0/0
581	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]NHAI, JHARKHAND	09/2015	341.61 -	09/2017 -	09/2017	0/0
582	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	09/2017	0/0
583	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	09/2017	0/0
584	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	07/2013 -	10/2017	0/0
585	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	10/2017	0/0
586	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH, ODISHA	01/1991	218.63 251.92	10/2017 -	10/2017	0/0
587	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	10/2017	0/0
588	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH, ODISHA	02/2015	239.91 240.00	10/2017 -	10/2017	0/0
589	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH, ODISHA	03/2015	226.31 226.00	10/2017 -	10/2017	0/0
590	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	11/2017	0/0
591	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.00	11/2017 -	11/2017	0/0
592	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH, KARNATAKA	03/2015	165.67 -	11/2015 -	11/2017	0/0
593	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH, KARNATAKA	03/2015	159.12 -	11/2015 -	11/2017	0/0
594	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	11/2017	0/0
595	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	11/2017	0/0
596	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- -	11/2017	0/0
597	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI, PUNJAB	09/2015	273.06 -	- -	11/2017	0/0
598	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD, ODISHA	12/2011	159.39 -	11/2017 -	11/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
599	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2017	0/0
600	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2017	0/0
601	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2017	0/0
602	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2017	0/0
603	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	12/2017	0/0
604	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	08/2013 -	12/2017	0/0
605	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2017	0/0
606	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	12/2017	0/0
607	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	12/2017	0/0
608	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	12/2017	0/0
609	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366]NHAI,ODISHA	06/2015	996.37 -	12/2017 -	12/2017	0/0
610	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	12/2017	0/0
611	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	12/2017	0/0
612	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	-	12/2017	0/0
613	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	-	12/2017	0/0
614	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	01/2018	0/0
615	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 -	-	01/2018	0/0
616	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	01/2018	0/0
617	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	-	01/2018	0/0
618	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	01/2018	0/0
619	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	02/2018	0/0
620	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	02/2018	0/0
621	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	02/2018	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
622	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN	08/2015	482.27 -	02/2018 -	02/2018	0/0
623	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD, ASSAM	05/2011	176.22 -	02/2018 -	02/2018	0/0
624	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD, ASSAM	11/2014	218.31 -	02/2018 -	02/2018	0/0
625	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	-	02/2018	0/0
626	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	03/2018	0/0
627	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI, RAJASTHAN	09/2015	567.51 -	03/2018 -	03/2018	0/0
628	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH	06/2015	774.57 -	03/2018 -	03/2018	0/0
629	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL	01/1991	322.00 -	03/2018 -	03/2018	0/0
630	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	03/2018	0/0
631	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	03/2018	0/0
632	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	03/2018	0/0
633	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI, MULTI STATE	09/2015	788.51 -	03/2018 -	03/2018	0/0
634	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI, UTTAR PRADESH	09/2015	785.78 -	03/2018 -	03/2018	0/0
635	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	03/2018	0/0
636	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2018	0/0
637	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	03/2018	0/0
638	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	08/2015 -	03/2018	0/0
639	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	-	03/2018	0/0
640	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	04/2018	0/0
641	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI, RAJASTHAN	08/2014	822.90 -	04/2018 -	04/2018	0/0
642	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 -	-	04/2018	0/0
643	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	-	04/2018	0/0
644	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI, CHHATISGARH	12/2015	726.67 -	04/2018	04/2018	0/0

Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule

Costing Rs. 150 crore & above				(January 2017)		
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
645	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	- -	04/2018	0/0
646	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	04/2018	0/0
647	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 265.35	05/2018 -	05/2018	0/0
648	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	- -	05/2018	0/0
649	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	- -	05/2018	0/0
650	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	- -	05/2018	0/0
651	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	- -	05/2018	0/0
652	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	- -	05/2018	0/0
653	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	- 05/2018	05/2018	0/0
654	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	- -	05/2018	0/0
655	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	- -	05/2018	0/0
656	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	06/2018	0/0
657	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2018	0/0
658	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	06/2018	0/0
659	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	06/2018	0/0
660	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	06/2018	0/0
661	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	06/2018 -	06/2018	0/0
662	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	06/2018	0/0
663	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	06/2018	0/0
664	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	06/2018	0/0
665	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	06/2018	0/0
666	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	06/2018	0/0
667	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	- -	06/2018	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
668	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	- -	06/2018	0/0
669	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
670	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
671	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	- -	07/2018	0/0
672	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	- -	07/2018	0/0
673	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	- -	07/2018	0/0
674	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	- -	08/2018	0/0
675	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	- -	08/2018	0/0
676	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	- -	08/2018	0/0
677	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	- -	10/2018	0/0
678	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	- -	11/2018	0/0
679	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	- -	11/2018	0/0
680	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	- -	11/2018	0/0
681	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	- -	11/2018	0/0
682	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	- -	11/2018	0/0
683	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
684	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
685	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
686	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	- -	01/2019	0/0
687	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	- -	01/2019	0/0
688	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	- -	01/2019	0/0
689	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	- -	03/2019	0/0
690	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	- -	03/2019	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
691	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
692	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	- -	03/2019	0/0
693	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	- -	04/2019	0/0
694	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
695	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	- -	04/2019	0/0
696	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	- -	05/2019	0/0
697	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH	01/2016	701.12 -	- -	05/2019	0/0
698	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	- -	05/2019	0/0
699	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
700	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	- -	06/2019	0/0
701	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	06/2019	0/0
702	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]NHAI,RAJASTHAN	06/2016	725.95 -	06/2019 -	06/2019	0/0
703	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
704	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
705	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	-	0/0
706	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
707	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
708	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
709	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.31	- 03/2013	-	0/0
710	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
711	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
712	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
713	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0

Details of All Central Sector Infrastructure Projects having Without Milestones w.r.t. Original Schedule

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
714	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
715	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69(280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
716	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
717	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
718	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
719	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
720	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
721	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
722	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
723	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
724	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
725	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
726	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
727	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
728	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
729	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
730	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
731	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
732	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
733	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 268.92	08/2015 -	-	0/0
734	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
735	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
736	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWADI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	- -	0/0
737	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	- -	0/0
738	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	- -	0/0
739	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	- -	0/0
740	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	- -	0/0
741	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	- -	0/0
742	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	- -	0/0
743	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	- -	0/0
744	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	- -	0/0
745	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	- -	0/0
746	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	- -	0/0
747	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	- -	0/0
748	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	- -	0/0
749	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	- -	0/0
750	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	- -	0/0
751	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	- -	0/0
752	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	- -	0/0
753	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	- -	0/0
754	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	- -	0/0
755	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	- -	0/0
756	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	- -	- -	0/0
757	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	- -	0/0
758	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	- -	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
759	FOUR LANE OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-	0/0
760	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
761	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH, GOA	12/2015	773.98 -	- -	-	0/0
762	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH, GOA	12/2015	819.95 -	- -	-	0/0
763	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH, BIHAR	01/1991	478.35 -	- -	-	0/0
764	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD, PUNJAB	06/2015	892.17 -	- -	-	0/0
765	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD, PUNJAB	06/2015	899.21 -	- -	-	0/0
766	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
767	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH, UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
768	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40 - [N24000530]PWD, BIHAR	01/1991	154.62 -	- -	-	0/0
769	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD, BIHAR	01/1991	319.68 -	- -	-	0/0
770	MEERUT-BULANDSHAHAR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
771	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	- -	-	0/0
772	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
773	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
774	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-	0/0
775	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	- -	-	0/0
776	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI, KARNATAKA	03/2016	701.40 -	- -	-	0/0
777	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	- -	-	0/0
778	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	- -	-	0/0
779	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
780	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
781	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
782	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0
783	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
784	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0
785	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-	0/0
786	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-	0/0
787	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-	0/0
788	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
789	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-	0/0
790	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
791	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
792	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
793	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
794	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
795	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
796	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	- -	-	0/0
797	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	- -	-	0/0
798	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	-	0/0
799	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE- IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	- -	-	0/0
800	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	- -	-	0/0
801	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	- -	-	0/0
802	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
803	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
804	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above				(January 2017)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
805	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL PRADESH - [N24000618]NHAI,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
806	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	- -	-	0/0
807	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	- -	-	0/0
808	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
809	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	- -	-	0/0
810	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
811	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
812	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	- -	-	0/0
813	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
814	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
815	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	- -	-	0/0
816	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	- -	-	0/0
817	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
818	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
819	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
820	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-	0/0
821	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
822	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
823	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
824	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
825	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	- -	-	0/0
826	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	12/2016	0/0
827	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
828	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-	0/0
	Total		2,67,636.65 -			0/0
	<u>SHIPPING AND PORTS</u>					
829	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	03/2006 03/2016	12/2016	0/0
830	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068]KPL, TAMIL NADU	09/2015	210.00 -	01/2018 -	01/2018	0/0
831	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA	01/2007	366.39 669.46	12/2010 12/2018	12/2018	0/0
832	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
833	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	04/2009 -	-	0/0
	Total		3,399.46 -			0/0
	<u>TELECOMMUNICATIONS</u>					
834	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL, DELHI	06/2016	418.26 -	06/2017 -	06/2017	0/0
835	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	07/2015 09/2017	09/2017	0/0
	Total		13,752.26 -			0/0
	<u>URBAN DEVELOPMENT</u>					
836	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	12/2015	0/0
837	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI	09/2011	38,585.00 -	03/2016 -	12/2016	0/0
838	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	12/2015 12/2016	06/2017	0/0
839	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	09/2016 01/2017	06/2017	0/0
840	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL, KERALA	07/2012	5,181.79 -	07/2017 -	06/2017	0/0
841	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN - [N28000091]CPWD, RAJASTHAN	08/2014	350.02 479.87	03/2015 03/2017	07/2017	0/0
842	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD, KERALA	07/2015	154.00 -	11/2015 -	11/2017	0/0
843	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD, HIMACHAL PRADESH	11/2012	270.83 270.83	11/2014 05/2017	12/2017	0/0

**Details of All Central Sector Infrastructure Projects having Without Milestones
w.r.t. Original Schedule**

Costing Rs. 150 crore & above (January 2017)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
844	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	03/2016 12/2017	12/2017	0/0
845	CONSTRUCTION OC 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]MEGA,MADHYA PRADESH	05/2011	164.00 -	01/2018 -	01/2018	0/0
846	CONSTRUCTION OF 1003 NOS (900 NOS TYPE II 54 NOS TYPE III 33 NOS TYPE IV 16 NOS TYPE V) FAMILY QUAR - [N28000096]CPWD,MADHYA PRADESH	05/2016	164.30 -	01/2018 -	01/2018	0/0
847	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	03/2018	0/0
848	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
849	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
850	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	10/2019 -	03/2020	0/0
851	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	08/2014 -	-	0/0
852	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 IN - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	Total		1,13,132.41 -			0/0
	Grand Total		9,32,702.02			0/0

**List of All Central Sector Infrastructure Projects having Ahead of Schedule
w.r.t. Latest Schedule**

Annexure - XI

Costing Rs. 150 crore & above						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 486.57	486.57	250.31	03/2012 03/2018	03/2017
	Total		259.40 -	486.57	250.31		
	<u>POWER</u>						
2	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	686.90	11/2017 -	04/2017
	Total		972.42 -	972.42	686.90		
	<u>URBAN DEVELOPMENT</u>						
3	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	06/2017
	Total		5,181.79 -	5,181.79	.00		
	<u>PETROLEUM</u>						
4	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	36.47	07/2018 11/2019	08/2019
	Total		690.00 -	690.00	36.47		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
5	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]	6/2016	667.00 -	667.00	21.92	07/2018 -	06/2018
	Total		667.00 -	667.00	21.92		
	<u>POWER</u>						
6	TRANSMISSION SYSTEM ASSOCIATED WITH DARLIPALLI TPS [N18000211]	1/2016	187.04 -	187.04	20.80	06/2018 -	09/2017
	Total		187.04 -	187.04	20.80		

**List of All Central Sector Infrastructure Projects having Ahead of Schedule
w.r.t. Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
7	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 247.52	247.52	-	02/2019 -	12/2018
8	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT) - [N16000217]	6/2012	150.00	150.00	140.02	07/2014 09/2017	01/2017
9	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	21.71	05/2019 -	12/2018
10	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	8.43	08/2019 -	12/2018
	Total		1,176.52 -	1,176.52	170.16		
	Grand Total		9,134.17	9,361.34	1,186.56		

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Annexure - XII

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.59	53.25	03/2015 03/2020	03/2020
2	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	203.87	03/2022 -	03/2022
3	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	5.70	03/2023 03/2023	03/2023
4	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	-	03/2022 -	03/2022
5	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	-	03/2023 -	03/2023
6	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	-	03/2021 -	03/2021
7	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	6.68	03/2022 -	03/2022
8	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	45.26	04/2017 -	04/2017
9	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	94.56	03/2020 -	03/2020
10	GOKUL - [N06000120]	11/2014	267.67 -	267.67	179.27	03/2018 -	03/2018
11	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	114.50	03/2021 -	03/2021
12	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	290.81	03/2020 -	03/2020
13	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	338.01	03/2021 -	03/2021
14	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
15	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	2.03	03/2019 -	03/2019
16	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	637.53	03/2026 -	03/2026
17	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	19.07	03/2019 -	03/2019
18	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]	4/2012	364.75 -	364.75	252.03	10/2014 06/2017	06/2017
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	111.09	03/2020 -	03/2020
20	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	3,328.28	12/2015 04/2018	04/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [N060100093]	6/2010	11,816.40 -	11,816.40	2,158.41	03/2023 -	03/2023
22	PENGANGA OCP(REVISED) - [N060000066]	9/2014	441.82 -	441.82	160.89	03/2020 -	03/2020
23	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	63.42	03/2021 -	03/2021
24	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	68.09	03/2020 -	03/2020
25	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	397.09	2.40	03/2019 -	03/2019
26	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	87.32	03/2019 -	03/2019
27	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	28.88	03/2021 -	03/2021
28	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	112.25	03/2021 -	03/2021
29	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	42.57	03/2018 -	03/2018
30	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
31	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	71.66	03/2023 -	03/2023
32	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	112.48	03/2019 -	03/2019
33	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	16.97	03/2019 -	03/2019
34	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	108.75	03/2021 -	03/2021
35	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
36	KOYAGUDEM OPENCAST PROJECT - [N06000146]	10/2015	426.79 -	426.79	-	03/2018 -	03/2018
37	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	75.10	12/2019 -	12/2019
38	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	2.57	09/2019 -	09/2019
39	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	377.37	03/2018 -	03/2018
40	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	929.15	03/2023 03/2023	03/2023
41	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	-	03/2023 -	03/2023
42	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	18.31	03/2020 -	03/2020

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
43	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
44	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
45	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	88.50	03/2025 -	03/2025
46	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.36	03/2021 -	03/2021
47	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.00	795.95	11/2021 -	11/2021
48	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	5/2016	687.28 -	687.28	91.73	06/2017 -	06/2017
49	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	10.87	03/2020 -	03/2020
50	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
51	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	156.53	06/2015 08/2019	08/2019
52	RAMPUR BATURA OCP (4.0 MTY) - [N06000049]	8/2015	1,186.64 -	1,186.64	26.79	03/2023 -	03/2023
	Total		73,191.59 -	72,749.64	11,293.26		
	DEFENCE PRODUCTION						
53	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	167.69	8.38	05/2018 -	05/2018
54	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	14.29	08/2020 -	08/2020
	Total		453.64 -	453.64	22.67		
	FERTILISERS						
55	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	209.44	79.51	11/2016 09/2017	09/2017
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]	2/2016	482.85 -	494.00	61.66	12/2017 -	12/2017
	Total		680.64 -	703.44	141.17		
	HEALTH AND FAMILY WELFARE						
57	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	505.58	140.00	03/2018 -	03/2018
58	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	152.95	9.00	02/2018 -	02/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	312.99	25.00	08/2018 -	08/2018
60	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	19.00	09/2018 -	09/2018
61	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]	10/2016	363.99 -	363.99	-	05/2018 -	05/2018
	Total		1,579.51 -	1,579.51	193.00		
	<u>MINES</u>						
62	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	.88	04/2021 -	04/2021
63	UTKAL D AND E COAL MINE PROJECT - [N10000011]	5/2016	534.00 -	534.00	34.50	01/2020 -	01/2020
	Total		6,074.00 -	6,074.00	35.38		
	<u>PETROLEUM</u>						
64	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,882.07	03/2013 03/2018	03/2018
65	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE [N16000173]	4/2013	284.82 -	284.82	7.98	04/2015 05/2017	05/2017
66	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	4,588.29	626.25	08/2018 -	08/2018
67	ENNORE TERMINAL - [N16000224]	8/2014	393.00 -	393.00	118.59	04/2018 -	04/2018
68	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	72.21	10/2018 -	10/2018
69	NEW 250 TMTA LPG PLANT AT PANAGARH - [N16000222]	8/2014	190.45 -	190.45	-	09/2017 -	09/2017
70	SIX PIPELINE REPLACEMENT PROJECT - [N16000214]	3/2009	181.02 -	173.28	108.85	01/2017 06/2017	06/2017
71	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,190.69	210.27	04/2018 04/2018	04/2018
72	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM - [N16000212]	1/2015	4,619.94 -	3,961.54	2,468.50	12/2017 03/2019	03/2019
73	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	110.36	09/2018 09/2018	09/2018
74	DIESEL HYDROTREATOR - [N16000207]	7/2015	1,031.37 -	1,031.37	144.96	01/2018 -	01/2018
75	BSVI UP GRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	8.95	12/2019 -	12/2019

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	33.30	03/2019 -	03/2019
77	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	24.54	04/2019 -	04/2019
78	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	-	11/2018 -	11/2018
79	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	128.56	06/2020 -	06/2020
80	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A - [N16000246]	5/2016	215.38 -	215.38	108.03	06/2017 06/2017	06/2017
81	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY - [N16000245]	2/2016	931.00 -	931.00	63.30	07/2017 02/2018	02/2018
82	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	48.72	11/2019 -	11/2019
83	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242]	11/2016	230.00 -	230.00	.53	01/2019 -	01/2019
84	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]	11/2015	390.52 -	390.52	-	03/2019 -	03/2019
85	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	658.62	-	03/2023 -	03/2023
86	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION(GUJARAT,RAJASTH - [N16000238]	9/2016	1,879.00 -	1,879.00	9.94	03/2020 -	03/2020
87	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	3.42	09/2019 -	09/2019
88	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	-	07/2020 -	07/2020
89	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	678.00	5.01	02/2017 -	02/2017
90	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]	4/2016	327.78 -	327.78	2.40	04/2018 -	04/2018
91	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]	7/2014	199.95 -	199.95	84.91	03/2018 -	03/2018
92	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	1,427.94	105.76	12/2018 -	12/2018
93	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	1,200.00	830.93	03/2015 05/2017	05/2017
94	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	375.76	12/2014 03/2018	03/2018
95	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	1,869.67	05/2014 12/2017	12/2017

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
96	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,130.70	03/2015 03/2018	03/2018
97	DE-BOTTLENECKING OF SMPL - [N16000089]	12/2009	1,584.00 -	1,584.00	1,554.08	03/2017 -	03/2017
98	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,057.18	05/2013 05/2017	05/2017
99	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	341.70	2.95	01/2014 11/2019	11/2019
100	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	7/2009	3,957.00 -	3,397.00	456.75	01/2013 12/2018	12/2018
101	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	306.51	02/2020 -	02/2020
102	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	325.80	03/2013 01/2017	01/2017
103	50 MW 10 PERCENT WIND ENERGY POWER PROJECT - [N16000208]	11/2015	500.00 -	435.00	57.81	03/2017 -	03/2017
104	CONSTRUCTION OF 6 ETPS - [N16000117]	3/2009	317.64 -	240.95	159.43	09/2012 03/2017	03/2017
105	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	-	03/2019 05/2020	05/2020
106	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,098.43	1,237.43	05/2017 -	05/2017
107	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 -	1,881.22	-	11/2019 -	11/2019
108	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY - [N16000201]	3/2014	238.50 -	238.50	111.81	03/2017 10/2017	10/2017
109	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	6,086.08	1,763.35	05/2019 05/2019	05/2019
110	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	6,068.80	2,765.05	04/2019 03/2019	03/2019
111	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	5,088.83	05/2017 05/2018	05/2018
112	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	515.65	09/2017 12/2018	12/2018
113	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	892.55	09/2017 06/2018	06/2018
114	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,259.49	2,122.24	04/2016 12/2017	12/2017
115	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	144.74	10/2017 08/2018	08/2018
116	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	99.51	07/2016 06/2018	06/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
117	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	671.29	04/2015 03/2017	03/2017
118	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) [N16000084]	6/2007	736.65 -	736.65	533.16	09/2011 06/2017	06/2017
	Total		1,38,823.59 -	1,38,171.88	30,450.59		
	POWER						
119	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	6,888.00	09/2017 -	09/2017
120	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	1,668.70	05/2018 -	05/2018
121	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	93.30	07/2017 -	07/2017
122	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	1/2015	871.62 -	871.62	94.10	10/2017 -	10/2017
123	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	1/2015	268.80 -	268.80	103.30	03/2018 -	03/2018
124	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) [N18000179]	12/2014	6,517.36 -	6,517.36	1,688.20	04/2018 -	04/2018
125	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	234.00	09/2019 -	09/2019
126	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	3,934.00	02/2019 02/2020	02/2020
127	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	4,863.00	08/2018 -	08/2018
128	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	2,172.00	03/2019 -	03/2019
129	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	1,880.00	12/2016 03/2017	03/2017
130	TRANSMISSION SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
131	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	998.10	03/2018 -	03/2018
132	TRANSMISSION SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC [N18000167]	6/2014	400.47 -	400.47	232.10	04/2017 -	04/2017
133	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	1/2008	4,375.35 -	6,749.18	6,405.00	09/2011 06/2017	06/2017
134	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,053.00	03/2013 06/2019	06/2019

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
135	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	146.00	08/2017 -	08/2017
136	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	7,539.00	06/2017 09/2017	09/2017
137	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	7,337.00	11/2016 08/2017	08/2017
138	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	12,777.00	01/2017 07/2017	07/2017
139	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	7/1998	368.72 -	1,352.53	1,137.81	07/2006 09/2017	09/2017
140	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	12,694.00	01/2011 05/2018	05/2018
141	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,337.76	1,341.09	08/2013 05/2017	05/2017
142	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	7/2006	1,657.00 -	2,978.86	2,068.02	02/2016 09/2019	09/2019
143	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	5,331.03	12/2009 10/2017	10/2017
144	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]	7/2015	307.18 -	307.18	73.10	11/2017 -	11/2017
145	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]	7/2015	2,247.37 -	2,247.37	129.50	07/2018 -	07/2018
146	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	04/2018 -	04/2018
147	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	1.00	07/2017 -	07/2017
148	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	1.90	05/2017 -	05/2017
149	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION [N18000186]	3/2015	550.06 -	550.06	-	03/2018 -	03/2018
150	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	26.70	03/2018 -	03/2018
151	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) [N18000235]	11/2016	330.00 -	330.00	-	11/2017 -	11/2017
152	KANDORNA AND BHANWAD WIND FARM - [N18000234]	11/2016	415.49 -	415.49	24.00	03/2017 -	03/2017
153	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	-	03/2019 -	03/2019
154	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	1.00	02/2019 -	02/2019

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
155	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	.30	02/2019 -	02/2019
156	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	5.90	03/2019 -	03/2019
157	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]	7/2016	150.99 -	150.99	-	07/2018 -	07/2018
158	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	-	12/2018 -	12/2018
159	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	16.00	01/2019 -	01/2019
160	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	1,892.86	10/2017 -	10/2017
161	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	8.00	11/2018 -	11/2018
162	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	14.60	04/2019 -	04/2019
163	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS [N18000222]	4/2016	790.13 -	790.13	48.50	06/2019 -	06/2019
164	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]	4/2016	287.99 -	287.99	6.10	06/2018 -	06/2018
165	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	67.10	12/2018 -	12/2018
166	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	8.40	11/2019 -	11/2019
167	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	161.60	05/2019 -	05/2019
168	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	-	11/2018 -	11/2018
169	NORTH EASTERN REGION STRENGTHENING SCHEME IV - [N18000216]	5/2016	409.19 -	409.19	25.20	05/2018 -	05/2018
170	SRINAGAR-LEH TRANSMISSION PROJECT - [N18000215]	1/2014	1,788.41 -	1,788.41	476.46	09/2017 -	09/2017
171	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	7.10	04/2018 -	04/2018
172	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	25.80	01/2018 -	01/2018
173	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	590.00	07/2020 -	07/2020

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
174	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS - [N18000210]	1/2016	207.88 -	207.88	4.90	07/2018 -	07/2018
175	CONNECTIVITY FOR KUDANKULAM 3 AND 4 (2000MW) WITH INTERSTATE TRANSMISSION SYSTEM - [N18000209]	1/2016	162.11 -	162.11	15.10	05/2018 -	05/2018
176	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]	1/2016	1,455.47 -	1,455.47	104.80	07/2018 -	07/2018
177	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-A) - [N18000207]	1/2016	244.19 -	244.19	38.10	07/2018 -	07/2018
178	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	9,870.51	2,209.00	09/2019 -	09/2019
179	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,137.80	08/2013 12/2017	12/2017
	Total		2,05,414.11 -	2,24,757.61	1,02,798.57		
	RAILWAYS						
180	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	470.92 727.13	2,650.00	377.44	- 03/2023	03/2023
181	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) [N22000113]	4/2008	653.19 -	658.07	523.26	03/2014 03/2019	03/2019
182	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	4/2010	423.66 -	720.59	528.58	03/2017 -	03/2017
183	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	297.85 -	540.02	28.59	- 03/2022	03/2022
184	JAGGAYYAPET - MELLACHERUVU - [N22000304]	4/2007	313.24 -	554.70	461.48	01/1999 06/2017	06/2017
185	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	3/1996	495.44 -	1,781.98	557.65	03/2004 03/2020	03/2020
186	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	9/1998	247.66 -	6,093.31	1,271.49	05/2008 03/2023	03/2023
187	PIRPAINTI-BHAGALPUR - [N22000222]	4/2011	261.38 -	332.14	169.99	- 03/2019	03/2019
188	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	4/1998	271.24 -	520.00	464.49	- 12/2018	12/2018
189	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	12.23	02/2019 12/2022	12/2022
190	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	362.55	- 03/2022	03/2022
191	HAJIPUR - BACHAWARA - [N22000334]	5/2015	720.00 -	678.54	.75	- 12/2018	12/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
192	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,900.00 -	1,141.00	226.10	- 03/2020	03/2020
193	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]	4/1997	218.24 236.41	525.00	557.98	- 03/2019	03/2019
194	NANDYAL-YERRAGUNTLA(NL),SCR - [N220100192]	3/1996	155.74 164.36	966.98	924.00	02/2009 12/2017	12/2017
195	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092]	4/2008	5,300.00 -	7,986.04	2,423.55	03/2014 03/2019	03/2019
196	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	4/2004	293.74 -	229.33	141.72	12/2010 03/2017	03/2017
197	KHURDA ROAD-BOLANGIR(NL)ECOR - [N220100284]	4/1994	470.21 -	3,004.90	674.28	- 06/2021	06/2021
198	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [N220100168]	4/1995	900.05 -	1,125.89	1,035.41	12/2011 03/2020	03/2020
199	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [N220100181]	2/1997	514.68 -	2,271.50	1,040.88	- 12/2020	12/2020
200	PEN ROHA DOUBLING - [N22000254]	4/2007	98.74 -	381.39	338.87	- 03/2017	03/2017
201	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	16.01	03/2021 -	03/2021
202	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	10.00	03/2020 -	03/2020
203	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	912.00 -	637.95	-	- 03/2022	03/2022
204	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	2/2016	854.00 -	1,035.16	-	- 03/2022	03/2022
205	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	-	- 03/2023	03/2023
206	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	4,670.00 3,627.00	3,627.47	1.17	- 03/2023	03/2023
207	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,326.00 -	2,449.91	-	- 03/2023	03/2023
208	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	630.00 -	1,272.19	5.90	- 03/2022	03/2022
209	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	2,425.00	-	- 03/2024	03/2024
210	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	- 03/2024	03/2024
211	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
212	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	.12	12/2020 -	12/2020
213	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	.23	12/2020 -	12/2020

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
214	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00 -	1,750.00	-	03/2022 -	03/2022
215	AMRAVATI-NARKHER NL(CR) - [220100118	6/1994	663.01 175.30	858.23	680.93	06/1999 12/2020	12/2020
216	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	1,010.00	983.96	- 03/2017	03/2017
217	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	826.57 -	1,160.83	356.19	- 03/2020	03/2020
218	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428	10/2013	343.00 -	343.00	217.84	03/2019 -	03/2019
219	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427	12/2015	174.00 -	174.00	65.39	03/2019 -	03/2019
220	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426	12/2015	346.32 -	300.00	170.54	03/2019 -	03/2019
221	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425	5/2014	207.00 -	207.00	127.56	03/2018 -	03/2018
222	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424	1/2013	387.70 -	387.70	293.89	03/2018 -	03/2018
223	MULTI MODAL LOGISTICS PARK AT SWARUPGANJ - [N22000423	4/2012	471.82 -	471.82	18.81	03/2019 -	03/2019
224	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422	10/2013	305.00 -	305.00	168.12	03/2019 -	03/2019
225	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421	1/2011	493.17 -	493.17	358.87	03/2018 -	03/2018
226	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	9/2016	1,273.00 1,908.00	1,908.00	.20	12/2021 -	12/2021
227	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407	3/2009	1,514.45 -	1,514.45	1,024.69	03/2020 -	03/2020
228	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	.14	12/2025 -	12/2025
229	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	4,295.30	157.32	12/2026 -	12/2026
230	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405	4/2015	1,765.90 -	1,765.90	-	12/2025 -	12/2025
231	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404	4/2011	927.01 -	927.01	599.94	03/2019 -	03/2019
232	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403	4/2015	728.10 -	728.10	.34	12/2024 -	12/2024
233	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401	4/2015	750.55 -	943.60	-	12/2024 -	12/2024
234	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	4/1995	524.43 -	939.00	183.98	12/2021 -	12/2021
235	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	1/1991	763.18 -	1,428.00	480.27	12/2021 -	12/2021

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
236	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
237	RAMNA - SINGRAULI DOUBLING - [N22000417]	8/2015	2,436.21 -	2,436.21	4.01	03/2020 -	03/2020
238	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 03/2020	03/2020
239	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	.04	03/2022 03/2022	03/2022
240	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.65	558.06	12/2020 -	12/2020
241	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,183.25	652.02	12/2020 -	12/2020
242	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	942.95	722.82	03/2019 -	03/2019
243	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	513.66	03/2020 -	03/2020
244	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	960.18	580.79	03/2020 -	03/2020
245	BONDAMUNDA RANCHI DOUBLING - [N22000396]	3/2016	1,724.20 -	1,724.20	108.73	03/2021 -	03/2021
246	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	969.83	31.23	03/2020 -	03/2020
247	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	11.08	- 03/2021	03/2021
248	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	-	03/2021 -	03/2021
249	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	5.65	03/2021 -	03/2021
250	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	701.61	6.15	03/2021 -	03/2021
251	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	5.92	03/2021 -	03/2021
252	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	2.89	03/2021 -	03/2021
253	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	199.12	102.10	- 03/2019	03/2019
254	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	277.70 -	792.89	85.63	- 03/2021	03/2021
255	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	269.60	1.11	03/2017 -	03/2017
256	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	499.30 -	2,491.43	331.52	- 03/2023	03/2023
	Total		95,229.91 -	1,20,541.90	21,767.11		

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	ROAD TRANSPORT AND HIGHWAYS						
257	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305	5/2015	454.89 -	454.89	45.48	05/2018 -	05/2018
258	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319	6/2015	437.39 -	437.39	21.86	06/2018 -	06/2018
259	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310	2/2015	377.83 -	377.83	63.38	07/2017 -	07/2017
260	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320	6/2015	463.49 -	463.49	9.26	06/2018 -	06/2018
261	JODHPUR - BARMER SECTION OF PACKAGE -II - [N24000338	10/2014	206.12 -	206.12	161.60	04/2017 -	04/2017
262	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337	8/2015	538.08 -	538.08	129.39	02/2018 -	02/2018
263	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	-	02/2017 -	02/2017
264	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263	2/2015	241.61 -	241.61	46.68	02/2017 -	02/2017
265	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	1/2014	267.16 352.00	352.05	.02	11/2017 -	11/2017
266	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	1/2014	255.75 348.00	348.43	.02	09/2017 -	09/2017
267	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248	3/2015	153.21 -	153.21	-	01/2017 -	01/2017
268	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA- JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	-	02/2017 -	02/2017
269	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329	5/2014	497.89 -	497.89	128.93	04/2017 -	04/2017
270	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379	1/1991	218.63 -	218.63	106.15	10/2017 -	10/2017
271	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376	1/1991	219.40 -	219.40	-	01/2018 -	01/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
272	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373	11/2010	305.49 -	305.49	-	03/2017 -	03/2017
273	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371	10/2013	445.89 -	445.89	20.11	03/2017 -	03/2017
274	2/4 LANING OF TALCHAR -DUBARI-CHANDIKHOLE SECTION OF NH-200 FROM KM 301.89 TO KM 427.85 INCLUDING KM - [N24000366	6/2015	996.37 -	996.37	2.18	12/2017 -	12/2017
275	THIRUMAYAM - MANAMADURAI SECTION - [N24000359	7/2014	401.11 -	401.11	269.47	01/2017 -	01/2017
276	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357	9/2015	567.51 -	567.51	54.02	03/2018 -	03/2018
277	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358	10/2015	562.34 -	562.34	71.13	04/2018 -	04/2018
278	FOUR LANING OF VARANASI BYPASS - [N24000356	5/2015	261.09 -	261.09	41.87	05/2017 -	05/2017
279	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642	3/2015	226.31 226.00	226.00	69.69	10/2017 -	10/2017
280	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	2/2015	239.91 240.00	240.00	14.71	10/2017 -	10/2017
281	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640	1/2015	326.63 327.00	327.00	87.58	04/2018 -	04/2018
282	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632	9/2014	1,684.00 -	1,684.00	-	02/2017 -	02/2017
283	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433	9/2015	768.56 -	768.56	170.97	03/2018 -	03/2018
284	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430	12/2015	223.30 -	223.30	-	06/2018 -	06/2018
285	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
286	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423	10/2015	597.00 -	597.00	206.52	10/2017 -	10/2017
287	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421	3/2015	235.08 -	235.08	92.86	05/2018 -	05/2018
288	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418	10/2013	493.94 -	493.94	20.76	03/2017 -	03/2017

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
289	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]	7/2014	342.05 -	342.05	-	01/2017 -	01/2017
290	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]	1/1991	229.41 -	229.41	67.86	05/2018 -	05/2018
291	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]	11/2014	218.31 -	218.31	-	02/2018 -	02/2018
292	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
293	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - [N24000588]	6/2016	725.95 -	725.95	-	06/2019 -	06/2019
294	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
295	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]	6/2016	637.18 -	637.18	-	06/2019 -	06/2019
296	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]	1/2016	1,027.53 -	1,027.53	39.63	06/2018 -	06/2018
297	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]	1/2016	815.28 -	815.28	13.56	06/2018 -	06/2018
298	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]	12/2015	2,136.97 -	2,136.97	356.65	12/2018 -	12/2018
299	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]	12/2015	239.23 -	239.23	89.22	12/2017 -	12/2017
300	FOUR LANING OF PARWANOO - SOLAN - [N24000479]	9/2015	934.46 -	934.46	83.52	03/2018 -	03/2018
301	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]	12/2015	927.54 -	927.54	29.18	06/2018 -	06/2018
302	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]	11/2015	628.45 -	628.45	20.74	03/2018 -	03/2018
303	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]	2/2015	327.32 -	327.32	162.33	05/2017 -	05/2017
304	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
305	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]	12/2011	159.39 -	159.39	-	11/2017 -	11/2017
306	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]	3/2015	511.83 -	511.83	40.87	08/2017 -	08/2017

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
307	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]	12/2015	726.67 -	726.67	-	- 04/2018	04/2018
308	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]	7/2015	1,871.34 -	1,871.34	1,996.84	01/2018 -	01/2018
309	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]	12/2015	509.13 -	509.13	-	- 04/2018	04/2018
310	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]	1/2016	830.36 -	830.36	257.45	07/2018 -	07/2018
311	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]	12/2015	667.00 -	667.00	31.96	06/2018 -	06/2018
312	FOUR LANING OF SIMGA - SARAGAON - [N24000495]	12/2015	596.67 -	596.67	-	- 05/2018	05/2018
313	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]	12/2015	1,083.00 -	1,083.00	23.39	06/2018 -	06/2018
314	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]	9/2015	785.78 -	785.78	209.82	03/2018 -	03/2018
315	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	16.61	07/2018 -	07/2018
316	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]	9/2015	788.51 -	788.51	70.46	03/2018 -	03/2018
317	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	208.00	04/2018 -	04/2018
318	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]	9/2015	789.31 -	789.31	208.59	03/2018 -	03/2018
319	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
320	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]	9/2015	664.53 -	664.53	155.16	03/2018 -	03/2018
321	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]	6/2015	641.02 -	641.02	89.88	12/2017 -	12/2017
322	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]	5/2011	176.22 -	176.22	-	02/2018 -	02/2018
323	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]	10/2013	317.76 -	317.76	15.70	03/2017 -	03/2017
324	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]	1/1991	322.00 -	322.00	66.59	03/2018 -	03/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
325	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]	6/2015	774.57 -	774.57	6.33	03/2018 -	03/2018
326	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]	6/2015	532.49 -	532.49	166.22	05/2017 -	05/2017
327	2 LANING FROM KANUBARI TO START OF BOGIBEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	268.08	-	05/2017 -	05/2017
328	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]	11/2013	497.05 -	497.05	.54	05/2017 -	05/2017
329	PADI - DAHOD - [N24000353]	11/2014	279.14 -	279.14	157.97	05/2017 -	05/2017
330	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]	10/2014	264.72 -	264.72	175.75	04/2017 -	04/2017
331	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]	7/2015	455.60 -	455.60	141.89	07/2017 -	07/2017
332	JAISALMER - BARMER - [N24000348]	8/2015	482.27 -	482.27	159.09	02/2018 -	02/2018
333	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]	5/2015	1,387.11 -	1,387.11	414.31	11/2017 -	11/2017
334	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]	8/2015	723.54 -	723.54	483.45	02/2018 -	02/2018
335	TWO LANE WITH PAVED SHOULDERS OF CHAS - RAMGARH SECTION OF NH-23 - [N24000343]	9/2015	341.61 -	341.61	195.07	09/2017 -	09/2017
336	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]	5/2015	709.00 -	709.00	32.70	09/2017 -	09/2017
337	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]	10/2014	369.00 -	369.00	36.90	03/2018 -	03/2018
338	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	3/2015	394.00 -	394.00	80.27	06/2018 -	06/2018
339	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	49.00	10/2018 -	10/2018
340	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]	10/2015	179.82 -	179.82	31.31	01/2019 -	01/2019
341	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]	3/2015	194.11 -	194.11	43.99	05/2018 -	05/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
342	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	125.00	11/2018 -	11/2018
343	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
344	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
345	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333	12/2015	621.43 -	621.43	-	06/2018 -	06/2018
	Total		49,639.55 -	49,801.47	8,465.13		
	<u>SHIPPING AND PORTS</u>						
346	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	-	06/2017 -	06/2017
347	CONSTRUCTION OF RORO CUM GCB-II AT KAMARAJAR PORT LIMITED - [N25000068	9/2015	210.00 -	210.00	-	01/2018 -	01/2018
348	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED - [N25000067	12/2014	274.85 -	274.85	-	04/2017 -	04/2017
349	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	1/2007	366.39 -	669.46	415.01	12/2010 12/2018	12/2018
350	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	2/2015	244.50 258.00	258.33	-	12/2017 -	12/2017
	Total		1,294.68 -	1,647.79	415.01		
	<u>STEEL</u>						
351	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	146.51	12/2016 07/2017	07/2017
352	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCP - [N12000103	4/2014	151.33 -	151.33	35.73	09/2017 -	09/2017
353	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107	5/2015	189.00 -	189.00	19.75	03/2017 -	03/2017
354	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110	12/2007	200.00 -	200.00	140.40	03/2018 -	03/2018
355	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118	11/2016	262.87 -	262.87	11.13	06/2019 -	06/2019

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
356	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,500.00	349.35	12/2017 -	12/2017
357	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	1,682.85	39.27	09/2018 -	09/2018
358	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	15.17	06/2020 -	06/2020
359	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]	2/2014	4,749.00 -	4,749.00	24.02	09/2017 -	09/2017
360	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	466.13	04/2018 -	04/2018
361	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	115.57	03/2018 -	03/2018
362	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	10,986.26	05/2015 12/2017	12/2017
363	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]	4/2013	170.00 -	170.00	93.66	04/2018 -	04/2018
	Total		30,164.03 -	29,837.25	12,442.95		
	TELECOMMUNICATIONS						
364	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	5,231.54	07/2015 09/2017	09/2017
365	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]	6/2016	418.26 -	418.26	-	06/2017 -	06/2017
	Total		13,752.26 -	13,752.26	5,231.54		
	URBAN DEVELOPMENT						
366	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI(MOD - [N28000087]	6/2015	197.33 -	197.33	2.39	- 04/2019	04/2019
367	CONSTRUCTION OF 1003 NOS (900 NOS TYPE II 54 NOS TYPE III 33 NOS TYPE IV 16 NOS TYPE V) FAMILY QUAR - [N28000096]	5/2016	164.30 -	164.30	9.13	01/2018 -	01/2018
368	CONSTRUCTION OC 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE 3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	5/2011	164.00 -	164.00	13.97	01/2018 -	01/2018
369	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	1,933.60	03/2019 -	03/2019
370	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA [N28000068]	2/2011	241.33 -	349.33	159.77	03/2016 12/2017	12/2017
371	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	1,188.76	03/2018 -	03/2018

**List of All Central Sector Infrastructure Projects having on schedule w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above,						(January 2017)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
372	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,118.00	2,087.10	11/2019 -	11/2019
373	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]	5/2012	405.01 -	405.01	-	12/2014 03/2017	03/2017
374	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]	1/2010	165.23 -	165.23	36.54	10/2012 04/2017	04/2017
375	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]	9/2012	171.86 -	171.86	32.86	03/2016 02/2018	02/2018
376	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	178.88	05/2017 08/2017	08/2017
	Total		21,769.06 -	21,731.06	5,643.00		
	Grand Total		6,38,066.57	6,81,801.45	1,98,899.38		

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Annexure - XIII

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,000.00	09/2010 -	10/2017	71.82
2	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	22,462.00	12/2008 -	02/2017	70.54
	Total		16,663.00 -	28,462.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050	01/2009	309.46 -	553.53	01/2011 -	12/2017	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS [N04000071	10/2012	217.60 -	244.10	03/2015 -	03/2015	12.18
	Total		841.67 -	1,238.96			
	<u>COAL</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.53 -	479.63	03/2013 -	03/2019	.02
8	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	486.27	03/2016 -	03/2018	12.97
	Total		1,328.95 -	1,455.52			
	<u>HEALTH AND FAMILY WELFARE</u>						
9	SAFDARJUNG HOSPITAL, NEW DELHI-REDEVELOPMENT and OTHERS-EMERGENCY BLOCK [N21000005	11/2013	196.70 -	209.00	01/2016 -	01/2016	6.25
	Total		196.70 -	209.00			
	<u>HEAVY INDUSTRY</u>						

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
11	INSTALLATION OF DIESEL HYDROTREATMENT UNIT (DHT) AND ASSOCIATED FACILITIES - [N16000205	05/2015	2,443.00 -	2,443.00	12/2017 -	12/2017	.00
12	GAMJI REDEVELOPMENT PROJECT - [N16000202	05/2015	1,671.22 -	1,881.22	11/2019 -	11/2019	12.57
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	05/2017	37.72
14	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	Total		5,209.57 -	5,731.47			
	<u>POWER</u>						
15	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2018	114.28
16	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	09/2003	6,285.33 -	17,435.15	09/2010 -	-	177.39
17	WIND POWER PROJECT AT LAKHMANA IN JAISALMER (RAJASTHAN) 50MW - [N18000203	02/2015	302.49 302.00	302.49	02/2016 -	-	.16
18	BOKARO THERMAL POWER STATION-A - [N18000199	08/2006	2,313.00 4,139.00	4,366.64	12/2011 -	02/2017	5.50
19	RAGHUNATHPUR THERMAL POWER STATION PHASE-I - [N18000202	04/2007	4,122.00 8,781.00	9,142.58	02/2011 -	03/2016	4.12
20	KISHANGANGA HEP (3X110 MW) - [N18000031	01/2009	3,642.04 -	5,783.17	01/2016 -	01/2018	58.79
	Total		20,584.45 -	45,428.78			
	<u>RAILWAYS</u>						
21	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	02/2016	131.09
22	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	36.80 274.41	614.00	- -	-	123.75
23	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	-	141.40

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
24	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	870.00	- -	-	459.31
25	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
26	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	1,542.41	- 05/2009	-	317.21
27	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
28	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	2,125.18	- -	03/2021	543.99
29	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
30	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	350.00	02/2011 -	-	277.85
31	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
32	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	01/2016	210.19
33	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	03/2019	293.06
34	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,650.00	- -	03/2023	264.45
35	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	06/2017	57.20
36	KICHHA-KHATIMA (NL) - NER - [220100317	04/2003	142.45 -	208.40	- -	-	46.30
37	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
38	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	1,202.70	02/2015 -	12/2019	556.39
39	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	340.00	03/2009 03/2009	02/2017	64.25
40	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	376.00	12/2007 03/2010	-	175.22
41	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	318.00	02/2006 -	12/2019	21.51
42	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	950.00	03/2010 -	06/2017	38.24
43	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	03/2016	60.77
44	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
45	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
46	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,825.00	03/2008 06/2008	03/2020	145.63
47	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125	04/2006	117.36 196.95	203.00	03/2011 -	01/2011	3.07
48	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	509.00	12/2012 -	03/2016	123.34
49	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	365.67	- -	-	.14
50	HANSDIHA-GODDA NL - [N22000236	04/2011	267.09 -	350.78	- -	-	31.33
51	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL [N22000241	04/2000	297.47 -	153.02	- -	-	-48.56
52	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESTALA AND CHA - [N22000242	04/2003	337.96 -	186.89	- -	-	-44.70
53	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245	04/2010	423.66 -	720.59	03/2017 -	03/2017	70.09
54	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	381.39	- -	03/2017	286.26
55	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	280.00	- -	-	191.18
56	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
57	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261	04/2012	1,054.35 -	2,200.00	- -	-	108.66
58	GUDUR-DURGARAJPATNAM - [N22000265	04/2011	283.54 -	759.41	- -	-	167.83
59	ROHTAK-MEHAM HANSI - [N22000272	04/2012	287.00 -	625.00	- -	-	117.77
60	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
61	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	337.49 -	792.01	- -	-	134.68
62	HARIDWAR-LAKSAR - [N22000289	04/2012	219.83 -	346.63	- -	-	57.68
63	CHANDIGARH-BADDI NL - [N22000296	04/2007	328.14 -	1,540.00	- -	-	369.31
64	TORANAGALLU-RANJITPURA DL - [N22000298	04/2011	146.75 -	167.50	- -	-	14.14

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
65	JAGGAYYAPET - MELLACHERUVU - [N22000304]	04/2007	313.24 -	554.70	01/1999 -	06/2017	77.08
66	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	750.00	01/1999 -	-	60.78
67	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
68	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,000.00	04/2008 12/2011	06/2018	233.33
69	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
70	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
71	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
72	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
73	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	3,010.00	12/2008 -	03/2019	310.64
74	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,004.90	- -	06/2021	539.05
75	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	9,658.00	03/2011 -	03/2020	1,227.45
76	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
77	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	436.00	03/2011 -	10/2011	156.47
78	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	780.00	- -	03/2019	290.00
79	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	2,145.00	- -	03/2020	615.00
80	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	293.74 -	229.33	12/2010 -	03/2017	-21.93
81	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
82	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
83	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	7,000.00	03/2009 -	03/2017	317.58
84	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,451.00	03/2014 -	03/2020	324.30
85	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	- -	-	27.24

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
86	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
87	KANPUR KASGANJ MATHURA(GC) NER - [220100197	03/1997	677.97 1,062.36	1,679.13	- -	12/2016	58.06
88	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	744.71 -	1,126.79	- -	02/2017	51.31
89	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	410.08 -	780.98	- -	-	90.45
90	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) [N22000114	04/2008	516.23 -	735.00	03/2014 -	-	42.38
91	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
92	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
93	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
94	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,581.53	03/2010 -	03/2017	386.62
95	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	631.78	12/2012 -	-	107.82
96	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	370.00	02/2009 02/2009	02/2017	122.68
97	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	516.40	03/2010 -	12/2017	58.94
98	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	966.98	02/2009 -	12/2017	488.33
99	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	525.00	- -	03/2019	122.07
100	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	-	284.00
101	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
102	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
103	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	11/2015	155.02
104	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	-	72.62
105	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
106	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	712.82	- -	-	612.82
107	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
108	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,579.27	- -	03/2021	132.50
109	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	- -	03/2020	52.77
110	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	07/2015	42.11
111	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
112	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]	04/2011	190.10 -	355.96	- -	03/2019	87.25
113	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
114	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]	04/2010	203.40 -	273.84	- -	-	34.63
115	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	620.00	- -	09/2019	3.33
116	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,010.00	- -	03/2017	711.70
117	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.23	06/1999 -	12/2020	389.58
118	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
119	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
120	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	431.00	- -	-	75.15
121	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	- -	03/2020	72.01
122	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	- -	12/2020	71.11
123	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	845.68	- -	-	92.25
124	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	399.63	- -	03/2019	24.63
125	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	1,037.15	- -	03/2019	132.54
126	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]	04/2010	279.40 -	355.00	- -	09/2015	27.06
127	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
128	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
129	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	276.89	- -	-	16.87
130	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	860.00	- -	12/2018	88.60
131	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	03/2017	17.92
132	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]	04/2011	239.73 -	257.78	- -	-	7.53
133	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	272.99	- -	-	27.93
134	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	369.08	- -	-	27.72
135	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	293.68	- -	-	21.31
136	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
137	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
138	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	-	82.25
139	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
140	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
141	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	171.02 -	235.00	06/2013 -	12/2016	37.41
142	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	-	88.40
143	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
144	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
145	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
146	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
147	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
148	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
149	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	12/2018	91.71

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
150	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,480.83	- -	03/2018	80.06
151	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
152	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62
153	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,857.00	03/2007 -	03/2016	107.49
154	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	445.00	- -	03/2018	112.14
155	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	330.00	- -	03/2018	16.38
156	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	342.85	- -	-	78.83
157	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	- -	03/2021	46.95
158	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	- -	-	94.45
159	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25
160	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	- -	03/2019	171.38
161	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
162	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	508.00	- -	03/2019	62.76
163	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	- -	03/2019	62.12
164	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2017	29.06
165	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	160.97	- -	-	-7.79
166	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	- -	03/2023	5.33
167	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	- -	03/2023	10.94
168	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	- -	03/2022	21.21
169	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
170	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS - [N22000386]	04/2003	4,300.00 -	4,520.00	- -	05/2015	5.12

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
171	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	- -	-	10.01
172	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
173	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2021	79.05
174	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	943.60	12/2024 -	12/2024	25.72
175	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	-	130.97
	Total		81,661.69 -	2,10,422.08			
	ROAD TRANSPORT AND HIGHWAYS						
176	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	02/2017	28.93
177	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2017	92.75
178	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	02/2017	80.68
179	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	03/2017	68.99
180	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50
181	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]	01/2014	361.30 -	207.40	07/2014 -	-	-42.60
182	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	05/2017	2.29
183	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	03/2017	114.56
184	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	03/2017	2.65
185	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	02/2017	6.02
186	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
187	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	09/2017	.12

**List of All Central Sector Infrastructure Projects having cost overrun w.r.t. to
Revised schedule**

Costing Rs. 150 crore & above					(January 2017)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
188	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	11/2017	.01
189	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
190	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	09/2010	93.27
191	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	03/2017	51.83
	Total		7,656.06 -	11,935.63			
	<u>SHIPPING AND PORTS</u>						
192	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2016	300.00
193	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - [N25000065	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20
194	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	.13
195	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	409.83	04/2009 -	-	66.82
	Total		839.11 -	1,503.31			
	<u>STEEL</u>						
196	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	03/2016	3.96
197	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	12/2017	42.39
198	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	03/2017	1.70
	Total		1,261.61 -	1,777.68			
	Grand Total		1,37,960.81	3,11,991.73			

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Annexure-XIV

Costing Rs. 150 crore & above						(January 2017)			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	22,462.00	21,994.00	12/2008 10/2013	02/2017	98	40
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,000.00	5,356.82	09/2010 09/2016	10/2017	85	13
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	9,417.00	12/2015 11/2016	11/2019	47	36
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	7,169.00	12/2016 03/2017	12/2020	48	45
	Total		40,442.00 -	52,241.00	43,936.82				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	553.53	454.71	01/2011 -	12/2017	83	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,ANDAMAN & NICOBAR ISLANDS	10/2013	314.61 -	441.33	26.35	09/2018 -	06/2020	21	-
	Total		624.07 -	994.86	481.06				
	<u>COAL</u>								
7	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	321.95	03/2010 -	03/2017	84	-
8	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	122.29	12/2012 -	03/2017	51	-
9	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	95.92	03/2015 -	03/2017	24	-
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	176.64	03/2012 -	03/2017	60	-
11	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	45.47	06/2015 -	03/2017	21	-
12	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	269.82	101.20	04/2014 -	08/2017	40	-
13	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	135.47	05/2014 -	09/2017	40	-
14	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	90.82	03/2014 -	12/2017	45	-
15	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	125.78	03/2012 -	03/2018	72	-
16	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	198.64	03/2014 -	03/2018	48	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
17	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	166.21	03/2016 -	03/2018	24	-
18	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	153.82	03/2013 -	03/2018	60	-
19	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	148.00	03/2012 -	03/2018	72	-
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	225.57	03/2016 -	03/2018	24	-
21	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	.09	03/2015 -	03/2018	36	-
22	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	1.31	03/2015 -	03/2018	36	-
23	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	246.83	03/2015 -	03/2018	36	-
24	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	133.99	03/2016 -	03/2018	24	-
25	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	35.41	07/2016 -	03/2018	20	-
26	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	486.27	121.04	03/2016 -	03/2018	24	-
27	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10 -	490.10	221.58	03/2017 -	05/2018	14	-
28	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	269.36	03/2018 -	09/2018	6	-
29	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	310.50	03/2013 -	11/2018	68	-
31	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	185.94	03/2010 -	03/2019	108	-
32	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	215.34	03/2012 -	03/2019	84	-
33	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53 -	479.63	188.68	03/2013 -	03/2019	72	-
34	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	96.78	03/2012 -	03/2019	84	-
35	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	72.47	03/2014 -	03/2019	60	-
36	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	145.11	04/2015 -	04/2019	48	-
37	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	4.76	03/2014 -	03/2020	72	-
38	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	36.17	03/2011 -	03/2020	108	-
39	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	80.61	07/2012 03/2017	03/2021	104	48
40	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	481.31	03/2012 -	03/2023	132	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		12,181.35	12,307.92	4,967.14				
	<u>STEEL</u>								
41	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73	877.73	700.36	07/2015	02/2017	19	-
42	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00	280.00	95.81	09/2016	03/2017	6	-
43	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	175.94	179.14	12/2015	03/2017	15	-
44	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	227.00	203.43	12/2016	03/2017	3	-
45	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00	956.00	657.66	03/2015	03/2017	24	-
46	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76	974.76	451.53	07/2016	05/2017	10	-
47	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16	404.16	380.93	07/2015	05/2017	22	-
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00	17,265.00	17,033.59	03/2013	06/2017	51	-
49	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67	245.67	182.95	05/2016	10/2017	17	-
50	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00	488.40	142.68	10/2016	12/2017	14	-
51	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18	1,154.18	221.73	12/2017	05/2018	5	-
52	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01	1,034.01	116.00	10/2017	07/2018	9	-
	Total		23,886.85	24,082.85	20,365.81				
	<u>PETROLEUM</u>								
53	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 222.81	222.81	189.51	09/2016	02/2017	5	-
54	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00	586.00	529.25	08/2015	03/2017	19	-
55	RESID UPGRADEATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36	3,110.36	2,338.88	11/2015 12/2016	03/2017	16	3
56	DHDS REVAMP FOR MEETING BS-IV DIESEL QUALITY - [N16000218]CPCL,TAMIL NADU	02/2016	367.11	367.11	103.03	04/2017	05/2017	1	-
57	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96	191.96	133.65	05/2015	06/2017	25	-
58	PALAKKAD LPG PLANT - [N16000225]BPCL,KERALA	02/2015	184.00	184.00	46.02	06/2017	12/2017	6	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
59	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU	05/2015	257.87 -	257.87	88.97	11/2016 -	02/2018	15	-
60	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	318.90	10/2014 03/2017	03/2018	41	12
61	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	209.19	142.22	12/2016 -	03/2018	15	-
62	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 439.03	439.03	5.87	03/2017 -	06/2018	15	-
	Total		5,730.17 -	6,031.12	3,896.30				
	<u>POWER</u>								
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	635.96	11/2011 -	01/2017	62	-
64	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 1,428.87	1,428.87	1,092.09	08/2012 09/2016	01/2017	53	4
65	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	1,265.03	06/2015 -	01/2017	19	-
66	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	6,102.00	09/2016 01/2017	02/2017	5	1
67	BOKARO THERMAL POWER STATION-A - [N18000199]DVC,JHARKHAND	08/2006	2,313.00 4,138.41	4,366.64	3,820.69	12/2011 03/2016	02/2017	62	11
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 689.03	689.03	605.02	07/2013 11/2015	03/2017	44	16
69	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	2,281.56	09/2014 -	03/2017	30	-
70	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 1,875.13	1,875.13	1,721.72	01/2015 06/2016	03/2017	26	9
71	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	1,235.60	05/2016 -	03/2017	10	-
72	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	245.30	10/2016 -	04/2017	6	-
73	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	120.73	09/2014 -	05/2017	32	-
74	SYSTEM STRENGTHENING XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	237.09	06/2012 -	06/2017	60	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above							(January 2017)		
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
75	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51 2,619.56	2,619.56	2,525.03	07/2014 06/2016	06/2017	35	12
76	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	6,707.99	06/2015 -	06/2017	24	-
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	687.82	11/2014 -	06/2017	31	-
78	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	1,050.44	04/2016 -	06/2017	14	-
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	352.50	06/2016 -	06/2017	12	-
80	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	337.20	08/2016 -	06/2017	10	-
81	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	182.30	07/2016 -	06/2017	11	-
82	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	311.90	11/2016 -	06/2017	7	-
83	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	69.60	03/2016 -	06/2017	15	-
84	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	78.70	02/2016 -	06/2017	16	-
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	559.10	06/2016 -	09/2017	15	-
86	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	171.20	02/2017 -	09/2017	7	-
87	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 7,998.00	5,353.00	6,266.92	05/2014 03/2017	09/2017	40	6
88	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	6,117.37	12/2016 -	09/2017	9	-
89	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	634.29	09/2010 12/2016	12/2017	87	12
90	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	3,261.45	01/2015 -	12/2017	35	-
91	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,358.23	11/2012 12/2016	12/2017	61	12
92	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	475.32	06/2014 03/2016	12/2017	42	21
93	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	339.27	08/2014 06/2015	12/2017	40	30

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
94	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.71	2,228.71	1,822.73	08/2014 12/2015	12/2017	40	24
95	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	489.20	06/2015 -	12/2017	30	-
96	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	1,663.25	12/2015 -	12/2017	24	-
97	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	51.90	04/2016 -	12/2017	20	-
98	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	137.20	09/2017 -	12/2017	3	-
99	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	41.20	03/2017 -	12/2017	9	-
100	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,783.17	4,800.42	01/2016 -	01/2018	24	-
101	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,420.88	10/2012 03/2017	02/2018	64	11
102	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,431.10	12/2012 12/2016	02/2018	62	14
103	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	100.27	02/2014 -	02/2018	48	-
104	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	8,189.41	01/2018 -	06/2018	5	-
105	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	1,919.35	11/2008 12/2016	09/2018	118	21
106	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,086.47	09/2009 -	12/2018	111	-
107	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	383.60	04/2017 -	12/2018	20	-
108	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	2,491.58	1,016.89	06/2013 -	12/2019	78	-
109	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	696.27	04/2020 -	01/2023	33	-
	Total		1,08,022.57 -	1,20,636.57	85,099.56				

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	HEAVY INDUSTRY								
110	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	12/2017	75	-
	Total		1,718.00 -	3,827.30	2,289.00				
	HEALTH AND FAMILY WELFARE								
111	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	97.00	05/2017 -	06/2017	1	-
112	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	159.00	05/2017 -	06/2017	1	-
113	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	168.90	38.00	05/2017 -	07/2017	2	-
	Total		666.99 -	666.99	294.00				
	RAILWAYS								
114	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	370.00	363.32	02/2009 02/2009	02/2017	96	96
115	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	340.00	344.04	03/2009 03/2009	02/2017	95	95
116	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,581.53	690.91	03/2010 -	03/2017	84	-
117	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	7,000.00	6,630.23	03/2009 -	03/2017	96	-
118	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.20	04/2016 -	03/2017	11	-
119	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	950.00	963.74	03/2010 -	06/2017	87	-
120	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	516.40	441.77	03/2010 -	12/2017	93	-
121	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,641.30	03/2014 -	12/2017	45	-
122	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	325.99	03/2016 -	12/2017	21	-
123	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 -	5,000.00	4,464.70	04/2008 12/2011	06/2018	122	78
124	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	06/2018	27	-
125	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	19,565.00	14,922.23	11/2002 -	12/2018	193	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,619.00	685.23	03/2016 -	12/2018	33	-
127	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,010.00	2,419.18	12/2008 -	03/2019	123	-
128	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 1,319.33	1,319.33	794.39	- 12/2009	03/2019	-	111
129	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	301.64 -	1,185.64	772.88	- 09/2009	03/2019	-	114
130	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR, RAJASTHAN	04/2008	829.74 -	829.74	280.08	03/2015 -	03/2019	48	-
131	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	321.62	58.86	03/2012 -	03/2019	84	-
132	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	03/2019	12	-
133	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	386.30 1,160.54	1,776.81	1,181.00	03/1998 -	12/2019	261	-
134	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	1,202.70	294.14	02/2015 -	12/2019	58	-
135	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL, JHARKHAND	03/1997	261.70 -	318.00	299.61	02/2006 -	12/2019	166	-
136	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 4,454.18	9,658.00	5,918.56	03/2011 -	03/2020	108	-
137	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,825.00	1,154.14	03/2008 06/2008	03/2020	144	141
138	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	3,451.00	1,936.18	03/2014 -	03/2020	72	-
139	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 2,393.48	4,600.00	1,023.83	04/2014 -	03/2020	71	-
140	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	389.32	12/2015 -	03/2020	51	-
141	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	49.69	03/2013 -	03/2020	84	-
142	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	3,000.00	171.69	03/2015 -	03/2020	60	-
143	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	960.00 578.00	578.00	176.03	- 11/2015	03/2020	-	52
144	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	3,161.58	1,212.65	03/2016 -	12/2020	57	-
145	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 1,111.99	1,579.27	352.12	- 03/2020	03/2021	-	12
146	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 1,928.07	1,928.07	310.45	- 03/2021	06/2022	-	15

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
147	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
	Total		35,633.78 -	94,326.00	52,217.64				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
148	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	478.32	05/2013 -	01/2017	44	-
149	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	2,418.23	07/2013 -	01/2017	42	-
150	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	2,126.85	04/2015 -	01/2017	21	-
151	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION - [N24000239]NHAI,RAJASTHAN	01/2014	368.15 -	368.15	231.79	01/2016 -	01/2017	12	-
152	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	442.64	02/2009 -	02/2017	96	-
153	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	204.64	11/2008 -	02/2017	99	-
154	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	316.94	06/2008 06/2016	02/2017	104	8
155	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	436.38	04/2010 09/2016	02/2017	82	5
156	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	4,554.86	06/2015 -	02/2017	20	-
157	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	351.23	05/2013 -	02/2017	45	-
158	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	1,898.25	09/2015 -	02/2017	17	-
159	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	4,700.69	12/2015 -	02/2017	14	-
160	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	251.55	38.13	02/2015 -	02/2017	24	-
161	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	503.16	331.09	08/2016 -	02/2017	6	-
162	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	299.99	11/2008 -	03/2017	100	-
163	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	266.81	04/2009 -	03/2017	95	-
164	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	214.88	03/2008 10/2016	03/2017	108	5
165	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	204.93	05/2008 12/2016	03/2017	106	3
166	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	212.00	125.45	09/2007 -	03/2017	114	-
167	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	331.23	403.94	07/2009 -	03/2017	92	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
168	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	472.83	05/2010 -	03/2017	82	-
169	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 2,782.54	3,237.87	3,407.69	09/2012 -	03/2017	54	-
170	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,675.74	08/2011 -	03/2017	67	-
171	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,206.10	04/2013 -	03/2017	47	-
172	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	741.37	08/2012 -	03/2017	55	-
173	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,666.66	06/2013 -	03/2017	45	-
174	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,503.50	08/2014 -	03/2017	31	-
175	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,968.37	03/2013 -	03/2017	48	-
176	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	832.39	11/2013 -	03/2017	40	-
177	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	1,972.30	08/2013 -	03/2017	43	-
178	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	654.59	02/2014 -	03/2017	37	-
179	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	901.28	03/2014 -	03/2017	36	-
180	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	534.11	04/2014 -	03/2017	35	-
181	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	1,047.00	1,718.55	06/2014 -	03/2017	33	-
182	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	398.85	01/2014 -	03/2017	38	-
183	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	1,084.00	09/2016 -	03/2017	6	-
184	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - [N24000236]NHAI,RAJASTHAN	10/2013	677.79 -	677.79	883.59	04/2016 -	03/2017	11	-
185	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN	03/2014	240.10 -	240.10	178.69	03/2016 -	03/2017	12	-
186	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	523.85	155.59	01/2016 -	03/2017	14	-
187	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	351.34	304.01	01/2016 -	03/2017	14	-
188	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	495.78	414.93	01/2016 -	03/2017	14	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
189	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	509.86	08/2016 -	03/2017	7	-
190	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	1,232.00	1,173.20	08/2015 -	03/2017	19	-
191	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	1,601.77	1,383.55	11/2015 -	03/2017	16	-
192	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	320.00	212.33	05/2016 -	03/2017	10	-
193	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	172.00	53.85	06/2016 -	03/2017	9	-
194	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	163.00	91.92	05/2016 -	03/2017	10	-
195	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	905.31	03/2013 -	04/2017	49	-
196	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	977.69	07/2013 -	04/2017	45	-
197	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	731.90	03/2014 -	04/2017	37	-
198	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	04/2017	7	-
199	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	237.03	04/2009 -	05/2017	97	-
200	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	226.32	02/2010 -	05/2017	87	-
201	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,415.36	07/2012 -	05/2017	58	-
202	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	769.68	09/2013 -	05/2017	44	-
203	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,567.40	09/2014 -	05/2017	32	-
204	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	224.83	-	05/2015 -	05/2017	24	-
205	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	563.92	185.13	11/2016 -	05/2017	6	-
206	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	316.60	04/2008 01/2017	06/2017	110	5
207	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,131.46	05/2013 -	06/2017	49	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
208	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	717.40	01/2014 -	06/2017	41	-
209	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	552.91	11/2013 -	06/2017	43	-
210	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	875.61	08/2013 -	06/2017	46	-
211	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	2,228.56	09/2014 -	06/2017	33	-
212	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,281.38	08/2013 -	06/2017	46	-
213	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	255.60	05/2017 -	06/2017	1	-
214	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	192.00	46.64	05/2016 -	06/2017	13	-
215	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,889.98	07/2015 -	07/2017	24	-
216	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,864.02	11/2011 -	08/2017	69	-
217	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	309.01	61.94	09/2015 -	08/2017	23	-
218	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,130.00	08/2016 -	08/2017	12	-
219	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	342.00	145.03	01/2017 -	08/2017	7	-
220	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	881.43	02/2013 -	09/2017	55	-
221	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	621.88	07/2013 -	09/2017	50	-
222	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	407.21	07/2014 -	09/2017	38	-
223	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	363.06	06/2014 -	09/2017	39	-
224	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,856.83	02/2014 -	09/2017	43	-
225	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	368.73	-	09/2016 -	09/2017	12	-
226	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,064.23	10/2011 -	09/2017	71	-
227	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	1,038.84	07/2013 -	10/2017	51	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
228	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	871.49	09/2014 -	10/2017	37	-
229	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	271.45	-	10/2015 -	10/2017	24	-
230	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,251.64	03/2013 -	11/2017	56	-
231	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	165.67	-	11/2015 -	11/2017	24	-
232	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	159.12	-	11/2015 -	11/2017	24	-
233	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	405.44	11/2016 -	11/2017	12	-
234	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,284.34	06/2013 -	12/2017	54	-
235	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,328.82	12/2013 -	12/2017	48	-
236	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.46	05/2013 -	12/2017	55	-
237	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2017	52	-
238	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	623.74	10/2013 -	12/2017	50	-
239	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	1,492.40	06/2014 -	12/2017	42	-
240	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,WEST BENGAL	02/2011	580.43 -	580.43	279.95	08/2013 -	12/2017	52	-
241	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	321.08	10/2013 -	12/2017	50	-
242	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	1,479.00	690.66	06/2015 -	12/2017	30	-
243	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	278.17	02/2015 -	12/2017	34	-
244	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	182.91	10/2015 -	12/2017	26	-
245	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	972.50	1,393.23	07/2017 -	01/2018	6	-
246	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,643.50	11/2016 -	02/2018	15	-

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
247	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	998.79	1,802.57	08/2013 -	03/2018	55	-
248	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	1,170.52	2,145.48	06/2012 -	03/2018	69	-
249	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD, ODISHA	12/2011	191.08 -	191.08	-	08/2015 -	03/2018	31	-
250	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	44.40	12/2017 -	06/2018	6	-
251	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	16.61	06/2016 -	06/2018	24	-
252	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	611.65	11.60	06/2016 -	06/2018	24	-
253	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
254	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	280.36	03/2016 -	03/2019	36	-
255	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	-	12/2017 -	04/2019	16	-
	Total		85,025.35 -	89,137.26	99,159.05				
	<u>TELECOMMUNICATIONS</u>								
256	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C - [N26000102]ITI, MULTI STATE	09/2014	2,111.17 -	2,011.17	301.57	09/2014 -	03/2017	30	-
	Total		2,111.17 -	2,011.17	301.57				
	<u>URBAN DEVELOPMENT</u>								
257	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 315.00	315.00	258.64	06/2015 08/2016	03/2017	21	7
258	BANGALORE METRO RAIL PROJECT - [N28000008]JMRTD, KARNATAKA	05/2006	6,395.00 14,405.01	14,405.01	14,282.31	06/2011 12/2015	04/2017	70	16
259	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD, MADHYA PRADESH	12/2012	188.87 -	188.87	143.39	12/2015 12/2016	06/2017	18	6
260	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD, TAMIL NADU	04/2014	332.72 -	332.72	188.26	09/2016 01/2017	06/2017	9	5

**List of All Central Sector Infrastructure Projects having Time overrun w.r.t.
Latest Schedule**

Costing Rs. 150 crore & above						(January 2017)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
261	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	67.62	03/2017 -	06/2017	3	-
262	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN - [N28000091]CPWD,RAJASTHAN	08/2014	350.02 479.87	479.87	233.50	03/2015 03/2017	07/2017	28	4
263	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 170.62	170.62	139.57	03/2012 08/2016	10/2017	67	14
264	CONSTRUCTION OF CIVIL STRUCTURES AN OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AI IISER CAMUS - [N28000093]CPWD,KERALA	07/2015	154.00 -	154.00	33.07	11/2015 -	11/2017	24	-
265	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 270.83	270.83	98.76	11/2014 05/2017	12/2017	37	7
266	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	13,305.52	12/2015 -	12/2017	24	-
267	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	51.38	03/2015 10/2017	12/2017	33	2
268	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	80.60	09/2015 03/2017	03/2018	30	12
269	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	1,753.99	02/2019 -	03/2020	13	-
270	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	12.76	10/2019 -	03/2020	5	-
	Total		50,966.89 -	59,072.37	30,649.37				
	Grand Total		3,67,009.19	4,65,335.41	3,43,657.32				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11/2019	11459	47
3	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	02/2017	13171	98
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	12/2017	309.46	83

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2018	430.45	24
8	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2018	417.33	20
9	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
10	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
11	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2018	162.76	36
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2018	258.56	24
13	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
14	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84
15	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2018	510.85	24
16	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	11/2018	457.77	68
17	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2018	321.5	48
18	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	05/2018	490.1	14
19	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2019	207.28	84
20	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2019	479.53	72

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2017	209.78	24
22	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
23	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2018	198.59	24
24	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2017	181.19	60
25	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	08/2019	1458.17	50
26	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	09/2018	1055.05	6
27	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	06/2017	364.75	32
28	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	09/2017	289.45	40
29	PATHERDIH NLW WASHERY	BCCL	10/2012	04/2014	08/2017	269.82	40
30	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
31	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
32	JAGANNATHPOR OCP (3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
33	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
34	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.4	60
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2018	210.98	60
38	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
39	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2018	264.68	72
40	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
41	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2018	249.03	72
42	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	12/2017	153.82	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
44	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36
45	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
46	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	09/2017	197.79	10

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	12/2017	1718	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	BS-IV QUALITY IMPROVEMENT PROJECT (PHASE-I) AT GUJARAT REFINERY	IOCL	02/2016	07/2017	02/2018	931	7
49	PALAKKAD LPG PLANT	BPCL	02/2015	06/2017	12/2017	184	6
50	RESITING OF TINSUKIA TERMINAL PROJECT (DIGBOI MARKETING TERMINAL PROJECT)	IOCL	06/2012	07/2014	01/2017	150	30
51	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	HPCL	11/2011	03/2013	01/2017	310	46
52	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE	IOCL	08/2011	08/2015	03/2017	586	19
53	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	41
54	TWENTY NOS. FEEDER GAS LINES	OIL	03/2009	12/2016	03/2018	228.64	15
55	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	08/2019	690	13
56	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	02/2018	257.87	15
57	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY	IOCL	03/2014	03/2017	10/2017	238.5	7
58	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
59	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	03/2017	317.64	54
60	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	12/2018	3957	71

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
61	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
62	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2017	861.79	48
63	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA FORM	ONGC	01/2015	12/2017	03/2019	4619.94	15
64	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2018	2465.15	60
65	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	06/2018	352.56	15
66	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	08/2018	607.06	10
67	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	20
68	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
69	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	06/2018	3076	9
70	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
71	RESID UPGRADATION PROJECT	CPCL	03/2013	11/2015	03/2017	3110.36	16
72	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	06/2017	191.96	25
73	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	12
74	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	ONGC	09/2011	07/2016	06/2018	202.25	23
75	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	03/2017	1138.5	23
76	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	ONGC	06/2007	09/2011	06/2017	736.65	69
77	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	36
78	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	12/2017	2592.17	43
79	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	03/2018	600.17	39
80	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	05/2017	871.35	26

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
81	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	12/2017	305.04	9
82	COMMON SYS. ASSOCIATED WITH EAST	PGCIL	03/2013	12/2015	12/2017	2514.88	24

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B						
83	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	05/2017	198.63	32
84	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2017	1422.85	26
85	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	03/2017	1940.13	30
86	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657	43
87	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2017	487.49	42
88	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	06/2017	2127.51	35
89	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2017	573.99	45
90	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2017	297.33	40
91	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	40
92	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	01/2018	3642.04	24
93	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	118
94	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	88
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	PGCIL	07/2010	07/2013	03/2017	752.64	44
96	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.8	61
97	SYSTEM STRENGTHENING XII OF SR	PGCIL	02/2010	06/2012	06/2017	232.34	60
98	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	02/2018	195.42	48
99	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	09/2017	5353	40
100	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A	PGCIL	04/2015	04/2017	12/2018	1479.3	20
101	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	02/2017	2313	62
102	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2019	2491.58	78
103	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2017	2496.9	94
104	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2017	522.29	7
105	AUGMENTATION OF TRANSFORMERS IN	PGCIL	03/2014	03/2016	06/2017	155.57	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	NORTHERN REGION - PART B						
106	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	PGCIL	02/2014	10/2016	04/2017	378.71	6
107	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	75
108	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2017	4375.35	69
109	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	09/2017	288.49	7
110	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	06/2017	196.58	16
111	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	01/2023	8112.12	33
112	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	02/2020	14366.58	12
113	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
114	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
115	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	87
116	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	64
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	01/2017	509.66	62
118	TRANSMISSION SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER	PGCIL	04/2010	01/2015	12/2017	4404.57	35
119	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	11130.19	52
120	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	01/2017	1216.83	53
121	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144	62
122	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II	PGCIL	09/2013	05/2016	03/2017	1575.3	10
123	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	06/2017	1364.52	14
124	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2017	374.63	20
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	06/2017	539.82	12
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII	PGCIL	02/2014	06/2016	09/2017	908.08	15
127	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION	PGCIL	05/2014	08/2016	06/2017	829.98	10
128	INSTALLATION OF BUS RECTOR AND ICT IN	PGCIL	05/2014	07/2016	06/2017	303.07	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WESTERN REGION						
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	134
130	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	06/2017	9569.76	24
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	06/2017	723.63	31
132	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	07/2017	15166.19	6
133	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
134	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2017	514.2	30
135	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	01/2017	1909.24	19

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
136	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	03/2019	528.57	12
137	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.9	93
138	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	12/2020	3951.98	57
139	NANDYAL-YERRAGUNTALA(NL),SCR	SCR	03/1996	02/2009	12/2017	155.74	106
140	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
141	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	12/2017	1389.62	45
142	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
143	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
144	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2019	829.74	48
145	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	12/2020	663.01	258
146	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	58
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	02/2017	133.41	95
148	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2019	261.7	166
149	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.2	87

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
151	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	12/2018	2913.51	33
153	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
154	PANDABESWAR-CHINPAI DOUBLING (ER)	ER	04/2004	12/2010	03/2017	293.74	75
155	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
156	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	MRTPT	04/2008	03/2014	03/2019	5300	60
157	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2017	1676.31	96
158	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
159	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
160	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	NR	03/1995	11/2002	12/2018	2500	193
161	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
162	RAJATGARH-BARANG(LD),ECOR	RVNL	04/1999	02/2009	02/2017	166.16	96
163	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	221
164	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTPT	03/1996	03/2004	03/2020	495.44	192
165	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
166	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500	122
167	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
168	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
169	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
170	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	MRTPT	03/2013	03/2016	06/2018	4874.58	27
171	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
172	DHOLPUR-SIRMUTTRA WITH EXTENSION TO	NCR	04/2010	02/2019	12/2022	622.41	46

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR						
173	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
174	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	21

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
175	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	MORTH	03/2014	05/2016	03/2017	162.51	10
176	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
177	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	NHAI	02/2013	08/2015	03/2017	1232	19
178	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	08/2017	1655.01	12
179	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	09/2017	1673.7	71
180	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	03/2017	1055	16
181	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	02/2017	280	96
182	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2017	199.81	97
183	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	03/2017	167.64	100
184	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	02/2017	155.04	99
185	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	03/2017	200	95
186	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	03/2017	160	106
187	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	03/2017	574	36
188	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	06/2017	500.29	46
189	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2017	1410	33
190	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	05/2017	1046	44
191	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	11/2017	754	56
192	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	06/2017	1078.84	46
193	4-LANING OF BRAHMAPORE-FARAKA	NHAI	02/2011	08/2013	03/2018	998.79	55

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	12/2017	580.43	52
195	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2017	1047	33
196	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	PWD	07/2014	02/2015	02/2017	251.55	24
197	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	PWD	02/2015	05/2015	05/2017	224.83	24
198	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	PWD	03/2015	09/2015	08/2017	309.01	23
199	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	PWD	03/2015	10/2015	10/2017	271.45	24
200	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	MORTH	03/2015	11/2015	11/2017	165.67	24
201	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	MORTH	03/2015	11/2015	11/2017	159.12	24
202	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	PWD	12/2011	08/2015	03/2018	191.08	31
203	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34
204	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	03/2017	2498.76	31
205	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	07/2017	1987	24
206	NASHRI- CHANANI	NHAI	05/2011	06/2015	02/2017	2159	20
207	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	01/2017	1813.76	42
208	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	09/2017	671.3	55
209	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	02/2017	351.54	45
210	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2017	374	55
211	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2017	485	52
212	JORBAT - BARAPANI	NHAI	01/2011	01/2014	06/2017	536	41
213	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	03/2017	664	37
214	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	09/2017	575	50
215	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	06/2017	511.54	43
216	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2017	1100.7	42

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
217	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	09/2017	702.16	38
218	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2017	1479	30
219	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	03/2017	486	82
220	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	08/2017	1108	69
221	DEOLI-KOTA	NHAI	01/2011	07/2013	10/2017	593	51
222	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	10/2017	828	37
223	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	09/2017	1348.2	43
224	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	03/2017	617	55
225	MURADABAD-BAREILY	NHAI	04/2010	06/2013	03/2017	1267	45
226	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	03/2017	1724.55	48
227	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	01/2017	325	44
228	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	04/2017	852	49
229	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	06/2017	1585	49
230	4-LANING OF ROHATAK JIND(LENGTH 45 KM)	NHAI	10/2013	10/2015	12/2017	283.25	26
231	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	02/2018	1916.79	15
232	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	03/2017	1266.6	6
233	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	03/2017	1509.1	54
234	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	03/2017	1175	47
235	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	03/2005	07/2012	05/2017	940	58
236	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	03/2017	1693.75	67
237	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA	NHAI	10/2013	04/2016	03/2017	677.79	11
238	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	12/2017	1008.5	54
239	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2017	650	40

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
240	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	03/2017	1141	43
241	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2017	1250	48
242	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	04/2017	953.88	45
243	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2017	571	50
244	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
245	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2017	1396.18	32
246	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	03/2017	291.36	38
247	ETAWAH CHAKERI	NHAI	03/2013	09/2015	02/2017	1573	17
248	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	12/2015	02/2017	2125.24	14
249	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	01/2017	1928.22	21
250	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	03/2017	530.07	7
251	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	07/2017	01/2018	972.5	6
252	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	NHAI	06/2014	11/2016	11/2017	923.04	12
253	HARANGAJO TO MAIBANG, KM 164.08- 190.587 NH-54	NHAI	12/2003	09/2007	03/2017	212	114
254	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2017	196	92
255	WIDENING AND STRENGTHENING TO 2-LANE WITH PS OF NIMBI JODHA-DEGANA-MERTA CITY SECTION	NHAI	01/2014	01/2016	01/2017	368.15	12
256	2-LANING WITH PS BHILWARA-LODPURA SECTION	NHAI	03/2014	03/2016	03/2017	240.1	12
257	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2017	375.09	35
258	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2017	478.51	50
259	PANVEL-INDAPUR	NHAI	12/2011	06/2014	09/2017	942.69	39
260	JALANDHAR - AMRITSAR	NHAI	01/2014	01/2016	03/2017	523.85	14
261	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2018	563.92	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
262	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	01/2016	03/2017	351.34	14
263	VADODARA-SURAT SECTION	NHAI	03/2014	08/2016	02/2017	503.16	6
264	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	NHAI	09/2015	09/2016	09/2017	368.73	12
265	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI	NHAI	04/2014	01/2016	03/2017	495.78	14
266	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	NHAI	11/2014	11/2016	05/2017	563.92	6
267	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	06/2018	602.95	24
268	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	06/2016	06/2018	611.65	24
269	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	03/2017	245	108
270	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	02/2017	217.61	82
271	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	06/2017	208	110
272	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	02/2017	225	104
273	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	05/2017	275	87
274	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	04/2017	425.19	7
275	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
276	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	06/2012	03/2018	1170.52	69
277	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	MORTH	08/2013	06/2016	03/2017	171.96	9
278	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	MORTH	07/2014	01/2017	08/2017	342.05	7
279	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	MORTH	12/2013	05/2016	03/2017	319.8	10
280	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	MORTH	03/2014	05/2016	06/2017	191.5	13

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
281	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
282	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HACL	03/2007	12/2015	03/2017	149.73	15
283	REBUILDING OF COB-7 AT BSL	SAIL	10/2013	05/2016	10/2017	245.67	17
284	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	HACL	10/2011	12/2016	07/2017	175.49	7
285	IRRIGATION WORK OF BAGMATI	HACL	10/2005	03/2015	03/2017	956	24
286	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	06/2017	17265	51
287	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2017	15525	31
288	3RD CONVERTER AND 4TH CASTER	RINL	07/2011	07/2016	05/2017	974.76	10
289	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	02/2017	877.73	19
290	TURBO BLOWER - 5	RINL	12/2009	09/2016	03/2017	280	6
291	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	12/2017	343	14
292	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	07/2018	1034.01	9
293	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	05/2017	404.16	22

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
294	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	09/2017	13334	26
295	NETWORK FOR SPECTRUM (NFS) OFC LAYING PROJECT, PACKAGE F AND G, A PART OF INTELLIGENT FIBER OPTIC C	ITI	09/2014	09/2014	03/2017	2111.17	30

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
296	CONSTRUCTION OF CIVIL STRUCTURES AND OTHER INFRASTRUCTURE FACILITIES FOR ACADEMIC AREA AT IISER CAMUS	CPWD	07/2015	11/2015	11/2017	154	24
297	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2017	14600	24
298	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	03/2017	405.01	27
299	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	04/2017	165.23	54
300	CONSTRUCTION OF NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA	CPWD	12/2012	06/2015	03/2017	315	21
301	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	10/2017	205	67

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
302	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	21
303	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	02/2018	171.86	23
304	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	07/2017	350.02	28
305	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	12/2017	216.69	33
306	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	04/2017	6395	70
307	BANGALORE METRO RAIL PROJECT PHASE-2	BM RCL	02/2014	02/2019	03/2020	26405.14	13
308	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2015	06/2017	188.87	18
309	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	06/2017	332.72	9
310	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	03/2018	156.57	30
311	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	12/2017	270.83	37

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(JANUARY 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6000	2508
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	22462	9291

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.59	307.16
6	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
8	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9965	4504.39

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
10	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
11	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	4124.35	4259.49	135.14
12	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
14	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	N.A.	913	1330	417
15	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	768.25	102.25

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
16	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
18	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	341.7	138.76
19	GAMJI REDEVELOPMENT PROJECT	ONGC	05/2015	11/2019	1671.22	1881.22	210
20	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
22	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	17435.15	11149.82
24	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
25	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
26	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
27	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1352.53	983.81
28	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	1422.85	1875.13	452.28
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
31	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5783.17	2141.13
32	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.71	482.06
33	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1337.76	763.77
34	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	2127.51	2619.56	492.05
35	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
36	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
37	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
38	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	2978.86	1321.86
39	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
40	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	DVC	04/2007	02/2011	4122	9142.58	5020.58
41	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	2313	4366.64	2053.64
42	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
43	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83
44	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
45	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	1961.87	2310.58	348.71
46	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	1216.83	1428.87	212.04

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
47	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
48	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	N.A.	36.8	614	577.2
49	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
50	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	870	714.45
51	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
52	GULBARGA-BIDAR, SCR(NL)	SCR	02/1998	N.A.	242.42	1542.41	1299.99
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
54	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	950	262.8
55	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	04/2003	12/2007	136.62	376	239.38
56	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	N.A.	810.78	1928.07	1117.29
57	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	340	206.59
58	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
59	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
60	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
61	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
62	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	N.A.	470.92	2650	2179.08
63	KALYAN-KASARA 3RD LINE	CR	04/2011	N.A.	277.7	792.89	515.19
64	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2491.43	1992.13
65	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	509	281.1
66	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
67	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1825	1082
68	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	N.A.	378.56	1160.47	781.91
69	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
70	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
71	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
72	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
73	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5000	3500
74	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	900.05	1125.89	225.84
75	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
76	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	N.A.	514.68	2271.5	1756.82
77	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
78	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	750	283.52
79	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	313.24	554.7	241.46
80	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	792.01	454.52
81	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
82	KANPUR KASGANJ MATHURA(GC) NER	NER	03/1997	N.A.	677.97	1679.13	1001.16
83	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
84	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3451	2637.66
85	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	7000	5323.69
86	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
87	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
88	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
89	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	2145	1845
90	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
91	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
92	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	12/2024	750.55	943.6	193.05
93	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
94	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
95	RANGIA-MURKONGSELEK ALONG WITH LINKED FINGERS	NFR	04/2003	N.A.	4300	4520	220
96	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
97	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
98	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	N.A.	854	1035.16	181.16
99	DAUND - MANMAD (236 KM)	CR	02/2016	N.A.	1876	2081.27	205.27
100	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	N.A.	2326	2449.91	123.91
101	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	N.A.	630	1272.19	642.19
102	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
103	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
104	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
105	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	398.93	152.86
106	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	508	195.88
107	NEW JALPAIGURI SILIGURI-NEW BONGAIGAON INCLUDING BR LINE AND MM FOR CHALSA NAXAL RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1871	1347.83
108	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	450	284.18
109	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
110	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	471	228.78
111	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	6000	1916.98
112	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	342.85	151.13
113	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
114	NEW COOCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	445	235.23
115	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	972.52	720.52
116	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
117	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
118	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RVNL	04/2008	N.A.	822.39	1480.83	658.44
119	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
120	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
121	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
122	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
123	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
124	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
125	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
126	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
127	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
128	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
129	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
130	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
131	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
132	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
133	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	860	404
134	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
135	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
136	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	1037.15	591.15
137	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	845.68	405.8
138	DHASA-JETALSAR (GC)	RVNL	04/2012	N.A.	376.59	644.38	267.79
139	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	N.A.	567.18	975.62	408.44
140	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	N.A.	246.08	431	184.92
141	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
142	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	227	2135	1908
143	RANCHI-LOHARDAGA(GC), SER	SER	04/1997	06/2004	194.07	335	140.93
144	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
145	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
146	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
147	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	480	355
148	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	N.A.	218.24	525	306.76
149	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	966.98	811.24

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
150	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	516.4	191.5
151	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	1566	1016
152	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.23	195.22
153	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1010	885.57
154	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM)	RVNL	04/2011	N.A.	190.1	355.96	165.86
155	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1160.83	334.26
156	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1579.27	900
157	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	N.A.	100	712.82	612.82
158	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
159	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
160	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	SWR	02/1997	N.A.	295	1289.92	994.92
161	GONDA GORAKHPUR LOOP WITH ANAND NAGAR NAUTANWA GC (260 KM)	NER	04/1997	N.A.	836.26	1072.52	236.26
162	RAJATGARH-BARANG(LD), Ecor	RVNL	04/1999	02/2009	166.16	370	203.84
163	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	631.78	327.78
164	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
165	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
166	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	19565	17065
167	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
168	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	516.23	735	218.77
169	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	N.A.	410.08	780.98	370.9
170	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	N.A.	200	780	580
171	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	436	266
172	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	9658	8930.44

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
173	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	N.A.	470.21	3004.9	2534.69
174	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3010	2277
175	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
176	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
177	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
178	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	1714.49	744.15
179	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
180	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
181	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
182	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	N.A.	1046.88	2966.99	1920.11
183	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
184	GUDUR-DURGARAJAPATNAM	SCR	04/2011	N.A.	283.54	759.41	475.87
185	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
186	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
187	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
188	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
189	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
190	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
191	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
192	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	280	183.84
193	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	381.39	282.65
194	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	N.A.	297.85	540.02	242.17
195	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
196	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
197	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	2125.18	1795.18
198	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
199	GADWAL - RAICHUR (NL), SCR	SCR	04/1998	02/2011	92.63	350	257.37
200	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	N.A.	1188.91	1319.33	130.42
201	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
202	JIND-SONEPAT (NL), NR	NR	01/2004	03/2012	238.56	740	501.44
203	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	N.A.	301.64	1185.64	884

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
204	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
205	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
206	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
207	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
208	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
209	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
210	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
211	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
212	ENORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
213	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
214	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	409.83	164.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JANUARY 2017)

STEEL

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
215	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCCL	05/2005	02/2014	768.88	1113.34	344.46
216	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4

URBAN DEVELOPMENT

Sr	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
217	BANGALORE METRO RAIL PROJECT	MRTD	05/2006	06/2011	6395	14405.01	8010.01
218	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1), AT KARWAR, NH-65, JODHPUR RAJASTHAN	CPWD	08/2014	03/2015	350.02	479.87	129.85
219	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2017)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	02/2017	1,3171.00	2,2462.00	9291	98
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2017	3492.00	6000.00	2508	85

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	12/2017	309.46	553.53	244.07	83

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2017	259.40	486.57	227.17	60
6	JAGANNATHPUR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.59	307.16	60

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	05/2017	871.35	1200.00	328.65	26
9	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	03/2018	309.81	462.79	152.98	41
10	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	341.70	138.76	70
11	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	05/2017	861.79	1256.72	394.93	48
12	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	ONGC	05/2013	04/2016	12/2017	4124.35	4259.49	135.14	20

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	08/2018	607.06	714.25	107.19	10
14	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	05/2018	5706.47	5813.25	106.78	12
15	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	03/2018	2059.63	2665.65	606.02	36

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
16	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	09/2017	368.72	1352.53	983.81	134
17	SYSTEM STRENGTHENING IN RAIPUR WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2017	1422.85	1875.13	452.28	26
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	09/2018	1779.29	2187.32	408.03	118
19	SYSTEM STRENGTHENING IN NORTH AND WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	12/2017	1746.65	2228.71	482.06	40
20	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	06/2017	2127.51	2619.56	492.05	35
21	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	09/2019	1657.00	2978.86	1321.86	43
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	8398.75	4479.16	111
23	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	06/2019	2978.48	3846.30	867.82	75
24	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	06/2017	4375.35	6749.18	2373.83	69
25	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2017	1272.80	1731.10	458.3	61
26	BOKARO THERMAL POWER STATION-A	DVC	08/2006	12/2011	02/2017	2313.00	4366.64	2053.64	62
27	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	10/2017	2496.90	6179.96	3683.06	94
28	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2017	487.49	639.46	151.97	42

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	05/2017	573.99	1337.76	763.77	45
30	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	01/2018	3642.04	5783.17	2141.13	24
31	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2017	477.69	738.48	260.79	87
32	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2018	4824.12	5071.94	247.82	64
33	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	12/2017	1,1130.19	1,3762.80	2632.61	52
34	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	01/2017	1216.83	1428.87	212.04	53
35	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	02/2018	2144.00	2932.88	788.88	62
36	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	05/2018	8692.97	1,5095.67	6402.7	88

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
37	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2017	632.68	816.55	183.87	21
38	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANTPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	2030.50	1408.09	46
39	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	12/2020	663.01	858.23	195.22	258
40	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	12/2017	155.74	966.98	811.24	106
41	RAJATGARH-BARANG(LD), ECR	RVNL	04/1999	02/2009	02/2017	166.16	370.00	203.84	96
42	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
43	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	3451.00	2637.66	72
44	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTPT	03/1996	03/2004	03/2020	495.44	1781.98	1286.54	192

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
45	MANDARHILL -DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	03/2020	900.05	1125.89	225.84	99
46	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2018	1500.00	5000.00	3500	122
47	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2019	733.00	3010.00	2277	123
49	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	9658.00	8930.44	108
50	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	3000.00	2150	60
51	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	7986.04	2686.04	60
52	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2017	1676.31	7000.00	5323.69	96
53	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2019	183.23	1202.70	1019.47	58
54	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	02/2017	133.41	340.00	206.59	95
55	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	06/2017	687.20	950.00	262.8	87
56	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	4600.00	3980.66	71
57	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743.00	1825.00	1082	144
58	JAGGAYYAPET - MELLACHERUVU	SCR	04/2007	01/1999	06/2017	313.24	554.70	241.46	221
59	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1581.53	1256.53	84
61	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2017	324.90	516.40	191.5	93
62	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1776.81	1390.51	261

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	3845.60	2669.51	34

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
64	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	03/2017	196.00	331.23	135.23	92
65	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2017	199.81	385.13	185.32	97
66	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	03/2017	1055.00	1601.77	546.77	16
67	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	08/2017	1108.00	2288.00	1180	69
68	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	03/2017	1509.10	3237.87	1728.77	54
69	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	02/2017	155.04	280.13	125.09	99

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
70	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TRU	01/2007	12/2010	12/2018	366.39	669.46	303.07	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
71	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	12/2017	343.00	488.40	145.4	14

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
72	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	12/2017	241.33	349.33	108	21
73	BANGALORE METRO RAIL PROJECT	M RTP	05/2006	06/2011	04/2017	6395.00	1,4405.01	8010.01	70
74	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-	CPWD	08/2014	03/2015	07/2017	350.02	479.87	129.85	28

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

**DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS
OF RS.100 CRORE AND ABOVE**

(JANUARY 2017)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	1), AT KARWAR, NH-65, JODHPUR RAJASTHAN								

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of All Central Sector Infrastructure Projects having Under -Public Private Partnership Mode

Annexure- XVIII

Costing Rs. 150 crore & above, (January 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>MINES</u>							
1	IMPLEMENTATION OF 50 MW WIND POWER PROJECT AT DEVIKOT PPP (ANNUITY) - [N10000009]	12/2015	344.50 -	344.50	11/2016 -	09/2016	.00	-2
	Total		344.50 -	344.50				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
2	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - PPP (BOT) - [N24000231]	10/2013	283.25 -	283.25	10/2015 -	12/2017	.00	26
3	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	03/2017	.00	38
4	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	01/2017	.00	44
5	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	02/2017	.00	45
6	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - PPP (BOT) - [N24000153]	03/2011	359.00 -	359.00	09/2013 -	12/2016	.00	39
7	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2017	.00	55
8	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2017	.00	52
9	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	03/2017	.00	82
10	BHUBANESWAR TO PURI - PPP (BOT) - [N24000195]	03/2011	500.29 -	500.29	08/2013 -	06/2017	.00	46
11	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	06/2017	.00	43
12	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
13	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	03/2017	.00	7
14	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	06/2017	.00	41
15	TALEGAON-AMRAVATI - PPP (BOT) - [N24000140]	11/2009	567.00 -	567.00	11/2013 -	-	.00	0
16	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2017	.00	50

Details of All Central Sector Infrastructure Projects having Under -Public Private Partnership Mode

Costing Rs. 150 crore & above,					(January 2017)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
17	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	03/2017	.00	36
18	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	09/2017	.00	50
19	4-LANING OF RAIGANJ-DALKOLA - PPP (BOT) - [N24000204]	02/2011	580.43 -	580.43	08/2013 -	12/2017	.00	52
20	NIROLI-ROXY-RAJAMUNDA - PPP (BOT) - [N24000194]	07/2011	586.00 -	586.00	01/2014 -	12/2016	.00	35
21	DEOLI-KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	10/2017	.00	51
22	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
23	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	03/2017	.00	55
24	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	32
25	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	06/2019	.00	0
26	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	03/2017	.00	40
27	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	03/2017	.00	37
28	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	09/2017	.00	55
29	4 - LANING OF RAJSAMAND-GANGAPUR-BHILWARA - PPP (BOT) - [N24000236]	10/2013	677.79 -	677.79	04/2016 -	03/2017	.00	11
30	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	09/2017	.00	38
31	SIX LANE OF GREENFIELD PROPOSED UDAIPUR BYPASS [CONNECTION BETWEEN NH-76 AT EXISTING KM - PPP (BOT) - [N24000588]	06/2016	725.95 -	725.95	06/2019 -	06/2019	.00	0
32	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	11/2017	.00	56
33	FOUR LANING OF MAHUA TO KAGAVADAR OF NH- 8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	-	.00	0
34	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	04/2018	.00	0
35	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - PPP (BOT) - [N24000225]	03/2012	828.00 -	828.00	09/2014 -	10/2017	.00	37
36	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	.00	0

Details of All Central Sector Infrastructure Projects having Under -Public Private Partnership Mode

Costing Rs. 150 crore & above, (January 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
37	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM (BOT) - [N24000144] - PPP	09/2010	852.00 -	852.00	03/2013 -	04/2017	.00	49
38	BARSAT-KRISHNANAGAR - PPP (ANNUITY) - [N24000229]	08/2012	867.00 -	867.00	02/2015 -	12/2017	.00	34
39	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	11/2017	.00	12
40	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - PPP (BOT) - [N24000123]	03/2005	940.00 -	940.00	07/2012 -	05/2017	.00	58
41	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	04/2017	.00	45
42	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	01/2018	.00	6
43	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	03/2018	.00	55
44	4 LANNING OF AHMEDABAD TO GODHARA - PPP (BOT) - [N24000167]	12/2010	1,008.50 -	1,008.50	06/2013 -	12/2017	.00	54
45	BAREILY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	05/2017	.00	44
46	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	03/2017	.00	33
47	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	03/2017	51.83	16
48	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	06/2017	.00	46
49	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	12/2017	.00	42
50	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	08/2017	106.50	69
51	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	03/2017	.00	43
52	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	03/2017	2.65	47
53	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2017	.00	48
54	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60 -	1,266.60	09/2016 -	03/2017	.00	6
55	MURADABAD-BAREILY - PPP (BOT) - [N24000154]	04/2010	1,267.00 -	1,267.00	06/2013 -	03/2017	.00	45
56	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	09/2017	.00	43

Details of All Central Sector Infrastructure Projects having Under -Public Private Partnership Mode

Costing Rs. 150 crore & above, (January 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
57	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	-	08/2018	.00	0
58	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	01/2018	.00	0
59	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	05/2017	.00	32
60	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	06/2017	.00	33
61	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	12/2017	.00	30
62	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	3,237.87	09/2012	03/2017	114.56	54
63	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	12/2016	.00	31
64	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	02/2017	.00	17
65	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	-	01/2019	.00	0
66	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	06/2017	.00	49
67	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	08/2017	.00	12
68	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	-	01/2019	.00	0
69	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	03/2017	.00	0
70	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	09/2017	.00	71
71	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	03/2017	.00	67
72	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	03/2017	.00	48
73	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	01/2017	.00	42
74	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	01/2018	.00	0
75	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	02/2018	.00	15
76	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	01/2017	.00	21
77	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	07/2017	.00	24

Details of All Central Sector Infrastructure Projects having Under -Public Private Partnership Mode

Costing Rs. 150 crore & above, (January 2017)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
78	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	02/2017	.00	14
79	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	- -	04/2019	.00	0
80	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	02/2017	.00	20
81	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	- -	05/2019	.00	0
82	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	03/2017	.00	31
83	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	04/2017	.00	37
	Total		90,052.69 -	93,539.33				
	<u>SHIPPING AND PORTS</u>							
84	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000065]	10/2013	198.94 -	235.15	06/2017 -	06/2017	18.20	0
85	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	258.33	12/2017 -	12/2017	5.66	0
86	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		809.83 -	1,162.94				
	Grand Total		91,207.02	95,046.77				
