

393th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
July 2018



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

- **AAI** **Airport Authority of India**
- **AERB** **Atomic Energy Regulatory Board**
- **AIBP** **Accelerated Irrigation Benefit Programme**
- **AIR** **All India Radio**
- **APW** **Active Process Water**
- **ATU** **Atomic Treating**
- **BCM** **Billion Cubic Meter**
- **BHEL** **Bharat Heavy Electricals**
- **BHPV** **Bharat Heavy Plates & Vessel Ltd.**
- **BLU** **Boiler Light Up**
- **BOLT** **Build , Operate, Lease & Transfer**
- **BPST** **Bureau of Parliamentary Studies & Training**
- **CCEA** **Cabinet Committee on Economic Affairs**
- **CCU** **Catalytic Cracking**
- **CDS** **Crude Distribution System**
- **CDU** **Crude Distillation Unit**
- **CEA** **Central Electricity Authority**
- **CEC** **Central Empowered Committee**
- **CHP** **Coal Handling Plant**
- **CLW** **Chittaranjan Locomotive Works**
- **CMPDI** **Central Mine Planning & Design Institute**
- **COS** **Committee of Secretaries**
- **COR** **Cost Overrun**
- **CPP** **Captive Power Plant**
- **CRIS** **Centre for Railway Information System**
- **CRL** **Cochin Refinery Ltd.**
- **CSL** **Cochin Shipyard Ltd.**
- **CTU** **Crude Topping Unit**
- **DAE** **Department of Atomic Energy**
- **DB** **Dumb Barges**
- **DCME** **Digital Circuit Multiplexing Equipment**
- **DGMS** **Director General Mines Safety**
- **DHDS** **Diesel Hydro Desulphurisation project**
- **DOA** **Date of Approval**

- **DOC** **Date of Commissioning**
- **DOT** **Department of Telecommunication**
- **DVC** **Damodar Valley Corporation**
- **ECL** **Eastern Coalfields Ltd.**
- **EIL** **Engineers India Ltd.**
- **EMP** **Enivronment Management Plan**
- **EOT** **Electrical Overhead Travelling crane**
- **ESP** **Electrostatic Precipitator**
- **FCCU** **Fluidised Catalytic Cracker Unit**
- **ERP** **Enterprise Resource Planning**
- **FE** **Foreign Exchange**
- **FOIS** **Freight Operation Information System**
- **FPU** **Feed Preparation Unit**
- **GAIL** **Gas Authority of India Ltd.**
- **GC** **Gauge Conversion**
- **GDS** **Gateway Digital Switch**
- **GIS** **Gas Insulated Station**
- **GT** **Gas Turbine**
- **GTPP** **Gas Turbine Power Plant**
- **HCU** **Hydro- cracker Unit**
- **HEC** **Heavy Engineering Corporation**
- **HEMM** **Heavy Equipment & Mining Machinery**
- **HEP** **Hydro Electric Project**
- **HPCL** **Hindustan Petroleum Corporation Ltd.**
- **HRT** **Head Race Tunnel**
- **HSCL** **Hindustan Steel Construction Ltd.**
- **HVDC** **High Voltage Direct Current**
- **IAAI** **International Airport Authority of India**
- **ICT** **Inter Connecting Transformer**
- **IDC** **Interest During construction**
- **IFFCO** **Indian Farmer Fertilizer Co-operative Ltd.**
- **IMG** **Inter Ministrial Group**
- **IOC** **Indian Oil Corporation Ltd.**
- **IPCL** **Indian Petrochemicals Ltd.**

- **KV** **Kilo Volts.**
- **L&T** **Larsen & Toubro**
- **LEP** **Life Extension Program**
- **LOI** **Letter of Intent**
- **LPG** **Liquified Petroleum Gas**
- **LSTK** **Lump sum Turnkey contract**
- **MAMC** **Minning & Allied Machinery Corporation.**
- **MFL** **Madras Fertilizer Ltd.**
- **MGCL** **Madras Gas Cracker Complex**
- **MIS** **Management Information System**
- **MMSCMD** **Million Metric Standard Cubic Meter day**
- **MMT** **Million Metric Tonnes**
- **MOE&F** **Ministry of Environment & Forest**
- **MT** **Metric Tonnes**
- **MTY** **Metric Tonne per year**
- **MU** **Million Unit**
- **MW** **Mega Watts**
- **NAC** **New Anticipated Cost**
- **NALCO** **National Aluminium Company**
- **NBCC** **National Building Construction Corporation.**
- **NCL** **Northern Coalfields Ltd**
- **NEC** **North East Council**
- **NEEPCO** **North-Eastern Electric Power Corporation Ltd.**
- **NFL** **National Fertilizer Ltd.**
- **NH** **National Highway**
- **NHPC** **National Hydro-Electric Power Corporation**
- **NIRE** **National Institute of Renewable Energy**
- **NIT** **Notice Inviting Tender**
- **NJPC** **Nathpa Jhakri Power Corporation Ltd.**
- **NGN** **Next Generation Network**
- **NLC** **Neyveli Lignite Corporation Ltd.**
- **NMDC** **National Mineral Development Corporation Ltd.**
- **NPC** **Nuclear Power Corporation Ltd.**
- **NRL** **Numaligarh Refinery Ltd.**

- **OB** Over Burden
- **OC** Opencast
- **OECF** Overseas Economic Co-operation Fund
- **ONGC** Oil & Natural Gas Commission
- **OPGC** Orissa Power Generation Corporation
- **P & M** Plant & Machinery
- **PERT** Project Evaluation & Review Technique
- **PSTN** Public Switched Telephone Network
- **PHT** Primary Heat Transport
- **PIB** Public Investment Board
- **PSLW** Powered Support Longwall
- **QRC** Quick Roll Changer
- **RAPP** Rajasthan Atomic Power Plant
- **RCE** Revised Cost Estimates
- **RCF** Railway Coach Factory
- **ROB** Road Over Bridge
- **ROH** Regular Overhauling
- **RTU** Remote Terminal Unit
- **SAIL** Steel Authority of India Ltd.
- **SCI** Shipping Corporation of India Ltd.
- **SDH** Synchronous Digital Hierarchy
- **SG** Steam Generator
- **SP** Self Propelled
- **ST** Steam Turbine
- **STPS** Super Thermal Power Station
- **SUR** Sulphur Recovery Unit
- **SWSU** Sour Water Stripping Unit
- **TBM** Tunnel Boring Machine
- **TG** Turbo Generator
- **TPA** Tonnes Per Annum
- **TPS** Thermal Power Station
- **TOR** Time Overrun
- **TPY** Tonnes per year
- **UG** Under Ground

- **ULDCS** Unified Load Despatch & Communication Scheme
- **VDU** Vacuum Distillation Unit
- **WHRB** Waste Heat Recovery Boiler
- **WO_DOC** With out Date of Commissioning
- **WO_ODC** With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for July 2018 contains information on the status of the 1361 Central Sector Infrastructure Projects costing ₹150 crore and above. During July 2018, 10 projects (7 projects in Petroleum, 2 projects in Power and 1 project in Steel sectors) have reported completion.
2. During the reference month, out of 1361 projects, 296 projects are delayed with respect to their original schedules and 32 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 32 projects, 14 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	543	53	5	3
2	RAILWAYS	350	65	4	2
3	PETROLEUM	136	24	2	0
4	POWER	110	65	12	7
5	COAL	94	35	2	0
6	URBAN DEVELOPMENT	43	19	3	0
7	STEEL	28	13	1	1
8	HEALTH AND FAMILY WELFARE	22	6	1	0
9	TELECOMMUNICATIONS	10	6	1	0
10	FERTILISERS	6	1	0	0
11	SHIPPING AND PORTS	5	2	0	0
12	ATOMIC ENERGY	4	4	1	1
13	MINES	4	0	0	0
14	CIVIL AVIATION	2	2	0	0
15	HEAVY INDUSTRY	2	1	0	0
16	DEFENCE PRODUCTION	2	0	0	0
Total		1361	296	32	14

3. Total original cost of implementation of the 1361 projects was ₹16,78,634.82 crore and their anticipated completion cost is likely to be ₹20,16,360.99 crore, which reflects overall cost overruns of ₹3,37,726.17 crore (20.12% of original cost). The expenditure incurred on these projects till July 2018 is ₹7,68,186.93 crore, which is 38.10% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 01-08-2018)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	74.68
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	78.87
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	87.58
5	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	1.87
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	1.60
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	13.31
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	2.88
4	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	08/2017	272.19	272.54	0.13
5	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROLEUM					
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
3	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1256.72	45.83
5	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	913.00	1330.00	45.67
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4401.90	165.65

3	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1078.31	156.12
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	147.51
5	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.75	114.28
RAILWAYS					
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	13809.00	1797.99
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	614.00	1568.48
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
5	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
ROAD TRANSPORT AND HIGHWAYS					
1	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	114.56
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
3	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	17.79
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	17.50
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	12.04
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	44.75
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	4.11

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-08-2018)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6100.00	2608.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	553.53	244.07
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	486.57	227.17
3	BHANEAGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 3B	12/2016	285.95	291.29	5.34
2	CONSTRUCTION WORKS PHASE 4	12/2016	167.69	170.37	2.68
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	191.38	22.48
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	322.00	9.01
4	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	08/2017	272.19	272.54	0.35
5	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
PETROLEUM					
1	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3076.00	4190.00	1114.00
2	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
3	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	4588.29	5245.96	657.67
4	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	2059.63	2665.65	606.02
5	PARADIP HALDIA DURGAPUR LPG PIPELINE	02/2011	913.00	1330.00	417.00
POWER					

1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	8398.75	4479.16
4	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9141.97	4387.55
5	BONGAIGAON THERMAL POWER PROJECT	01/2008	4375.35	8150.00	3774.65
RAILWAYS					
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	727.56	13809.00	13081.44
5	RISHIKESH - KARNAPRAYAG NEW LINE	04/2011	4295.30	16216.00	11920.70
ROAD TRANSPORT AND HIGHWAYS					
1	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	03/2010	1509.10	3237.87	1728.77
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
3	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
4	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	03/2017	993.16	1434.00	440.84
5	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	03/2017	2064.99	2447.00	382.01
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
3	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	175.49	206.71	31.22
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	26.21
5	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	24.39
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
3	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23
4	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
5	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	02/2011	241.33	349.33	108.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 1361 projects, 386 are on schedule, 296 are delayed, 358 projects reported cost overrun and 123 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 226 if delay is calculated on the basis of latest schedule of completion. Further, for 660 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 296 delayed projects, 77 projects have overall delay in the range of 1 to 12 months, 51 projects have delay in the range of 13 to 24 months, 83 projects have delay in the range of 25 to 60 months and 85 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-08-2018)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	03/2019	102
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	09/2018	92
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
COAL					
1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
2	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2019	108
4	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2020	108
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	03/2021	108
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	04/2019	29
HEALTH AND FAMILY WELFARE					
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	12/2018	19
2	AIIMS - OPD(NEW)	08/2014	05/2017	09/2018	16
3	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	09/2018	16
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
5	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	12/2018	10
HEAVY INDUSTRY					
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	08/2016	09/2019	37
PETROLEUM					

2	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2019	74
3	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	03/2019	72
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2018	67
	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	03/2015	12/2019	57
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2020	135
2	BARH STPP(3X660MW) NTPC	02/2005	01/2011	04/2021	123
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	12/2018	121
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	03/2019	111
5	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	03/2022	103
	RAILWAYS				
1	MM FROM PANSKURA-GHATAL NL	04/2011	01/1999	03/2030	374
2	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
3	MM FROM BURAMARA-CHAKULIA	04/2008	01/1999	12/2024	311
4	MARIKUPPAM - KUPPAM	04/2012	01/1999	12/2023	299
5	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
	ROAD TRANSPORT AND HIGHWAYS				
1	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	09/2018	118
2	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	10/2018	114
3	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	10/2018	101
4	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	11/2011	06/2019	91
5	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	02/2008	10/2011	10/2018	84
	SHIPPING AND PORTS				
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	12/2018	96
2	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
	STEEL				
1	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
2	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	12/2018	43
3	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2019	29
4	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	02/2014	12/2016	12/2018	24
5	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	05/2015	03/2017	08/2018	17
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MADHYA PRADESH ACCESS (LOT1)	08/2017	05/2018	10/2018	5
3	MAHARASHTRA NODAL (LOT 1)	08/2017	04/2018	08/2018	4
4	MAHARASHTRA CORE (LOT1)	08/2017	04/2018	08/2018	4
5	MAHARASHTRA ACESS (LOT 1)	08/2017	05/2018	08/2018	3
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2019	77
2	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
3	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	12/2018	49
4	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	12/2019	45

1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	414.11	141.00	11/2013	N.A.
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	272.00	06/2020	06/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	39.35	04/2020	04/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	214.62	09/2018	09/2018
HEAVY INDUSTRY							
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	2289.00	09/2011	N.A.
2	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	161.86	08/2016	09/2019
MINES							
1	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	483.00	483.00	0.00	04/2021	04/2021
PETROLEUM							
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	736.65	571.47	543.05	09/2011	05/2018
3	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
4	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	438.84	170.50	03/2017	03/2019
5	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.12	02/2017	N.A.
POWER							
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10234.01	09/2010	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	2734.43	10/2017	12/2016
3	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	08/2008	771.00	1642.00	1429.45	02/2013	10/2018
4	TRANMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH	01/2014	1788.41	2333.71	1513.68	09/2017	09/2018

1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	200.00	200.00	131.15	03/2018	N.A.
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	172.30	06/2017	N.A.
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	215.30	0.00	05/2018	10/2018
4	MAHARASHTRA ACCESS (LOT 1)	08/2017	212.70	212.70	37.08	05/2018	08/2018
5	MAHARASHTRA CORE (LOT1)	08/2017	167.68	167.68	30.21	04/2018	08/2018
URBAN DEVELOPMENT							
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
2	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	10/2019
3	DELHI MRTS PHASE-III	09/2011	38585.00	38585.00	34270.32	03/2016	N.A.
4	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	884.30	620.49	12/2015	07/2018
5	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5181.79	0.00	07/2017	12/2019

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost
Estimates (as on 01-08-2018)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
CIVIL AVIATION					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	546.69
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	302.96	0.00	334.77
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	0.00	410.19
3	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	263.24
4	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	581.49
5	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	233.26
HEALTH AND FAMILY WELFARE					
1	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	237.80
2	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	191.38
3	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	07/2016	312.99	0.00	469.00
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	2289.00
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	09/2012	871.35	0.00	961.00
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	6955.14
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10234.01
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6179.96	6604.01
4	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3611.12
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	7128.72
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	968.28
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
4	KHURDA ROAD-BOLANGIR(NL)ECOR	04/1994	470.21	0.00	1069.54
5	AMRAVATI-NARKHER NL(CR)	06/1994	663.01	668.34	713.16
ROAD TRANSPORT AND HIGHWAYS					
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	410.32
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	268.94
3	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	0.00	209.80
4	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	200.00	0.00	245.83
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	0.00	195.35
SHIPPING AND PORTS					
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	413.91

2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.98
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	INSTALLATION OF NEW HOT STRIP MILL AT RSP	04/2015	3127.30	0.00	5467.78
4	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	1154.18	0.00	1607.72
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on as on 01-08-2018)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	N.A.	03/2018
2	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	03/2012	N.A.	N.A.
3	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
4	RAJMAHAL OC EXP.	09/2009	03/2014	N.A.	N.A.
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	N.A.	05/2018
FERTILISERS					
1	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	02/2016	12/2017	05/2018	05/2018
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	N.A.	N.A.
3	HOSPITAL AND TEACHING- AIIMS GUNTUR	03/2018	N.A.	N.A.	N.A.
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	05/2018	05/2018
3	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.

POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	12/2016
3	TRIPURA GAS BASED POWER PROJECT	07/2009	07/2013	N.A.	N.A.
4	KUDGI STPP STAGE 1	01/2012	01/2017	N.A.	N.A.
5	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
2	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
3	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.A.	N.A.	N.A.
5	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	01/1991	05/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
STEEL					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	06/2016	N.A.	N.A.
4	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.
5	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	03/2018	N.A.	N.A.
TELECOMMUNICATIONS					

1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
2	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-43 G BLOCK BANDRA	02/2011	03/2016	12/2017	04/2018
3	DELHI MRTS PHASE-III	09/2011	03/2016	N.A.	N.A.
4	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	N.A.	N.A.
5	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	06/2014	03/2017	N.A.	N.A.

N.A.: Not Available.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

11. The status as on 31.07.2018 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	543	5
2	RAILWAYS	350	4
3	PETROLEUM	136	2
4	POWER	110	12
5	COAL	94	2
6	URBAN DEVELOPMENT	43	3
7	STEEL	28	1
8	HEALTH AND FAMILY WELFARE	22	1
9	TELECOMMUNICATIONS	10	1
10	FERTILISERS	6	0
11	SHIPPING AND PORTS	5	0
12	ATOMIC ENERGY	4	1
13	MINES	4	0
14	CIVIL AVIATION	2	0
15	HEAVY INDUSTRY	2	0
16	DEFENCE PRODUCTION	2	0
	Total	1361	32

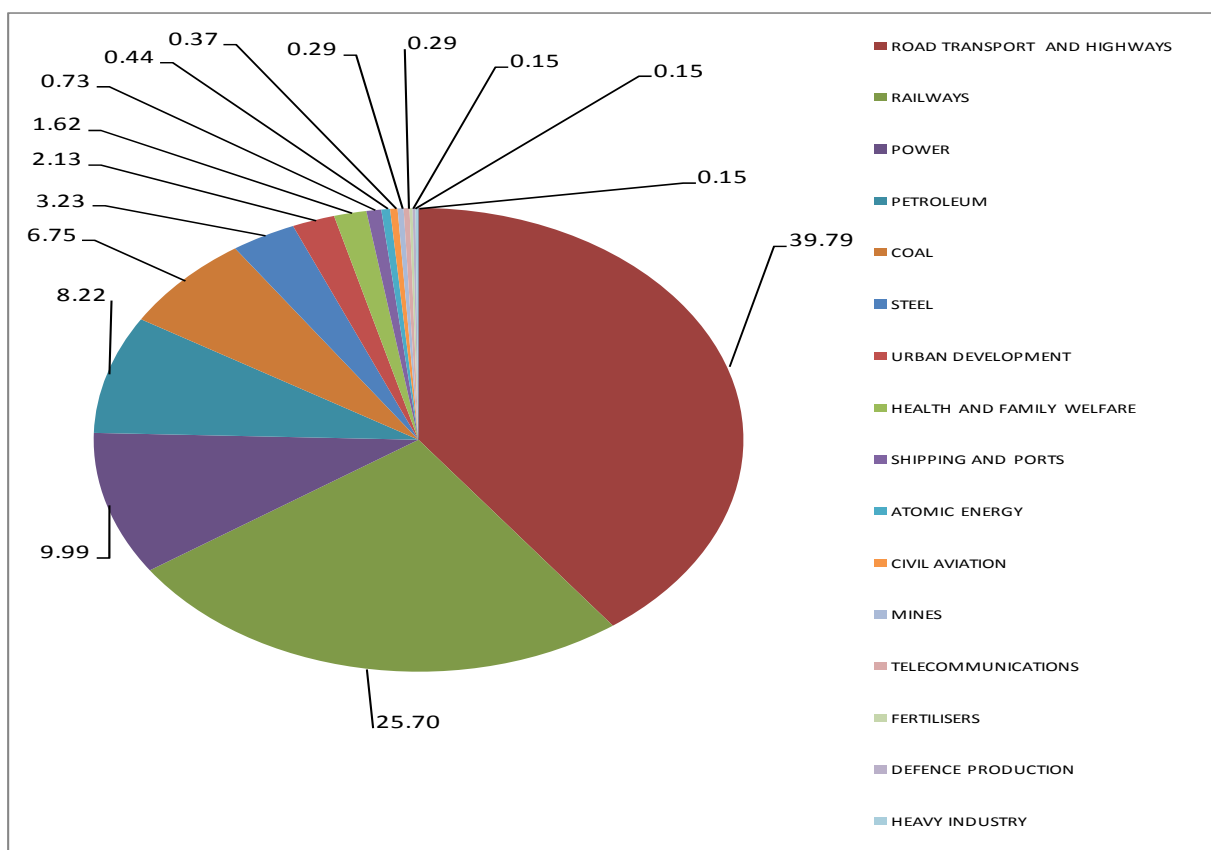


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2018			
	<u>STEEL</u>			
1	ALTERNATE GAS NETWORK AT BSL (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000093]	255.19	03/2018	177.21
	<u>PETROLEUM</u>			
2	ENNORE TERMINAL (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000224]	393.00	04/2018	281.45
	<u>POWER</u>			
3	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000123]	198.63	09/2014	127.13
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000179]	6,517.36	04/2018	3,772.80
5	REMOVAL OF CONSTRAINTS IN 400KV BAYS EXTENSIONS AT 400KV VEMAGIRI SS (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000210]	207.88	07/2018	17.00
	<u>HEALTH AND FAMILY WELFARE</u>			
6	AIIMS-RAE BARELI-HOUSING (HOSPITAL SERVICES CONSULTANCY CORPORATION LTD) - [N21000006]	159.50	11/2013	158.65
	<u>RAILWAYS</u>			
7	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION (RAIL VIKAS NIGAM LTD.) - [N22000189]	822.39	-	1,713.20
8	NEW COOCHBEHAR TO SAMUKTALA (NORTH EAST FRONTIER RAILWAY) - [N22000197]	209.77	-	620.04
9	DELANG-PURI DOUBLING (EAST COAST RAILWAY) - [N22000320]	165.16	03/2015	226.35
10	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) (RAIL VIKAS NIGAM LTD.) - [N22000322]	190.10	-	320.41
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	TALEGAON-AMRAVATI PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000140]	567.00	11/2013	1,055.94
12	MURADABAD-BAREILY PPP (BOT)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000154]	1,267.00	06/2013	2,667.96
	<u>SHIPPING AND PORTS</u>			

Month wise List of Completed Projects Costing Rs.150 crore and above during

2018-2019

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	CONSTRUCTION OF COAL BERTH-3 AT KAMARAJAR PORT LIMITED PPP (ANNUITY)(KAMARAJAR PORT LIMITED) - [N25000065]	198.94	06/2017	255.02
14	CAPITAL DREDGING PHASE-III AT KAMARAJAR PORT LIMITED (KAMARAJAR PORT LIMITED) - [N25000067]	274.85	04/2017	251.64
	<u>URBAN DEVELOPMENT</u>			
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE-1),AT KARWAR,NH-65,JODHPUR RAJASTHAN Central Sector Projects(CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000091]	350.02	03/2015	452.35
	May,2018			
	<u>PETROLEUM</u>			
16	TWENTY NOS. FEEDER GAS LINES (OIL INDIA LIMITED) - [N16000192]	228.64	12/2016	149.73
17	PETCOKE EVACUATION PROJECT AT PARADIP REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000201]	238.50	03/2017	203.98
18	SIX PIPELINE REPLACEMENT PROJECT Central Sector Projects(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000214]	181.02	01/2017	174.88
19	FUEL QUALITY UPGRADATION (DHDT/DHDS) PROJECT AT GUJARAT REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000245]	931.00	07/2017	684.74
	<u>POWER</u>			
20	PARE HYDRO ELECTRIC PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000045]	573.99	08/2013	1,637.60
	<u>RAILWAYS</u>			
21	GADWAL - RAICHUR (NL), SCR (SOUTH CENTRAL RAILWAY) - [220100270]	92.63	02/2011	319.43
22	JAGGAYYAPET - MELLACHERUVU (SOUTH CENTRAL RAILWAY) - [N22000304]	313.24	01/1999	578.00
	June,2018			
	<u>POWER</u>			
23	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000197]	1,479.30	04/2017	897.12
24	AUGMENTATION OF TRANSFORMATION CAPACITY IN SOUTHERN REGION (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000237]	167.75	04/2019	86.62
	<u>RAILWAYS</u>			
25	RANCHI-LOHARDAGA(GC),SER (SOUTH EASTERN RAILWAY) - [220100214]	194.07	06/2004	194.07
26	BHOPAL BINA 3D LINE DOUBLING (RAIL VIKAS NIGAM LTD.) - [N22000077]	687.20	03/2010	1,033.77

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2018-2019				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	July,2018			
	<u>STEEL</u>			
27	EXPANSION OF BHILAI STEEL PLANT (STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000057]	17,265.00	03/2013	19,855.23
	<u>PETROLEUM</u>			
28	DEVELOPMENT OF C-26 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000133]	2,592.17	05/2014	2,049.26
29	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000134]	200.69	07/2014	109.58
30	CONSTRUCTION OF THREE ETPS, MEHSANA (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000135]	260.74	11/2014	83.44
31	PIPELINE REPLACEMENT PROJECT, AHMEDABAD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000159]	202.25	07/2016	130.21
32	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000172]	4,124.35	04/2016	5,347.49
33	MH NORTH REDEVELOPMENT PHASE III (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000188]	5,706.47	05/2017	5,724.54
34	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000246]	215.38	06/2017	198.98
	<u>POWER</u>			
35	BOKARO THERMAL POWER STATION-A (DAMODAR VALLEY CORPORATION) - [N18000199]	2,313.00	12/2011	3,965.00
36	RAGHUNATHPUR THERMAL POWER STATION PHASE-I (DAMODAR VALLEY CORPORATION) - [N18000202]	4,122.00	02/2011	8,479.00


Summary of projects in the Flash Report for the month of July, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1362
Number of Projects completed/dropped/frozen in Current Month	10
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	8
Number of Projects in Current Month	1361

Brief Analysis

Project Status with respect to Original Schedule: Out of 1361 projects, 19 projects are ahead of schedule, 386 projects are on schedule 296 projects are delayed. 622 projects do not have fixed dates of commissioning. 38 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

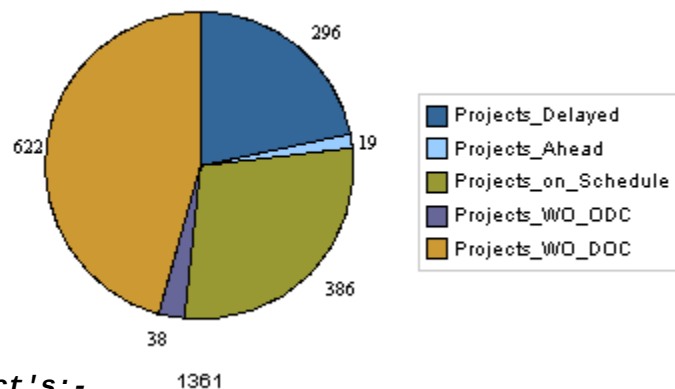

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1361 projects when sanctioned, was of the order of Rs. 1678634.82 crore but this was subsequently revised to Rs. 2016360.99 crore implying a cost overrun of 20.1%. The expenditure incurred on these projects till July, 2018 is Rs. 768186.93 crore, which is 38.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

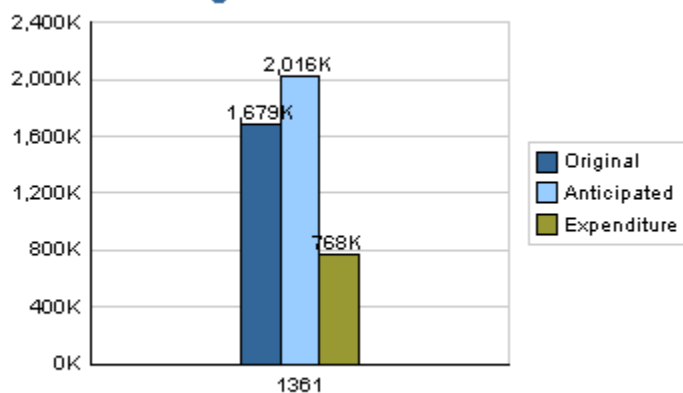


TABLE-3

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1362
No of Projects Completed/Dropped/Frozen in Current Month	10
No. of project elevated	1
No of Projects added in Current Month	8
No of Projects in Current Month	1361

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	296 (21.75%)	19 (1.40%)	386(28.36%)	38 (2.79%)	622(5.70%)	1361
Latest Approved (Date)	226 (16.61%)	17 (1.25%)	479(35.19%)	17 (1.25%)	622(5.70%)	1361

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1159	14,25,418.52	16,14,419.35	5,53,431.39	34.30	1,89,000.83	13.30
Project with Revision in Cost	202	3,91,095.93	4,01,941.64	2,14,755.54	53.40	10,845.71	2.80
Total	1,361	18,16,514.45	20,16,360.99	7,68,186.93	38.10	1,99,846.54	11.00
Original Cost of All Projects							
Original Cost	1,361	16,78,634.82	20,16,360.99	7,68,186.93	38.10	3,37,726.17	20.12

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	296	5,84,127.66	7,46,566.91	4,07,716.16	54.60	1,62,439.25	27.80
Latest Approved (RCE)	226	3,81,013.22	4,53,497.63	2,41,122.23	53.20	72,484.41	19.00

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	32	63,925.98	1,03,260.20	76,327.29	73.90	39,334.22	61.50
Total	32	63,925.98	1,03,260.20	76,327.29	73.92	39,334.22	61.53

TABLE-4

Extent of cost overrun in projects with respect to original schedule(Sector Wise) Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	94	91,364.09	90,827.28	-0.59	9	19,751.90	21,082.91	6.74
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	5.89
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	28	37,451.14	37,664.82	0.57	5	1,639.71	2,211.39	34.86
7	PETROLEUM	136	2,17,011.11	2,17,989.15	0.45	15	19,129.74	24,486.29	28.00
8	POWER	110	3,13,586.68	3,77,560.50	20.40	45	1,78,005.08	2,41,978.90	35.94
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	6	1,665.23	1,714.64	2.97
11	RAILWAYS	350	4,07,092.54	6,46,528.15	58.82	216	1,65,343.22	4,12,160.04	149.28
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,175.11	3,64,610.12	1.80	43	25,879.88	33,000.93	27.52
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	3	760.89	1,545.44	103.11
14	TELECOMMUNICATIONS	10	17,191.20	28,421.20	65.32	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	43	1,44,199.91	1,49,477.76	3.66	7	21,267.70	26,545.55	24.82
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	2	453.64	461.66	1.77
Total		1361	16,78,634.82	20,16,360.99	20.12	358	4,64,721.85	8,17,563.35	75.93

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-5

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above
(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	61	98,363.19	1,03,681.73	5.41	12	9,090.11	15,647.76	72.14
2	ARUNACHAL PRADESH	30	16,028.42	33,154.93	106.85	5	9,181.79	26,308.30	186.53
3	ASSAM	46	28,862.47	39,548.00	37.02	13	9,627.25	20,520.33	113.15
4	BIHAR	84	70,606.42	87,437.49	23.84	21	33,916.51	51,043.53	50.50
5	GOA	10	4,292.52	4,300.60	0.19	3	702.65	710.73	1.15
6	GUJARAT	48	44,417.71	53,141.00	19.64	11	18,043.92	28,016.06	55.27
7	HARYANA	24	17,887.77	19,800.43	10.69	5	2,452.13	4,498.00	83.43
8	HIMACHAL PRADESH	12	14,659.32	25,091.60	71.16	2	4,966.47	15,398.75	210.05
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
10	KARNATAKA	42	71,151.56	81,641.15	14.74	17	23,776.18	35,429.55	49.01
11	KERALA	22	23,243.87	26,990.43	16.12	7	7,359.98	11,278.04	53.23
12	MADHYA PRADESH	61	65,252.10	70,966.23	8.76	9	26,941.86	33,639.61	24.86
13	MAHARASHTRA	129	1,72,945.28	1,86,576.57	7.88	29	34,384.95	51,743.91	50.48
14	MANIPUR	2	944.25	14,025.69	1385.38	1	727.56	13,809.00	1797.99
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	1	4,083.02	6,000.00	46.95
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	642.73
17	NAGALAND	21	12,234.55	14,384.55	17.57	1	850.00	3,000.00	252.94
18	ODISHA	79	81,330.92	91,471.24	12.47	19	20,303.29	30,459.90	50.02
19	PUNJAB	31	16,717.41	16,723.14	0.03	2	1,328.50	1,361.27	2.47
20	RAJASTHAN	60	44,903.52	47,181.46	5.07	13	5,724.18	8,037.94	40.42
21	SIKKIM	6	2,537.08	5,585.45	120.15	3	2,036.94	5,085.59	149.67
22	TAMIL NADU	68	1,13,886.72	1,30,183.04	14.31	24	29,335.23	46,722.76	59.27
23	TRIPURA	9	3,776.07	8,365.85	121.55	7	2,909.18	7,498.96	157.77
24	UTTAR PRADESH	100	1,17,454.69	1,21,491.75	3.44	21	29,300.03	34,665.37	18.31
25	WEST BENGAL	53	54,028.97	63,055.17	16.71	19	16,606.85	26,002.73	56.58
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	40.28
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	23	56,043.88	56,632.51	1.05	4	5,796.42	6,385.05	10.16
29	CHHATISGARH	38	67,062.14	69,718.38	3.96	5	13,453.90	16,110.14	19.74
30	JHARKHAND	48	45,550.26	47,819.80	4.98	9	21,306.82	23,580.14	10.67
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	8	13,425.90	30,895.91	130.12
32	TELANGANA	38	29,795.41	34,600.88	16.13	14	6,228.73	11,258.30	80.75
33	MULTI STATE	172	3,44,126.91	4,53,016.12	31.64	69	1,05,639.14	2,17,131.68	105.54
Total		1361	16,78,634.82	20,16,360.99	20.12	358	4,64,721.85	8,17,563.35	75.93

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of time overrun in projects with respect to original schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 92
3	COAL	94	91,364.09	90,827.28	-0.59	35	20,501.12	20,380.18	12 - 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29 - 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	28	37,451.14	37,664.82	0.57	13	28,594.47	28,381.87	2 - 72
7	PETROLEUM	136	2,17,011.11	2,17,989.15	0.45	24	75,183.68	76,984.18	1 - 74
8	POWER	110	3,13,586.68	3,77,560.50	20.40	65	2,14,463.57	2,60,933.99	1 - 135
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	6	1,689.51	1,729.41	6 - 19
11	RAILWAYS	350	4,07,092.54	6,46,528.15	58.82	65	57,194.36	1,42,816.18	3 - 374
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,175.11	3,64,610.12	1.80	53	41,568.84	46,011.96	2 - 118
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	2	966.39	927.36	29 - 96
14	TELECOMMUNICATIONS	10	17,191.20	28,421.20	65.32	6	14,260.52	25,590.52	3 - 58
15	URBAN DEVELOPMENT	43	1,44,199.91	1,49,477.76	3.66	19	60,209.34	65,203.96	2 - 77
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	0	0.00	0.00	-
Total		1361	16,78,634.82	20,16,360.99	20.12	296	5,84,127.66	7,46,566.91	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-7

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	98,363.19	1,03,681.73	5.41	13	45,343.81	47,961.39	2 - 144
2	ARUNACHAL PRADESH	30	16,028.42	33,154.93	106.85	2	2,635.83	6,334.96	36 - 111
3	ASSAM	46	28,862.47	39,548.00	37.02	7	7,961.08	13,108.88	8 - 118
4	BIHAR	84	70,606.42	87,437.49	23.84	9	30,348.43	42,176.36	12 - 123
5	GOA	10	4,292.52	4,300.60	0.19	0	0.00	0.00	-
6	GUJARAT	48	44,417.71	53,141.00	19.64	10	15,349.10	22,604.23	3 - 84
7	HARYANA	24	17,887.77	19,800.43	10.69	3	2,099.58	3,297.00	6 - 101
8	HIMACHAL PRADESH	12	14,659.32	25,091.60	71.16	3	6,107.21	10,586.37	29 - 135
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	4	14,387.53	40,381.83	12 - 220
10	KARNATAKA	42	71,151.56	81,641.15	14.74	8	31,995.77	32,776.00	2 - 299
11	KERALA	22	23,243.87	26,990.43	16.12	7	11,682.28	12,624.71	9 - 77
12	MADHYA PRADESH	61	65,252.10	70,966.23	8.76	8	16,946.52	18,632.24	4 - 120
13	MAHARASHTRA	129	1,72,945.28	1,86,576.57	7.88	24	49,492.06	54,803.56	2 - 192
14	MANIPUR	2	944.25	14,025.69	1,385.38	2	944.25	14,025.69	44 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	3	1,051.32	1,051.32	15 - 55
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	21	12,234.55	14,384.55	17.57	4	2,049.11	4,199.11	36 - 60
18	ODISHA	79	81,330.92	91,471.24	12.47	19	27,806.01	31,816.72	3 - 117
19	PUNJAB	31	16,717.41	16,723.14	0.03	4	1,282.24	1,282.24	2 - 16
20	RAJASTHAN	60	44,903.52	47,181.46	5.07	13	19,727.97	20,619.04	3 - 84
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 92
22	TAMIL NADU	68	1,13,886.72	1,30,183.04	14.31	20	78,078.57	85,471.46	1 - 121
23	TRIPURA	9	3,776.07	8,365.85	121.55	2	1,065.34	3,954.00	4 - 72
24	UTTAR PRADESH	100	1,17,454.69	1,21,491.75	3.44	15	29,187.26	30,339.86	3 - 235
25	WEST BENGAL	53	54,028.97	63,055.17	16.71	15	16,054.61	19,160.67	2 - 374
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	23	56,043.88	56,632.51	1.05	6	5,550.12	5,922.91	5 - 37
29	CHHATISGARH	38	67,062.14	69,718.38	3.96	9	29,109.42	31,431.40	24 - 117
30	JHARKHAND	48	45,550.26	47,819.80	4.98	18	24,416.00	26,010.21	9 - 154
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	5	7,719.83	12,781.81	62 - 102
32	TELANGANA	38	29,795.41	34,600.88	16.13	14	17,291.69	18,074.07	3 - 144
33	MULTI STATE	172	3,44,126.91	4,53,016.12	31.64	44	79,775.75	1,19,617.01	1 - 311
Total		1361	16,78,634.82	20,16,360.99	20.12	296	5,84,127.66	7,46,566.91	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to latest schedule Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	4	74,426.00	74,849.00	36 - 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21 - 92
3	COAL	94	90,599.31	90,827.28	0.25	25	10,834.73	10,834.73	0 - 108
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	-
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	-
6	STEEL	28	37,832.11	37,664.82	-0.44	13	28,594.47	28,381.87	2 - 72
7	PETROLEUM	136	2,19,470.50	2,17,989.15	-0.68	8	6,281.44	6,347.13	1 - 57
8	POWER	110	3,37,834.23	3,77,560.50	11.76	36	1,05,882.07	1,23,424.41	1 - 135
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	6	1,689.51	1,729.41	6 - 19
11	RAILWAYS	350	4,99,489.53	6,46,528.15	29.44	61	63,968.60	1,13,225.25	0 - 261
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,816.38	3,64,610.12	1.61	53	41,762.18	46,011.96	2 - 118
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	2	624.39	927.36	29 - 96
14	TELECOMMUNICATIONS	10	28,521.20	28,421.20	-0.35	0	0.00	0.00	-
15	URBAN DEVELOPMENT	43	1,44,398.64	1,49,477.76	3.52	15	44,771.76	45,217.65	2 - 77
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	-
Total		1361	18,16,514.45	20,16,360.99	11.00	226	3,81,013.22	4,53,497.63	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

Extent of cost overrun in projects with respect to latest schedule RS.150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	7.45
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	59.41
3	COAL	94	90,599.31	90,827.28	0.25	2	17,496.40	17,724.37	1.30
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0.00
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0.00
6	STEEL	28	37,832.11	37,664.82	-0.44	3	1,586.97	1,777.68	12.02
7	PETROLEUM	136	2,19,470.50	2,17,989.15	-0.68	7	6,531.66	7,870.53	20.50
8	POWER	110	3,37,834.23	3,77,560.50	11.76	22	1,28,670.18	1,68,396.45	30.87
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	6	1,665.23	1,714.64	2.97
11	RAILWAYS	350	4,99,489.53	6,46,528.15	29.44	185	1,35,567.02	2,92,594.96	115.83
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,816.38	3,64,610.12	1.61	31	22,821.18	29,559.57	29.53
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	3	774.39	1,545.44	99.57
14	TELECOMMUNICATIONS	10	28,521.20	28,421.20	-0.35	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	43	1,44,398.64	1,49,477.76	3.52	6	21,121.93	26,201.05	24.05
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	2	454.00	461.66	1.69
Total		1361	18,16,514.45	20,16,360.99	11.00	271	3,44,708.03	5,58,768.51	62.10

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of time & cost overrun in projects with respect to latest schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	102- 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 92
3	COAL	94	90,599.31	90,827.28	0.25	0	0.00	0.00	0- 0
4	FERTILISERS	6	1,793.57	1,793.57	0.00	0	0.00	0.00	0- 0
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	28	37,832.11	37,664.82	-0.44	1	343.00	488.40	29- 29
7	PETROLEUM	136	2,19,470.50	2,17,989.15	-0.68	2	959.62	1,153.09	17- 24
8	POWER	110	3,37,834.23	3,77,560.50	11.76	11	41,247.96	58,790.30	12- 135
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	2	674.48	714.38	6- 16
11	RAILWAYS	350	4,99,489.53	6,46,528.15	29.44	32	27,710.81	78,170.28	4- 261
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,816.38	3,64,610.12	1.61	10	11,003.57	15,253.86	2- 91
13	SHIPPING AND PORTS	5	3,459.79	4,230.74	22.28	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	10	28,521.20	28,421.20	-0.35	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	43	1,44,398.64	1,49,477.76	3.52	4	2,257.93	2,703.82	5- 49
16	DEFENCE PRODUCTION	2	454.00	461.66	1.69	0	0.00	0.00	0- 0
Total		1361	18,16,514.45	20,16,360.99	11.00	66	90,864.83	1,65,038.45	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-11

Extent of time & cost overrun in projects with respect to original schedule Rs. 150 Crore and above

(All Cost/ Expenditure in Rs. crore)

						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	CIVIL AVIATION	2	624.07	994.86	59.41	2	624.07	994.86	21- 92
3	COAL	94	91,364.09	90,827.28	-0.59	4	983.19	1,747.25	60- 144
4	FERTILISERS	6	1,781.92	1,793.57	0.65	1	197.79	209.44	29- 29
5	MINES	4	6,912.00	6,912.00	0.00	0	0.00	0.00	0- 0
6	STEEL	28	37,451.14	37,664.82	0.57	1	343.00	488.40	29- 29
7	PETROLEUM	136	2,17,011.11	2,17,989.15	0.45	9	13,085.77	15,952.36	4- 70
8	POWER	110	3,13,586.68	3,77,560.50	20.40	38	1,39,706.95	1,86,177.37	6- 135
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	22	8,611.12	8,658.88	0.55	2	674.48	714.38	6- 16
11	RAILWAYS	350	4,07,092.54	6,46,528.15	58.82	44	35,081.23	1,20,230.56	3- 324
12	ROAD TRANSPORT AND HIGHWAYS	543	3,58,175.11	3,64,610.12	1.80	13	11,665.41	16,109.34	2- 91
13	SHIPPING AND PORTS	5	3,788.29	4,230.74	11.68	1	366.39	669.46	96- 96
14	TELECOMMUNICATIONS	10	17,191.20	28,421.20	65.32	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	43	1,44,199.91	1,49,477.76	3.66	5	16,762.37	21,756.99	5- 70
16	DEFENCE PRODUCTION	2	453.64	461.66	1.77	0	0.00	0.00	0- 0
Total		1361	16,78,634.82	20,16,360.99	20.12	123	2,47,775.65	4,12,394.41	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	61	98,363.19	1,03,681.73	5.41	5	2,692.12	5,880.66	2 - 144
2	ARUNACHAL PRADESH	30	16,028.42	33,154.93	106.85	2	2,635.83	6,334.96	36 - 111
3	ASSAM	46	28,862.47	39,548.00	37.02	3	4,778.29	10,012.35	12 - 84
4	BIHAR	84	70,606.42	87,437.49	23.84	6	28,243.43	40,071.36	12 - 123
5	GOA	10	4,292.52	4,300.60	0.19	0	0.00	0.00	-
6	GUJARAT	48	44,417.71	53,141.00	19.64	4	13,607.00	20,998.45	36 - 84
7	HARYANA	24	17,887.77	19,800.43	10.69	2	1,613.58	2,811.00	6 - 91
8	HIMACHAL PRADESH	12	14,659.32	25,091.60	71.16	1	3,919.59	8,398.75	135 - 135
9	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	12 - 220
10	KARNATAKA	42	71,151.56	81,641.15	14.74	2	1,824.74	2,611.00	2 - 3
11	KERALA	22	23,243.87	26,990.43	16.12	4	5,718.26	6,660.69	9 - 17
12	MADHYA PRADESH	61	65,252.10	70,966.23	8.76	3	13,416.59	15,102.31	21 - 120
13	MAHARASHTRA	129	1,72,945.28	1,86,576.57	7.88	11	16,027.93	21,734.75	2 - 192
14	MANIPUR	2	944.25	14,025.69	1,385.38	1	727.56	13,809.00	108 - 108
15	MEGHALAYA	6	7,108.02	9,025.00	26.97	0	0.00	0.00	-
16	MIZORAM	4	1,632.48	5,613.14	243.84	1	619.34	4,600.00	71 - 71
17	NAGALAND	21	12,234.55	14,384.55	17.57	1	850.00	3,000.00	60 - 60
18	ODISHA	79	81,330.92	91,471.24	12.47	5	14,184.29	18,195.30	3 - 117
19	PUNJAB	31	16,717.41	16,723.14	0.03	0	0.00	0.00	-
20	RAJASTHAN	60	44,903.52	47,181.46	5.07	2	1,482.93	2,374.00	60 - 60
21	SIKKIM	6	2,537.08	5,585.45	120.15	2	1,648.94	4,638.22	51 - 92
22	TAMIL NADU	68	1,13,886.72	1,30,183.04	14.31	6	22,639.88	31,123.98	24 - 121
23	TRIPURA	9	3,776.07	8,365.85	121.55	2	1,065.34	3,954.00	4 - 72
24	UTTAR PRADESH	100	1,17,454.69	1,21,491.75	3.44	4	1,944.47	3,292.83	12 - 235
25	WEST BENGAL	53	54,028.97	63,055.17	16.71	6	7,876.96	10,833.72	12 - 324
26	A & N ISLANDS	6	1,889.87	2,016.59	6.71	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	23	56,043.88	56,632.51	1.05	1	1,219.21	1,592.00	5 - 5
29	CHHATISGARH	38	67,062.14	69,718.38	3.96	4	12,627.33	14,949.31	24 - 117
30	JHARKHAND	48	45,550.26	47,819.80	4.98	5	15,986.54	17,580.75	20 - 154
31	UTTARAKHAND	17	18,576.59	36,046.09	94.04	4	7,241.32	12,303.81	63 - 102
32	TELANGANA	38	29,795.41	34,600.88	16.13	5	2,730.04	3,648.31	33 - 144
33	MULTI STATE	172	3,44,126.91	4,53,016.12	31.64	28	55,851.12	95,158.86	4 - 261
Total		1361	16,78,634.82	20,16,360.99	20.12	123	2,47,775.65	4,12,394.41	

TABLE-13

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	140	2
2	ROAD TRANSPORT AND HIGHWAYS	111	3
3	POWER	58	7
4	PETROLEUM	49	0
5	COAL	13	0
6	URBAN DEVELOPMENT	11	0
7	STEEL	8	1
8	ATOMIC ENERGY	4	1
9	HEAVY INDUSTRY	2	0
10	TELECOMMUNICATIONS	2	0
11	MINES	1	0
12	SHIPPING AND PORTS	1	0
	Total	400	14

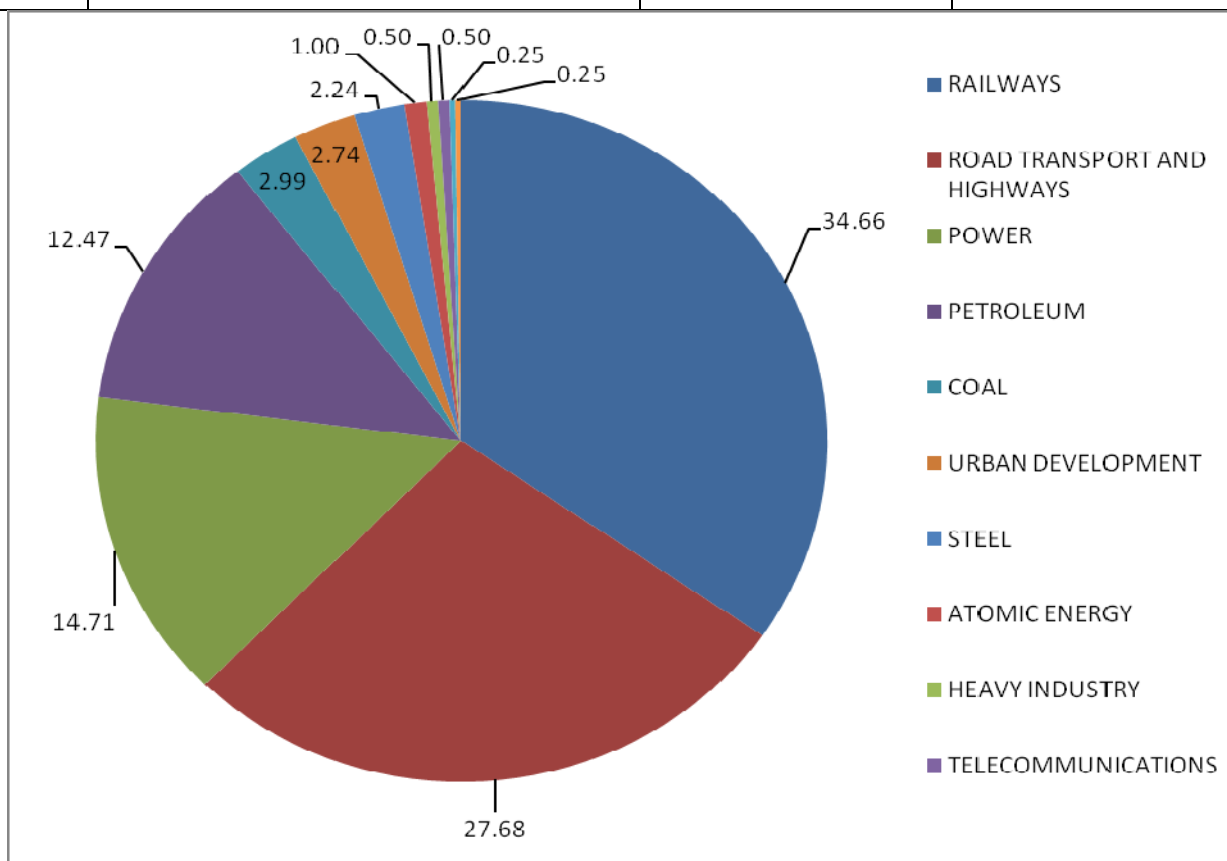


TABLE-14

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	401
No of Projects Completed/Dropped/Frozen in Current Month	6
No of Projects added in Current Month	3
No of Projects in Current Month	400

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	131 (32.75%)	5 (1.25%)	120(30.00%)	19 (4.75%)	125(31.25%)	400
Latest Approved (Date)	100 (25.00%)	5 (1.25%)	163(40.75%)	7 (1.75%)	125(1.25%)	400

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	320	10,78,542.36	12,54,385.27	4,44,231.81	35.40	1,75,842.91	16.30
Project with Revision in Cost	80	3,41,140.13	3,46,762.25	1,89,629.67	54.70	5,622.12	1.60
Total	400	14,19,682.49	16,01,147.52	6,33,861.48	39.59	1,81,465.03	12.78
Original Cost of All Projects							
Original Cost	400	12,85,898.53	16,01,147.52	6,33,861.48	39.59	3,15,248.99	24.52

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	131	5,19,599.61	6,75,859.00	3,69,127.62	54.60	1,56,259.39	30.10
Latest Approved (RCE)	100	3,29,357.50	3,99,069.36	2,10,842.68	52.80	69,711.86	21.20
Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	15	56,411.53	95,260.78	73,214.75	76.90	38,849.25	68.90
Total	15	56,411.53	95,260.78	73,214.75	76.86	38,849.25	68.87

TABLE-15

Extent of cost overrun in projects with respect to original schedule(Sector Wise) RS.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	51.70
2	COAL	13	57,659.35	57,660.15	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	8	30,899.22	30,885.68	-0.04	1	768.88	1,113.34	44.80
5	PETROLEUM	49	1,80,467.45	1,82,685.00	1.23	8	16,553.75	20,828.52	25.82
6	POWER	58	2,93,355.36	3,55,901.85	21.32	32	1,73,171.13	2,35,717.62	36.12
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	140	3,29,327.44	5,48,251.94	66.48	101	1,28,638.27	3,51,990.72	173.63
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	15	17,694.40	23,193.27	31.08
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	3	20,083.21	25,089.23	24.93
Total		400	12,85,898.53	16,01,147.52	24.52	165	4,04,149.64	7,26,341.80	79.72

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-16

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 1000 Crore and above
(All Cost/ Expenditure in Rs. Crore)

						Projects with cost overrun [^]			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	18	84,439.97	88,803.63	5.17	6	7,503.36	12,594.02	67.85
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	2	8,782.23	25,676.30	192.37
3	ASSAM	9	16,479.54	26,098.26	58.37	4	6,946.70	16,702.00	140.43
4	BIHAR	14	39,632.94	54,375.80	37.20	7	28,983.86	43,726.72	50.87
5	GUJARAT	11	27,846.79	36,035.56	29.41	4	15,624.61	23,813.38	52.41
6	HARYANA	5	9,163.39	10,343.39	12.88	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	12,226.08	22,658.36	85.33	2	4,966.47	15,398.75	210.05
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	606.15
9	KARNATAKA	18	59,444.23	69,221.30	16.45	10	21,327.46	31,863.53	49.40
10	KERALA	7	16,769.19	20,224.38	20.60	3	6,038.29	9,493.48	57.22
11	MADHYA PRADESH	16	40,412.79	46,883.37	16.01	8	26,682.46	33,153.04	24.25
12	MAHARASHTRA	43	1,37,969.80	1,49,898.03	8.65	19	30,746.55	45,994.52	49.59
13	MANIPUR	1	727.56	13,809.00	1797.99	1	727.56	13,809.00	1797.99
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	1	4,083.02	6,000.00	46.95
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	642.73
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	252.94
17	ODISHA	25	57,615.98	66,824.19	15.98	7	16,265.64	25,473.85	56.61
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	11	23,282.41	24,680.35	6.00	4	3,178.64	4,576.58	43.98
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	24	95,076.44	1,10,140.00	15.84	11	25,349.22	40,412.78	59.42
22	TRIPURA	3	2,129.35	6,309.31	196.30	3	2,129.35	6,309.31	196.30
23	UTTAR PRADESH	34	87,489.74	91,102.74	4.13	8	24,836.64	28,904.22	16.38
24	WEST BENGAL	21	41,715.32	48,068.32	15.23	7	13,355.58	19,708.59	47.57
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	6	49,710.73	50,258.75	1.10	2	5,483.21	6,031.23	9.99
27	CHHATISGARH	10	55,666.21	57,785.29	3.81	3	12,976.57	15,095.65	16.33
28	JHARKHAND	10	32,030.41	33,367.76	4.18	3	19,504.59	20,841.94	6.86
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	5	12,949.36	30,054.88	132.10
30	TELANGANA	7	19,333.53	23,093.25	19.45	4	2,881.59	6,641.31	130.47
31	MULTI STATE	72	3,04,469.72	4,08,357.10	34.12	35	94,621.45	1,99,811.32	111.17
Total		400	12,85,898.53	16,01,147.52	24.52	165	4,04,149.64	7,26,341.80	79.72

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of time overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	4	67,120.00	74,849.00	36 - 102
2	COAL	13	57,659.35	57,660.15	0.00	4	9,323.71	9,323.71	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	8	30,899.22	30,885.68	-0.04	6	25,381.34	25,023.34	4 - 43
5	PETROLEUM	49	1,80,467.45	1,82,685.00	1.23	13	70,580.38	71,987.15	4 - 74
6	POWER	58	2,93,355.36	3,55,901.85	21.32	41	2,05,616.70	2,50,659.96	1 - 135
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	140	3,29,327.44	5,48,251.94	66.48	37	46,210.30	1,28,237.58	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	19	24,393.04	28,643.33	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	5	56,086.14	60,916.93	5 - 36
Total		400	12,85,898.53	16,01,147.52	24.52	131	5,19,599.61	6,75,859.00	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-18

Extent of time overrun in projects with respect to original schedule(State Wise) Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	84,439.97	88,803.63	5.17	7	42,988.04	45,672.68	2 - 144
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	9	16,479.54	26,098.26	58.37	3	7,040.50	12,060.89	12 - 84
4	BIHAR	14	39,632.94	54,375.80	37.20	4	27,310.57	38,969.93	12 - 123
5	GUJARAT	11	27,846.79	36,035.56	29.41	2	12,968.10	19,817.87	54 - 71
6	HARYANA	5	9,163.39	10,343.39	12.88	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	12,226.08	22,658.36	85.33	2	5,836.38	10,315.54	29 - 135
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	4	14,387.53	40,381.83	12 - 220
9	KARNATAKA	18	59,444.23	69,221.30	16.45	4	29,884.89	30,671.15	2 - 30
10	KERALA	7	16,769.19	20,224.38	20.60	2	9,770.08	10,427.75	9 - 29
11	MADHYA PRADESH	16	40,412.79	46,883.37	16.01	5	16,179.49	17,865.21	4 - 120
12	MAHARASHTRA	43	1,37,969.80	1,49,898.03	8.65	14	45,624.99	50,360.98	2 - 192
13	MANIPUR	1	727.56	13,809.00	1,797.99	1	727.56	13,809.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	66,824.19	15.98	6	22,165.49	25,510.34	3 - 82
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	11	23,282.41	24,680.35	6.00	4	15,476.63	16,367.70	48 - 84
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	24	95,076.44	1,10,140.00	15.84	9	71,771.64	80,008.19	18 - 121
22	TRIPURA	3	2,129.35	6,309.31	196.30	1	813.34	3,374.00	72 - 72
23	UTTAR PRADESH	34	87,489.74	91,102.74	4.13	7	25,982.50	27,181.34	3 - 235
24	WEST BENGAL	21	41,715.32	48,068.32	15.23	7	13,711.20	15,799.73	11 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	6	49,710.73	50,258.75	1.10	3	4,167.73	4,540.52	5 - 37
27	CHHATISGARH	10	55,666.21	57,785.29	3.81	3	27,675.00	29,459.82	24 - 111
28	JHARKHAND	10	32,030.41	33,367.76	4.18	6	20,409.29	21,432.60	9 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	63 - 102
30	TELANGANA	7	19,333.53	23,093.25	19.45	3	13,289.54	13,566.94	3 - 33
31	MULTI STATE	72	3,04,469.72	4,08,357.10	34.12	25	71,792.26	1,10,232.22	1 - 311
Total		400	12,85,898.53	16,01,147.52	24.52	131	5,19,599.61	6,75,859.00	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	4	74,426.00	74,849.00	36 - 102
2	COAL	13	57,659.35	57,660.15	0.00	3	3,416.60	3,416.60	12 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	8	31,201.31	30,885.68	-1.01	6	25,381.34	25,023.34	4 - 43
5	PETROLEUM	49	1,83,017.30	1,82,685.00	-0.18	2	3,995.65	3,995.65	4 - 57
6	POWER	58	3,16,429.11	3,55,901.85	12.47	24	1,01,648.62	1,18,937.60	1 - 135
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,554.00	1,554.00	37 - 37
8	RAILWAYS	140	4,18,549.71	5,48,251.94	30.99	37	53,056.11	1,00,790.91	0 - 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	19	24,393.04	28,643.33	2 - 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	26,775.17	26,675.17	-0.37	0	0.00	0.00	-
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	4	41,486.14	41,858.93	5 - 29
Total		400	14,19,682.49	16,01,147.52	12.78	100	3,29,357.50	3,99,069.36	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

Extent of cost overrun in projects with respect to latest schedule RS. 1000 Crore and above
(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	7.45
2	COAL	13	57,659.35	57,660.15	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	8	31,201.31	30,885.68	-1.01	1	1,070.97	1,113.34	3.96
5	PETROLEUM	49	1,83,017.30	1,82,685.00	-0.18	3	5,055.04	6,140.19	21.47
6	POWER	58	3,16,429.11	3,55,901.85	12.47	19	1,27,154.88	1,66,627.62	31.04
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	140	4,18,549.71	5,48,251.94	30.99	81	1,01,446.64	2,38,522.73	135.12
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	15	17,694.40	23,193.27	31.08
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	26,775.17	26,675.17	-0.37	0	0.00	0.00	0.00
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	3	20,083.21	25,089.23	24.93
Total		400	14,19,682.49	16,01,147.52	12.78	125	2,97,137.14	4,87,851.48	64.18

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	74,426.00	74,849.00	0.57	1	5,677.00	6,100.00	102- 102
2	COAL	13	57,659.35	57,660.15	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	8	31,201.31	30,885.68	-1.01	0	0.00	0.00	0- 0
5	PETROLEUM	49	1,83,017.30	1,82,685.00	-0.18	0	0.00	0.00	0- 0
6	POWER	58	3,16,429.11	3,55,901.85	12.47	9	40,522.79	57,811.77	12- 135
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	140	4,18,549.71	5,48,251.94	30.99	21	23,916.60	72,707.76	12- 261
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	10	11,003.57	15,253.86	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	26,775.17	26,675.17	-0.37	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	1	1,219.21	1,592.00	5- 5
Total		400	14,19,682.49	16,01,147.52	12.78	42	82,339.17	1,53,465.39	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule Rs.1000 Crore and above (All Cost/ Expenditure in Rs. Crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	74,849.00	11.52	2	14,951.00	22,680.00	54- 102
2	COAL	13	57,659.35	57,660.15	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	8	30,899.22	30,885.68	-0.04	0	0.00	0.00	0- 0
5	PETROLEUM	49	1,80,467.45	1,82,685.00	1.23	5	11,613.40	13,745.52	4- 67
6	POWER	58	2,93,355.36	3,55,901.85	21.32	26	1,35,663.13	1,80,706.39	10- 135
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	140	3,29,327.44	5,48,251.94	66.48	28	29,554.49	1,11,048.26	3- 324
9	ROAD TRANSPORT AND HIGHWAYS	111	1,64,922.00	1,70,420.87	3.33	10	11,003.57	15,253.86	2- 91
10	SHIPPING AND PORTS	1	2,427.40	2,427.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	11	1,35,463.14	1,40,469.16	3.70	2	15,819.21	20,650.00	5- 36
Total		400	12,85,898.53	16,01,147.52	24.52	74	2,31,938.80	3,88,748.03	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	18	84,439.97	88,803.63	5.17	3	2,114.62	5,157.26	2 - 144
2	ARUNACHAL PRADESH	3	10,035.33	26,929.40	168.35	1	2,496.90	6,179.96	111 - 111
3	ASSAM	9	16,479.54	26,098.26	58.37	2	4,575.35	9,682.00	12 - 84
4	BIHAR	14	39,632.94	54,375.80	37.20	4	27,310.57	38,969.93	12 - 123
5	GUJARAT	11	27,846.79	36,035.56	29.41	2	12,968.10	19,817.87	54 - 71
6	HARYANA	5	9,163.39	10,343.39	12.88	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	12,226.08	22,658.36	85.33	1	3,919.59	8,398.75	135 - 135
8	JAMMU AND KASHMIR	10	25,238.37	51,232.67	103.00	2	4,288.41	30,282.71	12 - 220
9	KARNATAKA	18	59,444.23	69,221.30	16.45	2	1,824.74	2,611.00	2 - 3
10	KERALA	7	16,769.19	20,224.38	20.60	1	4,588.29	5,245.96	9 - 9
11	MADHYA PRADESH	16	40,412.79	46,883.37	16.01	3	13,416.59	15,102.31	21 - 120
12	MAHARASHTRA	43	1,37,969.80	1,49,898.03	8.65	8	14,986.06	20,117.37	2 - 192
13	MANIPUR	1	727.56	13,809.00	1,797.99	1	727.56	13,809.00	108 - 108
14	MEGHALAYA	2	5,577.50	7,494.48	34.37	0	0.00	0.00	-
15	MIZORAM	1	619.34	4,600.00	642.73	1	619.34	4,600.00	71 - 71
16	NAGALAND	3	6,420.00	8,570.00	33.49	1	850.00	3,000.00	60 - 60
17	ODISHA	25	57,615.98	66,824.19	15.98	3	13,526.45	16,871.30	3 - 82
18	PUNJAB	2	2,557.95	2,557.95	0.00	0	0.00	0.00	-
19	RAJASTHAN	11	23,282.41	24,680.35	6.00	2	1,482.93	2,374.00	60 - 60
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	24	95,076.44	1,10,140.00	15.84	4	21,811.42	30,047.97	36 - 121
22	TRIPURA	3	2,129.35	6,309.31	196.30	1	813.34	3,374.00	72 - 72
23	UTTAR PRADESH	34	87,489.74	91,102.74	4.13	1	609.04	1,807.88	235 - 235
24	WEST BENGAL	21	41,715.32	48,068.32	15.23	3	7,277.80	9,366.34	108 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	6	49,710.73	50,258.75	1.10	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	10	55,666.21	57,785.29	3.81	2	12,150.00	13,934.82	24 - 111
28	JHARKHAND	10	32,030.41	33,367.76	4.18	2	15,266.63	16,289.94	20 - 99
29	UTTARAKHAND	6	14,392.36	31,497.88	118.85	3	7,127.06	12,037.81	63 - 102
30	TELANGANA	7	19,333.53	23,093.25	19.45	1	1,266.60	1,544.00	33 - 33
31	MULTI STATE	72	3,04,469.72	4,08,357.10	34.12	17	52,254.72	90,161.16	4 - 261
Total		400	12,85,898.53	16,01,147.52	24.52	74	2,31,938.80	3,88,748.03	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

<u>List of projects completed/dropped/Frozen during current month</u> Rs.150 Crore and above (All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	PIPELINE REPLACEMENT PROJECT, AHMEDABAD	09/2011	202.25	07/2016	160.16	07/2018	130.21
2	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS	05/2013	4,124.35	04/2016	5,725.50	07/2018	5,347.49
3	DEVELOPMENT OF C-26 CLUSTER FIELDS	03/2012	2,592.17	05/2014	2,592.17	07/2018	2,049.26
4	MH NORTH REDEVELOPMENT PHASE III	06/2014	5,706.47	05/2017	5,813.25	07/2018	5,724.54
5	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR	10/2011	200.69	07/2014	200.69	07/2018	109.58
6	SONAMURA GGS AND PIPELINE PROJECT (PART OF OVERALL SCHEME TO PRODUCE 5.1 MMMCMD GAS AT TRIPURA A	05/2016	215.38	06/2017	215.38	07/2018	198.98
7	CONSTRUCTION OF THREE ETPS, MEHSANA	03/2012	260.74	11/2014	260.74	07/2018	83.44
	<u>POWER</u>						
8	BOKARO THERMAL POWER STATION-A	08/2006	2,313.00	12/2011	4,366.64	N.A.	3,965.00
9	RAGHUNATHPUR THERMAL POWER STATION PHASE-I	04/2007	4,122.00	02/2011	9,142.58	N.A.	8,479.00
	<u>STEEL</u>						
10	EXPANSION OF BHILAI STEEL PLANT	08/2010	17,265.00	03/2013	17,265.00	06/2018	19,855.23

TABLE-25

List of projects added Rs.150 Crore and above					(July 2018)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	413.84	3/2019	413.84	3/2019
2	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	1,255.17	3/2022	1,255.17	3/2022
	<u>PETROLEUM</u>					
3	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	3,712.00	9/2022	3,712.00	9/2022
4	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	676.00	12/2021	676.00	12/2021
5	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	588.20	/	588.20	-
6	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	766.37	12/2019	766.37	12/2019
7	BARAUNI-GUWAHATI PIPELINE	6/2018	3,308.00	12/2021	3,308.00	12/2021
	<u>RAILWAYS</u>					
8	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	808.85	8/2022	808.85	8/2022

TABLE-26

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		4125	
Achieved up to month		2212	

TABLE-27

List of projects reporting additional delayed Rs.150 Crore and above							(July 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) BHAVNI	3,492.00	6,100.00	09/2010	10/2018	03/2019	5
	<u>COAL</u>						
2	BASUNDHARA (WEST) OC EXTN(7.00 MTY) MCL	479.15	479.15	03/2019	03/2019	03/2021	24
3	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) MCL	337.66	337.66	03/2019	03/2019	03/2021	24
	<u>STEEL</u>						
4	NMDC INTEGRATED STEEL PLANT NMDC	15,525.00	15,525.00	05/2015	10/2018	12/2018	2
	<u>PETROLEUM</u>						
5	HALDIA LPG IMPORT FACILITY BPCL	694.00	694.00	10/2018	10/2018	12/2018	2
6	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE GAIL	327.78	200.00	04/2018	10/2018	12/2018	2
	<u>POWER</u>						
7	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	8,150.00	09/2011	08/2018	09/2018	1
8	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C PGCIL	514.20	703.10	06/2015	07/2018	08/2018	1
9	WESTERN REGION STRENGTHENING SCHEME-XVI PGCIL	150.99	150.99	07/2018	07/2018	08/2018	1
10	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) PGCIL Central Sector Projects	2,525.00	2,525.00	11/2017	06/2018	07/2018	1
11	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B PGCIL Central Sector Projects	2,225.00	2,225.00	01/2018	06/2018	07/2018	1
12	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) PGCIL	771.00	1,642.00	02/2013	09/2018	10/2018	1
13	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B PGCIL	3,705.61	3,705.61	04/2018	10/2018	12/2018	2
14	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,187.32	11/2008	09/2018	12/2018	3


List of projects reporting additional delayed Rs.150 Crore and above							(July 2018)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
15	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX PGCIL	539.82	539.82	06/2016	09/2018	12/2018	3
16	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	13,731.26	01/2018	01/2020	05/2020	4
17	KAMENG HYDROELECTRIC PROJECT (NEEPCO) NEEPCO	2,496.90	6,179.96	12/2009	10/2018	03/2019	5
18	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT PGCIL Central Sector Projects	175.64	175.64	09/2018	09/2018	06/2019	9
	<u>HEALTH AND FAMILY WELFARE</u>						
19	NEIGRIHMS SHILLONG MEGHALYA HSCC	363.99	363.99	05/2018	08/2019	09/2019	1
	<u>RAILWAYS</u>						
20	MANDHANA - BRAHMAWART NEW LINE PROJECT. NER	609.04	1,807.88	04/1999	10/2018	11/2018	1
21	ROURKELA JHARSUGUDA THIRD LINE 101 KM SER	969.83	969.83	03/2020	03/2020	06/2020	3
22	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR NR	2,500.00	27,949.00	11/2002	12/2018	03/2021	27
23	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO SER	524.43	939.00	12/2021	12/2021	12/2024	36
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
24	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) NHAI	1,030.44	1,065.51	03/2020	03/2020	05/2020	2
25	FOUR LANNING OF TULJAPUR-AUSA SECTION NHAI	904.16	904.16	02/2020	02/2020	05/2020	3
26	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,423.96	11/2018	11/2018	03/2019	4
27	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) NHAI	988.34	1,043.28	03/2020	03/2020	08/2020	5
28	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH NHAI Central Sector Projects	641.17	641.17	07/2016	07/2018	04/2019	9
	<u>TELECOMMUNICATIONS</u>						
29	GUJARAT ACCESS (LOT 1) BSNL Central Sector Projects	171.54	171.54	05/2018	07/2018	08/2018	1

List of projects reporting additional delayed Rs.150 Crore and above						(July 2018)	
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	URBAN DEVELOPMENT						
30	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM CPWD	332.72	342.00	09/2016	08/2018	09/2018	1
31	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY CPWD EPC	164.00	164.00	11/2018	07/2018	09/2018	2
32	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI CPWD	223.37	223.37	07/2020	07/2020	09/2020	2


TABLE-28

<u>Sector wise analysis of projects Rs.150 Crore and above</u>					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	744,26.00	74,849.00	36,056.69
CIVIL AVIATION	2	624.07	6,24.07	994.86	632.48
COAL	94	91,364.09	905,99.31	90,827.28	27,126.67
FERTILISERS	6	1,781.92	17,93.57	1,793.57	598.32
MINES	4	6,912.00	69,12.00	6,912.00	426.27
STEEL	28	37,451.14	378,32.11	37,664.82	27,402.32
PETROLEUM	136	2,17,011.11	2,194,70.50	2,17,989.15	61,469.73
POWER	110	3,13,586.68	3,378,34.23	3,77,560.50	2,32,240.73
HEAVY INDUSTRY	2	3,272.00	32,72.00	5,381.30	2,450.86
HEALTH AND FAMILY WELFARE	22	8,611.12	86,11.12	8,658.88	2,979.18
RAILWAYS	350	4,07,092.54	4,994,89.53	6,46,528.15	1,63,916.10
ROAD TRANSPORT AND HIGHWAYS	543	3,58,175.11	3,588,16.38	3,64,610.12	1,36,649.82
SHIPPING AND PORTS	5	3,788.29	34,59.79	4,230.74	1,662.35
TELECOMMUNICATIONS	10	17,191.20	285,21.20	28,421.20	8,980.63
URBAN DEVELOPMENT	43	1,44,199.91	1,443,98.64	1,49,477.76	65,471.13
DEFENCE PRODUCTION	2	453.64	4,54.00	461.66	123.65
Grand total	1361	16,78,634.82	18,16,514.45	20,16,360.99	7,68,186.93

Graphical Presentation of All Projects w.r.t. Original Schedule

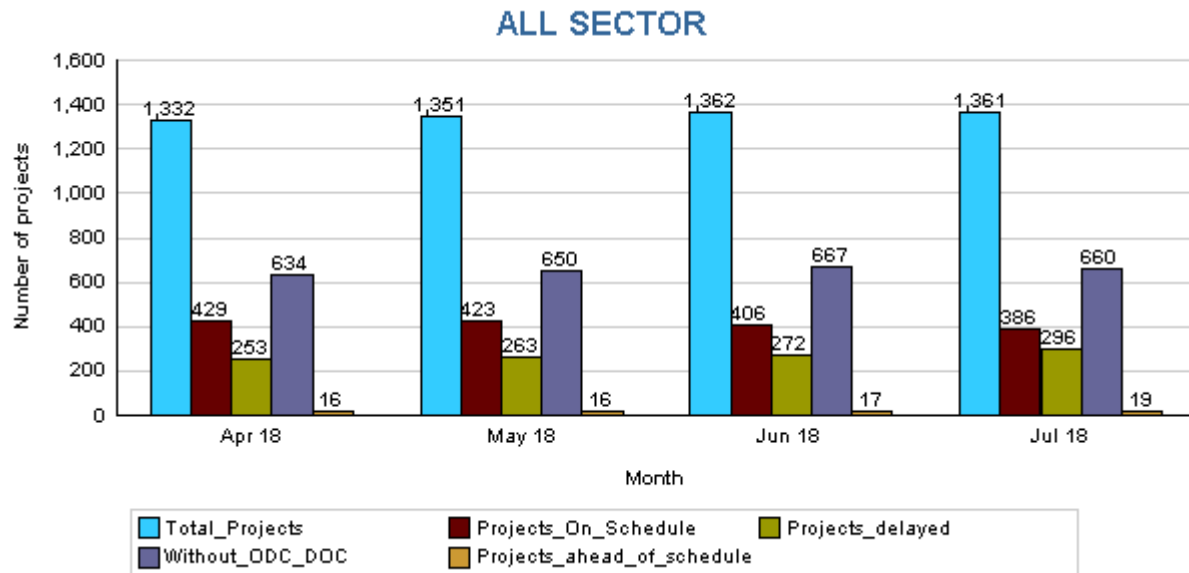


Break-up of 296 Delayed projects in July 2018

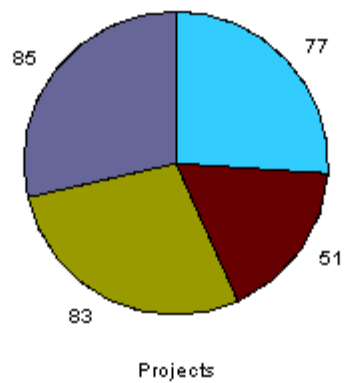


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

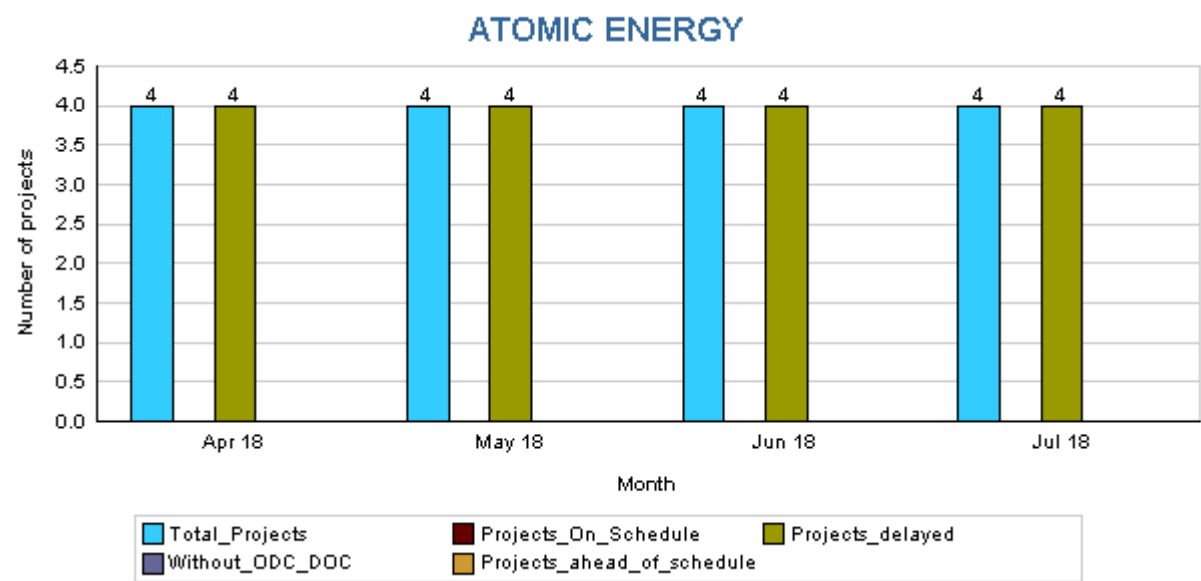


Break-up of 4 Delayed projects in July 2018

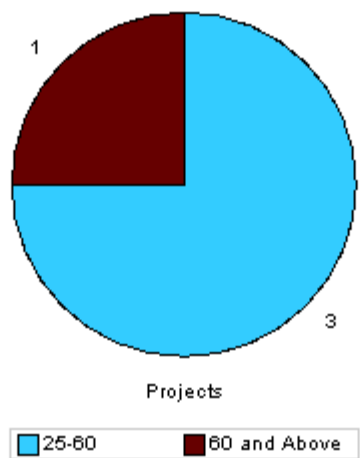


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

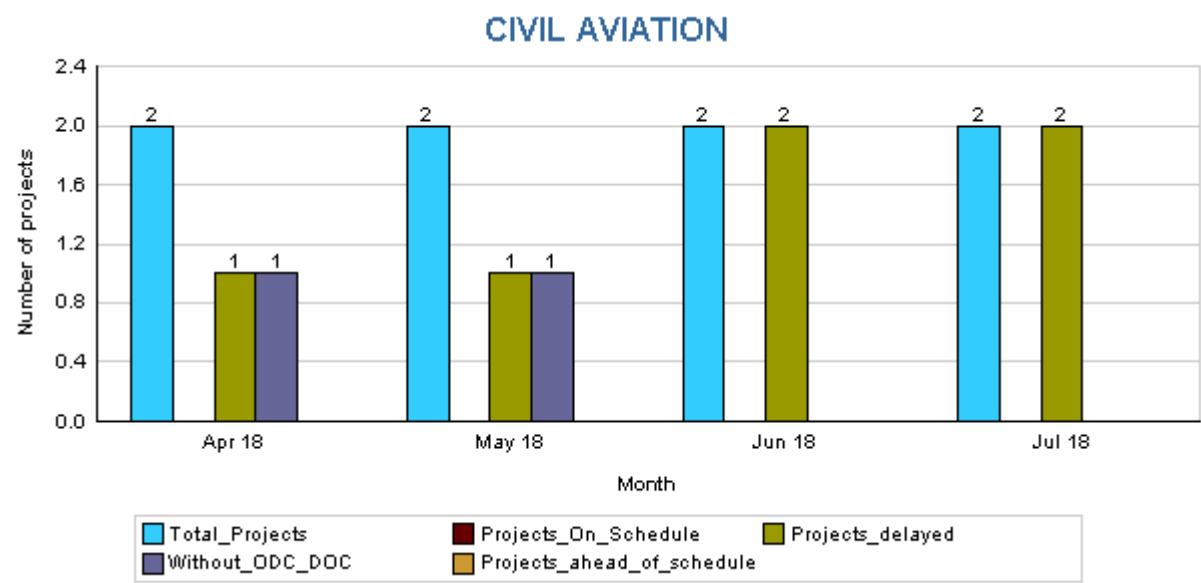


Break-up of 2 Delayed projects in July 2018

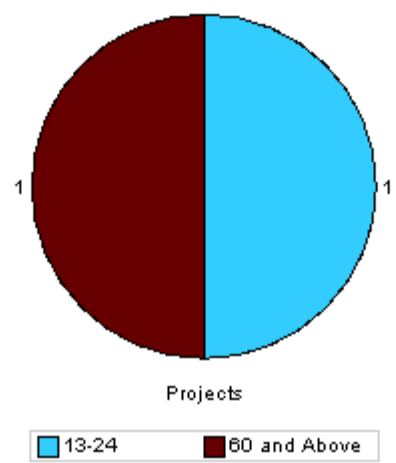


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

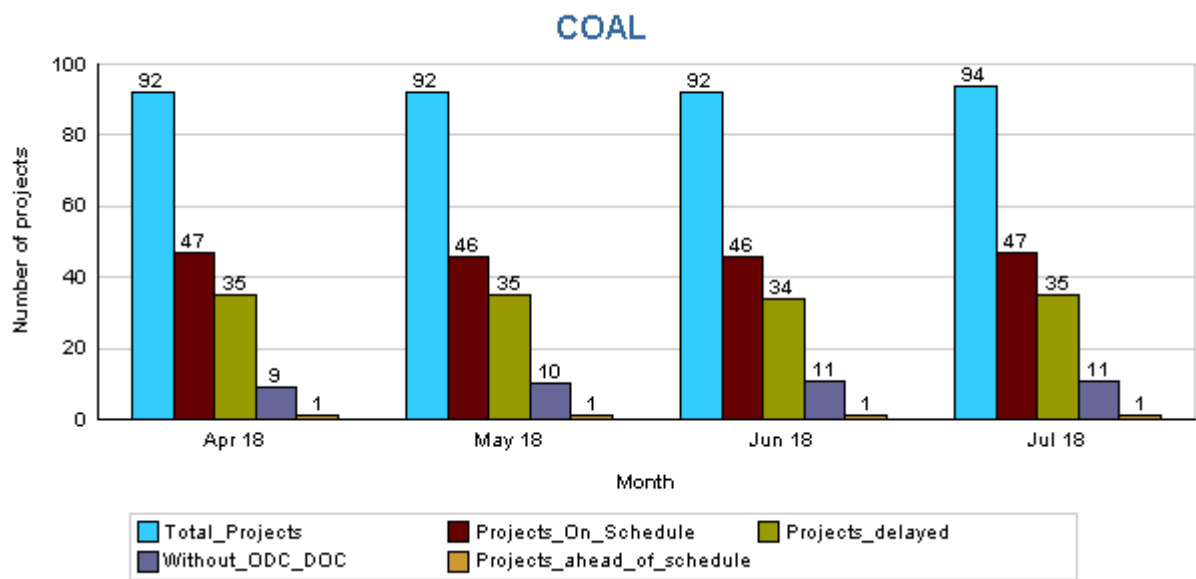


Break-up of 35 Delayed projects in July 2018

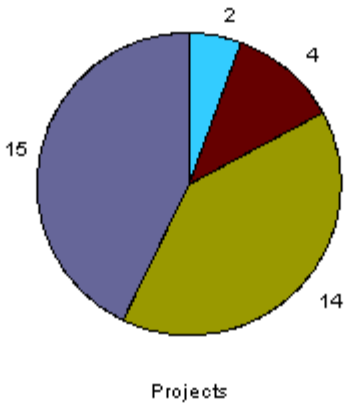


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

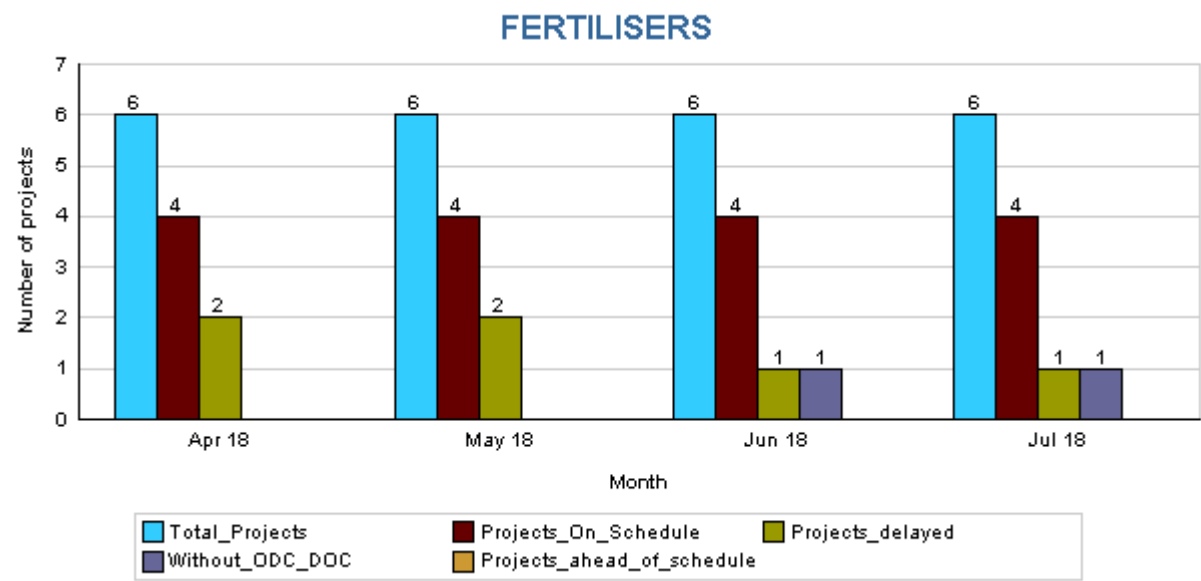


Break-up of 1 Delayed projects in July 2018



Delay in Months


25-60

Graphical Presentation of All Projects w.r.t. Original Schedule

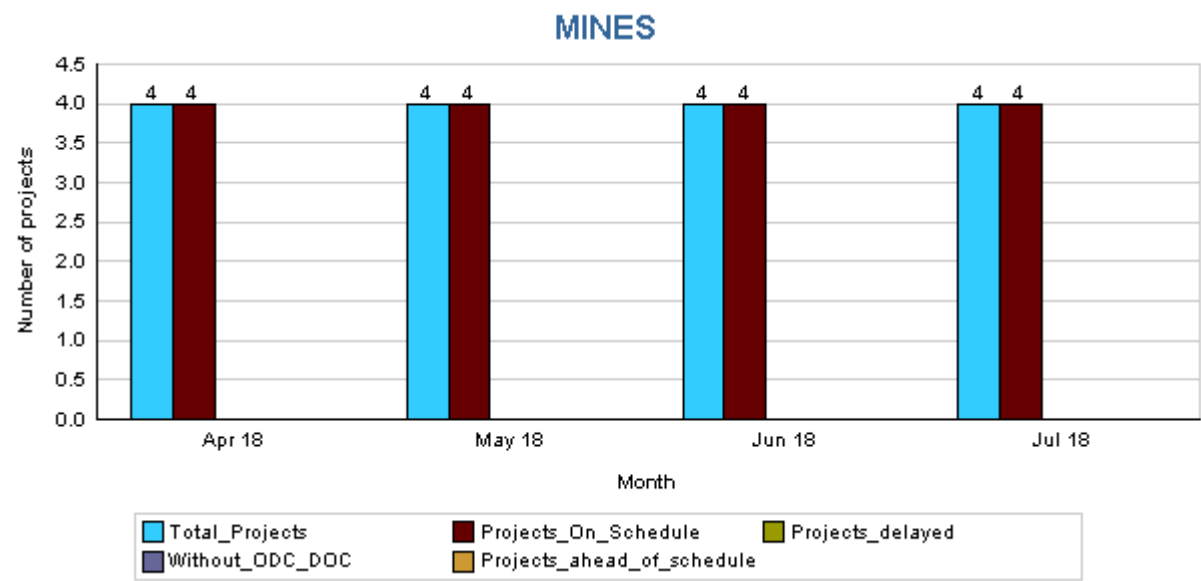


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

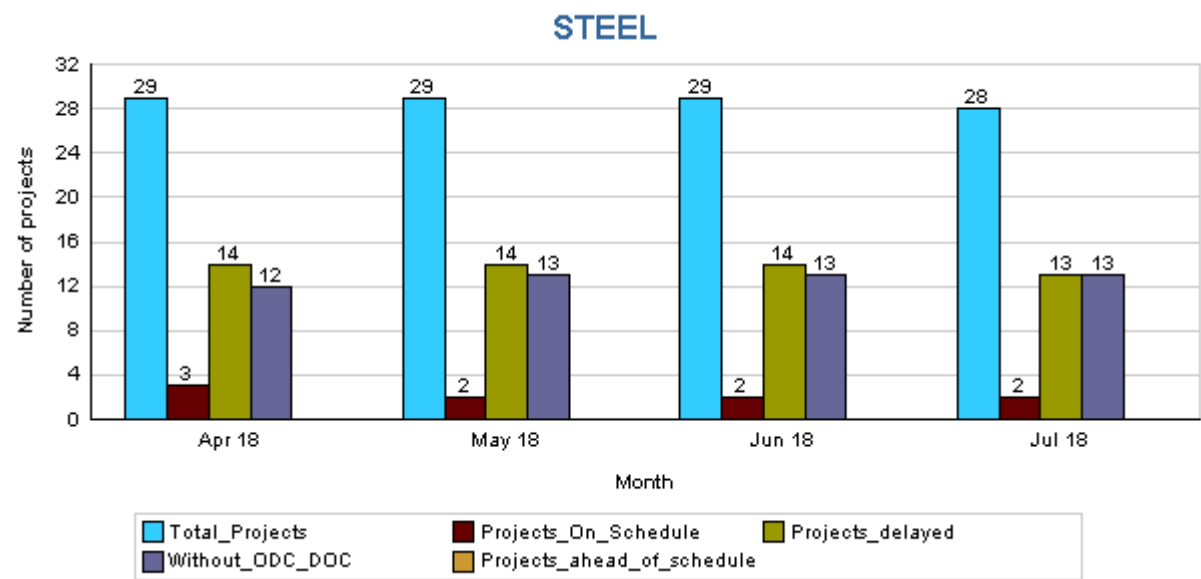


Break-up of 13 Delayed projects in July 2018

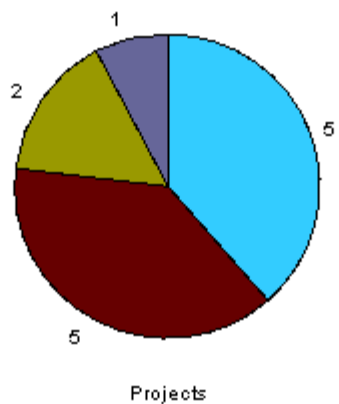


Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

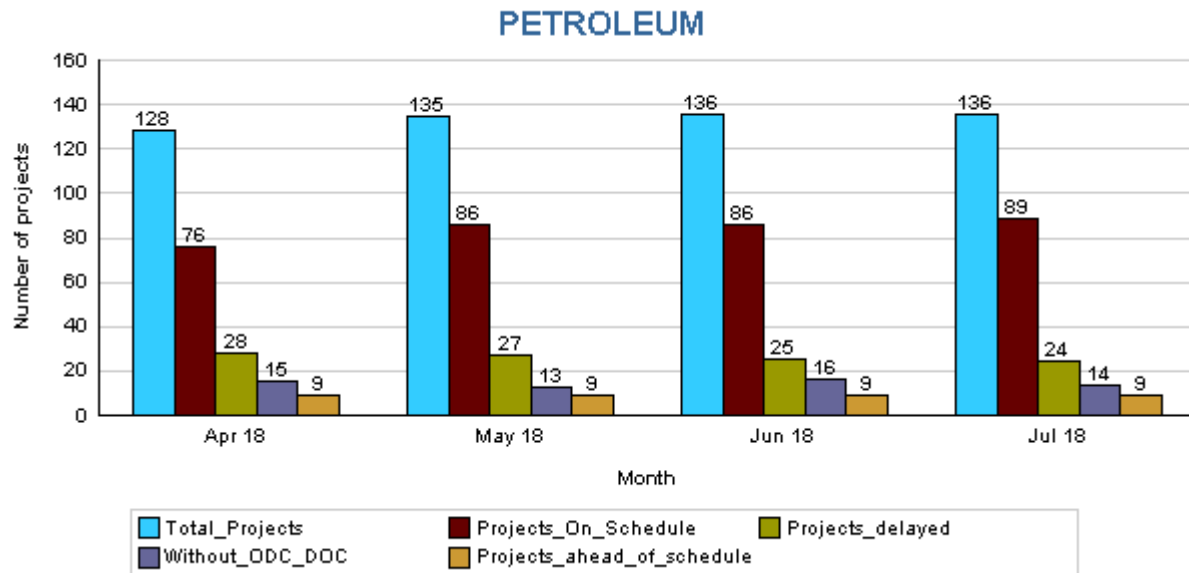


Break-up of 24 Delayed projects in July 2018

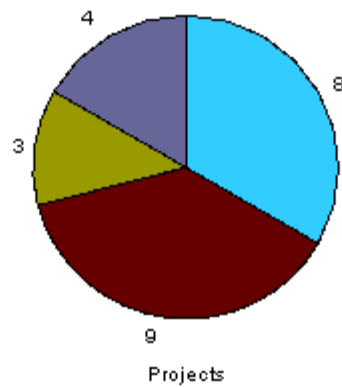


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

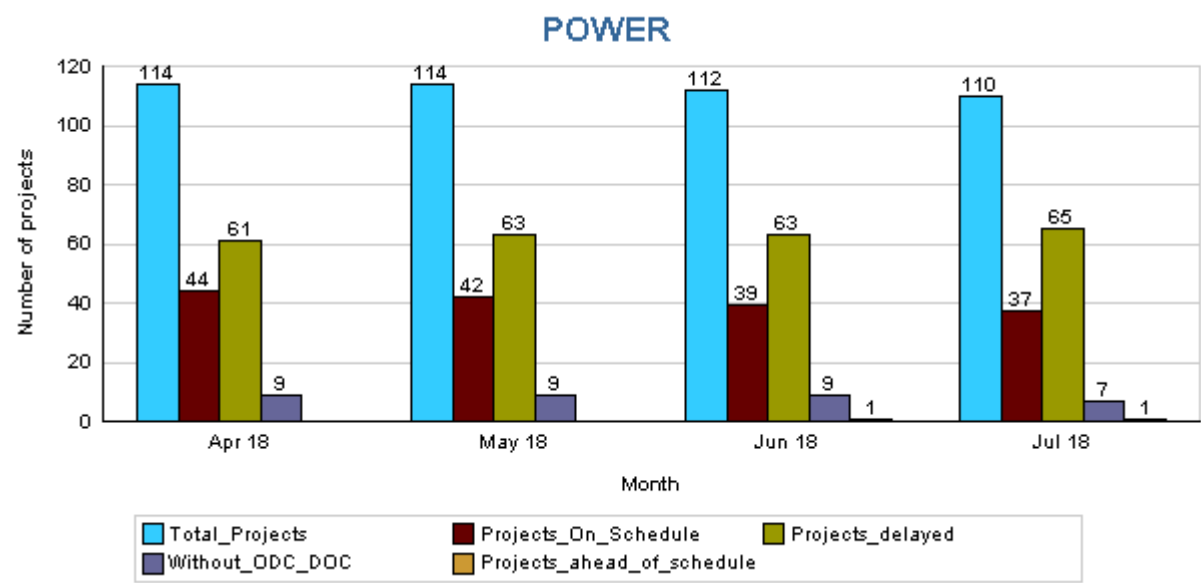


Break-up of 65 Delayed projects in July 2018

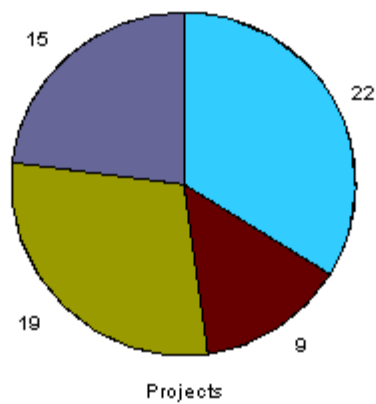


Delay in Months

Delay in Months	1-12	13-24	25-60	60 and Above
Projects	22	9	19	15

Graphical Presentation of All Projects w.r.t. Original Schedule

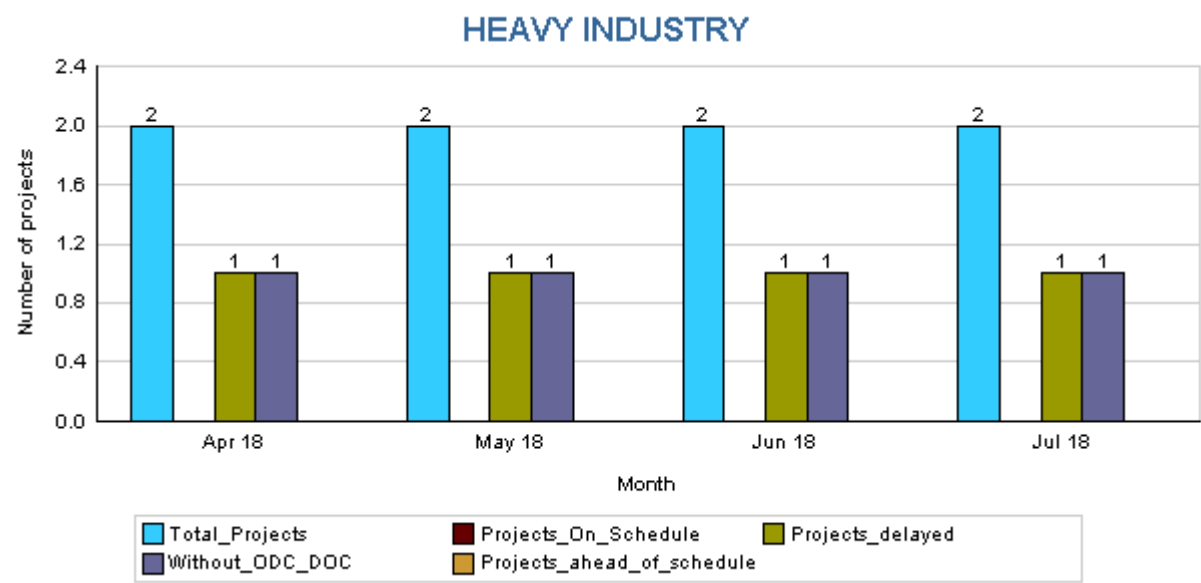


Break-up of 1 Delayed projects in July 2018




Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

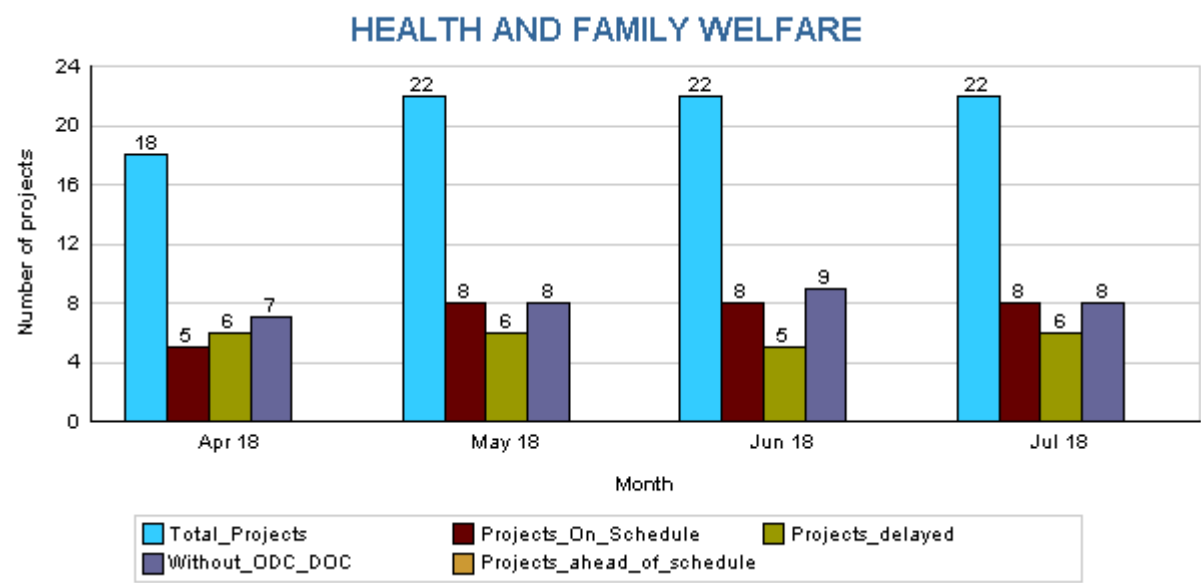


Break-up of 6 Delayed projects in July 2018

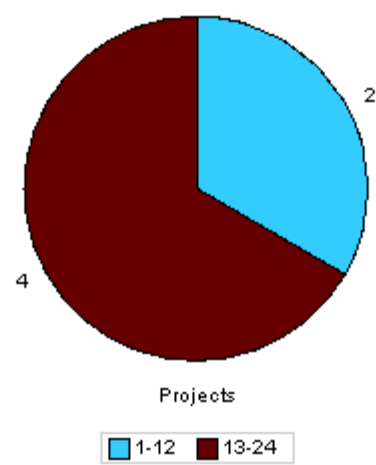


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

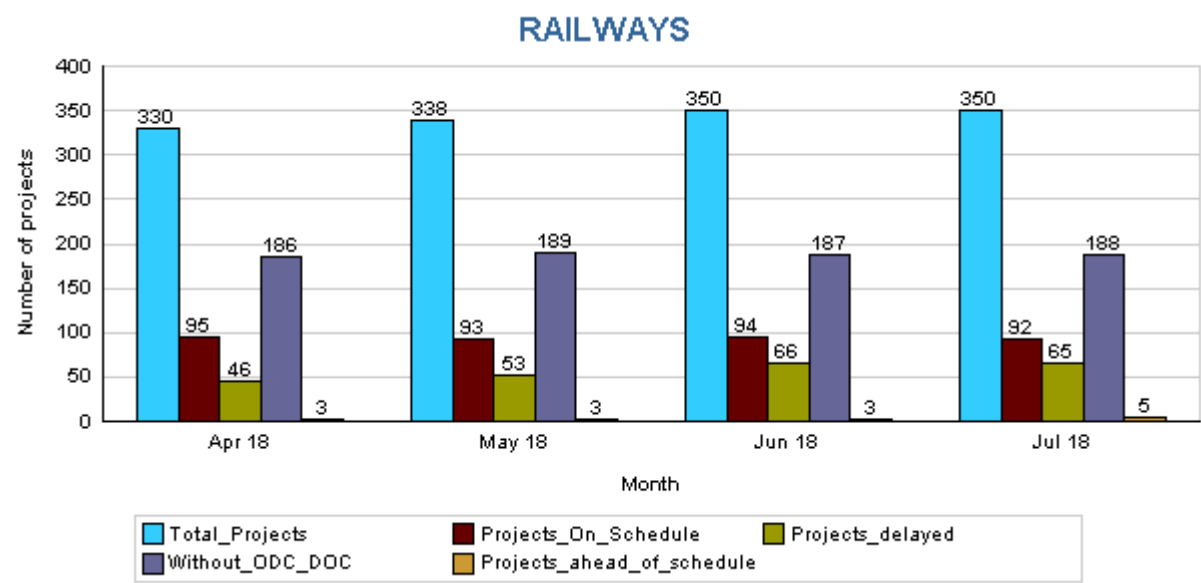


Break-up of 65 Delayed projects in July 2018

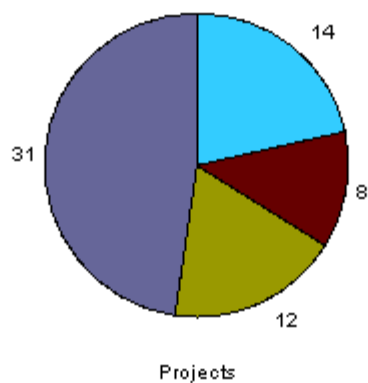


Delay in Months

1-12	13-24	25-60	60 and Above
------	-------	-------	--------------

Graphical Presentation of All Projects w.r.t. Original Schedule

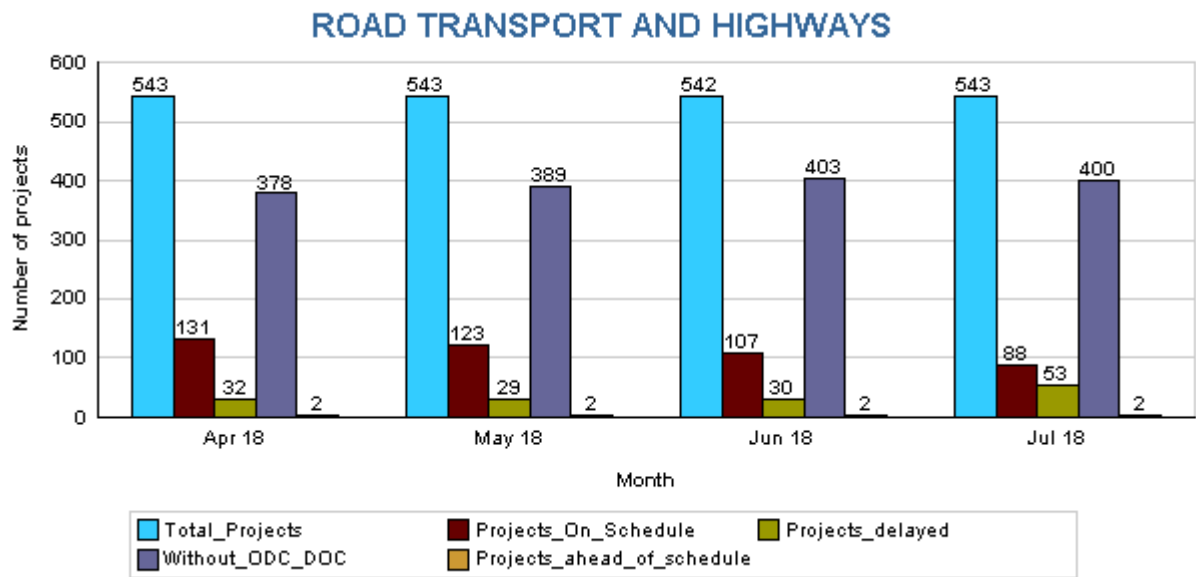


Break-up of 53 Delayed projects in July 2018

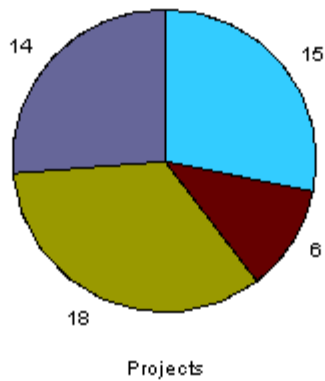


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

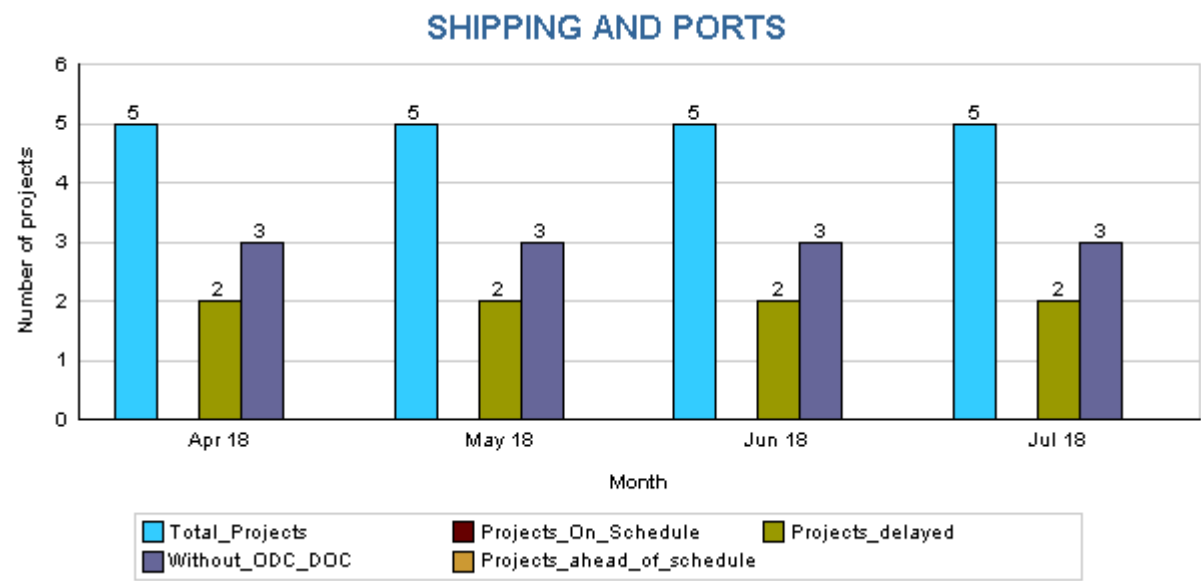


Break-up of 2 Delayed projects in July 2018

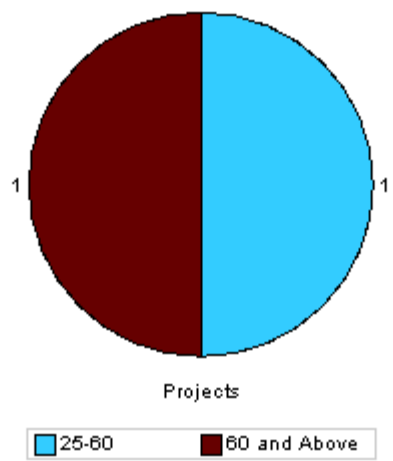


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

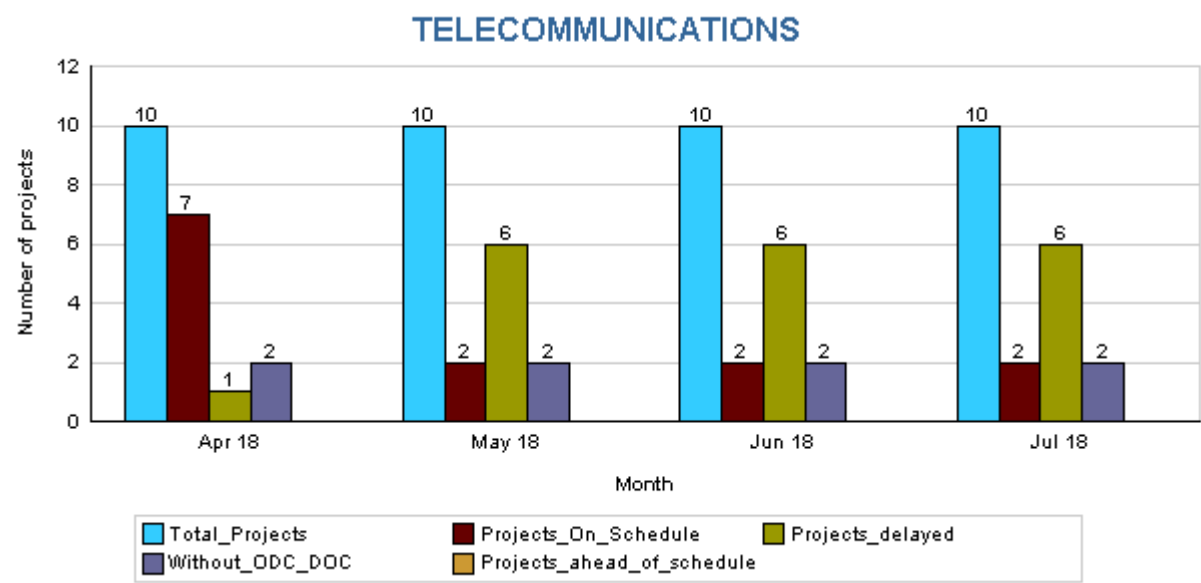


Break-up of 6 Delayed projects in July 2018

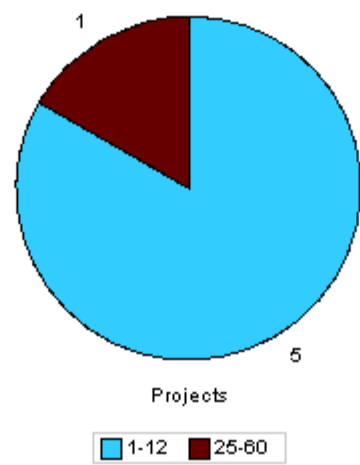


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

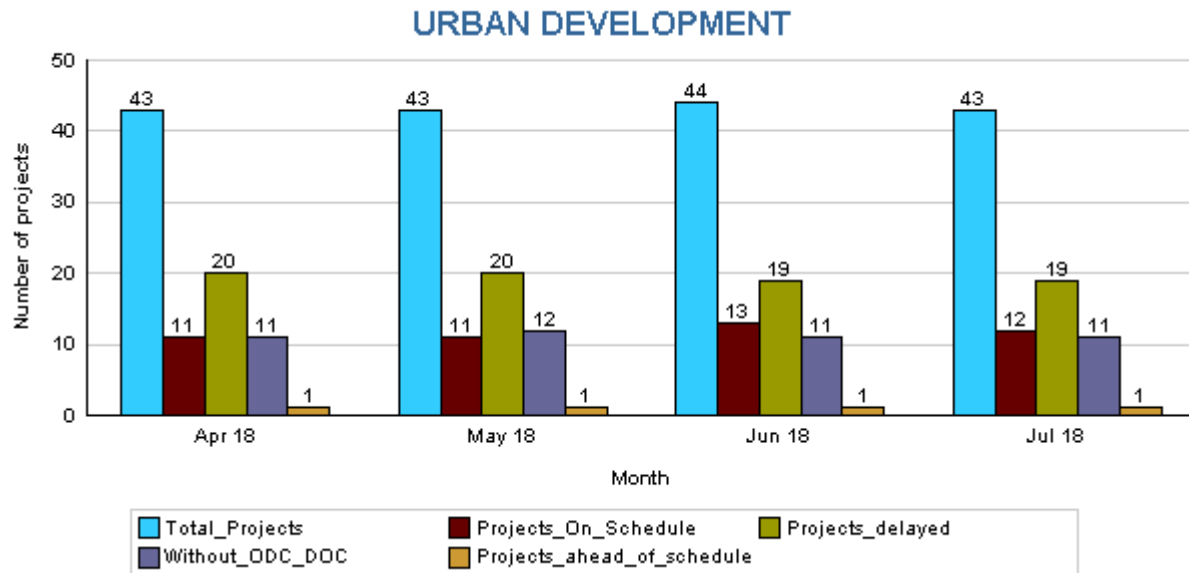


Break-up of 19 Delayed projects in July 2018

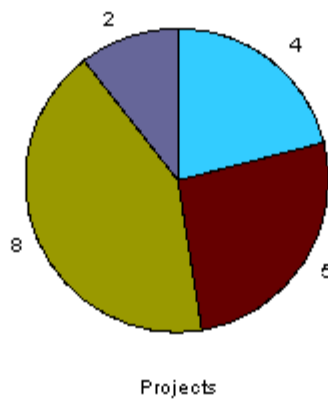

Delay in Months

Delay in Months	Count
1-12	4
13-24	5
25-60	8
60 and Above	2

Graphical Presentation of All Projects w.r.t. Original Schedule

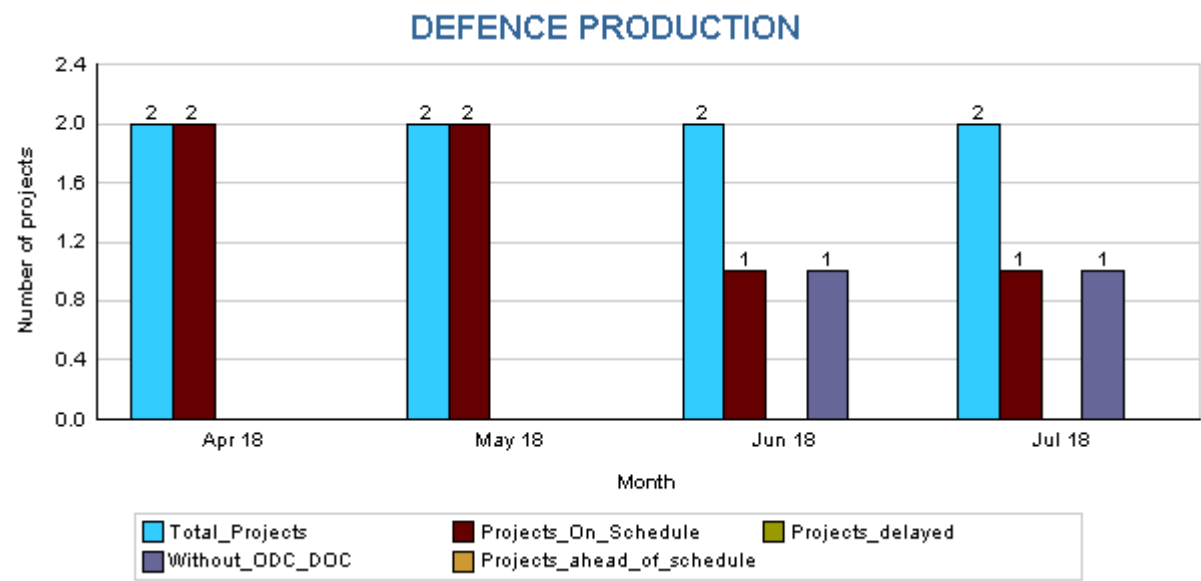

Delay in Months

TABLE-29

Detail of ongoing Projects Costing Rs.150 Crore and above.									
						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	12,120.00	12/2015 11/2016	06/2020	54(O) 43	49/70
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	9,520.00	12/2016 03/2017	12/2020	48(O) 48	36/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 5,677.00	6,100.00	5,655.69	09/2010 09/2016	03/2019	102(O) 102	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	8,761.00	11/2020 -	11/2023	0 -	16/76
	Total		67,120.00 -	74,849.00	36,056.69				184/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21 -	0/0
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM ,	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92 -	0/0
	Total		624.07 -	994.86	632.48				0/0
	<u>COAL</u>								
7	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,825.99	03/2023 -	03/2023	0 -	14/18
8	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	1,863.01	03/2023 -	03/2023	0 -	6/20
9	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.11	03/2023 -	03/2023	0 -	1/12
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	164.90	03/2015 03/2020	03/2020	60(O) 60	5/9
11	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72 -	1/7
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	204.04	03/2014 -	03/2020	72 -	0/4
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36 -	7/9
14	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	157.67	03/2016 -	03/2019	36 -	4/7
15	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	51.45	03/2022 -	03/2022	0 -	2/9
16	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	54.19	03/2020 -	03/2020	0 -	3/8

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	51.76	03/2018 -	03/2018	-	1/7
18	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	53.98	03/2020 -	03/2020	0 -	0/6
19	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	3.74	03/2023 -	03/2023	0 -	1/10
20	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0 -	0/4
21	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0 -	0/1
22	MAGADH OC 20 MTY (CCL) - [N06000015]JCL,JHARKHAND ,	08/2008	706.40 -	706.40	126.89	07/2012 -	03/2021	104 -	3/5
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND ,	09/2009	153.82 -	153.82	131.07	03/2014 -	-	-	6/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND ,	08/2007	163.51 -	163.51	93.47	03/2011 -	03/2020	108 -	3/5
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]JCL,JHARKHAND ,	12/2007	179.87 -	179.87	99.53	03/2012 -	03/2019	84 -	3/5
26	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND ,	08/2008	264.68 -	264.68	155.03	03/2012 -	03/2019	84 -	3/5
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL,JHARKHAND ,	12/2009	510.85 -	510.85	350.74	03/2016 -	03/2019	36 -	3/5
28	KARMA OCP (1.0MTY) - [N06000088]JCL,JHARKHAND ,	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	0 -	3/5
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54 -	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	288.72	04/2015 -	04/2019	48 -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]JCL,JHARKHAND ,	02/2012	858.11 -	858.11	223.12	03/2020 -	03/2020	0 -	5/6
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	4.57	03/2021 -	03/2021	0 -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	179.02	05/2014 -	04/2018	-	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	176.35	04/2014 -	04/2018	-	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	42.29	03/2022 -	03/2022	0 -	1/21
37	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY SINGRAULI - [N06000033]NCL,MADHYA PRADESH ,	10/2007	259.40 -	486.57	410.19	03/2012 -	-	-	1/3
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 203.82	203.82	95.48	03/2023 03/2021	03/2021	-24(O) -24	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0 -	2/8
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	114.49	03/2021 -	03/2021	0 -	2/9
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	41.16	03/2021 -	03/2021	0 -	1/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92	231.92	.00	03/2022	03/2022	0	1/7
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33	488.33	1.89	03/2023	03/2023	0	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44	869.44	112.67	03/2021	03/2021	0	2/4
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87	409.87	15.56	03/2022	03/2022	0	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09	1,783.09	167.20	03/2021	03/2021	0	0/9
47	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17	1,255.17	.00	03/2022	03/2022	0	0/0
48	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82	441.82	178.90	03/2020	03/2020	0	7/11
49	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16	611.16	387.44	03/2020	03/2020	0	2/8
50	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23	266.23	143.07	03/2021	03/2021	0	12/12
51	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67	267.67	207.28	03/2018	03/2018	-	7/7
52	BHANEGAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	91.90	03/2023 02/2017	03/2023	0(0) 0	7/11
53	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56	295.56	89.32	03/2019	03/2019	0	10/13
54	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49	205.49	100.50	03/2020	03/2020	0	5/10
55	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69	483.69	81.65	03/2021	03/2021	0	2/6
56	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28	727.28	236.21	03/2025	03/2025	0	4/13
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90	288.90	.00	03/2023	03/2023	0	2/10
58	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65	277.65	18.78	03/2021	03/2021	0	3/6
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42	498.42	52.83	03/2020	03/2020	0	2/6
60	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68	198.68	234.72	03/2019	03/2019	0	2/9
61	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52	304.52	128.39	03/2019	03/2019	0	2/8
62	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73	362.73	257.09	03/2020	03/2020	0	0/0
63	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76	319.76	58.04	03/2022	03/2022	0	0/3
64	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07	458.07	16.00	03/2022	03/2022	0	0/12
65	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00	328.00	88.10	03/2021	03/2021	0	1/6
66	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96	302.96	334.77	03/2010	03/2018	-	9/10

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10	490.10	344.12	03/2017	03/2020	72	11/12
68	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77	457.77	581.49	03/2013	03/2019	84	8/9
69	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08	172.08	263.24	03/2010	03/2019	120	3/4
70	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28	207.28	233.26	03/2012	03/2021	108	5/5
71	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53	479.53	242.14	03/2013	03/2020	84	6/9
72	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N060000112]MCL,ODISHA ,	05/2014	479.15	479.15	105.89	03/2019	03/2021	24	2/9
73	SIARMAL OCP (40.00MTY) - [N060000113]MCL,ODISHA ,	05/2014	3,756.36	3,756.36	689.20	03/2026	03/2026	0	5/15
74	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N060000114]MCL,ODISHA ,	05/2014	337.66	337.66	42.95	03/2019	03/2021	24	4/6
75	KULDA EXPN OC. (5.00 MTY) - [N060000115]MCL,ODISHA ,	06/2014	289.03	289.03	65.79	03/2018	03/2020	24	3/5
76	GARJANBAHAL OCP - [N060000117]MCL,ODISHA ,	11/2014	1,375.38	1,375.38	397.45	03/2021	03/2021	0	5/9
77	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N060000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45	522.45	10.45	09/2019	09/2019	0	0/0
78	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N060000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63	513.63	176.76	12/2019	12/2019	0	0/0
79	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N060000095]NLC,TAMIL NADU ,	06/2011	5,907.11	5,907.11	5,547.98	12/2015	12/2018	36(O) 36	25/35
80	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N060000138]NLC,TAMIL NADU ,	04/2013	1,458.17	709.06	388.25	06/2015	09/2019	51(O) 1	5/7
81	NEYVELI SOLAR POWER PROJECT 130 MW - [N060000151]NLC,TAMIL NADU ,	05/2016	687.28	759.19	758.30	06/2017	12/2017	-	0/0
82	SHANTIKHANI LONGWALL PROJ-SCCL - [N060000017]SCCL,TELANGANA ,	10/2006	249.03	448.86	186.91	03/2012	03/2024	144(O) 144	35/42
83	KAKATIYA LONGWALL - [N060000048]SCCL,TELANGANA ,	12/2008	453.63	453.63	121.91	12/2012	-	-	11/44
84	RAMAGUNDAM OC-II EXTENSION - [N060000078]SCCL,TELANGANA ,	12/2009	418.97	489.62	477.74	03/2012	03/2023	132(O) 132	0/2
85	RKP OCP PHASE-I - [N060000079]SCCL,TELANGANA ,	03/2010	209.78	209.78	154.52	03/2015	03/2019	48(O) 48	30/31
86	MANUGURU OC-II EXTENSION PHASE-II - [N060000080]SCCL,TELANGANA ,	03/2010	181.19	181.19	159.87	03/2012	03/2018	-	5/6
87	KISTARAM OCP - [N060000089]SCCL,TELANGANA ,	11/2010	242.29	164.04	12.69	03/2015	03/2021	72(O) 72	0/5
88	RCE OF INDARAM OCP(1.20 MTPA) - [N060000093]SCCL,TELANGANA ,	07/2011	162.76	349.28	1.31	03/2015	03/2021	72(O) 72	4/29
89	JALAGAM VENGALA RAO OCP-II - [N060000094]SCCL,TELANGANA ,	07/2011	447.06	437.51	353.61	03/2015	03/2021	72(O) 0	6/13
90	RG OC -III EXTENSION (PHASE -II) PROJECT - [N060000100]SCCL,TELANGANA ,	06/2012	365.01	365.01	204.26	06/2015	03/2019	45(O) 45	35/36
91	KALYANIKHANI OPENCAST PROJECT - [N060000101]SCCL,TELANGANA ,	07/2012	417.33	384.32	146.45	07/2016	03/2020	44	21/28

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
92	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 415.37	415.37	160.45	03/2016 03/2019	03/2019	36(O) 0	37/39
93	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 442.42	442.42	79.96	03/2019 03/2019	03/2019	0(O) 0	10/18
94	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.00	03/2018 -	03/2019	12 -	0/9
95	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	.00	03/2020 -	03/2020	0 -	1/17
96	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	.00	03/2019 -	03/2019	0 -	0/11
97	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA 6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH ,	06/2011	1,131.28 -	1,131.28	562.24	03/2018 -	03/2019	12 -	9/10
98	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	2,649.27	11/2021 -	11/2021	0 -	0/0
99	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]JCL,WEST BENGAL ,	11/2015	602.86 -	602.86	294.63	03/2022 -	03/2022	84 -	7/12
100	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]JCL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	349.57	03/2018 -	03/2020	24 -	11/16
	Total		91,364.09 -	90,827.28	27,126.67				475/945
	<u>FERTILISERS</u>								
101	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	17.35	11/2019 -	11/2019	0 -	0/1
102	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	112.27	11/2016 04/2019	04/2019	29(O) 29	1/13
103	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA ,	02/2016	482.85 482.85	482.85	413.01	12/2017 05/2018	05/2018	-	0/1
104	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	18.14	04/2020 -	04/2020	0 -	0/0
105	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	17.76	11/2019 -	11/2019	0 -	0/2
106	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	19.79	11/2019 -	11/2019	0 -	0/2
	Total		1,781.92 -	1,793.57	598.32				1/19
	<u>MINES</u>								
107	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	94.71	04/2021 04/2021	04/2021	0(O) 0	2/3
108	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	299.64	01/2020 01/2020	01/2020	0(O) 0	1/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 355.00	355.00	31.92	11/2020 11/2020	11/2020	0(O) 0	2/2
110	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.00	04/2021 04/2021	04/2021	0(O) 0	0/0
	Total		6,912.00 -	6,912.00	426.27				5/7
	STEEL								
111	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29 -	1/2
112	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	01/1999 -	-	-	0/0
113	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	935.45	12/2017 -	03/2019	15 -	4/6
114	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	63.07	08/2018 -	10/2018	2 -	2/4
115	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	170.25	07/2018 -	09/2018	2 -	2/4
116	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72 -	0/0
117	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	141.50	04/2015 -	-	-	4/5
118	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	15,525.00	14,116.06	05/2015 10/2018	12/2018	43(O) 24	60/86
119	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	32.30	06/2020 -	06/2020	0 -	5/12
120	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
121	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	471.38	10/2017 -	12/2018	14 -	0/2
122	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	1,607.72	12/2017 -	11/2018	11 -	1/2
123	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	142.56	09/2017 -	-	-	0/0
124	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
125	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
126	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
127	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
128	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	108.77	06/2019 -	06/2019	0 -	0/1
129	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
130	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
131	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15 -	0/0
132	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	5,467.78	04/2018 -	02/2019	10 -	3/3
133	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	08/2018	17 -	0/0
134	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
135	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
136	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
137	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	502.10	09/2018 -	01/2019	4 -	3/5
138	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
	Total		37,451.14 -	37,664.82	27,402.32				85/132
	<u>PETROLEUM</u>								
139	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020	0 -	0/1
140	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	138.28	09/2019 -	09/2019	0 -	19/27
141	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	870.29	06/2020 08/2021	08/2021	14(O) 14	0/0
142	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0 -	0/0
143	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
144	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 207.80	207.80	11.24	09/2018 02/2019	02/2019	5(O) 5	0/0
145	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	22.24	04/2021 -	04/2020	-12 -	0/0
146	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]IOCL,ARUNACHAL PRADESH ,	01/2016	247.52 -	247.52	130.75	02/2019 -	12/2018	-2 -	3/10
147	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.89	2,099.23	03/2013 03/2019	03/2019	72(O) 72	5/15
148	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	31.35	01/2014 11/2019	11/2019	70(O) 70	2/2
149	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM , Central Sector Projects	07/2015	1,031.37 -	1,031.37	305.91	01/2018 -	-	-	46/61
150	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	122.85	08/2019 -	08/2019	8 -	2/13
151	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	917.79	11/2019 -	11/2019	0 -	10/17
152	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	35.56	05/2020 05/2020	05/2020	0(O) 0	0/0
153	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	0 -	0/0
154	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	179.85	09/2019 -	09/2019	0 -	0/0
155	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	543.91	1.65	02/2020 -	02/2020	0 -	0/0
156	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	961.00	03/2015 -	-	-	0/5
157	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	640.72	11/2018 -	11/2018	0 -	6/8
158	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	315.56	12/2020 -	02/2020	-10 -	2/2
159	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	78.63	06/2020 -	06/2020	0 -	2/2
160	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	.00	03/2021 -	03/2021	0 -	4/26
161	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	.00	10/2020 -	10/2020	0 -	0/0
162	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	30.45	10/2022 -	10/2022	0 -	0/0
163	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	.00	04/2021 -	04/2021	0 -	0/0
164	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	3,986.30	05/2019 10/2019	10/2019	5(O) 5	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
165	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT ,	05/2015	1,671.22 567.22	567.22	443.27	11/2019 12/2018	07/2018	-16(O) -16	0/0
166	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT , Central Sector Projects	11/2014	195.63 -	187.10	168.13	09/2018 09/2018	09/2018	0(O) 0	0/0
167	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT ,	07/2014	199.95 -	199.95	156.83	03/2018 -	03/2018	-	20/22
168	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	95.81	04/2018 -	12/2018	8 -	18/20
169	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	249.44	03/2026 03/2026	03/2026	0(O) 0	0/0
170	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	54.11	07/2020 -	07/2020	0 -	0/0
171	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018	12 -	0/0
172	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT ,	08/2017	1,342.00 -	1,342.00	3.08	08/2020 -	08/2020	0 -	0/0
173	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	875.63	09/2019 -	09/2019	0 -	0/0
174	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020	0 -	0/0
175	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	.00	- -	-	-	0/0
176	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	1.02	11/2020 -	11/2020	0 -	0/0
177	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	.12	02/2020 -	02/2020	0 -	0/0
178	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	493.66	09/2019 -	09/2019	0 -	0/0
179	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA HP - [N16000226]IOCL,HIMACHAL PRADESH ,	02/2016	356.00 -	356.00	159.71	05/2019 -	12/2018	-5 -	3/13
180	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	71.22	09/2019 -	09/2019	0 -	2/2
181	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12
182	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	44.07	03/2023 03/2022	03/2022	-12(O) -12	0/0
183	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	15.86	06/2020 -	06/2020	0 -	0/0
184	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	16.32	10/2022 -	10/2022	0 -	4/9
185	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	12.16	10/2022 -	10/2022	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
186	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
187	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	749.00	660.88	02/2020 -	02/2020	0 -	0/0
188	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019	0 -	6/8
189	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019	0 -	4/11
190	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019	0 -	7/9
191	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	581.00	.00	03/2020 -	03/2020	0 -	0/0
192	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	714.25	337.32	10/2017 -	03/2019	38 -	38/52
193	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	1,938.81	08/2018 05/2019	05/2019	9(O) 9	0/20
194	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 -	3,313.00	203.89	02/2020 -	02/2020	0 -	0/20
195	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]BPCL,KERALA ,	05/2015	337.06 -	337.06	157.18	08/2018 -	08/2018	0 -	0/12
196	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0 -	0/0
197	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	.00	06/2020 -	06/2020	0 -	0/0
198	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,256.72	1,256.72	1,195.29	05/2013 12/2018	12/2018	67(O) 0	1/5
199	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 03/2018	12/2019	57(O) 57	0/17
200	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,511.38	04/2019 03/2019	03/2019	-1(O) -1	0/0
201	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA ,	02/2015	2,899.93 -	2,504.61	1,832.82	05/2017 12/2018	12/2018	19(O) 19	0/0
202	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	1,429.33	03/2019 05/2020	05/2020	14(O) 14	0/0
203	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	4,619.94	3,878.77	12/2017 03/2019	03/2019	15(O) 15	0/0
204	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019	13(O) 13	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
205	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	456.52	08/2021 -	08/2021	0 -	2/2
206	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	78.88	02/2020 -	02/2020	0 -	0/10
207	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	107.14	12/2019 -	12/2019	0 -	0/0
208	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]BPCL,MAHARASHTRA ,	05/2015	193.40 -	193.40	76.81	01/2019 -	01/2019	0 -	0/18
209	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	.08	01/2021 -	01/2021	0 -	0/0
210	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	.05	01/2021 -	01/2021	0 -	0/0
211	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	.05	01/2021 -	01/2021	0 -	0/0
212	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA , Central Sector Projects	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8 -	0/0
213	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	255.08	05/2019 05/2019	05/2019	0(O) 0	0/0
214	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	47.18	11/2019 11/2019	11/2019	0(O) 0	0/0
215	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	33.34	11/2019 11/2019	11/2019	0(O) 0	0/0
216	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	185.84	11/2019 11/2019	11/2019	0(O) 0	0/0
217	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	396.86	05/2021 05/2021	05/2021	0(O) 0	0/0
218	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	43.55	08/2020 -	08/2020	0 -	0/15
219	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	56.00	06/2020 -	06/2020	0 -	0/0
220	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	.00	12/2019 -	12/2019	0 -	0/0
221	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	2,104.60	12/2018 -	12/2018	0 -	32/39
222	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	543.05	09/2011 05/2018	05/2018	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
223	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
224	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE ,	02/2011	913.00 1,330.00	1,330.00	1,291.40	06/2018 -	10/2018	4 -	1/1
225	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	536.27	10/2014 02/2019	02/2019	52(O) 52	31/40
226	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	170.50	03/2017 11/2018	03/2019	24(O) 24	0/0
227	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 -	1,823.00	279.79	12/2020 -	12/2020	0 -	0/0
228	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 -	2,321.00	354.43	12/2020 -	08/2020	-4 -	2/2
229	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	437.05	10/2019 -	10/2019	0 -	3/3
230	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	143.47	07/2018 10/2020	10/2020	27(O) 27	20/36
231	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	750.43	06/2020 -	06/2020	0 -	14/24
232	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB HARYANA) - [N16000242]HPCL,MULTI STATE ,	11/2016	230.00 -	230.00	80.53	02/2019 -	02/2019	0 -	8/13
233	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	12.73	10/2020 -	10/2020	0 -	0/0
234	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	17.97	12/2019 -	12/2019	0 -	0/0
235	LAYING OF VIJAIPIUR-AURAIYA PIPELINE SECTION OF VIJAIPIUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,881.40	467.97	12/2019 12/2020	12/2019	0(O) 0	15/24
236	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	152.80	12/2020 -	12/2020	0 -	13/24
237	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	177.17	12/2020 -	12/2020	0 -	13/24
238	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 2,915.00	2,915.00	1,856.19	12/2012 02/2019	02/2019	74(O) 0	12/42
239	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	24.62	03/2021 -	03/2021	0 -	2/26
240	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
241	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	.00	12/2021 -	12/2021	0 -	0/0
242	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,061.99	09/2017 12/2018	12/2018	15(O) 15	5/6
243	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	421.08	12/2020 -	12/2020	0 -	14/24

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
244	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	197.48	01/2019 -	01/2019	0 -	4/6
245	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	32.91	12/2019 -	12/2019	0 -	7/26
246	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	27.09	07/2022 -	07/2022	0 -	0/0
247	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	2.12	12/2021 -	12/2021	0 -	0/0
248	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	181.20 -	181.20	13.66	07/2022 -	07/2022	0 -	0/0
249	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
250	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.00	- -	-	-	0/26
251	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0 -	0/0
252	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	-	-	52/52
253	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL,TAMIL NADU ,	05/2015	257.87 -	257.87	226.81	11/2016 -	07/2018	20 -	19/22
254	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.12	02/2017 -	-	-	0/0
255	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	131.04	03/2019 -	04/2019	1 -	0/0
256	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 -	4,497.00	253.96	12/2018 -	12/2018	0 -	2/2
257	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	.28	06/2020 -	06/2020	0 -	2/2
258	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	351.69	12/2019 -	12/2019	0 -	0/0
259	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	1.31	08/2020 -	08/2020	0 -	0/0
260	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020	0 -	0/0
261	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]GAIL,UTTAR PRADESH ,	07/2015	1,427.94 -	750.00	558.94	12/2018 -	12/2018	0 -	15/20
262	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	84.64	04/2022 -	04/2022	0 -	24/33
263	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	.00	08/2021 -	08/2021	0 -	0/0
264	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	137.03	09/2019 -	09/2019	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
265	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.00	08/2020 -	08/2020	0 -	0/0
266	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	.90	12/2021 -	12/2021	0 -	0/0
267	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	24.22	02/2020 -	02/2020	0 -	18/26
268	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL ,	03/2014	3,076.00 4,190.00	4,190.00	2,945.09	09/2017 06/2018	06/2018	-	6/7
269	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL ,	03/2015	694.00 1,097.54	694.00	431.49	10/2018 12/2018	12/2018	2(O) 2	0/15
270	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL, WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020	0 -	0/0
271	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL, WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	18.21	12/2020 -	12/2020	0 -	9/24
272	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL ,	04/2017	163.02 -	163.02	31.03	04/2020 -	04/2020	0 -	9/26
273	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL, WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	536.51	09/2019 -	09/2019	0 -	0/0
274	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL, WEST BENGAL ,	03/2018	3,712.00 -	3,712.00	.00	09/2022 -	09/2022	0 -	0/0
	Total		2,17,011.11 -	2,17,989.15	61,469.73				574/1113
	<u>POWER</u>								
275	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,234.01	09/2010 -	-	-	0/0
276	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH ,	12/2004	2,496.90 6,179.96	6,179.96	6,604.01	12/2009 10/2018	03/2019	111(O) 24	28/30
277	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM ,	01/2008	4,375.35 8,150.00	8,150.00	7,117.65	09/2011 06/2018	09/2018	84(O) 84	34/37
278	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	14,762.17	01/2011 04/2021	04/2021	123(O) 106	26/47
279	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 09/2017	05/2019	60(O) 60	3/18
280	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	11,425.00	01/2018 -	05/2020	28 -	31/34
281	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN, BIHAR ,	05/2015	436.68 -	602.44	495.12	12/2016 -	12/2018	24 -	13/19
282	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL, BIHAR ,	04/2016	790.13 -	790.30	485.35	06/2019 -	06/2019	0 -	0/0
283	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	9,989.31	06/2017 06/2019	06/2019	24(O) 24	34/40

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
284	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,195.00	11/2019 -	11/2019	-1 -	0/0
285	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 -	1,394.52	173.34	05/2017 06/2019	06/2019	25(O) 25	4/9
286	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI ,	05/2015	780.33 -	780.33	478.41	10/2018 -	09/2018	-1 -	0/0
287	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL,GUJARAT ,	07/2016	300.94 -	300.94	177.77	12/2018 -	12/2018	0 -	0/0
288	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	274.39	11/2017 -	09/2018	10 -	1/4
289	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	44.73	09/2018 -	06/2019	9 -	0/0
290	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPPT AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 -	193.14	2.35	06/2019 -	06/2019	0 -	0/0
291	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	8,398.75	6,955.14	09/2009 -	12/2020	106 -	2/3
292	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,064.54	04/2020 -	10/2023	42 -	0/0
293	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI- LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR ,	01/2014	1,788.41 -	2,333.71	1,513.68	09/2017 -	09/2018	12 -	0/0
294	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	7,300.02	02/2019 10/2020	10/2020	20(O) 20	20/23
295	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,552.00	4,552.00	2,734.43	10/2017 -	12/2016	-	0/0
296	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-	-	48/48
297	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	445.89	166.83	02/2019 -	02/2019	0 -	0/0
298	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	9,449.14	09/2017 06/2019	06/2019	21(O) 21	32/41
299	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	5,651.48	09/2019 -	09/2019	0 -	26/26
300	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH ,	01/2016	305.04 -	305.04	199.28	03/2017 09/2018	09/2018	18(O) 18	0/0
301	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH ,	04/2016	287.99 -	287.99	155.62	06/2018 -	10/2018	4 -	0/0
302	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	2,104.21	62.05	09/2020 -	09/2020	0 -	9/16

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
303	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH , Central Sector Projects	02/2015	1,750.00 -	1,750.00	1,171.00	06/2018 -	10/2018	4 -	0/0
304	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	664.31	09/2010 12/2018	12/2018	99(O) 99	5/8
305	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
306	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	8,774.15	11/2016 03/2019	03/2019	28(O) 28	34/38
307	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA , Central Sector Projects	04/2015	2,225.00 2,225.00	2,225.00	1,556.00	01/2018 -	07/2018	6 -	0/0
308	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,531.14	10/2012 12/2018	02/2019	76(O) 76	8/11
309	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 13,762.80	13,762.80	12,705.71	08/2013 03/2022	03/2022	103(O) 103	23/26
310	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE ,	02/2010	2,144.00 2,932.88	2,932.88	2,643.53	12/2012 06/2018	09/2018	69(O) 69	18/23
311	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE ,	07/2010	1,272.80 1,731.10	1,731.10	1,456.53	11/2012 09/2018	09/2018	70(O) 70	12/13
312	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	493.77	06/2014 12/2018	12/2018	54(O) 54	10/12
313	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE ,	12/2011	297.33 534.02	534.02	418.03	08/2014 09/2018	09/2018	49(O) 49	8/10
314	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE ,	03/2013	514.20 703.10	703.10	603.15	06/2015 05/2018	08/2018	38(O) 38	10/10
315	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE ,	03/2013	2,514.88 3,190.27	3,190.27	2,248.47	12/2015 06/2018	09/2018	33(O) 33	15/18
316	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,200.95	04/2016 12/2018	12/2018	32(O) 31	8/12
317	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	180.77	04/2016 12/2017	10/2018	30(O) 30	0/0
318	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 -	539.82	416.39	06/2016 09/2018	12/2018	30(O) 30	9/11
319	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 550.18	550.18	423.38	11/2016 06/2019	06/2019	31(O) 31	8/12
320	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE ,	03/2014	155.57 206.42	206.42	145.07	03/2016 09/2018	09/2018	30(O) 30	4/6
321	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	2,543.37	03/2018 03/2019	03/2019	12(O) 12	9/12
322	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE ,	08/2014	288.49 -	376.09	264.15	02/2017 06/2018	09/2018	19(O) 19	10/12
323	EASTERN REGION STRENGTHENING SCHEME-IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	146.48	02/2016 09/2018	09/2018	31(O) 31	16/17

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
324	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	222.24	03/2018 09/2018	09/2018	6(O) 6	1/3
325	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	871.62	269.23	10/2017 09/2019	09/2019	23(O) 22	0/5
326	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	180.99	07/2017 06/2019	06/2019	23(O) 23	3/5
327	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	73.19	03/2018 -	09/2018	6 -	0/0
328	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE ,	03/2015	1,071.24 -	1,071.24	611.76	09/2017 09/2018	09/2018	12(O) 11	0/0
329	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE ,	04/2015	3,705.61 -	3,705.61	2,490.86	04/2018 09/2018	12/2018	8(O) 8	5/9
330	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE ,	07/2015	2,247.37 -	2,247.37	1,395.18	07/2018 -	10/2018	3 -	0/0
331	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE ,	01/2016	1,455.47 -	1,455.47	1,015.50	07/2018 -	08/2018	1 -	0/0
332	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	316.47	01/2018 03/2019	03/2019	14(O) 14	0/0
333	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL,MULTI STATE ,	05/2016	766.21 -	766.21	303.68	11/2018 -	11/2018	0 -	0/0
334	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	1,680.63	05/2019 -	05/2019	0 -	0/0
335	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	2,724.41	11/2019 -	11/2019	0 -	0/0
336	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL,MULTI STATE ,	04/2016	810.48 -	810.48	512.21	12/2018 -	12/2018	0 -	0/0
337	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL,MULTI STATE ,	05/2016	167.01 -	167.01	90.13	11/2018 -	11/2018	-12 -	0/0
338	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE ,	07/2016	150.99 -	150.99	85.46	07/2018 -	08/2018	1 -	0/0
339	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL,MULTI STATE ,	07/2016	333.17 -	333.17	245.93	03/2019 -	03/2019	0 -	0/0
340	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL,MULTI STATE ,	08/2016	431.89 -	431.89	154.46	02/2019 -	02/2019	0 -	0/0
341	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL,MULTI STATE ,	08/2016	177.52 -	177.52	74.98	02/2019 -	02/2019	0 -	0/0
342	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 -	562.25	24.20	03/2019 -	03/2019	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
343	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 -	251.60	22.13	06/2019 -	06/2019	0 -	0/0
344	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	24.85	11/2019 -	11/2019	0 -	0/0
345	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	408.46	123.13	01/2019 -	01/2019	0 -	0/0
346	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	301.40	04/2019 -	04/2019	0 -	0/0
347	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 -	195.05	52.81	02/2020 -	02/2020	0 -	0/0
348	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	88.86	02/2019 -	02/2019	0 -	0/0
349	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]PGCIL,MULTI STATE ,	03/2017	162.31 -	162.31	20.90	03/2019 -	03/2019	0 -	0/0
350	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	14.29	06/2019 -	06/2019	0 -	0/0
351	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	21.24	12/2019 -	12/2019	0 -	0/0
352	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL,MULTI STATE ,	02/2017	204.12 -	204.12	74.37	09/2019 -	09/2019	0 -	0/0
353	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	438.09	04/2020 -	04/2020	0 -	0/0
354	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 -	337.75	6.80	06/2019 -	06/2019	0 -	0/0
355	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 -	9,141.97	823.37	12/2018 -	12/2019	0 -	0/0
356	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 -	6,652.57	719.88	12/2018 -	12/2019	0 -	0/0
357	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE , Central Sector Projects	03/2015	955.00 1,161.00	1,364.00	1,158.00	12/2015 -	09/2018	6 -	0/0
358	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE , Central Sector Projects	04/2015	2,525.00 -	2,525.00	1,940.00	11/2017 -	07/2018	8 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
359	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	2,141.00	04/2019 -	04/2019	0 -	0/0
360	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	383.00	07/2020 -	07/2020	0 -	0/0
361	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	157.04	02/2020 -	02/2020	0 -	0/0
362	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	.18	09/2019 -	09/2019	0 -	0/0
363	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	.00	05/2020 -	05/2020	0 -	0/0
364	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE ,	08/2008	771.00 1,642.00	1,642.00	1,429.45	02/2013 -	10/2018	1 -	0/0
365	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	7,879.74	08/2018 06/2019	06/2019	10(O) 10	27/37
366	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 -	844.64	274.50	04/2019 -	04/2019	0 -	0/0
367	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN ,	07/2015	307.18 -	307.18	203.36	11/2017 10/2018	10/2018	11(O) 11	0/0
368	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 -	1,429.38	623.84	01/2019 -	01/2019	0 -	0/0
369	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,041.61	11/2008 09/2018	12/2018	121(O) 117	20/22
370	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU ,	09/2011	1,940.13 2,702.65	2,702.65	2,492.04	09/2014 09/2018	09/2018	48(O) 48	11/13
371	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 -	186.17	41.36	07/2019 -	07/2019	0 -	0/0
372	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	2,201.67	07/2020 10/2020	10/2020	3(O) 3	18/19
373	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA ,	07/2009	421.01 -	1,078.31	963.23	07/2013 -	-	-	26/26
374	FGUTPP UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
375	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	4,820.27	03/2019 09/2019	09/2019	6(O) 6	19/30
376	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	187.40	02/2014 02/2018	03/2019	61(O) 18	5/8
377	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	8,270.00	12/2016 -	08/2019	23 -	31/34
378	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	4,401.90	2,597.73	02/2016 12/2020	05/2021	63(O) 97	16/30

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
379	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,611.12	03/2013 12/2020	12/2020	93(O) 93	3/15
380	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	3,789.61	1,446.85	06/2013 -	12/2021	102 -	9/13
381	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	146.27	08/2017 -	-	-	0/15
382	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	111.89	12/2021 -	12/2021	0 -	0/32
383	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	349.94	09/2019 02/2022	02/2022	29(O) 29	5/9
384	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	229.72	04/2018 -	08/2018	4 -	0/0
	Total		3,13,586.68 -	3,77,560.50	2,32,240.73				786/1040
	<u>HEAVY INDUSTRY</u>								
385	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	7 -	0/0
386	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-	-	0/0
	Total		3,272.00 -	5,381.30	2,450.86				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
387	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	76.88	03/2019 -	03/2019	0 -	0/0
388	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	36.93	- -	-	-	0/0
389	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
390	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	174.00	05/2021 -	05/2021	0 -	0/0
391	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	414.11	141.00	11/2013 -	-	-	0/0
392	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	237.80	05/2017 -	12/2018	19 -	0/2
393	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	242.20	05/2017 -	09/2018	16 -	0/5
394	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	22.59	- -	02/2020	0 -	0/0
395	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	17.00	- -	03/2020	0 -	0/0
396	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6 -	0/2

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
397	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]HSCC,HARYANA ,	07/2016	312.99 -	322.00	469.00	08/2018 -	08/2018	0 -	0/1
398	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	272.54	122.66	03/2019 -	03/2019	0 -	0/0
399	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	14.08	- -	01/2020	0 -	0/0
400	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	69.24	05/2018 -	09/2019	16 -	0/0
401	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	60.45	02/2018 -	12/2018	10 -	0/1
402	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	272.00	06/2020 -	06/2020	0 -	0/0
403	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	18.50	- -	04/2020	0 -	0/0
404	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	39.35	04/2020 -	04/2020	0 -	0/0
405	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.38	191.38	05/2017 -	09/2018	16 -	0/3
406	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	214.62	09/2018 -	09/2018	0 -	0/0
407	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	71.50	03/2019 -	03/2019	0 -	0/0
408	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	19.50	- -	01/2020	0 -	0/0
	Total		8,611.12 -	8,658.88	2,979.18				0/14
	<u>RAILWAYS</u>								
409	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	155.74 164.36	966.43	989.99	02/2009 -	-	-	0/0
410	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	330.00 -	2,120.16	256.74	03/2021 03/2023	03/2023	24(O) 0	0/0
411	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	743.00 -	1,850.00	1,784.18	03/2008 06/2008	03/2020	144(O) 144	0/0
412	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	283.54 -	761.37	.52	- -	-	-	0/0
413	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	- -	-	-	0/1
414	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	1,313.48 -	2,288.70	334.95	- 03/2022	03/2022	- 0	0/1
415	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	789.79	03/2020 -	03/2022	0 -	0/0
416	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
417	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	4,000.00 -	3,631.00	79.73	- 03/2023	03/2023	- 0	0/0
418	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	83.04	- -	12/2023	0 -	0/0
419	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 2,499.71	2,499.71	148.37	03/2021 -	03/2022	12 -	0/0
420	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	385.63	03/2018 -	-	-	0/0
421	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	.39	03/2019 -	12/2020	21 -	0/0
422	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM ,	09/1997	1,500.00 4,857.00	5,820.00	5,178.44	04/2008 12/2011	06/2018	-	0/0
423	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	200.00 -	1,532.00	525.15	03/2019 -	03/2020	0 -	0/0
424	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	312.12 -	551.00	590.20	03/2019 -	03/2019	0 -	0/0
425	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 -	398.93	203.30	03/2019 -	03/2019	0 -	0/0
426	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	178.69	03/2022 -	03/2022	0 -	0/0
427	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	871.00	148.14	03/2021 -	03/2021	0 -	0/0
428	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	501.69 335.77	1,043.56	876.49	03/2012 -	-	-	0/0
429	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	492.98 -	1,320.00	926.94	12/2010 -	-	-	0/0
430	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	541.00	183.72	- -	-	-	0/0
431	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	324.66	330.82	- -	-	-	0/0
432	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	322.95 -	341.41	640.78	03/2012 -	-	-	0/0
433	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	- -	-	-	0/0
434	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	412.05	395.34	06/2018 -	06/2018	-	0/0
435	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	332.92 283.95	477.88	495.40	03/2012 -	-	-	0/0
436	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	300.00 -	2,145.00	928.69	03/2019 -	03/2020	0 -	0/0
437	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	282.92 -	360.00	3.13	03/2020 -	03/2020	0 -	0/0
438	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR ,	04/2008	490.80 -	490.80	.39	- -	-	-	0/0
439	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	620.57	.00	- -	-	-	0/0
440	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR ,	04/2008	445.25 -	445.25	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
441	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR ,	04/2008	326.20 -	326.20	1.68	-	-	-	0/0
442	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR ,	04/1999	175.69 -	325.00	253.10	-	-	-	0/0
443	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR ,	04/2006	285.07 -	378.56	111.71	-	-	-	0/0
444	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
445	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	-	-	-	0/0
446	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	-	-	-	0/0
447	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	-	-	-	0/0
448	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	304.41 -	304.41	.19	-	-	-	0/0
449	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	-	-	-	0/0
450	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	-	-	-	0/0
451	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	355.81	283.44	-	-	-	0/0
452	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	470.00 -	470.00	40.00	-	-	-	0/0
453	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
454	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	.00	-	-	-	0/0
455	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.00	12/2020 -	12/2020	0 -	0/1
456	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.00	12/2020 -	12/2020	0 -	1/1
457	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
458	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	304.00 632.00	1,195.00	607.24	12/2012 -	03/2022	111 -	0/0
459	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH ,	09/2006	324.90 -	555.00	553.72	03/2010 -	12/2019	117 -	0/3
460	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	826.57 1,160.83	1,160.83	552.18	03/2020 -	03/2020	0 -	1/1
461	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	758.09 -	758.09	782.62	03/2020 -	03/2020	0 -	0/0
462	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	154.06	03/2018 -	03/2018	-	0/0
463	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	-	-	-	0/0
464	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
465	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	394.14 416.86	385.60	336.20	03/2013 -	03/2020	84 -	0/0
466	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT ,	04/2008	1,389.62 2,446.85	2,446.85	2,091.84	03/2014 03/2018	05/2018	-	0/0
467	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	99.58	03/2012 -	03/2019	84 -	0/0
468	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
469	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	567.18 -	975.62	541.05	12/2021 -	12/2021	0 -	0/0
470	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	376.59 -	644.38	74.67	03/2021 -	03/2021	0 -	0/0
471	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	439.88 -	844.10	48.99	- 03/2022	03/2023	- 0	0/0
472	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 1,378.12	858.96	550.66	03/2019 03/2019	03/2022	36(O) 0	0/0
473	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,266.89 -	1,548.66	677.61	12/2021 -	12/2021	0 -	0/0
474	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT ,	04/2010	279.40 384.32	355.00	335.40	- -	-	-	0/0
475	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	196.00	03/2021 03/2019	03/2021	0(O) 0	0/0
476	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	279.71	03/2019 -	12/2019	9 -	0/0
477	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
478	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
479	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
480	JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
481	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	- -	-	-	0/0
482	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	- -	-	-	0/0
483	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	241.26	03/2019 -	03/2019	0 -	0/0
484	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	1,046.88 -	7,000.00	182.77	12/2026 -	12/2026	0 -	0/0
485	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	16,344.71	11/2002 03/2021	03/2021	220(O) 39	0/0
486	MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]ER,JHARKHAND ,	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99(O) 120	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
487	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	-	-	-	0/0
488	GOELKERA-MANOHARPUR (LD)(SER) - [N22000045]RVNL,JHARKHAND ,	03/1997	261.70 -	388.00	382.21	02/2006 -	12/2018	0 -	0/1
489	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND ,	04/2008	167.73 -	167.73	264.07	03/2012 -	-	-	0/0
490	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 309.44	525.81	465.59	12/2015 11/2018	11/2018	35(O) 35	0/0
491	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 258.20	365.00	167.92	- 12/2018	12/2018	- 33	0/0
492	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 148.77	377.00	138.99	12/2016 08/2018	12/2018	24(O) 24	0/0
493	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 1,724.20	1,724.20	188.19	03/2021 03/2021	12/2021	9(O) 9	0/0
494	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	348.23	76.53	03/2021 -	12/2020	0 -	0/0
495	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	227.00 -	2,135.00	134.15	- 12/2024	12/2024	- 0	0/0
496	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	138.00 1,382.78	1,382.78	7.90	- 03/2024	03/2024	- 0	0/0
497	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	913.00 -	1,801.01	8.90	- 12/2023	12/2023	- 0	0/0
498	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	873.61	- -	12/2023	0 -	0/1
499	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	377.93 986.30	986.30	282.37	- -	-	-	0/1
500	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- 12/2023	12/2023	- 0	0/0
501	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	562.74 -	832.47	.94	- 03/2024	03/2024	- 0	0/0
502	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	341.05 -	348.85	.35	- 12/2023	12/2023	- 0	0/0
503	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,127.00	1,041.63	03/2023 -	03/2023	0 -	0/1
504	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	- 0	0/0
505	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	1,117.00 2,841.84	2,841.84	17.97	- 12/2024	12/2024	- 0	0/0
506	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.34	- -	-	-	0/0
507	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	285.57 279.54	279.54	5.03	01/1999 12/2023	12/2023	299(O) 299	0/0
508	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,900.00 1,141.00	1,141.00	625.25	03/2020 03/2020	03/2020	0(O) 0	0/5
509	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	960.00 578.00	578.00	418.85	03/2020 11/2015	03/2020	0(O) 0	0/2
510	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	550.00 1,566.00	2,815.62	255.37	- -	-	-	0/0
511	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 342.85	369.83	421.57	- -	- -	- -	0/0
513	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.70	- -	- -	- -	0/0
514	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	900.00 -	1,431.90	11.88	- -	- -	- -	0/0
515	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.07	- -	- -	- -	0/0
516	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	- -	- -	0/0
517	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,	02/2005	241.00 -	241.00	273.36	03/2014 -	- -	- -	0/0
518	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	470.92 727.13	2,713.09	879.76	03/2021 -	03/2021	0 -	0/0
519	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	- -	- -	0/0
520	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	603.04 2,473.40	1,030.29	932.24	03/2012 03/2019	03/2022	120(O) 120	0/0
521	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,762.94 -	1,762.94	.00	12/2020 -	12/2020	0 -	1/1
522	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.65 -	1,485.85	797.18	12/2020 -	12/2020	0 -	0/0
523	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022	0 -	0/1
524	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	582.13	.00	03/2020 -	03/2020	0 -	0/1
525	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	135.50	03/2019 -	08/2019	5 -	0/0
526	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	737.72 -	737.72	104.10	12/2018 -	12/2018	0 -	0/0
527	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.97	713.16	06/1999 -	- -	- -	0/0
528	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	1,781.98	1,300.41	03/2004 -	03/2020	144 -	0/0
529	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	514.68 2,271.50	2,271.50	1,600.99	03/2021 -	03/2021	0 -	0/0
530	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60 -	0/0
531	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	- -	- -	0/0
532	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	499.30 3,168.29	3,168.29	880.98	03/2023 -	03/2023	0 -	0/0
533	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	277.70 792.89	792.89	254.13	03/2021 -	03/2021	0 -	0/0
534	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	199.12	214.79	03/2019 -	03/2019	0 -	0/0
535	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	297.85 540.02	540.02	145.70	03/2022 -	03/2022	0 -	0/0
536	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	8,857.98	.00	03/2024 -	03/2024	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
537	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0 -	0/0
538	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0 -	0/0
539	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	630.00 1,272.19	1,272.19	91.38	03/2022 -	03/2022	0 -	0/0
540	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,326.00 2,449.91	2,449.91	67.04	03/2023 -	03/2023	0 -	0/0
541	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	4,670.00 3,627.47	3,627.47	108.33	03/2024 -	03/2024	0 -	0/0
542	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	.82	03/2023 -	03/2023	0 -	0/0
543	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	854.00 1,035.16	1,035.16	13.90	03/2023 -	03/2023	0 -	0/0
544	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	912.00 637.95	637.95	19.30	03/2023 -	03/2023	0 -	0/0
545	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	1,514.45 -	1,750.00	1,443.07	03/2020 -	03/2020	0 -	0/0
546	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.22	12/2025 -	03/2025	-9 -	0/0
547	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,273.00 1,908.00	1,908.00	.00	12/2021 -	12/2021	0 -	0/0
548	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	250.50	03/2019 -	03/2019	0 -	0/0
549	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
550	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
551	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	727.56 -	13,809.00	7,765.91	03/2011 -	03/2020	72 -	0/0
552	NEW BG LINE FROM BYRNIAH TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	4,083.02 -	6,000.00	259.12	03/2021 -	03/2021	0 -	0/0
553	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	619.34 -	4,600.00	2,252.69	04/2014 -	03/2020	71 -	0/0
554	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
555	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	-	0/0
556	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	0 -	0/0
557	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	968.28	07/2012 -	-	-	0/0
558	MUNEERABAD-MAHABOONAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	218.24 236.41	645.00	707.07	03/2019 03/2019	03/2019	0(O) 0	0/0
559	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	165 -	0/4
560	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 744.71	1,126.79	761.70	- -	-	-	1/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
561	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
562	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.87	- -	-	-	0/6
563	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	733.00 -	3,040.00	3,000.76	12/2008 -	03/2019	111 -	0/0
564	DEOGHAR - SULTANGANJ (NL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	973.33	1,069.18	12/2012 12/2012	-	-	0/0
565	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	718.54	274.24	05/2019 -	05/2019	0 -	0/0
566	CHHITAUNI TAMKUI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	268.78	96.74	08/2018 -	08/2018	0 -	0/0
567	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	165.93	01/2019 -	01/2019	0 -	0/0
568	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	576.05	- 03/2019	03/2022	- 0	0/0
569	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	585.99	03/2022 03/2019	03/2022	0(O) 0	0/0
570	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	2,878.97	181.91	- -	-	-	0/1
571	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34 -	0/0
572	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46 -	0/0
573	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	553.63 553.63	1,440.00	7.96	- 03/2024	03/2024	- 0	0/0
574	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	- -	-	-	0/0
575	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	0 -	0/0
576	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	- -	-	-	0/0
577	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 346.15	457.08	343.65	- -	-	-	0/0
578	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	63.66	03/2020 -	03/2020	0 -	0/0
579	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	- -	-	-	0/0
580	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	165.82 -	450.00	122.97	03/2020 -	03/2020	0 -	0/0
581	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	523.17 -	1,871.00	1,082.01	- -	03/2018	-	0/0
582	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	601.43 -	1,800.00	98.26	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
583	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	319.58	147.95	- -	-	-	0/0
584	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	290.85	9.31	- -	-	-	0/0
585	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.60	6.96	- -	-	-	0/0
586	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	1,130.13	291.31	- -	-	-	0/0
587	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE ,	04/2011	248.07 -	234.41	161.17	03/2015 -	-	-	0/0
588	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	272.21	- -	-	-	0/0
589	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	321.05	- -	-	-	0/0
590	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	923.52	332.87	- -	-	-	0/0
591	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.91 -	595.91	103.62	- -	-	-	0/0
592	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	160.97	70.86	- -	-	-	0/0
593	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.00	143.44	- -	-	-	0/0
594	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	296.44 -	198.88	85.03	- -	-	-	0/0
595	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.06	11/2018 -	11/2018	0 -	0/0
596	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	251.05	19.69	- -	-	-	0/0
597	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	365.67	1.76	- -	-	-	0/0
598	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	267.09 -	350.78	297.37	- -	-	-	0/0
599	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE ,	04/2011	193.44 -	186.64	152.40	- -	-	-	0/0
600	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	140.05	- -	-	-	0/0
601	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.12	03/2017 -	-	-	0/0
602	NEW ALIPUR TO AKRA MM FOR BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	369.69	31.99	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
603	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.02	- -	-	-	0/0
604	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	186.89	69.96	- -	-	-	0/0
605	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	493.96 -	681.68	143.42	- -	-	-	0/0
606	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE ,	04/2010	423.66 -	720.59	518.14	03/2017 -	-	-	0/0
607	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
608	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	-	-	0/0
609	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,054.35 1,856.95	2,200.00	222.91	- 03/2024	03/2024	- 0	0/0
610	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.54	- -	-	-	0/1
611	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	-	-	0/0
612	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
613	SRINIVASA-PURAMADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- 12/2023	12/2023	- 0	0/0
614	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	970.34 -	2,062.20	674.76	- -	03/2022	0 -	0/2
615	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	337.49 704.31	704.31	119.69	- 03/2020	03/2020	- 0	0/1
616	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,050.00 -	2,132.77	317.57	- 03/2023	03/2023	- 0	0/1
617	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
618	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
619	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	-	-	0/0
620	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
621	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	176.89	- -	-	-	0/0
622	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 466.48	1,000.00	.83	01/1999 12/2024	12/2024	311(O) 311	0/0
623	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	3.38	03/2020 -	03/2020	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
624	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	166.00	- 03/2021	03/2021	- 0	0/0
625	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	422.93	03/2020 03/2020	03/2020	0(O) 0	0/0
626	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,618.00 1,614.59	1,614.59	635.98	- 03/2021	03/2021	- 0	0/0
627	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	720.00 -	678.54	.00	12/2018 -	12/2018	0 -	0/38
628	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 -	28,181.00	.00	- -	-	-	0/0
629	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	295.91	03/2021 -	03/2021	0 -	0/0
630	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
631	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	557.99	12/2023 12/2023	12/2023	0(O) 0	0/0
632	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0 -	0/0
633	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	850.00 -	3,000.00	638.43	03/2015 -	03/2020	60 -	0/0
634	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0 -	0/0
635	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	470.21 -	3,798.80	1,069.54	06/2021 -	06/2021	162 -	0/0
636	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	301.64 -	1,844.47	1,270.29	03/2020 09/2009	03/2020	0(O) 126	0/0
637	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	183.23 -	1,202.70	592.80	02/2015 -	12/2021	82 -	0/0
638	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	366.77	03/2009 03/2009	12/2018	117(O) 106	1/1
639	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	561.81	12/2022 -	03/2023	0 -	0/0
640	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
641	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	679.27 1,539.28	1,539.28	716.89	03/2021 -	03/2021	0 -	0/0
642	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	858.67 843.04	843.04	70.62	03/2021 -	03/2021	0 -	0/0
643	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	178.13	03/2020 -	03/2020	0 -	0/0
644	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	155.50	03/2021 -	03/2021	0 -	0/0
645	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 2,361.74	2,361.74	67.43	03/2021 -	03/2022	12 -	0/0
646	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	81.68	03/2021 -	03/2021	0 -	0/0
647	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	202.87	03/2021 -	03/2021	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
648	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 969.83	969.83	326.40	03/2020 03/2020	06/2020	3(O) 3	0/0
649	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 524.43	939.00	184.09	12/2021 12/2024	12/2024	36(O) 36	0/0
650	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 2,735.00	2,335.67	241.54	12/2024 -	12/2024	0 -	0/0
651	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	960.18 -	970.00	867.19	03/2020 -	03/2020	0 -	0/0
652	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	942.95	874.64	03/2019 -	03/2021	24 -	0/0
653	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA ,	04/2016	5,200.00 -	5,200.00	.00	03/2020 -	03/2020	0 -	0/0
654	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
655	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	1.59	- -	-	-	0/0
656	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	423.40	02/2019 -	02/2019	0 -	0/0
657	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,216.00	630.24	03/2015 -	03/2020	60 -	0/0
658	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN ,	04/2008	653.19 -	1,158.00	723.56	03/2014 03/2019	03/2019	60(O) 60	0/0
659	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	100.17	12/2019 -	06/2019	0 -	0/0
660	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	144.49	10/2018 -	10/2018	0 -	0/0
661	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
662	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
663	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	456.00 295.02	420.18	56.05	12/2019 -	12/2019	0 -	0/0
664	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	150.49	11/2019 -	11/2019	0 -	0/0
665	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN ,	04/2012	288.97 -	346.35	270.36	11/2018 -	11/2018	0 -	0/0
666	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	234.37	02/2019 -	02/2019	0 -	0/0
667	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	2.32	- -	-	-	0/0
668	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	402.91	03/2018 -	12/2019	21 -	0/0
669	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	.00	08/2022 -	08/2022	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
670	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51 -	0/0
671	KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
672	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 495.74	734.01	433.38	06/2013 03/2019	03/2019	69(O) 84	1/4
673	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	404.19 -	2,072.50	1,102.29	- -	-	-	0/0
674	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
675	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	456.00 -	2,300.00	233.59	- -	-	-	0/0
676	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	446.87 527.37	1,105.00	3.34	- -	-	-	0/0
677	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
678	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
679	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
680	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	55.87	- -	03/2020	0 -	0/0
681	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,	02/1997	458.63 -	458.63	.92	03/2015 -	-	-	0/0
682	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,	02/2000	200.84 -	200.84	394.26	03/2014 -	-	-	0/0
683	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	302.02	304.07	03/2005 -	-	-	0/0
684	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	257.00	.00	03/2018 -	03/2018	-	0/0
685	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	0 -	0/0
686	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,	02/2005	600.00 600.00	645.54	671.00	03/2010 -	-	-	0/0
687	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,700.00	.00	03/2022 -	03/2022	0 -	0/0
688	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,	02/2003	199.55 -	330.32	2.12	03/2009 -	-	-	0/0
689	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	.00	03/2020 -	03/2020	0 -	0/0
690	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU ,	02/2006	208.00 -	208.00	3.58	03/2012 -	-	-	0/0
691	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA ,	12/1994	124.43 926.23	1,025.00	1,016.69	- 03/2017	03/2017	-	0/0
692	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	125.00 -	458.26	3.69	07/2008 -	-	-	0/0
693	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	378.56 -	1,160.47	71.23	03/2022 03/2022	03/2022	0(O) 0	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
694	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	546.32	03/2016 -	12/2020	33 -	0/0
695	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 2,911.84	2,911.84	.92	- -	-	-	0/1
696	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	616.08 -	616.08	.00	- -	-	-	0/1
697	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0 -	3/3
698	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	728.10 -	773.94	174.56	12/2024 -	12/2024	0 -	0/0
699	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	184.97	.00	03/2022 -	03/2022	0 -	0/0
700	AGARTALA SABROOM NL NEFR - [N22000099]NFR,TRIPURA ,	04/2008	813.34 -	3,374.00	2,951.92	03/2014 -	03/2020	72 -	0/0
701	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA ,	04/1999	895.00 4,118.00	1,857.00	1,540.32	03/2007 -	04/2016	-	0/0
702	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	252.00 -	580.00	.00	03/2019 -	07/2019	0 -	2/3
703	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
704	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
705	UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH ,	04/2006	325.00 -	1,581.53	618.19	03/2010 -	-	-	0/0
706	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
707	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
708	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH ,	03/2008	195.64 -	474.30	441.25	- -	03/2018	-	0/0
709	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH ,	03/2012	199.75 -	270.00	249.40	08/2018 -	08/2018	0 -	0/0
710	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
711	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
712	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH ,	04/2013	654.00 -	654.00	.00	- -	-	-	0/0
713	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	380.00 -	380.00	4.12	- -	-	-	0/0
714	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
715	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,750.00 -	1,295.42	69.56	03/2022 -	02/2019	-37 -	0/0
716	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	524.00 668.00	668.00	.00	03/2020 -	03/2020	0 -	0/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
717	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	750.55 -	750.56	86.24	12/2024 -	12/2024	0 -	0/0
718	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	977.00	921.55	03/2019 -	03/2020	12 -	0/0
719	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.90 -	1,765.92	213.57	12/2025 -	12/2025	0 -	0/0
720	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	858.40	12/2020 -	03/2021	3 -	0/0
721	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	210.62	03/2020 -	03/2021	12 -	0/0
722	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	.61	03/2018 -	12/2019	9 -	0/0
723	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,	04/1997	233.00 -	318.42	326.10	04/1999 -	-	-	0/0
724	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	.00	04/2016 -	01/2022	0 -	0/0
725	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,900.00	.00	01/2022 -	01/2022	0 -	0/0
726	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,	04/1997	609.04 1,063.00	1,807.88	1,792.10	04/1999 -	11/2018	1 -	0/0
727	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	0 -	0/0
728	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	01/2018	-	0/0
729	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	.00	04/2017 -	10/2022	0 -	0/0
730	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	0 -	0/0
731	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	- -	-	-	0/0
732	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	- -	-	-	0/0
733	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	4,295.30 -	16,216.00	877.71	12/2026 -	03/2026	-9 -	0/0
734	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	36.80 274.41	614.00	266.92	03/2019 -	03/2020	0 -	0/0
735	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 393.46	662.00	182.49	03/2007 03/2025	03/2025	216(O) 0	0/0
736	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
737	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,319.33	837.35	03/2019 12/2009	03/2019	0(O) 111	0/0
738	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,106.62	689.50	12/2010 -	-	-	7/7
739	TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 293.97	749.69	.00	06/2005 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
740	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
741	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.16	03/2014 -	12/2025	141 -	0/0
742	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	1,801.39	03/2016 -	03/2025	108 -	0/0
743	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL ,	04/2010	2,913.51 4,200.00	2,913.50	760.90	03/2016 -	03/2025	108 -	0/0
744	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL ,	04/2009	533.38 -	533.38	144.51	12/2011 -	-	-	0/0
745	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL ,	04/2009	611.03 -	611.03	149.77	12/2011 -	-	-	0/0
746	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL ,	04/2004	293.74 -	229.33	140.60	12/2010 -	-	-	0/0
747	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL ,	04/1999	207.52 -	334.87	334.51	12/2012 -	-	-	0/0
748	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	-	-	0/0
749	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL ,	04/2010	267.37 267.37	620.00	40.77	- 03/2025	03/2025	- 0	0/0
750	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL ,	04/2011	289.64 289.64	981.00	.13	- -	-	-	0/0
751	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL ,	04/2010	221.42 -	380.00	97.41	03/2020 -	03/2020	0 -	0/0
752	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR,WEST BENGAL ,	04/2012	283.55 -	451.00	455.01	03/2019 -	03/2019	0 -	0/0
753	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
754	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL ,	04/2012	255.64 -	272.20	60.68	- -	-	-	0/0
755	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL ,	04/2011	276.69 276.69	426.00	.00	01/1999 03/2030	03/2030	374(O) 374	0/0
756	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL ,	04/2016	556.31 -	612.00	14.25	03/2020 -	03/2020	0 -	0/0
757	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL ,	01/1991	763.18 1,013.45	1,428.00	484.48	12/2021 12/2021	12/2021	0(O) 0	0/0
758	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	484.39	03/2003 03/2030	03/2030	324(O) 108	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		4,07,092.54	6,46,528.15	1,63,916.10				18/105
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
759	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97	262.97	.00	10/2018	10/2018	0	0/0
760	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85	409.85	.00	12/2017	-	-	0/0
761	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17	277.17	.00	04/2017	-	-	0/0
762	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00	391.00	.00	10/2018	10/2018	0	0/0
763	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27	234.27	.00	10/2018	10/2018	0	0/0
764	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00	1,585.00	2,159.63	05/2013	-	-	0/0
765	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00	571.00	582.52	10/2013	12/2018	62	0/0
766	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00	1,535.00	2,993.77	05/2014	-	-	0/0
767	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12	201.12	.00	02/2015	-	-	0/4
768	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61	241.61	7.71	02/2017	-	-	0/1
769	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78	330.00	.00	02/2017	-	-	0/0
770	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30	207.40	44.08	07/2014	-	-	0/1
771	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99	258.99	16.54	07/2014	-	-	0/1

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
772	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/1
773	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	.00	- -	-	-	0/1
774	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	.00	- -	-	-	0/4
775	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	.00	- -	-	-	0/0
776	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH.0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	.00	12/2015 -	-	-	0/2
777	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
778	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	-	-	0/4
779	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	.00	- -	-	-	0/0
780	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	05/2015 -	-	-	2/4
781	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOUT - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	.00	09/2015 -	-	-	0/4
782	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	.00	10/2015 -	-	-	0/0
783	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	.00	12/2015 -	-	-	0/0
784	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	.00	06/2014 -	-	-	0/2
785	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	.00	11/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
786	REHABILITATION AND UPGRADE OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	04/2015 -	-	-	0/0
787	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018	0 -	0/0
788	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
789	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	03/2020	0 -	0/0
790	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2 -	0/0
791	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	.00	06/2017 -	-	-	0/0
792	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	.00	- -	-	-	0/0
793	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	- -	-	-	0/0
794	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
795	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0
796	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2011 -	-	-	0/0
797	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	.00	05/2012 -	-	-	0/0
798	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	-	-	1/4
799	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019	0 -	1/4
800	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	10/2018	0 -	1/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
801	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	.00	06/2018 -	-	-	0/3
802	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	.00	- -	-	-	0/0
803	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	.00	09/2010 -	-	-	0/0
804	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	.00	09/2010 -	-	-	0/0
805	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	-	-	1/4
806	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROMKM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	.00	11/2016 -	-	-	0/0
807	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	.00	06/2016 -	-	-	0/4
808	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	.00	- -	-	-	0/0
809	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	.00	10/2016 -	-	-	0/4
810	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	.00	- -	-	-	0/0
811	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	.00	01/2017 -	01/2020	0 -	0/0
812	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	.00	03/2017 -	-	-	0/0
813	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	.00	04/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
814	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	.00	04/2017 -	-	-	0/0
815	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	.00	04/2017 -	-	-	0/0
816	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	.00	04/2017 -	-	-	0/0
817	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	.00	04/2017 -	-	-	0/0
818	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	.00	04/2017 -	-	-	0/0
819	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	.00	04/2017 -	-	-	0/0
820	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	.00	04/2017 -	-	-	0/0
821	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	.00	04/2017 -	-	-	0/0
822	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	361.00	410.32	02/2009 -	-	-	0/0
823	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	209.80	04/2009 -	-	-	0/0
824	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	106 -	0/0
825	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
826	MAIBANG TO LUMDING (AS-27) KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM ,	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	106 -	0/0
827	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	245.00	214.88	03/2008 -	11/2017	-	0/0
828	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 -	-	-	0/0
829	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	208.00	.00	04/2008 -	-	-	0/0
830	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	160.00	198.82	05/2008 -	-	-	0/0
831	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
832	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	309.56	389.08	04/2010 -	-	-	0/0
833	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	-	-	0/4
834	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	-	-	0/4
835	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	-	-	0/4
836	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	01/2019	0 -	0/4
837	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	11/2018	0 -	0/4
838	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018	0 -	0/4
839	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	.00	05/2017 -	-	-	0/0
840	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	.00	02/2011 -	-	-	0/0
841	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	.00	02/2018 -	-	-	0/0
842	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	.00	02/2018 -	-	-	0/0
843	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429]NHIDCL,ASSAM , EPC	12/2015	225.02 -	159.20	.00	12/2018 -	12/2018	0 -	0/4
844	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM , EPC	12/2015	223.30 -	223.30	.00	06/2018 -	-	-	0/0
845	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	.00	- -	-	-	0/0
846	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	.00	12/2018 -	12/2018	0 -	0/0
847	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	.00	01/2016 -	-	-	0/4
848	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
849	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	880.29	02/2013 -	-	-	0/0
850	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	351.23	05/2013 -	-	-	0/0
851	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR , PPP (ANNUITY)	05/2011	664.00 -	664.00	654.59	02/2014 -	-	-	0/0
852	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54 -	0/0
853	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
854	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	811.54	07/2013 -	12/2018	65 -	0/0
855	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	545.27	11/2013 -	-	-	0/0
856	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR , EPC	01/1991	675.00 -	675.00	.00	- -	-	-	0/0
857	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
858	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
859	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	- -	-	-	0/0
860	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	116.89	04/2019 -	04/2019	0 -	0/0
861	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	.00	- -	-	-	0/0
862	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	.00	04/2018 -	-	-	0/0
863	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	.00	- -	-	-	0/0
864	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	.00	- -	-	-	0/0
865	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	.00	04/2019 -	04/2019	0 -	0/0
866	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
867	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	.00	- -	-	-	0/0
868	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	18.48	04/2018 -	-	-	0/0
869	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
870	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
871	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	.00	03/2014 -	-	-	0/0
872	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
873	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	.00	08/2014 -	-	-	0/0
874	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	.00	07/2016 -	-	-	0/0
875	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
876	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	.00	05/2016 -	-	-	0/0
877	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
878	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	.00	05/2016 -	-	-	0/0
879	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	.00	10/2016 -	-	-	0/0
880	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	.00	07/2016 -	-	-	0/0
881	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	.00	11/2015 -	-	-	0/0
882	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	-	-	0/0
883	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	.00	12/2016 -	-	-	0/0
884	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0 -	0/0
885	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	03/2020	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
886	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	.00	08/2017 -	-	-	0/0
887	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	-	-	-	0/0
888	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	-	-	-	0/0
889	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	-	-	-	0/0
890	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	.00	03/2015 -	-	-	0/0
891	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	.00	03/2015 -	-	-	0/0
892	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	.00	03/2015 -	-	-	0/0
893	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	.00	-	-	-	0/0
894	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH - [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	.00	12/2012 -	-	-	0/0
895	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	.00	-	-	-	0/0
896	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	.00	12/2015 -	-	-	0/0
897	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	-	-	-	0/0
898	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH ,	02/2013	1,232.00 -	1,232.00	1,090.17	08/2015 -	-	-	0/0
899	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	.00	05/2018 -	-	-	0/0
900	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	.00	04/2018 -	-	-	0/0
901	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	.00	04/2018 -	-	-	0/0
902	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	771.18	261.77	-	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
903	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	04/2018 -	-	-	0/1
904	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
905	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	0/4
906	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	0/4
907	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	.00	- -	-	-	0/0
908	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	.00	- -	-	-	0/0
909	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	.00	- -	-	-	0/0
910	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018	71 -	2/3
911	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	974.73	07/2013 -	-	-	0/0
912	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3
913	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	346.60	08/2016 -	-	-	0/0
914	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	.00	- -	-	-	0/0
915	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	.00	- -	-	-	0/0
916	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	.00	- -	-	-	0/0
917	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT ,	05/2016	763.08 -	763.08	.00	- -	-	-	0/0
918	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
919	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT ,	05/2016	364.56 -	364.56	.00	- -	-	-	0/0
920	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT ,	07/2016	829.97 -	829.97	.00	- -	-	-	0/0
921	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT ,	12/2016	417.19 -	417.19	30.19	- -	09/2019	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
922	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	.00	-	-	-	0/0
923	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	.00	06/2020 -	06/2020	0 -	0/0
924	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
925	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101 -	0/0
926	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91 -	0/0
927	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA , PPP (BOT)	05/2011	650.00 -	650.00	832.39	11/2013 -	-	-	0/0
928	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
929	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA ,	10/2015	562.34 -	562.34	109.07	04/2018 -	-	-	0/0
930	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	54.89	06/2016 -	-	-	0/0
931	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	51.47	07/2018 -	07/2018	0 -	0/0
932	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	157.10	04/2019 -	04/2019	0 -	0/0
933	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA , PPP (BOT)	07/2015	1,393.00 -	1,393.00	1,917.27	-	-	-	0/0
934	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
935	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA ,	05/2015	600.85 -	600.85	99.84	05/2018 -	-	-	0/0
936	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	.00	05/2019 -	05/2019	0 -	0/0
937	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	0 -	0/0
938	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	.00	03/2020 -	03/2020	0 -	0/0
939	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29 -	0/0
940	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	104.98	03/2018 -	-	-	0/0
941	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	.00	02/2019 -	02/2019	0 -	0/0
942	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	-	09/2020	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
943	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	-	-	0/0
944	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	.00	- -	-	-	0/0
945	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	.00	06/2020 -	06/2020	0 -	0/0
946	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	03/2019	44 -	0/0
947	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
948	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
949	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	1,216.15	06/2014 -	-	-	0/0
950	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	.00	06/2019 -	06/2019	0 -	0/0
951	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	.00	12/2018 -	12/2018	0 -	0/0
952	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	.00	- -	-	-	0/0
953	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	881.08	06/2015 -	-	-	0/0
954	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	329.10	03/2019 -	03/2019	0 -	0/0
955	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	.00	- -	-	-	0/0
956	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	37.20	08/2018 -	08/2018	0 -	0/0
957	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	10.57	03/2020 -	06/2019	-9 -	0/0
958	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	21.98	03/2020 -	03/2020	0 -	0/0
959	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
960	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
961	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	06/2018	-	3/3

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
962	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
963	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
964	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	346.75	09/2017 -	09/2018	12 -	0/0
965	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
966	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	02/2019	30 -	0/0
967	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	735.94	08/2018 -	08/2018	0 -	0/0
968	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	22.02	03/2019 -	03/2019	0 -	0/0
969	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	7.34	03/2019 -	11/2020	0 -	0/0
970	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0
971	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	167.29	04/2020 -	04/2020	0 -	0/0
972	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	174.94	03/2019 -	03/2019	0 -	0/0
973	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	237.09	08/2019 -	08/2019	0 -	0/0
974	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	39.97	03/2020 -	06/2020	3 -	0/0
975	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	162.19	03/2020 -	05/2020	2 -	0/0
976	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	245.89	08/2012 -	09/2018	73 -	0/0
977	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.43	348.43	231.56	09/2017 08/2018	11/2018	14(O) 14	0/0
978	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.05	352.05	201.35	11/2017 08/2018	10/2018	11(O) 11	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
979	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	47.56	-	-	-	0/0
980	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	.00	06/2018 -	-	-	0/0
981	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	.00	09/2017 -	-	-	0/0
982	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67 -	0/0
983	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
984	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	-	-	0/0
985	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
986	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	-	-	-	0/0
987	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	.00	05/2015 -	-	-	0/0
988	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	-	-	0/0
989	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.00	05/2017 -	-	-	0/0
990	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	-	-	0/0
991	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	-	-	-	0/0
992	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	871.15 -	871.15	332.25	09/2015 -	-	-	0/0
993	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	-	-	0/0
994	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	381.86 -	381.86	252.03	04/2015 -	-	-	0/0
995	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	-	-	0/0
996	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	92.24	-	-	-	0/0
997	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	63.42	-	-	-	0/0
998	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	-	-	0/0
999	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	03/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1000	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHAI,MADHYA PRADESH , EPC	12/2015	927.54 -	927.54	29.17	06/2018 -	-	-	0/0
1001	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	139.75	-	-	-	0/0
1002	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,328.85	11/2015 -	-	-	0/0
1003	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36 -	0/0
1004	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH , PPP (BOT)	01/2016	830.36 -	830.36	315.98	07/2018 -	07/2018	0 -	0/0
1005	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	63.60	-	-	-	0/0
1006	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	375.53	01/2019 -	01/2019	0 -	0/0
1007	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	-	-	0/0
1008	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	.00	01/2019 -	01/2019	0 -	0/0
1009	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	.00	10/2017 -	-	-	0/0
1010	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1011	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1012	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	-	-	-	0/0
1013	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	-	-	-	0/0
1014	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	-	-	-	0/0
1015	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,091.65	03/2013 -	-	-	0/0
1016	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2019	57 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1017	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	5,577.73	02/2014 -	-	-	2/2
1018	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	-	-	0/2
1019	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	-	-	-	0/4
1020	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	-	-	0/12
1021	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	-	-	-	0/4
1022	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	-	-	0/4
1023	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.00	-	-	-	0/0
1024	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	-	-	-	0/0
1025	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	-	-	-	0/0
1026	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	-	-	-	0/0
1027	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	0	0/0
1028	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	157.92	05/2018 -	-	-	0/0
1029	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	-	-	0/0
1030	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	.00	05/2019 -	05/2019	0	0/0
1031	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	45.11	05/2018 -	-	-	0/0
1032	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	31.47	03/2019 -	03/2019	0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1033	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	161.13	05/2018 -	-	-	0/0
1034	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,479.56	07/2017 -	-	-	0/0
1035	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	535.52	11/2016 -	-	-	0/0
1036	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	279.92	06/2006 -	-	-	0/0
1037	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	2,881.81	01/2018 -	-	-	0/0
1038	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,263.02	06/2012 -	-	-	0/0
1039	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	-	-	0/0
1040	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	.00	07/2018 -	07/2018	0 -	0/0
1041	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	11.04	07/2019 -	07/2019	0 -	0/0
1042	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	130.72	07/2019 -	07/2019	0 -	0/0
1043	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	.00	07/2018 -	07/2018	0 -	0/0
1044	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	.00	- -	-	-	0/0
1045	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1046	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	- -	-	-	0/0
1047	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	-	-	0/0
1048	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	.00	03/2019 -	03/2019	0 -	0/0
1049	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	.00	03/2019 -	03/2019	0 -	0/0
1050	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1051	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA ,	01/2017	244.90 -	244.90	43.29	05/2019 -	05/2019	0 -	0/0
1052	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA ,	02/2017	904.16 -	904.16	34.61	02/2020 -	05/2020	3 -	0/0
1053	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	03/2020	0 -	0/0
1054	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0 -	0/0
1055	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	113.04	03/2020 -	05/2020	2 -	0/0
1056	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI, MAHARASHTRA ,	03/2017	988.34 -	1,043.28	133.93	03/2020 -	08/2020	5 -	0/0
1057	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI, MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	10.00	03/2017 -	11/2020	44 -	0/0
1058	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA ,	03/2017	296.19 -	254.00	86.42	03/2020 -	05/2019	-10 -	0/0
1059	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	.00	03/2020 -	03/2020	0 -	0/0
1060	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI, MAHARASHTRA ,	12/2017	404.94 -	404.94	.00	- -	-	-	0/0
1061	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI, MAHARASHTRA ,	01/2018	607.00 -	607.00	.00	- -	-	-	0/0
1062	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA ,	01/2018	621.00 -	621.00	.00	- -	-	-	0/0
1063	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	673.92	01/2014 -	08/2018	55 -	0/0
1064	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD, MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	.00	02/2011 -	-	-	0/0
1065	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA ,	12/2015	479.20 -	479.20	6.14	05/2018 -	-	-	0/0
1066	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD, MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	.00	03/2011 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1067	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	.00	10/2010 -	-	-	0/0
1068	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0
1069	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	-	-	0/0
1070	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	-	-	2/2
1071	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,489.54	08/2014 -	-	-	0/0
1072	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,135.19	03/2014 -	-	-	0/0
1073	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76 -	0/0
1074	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	1,928.22	2,211.94	04/2015 -	-	-	0/0
1075	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	-	-	-	0/0
1076	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1077	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	.00	-	-	-	0/0
1078	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1079	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	.00	08/2016 -	08/2019	0 -	0/0
1080	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	.00	08/2016 -	08/2019	0 -	0/0
1081	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	.00	08/2016 -	08/2019	0 -	0/0
1082	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	.00	04/2017 -	-	-	0/0
1083	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	.00	09/2018 -	09/2018	0 -	0/0
1084	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	09/2018	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1085	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	09/2018	0 -	0/0
1086	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	09/2018	0 -	0/0
1087	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	09/2018	0 -	0/0
1088	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	09/2018	0 -	0/0
1089	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	09/2018	0 -	0/0
1090	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	.00	09/2018 -	09/2018	0 -	0/0
1091	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	.00	09/2018 -	09/2018	0 -	0/0
1092	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	.00	09/2018 -	09/2018	0 -	0/0
1093	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	.00	09/2018 -	09/2018	0 -	0/0
1094	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	09/2018	0 -	0/0
1095	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	09/2018	0 -	0/0
1096	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	09/2018	0 -	0/0
1097	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	-	-	0/0
1098	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,613.62	06/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1099	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1100	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	.00	10/2016 -	-	-	0/0
1101	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1102	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	.00	01/2017 -	-	-	0/0
1103	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	-	-	0/0
1104	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	0 -	0/0
1105	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	.00	11/2017 -	-	-	0/0
1106	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	.00	08/2015 -	-	-	0/0
1107	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	-	-	0/0
1108	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0 -	0/0
1109	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	.00	-	-	-	0/0
1110	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	.00	05/2016 -	-	-	0/0
1111	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	.00	04/2018 -	-	-	0/0
1112	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	.00	10/2017 -	-	-	0/0
1113	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	.00	10/2017 -	-	-	0/0
1114	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	.00	05/2016 -	-	-	0/0
1115	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	.00	01/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1116	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	.00	06/2016 -	-	-	0/0
1117	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	.00	06/2018 -	11/2018	0 -	0/0
1118	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	.00	05/2016 -	-	-	0/0
1119	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	.00	03/2020 -	-	-	0/0
1120	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	-	-	0/0
1121	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	.00	- -	-	-	0/0
1122	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1123	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	-	-	0/0
1124	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	-	-	0/0
1125	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1126	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	-	-	0/0
1127	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	-	-	0/0
1128	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	.00	- -	-	-	0/0
1129	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1130	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1131	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	-	-	0/0
1132	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1133	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1134	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1135	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1136	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB ,	01/2014	523.85 -	523.85	170.68	01/2016 -	-	-	0/0
1137	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1138	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1139	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1140	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1141	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0
1142	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1143	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1144	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1145	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1146	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	17.85	- -	-	-	0/0
1147	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	391.33	- -	-	-	0/0
1148	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB ,	12/2015	239.23 -	239.23	123.47	12/2017 -	-	-	0/0
1149	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	4.88	12/2017 -	04/2019	16 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1150	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1151	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1152	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	.00	09/2019 -	09/2019	0 -	0/0
1153	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	59.82	- -	04/2020	0 -	0/0
1154	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	.00	03/2020 -	03/2020	0 -	0/0
1155	CHAMBAL BRIDGE NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN ,	12/2003	275.00 -	281.31	168.31	02/2010 -	-	-	0/0
1156	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN , PPP (BOT)	01/2011	593.00 -	593.00	1,036.26	07/2013 -	-	-	0/0
1157	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI,RAJASTHAN ,	03/2014	240.10 -	240.10	151.72	03/2016 -	-	-	0/0
1158	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1159	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1160	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1161	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1162	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	-	-	0/0
1163	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	.00	06/2018 -	-	-	0/0
1164	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN ,	08/2015	538.08 -	538.08	30.08	02/2018 -	-	-	0/0
1165	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30 -	0/0
1166	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN ,	08/2015	482.27 -	482.27	297.50	02/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1167	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN ,	07/2015	455.60 -	455.60	54.50	07/2017 -	-	-	0/0
1168	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN ,	11/2014	279.14 -	279.14	211.04	05/2017 -	09/2018	16 -	0/0
1169	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN ,	10/2014	264.72 -	264.72	98.18	04/2017 -	-	-	0/0
1170	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN ,	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8 -	0/0
1171	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	-	-	0/0
1172	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	-	-	0/0
1173	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	596.06	10/2017 -	-	-	0/0
1174	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27 -	0/0
1175	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	620.00	04/2018 -	12/2018	8 -	0/0
1176	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1177	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/0
1178	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 -	10/2018	33 -	0/0
1179	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	223.48	- -	10/2018	0 -	0/0
1180	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	474.40	06/2019 -	09/2019	3 -	0/0
1181	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	.00	06/2019 -	06/2019	0 -	0/0
1182	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	06/2019	0 -	0/0
1183	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1184	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	.00	10/2018 -	10/2018	0 -	0/0
1185	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	170.51	01/2019 -	01/2019	0 -	0/0
1186	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	.00	- -	-	-	0/0
1187	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	.00	- -	-	-	0/0
1188	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	.00	- -	-	-	0/0
1189	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	.00	04/2020 -	04/2020	0 -	0/0
1190	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	.00	10/2017 -	-	-	0/0
1191	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	-	-	0/0
1192	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	.00	08/2013 -	-	-	0/0
1193	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	.00	08/2013 -	-	-	0/0
1194	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1195	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	.00	10/2017 -	-	-	0/0
1196	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60 -	0/0
1197	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	322.45	06/2013 -	-	-	0/0
1198	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67 -	0/0
1199	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64 -	0/0
1200	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0
1201	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1202	REHABILITATION AND UPGRADE OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1203	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1204	FOUR LANNING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANNING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	830.16	11/2017 -	05/2019	18 -	0/0
1205	TWO LANNING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2019	18 -	0/0
1206	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1207	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU ,	11/2014	563.92 -	563.92	186.50	11/2016 -	-	-	0/0
1208	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	761.19	07/2008 -	-	-	0/0
1209	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	164.24	08/2018 -	06/2019	0 -	0/0
1210	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	204.31	07/2018 -	07/2018	0 -	0/0
1211	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	5.00	03/2020 -	03/2020	0 -	0/0
1212	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33 -	0/0
1213	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	-	-	0/0
1214	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	.00	09/2017 -	-	-	0/0
1215	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	-	-	0/0
1216	SIX LANNING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	.00	- -	-	-	0/0
1217	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,399.30	09/2016 -	06/2019	33 -	0/0
1218	REHABILITATION AND UPGRADE OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	3/4
1219	REHABILITATION AND UPGRADE OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	3/4

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1220	YAN TO NIRMAL SEREABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	1/4
1221	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	.00	03/2016 -	-	-	0/2
1222	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1223	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	.00	12/2016 -	-	-	0/4
1224	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1225	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1226	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1227	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	454.64	11/2018 -	03/2019	0 -	0/0
1228	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1229	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	36.90	03/2018 -	-	-	0/4
1230	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	-	-	0/4
1231	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,986.56	08/2013 -	-	-	0/0
1232	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1233	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	411.64	01/2014 -	09/2018	56 -	0/0
1234	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,898.25	09/2015 -	-	-	0/0
1235	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	.00	- -	-	-	0/0
1236	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	.00	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1237	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	.00	10/2016 -	-	-	0/0
1238	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	211.01	05/2017 -	-	-	0/0
1239	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	409.92	01/2016 -	-	-	0/0
1240	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	223.82	09/2016 -	-	-	0/0
1241	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	187.43	01/2016 -	-	-	0/0
1242	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	566.34	01/2016 -	-	-	0/0
1243	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	.00	03/2017 -	-	-	0/0
1244	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1245	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	.00	10/2016 -	-	-	0/0
1246	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	.00	03/2018 -	-	-	0/0
1247	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	-	-	0/0
1248	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	.00	10/2016 -	-	-	0/0
1249	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	.00	03/2017 -	-	-	0/0
1250	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH ,	09/2015	768.56 -	768.56	1,643.18	03/2018 -	-	-	0/0
1251	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH ,	09/2015	664.53 -	664.53	1,494.46	03/2018 -	-	-	0/0
1252	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH ,	09/2015	789.31 -	789.31	372.34	03/2018 -	-	-	0/0
1253	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.01	03/2018 -	-	-	0/0
1254	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	1,825.00	01/2019 -	01/2019	0 -	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1255	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	596.99	06/2016 -	-	-	0/0
1256	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	235.71	06/2018 -	-	-	0/0
1257	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	228.89	06/2018 -	-	-	0/0
1258	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	195.03	07/2018 -	-	-	0/0
1259	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	247.31	06/2018 -	-	-	0/0
1260	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	.00	08/2015 -	-	-	0/0
1261	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	-	-	-	0/0
1262	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	-	-	-	0/0
1263	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	359.94	-	-	-	0/0
1264	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI,UTTAR PRADESH ,	01/2016	701.12 -	701.12	841.92	05/2019 -	05/2019	0	0/0
1265	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	.00	06/2019 -	06/2019	0	0/0
1266	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	115.21	04/2019 -	04/2019	0	0/0
1267	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	28.08	-	-	-	0/0
1268	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	83.05	-	-	-	0/0
1269	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	70.80	04/2019 -	04/2019	0	0/0
1270	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	.00	04/2019 -	04/2019	0	0/0
1271	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	.00	-	-	-	0/0
1272	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	.00	-	07/2020	0	0/0
1273	4-LANNING OF NAGINA-KSHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	.00	-	04/2020	0	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1274	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	149.36	04/2019 -	04/2019	0 -	0/0
1275	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	49.05	- -	-	-	0/0
1276	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	165.66	- -	-	-	0/0
1277	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	.00	03/2020 -	03/2020	0 -	0/0
1278	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	.00	03/2020 -	03/2020	0 -	0/0
1279	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	.00	03/2020 -	03/2020	0 -	0/0
1280	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	314.52	03/2020 -	03/2020	0 -	0/0
1281	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	.00	- -	-	-	0/0
1282	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1283	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1284	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1285	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	12/2018	57 -	0/0
1286	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	.00	- -	-	-	0/0
1287	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	.00	- -	-	-	0/0
1288	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018	0 -	0/0
1289	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	.00	05/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1290	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	.00	06/2018 -	-	-	0/0
1291	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	.00	05/2018 -	-	-	0/0
1292	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,436.15	08/2013 -	-	-	0/0
1293	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,952.35	08/2013 -	-	-	0/0
1294	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,811.29	09/2014 -	-	-	0/0
1295	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	464.39	07/2014 -	-	-	0/0
1296	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1297	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	.00	-	12/2019	0	0/0
1298	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	05/2019	11	0/0
1299	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	2,313.68	-	-	-	0/0
1300	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	35.17	11/2018 -	11/2018	0	0/0
1301	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	123.31	08/2018 -	08/2018	0	0/0
	Total		3,58,175.11 -	3,64,610.12	1,36,649.82				23/182
	SHIPPING AND PORTS								
1302	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU, MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	413.91	12/2010 -	12/2018	35	0/0
1303	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1304	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1305	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL, TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	275.98	275.98	12/2017 -	-	-	1/1
1306	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL, TAMIL NADU ,	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	9	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		3,788.29	4,230.74	1,662.35				1/1
	<u>TELECOMMUNICATIONS</u>								
1307	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26	418.26	172.30	06/2017	-	-	0/0
1308	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL, GUJARAT , Central Sector Projects	09/2017	171.54	171.54	.00	05/2018 08/2018	08/2018	3(O) 4	0/0
1309	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	159.30	159.30	12.40	04/2018 08/2018	08/2018	4(O) 4	0/0
1310	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	167.68	167.68	30.21	04/2018 08/2018	08/2018	4(O) 4	0/0
1311	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	212.70	212.70	37.08	05/2018 08/2018	08/2018	3(O) 3	0/0
1312	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL, MAHARASHTRA , Central Sector Projects	08/2017	215.30	215.30	.00	05/2018 10/2018	10/2018	5(O) 5	0/0
1313	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL, MAHARASHTRA , Central Sector Projects	01/2018	231.80	231.80	.00	10/2018 10/2018	10/2018	0(O) 0	0/0
1314	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 24,664.00	24,664.00	8,397.00	07/2015 05/2020	05/2020	58(O) 58	0/0
1315	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI, MULTI STATE , Central Sector Projects	09/2014	2,111.17	2,011.17	253.90	09/2014	-	-	0/70
1316	UP (EAST) ACCESS LOT1 - [N26000112]BSNL, UTTAR PRADESH ,	11/2017	169.45	169.45	77.74	08/2018 08/2018	08/2018	0(O) 0	0/0
	Total		17,191.20	28,421.20	8,980.63				0/70
	<u>URBAN DEVELOPMENT</u>								
1317	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD, ANDHRA PRADESH ,	06/2014	157.84	157.84	132.01	03/2017	-	-	4/5
1318	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH ,	08/2007	246.90	246.90	.00	-	-	-	0/0
1319	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD, ANDHRA PRADESH ,	01/2018	206.58	206.58	.02	03/2019	03/2019	0	0/7
1320	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR ,	02/2016	496.18 496.00	498.99	27.09	06/2017	06/2020	36	0/0
1321	DELHI MRTS PHASE-III - [N28000056]DMRCL, DELHI ,	09/2011	38,585.00	38,585.00	34,270.32	03/2016	-	-	0/0

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1322	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	247.73	10/2019 -	03/2020	5 -	0/7
1323	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	620.49	12/2015 -	07/2018	30 -	0/0
1324	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,336.53	11/2019 -	11/2019	0 -	3/7
1325	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	5.03	04/2019 -	04/2019	0 -	0/2
1326	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1327	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	.00	05/2020 -	05/2020	0 -	0/0
1328	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	1.50	06/2019 -	06/2019	0 -	0/0
1329	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 -	422.00	.00	- -	-	-	0/0
1330	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 -	392.00	.00	- -	-	-	0/0
1331	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	.00	04/2018 -	-	-	0/0
1332	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019	0 -	0/0
1333	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 210.00	270.83	159.42	11/2014 -	12/2018	38 -	2/8
1334	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	41.21	03/2016 -	12/2019	43 -	1/6
1335	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13 -	0/0
1336	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	15.95	02/2020 09/2020	09/2020	7(O) 7	0/0
1337	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	66 -	1/5
1338	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA ,	07/2012	5,181.79 -	5,181.79	.00	07/2017 -	12/2019	29 -	0/0
1339	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	3.60	03/2020 06/2020	03/2020	0(O) 0	0/7

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1340	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]CPWD,MADHYA PRADESH , EPC	05/2016	164.00 -	164.00	111.06	11/2018 09/2018	09/2018	-2(O) -2	8/11
1341	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA ,	02/2011	241.33 349.33	349.33	307.50	03/2016 12/2017	04/2018	-	0/13
1342	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	3,669.58	03/2018 -	12/2019	21 -	0/0
1343	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	-	-	0/0
1344	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	.00	07/2020 09/2018	09/2020	2(O) 2	0/14
1345	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44 -	0/10
1346	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 -	388.00	354.09	05/2017 08/2018	08/2018	15(O) 15	7/12
1347	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 -	294.00	95.08	04/2019 06/2019	06/2019	2(O) 2	3/8
1348	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	549.31	126.11	07/2019 -	07/2019	0 -	0/0
1349	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU ,	04/2014	332.72 -	342.00	316.94	09/2016 03/2018	09/2018	24(O) 24	0/0
1350	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 12/2018	12/2018	36(O) 28	12/24
1351	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	26.00	10/2019 -	10/2019	0 -	0/6
1352	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/0
1353	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	.00	- -	-	-	0/0
1354	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	3.72	03/2020 -	03/2020	0 -	0/5
1355	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	0 -	0/0
1356	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	.00	03/2020 -	03/2020	0 -	0/0
1357	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	0 -	0/0
1358	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL ,	02/2014	156.57 -	156.57	138.67	08/2016 -	11/2018	27 -	8/15
1359	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	67.79	04/2018 -	07/2019	1 -	2/6

Detail of ongoing Projects Costing Rs.150 Crore and above.

(All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(July 2018)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		1,44,199.91 -	1,49,477.76	65,471.13				51/178
	<u>DEFENCE PRODUCTION</u>								
1360	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	170.37	73.70	05/2018 -	05/2018	-	5/10
1361	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020	0 -	4/8
	Total		453.64 -	461.66	123.65				9/18
	Grand Total		16,78,634.82	20,16,360.99	7,68,186.93				2212/4125


Summary of projects in the Flash Report for the month of July, 2018

Project Implementation - Current Status:

Number of Projects in Previous Month	1362
Number of Projects completed/dropped/frozen in Current Month	10
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	8
Number of Projects in Current Month	1361

Brief Analysis

Project Status with respect to Original Schedule: Out of 1361 projects, 19 projects are ahead of schedule, 386 projects are on schedule 296 projects are delayed. 622 projects do not have fixed dates of commissioning. 38 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

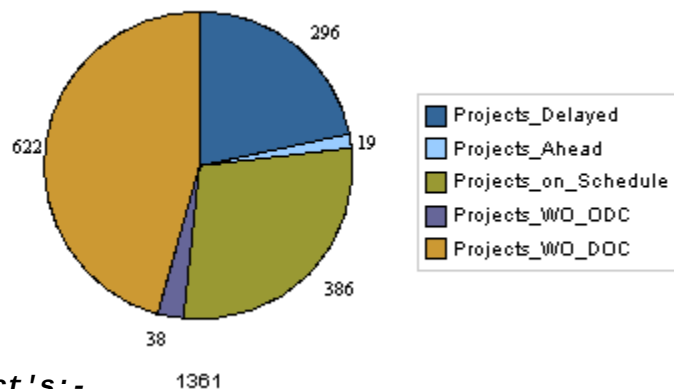


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1361 projects when sanctioned, was of the order of Rs. 1678634.82 crore but this was subsequently revised to Rs. 2016360.99 crore implying a cost overrun of 20.1%. The expenditure incurred on these projects till July, 2018 is Rs. 768186.93 crore, which is 38.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

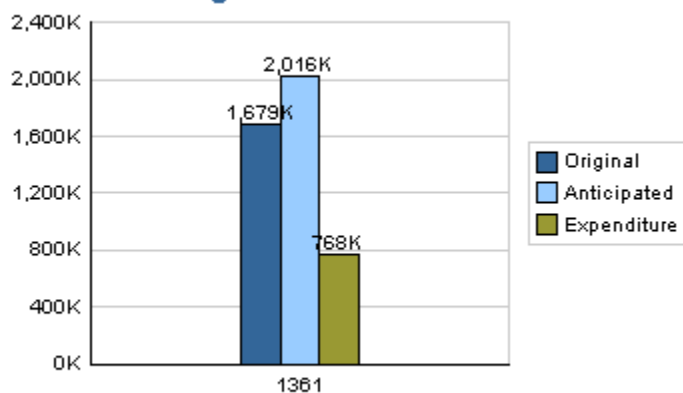

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

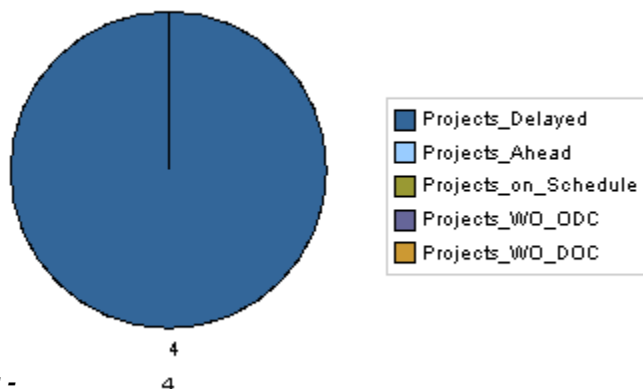


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 74849 crore implying a cost overrun of 11.5%. The expenditure incurred on these projects till July, 2018 is Rs. 36056.69 crore, which is 48.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

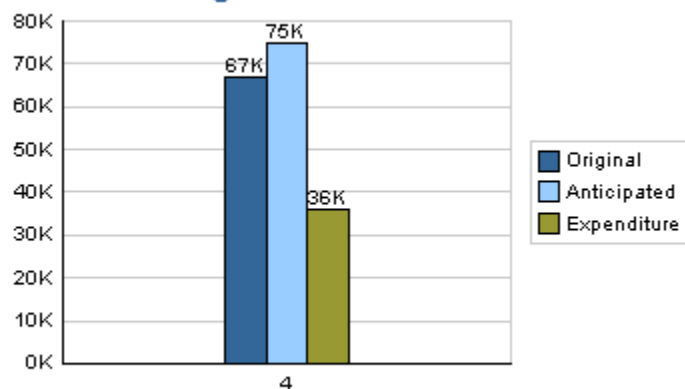

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	2
Number of Projects Delayed	2

Brief Analysis


Project Status with respect to Original Schedule: Out of 2 projects, 2 projects are delayed.



Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 624.07 crore but this was subsequently anticipated to Rs. 994.86 crore implying a cost overrun of 59.4%. The expenditure incurred on these projects till July, 2018 is Rs. 632.48 crore, which is 63.6% of the anticipated cost of the projects.

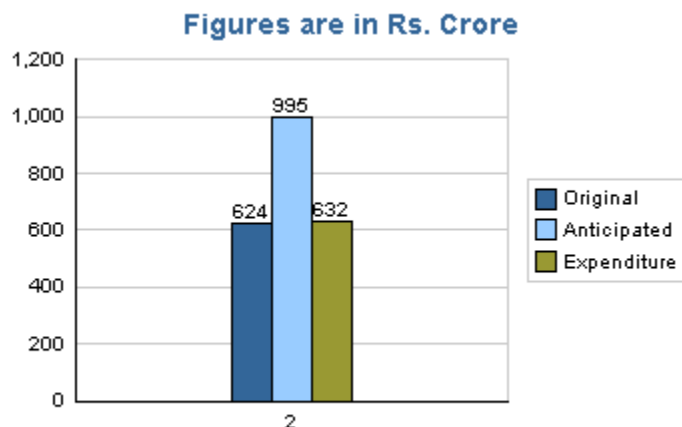

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	94
Number of Projects On Schedule	47
Number of Projects Delayed	35
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 94 projects, 1 project is ahead of schedule, 47 projects are on schedule 35 projects are delayed. 11 projects do not have fixed dates of commissioning.

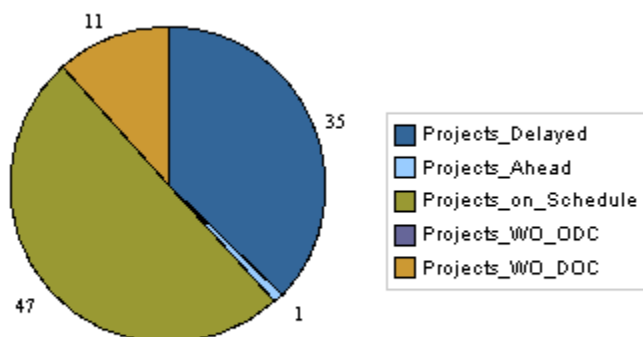


Total No Of Project's:-

94

Investment Scenario

Total original cost of implementation of 94 projects when sanctioned, was of the order of Rs. 91364.09 crore but this was subsequently anticipated to Rs. 90827.28 cr The expenditure incurred on these projects till July, 2018 is Rs. 27126.67 crore, which is 29.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

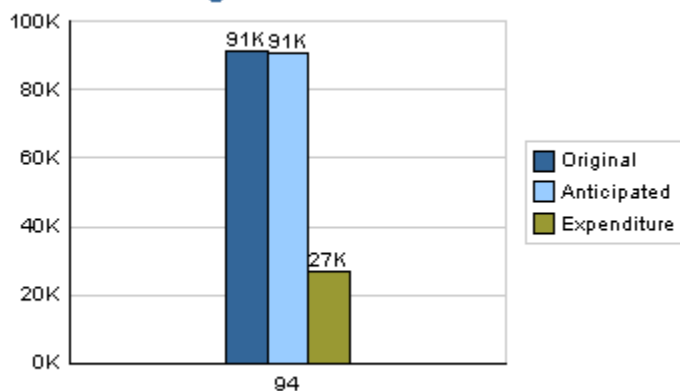

Sector wise current status of projects on the Flash Report

FERTILISERS


Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule 1 project is delayed. 1 project does not have fixed dates of commissioning.

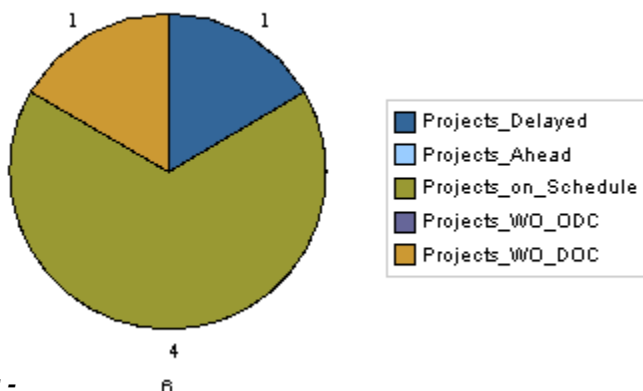


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 1781.92 crore but this was subsequently anticipated to Rs. 1793.57 crore implying a cost overrun of .7%. The expenditure incurred on these projects till July, 2018 is Rs. 598.32 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

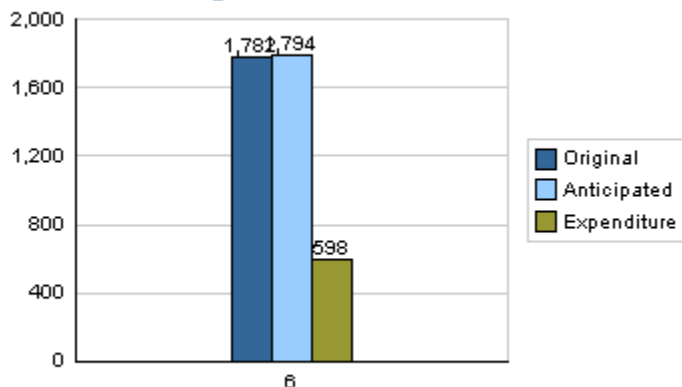

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	4
Number of Projects On Schedule	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are on schedule

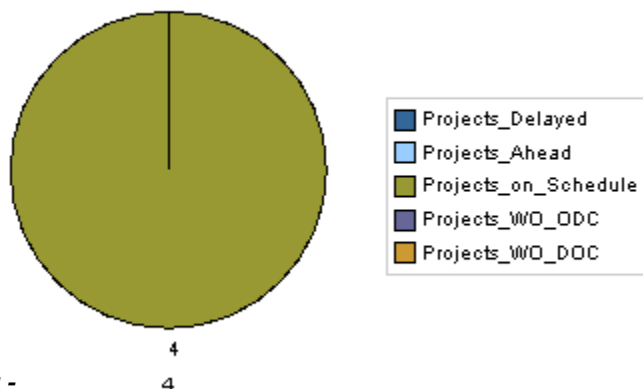


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 6912 crore but this was subsequently anticipated to Rs. 6912 crore. The expenditure incurred on these projects till July, 2018 is Rs. 426.27 crore, which is 6.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

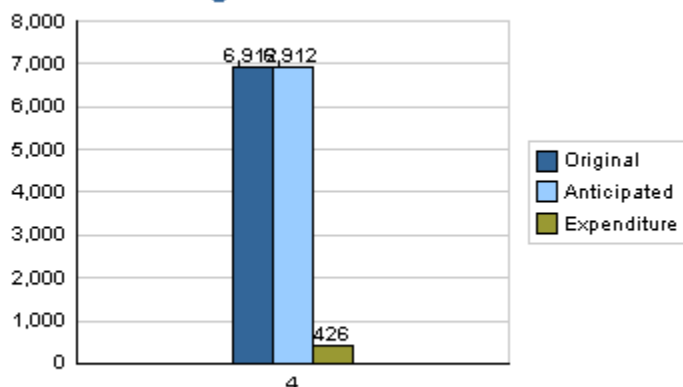

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	28
Number of Projects On Schedule	2
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning 13

Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 2 projects are on schedule 13 projects are delayed. 13 projects do not have fixed dates of commissioning.

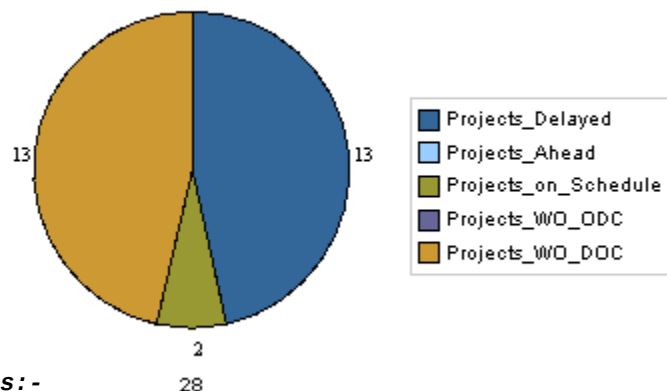


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 28 projects when sanctioned, was of the order of Rs. 37451.14 crore but this was subsequently anticipated to Rs. 37664.82 crore implying a cost overrun of .6%. The expenditure incurred on these projects till July, 2018 is Rs. 27402.32 crore, which is 72.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

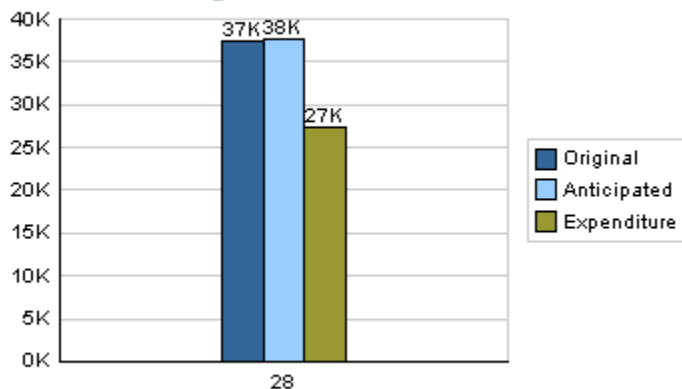

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	136
Number of Projects On Schedule	89
Number of Projects Delayed	24
Number of Projects Ahead	9
Number of Projects Without Date Of Commissioning	14

Brief Analysis

Project Status with respect to Original Schedule: Out of 136 projects, 9 projects are ahead of schedule, 89 projects are on schedule 24 projects are delayed. 14 projects do not have fixed dates of commissioning.

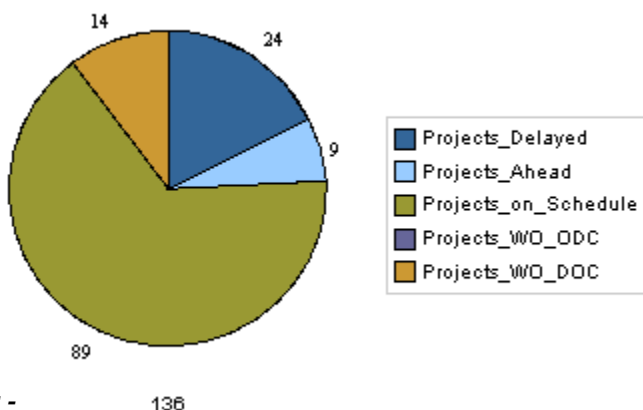


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 217011.11 crore but this was subsequently anticipated to Rs. 217989.15 crore implying a cost overrun of .5%. The expenditure incurred on these projects till July, 2018 is Rs. 61469.73 crore, which is 28.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

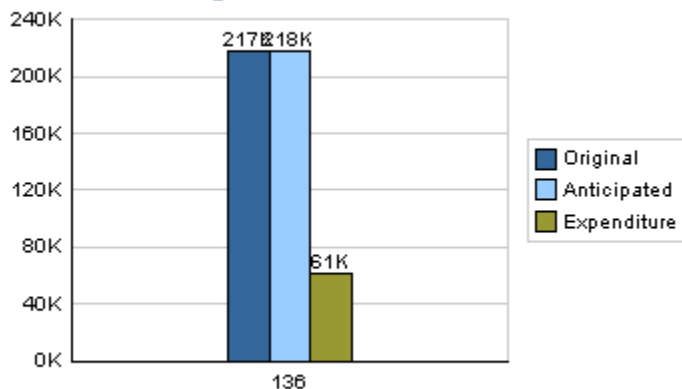

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	110
Number of Projects On Schedule	37
Number of Projects Delayed	65
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 110 projects, 1 project is ahead of schedule, 37 projects are on schedule 65 projects are delayed. 7 projects do not have fixed dates of commissioning.

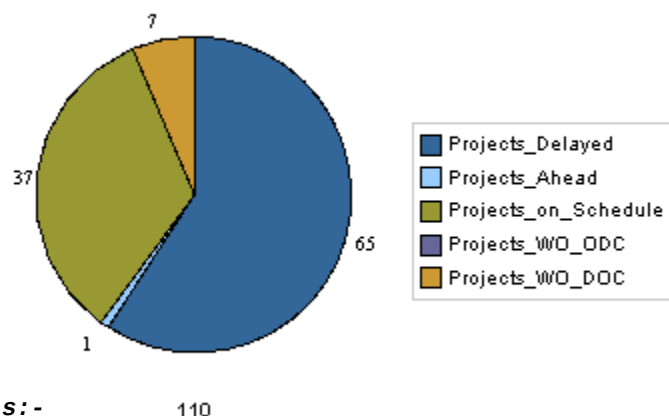


Total No Of Project's:-

110

Investment Scenario

Total original cost of implementation of 110 projects when sanctioned, was of the order of Rs. 313586.68 crore but this was subsequently anticipated to Rs. 377560.5 crore implying a cost overrun of 20.4%. The expenditure incurred on these projects till July, 2018 is Rs. 232240.73 crore, which is 61.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

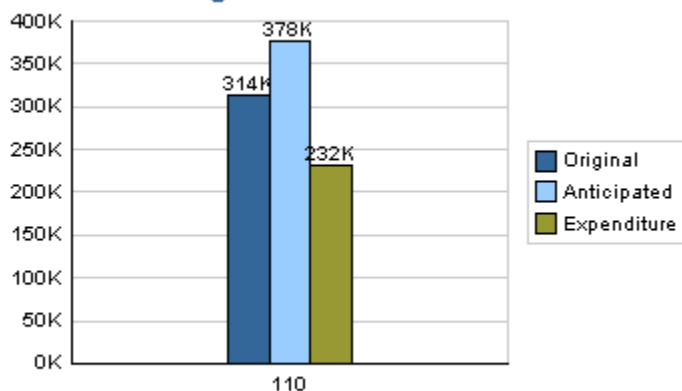

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY

Current Status:


Number of Projects 2

Number of Projects Delayed 1

Number of Projects Without Date Of Commissioning 1

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is delayed. 1 project does not have fixed dates of commissioning.

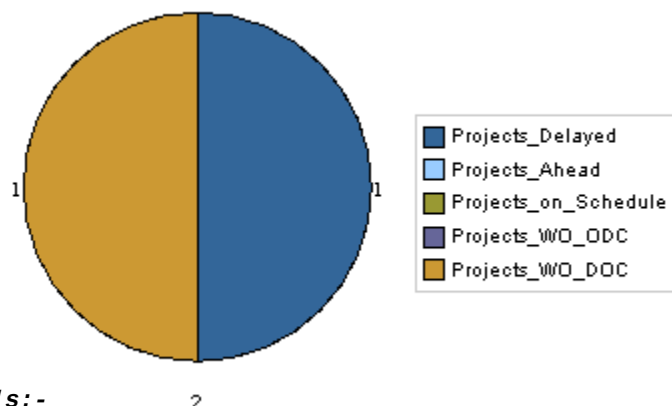


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till July, 2018 is Rs. 2450.86 crore, which is 45.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

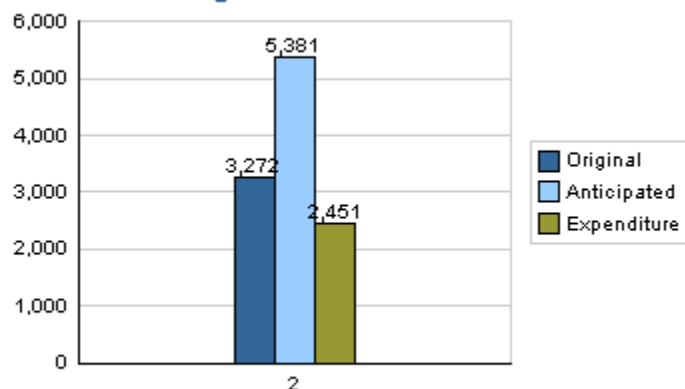

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	22
Number of Projects On Schedule	8
Number of Projects Delayed	6

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 8 projects are on schedule 6 projects are delayed. 3 projects do not have fixed dates of commissioning. 5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

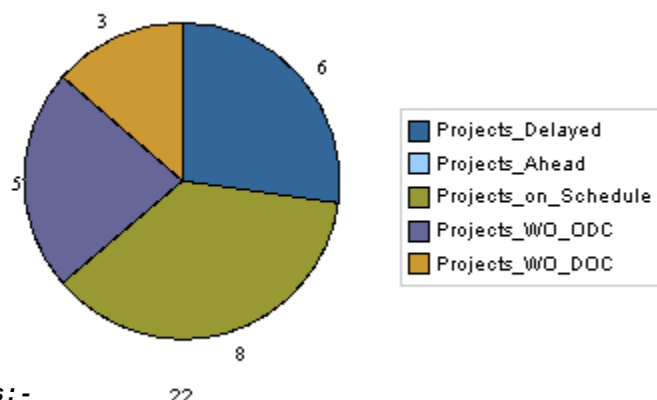


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 22 projects when sanctioned, was of the order of Rs. 8611.12 crore but this was subsequently anticipated to Rs. 8658.88 crore implying a cost overrun of .6%. The expenditure incurred on these projects till July, 2018 is Rs. 2979.18 crore, which is 34.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

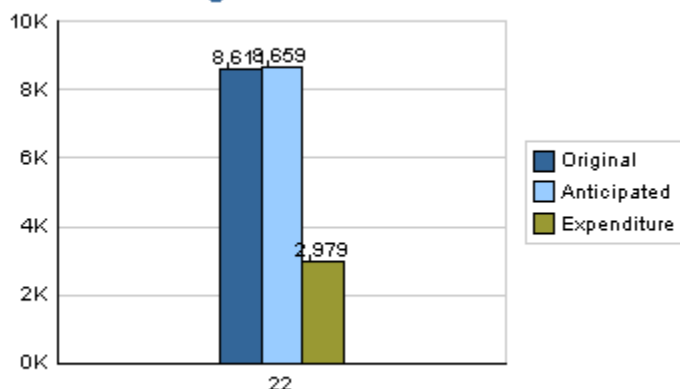

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	350
Number of Projects On Schedule	92
Number of Projects Delayed	65
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	25
Number of Projects Without Date Of Commissioning	163

Brief Analysis

Project Status with respect to Original Schedule: Out of 350 projects, 5 projects are ahead of schedule, 92 projects are on schedule 65 projects are delayed. 163 projects do not have fixed dates of commissioning. 25 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

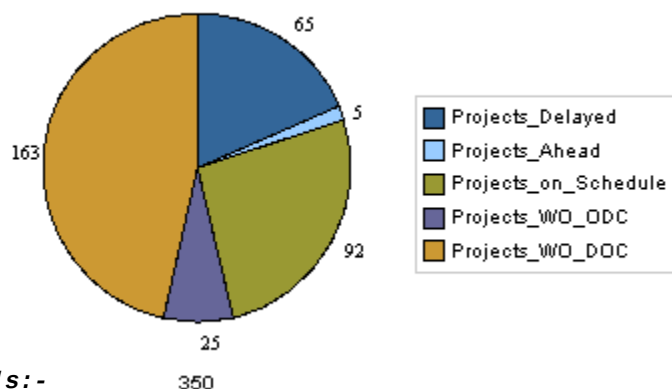

Investment Scenario

Total original cost of implementation of 350 projects when sanctioned, was of the order of Rs. 407092.54 crore but this was subsequently anticipated to Rs. 646528.15 crore implying a cost overrun of 58.8%. The expenditure incurred on these projects till July, 2018 is Rs. 163916.1 crore, which is 25.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

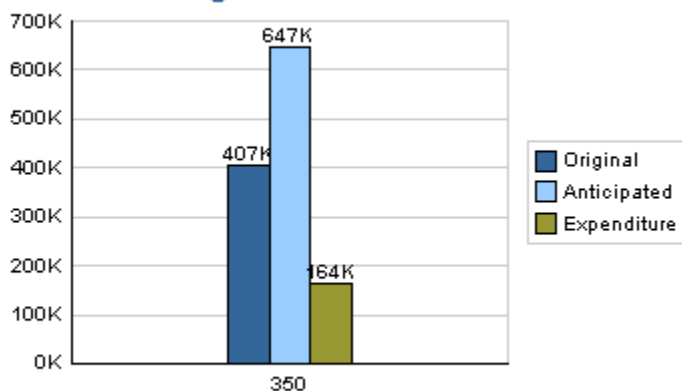

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	543
Number of Projects On Schedule	88
Number of Projects Delayed	53
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	8
Number of Projects Without Date Of Commissioning	392

Brief Analysis

Project Status with respect to Original Schedule: Out of 543 projects, 2 projects are ahead of schedule, 88 projects are on schedule 53 projects are delayed. 392 projects do not have fixed dates of commissioning. 8 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

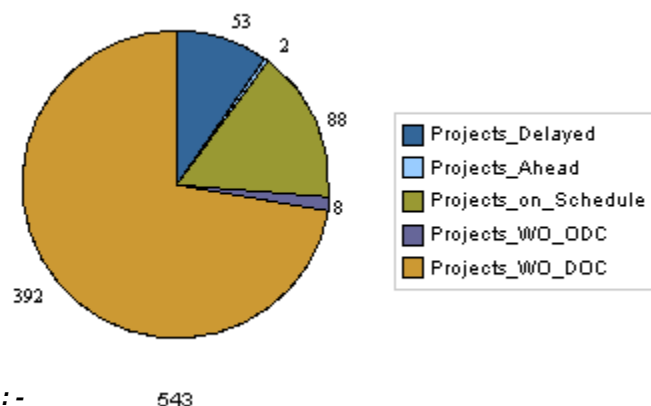


Total No Of Project's:-

543

Investment Scenario

Total original cost of implementation of 543 projects when sanctioned, was of the order of Rs. 358175.11 crore but this was subsequently anticipated to Rs. 364610.12 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till July, 2018 is Rs. 136649.82 crore, which is 37.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

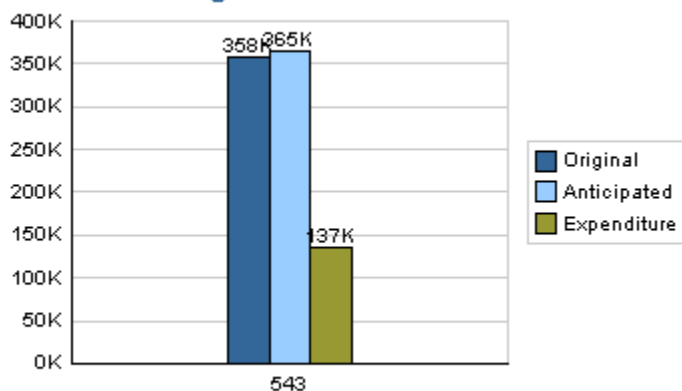

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects 5

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

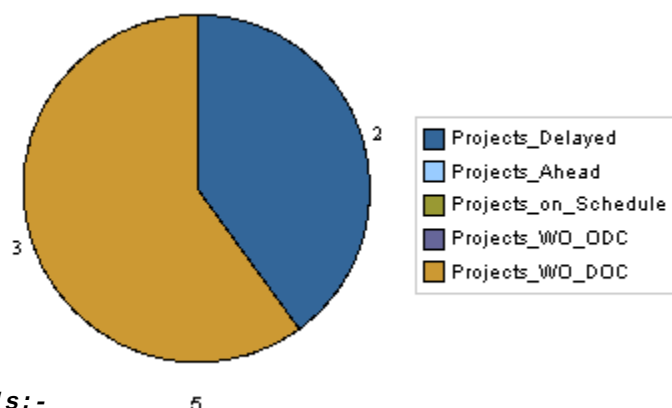


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 3788.29 crore but this was subsequently anticipated to Rs. 4230.74 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till July, 2018 is Rs. 1662.35 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

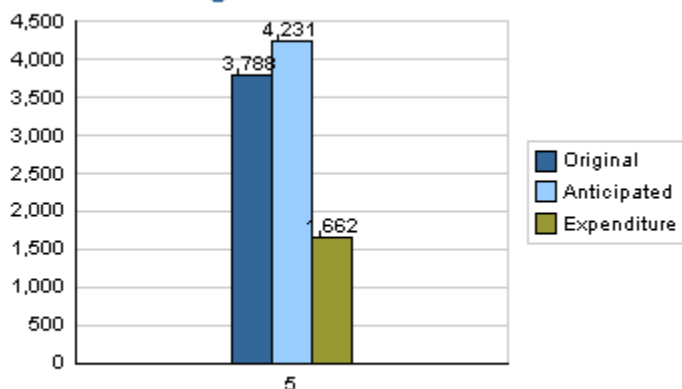

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects 5

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

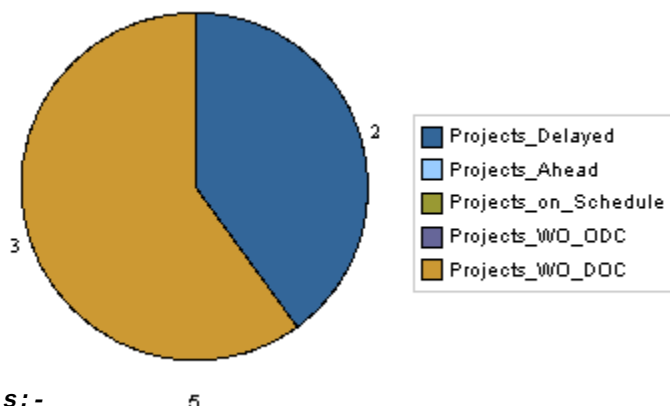


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 3788.29 crore but this was subsequently anticipated to Rs. 4230.74 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till July, 2018 is Rs. 1662.35 crore, which is 39.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

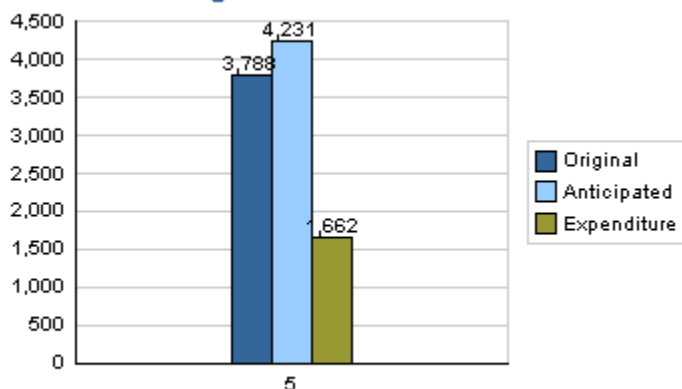

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	10
Number of Projects On Schedule	2
Number of Projects Delayed	6

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 2 projects are on schedule 6 projects are delayed. 2 projects do not have fixed dates of commissioning.

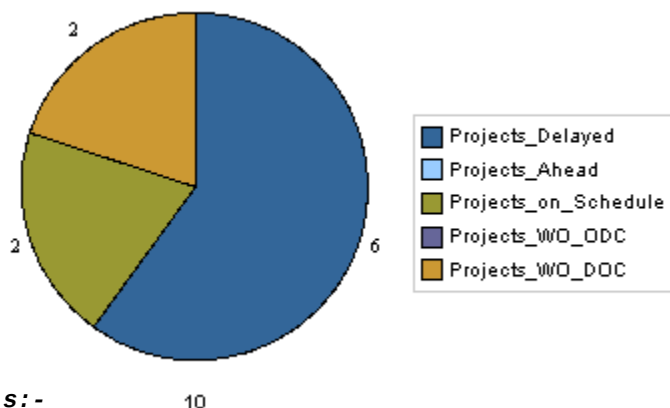


Total No Of Project's:-

10

Investment Scenario

Total original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 17191.2 crore but this was subsequently anticipated to Rs. 28421.2 crore implying a cost overrun of 65.3%. The expenditure incurred on these projects till July, 2018 is Rs. 8980.63 crore, which is 31.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

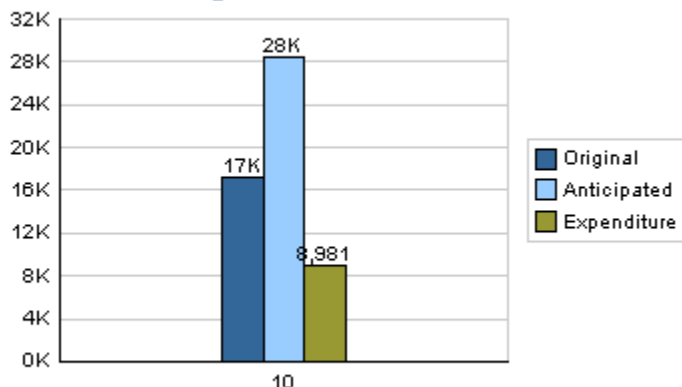

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	43
Number of Projects On Schedule	12
Number of Projects Delayed	19
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis

Project Status with respect to Original Schedule: Out of 43 projects, 1 project is ahead of schedule, 12 projects are on schedule 19 projects are delayed. 11 projects do not have fixed dates of commissioning.

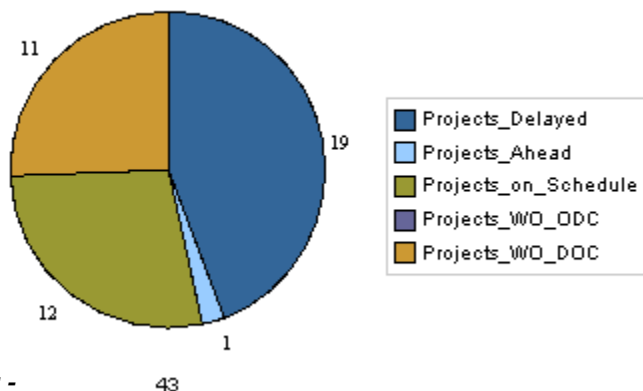


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 43 projects when sanctioned, was of the order of Rs. 144199.91 crore but this was subsequently anticipated to Rs. 149477.76 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till July, 2018 is Rs. 65471.13 crore, which is 43.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

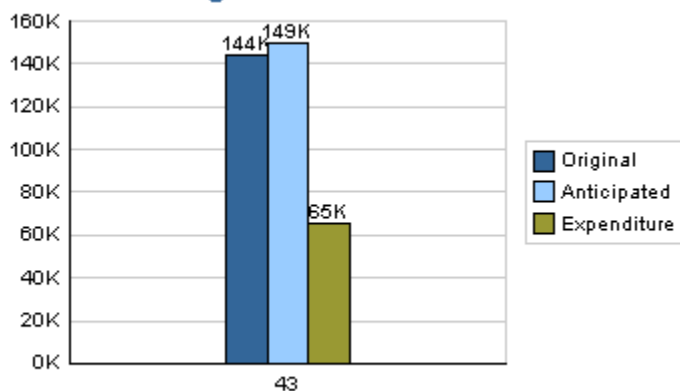

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.

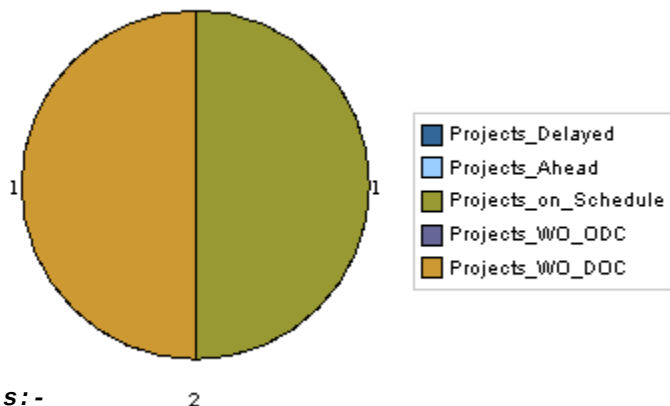


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 461.66 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till July, 2018 is Rs. 123.65 crore, which is 26.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

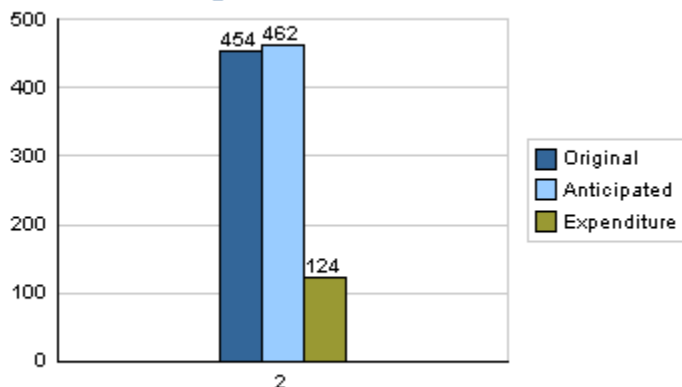

Annexure - I
STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (JULY 2018)
 (All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	6	1,889.87	2,016.59	85.79
2	ANDHRA PRADESH	61	98,363.19	1,03,681.73	13,997.15
3	ARUNACHAL PRADESH	30	16,028.42	33,154.93	17,226.82
4	ASSAM	46	28,862.47	39,548	21,882.8
5	BIHAR	84	70,606.42	87,437.49	47,397.59
6	CHHATISGARH	38	67,062.14	69,718.38	34,923.86
7	D & N HAVELI	1	6,086.08	5,842.31	3,986.3
8	DELHI	23	56,043.88	56,632.51	40,432.01
9	GOA	10	4,292.52	4,300.6	221.86
10	GUJARAT	48	44,417.71	53,141	29,501.61
11	HARYANA	24	17,887.77	19,800.43	10,904.94
12	HIMACHAL PRADESH	12	14,659.32	25,091.6	9,371.15
13	JAMMU AND KASHMIR	10	25,238.37	51,232.67	28,086.5
14	JHARKHAND	48	45,550.26	47,819.8	19,549
15	KARNATAKA	42	71,151.56	81,641.15	29,583.25
16	KERALA	22	23,243.87	26,990.43	4,512.25
17	MADHYA PRADESH	61	65,252.1	70,966.23	27,408.27
18	MAHARASHTRA	129	1,72,945.28	1,86,576.57	69,426.82
19	MANIPUR	2	944.25	14,025.69	7,817.91
20	MEGHALAYA	6	7,108.02	9,025	1,015.57
21	MIZORAM	4	1,632.48	5,613.14	2,383.51
22	MULTI STATE	172	3,44,126.91	4,53,016.12	1,31,091.48
23	NAGALAND	21	12,234.55	14,384.55	638.43
24	ODISHA	79	81,330.92	91,471.24	31,193.57
25	PUNJAB	31	16,717.41	16,723.14	3,734.95
26	RAJASTHAN	60	44,903.52	47,181.46	22,662.43
27	SIKKIM	6	2,537.08	5,585.45	954.97
28	TAMIL NADU	68	1,13,886.72	1,30,183.04	58,521.51
29	TELANGANA	38	29,795.41	34,600.88	8,512.03
30	TRIPURA	9	3,776.07	8,365.85	6,082.72
31	UTTAR PRADESH	100	1,17,454.69	1,21,491.75	46,033.59
32	UTTARAKHAND	17	18,576.59	36,046.09	9,985.9
33	WEST BENGAL	53	54,028.97	63,055.17	29,060.39
TOTAL		1,361	16,78,634.82	20,16,360.99	7,68,186.93

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

CIVIL AVIATION						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	309.46	-	546.69
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	302.96	-	334.77
3	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	259.4	-	410.19
4	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	457.77	-	581.49
5	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	263.24
6	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	233.26
7	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	198.68	-	234.72
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
8	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	204.44	-	237.8
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	168.9	-	191.38
10	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	HSCC	07/2016	312.99	-	469
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
13	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	871.35	-	961
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
14	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	6955.14
15	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	10234.01

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
16	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	2496.9	6179.96	6604.01
17	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3611.12
18	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	421.01	-	963.23
19	KUDGI STPP STAGE 1	NTPC	01/2012	15166.19	-	15364
20	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	5353	-	7128.72
21	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	-	495.12

RAILWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
22	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
23	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	124.43	926.23	1016.69
24	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	713.16
25	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
26	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	900.05	-	980.99
27	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	386.3	-	967.96
28	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	968.28
29	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	856.94
30	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	155.74	164.36	989.99
31	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	1500	4857	5178.44
32	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	218.24	236.41	707.07
33	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
34	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	501.69	335.77	876.49
35	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
36	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	492.98	-	926.94
37	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	744.71	761.7

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
38	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
39	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	408.76	841.57
40	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.87
41	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	733	-	3000.76
42	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	MRTPT	03/2000	1049.69	-	3544.3
43	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	1069.18
44	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	722.65
45	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	470.21	-	1069.54
46	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	301.64	-	1270.29
47	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	727.56	-	7765.91
48	KOSI BRIDGE (NL), ECR	ECR	04/2002	322.95	-	640.78
49	RAMGANJMUINDI-BHOPAL (NL), WCR	WCR	04/2001	470.92	727.13	879.76
50	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	395.34
51	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	120	-	210.67
52	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	274.24
53	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	183.23	-	592.8
54	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	366.77
55	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	332.92	283.95	495.4
56	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	261.7	-	382.21
57	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	743	-	1784.18
58	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	324.9	-	553.72
59	MAYLADUTHURAI - THIRUVARUR -KARAIKUDI - THIRU 'PONDI' - AGASTIYAMPALLI	SR	09/2007	404.19	-	1102.29

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
60	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1049.68
61	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	200	-	525.15
62	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	300	-	928.69
63	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	325	-	618.19
64	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	813.34	-	2951.92
65	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	619.34	-	2252.69
66	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	653.19	-	723.56
67	TINPAHAR - SAHIBGANJ (ER)	ER	04/2008	167.73	-	264.07
68	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	207.52	-	334.51
69	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29
70	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	441.25
71	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	249.4
72	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	309.44	465.59
73	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	175.69	-	253.1
74	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	468.18
75	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	283.55	-	455.01
76	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	342.85	421.57
77	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	523.17	-	1082.01
78	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	312.12	-	590.2
79	PIRPAINTI-BHAGALPUR	ER	04/2011	261.38	-	321.05
80	HANSDIHA-GODDA NL	ER	04/2011	267.09	-	297.37
81	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	423.66	-	518.14
82	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	184.06	199.12	214.79

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
83	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	ER	04/2011	166.89	-	246
84	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	155.81	-	178.13
85	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
86	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	758.09	-	782.62
87	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	SR	02/2000	200.84	-	394.26
88	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	268.87	-	304.07
89	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	SR	02/2005	600	600	671
90	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	SR	02/2005	241	-	273.36
91	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	NER	04/1997	233	-	326.1
92	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	609.04	1063	1792.1

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
93	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	410.32
94	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	209.8
95	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	268.94
96	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	195.35
97	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	200	-	245.83
98	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	312.79
99	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	198.82
100	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	340.12
101	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	-	389.08
102	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	-	3176.22
103	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	1693.75	-	2675.28
104	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1	NHAI	05/2009	1108	-	3869.3

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
	KM)					
105	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1209.67
106	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2159.63
107	DEOLI KOTA	NHAI	01/2011	593	-	1036.26
108	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2091.65
109	INDORE-DEWAS(NH-3)	NHAI	11/2010	325	-	469.54
110	NASHRI- CHANANI	NHAI	05/2011	2159	-	3986.82
111	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2393.99
112	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	880.29
113	ROHTAK-BAWAL	NHAI	05/2011	650	-	832.39
114	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1986.56
115	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1329.31
116	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	974.73
117	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	582.52
118	JORBAT - BARAPANI	NHAI	01/2011	536	-	673.92
119	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	2993.77
120	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	898.99
121	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	494.33
122	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	811.54
123	2 LANNING OF MUZZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	545.27
124	SRINAGAR TO BANIHAL	NHAI	06/2011	1100.7	-	1216.15
125	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1555.96
126	MUZZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1363.43

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
127	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2436.15
128	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	998.79	-	1952.35
129	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1613.62
130	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2811.29
131	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	411.64
132	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1898.25
133	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4659.71
134	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	2211.94
135	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	5577.73
136	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1399.3
137	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	409.92
138	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	566.34
139	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	530.07	-	556.02
140	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	NHAI	09/2015	768.56	-	1643.18
141	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	NHAI	09/2015	664.53	-	1494.46
142	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	NHAI	09/2015	785.78	-	839.01
143	6 LANING OF AGRA - ETAWAH BYPASS	NHAI	07/2015	1657.2	-	1825
144	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1479.56
145	NAGPUR - KONDHALI	NHAI	09/2005	168	-	279.92
146	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3079.44
147	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	NHAI	07/2015	1393	-	1917.27
148	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1328.85
149	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	2881.81

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(JULY 2018)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
150	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2263.02
151	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	2313.68
152	TRICHY - KARUR	NHAI	03/2007	516	-	761.19
153	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	NHAI	01/2016	701.12	-	841.92
154	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	605.84	-	722.46
SHIPPING AND PORTS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
155	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	413.91
156	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	KPL	02/2015	244.5	258	275.98
STEEL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
157	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	3127.3	-	5467.78
158	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	1154.18	-	1607.72
159	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
160	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64
URBAN DEVELOPMENT						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
161	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	14600	-	16352.77

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	467.97	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	2,321.00	354.43	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216]	1/2016	247.52 -	247.52	130.75	02/2019 -	12/2018
5	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	22.24	04/2021 -	04/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226]	2/2016	356.00 -	356.00	159.71	05/2019 -	12/2018
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	315.56	12/2020 -	02/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
8	GAMJI REDEVELOPMENT PROJECT - [N16000202]	5/2015	1,671.22 567.22	567.22	443.27	11/2019 12/2018	07/2018
	Total		12,724.72 -	11,620.72	2,088.90		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
9	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]	5/2015	780.33 -	780.33	478.41	10/2018 -	09/2018
	Total		780.33 -	780.33	478.41		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23	348.23	76.53	03/2021 -	12/2020
	<u>North Eastern Railway</u>						
11	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,750.00 -	1,295.42	69.56	03/2022 -	02/2019
	<u>North Western Railway</u>						
12	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	348.55	100.17	12/2019 -	06/2019
	<u>Rail Vikas Nigam Ltd.</u>						

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
13	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	4/2011	4,295.30 -	16,216.00	877.71	12/2026 -	03/2026
14	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	03/2025
	Total		7,363.39 -	18,931.98	1,124.19		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
15	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	86.42	03/2020 -	05/2019
16	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
	Total		461.69 -	426.16	96.99		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
17	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]	9/2017	150.29 -	150.29	3.60	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	3.60		
	Grand Total		21,480.42	31,909.48	3,792.09		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	223.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	294.63	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.29	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	397.45	03/2021 -	03/2021
6	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.20	03/2026 -	03/2026
	<u>Neyveli Lignite Corporation</u>						
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	2,649.27	11/2021 -	11/2021
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	176.76	12/2019 -	12/2019
9	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	10.45	09/2019 -	09/2019
	<u>Northern Coal Fields Limited</u>						
10	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	-	03/2022 -	03/2022
11	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	167.20	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
12	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 03/2019	03/2019
13	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020
14	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
	<u>South-Eastern Coal Fields Limited</u>						
15	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.67	03/2021 -	03/2021
16	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.89	03/2023 -	03/2023
17	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.16	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
19	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.49	03/2021 -	03/2021
20	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	53.98	03/2020 -	03/2020
21	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.74	03/2023 -	03/2023
22	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
23	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.11	03/2023 -	03/2023
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	51.45	03/2022 -	03/2022
25	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
26	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,863.01	03/2023 -	03/2023
27	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,825.99	03/2023 -	03/2023
28	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	54.19	03/2020 -	03/2020
29	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
	<u>Western Coal Fields Limited</u>						
30	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
31	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
32	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	100.50	03/2020 -	03/2020
33	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.07	03/2021 -	03/2021
34	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	91.90	03/2023 02/2017	03/2023
35	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	81.65	03/2021 -	03/2021
36	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
37	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	52.83	03/2020 -	03/2020
38	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	128.39	03/2019 -	03/2019
39	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	387.44	03/2020 -	03/2020
40	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	257.09	03/2020 -	03/2020
41	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	234.72	03/2019 -	03/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.90	03/2020 -	03/2020
43	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.21	03/2025 -	03/2025
44	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.10	03/2021 -	03/2021
45	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	89.32	03/2019 -	03/2019
46	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.56	03/2022 -	03/2022
47	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	18.78	03/2021 -	03/2021
	Total		65,486.79 -	65,754.66	12,118.04		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
48	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020
	Total		285.95 -	291.29	49.95		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
49	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	19.79	11/2019 -	11/2019
50	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	17.76	11/2019 -	11/2019
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	17.35	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
52	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	18.14	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	73.04		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
53	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
54	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
55	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Hospital Services Consultancy Corporation</u>						
56	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	8/2017	272.19 -	272.54	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
57	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	7/2016	312.99 -	322.00	469.00	08/2018 -	08/2018
58	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]	8/2017	274.19 -	272.54	122.66	03/2019 -	03/2019
59	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019
60	CNCI KOLKATA WEST BENGAL - [N21000015]	8/2016	244.00 -	244.00	214.62	09/2018 -	09/2018
	Total		3,821.52 -	3,829.23	1,440.01		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
61	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	299.64	01/2020 01/2020	01/2020
62	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	94.71	04/2021 04/2021	04/2021
63	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 11/2020	11/2020
64	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
	Total		6,912.00 -	6,912.00	426.27		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
65	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	76.81	01/2019 -	01/2019
66	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	157.18	08/2018 -	08/2018
67	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	43.55	08/2020 -	08/2020
68	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
69	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	107.14	12/2019 -	12/2019
70	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	78.88	02/2020 -	02/2020
71	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	203.89	02/2020 -	02/2020
	<u>Chennai Petroleum Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
72	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	1.31	08/2020 -	08/2020
73	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	351.69	12/2019 -	12/2019
	<u>Gas Authority Of India Limited</u>						
74	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	16.32	10/2022 -	10/2022
75	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	-	12/2021 -	12/2021
76	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	152.80	12/2020 -	12/2020
77	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	181.20 -	181.20	13.66	07/2022 -	07/2022
78	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	177.17	12/2020 -	12/2020
79	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	30.45	10/2022 -	10/2022
80	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	27.09	07/2022 -	07/2022
81	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	749.00	660.88	02/2020 -	02/2020
82	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	84.64	04/2022 -	04/2022
83	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	421.08	12/2020 -	12/2020
84	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]	3/2015	3,957.00 -	3,397.00	2,104.60	12/2018 -	12/2018
85	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	12.16	10/2022 -	10/2022
86	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	18.21	12/2020 -	12/2020
87	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,881.40	467.97	12/2019 12/2020	12/2019
88	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231]	7/2015	1,427.94 -	750.00	558.94	12/2018 -	12/2018
	<u>Hindustan Petroleum Corporation Limited</u>						
89	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB, HARYANA) - [N16000242]	11/2016	230.00 -	230.00	80.53	02/2019 -	02/2019
90	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	15.86	06/2020 -	06/2020
91	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	138.28	09/2019 -	09/2019
92	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
93	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	56.00	06/2020 -	06/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
94	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	750.43	06/2020 -	06/2020
95	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	1.02	11/2020 -	11/2020
96	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	24.62	03/2021 -	03/2021
97	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
<u>Indian Oil Corporation Limited</u>							
98	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	493.66	09/2019 -	09/2019
99	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	32.91	12/2019 -	12/2019
100	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
101	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	-	09/2022 -	09/2022
102	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	0.12	02/2020 -	02/2020
103	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	71.22	09/2019 -	09/2019
104	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	0.05	01/2021 -	01/2021
105	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
106	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020
107	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	0.08	01/2021 -	01/2021
108	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	253.96	12/2018 -	12/2018
109	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	640.72	11/2018 -	11/2018
110	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	179.85	09/2019 -	09/2019
111	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.08	08/2020 -	08/2020
112	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	137.03	09/2019 -	09/2019
113	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
114	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	197.48	01/2019 -	01/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
115	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	536.51	09/2019 -	09/2019
116	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	0.90	12/2021 -	12/2021
117	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	437.05	10/2019 -	10/2019
118	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	0.05	01/2021 -	01/2021
119	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	917.79	11/2019 -	11/2019
120	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	2.12	12/2021 -	12/2021
121	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	31.03	04/2020 -	04/2020
122	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	0.28	06/2020 -	06/2020
123	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
124	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
125	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
126	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020
127	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020
128	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
129	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
130	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	279.79	12/2020 -	12/2020
131	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	24.22	02/2020 -	02/2020
132	INFRASTRUCTURE DEVLOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	54.11	07/2020 -	07/2020
133	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
134	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	456.52	08/2021 -	08/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
135	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	122.85	08/2019 -	08/2019
136	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
137	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	875.63	09/2019 -	09/2019
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
138	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
139	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
140	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019
141	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
142	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	35.56	05/2020 05/2020	05/2020
143	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	47.18	11/2019 11/2019	11/2019
144	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	168.13	09/2018 09/2018	09/2018
145	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	185.84	11/2019 11/2019	11/2019
146	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	255.08	05/2019 05/2019	05/2019
147	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	33.34	11/2019 11/2019	11/2019
148	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	-	12/2019 -	12/2019
149	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	249.44	03/2026 03/2026	03/2026
150	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	396.86	05/2021 05/2021	05/2021
	<u>Oil India Limited</u>						
151	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	12.73	10/2020 -	10/2020
152	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
153	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	17.97	12/2019 -	12/2019
	Total		1,10,947.05 -	1,09,711.38	15,286.51		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
154	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,195.00	11/2019 -	11/2019
155	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,651.48	09/2019 -	09/2019
	<u>Power Grid Corporation Of India Limited</u>						
156	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	52.81	02/2020 -	02/2020
157	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	22.13	06/2019 -	06/2019
158	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]	9/2017	198.49 -	198.49	0.18	09/2019 -	09/2019
159	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	74.37	09/2019 -	09/2019
160	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.80	06/2019 -	06/2019
161	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	512.21	12/2018 -	12/2018
162	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]	7/2016	300.94 -	300.94	177.77	12/2018 -	12/2018
163	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	438.09	04/2020 -	04/2020
164	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]	5/2016	167.01 -	167.01	90.13	11/2018 -	11/2018
165	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	2,724.41	11/2019 -	11/2019
166	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	21.24	12/2019 -	12/2019
167	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	157.04	02/2020 -	02/2020
168	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	166.83	02/2019 -	02/2019
169	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	41.36	07/2019 -	07/2019
170	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,141.00	04/2019 -	04/2019
171	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	383.00	07/2020 -	07/2020
172	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
173	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]	9/2016	562.25 -	562.25	24.20	03/2019 -	03/2019
174	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 -	1,429.38	623.84	01/2019 -	01/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
175	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	485.35	06/2019 -	06/2019
176	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]	5/2016	766.21 -	766.21	303.68	11/2018 -	11/2018
177	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.35	06/2019 -	06/2019
178	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	24.85	11/2019 -	11/2019
179	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]	5/2016	3,519.59 -	3,519.59	1,680.63	05/2019 -	05/2019
180	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]	3/2017	162.31 -	162.31	20.90	03/2019 -	03/2019
181	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	123.13	01/2019 -	01/2019
182	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	301.40	04/2019 -	04/2019
183	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	88.86	02/2019 -	02/2019
184	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	14.29	06/2019 -	06/2019
185	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	274.50	04/2019 -	04/2019
186	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]	7/2016	333.17 -	333.17	245.93	03/2019 -	03/2019
187	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]	8/2016	431.89 -	431.89	154.46	02/2019 -	02/2019
188	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]	8/2016	177.52 -	177.52	74.98	02/2019 -	02/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
189	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	111.89	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
190	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	62.05	09/2020 -	09/2020
	Total		59,420.70 -	60,699.22	18,473.14		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
191	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	297.85 -	540.02	145.70	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
192	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	199.12	214.79	03/2019 -	03/2019
193	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
194	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	912.00 -	637.95	19.30	03/2023 -	03/2023
195	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
196	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	2/2016	854.00 -	1,035.16	13.90	03/2023 -	03/2023
197	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
198	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	0.82	03/2023 -	03/2023
199	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	630.00 -	1,272.19	91.38	03/2022 -	03/2022
200	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	499.30 -	3,168.29	880.98	03/2023 -	03/2023
201	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	514.68 -	2,271.50	1,600.99	03/2021 -	03/2021
202	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	4,670.00 3,627.00	3,627.47	108.33	03/2024 -	03/2024
203	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,326.00 -	2,449.91	67.04	03/2023 -	03/2023
204	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	277.70 -	792.89	254.13	03/2021 -	03/2021
	<u>Container Corporation Of India</u>						
205	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	250.50	03/2019 -	03/2019
206	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	241.26	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
207	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
208	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
209	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
210	HAJIPUR - BACHAWARA - [N22000334]	5/2015	720.00 -	678.54	-	12/2018 -	12/2018
	<u>East Coast Railway</u>						
211	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	202.87	03/2021 -	03/2021
212	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	679.27 -	1,539.28	716.89	03/2021 -	03/2021
213	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
214	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	155.50	03/2021 -	03/2021
215	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	470.21 -	3,798.80	1,069.54	06/2021 -	06/2021
216	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	178.13	03/2020 -	03/2020
217	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	81.68	03/2021 -	03/2021
218	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	552.18	03/2020 -	03/2020
219	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	858.67 -	843.04	70.62	03/2021 -	03/2021
	<u>Eastern Railways</u>						
220	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	4/2000	1,188.91 -	1,319.33	837.35	03/2019 12/2009	03/2019
221	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]	4/2010	157.94 -	157.94	51.06	11/2018 -	11/2018
	<u>North Central Railway</u>						
222	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>North East Frontier Railway</u>						
223	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	871.00	148.14	03/2021 -	03/2021
224	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	63.66	03/2020 -	03/2020
225	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	282.92 -	360.00	3.13	03/2020 -	03/2020
226	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
227	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
228	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	97.41	03/2020 -	03/2020
229	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	165.82 -	450.00	122.97	03/2020 -	03/2020
230	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	203.30	03/2019 -	03/2019
231	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	455.01	03/2019 -	03/2019
232	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	178.69	03/2022 -	03/2022
233	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	556.31 -	612.00	14.25	03/2020 -	03/2020
234	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	4/2010	4,083.02 -	6,000.00	259.12	03/2021 -	03/2021
235	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	312.12 -	551.00	590.20	03/2019 -	03/2019
	<u>North Eastern Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
236	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	268.78	96.74	08/2018 -	08/2018
237	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	3/2012	199.75 -	270.00	249.40	08/2018 -	08/2018
238	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	274.24	05/2019 -	05/2019
239	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	165.93	01/2019 -	01/2019
240	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,900.00	-	01/2022 -	01/2022
	<u>North Western Railway</u>						
241	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR - [N22000152]	4/2013	456.00 -	420.18	56.05	12/2019 -	12/2019
242	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	4/2012	288.97 -	346.35	270.36	11/2018 -	11/2018
243	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.38	03/2020 -	03/2020
244	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	294.90	144.49	10/2018 -	10/2018
245	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	423.40	02/2019 -	02/2019
246	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	349.00	234.37	02/2019 -	02/2019
247	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
248	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	150.49	11/2019 -	11/2019
	<u>National High Speed Rail Corporation Limited</u>						
249	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	557.99	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
250	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
251	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	773.94	174.56	12/2024 -	12/2024
252	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	970.00	867.19	03/2020 -	03/2020
253	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	86.24	12/2024 -	12/2024
254	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	782.62	03/2020 -	03/2020
255	DHASA-JETALSAR (GC) - [N22000141]	4/2012	376.59 -	644.38	74.67	03/2021 -	03/2021
256	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,443.07	03/2020 -	03/2020
257	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	797.18	12/2020 -	12/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
258	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,041.63	03/2023 -	03/2023
259	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	213.57	12/2025 -	12/2025
260	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	301.64 -	1,844.47	1,270.29	03/2020 09/2009	03/2020
261	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,266.89 -	1,548.66	677.61	12/2021 -	12/2021
262	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	241.54	12/2024 -	12/2024
263	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	1,046.88 -	7,000.00	182.77	12/2026 -	12/2026
264	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	567.18 -	975.62	541.05	12/2021 -	12/2021
	<u>South Central Railway</u>						
265	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	4/2006	378.56 -	1,160.47	71.23	03/2022 03/2022	03/2022
266	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	295.91	03/2021 -	03/2021
267	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
268	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	218.24 236.41	645.00	707.07	03/2019 03/2019	03/2019
	<u>South East Central Railway</u>						
269	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	4/2010	737.72 -	737.72	104.10	12/2018 -	12/2018
270	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021
	<u>South Eastern Railway</u>						
271	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	484.48	12/2021 12/2021	12/2021
	<u>South Western Railway</u>						
272	ARSIKERE-TUMKUR - [N22000332]	3/2015	960.00 -	578.00	418.85	03/2020 11/2015	03/2020
273	HUBLI- CHIKJAJUR - [N22000325]	3/2015	1,900.00 -	1,141.00	625.25	03/2020 03/2020	03/2020
274	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	422.93	03/2020 03/2020	03/2020
	<u>Southern Railway</u>						
275	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
276	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
	<u>West Central Railway</u>						
277	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
278	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
279	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	470.92 727.13	2,713.09	879.76	03/2021 -	03/2021
280	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						
281	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	585.99	03/2022 03/2019	03/2022
282	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	196.00	03/2021 03/2019	03/2021
	Total		2,28,308.16 -	2,92,757.87	48,519.45		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
283	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]	3/2018	215.79 -	215.79	-	09/2018 -	09/2018
284	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]	3/2018	240.64 -	240.64	-	09/2018 -	09/2018
285	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
286	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
287	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
288	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
289	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]	2/2018	391.00 -	391.00	-	10/2018 -	10/2018
290	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]	3/2018	251.97 -	251.97	-	09/2018 -	09/2018
291	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
292	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]	3/2018	237.72 -	237.72	-	09/2018 -	09/2018
293	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]	3/2018	500.09 -	500.09	-	09/2018 -	09/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
294	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762	3/2018	215.12 -	215.12	-	09/2018 -	09/2018
295	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765	3/2018	323.98 -	323.98	-	09/2018 -	09/2018
296	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757	3/2018	315.03 -	315.03	-	09/2018 -	09/2018
297	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756	3/2018	285.68 -	285.68	-	09/2018 -	09/2018
298	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018
299	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
300	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
301	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764	3/2018	272.89 -	272.89	-	09/2018 -	09/2018
302	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752	2/2017	387.00 -	387.00	-	09/2018 -	09/2018
303	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761	3/2018	282.98 -	282.98	-	09/2018 -	09/2018
304	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754	3/2018	339.57 -	339.57	-	09/2018 -	09/2018
305	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
306	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755	3/2018	239.30 -	239.30	-	09/2018 -	09/2018
<u>National Highways Authority Of India</u>							
307	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	1,041.10	116.89	04/2019 -	04/2019
308	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	314.52	03/2020 -	03/2020
309	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542	3/2016	197.69 -	197.69	-	07/2018 -	07/2018
310	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
311	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
312	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	-	04/2019 -	04/2019
313	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
314	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
315	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
316	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593	7/2016	331.46 -	331.46	-	10/2018 -	10/2018
317	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
318	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
319	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448	1/2016	574.28 -	574.28	51.47	07/2018 -	07/2018
320	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630	11/2016	446.17 -	446.17	-	03/2019 -	03/2019
321	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
322	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
323	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
324	NAGPUR RING ROAD PACKAGE-1 - [N24000558	3/2016	546.00 -	546.00	11.04	07/2019 -	07/2019
325	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	174.94	03/2019 -	03/2019
326	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
327	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
328	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439	7/2015	1,885.74 -	1,885.74	-	05/2019 -	05/2019
329	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490	3/2015	1,388.00 -	1,388.00	735.94	08/2018 -	08/2018
330	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
331	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
332	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	315.98	07/2018 -	07/2018
333	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	157.10	04/2019 -	04/2019
334	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452	7/2015	1,657.20 -	1,657.20	1,825.00	01/2019 -	01/2019
335	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505	6/2015	1,583.79 -	1,583.79	375.53	01/2019 -	01/2019
336	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018
337	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557	2/2016	641.17 -	641.17	204.31	07/2018 -	07/2018
338	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
339	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629	11/2016	400.25 -	400.25	-	03/2019 -	03/2019
340	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020
341	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	35.17	11/2018 -	11/2018
342	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605	8/2016	227.49 -	227.49	-	01/2019 -	01/2019
343	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442	12/2015	649.50 -	649.50	31.47	03/2019 -	03/2019
344	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561	3/2016	244.00 -	244.00	-	07/2018 -	07/2018
345	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	43.29	05/2019 -	05/2019
346	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552	3/2016	701.40 -	701.40	22.02	03/2019 -	03/2019
347	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
348	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548	2/2016	997.15 -	997.15	329.10	03/2019 -	03/2019
349	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
350	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599	8/2016	2,016.00 -	2,016.00	149.36	04/2019 -	04/2019
351	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	8/2016	323.72 -	323.72	37.20	08/2018 -	08/2018

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
352	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	130.72	07/2019 -	07/2019
353	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]	1/2016	701.12 -	701.12	841.92	05/2019 -	05/2019
354	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
355	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]	8/2016	320.30 -	320.30	170.51	01/2019 -	01/2019
356	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]	6/2016	649.00 -	649.00	-	06/2019 -	06/2019
357	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]	8/2016	248.97 -	248.97	-	05/2019 -	05/2019
358	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
359	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020
360	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	9/2016	950.69 -	950.69	237.09	08/2019 -	08/2019
361	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
362	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]	1/2016	1,081.57 -	1,081.57	-	06/2019 -	06/2019
363	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	70.80	04/2019 -	04/2019
364	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
365	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	167.29	04/2020 -	04/2020
366	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]	9/2016	767.03 -	767.03	123.31	08/2018 -	08/2018
367	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	-	02/2019 -	02/2019
368	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	-	09/2019 -	09/2019
369	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	115.21	04/2019 -	04/2019
370	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]	8/2015	399.54 -	399.54	-	04/2019 -	04/2019
	Total		70,818.27 -	71,291.41	7,772.21		
	STEEL						
	National Mineral Development Corporation (Nmhc)						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
371	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	32.30	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
372	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	108.77	06/2019 -	06/2019
	Total		1,080.87 -	1,080.87	141.07		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
373	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	77.74	08/2018 08/2018	08/2018
374	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	231.80	-	10/2018 10/2018	10/2018
	Total		401.25 -	401.25	77.74		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
375	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]	1/2018	206.58 -	206.58	0.02	03/2019 -	03/2019
376	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD [N28000098]	10/2016	209.84 -	209.84	3.72	03/2020 -	03/2020
377	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
378	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	1.50	06/2019 -	06/2019
379	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	197.33	5.03	04/2019 -	04/2019
380	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019
381	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	549.31	126.11	07/2019 -	07/2019
382	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	3.60	03/2020 06/2020	03/2020
383	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
384	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	26.00	10/2019 -	10/2019
	<u>Lucknow Metro Rail Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
385	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>National Building Construcion Corporation Ltd</u>						
386	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,336.53	11/2019 -	11/2019
	Total		13,584.53 -	13,759.76	6,041.12		
	Grand Total		5,62,168.37	6,27,590.22	1,10,418.55		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	22,680.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2018	78.87
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
5	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]	05/2016	687.28 -	759.19	06/2017 -	12/2017	10.46
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	<u>Singareni Colliers Company Limited</u>						
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
9	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
10	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2019	11.42
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
12	JAGANNATHPOR OCP(3.00MTY) - [N06000075 <u>Western Coal Fields Limited</u>	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
13	BHANEGAON OC - [N06000121 <u>Goa Shipyard Limited</u>	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
	Total		19,751.90 -	21,082.91			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
14	CONSTRUCTION WORKS PHASE 4 - [N39000001	12/2016	167.69 168.00	170.37	05/2018 -	05/2018	1.60
15	CONSTRUCTION WORKS PHASE 3B - [N39000002	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.87
	Total		453.64 -	461.66			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
16	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation</u>						
17	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	08/2017	272.19 -	272.54	03/2019 -	03/2019	.13
18	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022 <u>Hospital Services Consultancy Corporation Ltd</u>	01/2018	249.01 -	249.07	- -	03/2020	.02
19	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010	12/2014	168.90 -	191.38	05/2017 -	09/2018	13.31
20	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	09/2018	3.45
21	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014	07/2016	312.99 -	322.00	08/2018 -	08/2018	2.88
22	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,665.23 -	1,714.64			
	<u>HEAVY INDUSTRY</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Natrip Implementation Society</u>						
23	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
24	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33
	<u>Hindustan Petroleum Corporation Limited</u>						
25	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50
26	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
27	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
28	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175	03/2014	3,076.00 -	4,190.00	09/2017 -	06/2018	36.22
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	02/2011	913.00 -	1,330.00	06/2018 -	10/2018	45.67
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
31	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256	10/2015	135.00 171.00	170.70	03/2019 -	03/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
32	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128	03/2011	861.79 -	1,256.72	05/2013 -	12/2018	45.83
34	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
35	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
36	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
37	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47
38	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		19,129.74 -	24,486.29			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
39	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
40	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
41	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
42	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
43	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	09/2018	86.27
44	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
45	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
46	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
47	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
48	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65
49	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
50	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
51	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
52	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
53	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	12/2016	7.41
	<u>North East Electric Power Corporation</u>						
54	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
55	TRIPURA GAS BASED POWER PROJECT - [N18000071 <u>Power Grid Corporation Of India Limited</u>	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
56	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59
57	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14
58	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65
59	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080	02/2010	2,144.00 -	2,932.88	12/2012 -	09/2018	36.79
60	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61
61	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34
62	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165	03/2014	155.57 -	206.42	03/2016 -	09/2018	32.69
63	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID [N18000169	08/2014	288.49 -	376.09	02/2017 -	09/2018	30.37
64	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171	02/2014	196.58 -	225.28	02/2016 -	09/2018	14.60
65	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP [N18000180	01/2015	268.80 -	340.88	03/2018 -	09/2018	26.82
66	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92
67	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	07/2010	1,272.80 -	1,731.10	11/2012 -	09/2018	36.01
68	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30
69	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17
70	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	534.02	08/2014 -	09/2018	79.61
71	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2018	22.93
72	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143	03/2013	514.20 -	703.10	06/2015 -	08/2018	36.74
73	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144	03/2013	2,514.88 -	3,190.27	12/2015 -	09/2018	26.86
74	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
75	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
76	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
77	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
78	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	09/2018	42.83
79	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	08/2008	771.00 -	1,642.00	02/2013 -	10/2018	112.97
	<u>Satluj Jal Vidyut Nigam Limited</u>						
80	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
81	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75
82	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	12/2021	52.10
83	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,78,005.08 -	2,41,978.90			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
84	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	3,168.29	03/2023 -	03/2023	534.55
85	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	792.89	03/2021 -	03/2021	185.52
86	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	199.12	03/2019 -	03/2019	8.18
87	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	04/2012	297.85 -	540.02	03/2022 -	03/2022	81.31
88	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	514.68 -	2,271.50	03/2021 -	03/2021	341.34
89	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	29.56
90	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
91	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
92	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	630.00 -	1,272.19	03/2022 -	03/2022	101.93

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
93	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	02/2015	2,326.00 -	2,449.91	03/2023 -	03/2023	5.33
94	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
95	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	02/2016	854.00 -	1,035.16	03/2023 -	03/2023	21.21
	<u>Container Corporation Of India</u>						
96	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
97	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
98	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
99	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
100	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
101	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
102	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72
103	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
104	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
105	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
106	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	<u>East Coast Railway</u>						
107	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	12/2022 -	03/2023	137.80
108	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,798.80	06/2021 -	06/2021	707.89
109	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,539.28	03/2021 -	03/2021	126.61
110	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	03/2020 -	03/2020	40.44
111	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
112	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
113	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
114	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
115	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
<u>Eastern Railways</u>							
116	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	03/2019 12/2009	03/2019	10.97
117	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
118	TARAKESWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	- -	-	.14
119	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	- -	-	31.33
120	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	- -	-	38.00
121	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
122	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
123	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
124	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
125	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37
126	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	- -	-	51.49
127	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	- -	-	23.38
128	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
<u>Metropolitan Rapid Transport Projects</u>							
129	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
130	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	1,781.98	03/2004 -	03/2020	259.68
131	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
132	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
<u>North Central Railway</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
133	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
134	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
135	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
136	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
137	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
138	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372	04/2015	524.00 668.00	668.00	03/2020 -	03/2020	27.48
	<u>North East Frontier Railway</u>						
139	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	614.00	03/2019 -	03/2020	1,568.48
140	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
141	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
142	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	5,820.00	04/2008 12/2011	06/2018	288.00
143	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
144	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	13,809.00	03/2011 -	03/2020	1,797.99
145	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	1,532.00	03/2019 -	03/2020	666.00
146	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087	09/2006	300.00 -	2,145.00	03/2019 -	03/2020	615.00
147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
148	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	3,374.00	03/2014 -	03/2020	314.83
149	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	282.92 -	360.00	03/2020 -	03/2020	27.24
150	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
151	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	03/2020 -	03/2020	71.62
152	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,857.00	03/2007 -	04/2016	107.49
153	AGARTALA-AKHAURA NL - [N22000195	04/2012	252.00 -	580.00	03/2019 -	07/2019	130.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
154	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	451.00	03/2019 -	03/2019	59.05
155	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	03/2021 -	03/2021	46.95
156	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
157	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
158	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	03/2020 -	03/2020	171.38
159	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	- -	03/2018	257.63
160	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	551.00	03/2019 -	03/2019	76.53
161	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
162	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	03/2021 -	03/2021	.00
163	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	556.31 -	612.00	03/2020 -	03/2020	10.01
	<u>North Eastern Railway</u>						
164	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	06/2018 -	06/2018	88.85
165	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
166	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	05/2019 -	05/2019	212.37
167	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
168	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
169	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
170	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	08/2018 -	08/2018	10.26
171	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	- -	03/2018	142.44
172	AUNRIHAR MANDUADIIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
173	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2019	61.80
174	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
175	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
176	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
177	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	11/2018	196.84
178	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
	<u>North Western Railway</u>						
179	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,158.00	03/2014 -	03/2019	77.28
180	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
181	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
182	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
183	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
184	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
185	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	- -	-	38.23
186	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47
187	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
188	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
189	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35
190	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	11/2018	19.86
191	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	02/2019	44.16
	<u>Northern Railway</u>						
192	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
193	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
194	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
195	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
196	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
197	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
198	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
199	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
200	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
201	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,844.47	03/2020 09/2009	03/2020	511.48
202	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2021	556.39
203	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58
204	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26
205	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,850.00	03/2008 06/2008	03/2020	148.99
206	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	7,000.00	12/2026 -	12/2026	568.65
207	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	2,062.20	- -	03/2022	112.52
208	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,195.00	12/2012 -	03/2022	293.09
209	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2019	70.82
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
211	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
212	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	12/2021 -	12/2021	72.01
213	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	03/2021 -	03/2021	71.11
214	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	12/2021 -	12/2021	22.24
215	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
216	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	12/2023	9.32
217	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
218	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	728.10 -	773.94	12/2024 -	12/2024	6.30
219	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
220	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
221	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	03/2026	277.53
222	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
223	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	960.18 -	970.00	03/2020 -	03/2020	1.02
224	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	<u>Railway Electrification</u>						
225	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
226	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,120.16	03/2021 -	03/2023	542.47
227	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	03/2022 -	03/2022	206.55
228	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
229	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	03/2024	108.66
230	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
231	GUDUR-DURGARAJPATNAM - [N22000265]	04/2011	283.54 -	761.37	- -	-	168.52
232	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
233	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	1,313.48 -	2,288.70	- -	03/2022	74.25
234	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	704.31	- -	03/2020	108.69
235	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,050.00 -	2,132.77	- -	03/2023	4.04
236	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.43	02/2009 -	-	520.54
237	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	03/2019 -	03/2019	195.55
238	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	458.26	07/2008 -	-	266.61
239	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,025.00	- -	03/2017	723.76
240	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>South East Central Railway</u>						
241	CHHINDWARA - NAGPUR (GC)(SECR) - [N220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
242	GONDIA-JABALPUR(GC),(SECR) - [N220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
243	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,273.00 1,908.00	1,908.00	12/2021 -	12/2021	49.88
	<u>South Eastern Railway</u>						
244	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	01/1999 -	12/2024	114.37
245	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	03/2030	53.96
246	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [N220100208]	04/1974	393.46 154.30	662.00	03/2007 03/2007	03/2025	68.25
247	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
248	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41
249	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
250	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,440.00	- -	03/2024	160.10
251	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	981.00	- -	-	238.70
252	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
253	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	11/2018	69.92
254	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2018	41.36
255	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
256	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
257	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
258	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	12/2023	97.26
259	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	12/2023	651.97
260	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
261	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
262	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
263	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	03/2024	47.93
264	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	12/2023	2.29
265	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
266	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	2,841.84	- -	12/2024	154.42
267	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
268	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	12/2024	840.53
269	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	03/2024	902.01
	<u>Southern Railway</u>						
270	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
271	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
272	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
273	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
274	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
275	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	- -	-	404.39
276	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	- -	-	411.93
277	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	- -	-	147.28
278	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
279	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
280	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
281	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
282	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
283	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
284	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	369.83	- -	-	92.90
285	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	601.43 -	1,800.00	- -	-	199.29
286	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399	02/2015	900.00 -	1,431.90	- -	-	59.10
287	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	302.02	03/2005 -	-	12.33
288	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
289	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450	02/2003	199.55 -	330.32	03/2009 -	-	65.53
290	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
	<u>West Central Railway</u>						
291	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	2,713.09	03/2021 -	03/2021	476.13
292	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
	<u>Western Railway</u>						
293	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,030.29	03/2012 -	03/2022	70.85
294	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
295	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122	04/2008	1,389.62 -	2,446.85	03/2014 -	05/2018	76.08
296	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
297	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142	04/2011	439.88 -	844.10	- -	03/2023	91.89
298	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
299	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146	04/2010	279.40 -	355.00	- -	-	27.06
	Total		1,65,343.22 -	4,12,160.04			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
300	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316	03/2015	258.97 -	268.92	08/2015 -	-	3.84

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
301	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07
302	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639	03/2014	191.50 192.00	192.00	05/2016 -	-	.26
303	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640	01/2015	326.63 327.00	327.00	04/2018 -	-	.11
304	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641	02/2015	239.91 240.00	240.00	10/2017 -	-	.04
305	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
306	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645	08/2013	171.96 172.00	172.00	06/2016 -	-	.02
307	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647	03/2014	162.51 163.00	163.00	05/2016 -	-	.30
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
308	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
309	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
310	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	-	28.93
311	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
312	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
313	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
314	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
315	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	-	42.25
316	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
317	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
318	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
319	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
320	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
321	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
322	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
323	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
324	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
325	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
326	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
327	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
328	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
329	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
330	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
331	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24
332	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
333	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
334	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
	<u>Public Works Dept Of State</u>						
335	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]	11/2014	573.96 605.00	605.00	- -	-	5.41
336	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
337	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
338	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
339	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	11/2018	36.24
340	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	10/2018	31.78
341	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82
342	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		25,879.88 -	33,000.93			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
343	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
344	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
345	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
346	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
347	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
348	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(July 2018)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
349	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Rastrya Ispat Nigam Limited</u>						
350	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39
	Total		1,639.71 -	2,211.39			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
351	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
352	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]	04/2014	332.72 -	342.00	09/2016 -	09/2018	2.79
353	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]	02/2011	241.33 -	349.33	03/2016 -	04/2018	44.75
354	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
355	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57
356	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
	<u>Chennai Metro Rail Ltd</u>						
357	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2018	30.53
	<u>National Building Construcion Corporation Ltd</u>						
358	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		21,267.70 -	26,545.55			
	Grand Total		4,64,721.85	8,17,563.35			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044] BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,655.69	09/2010 09/2016	03/2019	102	74.68	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010] NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,120.00	12/2015 11/2016	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027] NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,520.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028] NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	8,761.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	74,849.00	36,056.69					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050] AAI, SIKKIM	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92	78.87	
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073] AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
	Total		624.07 -	994.86	632.48					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
7	MURADIH UG TURN-KEY PROJECT - [N06000096] BCCL, JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	0	
8	MOONDIH XV SEAM UG - [N06000098] BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	288.72	04/2015 -	04/2019	48	0	
	<u>Central Coal Fields Limited</u>									
9	NORTH URIMARI OCP (3.0 MTY) - [N06000084] CCL, JHARKHAND	12/2007	179.87 -	179.87	99.53	03/2012 -	03/2019	84	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	155.03	03/2012	03/2019	84	0	
11	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	350.74	03/2016	03/2019	36	0	
12	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	84.79	03/2014	03/2019	60	0	
13	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	93.47	03/2011	03/2020	108	0	
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40	706.40	126.89	07/2012	03/2021	104	0	
	<u>Eastern Coal Fields Limited</u>									
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	349.57	03/2018	03/2020	24	0	1.Rehabilitation of PAFs - Process of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting.
	<u>Mahanadi Coal Fields Limited</u>									
16	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	581.49	03/2013	03/2019	72	0	
17	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	263.24	03/2010	03/2019	108	0	
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	344.12	03/2017	03/2020	36	0	
19	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	242.14	03/2013	03/2020	84	0	
20	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA	06/2014	289.03	289.03	65.79	03/2018	03/2020	24	0	
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	233.26	03/2012	03/2021	108	0	
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	105.89	03/2019	03/2021	24	0	
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	42.95	03/2019	03/2021	24	0	
	<u>Neyveli Lignite Corporation</u>									
24	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11	5,907.11	5,547.98	12/2015 12/2018	12/2018	36	0	
25	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU	04/2013	1,458.17 709.06	709.06	388.25	06/2015 09/2019	09/2019	51	-51.37	
	<u>Northern Coal Fields Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
26	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	562.24	03/2018 -	03/2019	12	0	
	<u>Singareni Colliers Company Limited</u>									
27	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	154.52	03/2015 03/2019	03/2019	48	0	
28	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	204.26	06/2015 03/2019	03/2019	45	0	
29	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 415.37	415.37	160.45	03/2016 03/2019	03/2019	36	-3.5	
30	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	0	
31	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 384.32	384.32	146.45	07/2016 -	03/2020	44	-7.91	
32	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 164.04	164.04	12.69	03/2015 03/2021	03/2021	72	-32.3	
33	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 349.28	349.28	1.31	03/2015 03/2021	03/2021	72	114.6	
34	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 437.51	437.51	353.61	03/2015 03/2021	03/2021	72	-2.14	
35	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 489.62	489.62	477.74	03/2012 03/2023	03/2023	132	16.86	
36	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	186.91	03/2012 03/2024	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
37	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	0	
38	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	157.67	03/2016 -	03/2019	36	0	
39	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	164.90	03/2015 03/2020	03/2020	60	201.44	
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
41	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	204.04	03/2014 -	03/2020	72	0	
	Total		20,501.12 -	20,380.18	12,337.37					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
42	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	112.27	11/2016 04/2019	04/2019	29	5.89	
	Total		197.79 -	209.44	112.27					
	<u>STEEL</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
43	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	0	
44	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	0	
45	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	0	
46	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>National Mineral Development Corporation (Nmdc)</u>									
47	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	14,116.06	05/2015 10/2018	12/2018	43	0	
	<u>Rastriya Ispat Nigam Limited</u>									
48	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	170.25	07/2018 -	09/2018	2	0	No

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
49	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH	08/2015	320.66 -	320.66	63.07	08/2018 -	10/2018	2	0	NO
50	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	502.10	09/2018 -	01/2019	4	0	NO
51	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29	42.39	NO
52	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	935.45	12/2017 -	03/2019	15	-12.53	NO
	<u>Steel Authority Of India Limited (SAIL)</u>									
53	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	1,607.72	12/2017 -	11/2018	11	0	
54	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	471.38	10/2017 -	12/2018	14	0	
55	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	5,467.78	04/2018 -	02/2019	10	0	
	Total		28,594.47 -	28,381.87	24,514.58					
	<u>PETROLEUM</u>									
	<u>Bharat Petroleum Corporation Limited</u>									
56	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 1,097.54	694.00	431.49	10/2018 12/2018	12/2018	2	0	
57	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 5,245.96	5,245.96	1,938.81	08/2018 05/2019	05/2019	9	14.33	
	<u>Chennai Petroleum Corporation Limited</u>									
58	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	226.81	11/2016 -	07/2018	20	0	
	<u>Gas Authority Of India Limited</u>									
59	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	95.81	04/2018 -	12/2018	8	-38.98	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
60	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 2,915.00	2,915.00	1,856.19	12/2012 02/2019	02/2019	74	0	
	<u>Hindustan Petroleum Corporation Limited</u>									
61	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 723.40	723.40	536.27	10/2014 02/2019	02/2019	52	133.5	
	<u>Indian Oil Corporation Limited</u>									
62	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 1,330.00	1,330.00	1,291.40	06/2018 -	10/2018	4	45.67	
63	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	2,061.99	09/2017 12/2018	12/2018	15	0	
64	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	714.25	337.32	10/2017 -	03/2019	17	17.66	
65	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	143.47	07/2018 10/2020	10/2020	27	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,256.72	1,256.72	1,195.29	05/2013 12/2018	12/2018	67	45.83	
67	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	2,504.61	1,832.82	05/2017 12/2018	12/2018	19	-13.63	
68	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 207.80	207.80	11.24	09/2018 02/2019	02/2019	5	-50.61	
69	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	2,099.23	03/2013 03/2019	03/2019	72	-3.5	
70	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	4,619.94	3,878.77	12/2017 03/2019	03/2019	15	0	
71	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	131.04	03/2019 -	04/2019	1	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
72	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019	13	1.77	
73	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	3,986.30	05/2019 10/2019	10/2019	5	-4.01	
74	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	31.35	01/2014 11/2019	11/2019	70	62.78	
75	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 03/2018	12/2019	57	29.42	
76	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	1,429.33	03/2019 05/2020	05/2020	14	0	
77	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	870.29	06/2020 08/2021	08/2021	14	0	
	<u>Oil India Limited</u>									
78	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	170.50	03/2017 11/2018	03/2019	24	24.47	
79	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
	Total		75,183.68 -	76,984.18	28,572.59					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
80	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,064.54	04/2020 -	10/2023	42	0	
	<u>National Hydro-Electric Power Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
81	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,955.14	09/2009 -	12/2020	135	114.28	
	<u>National Thermal Power Corporation</u>									
82	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,117.65	09/2011 06/2018	09/2018	84	86.27	
83	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	8,774.15	11/2016 03/2019	03/2019	28	0	
84	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 09/2017	05/2019	60	49.41	
85	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	12,739.82	9,989.31	06/2017 06/2019	06/2019	24	7.55	
86	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	9,449.14	09/2017 06/2019	06/2019	21	10.55	
87	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	13,740.53	7,879.74	08/2018 06/2019	06/2019	10	9.64	
88	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,270.00	12/2016 -	08/2019	32	0	
89	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	4,820.27	03/2019 09/2019	09/2019	6	0	
90	NPGL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	11,425.00	01/2018 -	05/2020	28	5.91	
91	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,164.05	7,300.02	02/2019 10/2020	10/2020	20	5.55	
92	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 -	10,598.98	2,201.67	07/2020 10/2020	10/2020	3	0	
93	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,611.12	03/2013 12/2020	12/2020	93	29.14	
94	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	14,762.17	01/2011 04/2021	04/2021	123	73.65	
95	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84 -	1,381.84	349.94	09/2019 02/2022	02/2022	29	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>North East Electric Power Corporation</u>									
96	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,604.01	12/2009 10/2018	03/2019	111	147.51	
	<u>Power Grid Corporation Of India Limited</u>									
97	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL, MULTI STATE	04/2015	2,525.00 -	2,525.00	1,940.00	11/2017 -	07/2018	8	0	
98	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL, MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,556.00	01/2018 -	07/2018	6	0	
99	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL, MULTI STATE	03/2013	514.20 703.10	703.10	603.15	06/2015 05/2018	08/2018	38	36.74	765KV Bay commissioned in Jan'17 matching with associated line. ICT's ready. Commissioning matching with Srikakulam – Garivadi line (under TBCB route, expected by Aug'18).
100	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL, MULTI STATE	01/2016	1,455.47 -	1,455.47	1,015.50	07/2018 -	08/2018	1	0	Erection completed. Commissioning matching with Wind Generation project.
101	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 -	454.11	229.72	04/2018 -	08/2018	4	0	01 out of 04 elements completed. ROW issues being faced in Farraka & Behrampur area.
102	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL, MULTI STATE	07/2016	150.99 -	150.99	85.46	07/2018 -	08/2018	1	0	03 out of 04 elements completed. Completion likely to be delayed due to non-availability of down-stream system by MPPTCL. Critical

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2018)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
103	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,643.53	12/2012 06/2018	09/2018	69	36.79	14/17 line & 06/07 S/s completed. Implementation of balance lines affected due to local disturbances & geographical constraints. 01 line in Mizoram (Silcher-Melriat line) was affected due to tree cutting. Issue getting resolved with support of state/Distt. Admn.
104	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 1,731.10	1,731.10	1,456.53	11/2012 09/2018	09/2018	70	36.01	
105	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 2,702.65	2,702.65	2,492.04	09/2014 09/2018	09/2018	48	39.3	02 out of 03 line completed. Balance line affected due to severe ROW problem being faced in Karnataka on Salem PS – Madhugiri line. Obstruction are being removed progressively with the help of Police protection.
106	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 534.02	534.02	418.03	08/2014 09/2018	09/2018	49	79.61	Implementation affected due to severe ROW problem in Bengaluru area With the support of State Govt. ROW issues being resolved. Work under progress with the help of Police protection.
107	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 3,190.27	3,190.27	2,248.47	12/2015 06/2018	09/2018	33	26.86	Generation project delayed/uncertain. Implementation also affected due to severe ROW problem mostly at Angul end & huge forest involvement. Working permission issued. Progress affected due to difficult hilly terrain and heavy rains. Work under progress.
108	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 206.42	206.42	145.07	03/2016 09/2018	09/2018	30	32.69	04 out of 05 elements completed. Erection work affected due to heavy rains & non-readiness of down stream line by State Govt. at Hamirpur. Critical.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
109	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	264.15	02/2017 06/2018	09/2018	19	30.37	
110	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	146.48	02/2016 09/2018	09/2018	31	14.6	Project completed except procurement of ICT (500MVA, 765/400KV) at Gaya. Transformer supply also delayed. ICT expected to be dispatched by Aug'18.
111	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	222.24	03/2018 09/2018	09/2018	6	26.82	01 out of 02 lines completed. Work affected due to severe ROW problem at 01 loc. & 5 Kms stringing. Slow progress due to compensation issues which are being resolved. Govt. help required to resolve compensation issue. Critical.
112	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	73.19	03/2018 -	09/2018	6	0	
113	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	611.76	09/2017 09/2018	09/2018	12	0	
114	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	305.04	199.28	03/2017 09/2018	09/2018	18	0	
115	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,513.68	09/2017 -	09/2018	12	30.49	Khalsti & Leh S/Stn. and 220KV Leh – Khalsti line were charged on 31 Oct'17. Implementation affected due to delay in land acquisition of Kargil S/s. Land handed over by DM in Dec'16. ROW clearance of 01 loc. to be expedited. Increased BE-18-19 allocation from 500 Cr. to 883 Cr. Required.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
116	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,158.00	12/2015 -	09/2018	33	42.83	
117	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	180.77	04/2016 12/2017	10/2018	30	0	
118	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,395.18	07/2018 -	10/2018	3	0	Severe ROW problem faced. Completion matching with Gen. project. (Gen. proj. delayed ant. by Oct'18). Work slowed-down to the extent possible to match Generation.
119	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	307.18	203.36	11/2017 10/2018	10/2018	11	0	Generation project ant. in March 2020. Work slowed-down to extent possible to match the generation. Working permission received on end of Jun'18.
120	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	155.62	06/2018 -	10/2018	4	0	Completion matching with TBCB line (line under severe ROW issues).
121	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,171.00	06/2018 -	10/2018	4	0	
122	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 1,642.00	1,642.00	1,429.45	02/2013 -	10/2018	68	112.97	ROW constraints and delay in work permission in Tea Estates, delayed clearance from forest deptt. in West Bengal and repeated theft in Bihar portion.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
123	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,041.61	11/2008 09/2018	12/2018	121	22.93	06/07 lines & 02/02 S/stn completed ahead of Gen. Implementation of balance 01 line (Edamon-Muvattupuzha line) is affected due to severe ROW problem (long pending). Problem being addressed progressively as per latest Revised G.O. of 30.07.15 (compensation to be done on land value, to be finalised by concerned DC with the support of State Govt.). Work under progress. Site is getting police protection as per requirement from State Admn.
124	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	664.31	09/2010 12/2018	12/2018	99	54.59	02/03 line line completed. Balance portion (02 Kms) of line being executed using under ground cable. Work affected due to water logging. Severe ROW problem being encountered at Navi Mumbai end, miscreants have burnt and damaged part of laid cable. Matter critical. Commissioning linked to availability of State down stream system at Navi Mumbai . Critical.
125	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	493.77	06/2014 12/2018	12/2018	54	31.17	01 out of 02 lines completed. Balance 400KV Madugiri-Yelhanka line affected due to severe ROW problem being faced in Karnataka. In view of delay due to ROW, the existing contractor has expressed inability to continue the balance work. Balance work re-award in Dec'17. Work under progress.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
126	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,200.95	04/2016 12/2018	12/2018	32	38.61	Farakka - Gokarna portion of 400KV D/C Rajarhat - Purnea line (236 Ckm) including both LILOs at Farakka & Gokarna commissioned in Mar'17. Severe ROW problem at Rajarhat end as well as in Jharkhand area. Work in Rajarhat S/stn. area almost standstill since last 18 months due to protest/agitation by locals who not allowing to enter in S/s. Work resumed in Oct'17 again stopped due to protest w.e.f 01.12.17. Matter being followed up at all levels for early resolution.
127	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	416.39	06/2016 09/2018	12/2018	30	0	01 out of 02 lines completed. Implementation affected due to severe ROW problem at Singrauli end. Work also affected due to poor performance by executing agency. Working permission received in Jul'18 for MP portion.
128	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,490.86	04/2018 09/2018	12/2018	8	0	01 out of 03 line completed. Implementation affected due to forest clearance in Rajasthan portion awaited. ROW in Gujarat portion.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
129	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,531.14	10/2012 12/2018	02/2019	76	5.14	8 out of 9 lines completed progressively by Dec'16. Balance 400kV Wardha – Aurangabad (on 1200KV tower) affected due to delay in implementation arising out of complexities involved (1200KV tower) & poor performance by executing agency necessitating termination & re-awarding fresh contracts. Work under progress after re-award. Severe ROW problem being encountered. Due to thunderstorm and cyclone in Jun'18, about 10 foundations, 15 tower erection & 09 ckm stringing damaged.
130	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	2,543.37	03/2018 03/2019	03/2019	12	0	01 out of 03 element completed. Implementation affected due to delay in land acquisition & delay in off-shore supplies.
131	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	808.63	316.47	01/2018 03/2019	03/2019	14	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife clearance proposal submitted. SBWL meeting held. Proposal forwarded to NBWL. Clearance awaited. Alternate arrangements made for evacuation (contingency through Punatsanghu ATS ready). Generation project delayed (ant.by Nov'18).
132	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 550.18	550.18	423.38	11/2016 06/2019	06/2019	31	5.34	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
133	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	180.99	07/2017 06/2019	06/2019	23	27.92	03 elements out of 04 elements completed. Project commissioned except Bus Reactor at Yelankha As per MoM of 40th SCPSPSR held on 19.11.16. Procurement being taken up after resolution resolved. Award placed in May'18.
134	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	173.34	05/2017 06/2019	06/2019	25	0	Implementation affected due to delayed in land acquisition (land hand over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). Rajghat sub station annulled. Additional bay at Maharanibagh in place of Rajghat S/stn. However, only 400KV line bays are being made at Maharanibag. Award placed in Jan'18. Tree cutting permission awaited in line.
135	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	44.73	09/2018 -	06/2019	9	0	
136	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	269.23	10/2017 09/2019	09/2019	23	0	04 locs. under severe ROW problem. Line linked with Tehri Generation completion expected by December 2020.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
137	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	823.37	12/2018 -	12/2019	12	92.28	Award have been delayed due to poor response & high prices quoted by bidders. Out of 113 Sub stations land for only 83 nos land available. Non-availability of 08 nos. land for awarded Sub-station. Critical. Approval of new elements proposed by Govt. of Arunachal Pradesh.
138	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 -	6,652.57	719.88	12/2018 -	12/2019	12	30.15	Award have delayed due to poor response & high prices quoted by bidders. Increased BE 18-19 allocation from Rs. 282.5 Cr. to 1500 Cr. required.
139	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 13,762.80	13,762.80	12,705.71	08/2013 03/2022	03/2022	103	23.65	06/08 line completed. Balance 02 lines (linked to Gen. Proj.) to be completed matching with Gen. Proj. Lower Subhansiri HEP is schedule uncertain. Works presently stand-still over uncertainty of generation on a/c of local disturbance/ agitation against big dams.
	<u>Satluj Jal Vidyut Nigam Limited</u>									
140	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	274.39	11/2017 -	09/2018	10	0	
141	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 -	602.44	495.12	12/2016 -	12/2018	24	37.96	
	<u>Thdc India Limited</u>									
142	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	187.40	02/2014 02/2018	03/2019	61	50.75	IInd stage forest clearance of 1.39 Ha. land for compensatory afforestation in lieu of 1.39 Ha. forest land for power evacuation is pending.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
143	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,597.73	02/2016 12/2020	05/2021	63	165.65	
144	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,446.85	06/2013 -	12/2021	102	52.1	
	Total		2,14,463.57 -	2,60,933.99	1,76,301.24					
	<u>HEAVY INDUSTRY</u>									
	<u>Indira Gandhi Centre For Atomic Research</u>									
145	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR,DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	0	
	Total		1,554.00 -	1,554.00	161.86					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Hospital Services Consultancy Corporation Ltd</u>									
146	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	242.20	05/2017 -	09/2018	16	0	
147	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC, WEST BENGAL	12/2014	168.90 -	191.38	191.38	05/2017 -	09/2018	16	13.31	
148	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6	3.45	
149	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	237.80	05/2017 -	12/2018	19	0	
150	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	60.45	02/2018 -	12/2018	10	0	
151	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	69.24	05/2018 -	09/2019	16	0	
	Total		1,689.51 -	1,729.41	1,156.07					
	<u>RAILWAYS</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Container Corporation Of India</u>									
152	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	135.50	03/2019 -	08/2019	5	0	
153	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	402.91	03/2018 -	12/2019	21	0	
154	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	279.71	03/2019 -	12/2019	9	0	
155	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	.39	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
156	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	12/2019	21	0	
157	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	210.62	03/2020 -	03/2021	12	0	
	<u>East Coast Railway</u>									
158	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	148.37	03/2021 -	03/2022	12	0	
159	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	2,361.74	67.43	03/2021 -	03/2022	12	0	
160	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	561.81	12/2022 -	03/2023	3	137.8	
	<u>Eastern Railways</u>									
161	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	25.09	
	<u>Metropolitan Rapid Transport Projects</u>									
162	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 495.74	734.01	433.38	06/2013 03/2019	03/2019	69	48.06	
163	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	50.68	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2018)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
164	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,300.41	03/2004 -	03/2020	192	259.68	
	<u>North Central Railway</u>									
165	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	226.98	
166	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	226.23	
	<u>North East Frontier Railway</u>									
167	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 -	3,040.00	3,000.76	12/2008 -	03/2019	123	314.73	
168	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 -	580.00	-	03/2019 -	07/2019	4	130.16	
169	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	36.80 274.41	614.00	266.92	03/2019 -	03/2020	12	1568.48	
170	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 -	13,809.00	7,765.91	03/2011 -	03/2020	108	1797.99	
171	NEW B.G. LINE FROM TETELIA TO BYRNHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 -	1,532.00	525.15	03/2019 -	03/2020	12	666	
172	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 -	2,145.00	928.69	03/2019 -	03/2020	12	615	
173	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,374.00	2,951.92	03/2014 -	03/2020	72	314.83	
174	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	2,252.69	04/2014 -	03/2020	71	642.73	
175	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
176	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	638.43	03/2015 -	03/2020	60	252.94	
	<u>North Eastern Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2018)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
177	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,792.10	04/1999 -	11/2018	235	196.84	
178	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	-	04/2016 -	01/2022	69	.16	
179	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
180	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
181	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	-	04/2017 -	10/2022	66	-31.45	
	<u>North Western Railway</u>									
182	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	1,158.00	723.56	03/2014 03/2019	03/2019	60	77.28	
183	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	630.24	03/2015 -	03/2020	60	46.55	
	<u>Northern Railway</u>									
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	16,344.71	11/2002 03/2021	03/2021	220	1017.96	
	<u>Rail Vikas Nigam Ltd.</u>									
185	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	366.77	03/2009 03/2009	12/2018	117	188.58	
186	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	382.21	02/2006 -	12/2018	154	48.26	
187	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	555.00	553.72	03/2010 -	12/2019	117	70.82	
188	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,850.00	1,784.18	03/2008 06/2008	03/2020	144	148.99	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2018)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
189	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	977.00	921.55	03/2019 -	03/2020	12	5.39	
190	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	546.32	03/2016 -	12/2020	57	29.06	
191	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	942.95	874.64	03/2019 -	03/2021	24	0	
192	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	858.40	12/2020 -	03/2021	3	0	
193	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.70	592.80	02/2015 -	12/2021	82	556.39	
194	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 632.00	1,195.00	607.24	12/2012 -	03/2022	111	293.09	
195	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	789.79	03/2020 -	03/2022	24	0	
196	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,801.39	03/2016 -	03/2025	108	7.78	
197	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	760.90	03/2016 -	03/2025	108	0	
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.16	03/2014 -	12/2025	141	18.95	
	<u>South Central Railway</u>									
199	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	2,120.16	256.74	03/2021 03/2023	03/2023	24	542.47	
	<u>South East Central Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(July 2018)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
200	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	359.96	
	<u>South Eastern Railway</u>									
201	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 309.44	525.81	465.59	12/2015 11/2018	11/2018	35	69.92	
202	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 148.77	377.00	138.99	12/2016 08/2018	12/2018	24	153.41	
203	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 969.83	969.83	326.40	03/2020 03/2020	06/2020	3	0	
204	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	188.19	03/2021 03/2021	12/2021	9	0	
205	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 466.48	1,000.00	.83	01/1999 12/2024	12/2024	311	114.37	
206	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 524.43	939.00	184.09	12/2021 12/2024	12/2024	36	79.05	
207	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	662.00	182.49	03/2007 03/2025	03/2025	216	68.25	
208	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 276.69	426.00	-	01/1999 03/2030	03/2030	374	53.96	
209	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	484.39	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
210	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	279.54	5.03	01/1999 12/2023	12/2023	299	-2.11	
	<u>Southern Railway</u>									
211	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
212	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	<u>Western Railway</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
213	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	99.58	03/2012 -	03/2019	84	1.06	
214	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	385.60	336.20	03/2013 -	03/2020	84	-2.17	
215	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 2,473.40	1,030.29	932.24	03/2012 03/2019	03/2022	120	70.85	
216	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	858.96	550.66	03/2019 03/2019	03/2022	36	167.87	
	Total		57,194.36 -	1,42,816.18	62,135.21					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
217	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-19	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
218	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
219	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
220	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
221	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	<u>National Highways Authority Of India</u>									
222	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018	71	114.56	
223	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	673.92	01/2014 -	08/2018	55	0	
224	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	118	0	
225	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	09/2018	73	0	
226	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54	0	
227	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	411.64	01/2014 -	09/2018	56	0	
228	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	709.00	346.75	09/2017 -	09/2018	12	0	
229	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	279.14	211.04	05/2017 -	09/2018	16	0	
230	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	114	0	
231	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101	0	
232	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 -	10/2018	84	0	
233	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	2.65	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
234	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8	0	
235	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	0	
236	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	0	
237	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	0	
238	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	0	
239	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	0	
240	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	811.54	07/2013 -	12/2018	65	0	
241	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	12/2018	62	-11	
242	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	620.00	04/2018 -	12/2018	8	0	
243	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	02/2019	30	0	
244	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	03/2019	44	0	
245	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2019	57	0	
246	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
247	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI, TELANGANA	12/2015	1,423.96 -	1,423.96	454.64	11/2018 -	03/2019	4	0	
248	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	0	
249	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	0	
250	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI, PUNJAB	10/2015	447.29 -	447.29	4.88	12/2017 -	04/2019	16	0	
251	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	0	
252	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	1,387.11	830.16	11/2017 -	05/2019	18	0	
253	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	05/2019	11	0	
254	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91	106.5	
255	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,544.00	1,399.30	09/2016 -	06/2019	33	21.9	
256	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2019	18	0	
257	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	707.82	164.24	08/2018 -	06/2019	10	0	
258	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
259	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	474.40	06/2019 -	09/2019	3	0	
260	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	34.61	02/2020 -	05/2020	3	0	
261	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	113.04	03/2020 -	05/2020	2	3.4	
262	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	13.97	
263	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	162.19	03/2020 -	05/2020	2	44.39	
264	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	39.97	03/2020 -	06/2020	3	41.54	
265	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	133.93	03/2020 -	08/2020	5	5.56	
266	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	7.34	03/2019 -	11/2020	20	0	
267	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	10.00	03/2017 -	11/2020	44	1.06	
	<u>Public Works Dept Of State</u>									
268	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.05	352.05	201.35	11/2017 08/2018	10/2018	11	31.77	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
269	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.43	348.43	231.56	09/2017 08/2018	11/2018	14	36.24	
	Total		41,568.84 -	46,011.96	32,234.63					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
270	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	<u>Mumbai Port Trust</u>									
271	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	413.91	12/2010 -	12/2018	96	82.72	
	Total		966.39 -	927.36	415.36					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
272	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	159.30	12.40	04/2018 08/2018	08/2018	4	0	
273	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	167.68	30.21	04/2018 08/2018	08/2018	4	0	
274	MAHARASHTRA ACCESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	212.70 -	212.70	37.08	05/2018 08/2018	08/2018	3	0	
275	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	171.54	-	05/2018 08/2018	08/2018	3	0	
276	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 -	215.30	-	05/2018 10/2018	10/2018	5	0	
	<u>Department Of Telecommunication</u>									
277	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	8,397.00	07/2015 05/2020	05/2020	58	84.97	
	Total		14,260.52 -	25,590.52	8,476.69					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>URBAN DEVELOPMENT</u>									
	<u>Bangalore Metro Rail Corporation Limited</u>									
278	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
279	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	620.49	12/2015 -	07/2018	31	0	
280	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 -	388.00	354.09	05/2017 08/2018	08/2018	15	0	
281	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	342.00	316.94	09/2016 03/2018	09/2018	24	2.79	
282	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	138.67	08/2016 -	11/2018	27	0	
283	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	0	
284	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 210.00	270.83	159.42	11/2014 -	12/2018	49	0	
285	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	0	
286	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 -	294.00	95.08	04/2019 06/2019	06/2019	2	0	
287	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	67.79	04/2018 -	07/2019	15	0	
288	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (July 2018)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
289	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.21	03/2016 -	12/2019	45	0	
290	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	247.73	10/2019 -	03/2020	5	30.58	
291	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	27.09	06/2017 -	06/2020	36	.57	
292	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	15.95	02/2020 09/2020	09/2020	7	0	
293	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	-	07/2020 09/2018	09/2020	2	0	
	<u>Chennai Metro Rail Ltd</u>									
294	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 12/2018	12/2018	36	30.53	
	<u>Kochi Metro Rail Corporation Ltd</u>									
295	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
296	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	3,669.58	03/2018 -	12/2019	21	0	
	Total		60,209.34 -	65,203.96	24,609.12					
	Grand Total		5,84,127.66	7,46,566.91	4,07,716.16					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(July 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69	102
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	22,680.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
4	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2018	78.87	92
	Total		624.07 -	994.86				
	<u>COAL</u>							
	<u>Singareni Colliers Company Limited</u>							
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
8	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	Total		983.19 -	1,747.25				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY [N08000009]	10/2014	197.79 -	209.44	11/2016 -	04/2019	5.89	29
	Total		197.79 -	209.44				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	05/2017 -	09/2018	13.31	16
11	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	09/2018	3.45	6
	Total		674.48 -	714.38				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
12	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	08/2018 -	05/2019	14.33	9
	<u>Hindustan Petroleum Corporation Limited</u>							
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	02/2019	133.50	52
	<u>Indian Oil Corporation Limited</u>							
14	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66	17
15	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	02/2011	913.00 -	1,330.00	06/2018 -	10/2018	45.67	4
	<u>Oil & Natural Gas Corporation Limited</u>							
16	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78	70
17	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	1,256.72	05/2013 -	12/2018	45.83	67
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42	57
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77	13
	<u>Oil India Limited</u>							
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47	24
	Total		13,085.77 -	15,952.36				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
21	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28	135
	<u>National Thermal Power Corporation</u>							
22	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14	93
23	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41	60
24	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	8,150.00	09/2011 -	09/2018	86.27	84
25	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55	24
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55	21
27	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91	28
28	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64	10
29	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	04/2021	73.65	123
30	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55	20
	<u>North East Electric Power Corporation</u>							
31	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	6,179.96	12/2009 06/2016	03/2019	147.51	111
	<u>Power Grid Corporation Of India Limited</u>							
32	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	03/2014	155.57 -	206.42	03/2016 -	09/2018	32.69	30
33	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	09/2018	14.60	31
34	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92	23
35	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	09/2018	26.82	6
36	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	09/2018	30.37	19
37	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	08/2014 -	09/2018	79.61	49
38	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	550.18	11/2016 -	06/2019	5.34	31
39	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	12/2018	31.17	54
40	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	03/2013	514.20 -	703.10	06/2015 -	08/2018	36.74	38

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
41	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	12/2018	54.59	99
42	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	09/2018	42.83	33
43	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]	08/2008	771.00 -	1,642.00	02/2013 -	10/2018	112.97	68
44	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]	07/2010	1,272.80 -	1,731.10	11/2012 -	09/2018	36.01	70
45	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	12/2018	38.61	32
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	12/2018	22.93	121
47	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49	12
48	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	09/2011	1,940.13 -	2,702.65	09/2014 -	09/2018	39.30	48
49	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]	02/2010	2,144.00 -	2,932.88	12/2012 -	09/2018	36.79	69
50	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	03/2013	2,514.88 -	3,190.27	12/2015 -	09/2018	26.86	33
51	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	02/2019	5.14	76
52	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15	12
53	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28	12
54	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	13,762.80	08/2013 -	03/2022	23.65	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
55	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96	24
	<u>Thdc India Limited</u>							
56	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	03/2019	50.75	61
57	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	12/2021	52.10	102
58	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65	63

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		1,39,706.95	1,86,177.37				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
59	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431	08/2016	234.50	235.00	03/2019	12/2020	.21	21
	<u>East Coast Railway</u>							
60	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78	1,928.07	12/2022	03/2023	137.80	3
	<u>Eastern Railways</u>							
61	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	900.05	1,125.89	12/2011	03/2020	25.09	99
	<u>Metropolitan Rapid Transport Projects</u>							
62	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74	734.01	06/2013	03/2019	48.06	69
63	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44	1,781.98	03/2004	03/2020	259.68	192
64	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00	7,986.04	03/2014	03/2019	50.68	60
	<u>North Central Railway</u>							
65	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158	04/2010	622.41	2,030.50	02/2019	12/2022	226.23	46
66	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	1,176.09	3,845.60	02/2020	12/2022	226.98	34
	<u>North East Frontier Railway</u>							
67	AGARTALA-AKHAURA NL - [N22000195	04/2012	252.00	580.00	03/2019	07/2019	130.16	4
68	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	36.80	614.00	03/2019	03/2020	1,568.48	12
69	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00	1,532.00	03/2019	03/2020	666.00	12
70	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00	2,145.00	03/2019	03/2020	615.00	12
71	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00	3,000.00	03/2015	03/2020	252.94	60
72	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00	3,040.00	12/2008	03/2019	314.73	123
73	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34	3,374.00	03/2014	03/2020	314.83	72

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
74	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
75	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73	71
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	13,809.00	03/2011 -	03/2020	1,797.99	108
	<u>North Eastern Railway</u>							
77	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16	69
78	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	11/2018	196.84	235
	<u>North Western Railway</u>							
79	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,158.00	03/2014 -	03/2019	77.28	60
80	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55	60
	<u>Northern Railway</u>							
81	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
	<u>Rail Vikas Nigam Ltd.</u>							
82	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	188.58	117
83	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26	154
84	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2019	70.82	117
85	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
86	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39	12
87	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,195.00	12/2012 -	03/2022	293.09	111
88	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2021	556.39	82
89	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,850.00	03/2008 06/2008	03/2020	148.99	144
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,120.16	03/2021 -	03/2023	542.47	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>South East Central Railway</u>							
93	GONDIA-JABALPUR(GC),(SECR) - [N220100186	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96	261
	<u>South Eastern Railway</u>							
94	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41	24
95	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	11/2018	69.92	35
96	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	662.00	03/2007 03/2007	03/2025	68.25	216
97	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05	36
98	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>West Central Railway</u>							
99	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35	178
	<u>Western Railway</u>							
100	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) [N22000123	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06	84
101	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87	36
102	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	603.04 -	1,030.29	03/2012 -	03/2022	70.85	120
	Total		35,081.23 -	1,20,230.56				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
103	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 [N24000676	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
104	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
105	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
106	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
107	SIX LANEING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54	3
108	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
109	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
110	SIX LANEING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39	2
111	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
112	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
113	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56	71
	<u>Public Works Dept Of State</u>							
114	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	11/2018	36.24	14
115	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	10/2018	31.78	11
	Total		11,665.41 -	16,109.34				
	<u>SHIPPING AND PORTS</u>							
	<u>Mumbai Port Trust</u>							
116	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		366.39 -	669.46				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
117	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39	29
	Total		343.00 -	488.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
118	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97	58

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(July 2018)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		13,334.00 -	24,664.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
119	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80	70
120	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	04/2014	332.72 -	342.00	09/2016 -	09/2018	2.79	24
121	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18 496.00	498.99	06/2017 -	06/2020	.57	36
122	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58	5
	<u>Chennai Metro Rail Ltd</u>							
123	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00 -	19,058.00	12/2015 -	12/2018	30.53	36
	Total		16,762.37 -	21,756.99				
	Grand Total		2,47,775.65	4,12,394.41				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Eastern Coal Fields Limited</u>				
4	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	03/2014 -	-
	<u>Mahanadi Coal Fields Limited</u>				
5	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	03/2010 -	03/2018
	<u>Neyveli Lignite Corporation</u>				
6	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 759.19	06/2017 12/2017	12/2017
	<u>Northern Coal Fields Limited</u>				
7	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	03/2012 -	-
	<u>Singareni Colliers Company Limited</u>				
8	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	03/2012 03/2018	03/2018
9	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	12/2012 -	-
	<u>South-Eastern Coal Fields Limited</u>				
10	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	03/2018 -	03/2018
	<u>Western Coal Fields Limited</u>				
11	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
	Total		4,189.54 -		
	<u>FERTILISERS</u>				
	<u>Rashtriya Chemical & Fertiliser Limited</u>				
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL. - [N08000010]RCF,MAHARASHTRA	02/2016	482.85 482.85	12/2017 05/2018	05/2018
	Total		482.85 -		
	<u>STEEL</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Hindustan Steelwork Construction Limited</u>				
13	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
14	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
15	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
16	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
17	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
18	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-
19	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
20	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
21	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-
22	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
23	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL,WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Steel Authority Of India Limited (Sail)</u>				
24	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
25	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		7,775.80 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
26	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
27	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Gas Authority Of India Limited</u>				
28	ANKLESHWAR BARODA PIPELINE PROJECT - [N16000232]GAIL,GUJARAT	07/2014	199.95 -	03/2018 -	03/2018
	<u>Hindustan Petroleum Corporation Limited</u>				
29	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
30	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 4,190.00	09/2017 06/2018	06/2018
31	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
32	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
33	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	- -	-
34	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Numaligarh Refinery Limited</u>				
36	DIESEL HYDROTREATOR - [N16000207]NRL,ASSAM	07/2015	1,031.37 -	01/2018 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
37	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 05/2018	05/2018
	<u>Oil India Limited</u>				
38	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
39	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-
	Total		14,309.64 -		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
40	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
	<u>National Thermal Power Corporation</u>				
41	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016
42	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	01/2017 -	-
43	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	09/2016 -	-
44	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
45	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	12/2016 -	-
	<u>North East Electric Power Corporation</u>				
46	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 -	07/2013 -	-
	Total		38,922.08 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
47	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 -	09/2011 -	-
	Total		1,718.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation</u>				
48	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
49	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	-
50	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-
	Total		1,190.70 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
51	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Container Corporation Of India</u>				
52	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018
53	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
54	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 -	- -	-
	<u>East Central Railways</u>				
55	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
56	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
57	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
58	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
59	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
60	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
61	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-
62	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
64	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
65	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
66	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
67	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
68	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
69	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
70	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
71	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
72	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
73	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-
74	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>East Coast Railway</u>				
75	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
76	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
77	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
78	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
79	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
	<u>Eastern Railways</u>				
80	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
81	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
82	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
83	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-
84	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-
85	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-
86	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
88	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
89	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
90	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
91	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-
92	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
93	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
94	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
95	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
96	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
97	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
98	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
99	BARIARPUUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
100	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
101	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
102	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
103	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
104	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
105	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
106	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
107	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
108	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
109	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-
110	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
111	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
112	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
113	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
114	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
115	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
116	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
117	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-
118	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
119	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
120	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
121	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				
122	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016
123	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	523.17 -	- -	03/2018
124	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 4,857.00	04/2008 12/2011	06/2018
125	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	12/2010 -	-
126	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
	<u>North Eastern Railway</u>				
127	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	01/2018
128	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
129	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	06/2018
130	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 744.71	- -	-
131	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
132	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
133	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
134	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
135	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-
	<u>North Western Railway</u>				
136	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
137	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
138	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
139	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
140	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
141	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
142	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
143	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-
144	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
145	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
146	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
147	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
148	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
149	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
150	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
151	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
152	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
153	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
154	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
155	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
156	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
157	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
158	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
159	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
	<u>Rail India Technical And Economic Service</u>				
160	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Railway Electrification</u>				
161	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
162	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017
163	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-
164	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-
165	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 2,911.84	- -	-
166	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
167	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
168	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
169	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	616.08 -	- -	-
170	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
171	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
	<u>South Eastern Railway</u>				
172	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 289.64	- -	-
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
174	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
175	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 293.97	06/2005 -	-
	<u>South Western Railway</u>				
176	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 986.30	- -	-
177	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-
	<u>Southern Railway</u>				
178	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018
179	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
180	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
181	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 1,566.00	- -	-
182	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
183	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
184	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
185	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
186	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- -	-
187	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
188	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
189	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
190	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-
191	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
192	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
193	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-
194	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
195	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
196	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
197	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
198	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-
199	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-
200	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
201	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
202	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-
203	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-
204	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-
205	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-
	<u>Western Railway</u>				
206	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 03/2018	05/2018
207	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
208	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-
209	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
210	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
211	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
212	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
213	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		90,296.77 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
214	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA	03/2015	298.33 -	- -	-
215	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA	03/2015	184.05 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
216	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA	03/2015	280.16 -	- -	-
217	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
218	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-
219	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-
220	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-
221	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-
222	REHABILITATION AND UPGADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
223	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
224	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
225	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
226	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
227	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
228	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-
229	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
230	REHABILITATION AND UPGADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
231	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
232	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
233	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
234	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
235	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
236	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
237	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
238	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-
239	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-
240	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
246	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-
247	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
248	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
249	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
250	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
251	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
252	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
253	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
254	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
255	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
256	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
258	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-
259	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
260	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
261	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
262	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
263	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
264	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
265	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
266	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
267	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
268	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
269	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
270	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
271	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
272	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
273	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
274	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
275	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
276	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-
277	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	06/2018 -	-
278	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
279	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
280	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
281	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	-
282	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH	03/2015	235.08 -	05/2018 -	-
283	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-
284	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-
285	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	01/2016 -	-
286	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
287	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450 - [N24000614] NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
288	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY - KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615] NHIDCL, ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	-
289	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616] NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
290	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617] NHIDCL, ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
291	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618] NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
292	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677] NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
293	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678] NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
294	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679] NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
295	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680] NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
296	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681] NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
297	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682] NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-
298	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683] NHIDCL, ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
299	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684] NHIDCL, ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
300	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685] NHIDCL, ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
301	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689] NHIDCL, NAGALAND	02/2017	507.68 -	04/2017 -	-
302	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690] NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
303	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695] NHIDCL, SIKKIM	04/2017	388.00 -	10/2017 -	-
304	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741] NHIDCL, UTTARAKHAND	03/2018	274.31 -	05/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
305	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
306	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYQJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
307	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
308	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
	National Highways Authority Of India				
309	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017
310	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
311	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
312	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
313	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	-
314	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	-
315	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	-
316	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
317	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	-
318	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-
319	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-
320	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
321	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-
322	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-
323	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
324	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-
325	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
326	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
327	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
328	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
329	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	-
330	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	-
331	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
332	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENMORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	-
333	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
334	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	-
335	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
336	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	-
337	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-
338	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
339	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
340	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-
341	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
342	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-
343	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	08/2013 -	-
344	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-
345	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
346	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	-
347	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-
348	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-
349	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
350	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
351	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
352	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
353	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	-
354	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI, RAJASTHAN	08/2015	538.08 -	02/2018 -	-
355	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI, HARYANA	08/2015	723.54 -	02/2018 -	-
356	JAISALMER - BARMER - [N24000348]NHAI, RAJASTHAN	08/2015	482.27 -	02/2018 -	-
357	JALANDHAR - AMRITSAR - [N24000351]NHAI, PUNJAB	01/2014	523.85 -	01/2016 -	-
358	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI, RAJASTHAN	07/2015	455.60 -	07/2017 -	-
359	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI, RAJASTHAN	10/2014	264.72 -	04/2017 -	-
360	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
361	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI, HARYANA	10/2015	562.34 -	04/2018 -	-
362	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
363	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
364	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
365	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
366	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI, UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
367	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
368	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI, TAMIL NADU	11/2014	563.92 -	11/2016 -	-
369	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
370	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-
371	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 -	-
372	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI, UTTAR PRADESH	09/2015	768.56 -	03/2018 -	-
373	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI, MAHARASHTRA	10/2015	531.13 -	05/2018 -	-
374	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI, UTTAR PRADESH	09/2015	664.53 -	03/2018 -	-
375	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI, UTTAR PRADESH	09/2015	789.31 -	03/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
376	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	-
377	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
378	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-
379	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
380	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	-
381	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
382	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
383	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-
384	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
385	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
386	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
387	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
388	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
389	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	-
390	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
391	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	-
392	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-
393	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	-
394	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	-
395	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	-
396	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
397	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
398	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
399	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
400	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
401	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
402	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
403	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
404	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	-
405	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
406	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-
407	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-
408	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-
409	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
410	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
411	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	-
412	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-
413	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-
414	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-
415	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
416	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
417	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
418	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
419	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
420	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-
421	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
422	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
423	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
424	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	-
425	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
426	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
427	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
428	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
429	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
430	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	-
431	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
432	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
433	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
434	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
435	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI,HARYANA	05/2015	600.85 -	05/2018 -	-
436	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
437	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I), NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
438	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
439	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
440	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
441	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
442	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
443	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- -	-
444	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
445	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
446	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-
447	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
448	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	-
449	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
450	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
451	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-
452	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-
453	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-
454	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-
455	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
456	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-
457	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
458	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
459	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
460	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
461	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
462	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
463	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
464	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-
465	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
466	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-
467	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
468	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
469	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-
470	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
471	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
472	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
473	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
474	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
475	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
476	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
477	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
478	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
479	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
480	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
481	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
482	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
483	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-
484	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
485	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
486	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
487	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI, ODISHA	01/2018	953.09 -	- -	-
488	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA	01/2018	668.86 -	- -	-
489	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI, ODISHA	01/2018	633.68 -	- -	-
490	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI, ODISHA	01/2018	614.48 -	- -	-
491	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI, ODISHA	01/2018	564.66 -	- -	-
492	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA	01/2018	686.65 -	- -	-
493	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-
494	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-
495	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	-
496	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
497	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
498	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	06/2018
National Highways Development Project					
499	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	-
500	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
501	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
502	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
503	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	-
504	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-
505	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
506	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-
507	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-
508	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
509	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
510	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-
511	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-
512	SHAHOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-
513	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
514	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-
515	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-
516	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-
517	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
518	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-
519	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
520	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-
521	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-
522	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-
	<u>Public Works Dept Of State</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(July 2018)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
523	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
524	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPPLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-
525	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
526	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
527	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
528	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	-
529	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
530	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
531	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
532	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
533	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	-
534	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-
535	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
536	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	-
537	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
538	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
539	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
540	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
541	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
542	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
543	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
544	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
545	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
546	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
547	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	-
548	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
549	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
550	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
551	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
552	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
553	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
554	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	-
555	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	-
556	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-
557	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
558	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
559	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
560	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
561	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
562	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
563	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
564	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
565	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
566	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
567	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
568	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
569	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
570	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
571	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
572	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
573	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
574	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
575	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
576	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
577	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
578	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
579	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
580	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
581	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
582	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-
583	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
584	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
585	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
586	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-
587	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-
588	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
589	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
590	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-
591	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
592	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
593	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
594	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
595	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
596	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
597	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-
598	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
599	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
600	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-
601	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
602	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
603	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
604	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
605	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
	Total		2,37,622.00 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
606	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Port Trust</u>				
607	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
608	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		2,821.90 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
609	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				
610	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(July 2018)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
611	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 349.33	03/2016 12/2017	04/2018
612	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
613	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-
614	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-
615	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-
616	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
	<u>Chennai Metro Rail Ltd</u>				
617	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Delhi Metro Rail Corporation Ltd</u>				
618	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
619	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Mumbai Metro Rail Corporation Ltd</u>				
620	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-
	<u>National Building Construcion Corporation Ltd</u>				
621	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-
	Total		70,242.04 -		
	<u>DEFENCE PRODUCTION</u>				
	<u>Goa Shipyard Limited</u>				
622	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA	12/2016	167.69 168.00	05/2018 -	05/2018
	Total		167.69 -		
	Grand Total		4,72,268.44		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (July 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
1	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	14.08	- -	01/2020	-	0/0
2	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	19.50	- -	01/2020	-	0/0
3	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.07	17.00	- -	03/2020	-	0/0
4	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	18.50	- -	04/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
5	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	22.59	- -	02/2020	-	0/0
	Total		1,909.39 -	1,909.54	91.67				0/0
	<u>RAILWAYS</u>								
	<u>Rail Vikas Nigam Ltd.</u>								
6	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	970.34 -	2,062.20	674.76	- -	03/2022	-	0/2
7	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	3,548.67	83.04	- -	12/2023	-	0/0
	<u>South Central Railway</u>								
8	BHADRALALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 704.31	704.31	119.69	- 03/2020	03/2020	0(R3)	0/1
9	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	2,288.70	334.95	- 03/2022	03/2022	0(R3)	0/1
10	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,132.77	317.57	- 03/2023	03/2023	0(R3)	0/1
11	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	3,631.00	79.73	- 03/2023	03/2023	0(R3)	0/0
12	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,856.95	2,200.00	222.91	- 03/2024	03/2024	0(R3)	0/0
	<u>South Eastern Railway</u>								
13	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 258.20	365.00	167.92	- 12/2018	12/2018	0(R3)	0/0
14	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 553.63	1,440.00	7.96	- 03/2024	03/2024	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 267.37	620.00	40.77	- 03/2025	03/2025	0(R3)	0/0
	<u>South Western Railway</u>								
16	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	1,190.92	166.00	- 03/2021	03/2021	0(R3)	0/0
17	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	1,614.59	635.98	- 03/2021	03/2021	0(R3)	0/0
18	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	8.90	- 12/2023	12/2023	0(R3)	0/0
19	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	1,350.91	873.61	- -	12/2023	-	0/1
20	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- 12/2023	12/2023	0(R3)	0/0
21	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- 12/2023	12/2023	0(R3)	0/0
22	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	.35	- 12/2023	12/2023	0(R3)	0/0
23	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	0(R3)	0/0
24	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	1,382.78	7.90	- 03/2024	03/2024	0(R3)	0/0
25	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	.94	- 03/2024	03/2024	0(R3)	0/0
26	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	2,135.00	134.15	- 12/2024	12/2024	0(R3)	0/0
27	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 2,841.84	2,841.84	17.97	- 12/2024	12/2024	0(R3)	0/0
	<u>Southern Railway</u>								
28	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	55.87	- -	03/2020	-	0/0
	<u>Western Railway</u>								
29	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	576.05	- 03/2019	03/2022	36(R3)	0/0
30	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	844.10	48.99	- 03/2022	03/2023	12(R3)	0/0
	Total		23,929.86 -	36,458.96	4,576.35				0/6
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
31	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	275.90	223.48	- -	10/2018	-	0/0
32	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	417.19	30.19	- -	09/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (July 2018)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
33	FOUR LANE WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	752.28	-	-	11/2019	-	0/0
34	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	-	-	12/2019	-	0/0
35	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	-	-	04/2020	-	0/0
36	4 LANE FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	1,169.61	59.82	-	04/2020	-	0/0
37	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	-	-	07/2020	-	0/0
38	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI, HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	-	-	09/2020	-	0/0
	Total		7,704.31 -	7,704.31	313.49				0/0
	Grand Total		33,543.56	46,072.81	4,981.51				0/6

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 -	09/2018	0/0
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Neyveli Lignite Corporation</u>					
3	NEYVELI SOLAR POWER PROJECT 130 MW - [N06000151]NLC,TAMIL NADU	05/2016	687.28 759.19	06/2017 12/2017	12/2017	0/0
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
6	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Northern Coal Fields Limited</u>					
7	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17 -	03/2022 -	03/2022	0/0
	<u>Western Coal Fields Limited</u>					
8	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
9	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>FERTILISERS</u>					
	<u>Rashtriya Chemical & Fertiliser Limited</u>					
10	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72 -	04/2020 -	04/2020	0/0
	<u>MINES</u>					
	<u>National Aluminum Company Limited (Nalco)</u>					
11	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	04/2021 04/2021	04/2021	0/0
	<u>STEEL</u>					
	<u>Hindustan Steelwork Construction Limited</u>					
12	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	08/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
13	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	09/2017 -	12/2018	0/0
14	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	12/2016 -	12/2018	0/0
15	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
16	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL, TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
17	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL, TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
18	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL, TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
19	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL, KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
20	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL, KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
21	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL, ANDHRA PRADESH	07/2014	232.00 -	01/1999 -	-	0/0
22	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL, GUJARAT	01/2013	175.00 -	- -	-	0/0
23	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL, JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
24	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL, JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
25	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL, JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
26	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
<u>Steel Authority Of India Limited (Sail)</u>						
27	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL, JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
<u>PETROLEUM</u>						
<u>Bharat Petroleum Corporation Limited</u>						
28	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0
29	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL, MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
30	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
<u>Chennai Petroleum Corporation Limited</u>						
31	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	12/2019	0/0
32	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	08/2020	0/0
<u>Gas Authority Of India Limited</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
33	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00 -	02/2020 -	02/2020	0/0
34	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE	06/2018	3,308.00 -	12/2021 -	12/2021	0/0
35	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53 243.53	07/2022 -	07/2022	0/0
36	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	181.20 -	07/2022 -	07/2022	0/0
37	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25 -	10/2022 -	10/2022	0/0
38	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45 -	10/2022 -	10/2022	0/0
<u>Hindustan Petroleum Corporation Limited</u>						
39	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00 -	03/2020 -	07/2019	0/0
40	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	06/2020 -	06/2020	0/0
41	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	06/2020 -	06/2020	0/0
42	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA	11/2017	255.00 -	11/2020 -	11/2020	0/0
43	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00 -	04/2021 -	04/2021	0/0
<u>Indian Oil Corporation Limited</u>						
44	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	08/2018	0/0
45	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH	01/2018	666.64 -	09/2019 -	09/2019	0/0
46	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT	03/2018	3,380.00 -	09/2019 -	09/2019	0/0
47	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM	05/2018	1,222.00 -	09/2019 -	09/2019	0/0
48	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL	05/2018	2,934.40 -	09/2019 -	09/2019	0/0
49	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA	12/2017	3,529.00 -	09/2019 -	09/2019	0/0
50	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 -	02/2020 -	02/2020	0/0
51	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	02/2020 -	02/2020	0/0
52	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2020	0/0
53	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	06/2020	0/0
54	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
55	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT	09/2016	208.35 -	07/2020 -	07/2020	0/0
56	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]IOCL,GUJARAT	08/2017	1,342.00 -	08/2020 -	08/2020	0/0
57	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	08/2020 -	08/2020	0/0
58	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	10/2020	0/0
59	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	10/2020 -	10/2020	0/0
60	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	12/2020 -	12/2020	0/0
61	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00 -	12/2020 -	12/2020	0/0
62	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	01/2021	0/0
63	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	01/2021	0/0
64	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	01/2021 -	01/2021	0/0
65	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00 -	03/2021 -	03/2021	0/0
66	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00 -	03/2021 -	03/2021	0/0
67	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	08/2021	0/0
68	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00 -	12/2021 -	12/2021	0/0
69	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH	03/2018	676.00 -	12/2021 -	12/2021	0/0
70	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL	03/2018	3,712.00 -	09/2022 -	09/2022	0/0
71	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-	0/0
	<u>Indian Strategic Petroleum Reserves Ltd</u>					
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
	<u>Mangalore Refinery And Petrochemicals Limited</u>					
73	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	03/2020 -	03/2020	0/0
	<u>Oil & Natural Gas Corporation Limited</u>					
74	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 05/2018	05/2018	0/0
75	GAMJI REDEVELOPMENT PROJECT - [N16000202]ONGC,GUJARAT	05/2015	1,671.22 567.22	11/2019 12/2018	07/2018	0/0
76	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]ONGC,GUJARAT	11/2014	195.63 -	09/2018 09/2018	09/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]ONGC,MAHARASHTRA	02/2015	2,899.93 -	05/2017 12/2018	12/2018	0/0
78	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 207.80	09/2018 02/2019	02/2019	0/0
79	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 6,068.80	04/2019 03/2019	03/2019	0/0
80	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	12/2017 03/2019	03/2019	0/0
81	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	03/2019 -	04/2019	0/0
82	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	04/2018 05/2019	05/2019	0/0
83	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA	01/2017	474.15 474.15	05/2019 05/2019	05/2019	0/0
84	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	05/2019 10/2019	10/2019	0/0
85	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA	02/2017	546.15 546.15	11/2019 11/2019	11/2019	0/0
86	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA	02/2017	511.30 511.30	11/2019 11/2019	11/2019	0/0
87	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA	02/2017	968.61 968.61	11/2019 11/2019	11/2019	0/0
88	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA	04/2018	766.37 -	12/2019 -	12/2019	0/0
89	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	03/2019 05/2020	05/2020	0/0
90	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 249.85	05/2020 05/2020	05/2020	0/0
91	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,006.83	05/2021 05/2021	05/2021	0/0
92	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	06/2020 08/2021	08/2021	0/0
93	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND	12/2015	658.62 910.23	03/2023 03/2022	03/2022	0/0
94	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT	02/2017	1,162.56 1,162.56	03/2026 03/2026	03/2026	0/0
<u>Oil India Limited</u>						
95	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	03/2017 11/2018	03/2019	0/0
96	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
97	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	12/2019 -	12/2019	0/0
98	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 -	02/2020 -	02/2020	0/0
99	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	10/2020 -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
	<u>POWER</u>					
	<u>Chenab Valley Power Projects [P] Limited</u>					
101	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	10/2023	0/0
	<u>National Hydro-Electric Power Corporation</u>					
102	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
	<u>National Thermal Power Corporation</u>					
103	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,552.00	10/2017 -	12/2016	0/0
104	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
	<u>Power Grid Corporation Of India Limited</u>					
105	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	11/2017 -	07/2018	0/0
106	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	01/2018 -	07/2018	0/0
107	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	07/2018 -	08/2018	0/0
108	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 -	08/2018	0/0
109	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	07/2018 -	08/2018	0/0
110	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	09/2018	0/0
111	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	09/2017 09/2018	09/2018	0/0
112	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195]PGCIL,DELHI	05/2015	780.33 -	10/2018 -	09/2018	0/0
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206]PGCIL,MADHYA PRADESH	01/2016	305.04 -	03/2017 09/2018	09/2018	0/0
114	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS-KARGIL-KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	09/2017 -	09/2018	0/0
115	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	12/2015 -	09/2018	0/0
116	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	10/2018	0/0
117	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	07/2018 -	10/2018	0/0
118	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201]PGCIL,RAJASTHAN	07/2015	307.18 -	11/2017 10/2018	10/2018	0/0
119	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	06/2018 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
120	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL, MADHYA PRADESH	02/2015	1,750.00 -	06/2018 -	10/2018	0/0
121	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL, MULTI STATE	08/2008	771.00 1,642.00	02/2013 -	10/2018	0/0
122	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217]PGCIL, MULTI STATE	05/2016	766.21 -	11/2018 -	11/2018	0/0
123	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224]PGCIL, MULTI STATE	05/2016	167.01 -	11/2018 -	11/2018	0/0
124	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]PGCIL, MULTI STATE	04/2016	810.48 -	12/2018 -	12/2018	0/0
125	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228]PGCIL, GUJARAT	07/2016	300.94 -	12/2018 -	12/2018	0/0
126	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL, RAJASTHAN	07/2016	1,429.38 -	01/2019 -	01/2019	0/0
127	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL, MULTI STATE	10/2016	408.46 -	01/2019 -	01/2019	0/0
128	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231]PGCIL, MULTI STATE	08/2016	431.89 -	02/2019 -	02/2019	0/0
129	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232]PGCIL, MULTI STATE	08/2016	177.52 -	02/2019 -	02/2019	0/0
130	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL, MULTI STATE	02/2017	322.30 -	02/2019 -	02/2019	0/0
131	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL, KARNATAKA	05/2017	445.89 -	02/2019 -	02/2019	0/0
132	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL, MULTI STATE	03/2016	808.63 -	01/2018 03/2019	03/2019	0/0
133	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230]PGCIL, MULTI STATE	07/2016	333.17 -	03/2019 -	03/2019	0/0
134	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL, MULTI STATE	09/2016	562.25 -	03/2019 -	03/2019	0/0
135	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODISHA - [N18000243]PGCIL, MULTI STATE	03/2017	162.31 -	03/2019 -	03/2019	0/0
136	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL, ODISHA	04/2016	844.64 -	04/2019 -	04/2019	0/0
137	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL, MULTI STATE	10/2016	608.24 -	04/2019 -	04/2019	0/0
138	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL, MULTI STATE	12/2015	3,654.00 -	04/2019 -	04/2019	0/0
139	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL, MULTI STATE	05/2016	3,519.59 -	05/2019 -	05/2019	0/0
140	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL, BIHAR	04/2016	790.13 -	06/2019 -	06/2019	0/0
141	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL, MULTI STATE	03/2017	251.60 -	06/2019 -	06/2019	0/0
142	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL, MULTI STATE	02/2017	235.53 -	06/2019 -	06/2019	0/0
143	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL, MULTI STATE	03/2017	337.75 -	06/2019 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
144	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT	05/2017	175.64 -	09/2018 -	06/2019	0/0
145	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT	12/2017	193.14 -	06/2019 -	06/2019	0/0
146	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL, TAMIL NADU	05/2017	186.17 -	07/2019 -	07/2019	0/0
147	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]PGCIL, MULTI STATE	02/2017	204.12 -	09/2019 -	09/2019	0/0
148	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 -	09/2019 -	09/2019	0/0
149	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL, MULTI STATE	05/2016	14,733.37 -	11/2019 -	11/2019	0/0
150	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL, MULTI STATE	03/2017	283.72 -	11/2019 -	11/2019	0/0
151	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL, MULTI STATE	03/2017	379.95 -	12/2019 -	12/2019	0/0
152	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL, MULTI STATE	12/2014	4,754.42 -	12/2018 -	12/2019	0/0
153	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 -	12/2018 -	12/2019	0/0
154	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL, MULTI STATE	02/2017	195.05 -	02/2020 -	02/2020	0/0
155	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 -	02/2020 -	02/2020	0/0
156	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 -	04/2020 -	04/2020	0/0
157	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 -	05/2020 -	05/2020	0/0
158	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 - 3,500.00	07/2020 -	07/2020	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Indira Gandhi Centre For Atomic Research</u>					
159	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]IGCAR, DELHI	08/2016	1,554.00 -	08/2016 -	09/2019	0/0
	<u>Natip Implementation Society</u>					
160	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00 -	09/2011 -	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
161	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES, UTTAR PRADESH	07/2016	785.00 -	04/2020 -	04/2020	0/0
162	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES, PUNJAB	07/2016	703.00 -	06/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
163	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00	05/2021	05/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
164	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19	03/2019	03/2019	0/0
165	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99	-	01/2020	0/0
166	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL	04/2018	651.99	-	01/2020	0/0
167	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01	-	03/2020	0/0
168	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84	-	04/2020	0/0
169	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02	-	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
170	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00	09/2018	09/2018	0/0
171	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19	03/2019	03/2019	0/0
172	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15	03/2019	03/2019	0/0
173	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99	05/2018	09/2019	0/0
174	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56	-	02/2020	0/0
175	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	11/2013	-	0/0
176	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57	12/2014	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
177	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019	03/2019	0/0
178	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 2,271.50	03/2021	03/2021	0/0
179	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 792.89	03/2021	03/2021	0/0
180	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 540.02	03/2022	03/2022	0/0
181	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	630.00 1,272.19	03/2022	03/2022	0/0
182	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 3,168.29	03/2023	03/2023	0/0
183	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,326.00 2,449.91	03/2023	03/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
184	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	03/2023 -	03/2023	0/0
185	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	854.00 1,035.16	03/2023 -	03/2023	0/0
186	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	912.00 637.95	03/2023 -	03/2023	0/0
187	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
188	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
189	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
190	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	4,670.00 3,627.47	03/2024 -	03/2024	0/0
191	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
<u>Container Corporation Of India</u>						
192	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	03/2018	0/0
193	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	03/2019	0/0
194	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	03/2019	0/0
195	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	08/2019	0/0
196	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	12/2019	0/0
197	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
198	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
199	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
200	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
201	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 -	- -	-	0/0
<u>East Central Railways</u>						
202	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	03/2018 -	12/2019	0/0
203	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
204	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
205	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
206	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-	0/0
207	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-	0/0
208	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-	0/0
209	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
210	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
211	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 283.95	03/2012 -	-	0/0
212	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
213	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
214	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
215	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
216	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
217	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
218	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
219	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
220	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
221	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS (NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
222	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
223	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
224	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
<u>East Coast Railway</u>						
225	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
226	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
227	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 1,539.28	03/2021 -	03/2021	0/0
228	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 843.04	03/2021 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
229	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2021 -	03/2021	0/0
230	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	03/2021 -	03/2021	0/0
231	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	03/2021 -	03/2021	0/0
232	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	06/2021 -	06/2021	0/0
233	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 2,499.71	03/2021 -	03/2022	0/0
234	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 2,361.74	03/2021 -	03/2022	0/0
235	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	12/2022 -	03/2023	0/0
236	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
237	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
238	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
239	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
240	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
	<u>Eastern Railways</u>					
241	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	11/2018	0/0
242	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2019	0/0
243	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	03/2020	0/0
244	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-	0/0
245	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-	0/0
246	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	533.38 -	12/2011 -	-	0/0
247	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 -	-	0/0
248	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER,WEST BENGAL	04/2004	293.74 -	12/2010 -	-	0/0
249	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 -	12/2012 -	-	0/0
250	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-	0/0
251	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
253	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0
254	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	-	0/0
255	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
256	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
257	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
258	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
259	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
260	SONDALIA-CHAMPAPUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
261	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
262	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
263	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
264	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
265	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
266	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
267	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
268	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
269	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
270	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
271	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
272	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	-	0/0
273	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
274	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
275	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
276	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
277	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>					
278	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	03/2019	0/0
279	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [N220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
280	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [N220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
281	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
282	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
283	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
284	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	02/2020 -	12/2022	0/0
285	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	02/2019 -	12/2022	0/0
286	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [N220100007]NCR, MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
287	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [N220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
288	ETAWAH-MAINPURI (NL), NCR - [N220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>North East Frontier Railway</u>					
289	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 4,118.00	03/2007 -	04/2016	0/0
290	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	523.17 -	- -	03/2018	0/0
291	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [N220100201]NFR, ASSAM	09/1997	1,500.00 4,857.00	04/2008 12/2011	06/2018	0/0
292	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [N220100266]NFR, MULTI STATE	04/2000	733.00 -	12/2008 -	03/2019	0/0
293	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0
294	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 -	03/2019 -	03/2019	0/0
295	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	312.12 -	03/2019 -	03/2019	0/0
296	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 -	03/2019 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
297	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	03/2019 -	03/2020	0/0
298	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	03/2011 -	03/2020	0/0
299	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	03/2019 -	03/2020	0/0
300	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	03/2019 -	03/2020	0/0
301	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 -	03/2014 -	03/2020	0/0
302	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 -	04/2014 -	03/2020	0/0
303	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92 -	03/2020 -	03/2020	0/0
304	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
305	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	850.00 -	03/2015 -	03/2020	0/0
306	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	03/2020 -	03/2020	0/0
307	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
308	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
309	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	165.82 -	03/2020 -	03/2020	0/0
310	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	556.31 -	03/2020 -	03/2020	0/0
311	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	4,083.02 -	03/2021 -	03/2021	0/0
312	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
313	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	03/2022 -	03/2022	0/0
314	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	12/2010 -	-	0/0
315	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	- -	-	0/0
<u>North Eastern Railway</u>						
316	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	01/2018	0/0
317	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
318	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 -	06/2018 -	06/2018	0/0
319	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	08/2018 -	08/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
320	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	08/2018	0/0
321	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	11/2018	0/0
322	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2019	0/0
323	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,750.00 -	03/2022 -	02/2019	0/0
324	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	05/2019 -	05/2019	0/0
325	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	01/2022	0/0
326	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0
327	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
328	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
329	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	10/2022	0/0
330	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
331	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
332	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
333	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
334	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-	0/0
<u>North Western Railway</u>						
335	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	10/2018	0/0
336	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	11/2018 -	11/2018	0/0
337	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	02/2019	0/0
338	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2019	0/0
339	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	03/2014 03/2019	03/2019	0/0
340	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2019	0/0
341	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	11/2019	0/0
342	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 295.02	12/2019 -	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
343	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2020	0/0
344	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	03/2020	0/0
345	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	08/2022	0/0
346	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
347	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0
	<u>Northern Railway</u>					
348	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002 03/2021	03/2021	0/0
349	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
350	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
351	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
352	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 -	-	0/0
353	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
354	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
355	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
356	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
357	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
358	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
359	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
360	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
361	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
362	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
363	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
364	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
365	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
366	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
367	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
368	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
369	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
370	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
371	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	03/2020 09/2009	03/2020	0/0
372	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	03/2020	0/0
373	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
374	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	1,514.45 -	03/2020 -	03/2020	0/0
375	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	960.18 -	03/2020 -	03/2020	0/0
376	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	758.09 -	03/2020 -	03/2020	0/0
377	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 -	12/2020	0/0
378	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.65 -	12/2020 -	12/2020	0/0
379	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	376.59 -	03/2021 -	03/2021	0/0
380	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
381	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
382	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	12/2021	0/0
383	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	567.18 -	12/2021 -	12/2021	0/0
384	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,266.89 -	12/2021 -	12/2021	0/0
385	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 632.00	12/2012 -	03/2022	0/0
386	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
387	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	- -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
388	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	750.55 -	12/2024 -	12/2024	0/0
389	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	728.10 -	12/2024 -	12/2024	0/0
390	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 2,735.00	12/2024 -	12/2024	0/0
391	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
392	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 4,200.00	03/2016 -	03/2025	0/0
393	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
394	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
395	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.90 -	12/2025 -	12/2025	0/0
396	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	4,295.30 -	12/2026 -	03/2026	0/0
397	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	1,046.88 -	12/2026 -	12/2026	0/0
	<u>Railway Electrification</u>					
398	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
	<u>South Central Railway</u>					
399	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 926.23	- 03/2017	03/2017	0/0
400	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	03/2019 03/2019	03/2019	0/0
401	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2021	0/0
402	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
403	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	03/2021 03/2023	03/2023	0/0
404	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	4,000.00 -	- 03/2023	03/2023	0/0
405	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 1,856.95	- 03/2024	03/2024	0/0
406	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	-	0/0
407	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	-	0/0
408	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
409	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
	<u>South East Central Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
410	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	737.72 -	12/2018 -	12/2018	0/0
411	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	03/1998 -	12/2019	0/0
412	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,273.00 1,908.00	12/2021 -	12/2021	0/0
413	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-	0/0
<u>South Eastern Railway</u>						
414	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 309.44	12/2015 11/2018	11/2018	0/0
415	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 258.20	- 12/2018	12/2018	0/0
416	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 148.77	12/2016 08/2018	12/2018	0/0
417	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 969.83	03/2020 03/2020	06/2020	0/0
418	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	03/2021 03/2021	12/2021	0/0
419	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	763.18 1,013.45	12/2021 12/2021	12/2021	0/0
420	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 553.63	- 03/2024	03/2024	0/0
421	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 466.48	01/1999 12/2024	12/2024	0/0
422	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 524.43	12/2021 12/2024	12/2024	0/0
423	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2025	03/2025	0/0
424	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 267.37	- 03/2025	03/2025	0/0
425	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 276.69	01/1999 03/2030	03/2030	0/0
426	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
427	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 289.64	- -	-	0/0
428	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
429	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
430	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 293.97	06/2005 -	-	0/0
<u>South Western Railway</u>						
431	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 860.43	03/2020 03/2020	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	- 03/2021	03/2021	0/0
433	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,618.00 1,614.59	- 03/2021	03/2021	0/0
434	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- 12/2023	12/2023	0/0
435	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	- 12/2023	12/2023	0/0
436	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- 12/2023	12/2023	0/0
437	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- 12/2023	12/2023	0/0
438	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	- 12/2023	12/2023	0/0
439	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 279.54	01/1999 12/2023	12/2023	0/0
440	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 1,382.78	- 03/2024	03/2024	0/0
441	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- 03/2024	03/2024	0/0
442	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 -	- 12/2024	12/2024	0/0
443	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 2,841.84	- 12/2024	12/2024	0/0
444	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	- -	-	0/0
<u>Southern Railway</u>						
445	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	03/2018	0/0
446	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0
447	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	03/2020	0/0
448	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
449	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
450	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
451	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
452	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 1,566.00	- -	-	0/0
453	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-	0/0
454	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
455	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-	0/0
456	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 527.37	- -	-	0/0
457	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
458	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
459	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
460	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 346.15	- -	-	0/0
461	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
462	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
463	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 342.85	- -	-	0/0
464	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
465	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
466	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	900.00 -	- -	-	0/0
467	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
468	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-	0/0
469	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-	0/0
470	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
471	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
472	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-	0/0
473	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-	0/0
474	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-	0/0
475	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-	0/0
<u>West Central Railway</u>						
476	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	03/2021 -	03/2021	0/0
<u>Western Railway</u>						

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
477	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 2,446.85	03/2014 03/2018	05/2018	0/0
478	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
479	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	03/2013 -	03/2020	0/0
480	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	03/2021 03/2019	03/2021	0/0
481	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 2,473.40	03/2012 03/2019	03/2022	0/0
482	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- 03/2019	03/2022	0/0
483	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	03/2022 03/2019	03/2022	0/0
484	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 1,378.12	03/2019 03/2019	03/2022	0/0
485	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- 03/2022	03/2023	0/0
486	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
487	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 384.32	- -	-	0/0
488	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
489	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
490	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
491	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
492	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
493	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	11/2018	0/0
494	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(BRAHMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
495	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
496	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
497	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
498	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
499	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
500	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
501	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
502	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
503	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
504	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	03/2015 -	-	0/0
505	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
506	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
507	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
508	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
509	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
510	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
511	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-	0/0
512	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
513	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
514	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-	0/0
515	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-	0/0
516	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
517	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
518	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
519	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
520	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
521	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
522	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-	0/0
523	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0
524	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
525	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
526	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
527	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
528	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
529	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
530	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
531	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
532	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
533	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
534	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
535	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
536	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
537	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
538	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
539	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
540	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
541	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
542	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
543	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
544	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
545	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
546	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
547	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0
548	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
549	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
550	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-	0/0
National Highways And Infrastructure Development Corporation Ltd.						
551	(I) CONSTRUCTION OF FOUR/SIX LANE FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	09/2018	0/0
552	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	09/2018	0/0
553	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	09/2018	0/0
554	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	09/2018	0/0
555	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	09/2018	0/0
556	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	09/2018	0/0
557	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	09/2018	0/0
558	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	09/2018	0/0
559	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	09/2018	0/0
560	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	09/2018	0/0
561	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	09/2018	0/0
562	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	09/2018	0/0
563	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	09/2018	0/0
564	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	09/2018	0/0
565	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	10/2018	0/0
566	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	10/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
567	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	10/2018	0/0
568	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	12/2018 -	12/2018	0/0
569	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	08/2019	0/0
570	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	08/2019	0/0
571	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	08/2019	0/0
572	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	01/2017 -	01/2020	0/0
573	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL,ASSAM	12/2015	223.30 -	06/2018 -	-	0/0
574	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
575	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-	0/0
576	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	- -	-	0/0
577	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACHAL - [N24000618]NHIDCL,ARUNACHAL PRADESH	11/2015	434.06 -	- -	-	0/0
578	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-	0/0
579	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-	0/0
580	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-	0/0
581	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-	0/0
582	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-	0/0
583	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-	0/0
584	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-	0/0
585	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-	0/0
586	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-	0/0
587	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
588	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
589	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-	0/0
590	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-	0/0
591	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-	0/0
592	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYQJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-	0/0
593	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-	0/0
594	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-	0/0
National Highways Authority Of India						
595	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	07/2018	0/0
596	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	11/2017	0/0
597	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	07/2018	0/0
598	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500]NHAI,MADHYA PRADESH	01/2016	830.36 -	07/2018 -	07/2018	0/0
599	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	07/2018	0/0
600	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	07/2018	0/0
601	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	07/2018	0/0
602	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	08/2018	0/0
603	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	08/2018	0/0
604	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2018	0/0
605	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	08/2018	0/0
606	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	09/2018	0/0
607	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	09/2018	0/0
608	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	09/2018	0/0
609	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
610	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	09/2018	0/0
611	PADI - DAHOD - [N24000353]NHAI,RAJASTHAN	11/2014	279.14 -	05/2017 -	09/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
612	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	04/2009 -	10/2018	0/0
613	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018	0/0
614	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	10/2018	0/0
615	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	10/2018	0/0
616	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	10/2018	0/0
617	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	11/2018	0/0
618	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	03/2018 -	11/2018	0/0
619	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	11/2018	0/0
620	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	11/2018	0/0
621	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	11/2018 -	11/2018	0/0
622	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	12/2018	0/0
623	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	12/2018	0/0
624	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
625	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	12/2018	0/0
626	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2018	0/0
627	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	12/2018	0/0
628	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	12/2018	0/0
629	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	12/2018	0/0
630	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0
631	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	01/2019	0/0
632	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	01/2019	0/0
633	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	01/2019	0/0
634	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	02/2019	0/0
635	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	02/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
636	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
637	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	03/2019	0/0
638	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0
639	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 -	03/2019	0/0
640	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	03/2019	0/0
641	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	03/2019	0/0
642	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019	0/0
643	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2019	0/0
644	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019	0/0
645	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	03/2019	0/0
646	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	03/2019	0/0
647	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
648	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
649	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0
650	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	04/2019	0/0
651	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	04/2019	0/0
652	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
653	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0
654	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	04/2019	0/0
655	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	04/2019	0/0
656	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	04/2019	0/0
657	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	05/2019	0/0
658	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
659	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
660	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	05/2019	0/0
661	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540]NHAI, UTTAR PRADESH	01/2016	701.12 -	05/2019 -	05/2019	0/0
662	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI, HARYANA	08/2016	248.97 -	05/2019 -	05/2019	0/0
663	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI, HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
664	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI, MAHARASHTRA	01/2017	244.90 -	05/2019 -	05/2019	0/0
665	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI, MAHARASHTRA	03/2017	296.19 -	03/2020 -	05/2019	0/0
666	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	11/2011 -	06/2019	0/0
667	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2019	0/0
668	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	06/2019	0/0
669	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	06/2019	0/0
670	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
671	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI, TAMIL NADU	02/2016	707.82 -	08/2018 -	06/2019	0/0
672	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	06/2019	0/0
673	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	06/2019	0/0
674	4 LANING OF PISKA MORE TO PALMA SECTION (FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI, JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
675	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	07/2019	0/0
676	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI, MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
677	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI, MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0
678	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI, ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
679	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209 (EXISTING CHAINAGE FROM - [N24000622]NHAI, KARNATAKA	09/2016	950.69 -	08/2019 -	08/2019	0/0
680	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
681	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]NHAI, PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
682	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
683	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	- -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
684	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	12/2019	0/0
685	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI, TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
686	FOUR LANNING OF JHANSI-KHAJURAHO SECTION (PKG-I) FROM KM 0.00 TO KM 76.3 (EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI, UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	03/2020	0/0
687	FOUR LANNING OF JHANSI-KHAJURAHO SECTION (PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3 (EXISTING C - [N24000654]NHAI, UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	03/2020	0/0
688	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI, MAHARASHTRA	03/2017	247.02 -	03/2020 -	03/2020	0/0
689	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]NHAI, MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
690	4-LANNING OF MAHAGAON-YAVATMAL SECTION (KM 320.580 TO 400.575) - [N24000661]NHAI, MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	03/2020	0/0
691	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI, PUNJAB	03/2017	754.54 -	03/2020 -	03/2020	0/0
692	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI, UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	03/2020	0/0
693	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI, HARYANA	03/2017	639.79 -	03/2020 -	03/2020	0/0
694	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI, BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
695	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	03/2020	0/0
696	REHABILITATION AND UPGRADE OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI, ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	03/2020	0/0
697	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI, JHARKHAND	03/2017	239.68 -	03/2020 -	03/2020	0/0
698	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI, UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
699	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000665]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
700	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI, PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
701	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
702	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN	04/2017	894.00 -	04/2020 -	04/2020	0/0
703	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI, MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
704	4-LANNING OF WARDHA- BUTIBORI SECTION (KM 465.500 TO 524.690) - [N24000657]NHAI, MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0
705	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI, ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
706	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS (KM 189+000 TO KM 260+000 OF NH-48 (O - [N24000675]NHAI, KARNATAKA	03/2017	993.16 -	03/2020 -	05/2020	0/0
707	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48 (OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI, KARNATAKA	03/2017	831.58 -	03/2020 -	06/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
708	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	06/2020	0/0
709	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI, GUJARAT	06/2017	1,958.88 -	06/2020 -	06/2020	0/0
710	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	-	07/2020	0/0
711	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
712	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	-	09/2020	0/0
713	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
714	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
715	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
716	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
717	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
718	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	-	0/0
719	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	-	0/0
720	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	-	0/0
721	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
722	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	-	0/0
723	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	-	0/0
724	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	-	0/0
725	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	-	0/0
726	DEOLI KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	-	0/0
727	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
728	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	-	0/0
729	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
730	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
731	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
732	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	-	0/0
733	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
734	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	11/2013 -	-	0/0
735	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
736	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
737	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
738	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	03/2014 -	-	0/0
739	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
740	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, BIHAR	05/2011	664.00 -	02/2014 -	-	0/0
741	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
742	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
743	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
744	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
745	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
746	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	-	0/0
747	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	-	0/0
748	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
749	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
750	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	07/2014 -	-	0/0
751	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
752	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
753	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
754	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
755	2-LANING WITH PS BHILWARA-LODPURA SECTION - [N24000240]NHAI, RAJASTHAN	03/2014	240.10 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
756	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N - [N24000337]NHAI,RAJASTHAN	08/2015	538.08 -	02/2018 -	-	0/0
757	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
758	JAISALMER - BARMER - [N24000348]NHAI,RAJASTHAN	08/2015	482.27 -	02/2018 -	-	0/0
759	JALANDHAR - AMRITSAR - [N24000351]NHAI,PUNJAB	01/2014	523.85 -	01/2016 -	-	0/0
760	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50) - [N24000352]NHAI,RAJASTHAN	07/2015	455.60 -	07/2017 -	-	0/0
761	JODHPUR - BARMER SECTION OF PACKAGE -I - [N24000354]NHAI,RAJASTHAN	10/2014	264.72 -	04/2017 -	-	0/0
762	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
763	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA(PKG - 2) - [N24000358]NHAI,HARYANA	10/2015	562.34 -	04/2018 -	-	0/0
764	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
765	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
766	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
767	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
768	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
769	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
770	THANJAVUR - PUDUKOTTAI SECTION OF NH-226 - [N24000368]NHAI,TAMIL NADU	11/2014	563.92 -	11/2016 -	-	0/0
771	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	-	0/0
772	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
773	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	-	0/0
774	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI) - [N24000433]NHAI,UTTAR PRADESH	09/2015	768.56 -	03/2018 -	-	0/0
775	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	-	0/0
776	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V) - [N24000436]NHAI,UTTAR PRADESH	09/2015	664.53 -	03/2018 -	-	0/0
777	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV) - [N24000440]NHAI,UTTAR PRADESH	09/2015	789.31 -	03/2018 -	-	0/0
778	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	-	0/0
779	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
780	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
781	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
782	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	-	0/0
783	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
784	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
785	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	-	0/0
786	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
787	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
788	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
789	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
790	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
791	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	- -	-	0/0
792	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
793	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION - [N24000481]NHAI,CHHATISGARH	02/2013	1,232.00 -	08/2015 -	-	0/0
794	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	-	0/0
795	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	-	0/0
796	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21 - [N24000484]NHAI,PUNJAB	12/2015	239.23 -	12/2017 -	-	0/0
797	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - [N24000487]NHAI,HARYANA	07/2015	1,393.00 -	- -	-	0/0
798	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
799	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
800	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
801	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
802	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
803	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
804	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
805	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
806	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	-	0/0
807	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
808	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
809	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	-	0/0
810	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	-	0/0
811	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-	0/0
812	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
813	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	-	0/0
814	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
815	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
816	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	-	0/0
817	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
818	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
819	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
820	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
821	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
822	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	-	0/0
823	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
824	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
825	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
826	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	-	0/0
827	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
828	FOUR LANING OF TALAJA – MAHUA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-	0/0
829	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-	0/0
830	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-	0/0
831	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-	0/0
832	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	- -	-	0/0
833	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
834	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	- -	-	0/0
835	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	- -	-	0/0
836	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	- -	-	0/0
837	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA- BARWALA - PANCHKULA (PKG - 1) - [N24000597]NHAI, HARYANA	05/2015	600.85 -	05/2018 -	-	0/0
838	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI, KARNATAKA	05/2014	720.69 -	- -	-	0/0
839	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI, DELHI	09/2015	771.18 -	- -	-	0/0
840	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI, HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
841	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN	09/2016	1,239.82 -	- -	-	0/0
842	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
843	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT (APP - [N24000624]NHAI, MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
844	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- -	-	0/0
845	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- -	-	0/0
846	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI, MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
847	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI, ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
848	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-	0/0
849	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
850	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN	12/2016	1,031.95 -	- -	-	0/0
851	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI, UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
852	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
853	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	-	0/0
854	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-	0/0
855	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	-	0/0
856	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	-	0/0
857	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
858	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	-	0/0
859	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
860	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-	0/0
861	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
862	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
863	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
864	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
865	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
866	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	-	0/0
867	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
868	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	-	0/0
869	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
870	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
871	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	-	0/0
872	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
873	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-	0/0
874	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0
875	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
876	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
877	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
878	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
879	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
880	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
881	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
882	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
883	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
884	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
885	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	-	0/0
886	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
887	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
888	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-	0/0
889	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM 206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
890	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-	0/0
891	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
892	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
893	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
894	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-	0/0
895	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
896	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
897	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-	0/0
898	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
899	FOUR LANE OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
	<u>National Highways Development Project</u>					
900	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP, MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-	0/0
901	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP, UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
902	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO 150 - [N24000377]NHDP, UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-	0/0
903	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP, MADHYA PRADESH	06/2015	390.51 -	-	-	0/0
904	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP, MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
905	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP, MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
906	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP, MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-	0/0
907	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP, UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-	0/0
908	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP, MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-	0/0
909	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP, MADHYA PRADESH	08/2015	257.80 -	-	-	0/0
910	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP, UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-	0/0
911	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP, UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-	0/0
912	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP, MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-	0/0
913	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP, MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
914	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP, UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-	0/0
915	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP, MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
916	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP, MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-	0/0
917	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP, MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-	0/0
918	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP, MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-	0/0
	<u>Public Works Dept Of State</u>					
919	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.05	11/2017 08/2018	10/2018	0/0
920	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.43	09/2017 08/2018	11/2018	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
921	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
922	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-	0/0
923	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
924	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
925	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
926	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-	0/0
927	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
928	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-	0/0
929	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
930	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-	0/0
931	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-	0/0
932	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-	0/0
933	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-	0/0
934	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-	0/0
935	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-	0/0
936	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
937	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0
938	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
939	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
940	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
941	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
942	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
943	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
944	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
945	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
946	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
947	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
948	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
949	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
950	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
951	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
952	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
953	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
954	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
955	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
956	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
957	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
958	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
959	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-	0/0
960	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0
961	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
962	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
963	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-	0/0
964	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
965	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
966	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
967	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-	0/0
968	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
969	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
970	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
971	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
972	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-	0/0
973	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-	0/0
974	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
975	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
976	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
977	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
978	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
979	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
980	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
981	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
982	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Kamarajar Port Limited</u>					
983	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0
	<u>Mumbai Port Trust</u>					
984	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	12/2018	0/0
	<u>Port Trust</u>					
985	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
986	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
987	MAHARASHTRA NODAL (LOT 1) - [N26000107]BSNL,MAHARASHTRA	08/2017	159.30 -	04/2018 08/2018	08/2018	0/0
988	MAHARASHTRA CORE (LOT1) - [N26000108]BSNL,MAHARASHTRA	08/2017	167.68 -	04/2018 08/2018	08/2018	0/0
989	MAHARASHTRA ACESS (LOT 1) - [N26000109]BSNL,MAHARASHTRA	08/2017	212.70 -	05/2018 08/2018	08/2018	0/0
990	GUJARAT ACCESS (LOT 1) - [N26000111]BSNL,GUJARAT	09/2017	171.54 -	05/2018 08/2018	08/2018	0/0
991	UP (EAST) ACCESS LOT1 - [N26000112]BSNL,UTTAR PRADESH	11/2017	169.45 -	08/2018 08/2018	08/2018	0/0
992	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 -	05/2018 10/2018	10/2018	0/0
993	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 -	10/2018 10/2018	10/2018	0/0
	<u>Department Of Telecommunication</u>					
994	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	07/2015 05/2020	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
995	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Bangalore Metro Rail Corporation Limited</u>					
996	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
997	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	07/2018	0/0
998	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	09/2016 03/2018	09/2018	0/0
999	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
1000	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	07/2019	0/0
1001	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1002	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0
1003	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (July 2018)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1004	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1005	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 -	06/2020	0/0
1006	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 09/2020	09/2020	0/0
1007	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	-	0/0
1008	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 -	- -	-	0/0
1009	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 -	- -	-	0/0
1010	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
	<u>Chennai Metro Rail Ltd</u>					
1011	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-	0/0
	<u>Delhi Metro Rail Corporation Ltd</u>					
1012	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1013	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1014	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1015	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1016	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	-	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1017	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1018	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	Total		11,06,398.56 -			0/0
	Grand Total		11,06,398.56			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
1	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271	7/2015	2,881.40 -	2,881.40	467.97	12/2019 12/2020	12/2019
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281	9/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194	1/2015	2,321.00 -	2,321.00	354.43	12/2020 -	08/2020
4	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH - [N16000216	1/2016	247.52 -	247.52	130.75	02/2019 -	12/2018
5	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302	8/2017	384.58 -	384.58	22.24	04/2021 -	04/2020
6	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP - [N16000226	2/2016	356.00 -	356.00	159.71	05/2019 -	12/2018
7	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252	5/2016	664.00 -	664.00	315.56	12/2020 -	02/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
8	GAMJI REDEVELOPMENT PROJECT - [N16000202	5/2015	1,671.22 567.22	567.22	443.27	11/2019 12/2018	07/2018
	Total		12,724.72 -	11,620.72	2,088.90		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
9	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1) - [N18000195	5/2015	780.33 -	780.33	478.41	10/2018 -	09/2018
	Total		780.33 -	780.33	478.41		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
10	GARHWA ROAD-RAMNA - [N22000465	3/2015	348.23	348.23	76.53	03/2021 -	12/2020
	<u>North Eastern Railway</u>						
11	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347	3/2015	1,750.00 -	1,295.42	69.56	03/2022 -	02/2019
	<u>North Western Railway</u>						

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
12	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137 <u>Rail Vikas Nigam Ltd.</u>	4/2012	246.08 -	348.55	100.17	12/2019 -	06/2019
13	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	4/2011	4,295.30 -	16,216.00	877.71	12/2026 -	03/2026
14	DIGHI PORT NEW LINE - [N22000408	4/2015	723.78 -	723.78	0.22	12/2025 -	03/2025
	Total		7,363.39 -	18,931.98	1,124.19		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
15	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660	3/2017	296.19 -	254.00	86.42	03/2020 -	05/2019
16	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	3/2017	165.50 -	172.16	10.57	03/2020 -	06/2019
	Total		461.69 -	426.16	96.99		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
17	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112	9/2017	150.29 -	150.29	3.60	03/2020 06/2020	03/2020
	Total		150.29 -	150.29	3.60		
	Grand Total		21,480.42	31,909.48	3,792.09		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	4.57	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	223.12	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	294.63	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	42.29	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
5	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	689.20	03/2026 -	03/2026
6	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	397.45	03/2021 -	03/2021
	<u>Neyveli Lignite Corporation</u>						
7	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	388.25	06/2015 09/2019	09/2019
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	5,547.98	12/2015 12/2018	12/2018
9	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	10.45	09/2019 -	09/2019
10	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	2,649.27	11/2021 -	11/2021
11	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	176.76	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
12	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	167.20	03/2021 -	03/2021
13	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	-	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	477.74	03/2012 03/2023	03/2023
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	437.51	353.61	03/2015 03/2021	03/2021
16	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]	3/2017	413.84 -	413.84	-	03/2019 -	03/2019
17	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	415.37	160.45	03/2016 03/2019	03/2019
19	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	204.26	06/2015 03/2019	03/2019
20	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	1.31	03/2015 03/2021	03/2021
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	154.52	03/2015 03/2019	03/2019
22	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	5/2015	397.09 -	442.42	79.96	03/2019 03/2019	03/2019
23	KISTARAM OCP - [N06000089]	11/2010	242.29 -	164.04	12.69	03/2015 03/2021	03/2021
24	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	186.91	03/2012 03/2024	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
25	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	9/2008	152.43 -	459.49	164.90	03/2015 03/2020	03/2020
26	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	95.48	03/2023 03/2021	03/2021
27	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	1.89	03/2023 -	03/2023
28	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
29	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.67	03/2021 -	03/2021
31	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,825.99	03/2023 -	03/2023
32	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	1,863.01	03/2023 -	03/2023
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.74	03/2023 -	03/2023
34	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	53.98	03/2020 -	03/2020
35	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
36	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	41.16	03/2021 -	03/2021
37	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	114.49	03/2021 -	03/2021
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
39	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	54.19	03/2020 -	03/2020
40	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	51.45	03/2022 -	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
41	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.11	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
42	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	277.65	18.78	03/2021 -	03/2021
43	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	81.65	03/2021 -	03/2021
44	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	257.09	03/2020 -	03/2020
45	BHATADI EXPANSION OC MINE - [N06000150]	2/2016	304.52 -	304.52	128.39	03/2019 -	03/2019
46	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	2/2016	198.68 -	198.68	234.72	03/2019 -	03/2019
47	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	178.90	03/2020 -	03/2020
48	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	288.90	-	03/2023 -	03/2023
49	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	236.21	03/2025 -	03/2025
50	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	100.50	03/2020 -	03/2020
51	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	143.07	03/2021 -	03/2021
52	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	387.44	03/2020 -	03/2020
53	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	52.83	03/2020 -	03/2020
54	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	88.10	03/2021 -	03/2021
55	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	16.00	03/2022 -	03/2022
56	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
57	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	15.56	03/2022 -	03/2022
58	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	295.56	89.32	03/2019 -	03/2019
	Total		76,528.55 -	75,503.93	19,774.24		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
59	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	49.95	08/2020 -	08/2020
	Total		285.95 -	291.29	49.95		

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
60	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014	1/2018	215.92 -	215.92	17.35	11/2019 -	11/2019
61	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015	1/2018	218.83 -	218.83	17.76	11/2019 -	11/2019
62	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016	1/2018	239.81 -	239.81	19.79	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
63	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	112.27	11/2016 04/2019	04/2019
64	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018	4/2018	426.72 -	426.72	18.14	04/2020 -	04/2020
	Total		1,299.07 -	1,310.72	185.31		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
65	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
66	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
67	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
	<u>Hospital Services Consultancy Corporation</u>						
68	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017	8/2017	272.19 -	272.54	76.88	03/2019 -	03/2019
	<u>Hospital Services Consultancy Corporation Ltd</u>						
69	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014	7/2016	312.99 -	322.00	469.00	08/2018 -	08/2018
70	CNCI KOLKATA WEST BENGAL - [N21000015	8/2016	244.00 -	244.00	214.62	09/2018 -	09/2018
71	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016	8/2017	274.19 -	272.54	122.66	03/2019 -	03/2019
72	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018	8/2017	355.15 -	355.15	71.50	03/2019 -	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		3,821.52 -	3,829.23	1,440.01		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
73	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	94.71	04/2021 04/2021	04/2021
74	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 11/2020	11/2020
75	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
76	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	299.64	01/2020 01/2020	01/2020
	Total		6,912.00 -	6,912.00	426.27		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
77	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	431.49	10/2018 12/2018	12/2018
78	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
79	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	43.55	08/2020 -	08/2020
80	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	78.88	02/2020 -	02/2020
81	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	107.14	12/2019 -	12/2019
82	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY - [N16000262]	5/2015	193.40 -	193.40	76.81	01/2019 -	01/2019
83	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY - [N16000264]	5/2015	337.06 -	337.06	157.18	08/2018 -	08/2018
84	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,313.00	203.89	02/2020 -	02/2020
85	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	1,938.81	08/2018 05/2019	05/2019
	<u>Chennai Petroleum Corporation Limited</u>						
86	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	351.69	12/2019 -	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
87	RE-LIQUIFIED NATURAL GAS - [N16000301 <u>Gas Authority Of India Limited</u>	8/2017	421.00 -	421.00	1.31	08/2020 -	08/2020
88	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072	3/2015	3,957.00 -	3,397.00	2,104.60	12/2018 -	12/2018
89	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	2/2015	749.00 -	749.00	660.88	02/2020 -	02/2020
90	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289	7/2017	243.53 -	243.53	27.09	07/2022 -	07/2022
91	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288	4/2017	287.49 -	287.49	84.64	04/2022 -	04/2022
92	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285	6/2009	2,915.00 2,915.00	2,915.00	1,856.19	12/2012 02/2019	02/2019
93	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275	3/2017	1,740.00 -	1,740.00	18.21	12/2020 -	12/2020
94	BOKARO-ANGUL PIPELINE PROJECT - [N16000274	3/2017	3,437.00 -	3,437.00	177.17	12/2020 -	12/2020
95	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273	3/2017	2,433.00 -	2,433.00	152.80	12/2020 -	12/2020
96	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272	3/2017	1,933.00 -	1,933.00	421.08	12/2020 -	12/2020
97	AURAIYA PHULPUR PIPELINE PROJECT - [N16000231	7/2015	1,427.94 -	750.00	558.94	12/2018 -	12/2018
98	BARAUNI-GUWAHATI PIPELINE - [N16000334	6/2018	3,308.00 -	3,308.00	-	12/2021 -	12/2021
99	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330	10/2017	221.45 -	221.45	12.16	10/2022 -	10/2022
100	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329	10/2017	226.45 -	226.45	16.32	10/2022 -	10/2022
101	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328	7/2017	181.20 -	181.20	13.66	07/2022 -	07/2022
102	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327	10/2017	359.25 -	359.25	30.45	10/2022 -	10/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
103	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155	12/2009	309.81 -	723.40	536.27	10/2014 02/2019	02/2019
104	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237	9/2016	407.00 -	407.00	138.28	09/2019 -	09/2019
105	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA) - [N16000242	11/2016	230.00 -	230.00	80.53	02/2019 -	02/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	24.62	03/2021 -	03/2021
107	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	1.02	11/2020 -	11/2020
108	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	15.86	06/2020 -	06/2020
109	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	56.00	06/2020 -	06/2020
110	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
111	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	750.43	06/2020 -	06/2020
112	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	540.49	07/2020 -	07/2020
	Indian Oil Corporation Limited						
113	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
114	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	2,061.99	09/2017 12/2018	12/2018
115	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	78.63	06/2020 -	06/2020
116	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	4,497.00	253.96	12/2018 -	12/2018
117	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	5.73	12/2020 -	12/2020
118	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]	2/2016	151.00 -	151.00	71.22	09/2019 -	09/2019
119	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	456.52	08/2021 -	08/2021
120	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]	7/2015	822.66 -	822.66	640.72	11/2018 -	11/2018
121	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	917.79	11/2019 -	11/2019
122	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	423.00	122.85	08/2019 -	08/2019
123	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	.90	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,712.00	-	09/2022 -	09/2022
125	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	12.74	02/2020 -	02/2020
126	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	493.66	09/2019 -	09/2019
127	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	-	10/2020 -	10/2020
128	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	-	08/2020 -	08/2020
129	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	536.51	09/2019 -	09/2019
130	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	.12	02/2020 -	02/2020
131	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	179.85	09/2019 -	09/2019
132	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
133	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	875.63	09/2019 -	09/2019
134	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY - [N16000309]	8/2017	1,342.00 -	1,342.00	3.08	08/2020 -	08/2020
135	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	2.12	12/2021 -	12/2021
136	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	137.03	09/2019 -	09/2019
137	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]	12/2017	466.43 -	466.43	1.18	10/2020 -	10/2020
138	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	8/2017	236.00 -	236.00	-	06/2020 -	06/2020
139	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]	8/2017	318.80 -	318.80	-	08/2021 -	08/2021
140	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	163.02	31.03	04/2020 -	04/2020
141	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]	10/2014	279.00 -	279.00	200.05	08/2018 -	08/2018
142	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	.28	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
143	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	54.11	07/2020 -	07/2020
144	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	32.91	12/2019 -	12/2019
145	SITARGANJ LPG PROJECT - [N16000282]	2/2017	160.10 -	160.10	24.22	02/2020 -	02/2020
146	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]	5/2016	429.00 -	429.00	197.48	01/2019 -	01/2019
147	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	.05	01/2021 -	01/2021
148	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
149	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
150	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	5/2016	348.00 -	348.00	.05	01/2021 -	01/2021
151	ADDITIONAL FACILITIES AT MANMAD FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]	5/2016	212.00 -	212.00	.08	01/2021 -	01/2021
152	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	143.47	07/2018 10/2020	10/2020
153	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	437.05	10/2019 -	10/2019
154	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	1,823.00	279.79	12/2020 -	12/2020
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
155	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
156	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	111.05	03/2019 -	03/2019
157	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
158	BSVI UPGRADATION - [N16000257]	9/2016	1,810.00 1,810.00	1,810.00	130.79	12/2019 -	12/2019
	<u>Oil & Natural Gas Corporation Limited</u>						
159	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	2,099.23	03/2013 03/2019	03/2019
160	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,511.38	04/2019 03/2019	03/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
161	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	3,986.30	05/2019 10/2019	10/2019
162	PIPELINE REPLACEMENT PROJECT -4 - [N16000203]	2/2015	2,899.93 -	2,504.61	1,832.82	05/2017 12/2018	12/2018
163	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	31.35	01/2014 11/2019	11/2019
164	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	47.18	11/2019 11/2019	11/2019
165	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	255.08	05/2019 05/2019	05/2019
166	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	207.80	11.24	09/2018 02/2019	02/2019
167	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	249.44	03/2026 03/2026	03/2026
168	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	35.56	05/2020 05/2020	05/2020
169	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	870.29	06/2020 08/2021	08/2021
170	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	44.07	03/2023 03/2022	03/2022
171	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,172.39	04/2018 05/2019	05/2019
172	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	3,878.77	12/2017 03/2019	03/2019
173	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	-	12/2019 -	12/2019
174	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	396.86	05/2021 05/2021	05/2021
175	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	185.84	11/2019 11/2019	11/2019
176	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	33.34	11/2019 11/2019	11/2019
177	NAWAGAM-KOYALI PIPELINE PROJECT - [N16000211]	11/2014	195.63 -	187.10	168.13	09/2018 09/2018	09/2018
178	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	1,256.72	1,195.29	05/2013 12/2018	12/2018
179	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	1,429.33	03/2019 05/2020	05/2020
	<u>Oil India Limited</u>						
180	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	12.73	10/2020 -	10/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
181	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	17.97	12/2019 -	12/2019
182	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	543.91	1.65	02/2020 -	02/2020
	Total		1,84,718.33 -	1,83,674.19	43,849.22		
	POWER						
	National Thermal Power Corporation						
183	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	9,449.14	09/2017 06/2019	06/2019
184	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	7,879.74	08/2018 06/2019	06/2019
185	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	14,762.17	01/2011 04/2021	04/2021
186	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,195.00	11/2019 -	11/2019
187	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	2,201.67	07/2020 10/2020	10/2020
188	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	9,989.31	06/2017 06/2019	06/2019
189	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	5,651.48	09/2019 -	09/2019
190	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	8,774.15	11/2016 03/2019	03/2019
191	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	349.94	09/2019 02/2022	02/2022
192	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	7,300.02	02/2019 10/2020	10/2020
193	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,611.12	03/2013 12/2020	12/2020
194	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	4,820.27	03/2019 09/2019	09/2019
	Power Grid Corporation Of India Limited						
195	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	664.31	09/2010 12/2018	12/2018
196	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPS AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	2.35	06/2019 -	06/2019
197	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	157.04	02/2020 -	02/2020
198	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 -	445.89	166.83	02/2019 -	02/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
199	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	41.36	07/2019 -	07/2019
200	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	383.00	07/2020 -	07/2020
201	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]	12/2015	3,654.00 -	3,654.00	2,141.00	04/2019 -	04/2019
202	EASTERN REGION STRENGTHENING SCHEME XVII (PART B) - [N18000244]	2/2017	235.53 -	235.53	14.29	06/2019 -	06/2019
203	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA - [N18000243]	3/2017	162.31 -	162.31	20.90	03/2019 -	03/2019
204	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	88.86	02/2019 -	02/2019
205	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	52.81	02/2020 -	02/2020
206	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]	10/2016	608.24 -	608.24	301.40	04/2019 -	04/2019
207	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	123.13	01/2019 -	01/2019
208	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	24.85	11/2019 -	11/2019
209	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	22.13	06/2019 -	06/2019
210	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]	4/2016	844.64 -	844.64	274.50	04/2019 -	04/2019
211	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	6.80	06/2019 -	06/2019
212	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	438.09	04/2020 -	04/2020
213	WESTERN REGION STRENGTHENING SCHEME XVII - [N18000246]	2/2017	204.12 -	204.12	74.37	09/2019 -	09/2019
214	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	21.24	12/2019 -	12/2019
215	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	485.35	06/2019 -	06/2019
216	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I - [N18000220]	4/2016	810.48 -	810.48	512.21	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
217	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	2,724.41	11/2019 -	11/2019
218	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218	5/2016	3,519.59 -	3,519.59	1,680.63	05/2019 -	05/2019
219	EASTERN REGION STRENGTHENING SCHEME XI - [N18000217	5/2016	766.21 -	766.21	303.68	11/2018 -	11/2018
220	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213	3/2016	808.63 -	808.63	316.47	01/2018 03/2019	03/2019
221	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW) - [N18000206	1/2016	305.04 -	305.04	199.28	03/2017 09/2018	09/2018
222	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B - [N18000201	7/2015	307.18 -	307.18	203.36	11/2017 10/2018	10/2018
223	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268	11/2017	358.83 -	358.83	-	05/2020 -	05/2020
224	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267	9/2017	198.49 -	198.49	.18	09/2019 -	09/2019
225	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233	9/2016	562.25 -	562.25	24.20	03/2019 -	03/2019
226	PROVISION OF SERIES REACTORS IN NORTHERN REGION - [N18000232	8/2016	177.52 -	177.52	74.98	02/2019 -	02/2019
227	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION - [N18000231	8/2016	431.89 -	431.89	154.46	02/2019 -	02/2019
228	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN - [N18000230	7/2016	333.17 -	333.17	245.93	03/2019 -	03/2019
229	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B) - [N18000228	7/2016	300.94 -	300.94	177.77	12/2018 -	12/2018
230	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227	7/2016	1,429.38 -	1,429.38	623.84	01/2019 -	01/2019
231	EASTERN REGION STRENGTHENING SCHEME XIV - [N18000224	5/2016	167.01 -	167.01	90.13	11/2018 -	11/2018
232	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188	3/2015	1,394.52 -	1,394.52	173.34	05/2017 06/2019	06/2019
233	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185	3/2015	1,071.24 -	1,071.24	611.76	09/2017 09/2018	09/2018
234	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100	7/2010	1,272.80 -	1,731.10	1,456.53	11/2012 09/2018	09/2018
235	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182	1/2015	203.28 -	260.03	180.99	07/2017 06/2019	06/2019
236	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181	1/2015	871.62 -	871.62	269.23	10/2017 09/2019	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
237	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	340.88	222.24	03/2018 09/2018	09/2018
238	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	225.28	146.48	02/2016 09/2018	09/2018
239	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	2,543.37	03/2018 03/2019	03/2019
240	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	534.02	418.03	08/2014 09/2018	09/2018
241	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	493.77	06/2014 12/2018	12/2018
242	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]	9/2011	1,940.13 -	2,702.65	2,492.04	09/2014 09/2018	09/2018
243	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	206.42	145.07	03/2016 09/2018	09/2018
244	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	550.18	423.38	11/2016 06/2019	06/2019
245	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,200.95	04/2016 12/2018	12/2018
246	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	13,762.80	12,705.71	08/2013 03/2022	03/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
247	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	111.89	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
248	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	2,104.21	62.05	09/2020 -	09/2020
	Total		1,80,266.97 -	1,98,208.80	1,12,476.98		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
249	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	499.30 -	3,168.29	880.98	03/2023 -	03/2023
250	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	297.85 -	540.02	145.70	03/2022 -	03/2022
251	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	2/1997	514.68 -	2,271.50	1,600.99	03/2021 -	03/2021
252	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	199.12	214.79	03/2019 -	03/2019
253	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	912.00 -	637.95	19.30	03/2023 -	03/2023
254	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]	2/2016	854.00 -	1,035.16	13.90	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
255	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	.82	03/2023 -	03/2023
256	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	4,670.00 3,627.00	3,627.47	108.33	03/2024 -	03/2024
257	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,326.00 -	2,449.91	67.04	03/2023 -	03/2023
258	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	630.00 -	1,272.19	91.38	03/2022 -	03/2022
259	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
260	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
261	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	8,857.98	-	03/2024 -	03/2024
262	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	277.70 -	792.89	254.13	03/2021 -	03/2021
	<u>Container Corporation Of India</u>						
263	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]	10/2013	305.00 -	305.00	250.50	03/2019 -	03/2019
264	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]	12/2015	346.32 -	300.00	241.26	03/2019 -	03/2019
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
265	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
266	HAJIPUR - BACHAWARA - [N22000334]	5/2015	720.00 -	678.54	-	12/2018 -	12/2018
267	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350]	12/2015	1,491.47 -	1,491.47	-	12/2020 -	12/2020
268	KIUL - GAYA DOUBLING PROJECT - [N22000349]	12/2015	1,200.20 -	1,200.20	-	12/2020 -	12/2020
	<u>East Coast Railway</u>						
269	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	470.21 -	3,798.80	1,069.54	06/2021 -	06/2021
270	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	858.67 -	843.04	70.62	03/2021 -	03/2021
271	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	81.68	03/2021 -	03/2021
272	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
273	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	202.87	03/2021 -	03/2021
274	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	155.50	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
275	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	679.27 -	1,539.28	716.89	03/2021 -	03/2021
276	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,160.83	552.18	03/2020 -	03/2020
277	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	178.13	03/2020 -	03/2020
	<u>Eastern Railways</u>						
278	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) [N22000230]	4/2010	157.94 -	157.94	51.06	11/2018 -	11/2018
	<u>Metropolitan Rapid Transport Projects</u>						
279	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	433.38	06/2013 03/2019	03/2019
	<u>North Central Railway</u>						
280	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	524.00 668.00	668.00	-	03/2020 -	03/2020
	<u>North East Frontier Railway</u>						
281	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	4/2008	282.92 -	360.00	3.13	03/2020 -	03/2020
282	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	4/2010	221.42 -	380.00	97.41	03/2020 -	03/2020
283	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	4/2013	1,798.00 -	1,798.00	-	03/2019 -	03/2019
284	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
285	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	4,083.02 -	6,000.00	259.12	03/2021 -	03/2021
286	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	165.82 -	450.00	122.97	03/2020 -	03/2020
287	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	4/2012	246.07 -	398.93	203.30	03/2019 -	03/2019
288	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	556.31 -	612.00	14.25	03/2020 -	03/2020
289	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	871.00	148.14	03/2021 -	03/2021
290	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	178.69	03/2022 -	03/2022
291	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	4/2011	312.12 -	551.00	590.20	03/2019 -	03/2019
292	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	63.66	03/2020 -	03/2020
293	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	4/2012	283.55 -	451.00	455.01	03/2019 -	03/2019
	<u>North Eastern Railway</u>						
294	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	718.54	274.24	05/2019 -	05/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
295	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	477.31	165.93	01/2019 -	01/2019
296	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,900.00	-	01/2022 -	01/2022
297	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	268.78	96.74	08/2018 -	08/2018
298	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	3/2012	199.75 -	270.00	249.40	08/2018 -	08/2018
	<u>North Western Railway</u>						
299	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	4/2008	653.19 -	1,158.00	723.56	03/2014 03/2019	03/2019
300	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]	8/2018	808.85 -	808.85	-	08/2022 -	08/2022
301	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	349.00	234.37	02/2019 -	02/2019
302	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	4/2012	288.97 -	346.35	270.36	11/2018 -	11/2018
303	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	244.02	150.49	11/2019 -	11/2019
304	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTISURGARH-UDAIPUR - [N22000152]	4/2013	456.00 -	420.18	56.05	12/2019 -	12/2019
305	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	294.90	144.49	10/2018 -	10/2018
306	PHULERA - DIGANA DOUBLING - [N22000326]	5/2015	600.00 -	685.99	3.38	03/2020 -	03/2020
307	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	795.01	423.40	02/2019 -	02/2019
	<u>Northern Railway</u>						
308	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	3/1995	2,500.00 -	27,949.00	16,344.71	11/2002 03/2021	03/2021
	<u>National High Speed Rail Corporation Limited</u>						
309	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	557.99	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
310	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
311	BHANUPALI-BILASPUR BARI NL - [N22000273]	4/2008	1,046.88 -	7,000.00	182.77	12/2026 -	12/2026
312	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,127.00	1,041.63	03/2023 -	03/2023
313	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	567.18 -	975.62	541.05	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
314	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.65 -	1,485.85	797.18	12/2020 -	12/2020
315	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	758.09 -	758.09	782.62	03/2020 -	03/2020
316	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	960.18 -	970.00	867.19	03/2020 -	03/2020
317	VIZIANAGARAM -SAMBALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	241.54	12/2024 -	12/2024
318	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	1,514.45 -	1,750.00	1,443.07	03/2020 -	03/2020
319	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	4/2015	1,765.90 -	1,765.92	213.57	12/2025 -	12/2025
320	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	728.10 -	773.94	174.56	12/2024 -	12/2024
321	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	4/2015	750.55 -	750.56	86.24	12/2024 -	12/2024
322	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,266.89 -	1,548.66	677.61	12/2021 -	12/2021
323	DHASA-JETALSAR (GC) - [N22000141]	4/2012	376.59 -	644.38	74.67	03/2021 -	03/2021
	<u>South Central Railway</u>						
324	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,120.16	256.74	03/2021 03/2023	03/2023
325	NADIKUDE-SRI KALAHASTI - [N22000286]	4/2011	1,313.48 -	2,288.70	334.95	- 03/2022	03/2022
326	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	337.49 -	704.31	119.69	- 03/2020	03/2020
327	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	4/2006	378.56 -	1,160.47	71.23	03/2022 03/2022	03/2022
328	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	4/2012	1,054.35 -	2,200.00	222.91	- 03/2024	03/2024
329	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	4/2008	2,050.00 -	2,132.77	317.57	- 03/2023	03/2023
330	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
331	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	295.91	03/2021 -	03/2021
332	GUNTUR-GUNTAKAL - [N22000368]	4/2016	4,000.00 -	3,631.00	79.73	- 03/2023	03/2023
333	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	4/1997	218.24 236.41	645.00	707.07	03/2019 03/2019	03/2019
	<u>South East Central Railway</u>						
334	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,273.00 1,908.00	1,908.00	-	12/2021 -	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
335	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	737.72 -	737.72	104.10	12/2018 -	12/2018
	<u>South Eastern Railway</u>						
336	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	01/1999 12/2024	12/2024
337	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	01/1999 03/2030	03/2030
338	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	4/1974	393.46 154.30	662.00	182.49	03/2007 03/2025	03/2025
339	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	553.63 -	1,440.00	7.96	- 03/2024	03/2024
340	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.09	12/2021 12/2024	12/2024
341	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	4/1998	1,027.40 -	2,373.00	484.39	03/2003 03/2030	03/2030
342	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	763.18 -	1,428.00	484.48	12/2021 12/2021	12/2021
343	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	4/2012	258.20 -	365.00	167.92	- 12/2018	12/2018
344	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	4/2010	309.44 -	525.81	465.59	12/2015 11/2018	11/2018
345	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
	<u>South Western Railway</u>						
346	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	913.00 -	1,801.01	8.90	- 12/2023	12/2023
347	WHITE FIELD-KOLAR NL - [N22000280]	4/2011	341.05 -	348.85	.35	- 12/2023	12/2023
348	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
349	HUBLI-ANKOLA(NL),SWR - [220100193]	4/1997	227.00 -	2,135.00	134.15	- 12/2024	12/2024
350	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,618.00 -	1,614.59	635.98	- 03/2021	03/2021
351	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	422.93	03/2020 03/2020	03/2020
352	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	166.00	- 03/2021	03/2021
353	HUBLI- CHIKAJAJUR - [N22000325]	3/2015	1,900.00 -	1,141.00	625.25	03/2020 03/2020	03/2020
354	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	4/1996	138.00 -	1,382.78	7.90	- 03/2024	03/2024
355	TORANAGALLU-RANJITPURA DL - [N22000298]	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
356	MARIKUPPAM - KUPPAM - [N22000308]	4/2012	285.57 -	279.54	5.03	01/1999 12/2023	12/2023
357	GADAG-WADI NL - [N22000299]	4/2013	1,117.00 -	2,841.84	17.97	- 12/2024	12/2024
358	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
359	SHIMOGA-HARIHAR NL - [N22000278]	4/2011	562.74 -	832.47	.94	- 03/2024	03/2024
	<u>Southern Railway</u>						
360	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
361	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
	<u>West Central Railway</u>						
362	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	470.92 727.13	2,713.09	879.76	03/2021 -	03/2021
363	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	582.13	-	03/2020 -	03/2020
364	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
365	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,762.94 -	1,762.94	-	12/2020 -	12/2020
	Total		2,48,059.64 -	3,51,395.98	66,555.81		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
366	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]	6/2016	829.00 -	829.00	59.85	01/2019 -	01/2019
367	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]	3/2015	168.39 -	168.39	16.84	11/2018 -	11/2018
368	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]	3/2015	262.97 -	262.97	-	10/2018 -	10/2018
369	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]	3/2018	234.27 -	234.27	-	10/2018 -	10/2018
370	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]	3/2018	500.09 -	500.09	-	09/2018 -	09/2018
371	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]	3/2018	323.98 -	323.98	-	09/2018 -	09/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
372	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764	3/2018	272.89 -	272.89	-	09/2018 -	09/2018
373	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763	3/2018	215.79 -	215.79	-	09/2018 -	09/2018
374	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762	3/2018	215.12 -	215.12	-	09/2018 -	09/2018
375	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761	3/2018	282.98 -	282.98	-	09/2018 -	09/2018
376	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760	3/2018	251.97 -	251.97	-	09/2018 -	09/2018
377	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759	3/2018	237.72 -	237.72	-	09/2018 -	09/2018
378	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758	3/2018	240.64 -	240.64	-	09/2018 -	09/2018
379	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757	3/2018	315.03 -	315.03	-	09/2018 -	09/2018
380	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756	3/2018	285.68 -	285.68	-	09/2018 -	09/2018
381	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755	3/2018	239.30 -	239.30	-	09/2018 -	09/2018
382	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754	3/2018	339.57 -	339.57	-	09/2018 -	09/2018
383	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752	2/2017	387.00 -	387.00	-	09/2018 -	09/2018
384	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748	2/2018	391.00 -	391.00	-	10/2018 -	10/2018
385	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325	10/2015	179.82 -	179.82	8.99	01/2019 -	01/2019
386	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326	7/2015	197.16 -	197.16	38.50	10/2018 -	10/2018
387	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS - [N24000429	12/2015	225.02 -	159.20	-	12/2018 -	12/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
388	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438	12/2015	289.99 -	289.99	-	12/2018 -	12/2018
389	4 LANING FROM KALIABHOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323	10/2014	588.95 -	588.95	80.00	11/2018 -	11/2018
	<u>National Highways Authority Of India</u>						
390	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
391	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	-	06/2019 -	06/2019
392	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM - [N24000540	1/2016	701.12 -	701.12	841.92	05/2019 -	05/2019
393	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518	8/2015	399.54 -	399.54	-	04/2019 -	04/2019
394	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505	6/2015	1,583.79 -	1,583.79	375.53	01/2019 -	01/2019
395	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - [N24000500	1/2016	830.36 -	830.36	315.98	07/2018 -	07/2018
396	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490	3/2015	1,388.00 -	1,388.00	735.94	08/2018 -	08/2018
397	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488	12/2015	2,136.97 -	2,136.97	-	12/2018 -	12/2018
398	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480	12/2015	1,041.10 -	1,041.10	116.89	04/2019 -	04/2019
399	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471	12/2015	2,168.66 -	2,168.66	-	06/2019 -	06/2019
400	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603	8/2016	1,167.42 -	1,167.42	174.94	03/2019 -	03/2019
401	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605	8/2016	227.49 -	227.49	-	01/2019 -	01/2019
402	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	8/2016	323.72 -	323.72	37.20	08/2018 -	08/2018
403	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	167.29	04/2020 -	04/2020
404	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	1,388.34	-	09/2019 -	09/2019
405	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593	7/2016	331.46 -	331.46	-	10/2018 -	10/2018
406	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589	6/2016	649.00 -	649.00	-	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
407	FOUR LANNING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587	6/2016	763.23 -	763.23	-	06/2019 -	06/2019
408	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	-	04/2019 -	04/2019
409	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	3/2017	1,098.06 -	1,160.64	-	03/2020 -	03/2020
410	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
411	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655	3/2017	247.02 -	157.49	-	03/2020 -	03/2020
412	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	-	03/2020 -	03/2020
413	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	-	03/2020 -	03/2020
414	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	5.00	03/2020 -	03/2020
415	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	43.29	05/2019 -	05/2019
416	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	605.84	722.46	07/2018 -	07/2018
417	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630	11/2016	446.17 -	446.17	-	03/2019 -	03/2019
418	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	6/2017	1,958.88 -	1,958.88	-	06/2020 -	06/2020
419	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692	6/2017	2,485.93 -	2,485.93	-	06/2020 -	06/2020
420	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	4/2017	894.00 -	894.00	-	04/2020 -	04/2020
421	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	314.52	03/2020 -	03/2020
422	4 LANNING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670	3/2017	239.68 -	235.90	21.98	03/2020 -	03/2020
423	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667	3/2017	648.32 -	503.10	15.10	03/2020 -	03/2020
424	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666	3/2017	235.48 -	227.77	-	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
425	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
426	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664	3/2017	639.79 -	552.90	-	03/2020 -	03/2020
427	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663	3/2017	1,989.00 -	1,989.00	-	03/2020 -	03/2020
428	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	3/2017	754.54 -	756.27	-	03/2020 -	03/2020
429	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629	11/2016	400.25 -	400.25	-	03/2019 -	03/2019
430	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
431	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622	9/2016	950.69 -	950.69	237.09	08/2019 -	08/2019
432	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620	9/2016	767.03 -	767.03	123.31	08/2018 -	08/2018
433	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
434	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604	8/2016	320.30 -	320.30	170.51	01/2019 -	01/2019
435	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608	8/2016	248.97 -	248.97	-	05/2019 -	05/2019
436	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599	8/2016	2,016.00 -	2,016.00	149.36	04/2019 -	04/2019
437	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553	3/2016	229.37 -	229.37	35.17	11/2018 -	11/2018
438	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552	3/2016	701.40 -	701.40	22.02	03/2019 -	03/2019
439	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	1,587.49	70.80	04/2019 -	04/2019
440	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548	2/2016	997.15 -	997.15	329.10	03/2019 -	03/2019
441	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546	2/2016	273.20 -	273.20	-	02/2019 -	02/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
442	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]	1/2016	1,134.97 -	1,134.97	16.31	11/2018 -	11/2018
443	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	115.21	04/2019 -	04/2019
444	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]	3/2016	197.69 -	197.69	-	07/2018 -	07/2018
445	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]	3/2016	244.00 -	244.00	-	07/2018 -	07/2018
446	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	130.72	07/2019 -	07/2019
447	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	11.04	07/2019 -	07/2019
448	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]	2/2016	641.17 -	641.17	204.31	07/2018 -	07/2018
449	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	-	05/2019 -	05/2019
450	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]	12/2015	649.50 -	649.50	31.47	03/2019 -	03/2019
451	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]	1/2016	574.28 -	574.28	51.47	07/2018 -	07/2018
452	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]	7/2015	1,657.20 -	1,657.20	1,825.00	01/2019 -	01/2019
453	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]	7/2015	2,128.72 -	2,128.72	157.10	04/2019 -	04/2019
	Total		70,818.27 -	71,291.41	7,772.21		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
454	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	32.30	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
455	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]	11/2016	262.87 -	262.87	108.77	06/2019 -	06/2019
	Total		1,080.87 -	1,080.87	141.07		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
456	MAHARASHTRA NODAL (LOT 1) - [N26000107]	8/2017	159.30 -	159.30	12.40	04/2018 08/2018	08/2018

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
457	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	8/2017	215.30 -	215.30	-	05/2018 10/2018	10/2018
458	UP (EAST) ACCESS LOT1 - [N26000112]	11/2017	169.45 -	169.45	77.74	08/2018 08/2018	08/2018
459	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	1/2018	231.80 -	231.80	-	10/2018 10/2018	10/2018
460	GUJARAT ACCESS (LOT 1) - [N26000111]	9/2017	171.54 -	171.54	-	05/2018 08/2018	08/2018
461	MAHARASHTRA ACCESS (LOT 1) - [N26000109]	8/2017	212.70 -	212.70	37.08	05/2018 08/2018	08/2018
462	MAHARASHTRA CORE (LOT1) - [N26000108]	8/2017	167.68 -	167.68	30.21	04/2018 08/2018	08/2018
	<u>Department Of Telecommunication</u>						
463	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	24,664.00	8,397.00	07/2015 05/2020	05/2020
	Total		14,661.77 -	25,991.77	8,554.43		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
464	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	197.33	5.03	04/2019 -	04/2019
465	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	2/2014	388.00 -	388.00	354.09	05/2017 08/2018	08/2018
466	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	549.31	126.11	07/2019 -	07/2019
467	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	1.84	11/2019 -	11/2019
468	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	-	03/2020 -	03/2020
469	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP [N28000108]	1/2018	206.58 -	206.58	.02	03/2019 -	03/2019
470	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	1.50	06/2019 -	06/2019
471	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	-	05/2020 -	05/2020
472	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]	12/2016	246.31 -	246.31	15.95	02/2020 09/2020	09/2020
473	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB [N28000102]	8/2016	294.00 -	294.00	95.08	04/2019 06/2019	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(July 2018)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
474	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	3.72	03/2020 -	03/2020
475	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY - [N28000095]	5/2016	164.00 -	164.00	111.06	11/2018 09/2018	09/2018
476	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]	12/2015	209.00 -	209.00	26.00	10/2019 -	10/2019
	<u>Chennai Metro Rail Ltd</u>						
477	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	2/2009	14,600.00 -	19,058.00	16,352.77	12/2015 12/2018	12/2018
	<u>Lucknow Metro Rail Corporation Limited</u>						
478	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]	1/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019
	<u>National Building Construcion Corporation Ltd</u>						
479	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,336.53	11/2019 -	11/2019
	Total		29,126.55 -	33,759.78	22,966.47		
	Grand Total		8,17,579.49	9,53,249.97	2,84,191.97		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,100.00	09/2010 -	03/2019	74.69
	Total		3,492.00 -	6,100.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT [N04000050]	01/2009	309.46 -	553.53	01/2011 -	09/2018	78.87
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		624.07 -	994.86			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Northern Coal Fields Limited</u>						
5	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	259.40 -	486.57	03/2012 -	-	87.58
	Total		17,496.40 -	17,724.37			
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
6	CONSTRUCTION WORKS PHASE 4 - [N39000001]	12/2016	167.69 168.00	170.37	05/2018 -	05/2018	1.41
7	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	291.29	08/2020 -	08/2020	1.85
	Total		453.64 -	461.66			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
8	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2019	.13
9	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	03/2020	.02
	<u>Hospital Services Consultancy Corporation Ltd</u>						
10	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.38	05/2017 -	09/2018	13.31
11	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	523.00	03/2018 -	09/2018	3.45
12	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA - [N21000014]	07/2016	312.99 -	322.00	08/2018 -	08/2018	2.88
13	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,665.23 -	1,714.64			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
15	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
16	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	03/2019	17.66
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
18	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU [N16000255]	05/2015	224.00 207.00	207.25	04/2019 -	04/2019	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
19	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2019	1.77
	<u>Oil India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
20	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	03/2019	24.47
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
	Total		6,548.66 -	7,870.53			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
22	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	8,398.75	09/2009 -	12/2020	114.28
23	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
24	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	06/2019	10.55
25	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
26	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	06/2019	9.64
27	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	10/2020	5.55
28	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
29	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
30	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
31	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	06/2019	7.55
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
33	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	09/2019	12.95
	<u>North East Electric Power Corporation</u>						
34	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,078.31	07/2013 -	-	156.12
	<u>Power Grid Corporation Of India Limited</u>						
35	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	08/2014	288.49 -	376.09	02/2017 -	09/2018	30.37
36	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT - [N18000215]	01/2014	1,788.41 -	2,333.71	09/2017 -	09/2018	30.49

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
37	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
38	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,141.97	12/2018 -	12/2019	92.28
39	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,652.57	12/2018 -	12/2019	30.15
40	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]	03/2015	955.00 -	1,364.00	12/2015 -	09/2018	42.83
	<u>Satluj Jal Vidyut Nigam Limited</u>						
41	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT [N18000194]	05/2015	436.68 -	602.44	12/2016 -	12/2018	37.96
	<u>Thdc India Limited</u>						
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,789.61	06/2013 -	12/2021	52.10
43	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,401.90	02/2016 -	05/2021	165.65
	Total		1,27,142.32 -	1,68,396.45			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
44	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.97	06/1999 -	-	390.00
45	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
46	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
	<u>Container Corporation Of India</u>						
47	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
48	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	-7.17
	<u>East Central Railways</u>						
49	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	68.30
50	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	210.80
51	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
52	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	-	-	338.91
54	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	-	-	252.66
55	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	-	-	72.37
56	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
	<u>East Coast Railway</u>						
57	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	3,798.80	06/2021 -	06/2021	707.89
58	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
59	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	-	-	32.26
60	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	-	-	84.98
61	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	-	-	32.80
62	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE [N22000380]	04/2015	701.61 -	810.02	03/2021 -	03/2021	15.45
	<u>Eastern Railways</u>						
63	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,319.33	03/2019 12/2009	03/2019	10.97
64	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	973.33	12/2012 12/2012	-	60.33
65	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	365.67	-	-	.14
66	HANSDIHA-GODDA NL - [N22000236]	04/2011	267.09 -	350.78	-	-	31.33
67	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	493.96 -	681.68	-	-	38.00
68	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC [N22000245]	04/2010	423.66 -	720.59	03/2017 -	-	70.09
69	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	-	-	3.31
70	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	-	-	6.48
71	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	900.05 -	1,125.89	12/2011 12/2010	03/2020	25.09
72	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) [N22000119]	04/1999	207.52 -	334.87	12/2012 -	-	61.37

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
73	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.60	-	-	51.49
74	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	1,130.13	-	-	23.38
75	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	-	-	27.07
	<u>Metropolitan Rapid Transport Projects</u>						
76	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
77	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	03/2019	48.06
78	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	03/2019	50.68
	<u>North Central Railway</u>						
79	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
80	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
82	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	12/2022	226.98
83	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR- BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	12/2022	226.23
	<u>North East Frontier Railway</u>						
84	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	36.80 274.41	614.00	03/2019 -	03/2020	123.75
85	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,320.00	12/2010 -	-	167.76
86	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	4,600.00	04/2014 -	03/2020	642.73
87	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]	09/1997	1,500.00 -	5,820.00	04/2008 12/2011	06/2018	288.00
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	3,040.00	12/2008 -	03/2019	314.73
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	13,809.00	03/2011 -	03/2020	1,797.99
90	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	1,532.00	03/2019 -	03/2020	666.00
91	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	2,145.00	03/2019 -	03/2020	615.00

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
92	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	3,000.00	03/2015 -	03/2020	252.94
93	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	3,374.00	03/2014 -	03/2020	314.83
94	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	360.00	03/2020 -	03/2020	27.24
95	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
96	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	03/2020 -	03/2020	71.62
97	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	580.00	03/2019 -	07/2019	130.16
98	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	451.00	03/2019 -	03/2019	59.05
99	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	6,000.00	03/2021 -	03/2021	46.95
100	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
101	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	-	-	63.25
102	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	450.00	03/2020 -	03/2020	171.38
103	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	523.17 -	1,871.00	-	03/2018	257.63
104	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	551.00	03/2019 -	03/2019	76.53
105	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
106	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	871.00	03/2021 -	03/2021	.00
107	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	556.31 -	612.00	03/2020 -	03/2020	10.01
	<u>North Eastern Railway</u>						
108	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	412.05	06/2018 -	06/2018	88.85
109	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	-	-	60.34
110	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	718.54	05/2019 -	05/2019	212.37
111	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	-	-	51.31
112	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
113	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	-	358.99
114	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	268.78	08/2018 -	08/2018	10.26
115	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	474.30	-	03/2018	142.44
116	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	270.00	08/2018 -	08/2018	35.17
117	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2019	61.80
118	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16
119	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
120	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	01/2022	.16
121	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	11/2018	70.07
122	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
<u>North Western Railway</u>							
123	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	1,158.00	03/2014 -	03/2019	77.28
124	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	02/2019	93.87
125	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	03/2020	14.33
126	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	-	-	26.25
127	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	03/2020	46.55
128	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2019	41.64
129	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	2,878.97	-	-	38.23
130	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	10/2018	24.47
131	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	-	-	33.76
132	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	-	33.81
133	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	420.18	12/2019 -	12/2019	-7.86
134	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	11/2019	14.35

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
135	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]	04/2012	288.97 -	346.35	11/2018 -	11/2018	19.86
136	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	02/2019	44.16
	<u>Northern Railway</u>						
137	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
138	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
139	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	- -	-	117.77
140	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
141	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
142	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
143	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
144	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,581.53	03/2010 -	-	386.62
	<u>Rail Vikas Nigam Ltd.</u>						
145	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,844.47	03/2020 09/2009	03/2020	511.48
146	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	1,202.70	02/2015 -	12/2021	556.39
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	12/2018	85.99
148	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1997	261.70 -	388.00	02/2006 -	12/2018	48.26
149	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,850.00	03/2008 06/2008	03/2020	148.99
150	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	7,000.00	12/2026 -	12/2026	568.65
151	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	2,062.20	- -	03/2022	112.52
152	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	1,195.00	12/2012 -	03/2022	293.09
153	SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	555.00	03/2010 -	12/2019	70.82
154	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
155	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
156	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	567.18 -	975.62	12/2021 -	12/2021	72.01
157	DHASA-JETALSAR (GC) - [N22000141]	04/2012	376.59 -	644.38	03/2021 -	03/2021	71.11
158	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,266.89 -	1,548.66	12/2021 -	12/2021	22.24
159	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
160	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	- -	12/2023	9.32
161	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	750.55 -	750.56	12/2024 -	12/2024	.00
162	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	728.10 -	773.94	12/2024 -	12/2024	6.30
163	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	977.00	03/2019 -	03/2020	5.39
164	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]	04/2015	1,765.90 -	1,765.92	12/2025 -	12/2025	.00
165	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	4,295.30 -	16,216.00	12/2026 -	03/2026	277.53
166	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	1,514.45 -	1,750.00	03/2020 -	03/2020	15.55
167	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	960.18 -	970.00	03/2020 -	03/2020	1.02
168	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.65 -	1,485.85	12/2020 -	12/2020	.01
	<u>Railway Electrification</u>						
169	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
170	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	2,120.16	03/2021 -	03/2023	542.47
171	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	1,160.47	03/2022 -	03/2022	206.55
172	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,054.35 -	2,200.00	- -	03/2024	108.66
173	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
174	GUDUR-DURGARAJAPATNAM - [N22000265]	04/2011	283.54 -	761.37	- -	-	168.52
175	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
176	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	1,313.48 -	2,288.70	- -	03/2022	74.25

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
177	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,050.00 -	2,132.77	-	03/2023	4.04
178	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	966.43	02/2009 -	-	488.00
179	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	03/2019 -	03/2019	172.83
180	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	458.26	07/2008 -	-	266.61
181	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	1,025.00	- -	03/2017	723.76
<u>South East Central Railway</u>							
182	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
183	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,776.81	03/1998 -	12/2019	359.96
<u>South Eastern Railway</u>							
184	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	01/1999 -	12/2024	114.37
185	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	03/2030	53.96
186	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	662.00	03/2007 03/2007	03/2025	329.03
187	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
188	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	12/2018	153.41
189	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
190	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,440.00	- -	03/2024	160.10
191	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	981.00	- -	-	238.70
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
193	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	11/2018	69.92
194	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2018	41.36
195	TAMLUK DIGHA 88.9 KM WITH MM DESHPAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	763.18 -	1,428.00	12/2021 -	12/2021	87.11
196	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
197	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>South Western Railway</u>						
198	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	12/2023	97.26
199	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
200	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	03/2024	47.93
201	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	12/2023	2.29
202	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	12/2024	840.53
	<u>Southern Railway</u>						
203	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
204	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
205	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
206	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	2,072.50	- -	-	412.75
207	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
208	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	2,300.00	- -	-	404.39
209	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	2,815.62	- -	-	411.93
210	ATTIPPATTU PUTTUR - [N22000184]	04/2008	446.87 -	1,105.00	- -	-	147.28
211	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
212	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
213	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
214	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20
215	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
216	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
217	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
218	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	1,800.00	-	-	199.29
219	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]	02/2015	900.00 -	1,431.90	-	-	59.10
220	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
221	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
222	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
223	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
<u>West Central Railway</u>							
224	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	470.92 727.13	2,713.09	03/2021 -	03/2021	273.12
225	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
<u>Western Railway</u>							
226	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	3.07
227	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
228	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	04/2011	439.88 -	844.10	-	03/2023	91.89
	Total		1,26,737.05 -	2,92,594.96			
<u>ROAD TRANSPORT AND HIGHWAYS</u>							
<u>Dept Of Road Transport & Highways</u>							
229	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A) - [N24000262]	12/2014	201.12 201.00	201.12	02/2015 -	-	.06
<u>Ministry Of Road Transport And Highways</u>							
230	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
231	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
<u>National Highways Authority Of India</u>							
232	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	-	28.93

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
233	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	-	92.75
234	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
235	HARANGAJO TO MAIBANG, NH-54 - [N2400062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
236	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
237	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	-	42.25
238	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	-	2.29
239	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
240	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56
241	INDORE-JHABUA-GUJRAT/MP - [N24000136	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65
242	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	-	51.83
243	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	03/2020	10.58
244	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
245	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
246	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
247	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
248	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	03/2020	5.70
249	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	03/2020	.23
250	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
251	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
252	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
253	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
254	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
255	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	06/2020	41.54
256	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	05/2020	44.39
	<u>Public Works Dept Of State</u>						
257	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
258	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
259	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		22,821.30 -	29,559.57			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
260	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
261	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72
	<u>Port Trust</u>						
262	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>Hindustan Steelwork Construction Limited</u>						
263	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96
264	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Rastriya Ispat Nigam Limited</u>						
265	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	03/2019	42.39

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(July 2018)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		1,261.61	1,777.68			
			-				
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
266	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060	04/2014	332.72	342.00	09/2016	09/2018	2.79
			-		-		
267	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065	11/2012	270.83	270.83	11/2014	12/2018	.00
			-		-		
268	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21	1,592.00	10/2019	03/2020	30.58
			-		-		
269	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100	02/2016	496.18	498.99	06/2017	06/2020	.60
			496.00		-		
	<u>Chennai Metro Rail Ltd</u>						
270	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084	02/2009	14,600.00	19,058.00	12/2015	12/2018	30.53
			-		-		
	<u>National Building Construcion Corporation Ltd</u>						
271	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	06/2012	4,264.00	4,439.23	11/2019	11/2019	4.11
			-		-		
	Total		21,182.94	26,201.05			
			-				
	Grand Total		3,31,904.11	5,58,768.51			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above (July 2018)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	6,100.00	5,655.69	09/2010 09/2016	03/2019	102	30
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	12,120.00	12/2015 11/2016	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	9,520.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00 -	39,849.00	8,761.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	74,849.00	36,056.69				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	553.53	546.69	01/2011 -	09/2018	92	-
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
	Total		624.07 -	994.86	632.48				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
7	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	54	-
8	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	288.72	04/2015 -	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
9	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	99.53	03/2012 -	03/2019	84	-
10	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	155.03	03/2012 -	03/2019	84	-
11	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	350.74	03/2016 -	03/2019	36	-
12	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	84.79	03/2014 -	03/2019	60	-
13	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	93.47	03/2011 -	03/2020	108	-
14	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	706.40 -	706.40	126.89	07/2012 -	03/2021	104	-
	<u>Eastern Coal Fields Limited</u>								

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	349.57	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
16	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	581.49	03/2013 -	03/2019	72	-
17	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	263.24	03/2010 -	03/2019	108	-
18	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	344.12	03/2017 -	03/2020	36	-
19	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	242.14	03/2013 -	03/2020	84	-
20	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	65.79	03/2018 -	03/2020	24	-
21	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	233.26	03/2012 -	03/2021	108	-
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	105.89	03/2019 -	03/2021	24	-
23	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	42.95	03/2019 -	03/2021	24	-
	<u>Northern Coal Fields Limited</u>								
24	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	562.24	03/2018 -	03/2019	12	-
	<u>Singareni Colliers Company Limited</u>								
25	KOYAGUDEM OPENCASE PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	-	03/2018 -	03/2019	12	-
26	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 384.32	384.32	146.45	07/2016 -	03/2020	44	-
	<u>South-Eastern Coal Fields Limited</u>								
27	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	198.59	169.49	03/2016 -	03/2019	36	-
28	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	258.56	157.67	03/2016 -	03/2019	36	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	204.04	03/2014 -	03/2020	72	-
	<u>Western Coal Fields Limited</u>								
31	BHANEGAON OC - [N06000121]WCL, MAHARASHTRA	02/2015	187.94 409.68	409.68	91.90	03/2023 02/2017	03/2023	0	73
	Total		10,646.00 -	10,834.73	4,776.65				
	<u>STEEL</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
32	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL, RAJASTHAN	05/2015	189.00 -	189.00	-	03/2017 -	08/2018	17	-

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
33	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL, MEGHALAYA	04/2014	151.33 -	151.33	7.15	09/2017 -	12/2018	15	-
34	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL, JHARKHAND	02/2014	787.29 -	787.29	285.30	12/2016 -	12/2018	24	-
35	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL, BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>National Mineral Development Corporation (Nmdc)</u>								
36	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	14,116.06	05/2015 10/2018	12/2018	43	2
	<u>Rastrya Ispat Nigam Limited</u>								
37	ADDITIONAL WATER STORAGE RESERVOIR (KBR-II) - [N12000120]RINL, ANDHRA PRADESH	07/2015	465.85 -	465.85	170.25	07/2018 -	09/2018	2	-
38	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH	08/2015	320.66 -	320.66	63.07	08/2018 -	10/2018	2	-
39	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	502.10	09/2018 -	01/2019	4	-
40	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	237.11	10/2016 -	03/2019	29	-
41	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	935.45	12/2017 -	03/2019	15	-
	<u>Steel Authority Of India Limited (Sail)</u>								
42	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	1,607.72	12/2017 -	11/2018	11	-
43	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	471.38	10/2017 -	12/2018	14	-
44	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	5,467.78	04/2018 -	02/2019	10	-
	Total		28,594.47 -	28,381.87	24,514.58				
	<u>PETROLEUM</u>								
	<u>Chennai Petroleum Corporation Limited</u>								
45	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY - [N16000199]CPCL, TAMIL NADU	05/2015	257.87 -	257.87	226.81	11/2016 -	07/2018	20	-
	<u>Gas Authority Of India Limited</u>								
46	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL, GUJARAT	04/2016	327.78 -	200.00	95.81	04/2018 -	12/2018	8	-
	<u>Indian Oil Corporation Limited</u>								
47	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 1,330.00	1,330.00	1,291.40	06/2018 -	10/2018	4	-
48	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	10/2015	607.06 -	714.25	337.32	10/2017 -	03/2019	17	-
	<u>Oil & Natural Gas Corporation Limited</u>								

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
49	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	131.04	03/2019 -	04/2019	1	-
50	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,842.42	03/2015 03/2018	12/2019	57	21
	<u>Oil India Limited</u>								
51	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	170.50	03/2017 11/2018	03/2019	24	4
52	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
	Total		5,258.42 -	6,347.13	4,097.36				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
53	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,064.54	04/2020 -	10/2023	42	-
	<u>National Hydro-Electric Power Corporation</u>								
54	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	8,398.75	6,955.14	09/2009 -	12/2020	135	-
	<u>National Thermal Power Corporation</u>								
55	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 8,150.00	8,150.00	7,117.65	09/2011 06/2018	09/2018	84	3
56	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 09/2017	05/2019	60	20
57	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,270.00	12/2016 -	08/2019	32	-
58	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	11,425.00	01/2018 -	05/2020	28	-
	<u>North East Electric Power Corporation</u>								
59	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,179.96	6,179.96	6,604.01	12/2009 10/2018	03/2019	111	5
	<u>Power Grid Corporation Of India Limited</u>								
60	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A) - [N18000254]PGCIL,MULTI STATE	04/2015	2,525.00 -	2,525.00	1,940.00	11/2017 -	07/2018	8	-
61	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B - [N18000255]PGCIL,MAHARASHTRA	04/2015	2,225.00 2,225.00	2,225.00	1,556.00	01/2018 -	07/2018	6	-
62	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART - C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 703.10	703.10	603.15	06/2015 05/2018	08/2018	38	3
63	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION - [N18000208]PGCIL,MULTI STATE	01/2016	1,455.47 -	1,455.47	1,015.50	07/2018 -	08/2018	1	-
64	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	454.11	229.72	04/2018 -	08/2018	4	-
65	WESTERN REGION STRENGTHENING SCHEME-XVI - [N18000229]PGCIL,MULTI STATE	07/2016	150.99 -	150.99	85.46	07/2018 -	08/2018	1	-

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
66	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 2,932.88	2,932.88	2,643.53	12/2012 06/2018	09/2018	69	3
67	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 3,190.27	3,190.27	2,248.47	12/2015 06/2018	09/2018	33	3
68	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	376.09	264.15	02/2017 06/2018	09/2018	19	3
69	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	73.19	03/2018 -	09/2018	6	-
70	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT - [N18000215]PGCIL,JAMMU AND KASHMIR	01/2014	1,788.41 -	2,333.71	1,513.68	09/2017 -	09/2018	12	-
71	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A - [N18000253]PGCIL,MULTI STATE	03/2015	955.00 1,161.00	1,364.00	1,158.00	12/2015 -	09/2018	33	-
72	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	180.77	04/2016 12/2017	10/2018	30	10
73	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C - [N18000200]PGCIL,MULTI STATE	07/2015	2,247.37 -	2,247.37	1,395.18	07/2018 -	10/2018	3	-
74	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B) - [N18000221]PGCIL,MADHYA PRADESH	04/2016	287.99 -	287.99	155.62	06/2018 -	10/2018	4	-
75	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V - [N18000256]PGCIL,MADHYA PRADESH	02/2015	1,750.00 -	1,750.00	1,171.00	06/2018 -	10/2018	4	-
76	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV) - [N18000270]PGCIL,MULTI STATE	08/2008	771.00 1,642.00	1,642.00	1,429.45	02/2013 -	10/2018	68	-
77	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,041.61	11/2008 09/2018	12/2018	121	3
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	416.39	06/2016 09/2018	12/2018	30	3
79	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	2,490.86	04/2018 09/2018	12/2018	8	3
80	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,531.14	10/2012 12/2018	02/2019	76	2
81	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	175.64	44.73	09/2018 -	06/2019	9	-
82	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 -	9,141.97	823.37	12/2018 -	12/2019	12	-

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
83	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE <u>Satluj Jal Vidyut Nigam Limited</u>	12/2014	5,111.33 -	6,652.57	719.88	12/2018 -	12/2019	12	-
84	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	274.39	11/2017 -	09/2018	10	-
85	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR <u>Thdc India Limited</u>	05/2015	436.68 -	602.44	495.12	12/2016 -	12/2018	24	-
86	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	187.40	02/2014 02/2018	03/2019	61	13
87	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	4,401.90	2,597.73	02/2016 12/2020	05/2021	63	5
88	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,789.61	1,446.85	06/2013 -	12/2021	102	-
	Total		93,617.30 -	1,23,424.41	82,297.40				
	<u>HEAVY INDUSTRY</u>								
	<u>Indira Gandhi Centre For Atomic Research</u>								
89	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]JGCAR,DELHI	08/2016	1,554.00 -	1,554.00	161.86	08/2016 -	09/2019	37	-
	Total		1,554.00 -	1,554.00	161.86				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
90	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	293.65	242.20	05/2017 -	09/2018	16	-
91	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	191.38	191.38	05/2017 -	09/2018	16	-
92	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	523.00	355.00	03/2018 -	09/2018	6	-
93	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	237.80	05/2017 -	12/2018	19	-
94	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	60.45	02/2018 -	12/2018	10	-
95	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	69.24	05/2018 -	09/2019	16	-
	Total		1,689.51 -	1,729.41	1,156.07				
	<u>RAILWAYS</u>								
	<u>Container Corporation Of India</u>								
96	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	135.50	03/2019 -	08/2019	5	-

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	493.17	402.91	03/2018 -	12/2019	21	-
98	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	343.00	279.71	03/2019 -	12/2019	9	-
99	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	235.00	.39	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
100	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	.61	03/2018 -	12/2019	21	-
101	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	210.62	03/2020 -	03/2021	12	-
	<u>East Coast Railway</u>								
102	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH	04/2015	2,499.71 2,499.71	2,499.71	148.37	03/2021 -	03/2022	12	-
103	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 2,361.74	2,361.74	67.43	03/2021 -	03/2022	12	-
104	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 1,928.07	1,928.07	561.81	12/2022 -	03/2023	3	-
	<u>Eastern Railways</u>								
105	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,319.33	837.35	03/2019 12/2009	03/2019	0	111
106	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05 -	1,125.89	980.99	12/2011 12/2010	03/2020	99	111
	<u>Metropolitan Rapid Transport Projects</u>								
107	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	03/2019	60	-
108	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 1,781.98	1,781.98	1,300.41	03/2004 -	03/2020	192	-
	<u>North Central Railway</u>								
109	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	1,176.09 -	3,845.60	1.92	02/2020 -	12/2022	34	-
110	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	622.41 -	2,030.50	10.34	02/2019 -	12/2022	46	-
	<u>North East Frontier Railway</u>								
111	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 -	3,040.00	3,000.76	12/2008 -	03/2019	123	-
112	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00 -	580.00	-	03/2019 -	07/2019	4	-
113	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 274.41	614.00	266.92	03/2019 -	03/2020	12	-
114	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 -	13,809.00	7,765.91	03/2011 -	03/2020	108	-
115	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00 -	1,532.00	525.15	03/2019 -	03/2020	12	-
116	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	300.00 -	2,145.00	928.69	03/2019 -	03/2020	12	-

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
117	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 -	3,374.00	2,951.92	03/2014 -	03/2020	72	-
118	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 -	4,600.00	2,252.69	04/2014 -	03/2020	71	-
119	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
120	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	3,000.00	638.43	03/2015 -	03/2020	60	-
	<u>North Eastern Railway</u>								
121	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	1,807.88	1,792.10	04/1999 -	11/2018	235	-
122	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	-	04/2016 -	01/2022	69	-
123	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
124	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
125	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
126	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	630.24	03/2015 -	03/2020	60	-
	<u>Rail Vikas Nigam Ltd.</u>								
127	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	385.00	366.77	03/2009 03/2009	12/2018	117	117
128	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]RVNL,JHARKHAND	03/1997	261.70 -	388.00	382.21	02/2006 -	12/2018	154	-
129	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	555.00	553.72	03/2010 -	12/2019	117	-
130	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,844.47	1,270.29	03/2020 09/2009	03/2020	0	126
131	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,850.00	1,784.18	03/2008 06/2008	03/2020	144	141
132	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	977.00	921.55	03/2019 -	03/2020	12	-
133	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	546.32	03/2016 -	12/2020	57	-
134	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	942.95	874.64	03/2019 -	03/2021	24	-
135	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	858.40	12/2020 -	03/2021	3	-
136	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	1,202.70	592.80	02/2015 -	12/2021	82	-
137	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 632.00	1,195.00	607.24	12/2012 -	03/2022	111	-

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
138	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	789.79	03/2020 -	03/2022	24	-
139	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	1,801.39	03/2016 -	03/2025	108	-
140	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	760.90	03/2016 -	03/2025	108	-
141	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.16	03/2014 -	12/2025	141	-
	<u>South East Central Railway</u>								
142	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 -	1,776.81	967.96	03/1998 -	12/2019	261	-
	<u>South Eastern Railway</u>								
143	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 148.77	377.00	138.99	12/2016 08/2018	12/2018	24	4
144	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 969.83	969.83	326.40	03/2020 03/2020	06/2020	3	3
145	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	188.19	03/2021 03/2021	12/2021	9	9
	<u>South Western Railway</u>								
146	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA	03/2015	960.00 578.00	578.00	418.85	03/2020 11/2015	03/2020	0	52
	<u>Southern Railway</u>								
147	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
148	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
149	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	99.58	03/2012 -	03/2019	84	-
150	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 416.86	385.60	336.20	03/2013 -	03/2020	84	-
151	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	1,002.39	196.00	03/2021 03/2019	03/2021	0	24
152	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 2,473.40	1,030.29	932.24	03/2012 03/2019	03/2022	120	36
153	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	576.05	- 03/2019	03/2022	-	36
154	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	585.99	03/2022 03/2019	03/2022	0	36

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
155	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 1,378.12	858.96	550.66	03/2019 03/2019	03/2022	36	36
156	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	844.10	48.99	- 03/2022	03/2023	-	12
	Total		56,812.08 -	1,13,225.25	46,987.92				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
157	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH, ODISHA	06/2016	157.30 157.00	157.00	-	06/2018 -	11/2018	5	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
158	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL, NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
159	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL, NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
160	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL, NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-
161	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL, ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
162	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	3,237.87	3,176.22	09/2012 -	08/2018	71	-
163	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	673.92	01/2014 -	08/2018	55	-
164	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	268.94	11/2008 -	09/2018	118	-
165	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	245.89	08/2012 -	09/2018	73	-
166	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	898.99	03/2014 -	09/2018	54	-
167	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	411.64	01/2014 -	09/2018	56	-
168	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI, KARNATAKA	05/2015	709.00 -	709.00	346.75	09/2017 -	09/2018	12	-
169	PADI - DAHOD - [N24000353]NHAI, RAJASTHAN	11/2014	279.14 -	279.14	211.04	05/2017 -	09/2018	16	-

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
170	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	245.83	04/2009 -	10/2018	114	-
171	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	475.57	05/2010 -	10/2018	101	-
172	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	1,673.70	3,079.44	10/2011 -	10/2018	84	-
173	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,206.10	1,209.67	04/2013 -	11/2018	67	-
174	PHALODI - JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS - [N24000357]NHAI,RAJASTHAN	09/2015	567.51 -	567.51	42.79	03/2018 -	11/2018	8	-
175	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	530.07	556.02	08/2016 -	11/2018	27	-
176	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,329.31	12/2013 -	12/2018	60	-
177	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	237.00	05/2013 -	12/2018	67	-
178	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	64	-
179	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	582.52	10/2013 -	12/2018	62	-
180	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	811.54	07/2013 -	12/2018	65	-
181	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	12/2018	62	-
182	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	620.00	04/2018 -	12/2018	8	-
183	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	02/2019	30	-
184	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,566.61	07/2015 -	03/2019	44	-
185	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	437.90	06/2014 -	03/2019	57	-
186	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	425.19	274.20	09/2016 -	03/2019	30	-
187	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	454.64	11/2018 -	03/2019	4	-
188	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	03/2019	36	-
189	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,737.91	11/2016 -	04/2019	29	-
190	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	4.88	12/2017 -	04/2019	16	-

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
191	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	244.33	07/2016 -	04/2019	33	-
192	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	830.16	11/2017 -	05/2019	18	-
193	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	1,083.00	184.92	06/2018 -	05/2019	11	-
194	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,869.30	11/2011 -	06/2019	91	-
195	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,399.30	09/2016 -	06/2019	33	-
196	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	95.89	12/2017 -	06/2019	18	-
197	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	164.24	08/2018 -	06/2019	10	-
198	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	07/2019	76	-
199	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	474.40	06/2019 -	09/2019	3	-
200	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	34.61	02/2020 -	05/2020	3	-
201	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	113.04	03/2020 -	05/2020	2	-
202	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	5.37	03/2020 -	05/2020	2	-
203	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	162.19	03/2020 -	05/2020	2	-
204	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	39.97	03/2020 -	06/2020	3	-
205	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	133.93	03/2020 -	08/2020	5	-
206	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	7.34	03/2019 -	11/2020	20	-
207	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	10.00	03/2017 -	11/2020	44	-
	<u>Public Works Dept Of State</u>								

Costing Rs. 150 Crore and above

(July 2018)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.05	352.05	201.35	11/2017 08/2018	10/2018	11	2
209	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.43	348.43	231.56	09/2017 08/2018	11/2018	14	3
	Total		41,568.84 -	46,011.96	32,234.63				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
210	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	<u>Mumbai Port Trust</u>								
211	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	669.46	413.91	12/2010 -	12/2018	96	-
	Total		966.39 -	927.36	415.36				
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
212	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRLCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	2,391.46	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
213	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	620.49	12/2015 -	07/2018	31	-
214	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	342.00	316.94	09/2016 03/2018	09/2018	24	6
215	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	138.67	08/2016 -	11/2018	27	-
216	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	11/2018	44	-
217	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 210.00	270.83	159.42	11/2014 -	12/2018	49	-
218	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	58.85	10/2012 -	03/2019	77	-
219	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	67.79	04/2018 -	07/2019	15	-
220	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-

Costing Rs. 150 Crore and above

(July 2018)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
221	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	41.21	03/2016 -	12/2019	45	-
222	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	247.73	10/2019 -	03/2020	5	-
223	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	27.09	06/2017 -	06/2020	36	-
224	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	-	07/2020 09/2018	09/2020	2	24
	<u>Kochi Metro Rail Corporation Ltd</u>								
225	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	12/2019	29	-
	<u>Nagpur Metro Rail Corporation Ltd</u>								
226	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	3,669.58	03/2018 -	12/2019	21	-
	Total		44,681.03 -	45,217.65	7,791.23				
	Grand Total		3,53,132.11	4,53,497.63	2,41,122.23				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	03/2019	3492	102
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21
6	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	09/2018	309.46	92

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2019	430.45	36
8	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
9	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2019	365.01	45
10	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72
11	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
12	BAROUD OC EXPANSION (RCE)- 3MTY	SECL	04/2012	03/2016	03/2019	258.56	36
13	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	10/2018	339.88	54
14	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	NCL	06/2011	03/2018	03/2019	1131.28	12
15	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2019	510.85	36
16	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2019	457.77	72
17	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2020	321.5	72
18	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
19	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
20	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2020	479.53	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	RKP OCP PHASE-I	SCCL	03/2010	03/2015	03/2019	209.78	48
22	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2019	172.08	108
23	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
24	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
25	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	SECL	11/2009	03/2016	03/2019	198.59	36
26	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
27	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
28	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2021	479.15	24
29	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
30	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
31	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
32	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2019	426.79	12
33	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
34	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2021	706.4	104
35	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
36	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2020	163.51	108
37	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2019	179.87	84
38	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2019	264.68	84
39	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2019	162.46	60
40	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
41	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	12/2018	5907.11	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
42	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	04/2019	197.79	29

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
44	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	12/2018	152.95	10
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	03/2018	09/2018	505.58	6
46	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	12/2018	204.44	19
47	AIIMS - OPD(NEW)	HSCC	08/2014	05/2017	09/2018	293.65	16
48	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	HSCC	12/2014	05/2017	09/2018	168.9	16

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	IGCAR	08/2016	08/2016	09/2019	1554	37

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
50	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
51	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
52	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	05/2019	4588.29	9
53	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2018	327.78	8
54	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2018	861.79	67
55	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
56	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	CPCL	05/2015	11/2016	07/2018	257.87	20
57	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	12/2018	3150	15
58	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	ONGC	01/2015	12/2017	03/2019	4619.94	15
59	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2019	3190.69	13

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
60	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2019	2915	74
61	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2019	2465.15	72
62	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	03/2019	352.56	24
63	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2019	607.06	17
64	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
65	PIPELINE REPLACEMENT PROJECT -4	ONGC	02/2015	05/2017	12/2018	2899.93	19
66	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
67	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
68	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	02/2019	309.81	52

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
69	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	10/2018	771	68
70	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
71	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2019	5111.33	12
72	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	09/2018	4375.35	84
73	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	03/2019	5151.37	12
74	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	PGCIL	08/2014	02/2017	09/2018	288.49	19
75	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	09/2018	196.58	31
76	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2021	2491.58	102
77	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2019	2496.9	111
78	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	09/2018	1940.13	48
79	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	05/2021	1657	63
80	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	12/2018	487.49	54
81	SYSTEM STRENGTHENING OF SOUTHERN	PGCIL	12/2011	08/2014	09/2018	297.33	49

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	REGION - XIV						
82	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	12/2018	1779.29	121
83	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	04/2021	8692.97	123
84	SOLAPUR STPP	NTPC	03/2012	11/2016	03/2019	9395.18	28
85	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	06/2019	11846	24
86	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	08/2018	514.2	38
87	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	09/2018	2514.88	33
88	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	PGCIL	01/2016	03/2017	09/2018	305.04	18
89	EASTERN REGION STRENGTHENING SCHEME- III	PGCIL	07/2010	11/2012	09/2018	1272.8	70
90	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	09/2018	197.4	6
91	INSTALLATION OF STATCOMS IN WESTERN REGION	PGCIL	03/2015	09/2017	09/2018	1071.24	12
92	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	06/2019	1394.52	25
93	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	03/2019	195.42	61
94	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353	60
95	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	12/2018	436.68	24
96	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	PGCIL	04/2015	04/2018	12/2018	3705.61	8
97	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	PGCIL	07/2015	11/2017	10/2018	307.18	11
98	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
99	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	10/2023	8112.12	42
100	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	09/2019	9188.98	6
101	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	06/2019	12532.44	10
102	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	10/2020	14366.58	20
103	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
104	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	09/2018	268.8	6
105	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
106	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
107	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	09/2018	955	33
108	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A)	PGCIL	04/2015	11/2017	07/2018	2525	8
109	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B	PGCIL	04/2015	01/2018	07/2018	2225	6
110	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	06/2019	175.64	9
111	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	12964.6	28
112	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	08/2019	9750.89	32
113	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2020	3919.59	135
114	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	12/2018	477.69	99
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	02/2019	4824.12	76
116	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	06/2019	11638.55	21
117	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
118	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	09/2018	2144	69
119	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	12/2018	1364.52	32
120	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	10/2018	374.63	30
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	12/2018	539.82	30
122	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	06/2019	522.29	31
123	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	PGCIL	03/2014	03/2016	09/2018	155.57	30
124	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	03/2019	808.63	14
125	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	09/2018	1788.41	12
126	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	09/2018	330	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
127	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
128	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	10/2022	622.5	66
129	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
130	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	11/2018	609.04	235
131	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
132	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
133	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	03/2020	829.74	60
134	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
135	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2021	03/2022	2499.71	12
136	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2021	03/2022	2361.74	12
137	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
138	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	36
139	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
140	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	12
141	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
142	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
143	MUMBAI URBAN TRANSPORT PROJECT PHASE- II	M RTP	04/2008	03/2014	03/2019	5300	60
144	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2020	813.34	72
145	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
146	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500	220
147	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	304	111
148	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	12/2019	324.9	117
149	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
151	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
152	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
153	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	12/2011	03/2020	900.05	99
154	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
155	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	03/2019	733	123
156	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	727.56	108
157	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	03/2019	495.74	69
158	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	200	12
159	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	300	12
160	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
161	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	03/2025	393.46	216
162	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	03/2019	318.24	84
163	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2013	03/2020	394.14	84
164	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	12/2018	148.77	24
165	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
166	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	12/2022	1176.09	34
167	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	12/2022	622.41	46
168	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	11/2018	309.44	35
169	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	36.8	12
170	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2021	03/2023	330	24
171	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	183.23	82
172	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	12/2018	133.41	117

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	12/2018	261.7	154
174	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2020	619.34	71
175	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	743	144
176	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
177	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	03/2019	653.19	60
178	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	03/2022	603.04	120
179	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	12/2024	466.48	311
180	MARIKUPPAM - KUPPAM	SWR	04/2012	01/1999	12/2023	285.57	299
181	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	03/2030	276.69	374
182	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2018	12/2019	528.57	21
183	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	12/2019	493.17	21
184	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
185	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	01/2022	213	69
186	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
187	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
188	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
189	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
190	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	09/2018	709	12
191	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	NHAI	09/2014	09/2016	03/2019	425.19	30
192	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	05/2019	1387.11	18
193	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	06/2019	563.92	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
194	PADI - DAHOD	NHAI	11/2014	05/2017	09/2018	279.14	16
195	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	NHAI	09/2015	03/2018	11/2018	567.51	8
196	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	05/2019	1083	11
197	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	NHAI	06/2015	03/2016	03/2019	1012.9	36
198	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	04/2019	447.29	16
199	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
200	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	06/2019	707.82	10
201	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	09/2018	574	54
202	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	07/2019	754	76
203	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	09/2018	291.36	56
204	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	08/2016	11/2018	530.07	27
205	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	12/2018	822.9	8
206	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	02/2019	1655.01	30
207	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	10/2011	10/2018	1673.7	84
208	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	09/2018	167.64	118
209	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	10/2018	200	114
210	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108	91
211	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	09/2018	617	73
212	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	04/2019	1916.79	29
213	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.6	33
214	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	08/2018	1509.1	71
215	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	11/2018	1175	67
216	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO	NHAI	09/2011	12/2013	12/2018	1250	60

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	KM.148.3 NH-46						
217	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	12/2018	571	62
218	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	12/2018	478.51	62
219	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	04/2019	641.17	33
220	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	PWD	01/2014	09/2017	11/2018	255.75	14
221	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	PWD	01/2014	11/2017	10/2018	267.16	11
222	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	03/2019	1987	44
223	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	12/2018	374	67
224	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2018	485	64
225	JORBAT - BARAPANI	NHAI	01/2011	01/2014	08/2018	536	55
226	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2018	575	65
227	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	10/2018	486	101
228	PANVEL-INDAPUR	NHAI	12/2011	06/2014	03/2019	942.69	57
229	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
230	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
231	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29
232	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT TR	01/2007	12/2010	12/2018	366.39	96

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
233	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	03/2019	2858	15
234	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	02/2019	3127.3	10
235	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	11/2018	1154.18	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
236	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	12/2018	151.33	15
237	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	HSCL	05/2015	03/2017	08/2018	189	17
238	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
239	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	HSCL	02/2014	12/2016	12/2018	787.29	24
240	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2018	15525	43
241	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2019	343	29
242	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	12/2018	1034.01	14

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
243	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
244	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
245	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	12/2015	07/2018	884.3	31
246	2000 BOYS HOSTEL (1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	12/2019	171.86	45
247	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	11/2018	156.57	27
248	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	11/2018	216.69	44
249	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15
250	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2020	26405.14	13
251	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	08/2018	388	15
252	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	CPWD	04/2014	09/2016	09/2018	332.72	24
253	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	12/2018	270.83	49
254	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2019	165.23	77

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
255	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
256	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
257	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	12/2018	14600	36
258	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
259	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	06/2020	496.18	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6100	2608
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	AAI	01/2009	01/2011	309.46	553.53	244.07
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
6	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
7	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83
8	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
9	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	259.4	486.57	227.17

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
12	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
13	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67
14	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
15	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
16	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	06/2018	913	1330	417
17	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1256.72	394.93
19	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
21	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	IOCL	03/2014	09/2017	3076	4190	1114
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
22	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	8398.75	4479.16
23	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
24	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
25	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
26	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	13762.8	2632.61
27	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
28	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1078.31	657.3
29	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
30	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
31	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	297.33	534.02	236.69
32	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
33	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4401.9	2744.9
34	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	1940.13	2702.65	762.52
35	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
36	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6652.57	1541.24
37	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9141.97	4387.55
38	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TRANSMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL- KHALSTI-LEH PROJECT	PGCIL	01/2014	09/2017	1788.41	2333.71	545.3
40	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
41	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	PGCIL	03/2013	12/2015	2514.88	3190.27	675.39
42	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	514.2	703.1	188.9
43	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
44	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
45	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
46	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	1272.8	1731.1	458.3
47	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
48	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
49	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	8150	3774.65
50	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
51	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
52	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	2144	2932.88	788.88
53	400KV D/C TEESTA III - KISHANGANJ TRANSMISSION LINE (JV)	PGCIL	08/2008	02/2013	771	1642	871
54	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	PGCIL	03/2015	12/2015	955	1364	409
55	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6179.96	3683.06
56	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3789.61	1298.03
57	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
58	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
59	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
60	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	NFR	04/1983	03/2019	36.8	614	577.2

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	INCLUDING GAZOLE-ITAHAR(NL), NEFR						
61	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
62	KARUR-SALEM(NL), SR	SR	02/1997	N.A.	155.55	920	764.45
63	KATIHAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	492.98	1320	827.02
64	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
65	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2021	330	2120.16	1790.16
66	GOELKERA-MANOHARPUR, (LD)(SER)	RVNL	03/1997	02/2006	261.7	388	126.3
67	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	12/2022	810.78	1928.07	1117.29
68	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	385	251.59
69	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	183.23	1202.7	1019.47
70	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
71	HATHUA-BHATNI (N L) (NER)	NER	04/2005	05/2019	230.03	718.54	488.51
72	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	245.39	125.39
73	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	06/2018	218.19	412.05	193.86
74	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	470.92	2713.09	2242.17
75	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	1046.88	7000	5953.12
76	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	625	338
77	GUDUR-DURGARA JAPATNAM	SCR	04/2011	N.A.	283.54	761.37	477.83
78	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
79	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	N.A.	1054.35	2200	1145.65
80	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
81	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
82	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
84	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
85	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	5820	4320
86	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	12/2011	900.05	1125.89	225.84
87	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
88	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	514.68	2271.5	1756.82
89	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
90	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	1000	533.52
91	GADAG-WADI NL	SWR	04/2013	N.A.	1117	2841.84	1724.84
92	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
93	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
94	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	795.01	384.93
95	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
96	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
97	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	3374	2560.66
98	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	207.52	334.87	127.35
99	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
100	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	3000	2150
101	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	300	2145	1845
102	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	12/2021	1273	1908	635
103	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	1514.45	1750	235.55
104	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2026	4295.3	16216	11920.7
105	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	TRIVANDRUM-KANYAKUMARI DOUBLING	SR	02/2015	N.A.	900	1431.9	531.9
107	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
108	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	763.18	1428	664.82
109	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	03/2021	701.61	810.02	108.41
110	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
111	MATHURA-PLWAL 4TH LINE (80KM)	NCR	04/2015	03/2020	524	668	144
112	VIJAYAWADA-GUDUR	RVNL	04/2015	N.A.	3246.26	3548.67	302.41
113	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2023	854	1035.16	181.16
114	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
115	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	2326	2449.91	123.91
116	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	630	1272.19	642.19
117	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
118	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
119	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
120	PIRPAINTI-JASIDIH	ER	04/2013	N.A.	915.98	1130.13	214.15
121	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	1800	1198.57
122	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
123	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	246.07	398.93	152.86
124	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	312.12	551	238.88
125	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	523.17	1871	1347.83
126	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	165.82	450	284.18
127	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
128	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	4083.02	6000	1916.98
130	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	369.83	178.11
131	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
132	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
133	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	283.55	451	167.45
134	AGARTALA-AKHAURA NL	NFR	04/2012	03/2019	252	580	328
135	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1857	962
136	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	03/2020	221.42	380	158.58
137	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
138	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
139	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
140	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
141	ATTIPPATTU PUTTUR	SR	04/2008	N.A.	446.87	1105	658.13
142	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
143	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
144	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
145	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
146	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08
147	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
148	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	525.81	216.37
149	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	981	691.36
150	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1440	886.37
151	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
153	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	349	106.91
154	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
155	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
156	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
157	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	2878.97	796.22
158	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1266.89	1548.66	281.77
159	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
160	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	WR	04/2011	N.A.	439.88	844.1	404.22
161	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	376.59	644.38	267.79
162	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	567.18	975.62	408.44
163	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
164	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
165	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	474.3	278.66
166	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
167	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	03/2021	679.27	1539.28	860.01
168	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
169	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	609.04	1807.88	1198.84
170	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
171	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING	SR	02/2003	03/2009	199.55	330.32	130.77
172	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	WR	04/2008	03/2014	1389.62	2446.85	1057.23
173	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
174	HUBLI-ANKOLA(NL), SWR	SWR	04/1997	N.A.	227	2135	1908

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
176	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	662	268.54
177	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	03/1998	386.3	1776.81	1390.51
178	MACHERLA-NALGONDA(NL)(SCR)	SCR	07/1998	07/2008	125	458.26	333.26
179	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2019	218.24	645	426.76
180	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	550	2815.62	2265.62
181	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.97	195.96
182	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	12/1994	N.A.	124.43	1025	900.57
183	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1216	386.26
184	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33
185	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
186	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	826.57	1160.83	334.26
187	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	155.74	966.43	810.69
188	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
189	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
190	SALKA ROAD -ANUPNAGAR LINE DOUBLING	RVNL	09/2006	03/2010	324.9	555	230.1
191	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	304	1195	891
192	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1581.53	1256.53
193	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
194	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
195	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	200	1532	1332
196	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	734.01	238.27
197	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	727.56	13809	13081.44

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	06/2021	470.21	3798.8	3328.59
199	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	733	3040	2307
200	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
201	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
202	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
203	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
204	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	N.A.	337.49	704.31	366.82
205	NADIKUDE-SRI KALAHASTI	SCR	04/2011	N.A.	1313.48	2288.7	975.22
206	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
207	RAYADURGA-TUMKUR NL	RVNL	04/2007	N.A.	970.34	2062.2	1091.86
208	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
209	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
210	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
211	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	297.85	540.02	242.17
212	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	ER	04/2010	03/2017	423.66	720.59	296.93
213	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	N.A.	493.96	681.68	187.72
214	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	277.7	792.89	515.19
215	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	499.3	3168.29	2668.99
216	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1030.29	427.25
217	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	NWR	04/2008	03/2014	653.19	1158	504.81
218	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	743	1850	1107
219	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2022	378.56	1160.47	781.91
220	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
221	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	4600	3980.66
222	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
223	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	2300	1844
224	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
225	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	2072.5	1668.31
226	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
227	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1319.33	130.42
228	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	12/2012	607.09	973.33	366.24
229	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
230	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	03/2020	301.64	1844.47	1542.83

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
231	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
232	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
233	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
234	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
235	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
236	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
237	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
238	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
239	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
240	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
241	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
242	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(JULY 2018)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
243	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
244	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	09/2012	1509.1	3237.87	1728.77
245	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
246	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
247	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
248	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
249	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
250	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
251	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
252	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	CPWD	02/2011	03/2016	241.33	349.33	108
253	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OFUTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
254	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
255	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
256	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79

DOA -> Date of Approval

DOC -> date of Commissioning

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(July 2018)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2018	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	12/2018	.00	67
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	10/2018	.00	101
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	-	.00	0
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	11/2018	.00	27
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	08/2018	.00	55
11	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	12/2018	.00	62
12	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	09/2018	.00	54
13	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	12/2018	.00	65
14	DEOLI KOTA - PPP (BOT) - [N24000148]	01/2011	593.00 -	593.00	07/2013 -	-	.00	0
15	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	-	.00	0
16	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	09/2018	.00	73
17	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
18	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (July 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
19	ROHTAK-BAWAL - PPP (BOT) - [N24000169]	05/2011	650.00 -	650.00	11/2013 -	-	.00	0
20	2-LANNING WITH PS KHAGARIA-PURNEA - PPP (ANNUITY) - [N24000184]	05/2011	664.00 -	664.00	02/2014 -	-	.00	0
21	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	-	.00	0
22	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	-	.00	0
23	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	07/2019	.00	76
24	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	06/2019	.00	0
25	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	12/2018	.00	8
26	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I - PPP (BOT) - [N24000500]	01/2016	830.36 -	830.36	07/2018 -	07/2018	.00	0
27	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	-	.00	0
28	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	-	.00	0
29	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	-	.00	0
30	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	-	.00	0
31	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
32	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
33	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	-	.00	0
34	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
35	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
36	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,206.10	04/2013 -	11/2018	2.65	67
37	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	12/2018	.00	60
38	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	-	.00	0
39	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	08/2018	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (July 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
40	FOUR LANING OF KAITHAL - RAJASTHAN BORDER - PPP (BOT) - [N24000487]	07/2015	1,393.00	1,393.00	-	-	.00	0
41	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
42	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
43	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00	1,479.00	06/2015	-	.00	0
44	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
45	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	06/2019	21.90	33
46	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
47	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	01/2019	.00	0
48	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	-	.00	0
49	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
50	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	02/2019	.00	30
51	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	01/2019	.00	0
52	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	-	.00	0
53	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	10/2018	.00	84
54	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
55	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	-	.00	0
56	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
57	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	-	.00	0
58	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	04/2019	.00	29
59	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	-	.00	0
60	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	03/2019	.00	44

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (July 2018)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
61	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24 -	2,125.24	12/2015 -	-	.00	0
62	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72 -	2,128.72	04/2019 -	04/2019	.00	0
63	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,159.00	06/2015 -	-	.00	0
64	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
65	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18 -	2,288.18	05/2019 -	05/2019	.00	0
66	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
67	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	2,848.00	03/2014 -	-	.00	0
68	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	3,237.87	09/2012 -	08/2018	114.56	71
	Total		80,010.48 -	83,774.52				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
69	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88	0
	<u>Mumbai Port Trust</u>							
70	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	12/2018	82.72	96
	Total		610.89 -	945.44				
	Grand Total		80,621.37	84,719.96				

Details Of central sector Project's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.07.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	0.00 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [10/2018]	262.97 (-) [262.97]	0.00 (0.00) [0]
5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [10/2018]	391.00 (-) [391.00]	0.00 (0.00) [0]
6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [10/2018]	234.27 (-) [234.27]	0.00 (0.00) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
7	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [0/0]	601.02 (-) [601.02]	36.93 (0.00) [0]
8	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2019]	272.19 (-) [272.54]	76.88 (0.35) [0]
	<u>Petroleum</u>				
9	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
10	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2020]	384.58 (-) [384.58]	22.24 (0.00) [-12]
11	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (2/2019) [2/2019]	420.76 (207.80) [207.80]	11.24 (-212.96) [5]
12	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (8/2021) [8/2021]	34,012.00 (-) [34,012.00]	870.29 (0.00) [14]
13	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
14	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020	20,928.00	540.49

			(-) [7/2020]	(-) [20,928.00]	(0.00) [0]
15	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	138.28 (0.00) [0]
	<u>Railways</u>				
16	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
17	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
18	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	283.54 (-) [761.37]	0.52 (477.83) [0]
19	GUNTUR-GUNTAKAL	4/2016	/ (3/2023) [3/2023]	4,000.00 (-) [3,631.00]	79.73 (-369.00) [-]
20	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2021 (3/2023) [3/2023]	330.00 (-) [2,120.16]	256.74 (1,790.16) [24]
21	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2021 (-) [3/2022]	2,499.71 (2,499.71) [2,499.71]	148.37 (0.00) [12]
22	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	0.39 (0.50) [21]
23	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	385.63 (0.00) [0]
24	NADIKUDE-SRI KALAHASTI	4/2011	/ (3/2022) [3/2022]	1,313.48 (-) [2,288.70]	334.95 (975.22) [-]
25	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	155.74 (164.36) [966.43]	989.99 (810.69) [0]
26	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (6/2008) [3/2020]	743.00 (-) [1,850.00]	1,784.18 (1,107.00) [144]
27	VIJAYAWADA-GUDUR	4/2015	/ (-) [12/2023]	3,246.26 (-) [3,548.67]	83.04 (302.41) [-]
28	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	789.79 (0.00) [24]
	<u>Road Transport And Highways</u>				
29	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	0.00 (0.00) [0]
30	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
31	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [0/0]	1,585.00 (-) [1,585.00]	2,159.63 (0.00) [0]
32	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
33	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	0.00 (0.00) [0]

34	FOUR LANNING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
35	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [0/0]	648.33 (-) [648.33]	0.00 (0.00) [0]
36	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [11/2018]	1,134.97 (-) [1,134.97]	16.31 (0.00) [0]
37	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
38	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
39	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
40	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
41	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
42	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
43	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [0/0]	170.21 (-) [170.21]	5.65 (0.00) [0]
44	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]
45	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [0/0]	241.61 (-) [241.61]	7.71 (0.00) [0]
46	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	2/2015	4/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
47	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [0/0]	271.45 (-) [271.45]	0.00 (0.00) [0]
48	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [3/2020]	648.32 (-) [503.10]	15.10 (-145.22) [0]
49	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU	3/2015	9/2015 (-) [0/0]	309.01 (-) [309.01]	0.00 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [0/0]	258.99 (-) [258.99]	16.54 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	6/2014 (-) [0/0]	417.61 (-) [417.61]	0.00 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [0/0]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
54	REHABILITATION UPGRADATION OF NH-67 FROM KM	7/2014	2/2015	251.55	7.74

	641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC		(-) [0/0]	(-) [251.55]	(0.00) [0]
55	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/	1,323.15	0.00
			(-) [0/0]	(-) [1,323.15]	(0.00) [0]
56	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014	1,535.00	2,993.77
			(-) [0/0]	(-) [1,535.00]	(0.00) [0]
57	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020	1,041.62	5.37
			(-) [5/2020]	(-) [1,187.10]	(145.48) [2]
58	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013	571.00	582.52
			(-) [12/2018]	(-) [571.00]	(0.00) [62]
59	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017	1,684.00	54.13
			(-) [0/0]	(-) [1,684.00]	(0.00) [0]
	<u>Steel</u>				
60	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018	465.85	170.25
			(-) [9/2018]	(-) [465.85]	(0.00) [2]
61	CENTRAL DISPATCH YARD	8/2015	8/2018	320.66	63.07
			(-) [10/2018]	(-) [320.66]	(0.00) [2]
62	COKE OVEN BATTERY-5	12/2011	12/2017	2,858.00	935.45
			(-) [3/2019]	(-) [2,500.00]	(-358.00) [15]
63	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	1/1999	232.00	0.00
			(-) [0/0]	(-) [232.00]	(0.00) [0]
64	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	343.00	237.11
			(-) [3/2019]	(-) [488.40]	(145.40) [29]
	<u>Urban Development</u>				
65	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019	206.58	0.02
			(-) [3/2019]	(-) [206.58]	(0.00) [0]
66	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017	157.84	132.01
			(-) [0/0]	(-) [157.84]	(0.00) [0]
67	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/	246.90	0.00
			(-) [0/0]	(-) [246.90]	(0.00) [0]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
68	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019	247.52	130.75
			(-) [12/2018]	(-) [247.52]	(0.00) [-2]
	<u>Power</u>				
69	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	2,496.90	6,604.01
			(10/2018) [3/2019]	(6,179.96) [6,179.96]	(3,683.06) [111]
70	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010	6,285.33	10,234.01
			(-) [0/0]	(-) [19,496.34]	(13,211.01) [0]
	<u>Road Transport And Highways</u>				
71	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018	394.00	0.00
			(-) [0/0]	(-) [394.00]	(0.00) [0]
72	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018	235.08	47.81
			(-)	(-)	(0.00)

			[0/0]	[235.08]	[0]
73	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
74	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
75	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450)	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
76	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
77	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
78	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
79	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	38.50 (0.00) [0]
80	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
81	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
82	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]
83	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
84	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
85	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
86	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
87	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
88	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
89	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
90	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
91	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
92	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]

93	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
94	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
95	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
96	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
97	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	ASSAM				
	Health And Family Welfare				
98	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
99	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	Petroleum				
100	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (3/2019) [3/2019]	2,465.15 (-) [2,378.89]	2,099.23 (-86.26) [72]
101	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	179.85 (0.00) [0]
102	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
103	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	31.35 (127.41) [70]
104	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	122.85 (0.00) [0]
105	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
106	DIESEL HYDROTREATOR	7/2015	1/2018 (-) [0/0]	1,031.37 (-) [1,031.37]	305.91 (0.00) [0]
107	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	917.79 (0.00) [0]
108	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	35.56 (-5.15) [0]
109	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	961.00 (328.65) [0]
	Power				
110	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [9/2018]	4,375.35 (8,150.00) [8,150.00]	7,117.65 (3,774.65) [84]
	Railways				
111	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-)	312.12 (-)	590.20 (238.88)

			[3/2019]	[551.00]	[0]
112	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2022]	2,232.32 (-) [2,182.00]	178.69 (-50.32) [0]
113	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [6/2018]	1,500.00 (4,857.00) [5,820.00]	5,178.44 (4,320.00) [0]
114	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [871.00]	148.14 (0.04) [0]
115	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	203.30 (152.86) [0]
116	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	200.00 (-) [1,532.00]	525.15 (1,332.00) [12]
	<u>Road Transport And Highways</u>				
117	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
118	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
119	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]
120	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
121	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
122	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
123	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
124	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
125	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
126	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
127	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [0/0]	217.61 (-) [309.56]	389.08 (91.95) [0]
128	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [0/0]	160.00 (-) [160.00]	198.82 (0.00) [0]
129	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
130	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
131	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800	6/2015	6/2018 (-)	463.49 (-)	9.26 (0.00)

	TO KM 5		[0/0]	[463.49]	[0]
132	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
133	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
134	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
135	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
136	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
137	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [118]
138	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [114]
139	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [0/0]	208.00 (-) [208.00]	0.00 (0.00) [0]
140	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [0/0]	225.00 (-) [225.00]	312.79 (0.00) [0]
141	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [11/2017]	245.00 (-) [245.00]	214.88 (0.00) [0]
142	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
143	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>BIHAR</u>				
	<u>Petroleum</u>				
144	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	315.56 (0.00) [-10]
145	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	30.45 (0.00) [0]
146	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	0.00 (0.00) [0]
147	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [11/2018]	822.66 (-) [822.66]	640.72 (0.00) [0]
148	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	0.00 (0.00) [0]
149	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	78.63 (0.00) [0]
	<u>Power</u>				
150	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	6/2019 (-) [6/2019]	790.13 (-) [790.30]	485.35 (0.17) [0]

151	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (4/2021) [4/2021]	8,692.97 (15,095.67) [15,095.67]	14,762.17 (6,402.70) [123]
152	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (9/2017) [5/2019]	5,353.00 (-) [7,998.00]	7,128.72 (2,645.00) [60]
153	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [5/2020]	12,964.60 (-) [13,731.26]	11,425.00 (766.66) [28]
154	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [12/2018]	436.68 (-) [602.44]	495.12 (165.76) [24]
	<u>Railways</u>				
155	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	490.80 (-) [490.80]	0.39 (0.00) [0]
156	ARARIA-SUPAUL (NL)	4/2008	/ (-) [0/0]	304.41 (-) [304.41]	0.19 (0.00) [0]
157	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [0/0]	326.20 (-) [326.20]	1.68 (0.00) [0]
158	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [0/0]	285.07 (-) [378.56]	111.71 (93.49) [0]
159	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
160	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
161	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	0.00 (0.00) [0]
162	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (-) [0/0]	213.01 (-) [367.17]	13.00 (154.16) [0]
163	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (-) [0/0]	528.65 (-) [324.66]	330.82 (-203.99) [0]
164	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (-) [0/0]	501.69 (335.77) [1,043.56]	876.49 (541.87) [0]
165	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	/ (-) [0/0]	470.00 (-) [470.00]	40.00 (0.00) [0]
166	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010 (-) [0/0]	492.98 (-) [1,320.00]	926.94 (827.02) [0]
167	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [0/0]	162.87 (-) [541.00]	183.72 (378.13) [0]
168	KISHANGANJ JALALGARH, NL, NEFR	4/2008	3/2020 (-) [3/2020]	282.92 (-) [360.00]	3.13 (77.08) [0]
169	KIUL - GAYA DOUBLING PROJECT	12/2015	12/2020 (-) [12/2020]	1,200.20 (-) [1,200.20]	0.00 (0.00) [0]
170	KOSI BRIDGE (NL), ECR	4/2002	3/2012 (-) [0/0]	322.95 (-) [341.41]	640.78 (18.46) [0]

171	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-)	(-)	(0.00)
			[0/0]	[192.56]	[0]
172	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	6/2018	218.19	395.34
			(-)	(-)	(193.86)
			[6/2018]	[412.05]	[0]
173	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	332.92	495.40
			(-)	(283.95)	(144.96)
			[0/0]	[477.88]	[0]
174	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-)	(-)	(715.09)
			[0/0]	[926.09]	[0]
175	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58
			(-)	(-)	(0.00)
			[0/0]	[281.30]	[0]
176	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-)	(-)	(0.00)
			[0/0]	[228.05]	[0]
177	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014	332.15	538.21
			(-)	(-)	(227.76)
			[0/0]	[559.91]	[0]
178	NAWADA-LAXMIPUR (NL)	4/2008	/	620.57	0.00
			(-)	(-)	(0.00)
			[0/0]	[620.57]	[0]
179	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019	300.00	928.69
			(-)	(-)	(1,845.00)
			[3/2020]	[2,145.00]	[12]
180	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	12/2020	1,491.47	0.00
			(-)	(-)	(0.00)
			[12/2020]	[1,491.47]	[0]
181	SAKRI-HASANPUR ROAD (NL)	4/1999	/	175.69	253.10
			(-)	(-)	(149.31)
			[0/0]	[325.00]	[0]
182	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/	372.14	283.44
			(-)	(-)	(-16.33)
			[0/0]	[355.81]	[0]
183	SAMASTIPUR-DARBANGHA	5/2015	/	380.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[380.00]	[0]
184	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/	678.62	17.17
			(-)	(-)	(1,714.61)
			[0/0]	[2,393.23]	[0]
	<u>Road Transport And Highways</u>				
185	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013	351.54	351.23
			(-)	(-)	(0.00)
			[0/0]	[351.54]	[0]
186	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013	511.54	545.27
			(-)	(-)	(0.00)
			[0/0]	[511.54]	[0]
187	2-LANNING WITH PS KHAGARIA-PURNEA	5/2011	2/2014	664.00	654.59
			(-)	(-)	(0.00)
			[0/0]	[664.00]	[0]
188	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33
			(-)	(-)	(0.00)
			[0/0]	[375.09]	[0]
189	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013	575.00	811.54
			(-)	(-)	(0.00)
			[12/2018]	[575.00]	[65]
190	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017	581.84	77.43
			(-)	(-)	(0.00)
			[0/0]	[581.84]	[0]

191	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	0.00 (0.00) [0]
192	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
193	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [3/2020]	235.48 (-) [227.77]	0.00 (-7.71) [0]
194	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	0.00 (0.00) [0]
195	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	0.00 (0.00) [0]
196	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	0.00 (0.00) [0]
197	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
198	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/	1,167.45 (-) [1,167.45]	0.00 (0.00) [0]
199	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/	642.41 (-) [642.41]	0.00 (0.00) [0]
200	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [0/0]	322.09 (-) [322.09]	0.00 (0.00) [0]
201	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	0.00 (0.00) [0]
202	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/	814.04 (-) [814.04]	0.00 (0.00) [0]
203	FOUR LANING OF PATNA TO KOILWAR	8/2015	/	556.07 (-) [556.07]	0.00 (0.00) [0]
204	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [4/2019]	1,041.10 (-) [1,041.10]	116.89 (0.00) [0]
205	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [9/2018]	574.00 (-) [574.00]	898.99 (0.00) [54]
206	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	880.29 (0.00) [0]
207	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	0.00 (0.00) [0]
208	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/	573.70 (-) [573.70]	0.00 (0.00) [0]
209	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014 (-) [0/0]	377.64 (-) [377.64]	0.00 (0.00) [0]
210	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
211	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE	1/1991	/	478.35	0.00

	WITH PAVED SHOULDERS CONFIGURATION OF		(-) [0/0]	(-) [478.35]	(0.00) [0]
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/	319.68	0.00
			(-) [0/0]	(-) [319.68]	(0.00) [0]
213	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016	665.50	0.00
			(-) [0/0]	(-) [665.50]	(0.00) [0]
214	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016	282.41	67.52
			(-) [0/0]	(-) [282.41]	(0.00) [0]
215	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016	358.22	188.71
			(-) [0/0]	(-) [358.22]	(0.00) [0]
216	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/2013	8/2014	322.01	0.00
			(-) [0/0]	(-) [322.01]	(0.00) [0]
217	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/	675.00	0.00
			(-) [0/0]	(-) [675.00]	(0.00) [0]
218	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHI KM 40	1/1991	/	154.62	0.00
			(-) [0/0]	(-) [154.62]	(0.00) [0]
219	SIX LANNING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/	895.39	0.00
			(-) [0/0]	(-) [895.39]	(0.00) [0]
220	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017	950.64	0.00
			(-) [0/0]	(-) [950.64]	(0.00) [0]
221	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPROV	3/2015	7/2016	206.80	0.00
			(-) [0/0]	(-) [206.80]	(0.00) [0]
222	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019	399.54	0.00
			(-) [4/2019]	(-) [399.54]	(0.00) [0]
223	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/	854.80	0.00
			(-) [0/0]	(-) [854.80]	(0.00) [0]
224	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018	516.13	18.48
			(-) [0/0]	(-) [516.13]	(0.00) [0]
225	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020	672.89	0.00
			(-) [3/2020]	(-) [736.01]	(63.12) [0]
	<u>Steel</u>				
226	IRRIGATION WORK OF BAGMATI	10/2005	3/2015	956.00	651.21
			(-) [3/2021]	(-) [956.00]	(0.00) [72]
	<u>Urban Development</u>				
227	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017	496.18	27.09
			(-) [6/2020]	(496.00) [498.99]	(2.81) [36]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
228	AMERA OC RCE	2/2015	3/2018	335.97	51.76
			(-) [3/2018]	(-) [335.97]	(0.00) [0]
229	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020	316.10	53.98
			(-) [3/2020]	(-) [316.10]	(0.00) [0]
230	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016	198.59	169.49

			(-) [3/2019]	(-) [198.59]	(0.00) [36]
231	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2019]	258.56 (-) [258.56]	157.67 (0.00) [36]
232	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	54.19 (0.00) [0]
233	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	51.45 (0.00) [0]
234	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	3.74 (0.00) [0]
235	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,825.99 (0.00) [0]
236	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2020]	152.43 (459.49) [459.49]	164.90 (307.06) [60]
237	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
238	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	1,863.01 (0.00) [0]
239	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
240	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2020]	321.50 (-) [321.50]	204.04 (0.00) [72]
241	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.11 (0.00) [0]
242	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
243	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
244	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (6/2019) [6/2019]	11,846.00 (-) [12,739.82]	9,989.31 (893.82) [24]
245	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,195.00 (0.00) [0]
	<u>Railways</u>				
246	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [3/2022]	304.00 (632.00) [1,195.00]	607.24 (891.00) [111]
247	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2020]	826.57 (1,160.83) [1,160.83]	552.18 (334.26) [0]
248	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [3/2018]	207.00 (-) [207.00]	154.06 (0.00) [0]
249	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-)	758.09 (-)	782.62 (0.00)

			[3/2020]	[758.09]	[0]
250	SALKA ROAD -ANUPNAGAR LINE DOUBLING	9/2006	3/2010 (-) [12/2019]	324.90 (-) [555.00]	553.72 (230.10) [117]
	<u>Road Transport And Highways</u>				
251	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012 (-) [0/0]	169.26 (-) [169.26]	0.00 (0.00) [0]
252	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [0/0]	726.67 (-) [726.67]	0.00 (0.00) [0]
253	FOUR LANING OF ORISSA/CHATTISGARH BORDER - AURANG SECTION	2/2013	8/2015 (-) [0/0]	1,232.00 (-) [1,232.00]	1,090.17 (0.00) [0]
254	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	0.00 (0.00) [0]
255	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	0.00 (0.00) [0]
256	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015 (-) [0/0]	213.47 (-) [213.47]	0.00 (0.00) [0]
257	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (-) [0/0]	291.05 (-) [291.05]	0.00 (0.00) [0]
258	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/ (-) [0/0]	394.20 (-) [394.20]	0.00 (0.00) [0]
259	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	0.00 (0.00) [0]
260	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV	10/2014	3/2015 (-) [0/0]	298.34 (-) [298.34]	0.00 (0.00) [0]
261	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015 (-) [0/0]	262.54 (-) [262.54]	0.00 (0.00) [0]
262	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/ (-) [0/0]	422.34 (-) [422.34]	22.25 (0.00) [0]
	<u>Steel</u>				
263	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020 (-) [6/2020]	818.00 (-) [818.00]	32.30 (0.00) [0]
264	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015 (-) [0/0]	188.93 (-) [188.93]	141.50 (0.00) [0]
265	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (10/2018) [12/2018]	15,525.00 (-) [15,525.00]	14,116.06 (0.00) [43]
	<u>D & N HAVELI</u>				
	<u>Petroleum</u>				
266	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	3,986.30 (-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
267	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [12/2018]	204.44 (-) [204.44]	237.80 (0.00) [19]

268	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [9/2018]	293.65 (-) [293.65]	242.20 (0.00) [16]
269	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/	156.56	22.59
			(-) [2/2020]	(-) [156.65]	(0.09) [-]
270	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [0/0]	414.11 (-) [414.11]	141.00 (0.00) [0]
	<u>Heavy Industry</u>				
271	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	8/2016 (-) [9/2019]	1,554.00 (-) [1,554.00]	161.86 (0.00) [37]
	<u>Power</u>				
272	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [6/2019]	1,394.52 (-) [1,394.52]	173.34 (0.00) [25]
273	CREATION OF 400/220KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-B1)	5/2015	10/2018 (-) [9/2018]	780.33 (-) [780.33]	478.41 (0.00) [-1]
	<u>Railways</u>				
274	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/	295.68	1.20
			(-) [0/0]	(-) [295.68]	(0.00) [0]
275	GRADE SEPERATOR AT DAYABASTI	4/1999	/	156.65	56.10
			(-) [0/0]	(-) [197.17]	(40.52) [0]
	<u>Road Transport And Highways</u>				
276	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/	771.18	261.77
			(-) [0/0]	(-) [771.18]	(0.00) [0]
	<u>Telecommunications</u>				
277	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	172.30 (0.00) [0]
	<u>Urban Development</u>				
278	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (-) [4/2019]	197.33 (-) [197.33]	5.03 (0.00) [0]
279	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [7/2018]	884.30 (-) [884.30]	620.49 (0.00) [31]
280	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	1.84 (0.00) [0]
281	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	1.50 (0.00) [0]
282	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,270.32 (0.00) [0]
283	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	247.73 (372.79) [5]
284	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (-) [5/2020]	238.56 (-) [238.56]	0.00 (0.00) [0]
285	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,336.53 (175.23) [0]
286	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL	10/2016	/	392.00	0.00

	COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N		(-) [0/0]	(-) [392.00]	(0.00) [0]
287	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/	422.00	0.00
			(-) [0/0]	(-) [422.00]	(0.00) [0]
288	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/	2,694.00	0.00
			(-) [0/0]	(-) [2,694.00]	(0.00) [0]
289	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018	248.20	0.00
			(-) [0/0]	(-) [248.20]	(0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
290	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020	285.95	49.95
			(-) [8/2020]	(286.00) [291.29]	(5.34) [0]
291	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018	167.69	73.70
			(-) [5/2018]	(168.00) [170.37]	(2.68) [0]
	<u>Health And Family Welfare</u>				
292	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/	249.01	17.00
			(-) [3/2020]	(-) [249.07]	(0.06) [-]
	<u>Road Transport And Highways</u>				
293	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/	280.16	16.06
			(-) [0/0]	(-) [280.16]	(0.00) [0]
294	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/	184.05	10.72
			(-) [0/0]	(-) [184.05]	(0.00) [0]
295	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE	10/2015	/	936.40	0.00
			(-) [0/0]	(-) [936.40]	(0.00) [0]
296	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	16.10
			(-) [0/0]	(-) [298.33]	(0.00) [0]
297	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE	3/2015	4/2018	297.00	38.33
			(-) [0/0]	(-) [297.00]	(0.00) [0]
298	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	0.00
			(-) [0/0]	(-) [773.98]	(0.00) [0]
299	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	0.00
			(-) [0/0]	(-) [819.95]	(0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
300	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (11/2016) [6/2020]	11,459.00 (16,580.00) [16,580.00]	12,120.00 (5,121.00) [54]
	<u>Petroleum</u>				
301	ANKLESHWAR BARODA PIPELINE PROJECT	7/2014	3/2018	199.95	156.83
			(-) [3/2018]	(-) [199.95]	(0.00) [0]
302	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/	588.20	0.00
			(-) [0/0]	(-) [588.20]	(0.00) [0]
303	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019	3,380.00	875.63
			(-) [9/2019]	(-) [3,380.00]	(0.00) [0]
304	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018	327.78	95.81

			(-) [12/2018]	(-) [200.00]	(-127.78) [8]
305	CAPTIVE DHAMRA-HALDIA REFINERY NATURAL GAS PIPELINE WITH SPURLINE TO PARADIP REFINERY	8/2017	8/2020 (-) [8/2020]	1,342.00 (-) [1,342.00]	3.08 (0.00) [0]
306	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (-) [2/2020]	906.00 (-) [906.00]	12.74 (0.00) [0]
307	GAMJI REDEVELOPMENT PROJECT	5/2015	11/2019 (12/2018) [7/2018]	1,671.22 (567.22) [567.22]	443.27 (-1,104.00) [-16]
308	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	54.11 (0.00) [0]
309	NAWAGAM-KOYALI PIPELINE PROJECT	11/2014	9/2018 (9/2018) [9/2018]	195.63 (-) [187.10]	168.13 (-8.53) [0]
310	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	249.44 (0.00) [0]
311	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [8/2018]	279.00 (-) [279.00]	200.05 (0.00) [0]
	<u>Power</u>				
312	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [6/2019]	193.14 (-) [193.14]	2.35 (0.00) [0]
313	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [6/2019]	175.64 (-) [175.64]	44.73 (0.00) [9]
314	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH MUNDRA UMPP (PART-B)	7/2016	12/2018 (-) [12/2018]	300.94 (-) [300.94]	177.77 (0.00) [0]
315	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [9/2018]	330.00 (-) [330.00]	274.39 (0.00) [10]
	<u>Railways</u>				
316	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	567.18 (-) [975.62]	541.05 (408.44) [0]
317	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2013 (-) [3/2020]	394.14 (416.86) [385.60]	336.20 (-8.54) [84]
318	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
319	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2019]	318.24 (-) [321.62]	99.58 (3.38) [84]
320	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	376.59 (-) [644.38]	74.67 (267.79) [0]
321	GANDHINAGAR REDEVELOPMENT OF STATION ALOGLWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
322	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2022) [3/2023]	439.88 (-) [844.10]	48.99 (404.22) [-]
323	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	279.71 (0.00) [9]

324	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
325	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,266.89 (-) [1,548.66]	677.61 (281.77) [0]
326	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2019) [3/2022]	320.66 (1,378.12) [858.96]	550.66 (538.30) [36]
327	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (3/2019) [3/2021]	1,002.39 (-) [1,002.39]	196.00 (0.00) [0]
328	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR)	4/2008	3/2014 (3/2018) [5/2018]	1,389.62 (2,446.85) [2,446.85]	2,091.84 (1,057.23) [0]
329	VIRAMGAM-SURENDRANAGAR (DL)	4/2010	/ (-) [0/0]	279.40 (384.32) [355.00]	335.40 (75.60) [0]
330	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
<u>Road Transport And Highways</u>					
331	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	30.19 (0.00) [-]
332	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	0.00 (0.00) [0]
333	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [6/2020]	1,958.88 (-) [1,958.88]	0.00 (0.00) [0]
334	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,659.71 (0.00) [0]
335	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [0/0]	364.56 (-) [364.56]	0.00 (0.00) [0]
336	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	0.00 (0.00) [0]
337	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	0.00 (0.00) [0]
338	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	0.00 (0.00) [0]
339	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	0.00 (0.00) [0]
340	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [8/2018]	1,509.10 (-) [3,237.87]	3,176.22 (1,728.77) [71]
341	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
342	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	974.73 (0.00) [0]
343	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (-) [1,251.11]	0.00 (0.00) [0]

344	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
345	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	346.60 (0.00) [0]
	<u>Steel</u>				
346	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>Telecommunications</u>				
347	GUJARAT ACCESS (LOT 1)	9/2017	5/2018 (8/2018) [8/2018]	171.54 (-) [171.54]	0.00 (0.00) [3]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
348	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	17.35 (0.00) [0]
	<u>Health And Family Welfare</u>				
349	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2018]	505.58 (-) [523.00]	355.00 (17.42) [6]
350	NCI AIIMS JHAJJAR RESIDENTIAL HARYANA	7/2016	8/2018 (-) [8/2018]	312.99 (-) [322.00]	469.00 (9.01) [0]
	<u>Petroleum</u>				
351	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	9/2019 (-) [9/2019]	3,529.00 (-) [3,529.00]	493.66 (0.00) [0]
352	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	0.12 (0.00) [0]
353	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	1.02 (0.00) [0]
	<u>Railways</u>				
354	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/ (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
355	JIND-SONEPAT (NL),NR	1/2004	3/2012 (-) [0/0]	238.56 (-) [740.00]	722.65 (501.44) [0]
356	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2019]	346.32 (-) [300.00]	241.26 (-46.32) [0]
357	ROHTAK-MEHAM HANSI	4/2012	/ (-) [0/0]	287.00 (-) [625.00]	4.38 (338.00) [0]
	<u>Road Transport And Highways</u>				
358	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [602.95]	54.89 (0.00) [0]
359	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [7/2018]	574.28 (-) [574.28]	51.47 (0.00) [0]
360	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [3/2020]	639.79 (-) [552.90]	0.00 (-86.89) [0]
361	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-)	2,128.72 (-)	157.10 (0.00)

			[4/2019]	[2,128.72]	[0]
362	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [5/2019]	248.97 (-) [248.97]	0.00 (0.00) [0]
363	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
364	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [10/2018]	486.00 (-) [486.00]	475.57 (0.00) [101]
365	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
366	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
367	FOUR LANING OF KAITHAL - RAJASTHAN BORDER	7/2015	/ (-) [0/0]	1,393.00 (-) [1,393.00]	1,917.27 (0.00) [0]
368	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [6/2019]	1,108.00 (-) [2,288.00]	3,869.30 (1,180.00) [91]
369	ROHTAK-BAWAL	5/2011	11/2013 (-) [0/0]	650.00 (-) [650.00]	832.39 (0.00) [0]
370	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA (PKG - 1)	5/2015	5/2018 (-) [0/0]	600.85 (-) [600.85]	99.84 (0.00) [0]
371	UP/HARYANA BORDER - YAMUNA NAGAR -SAHA-BARWALA - PANCHKULA(PKG - 2)	10/2015	4/2018 (-) [0/0]	562.34 (-) [562.34]	109.07 (0.00) [0]
	<u>HIMACHAL PRADESH</u>				
	<u>Petroleum</u>				
372	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [9/2019]	151.00 (-) [151.00]	71.22 (0.00) [0]
373	CONSTRUCTION OF PIPELINE TAP OFF POINT (TOP) AT UNA, HP	2/2016	5/2019 (-) [12/2018]	356.00 (-) [356.00]	159.71 (0.00) [-5]
	<u>Power</u>				
374	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2020]	3,919.59 (-) [8,398.75]	6,955.14 (4,479.16) [135]
	<u>Railways</u>				
375	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	1,046.88 (-) [7,000.00]	182.77 (5,953.12) [0]
	<u>Road Transport And Highways</u>				
376	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [2/2019]	273.20 (-) [273.20]	0.00 (0.00) [0]
377	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [6/2020]	2,485.93 (-) [2,485.93]	0.00 (0.00) [0]
378	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,737.91 (0.00) [29]
379	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [0/0]	934.46 (-) [934.46]	104.98 (0.00) [0]
380	FOUR LANNING OF NERCHOWK-PANDOH BYPASS	9/2016	/	1,273.71	0.00

	SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH		(-) [0/0]	(-) [1,273.71]	(0.00) [0]
381	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/	447.75	0.00
			(-) [0/0]	(-) [447.75]	(0.00) [0]
382	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/	1,583.18	0.00
			(-) [9/2020]	(-) [1,583.18]	(0.00) [-]
	<u>Urban Development</u>				
383	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	270.83	159.42
			(-) [12/2018]	(210.00) [270.83]	(0.00) [49]
	<u>JAMMU AND KASHMIR</u>				
	<u>Power</u>				
384	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020	8,112.12	1,064.54
			(-) [10/2023]	(-) [8,112.12]	(0.00) [42]
385	TRANMISSION SYSTEM ASSOCIATED WITH ALUSTENG (SRINAGAR)- DRASS- KARGIL-KHALSTI-LEH PROJECT	1/2014	9/2017	1,788.41	1,513.68
			(-) [9/2018]	(-) [2,333.71]	(545.30) [12]
	<u>Railways</u>				
386	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002	2,500.00	16,344.71
			(3/2021) [3/2021]	(27,949.00) [27,949.00]	(25,449.00) [220]
	<u>Road Transport And Highways</u>				
387	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/	1,471.75	0.00
			(-) [0/0]	(-) [1,471.75]	(0.00) [0]
388	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019	2,168.66	0.00
			(-) [6/2019]	(-) [2,168.66]	(0.00) [0]
389	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018	2,136.97	0.00
			(-) [12/2018]	(-) [2,136.97]	(0.00) [0]
390	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013	1,813.76	2,393.99
			(-) [0/0]	(-) [1,813.76]	(0.00) [0]
391	NASHRI- CHANANI	5/2011	6/2015	2,159.00	3,986.82
			(-) [0/0]	(-) [2,159.00]	(0.00) [0]
392	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015	1,987.00	1,566.61
			(-) [3/2019]	(-) [1,987.00]	(0.00) [44]
393	SRINAGAR TO BANIHAL	6/2011	6/2014	1,100.70	1,216.15
			(-) [0/0]	(-) [1,100.70]	(0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
394	AMRAPALI OC(12MTY)	2/2012	3/2020	858.11	223.12
			(-) [3/2020]	(-) [858.11]	(0.00) [0]
395	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011	163.51	93.47
			(-) [3/2020]	(-) [163.51]	(0.00) [108]
396	HURA - C OC (3 MTY)	10/2015	3/2022	359.69	42.29
			(-) [3/2022]	(-) [359.69]	(0.00) [0]
397	KAPURIA UG(PSLW)	8/2011	4/2017	988.35	45.26
			(-) [0/0]	(-) [988.35]	(0.00) [0]
398	KARMA OCP (1.0MTY)	6/2009	3/2014	162.46	84.79

			(-) [3/2019]	(-) [162.46]	(0.00) [60]
399	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	179.02 (0.00) [0]
400	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2021]	706.40 (-) [706.40]	126.89 (0.00) [104]
401	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	288.72 (0.00) [48]
402	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [54]
403	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	4.57 (0.00) [0]
404	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	99.53 (0.00) [84]
405	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	176.35 (0.00) [0]
406	RAJMAHAL OC EXP.	9/2009	3/2014 (-) [0/0]	153.82 (-) [153.82]	131.07 (0.00) [0]
407	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2019]	510.85 (-) [510.85]	350.74 (0.00) [36]
408	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2019]	264.68 (-) [264.68]	155.03 (0.00) [84]
	<u>Petroleum</u>				
409	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	15.86 (0.00) [0]
410	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	12.16 (0.00) [0]
411	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	16.32 (0.00) [0]
412	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (910.23) [910.23]	44.07 (251.61) [-12]
413	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	<u>Power</u>				
414	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (10/2020) [10/2020]	14,366.58 (-) [15,164.05]	7,300.02 (797.47) [20]
415	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [12/2016]	4,237.96 (4,552.00) [4,552.00]	2,734.43 (314.04) [0]
	<u>Railways</u>				
416	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2021]	1,724.20 (1,724.20) [1,724.20]	188.19 (0.00) [9]
417	DANGO APOSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (11/2018)	309.44 (309.44)	465.59 (216.37)

			[11/2018]	[525.81]	[35]
418	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	76.53 (0.00) [-3]
419	GOELKERA-MANOHARPUR,(LD)(SER)	3/1997	2/2006 (-) [12/2018]	261.70 (-) [388.00]	382.21 (126.30) [154]
420	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
421	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	12/2011 (12/2010) [3/2020]	900.05 (-) [1,125.89]	980.99 (225.84) [99]
422	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (12/2018) [12/2018]	258.20 (258.20) [365.00]	167.92 (106.80) [-]
423	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [12/2018]	148.77 (148.77) [377.00]	138.99 (228.23) [24]
424	TINPAHAR - SAHIBGANJ (ER)	4/2008	3/2012 (-) [0/0]	167.73 (-) [167.73]	264.07 (0.00) [0]
	Road Transport And Highways				
425	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [3/2020]	239.68 (-) [235.90]	21.98 (-3.78) [0]
426	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	10.57 (6.66) [-9]
427	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [3/2019]	997.15 (-) [997.15]	329.10 (0.00) [0]
428	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
429	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [8/2018]	323.72 (-) [323.72]	37.20 (0.00) [0]
430	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	881.08 (0.00) [0]
431	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
432	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [458.03]	0.00 (0.00) [0]
	Steel				
433	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
434	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
435	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [12/2018]	787.29 (-) [787.29]	285.30 (0.00) [24]
436	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
437	EXPANSION OF GUA ORE MINES WITH BENEFICIATION	2/2014	9/2017	4,749.00	142.56

	FACILITIES AND INSTALLATION OF PELLET PLANT		(-) [0/0]	(-) [4,749.00]	(0.00) [0]
438	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [11/2018]	1,154.18 (-) [1,154.18]	1,607.72 (0.00) [11]
439	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [12/2018]	1,034.01 (-) [1,034.01]	471.38 (0.00) [14]
440	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2019]	262.87 (-) [262.87]	108.77 (0.00) [0]
	<u>Urban Development</u>				
441	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [12/2019]	171.86 (-) [171.86]	41.21 (0.00) [45]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
442	BSVI UPGRADATION	9/2016	12/2019 (-) [12/2019]	1,810.00 (1,810.00) [1,810.00]	130.79 (0.00) [0]
443	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [4/2019]	224.00 (207.00) [207.25]	99.99 (-16.75) [0]
444	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [749.00]	660.88 (0.00) [0]
445	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [3/2019]	135.00 (171.00) [170.70]	111.05 (35.70) [0]
446	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [3/2020]	581.00 (-) [581.00]	0.00 (0.00) [0]
447	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
448	KUDGI STPP STAGE 1	1/2012	1/2017 (-) [0/0]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [0]
449	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [2/2019]	445.89 (-) [445.89]	166.83 (0.00) [0]
	<u>Railways</u>				
450	ARSIKERE-TUMKUR	3/2015	3/2020 (11/2015) [3/2020]	960.00 (578.00) [578.00]	418.85 (-382.00) [0]
451	BAGALKOT-KUDACHI NL	4/2010	/ (-) [0/0]	377.93 (986.30) [986.30]	282.37 (608.37) [0]
452	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	/ (3/2024) [3/2024]	138.00 (1,382.78) [1,382.78]	7.90 (1,244.78) [-]
453	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [0/0]	327.25 (367.77) [367.77]	0.34 (40.52) [0]
454	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (12/2023) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
455	GADAG-WADI NL	4/2013	/ (12/2024) [12/2024]	1,117.00 (2,841.84) [2,841.84]	17.97 (1,724.84) [-]

456	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,127.00]	1,041.63 (0.00) [0]
457	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2020) [3/2020]	1,900.00 (1,141.00) [1,141.00]	625.25 (-759.00) [0]
458	HUBLI-ANKOLA(NL),SWR	4/1997	/ (12/2024) [12/2024]	227.00 (-) [2,135.00]	134.15 (1,908.00) [-]
459	MARIKUPPAM - KUPPAM	4/2012	1/1999 (12/2023) [12/2023]	285.57 (279.54) [279.54]	5.03 (-6.03) [299]
460	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [12/2023]	179.65 (1,350.91) [1,350.91]	873.61 (1,171.26) [-]
461	SHIMOGA-HARIHAR NL	4/2011	/ (3/2024) [3/2024]	562.74 (-) [832.47]	0.94 (269.73) [-]
462	TORANAGALLU-RANJITPURA DL	4/2011	/ (12/2023) [12/2023]	146.75 (167.50) [167.50]	0.34 (20.75) [-]
463	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (12/2023) [12/2023]	913.00 (-) [1,801.01]	8.90 (888.01) [-]
464	WHITE FIELD-KOLAR NL	4/2011	/ (12/2023) [12/2023]	341.05 (-) [348.85]	0.35 (7.80) [-]
	<u>Road Transport And Highways</u>				
465	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (-) [3/2019]	1,167.42 (-) [1,167.42]	174.94 (0.00) [0]
466	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [2/2019]	1,655.01 (-) [1,655.01]	1,515.16 (0.00) [30]
467	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/ (-) [0/0]	720.69 (-) [720.69]	99.03 (0.00) [0]
468	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [3/2019]	701.40 (-) [701.40]	22.02 (0.00) [0]
469	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	7.34 (0.00) [20]
470	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [8/2018]	1,388.00 (-) [1,388.00]	735.94 (0.00) [0]
471	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [4/2020]	1,664.20 (-) [1,664.20]	167.29 (0.00) [0]
472	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [6/2018]	946.00 (-) [946.00]	818.53 (0.00) [0]
473	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018 (-) [0/0]	219.40 (-) [219.40]	0.00 (0.00) [0]
474	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [5/2020]	993.16 (-) [1,434.00]	162.19 (440.84) [2]
475	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [6/2020]	831.58 (-) [1,177.00]	39.97 (345.42) [3]

476	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	0.00 (0.00) [0]
477	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
478	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017 (-) [9/2018]	709.00 (-) [709.00]	346.75 (0.00) [12]
479	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [8/2019]	950.69 (-) [950.69]	237.09 (0.00) [0]
	<u>Steel</u>				
480	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
481	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
	<u>Urban Development</u>				
482	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	2,391.46 (0.00) [13]
483	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (9/2020) [9/2020]	246.31 (-) [246.31]	15.95 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
484	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2019]	1,112.00 (-) [1,112.00]	108.79 (0.00) [0]
485	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT KOCHI REFINERY	5/2015	8/2018 (-) [8/2018]	337.06 (-) [337.06]	157.18 (0.00) [0]
486	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [3/2019]	607.06 (-) [714.25]	337.32 (107.19) [17]
487	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (-) [2/2020]	3,313.00 (-) [3,313.00]	203.89 (0.00) [0]
488	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (5/2019) [5/2019]	4,588.29 (5,245.96) [5,245.96]	1,938.81 (657.67) [9]
	<u>Railways</u>				
489	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	550.00 (1,566.00) [2,815.62]	255.37 (2,265.62) [0]
490	CHENGANNUR-CHINGAVANAM	4/2006	/ (-) [0/0]	191.72 (342.85) [369.83]	421.57 (178.11) [0]
491	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.70 (0.00) [0]
492	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
493	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	2/2005	3/2014 (-) [0/0]	241.00 (-) [241.00]	273.36 (0.00) [0]
494	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-)	550.00 (-)	0.00 (0.00)

			[0/0]	[550.00]	[0]
495	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	900.00	11.88
			(-)	(-)	(531.90)
			[0/0]	[1,431.90]	[0]
496	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.07
			(-)	(-)	(-171.50)
			[0/0]	[828.50]	[0]
	<u>Road Transport And Highways</u>				
497	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	47.56
			(-)	(-)	(0.00)
			[0/0]	[845.24]	[0]
498	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018	804.97	0.00
			(-)	(-)	(0.00)
			[0/0]	[804.97]	[0]
499	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,124.11]	[0]
500	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017	267.16	201.35
			(8/2018)	(352.05)	(84.89)
			[10/2018]	[352.05]	[11]
501	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	231.56
			(8/2018)	(348.43)	(92.68)
			[11/2018]	[348.43]	[14]
502	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	245.89
			(-)	(-)	(0.00)
			[9/2018]	[617.00]	[73]
	<u>Urban Development</u>				
503	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020	150.29	3.60
			(6/2020)	(-)	(0.00)
			[3/2020]	[150.29]	[0]
504	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012	165.23	58.85
			(-)	(-)	(0.00)
			[3/2019]	[165.23]	[77]
505	KOCHI METRO RAIL PROJECT	7/2012	7/2017	5,181.79	0.00
			(-)	(-)	(0.00)
			[12/2019]	[5,181.79]	[29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
506	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021	869.44	112.67
			(-)	(-)	(0.00)
			[3/2021]	[869.44]	[0]
507	AMRITDHARA OC PROJECT	2/2015	3/2023	481.60	0.00
			(-)	(-)	(0.00)
			[3/2023]	[481.60]	[0]
508	BATURA HIGHWALL PROJECT	7/2015	3/2022	231.92	0.00
			(-)	(-)	(0.00)
			[3/2022]	[231.92]	[0]
509	BATURA OCP (2.0 MTY)	8/2015	3/2023	1,186.64	95.48
			(3/2021)	(203.82)	(-982.82)
			[3/2021]	[203.82]	[-24]
510	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022	409.87	15.56
			(-)	(-)	(0.00)
			[3/2022]	[409.87]	[0]
511	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022	1,255.17	0.00
			(-)	(-)	(0.00)
			[3/2022]	[1,255.17]	[0]
512	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021	1,783.09	167.20
			(-)	(-)	(0.00)
			[3/2021]	[1,783.09]	[0]
513	KANCHAN OC EXPANSION	12/2014	3/2021	371.04	41.16
			(-)	(-)	(0.00)

			[3/2021]	[371.04]	[0]
514	MALACHUA OPENCAST PROJECT	10/2015	3/2023 (-) [3/2023]	488.33 (-) [488.33]	1.89 (0.00) [0]
515	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	3/2012 (-) [0/0]	259.40 (-) [486.57]	410.19 (227.17) [0]
516	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	114.49 (0.00) [0]
	<u>Petroleum</u>				
517	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [6/2020]	236.00 (-) [236.00]	0.00 (0.00) [0]
	<u>Power</u>				
518	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (-) [2,104.21]	62.05 (0.00) [0]
519	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (6/2019) [6/2019]	11,638.55 (-) [12,865.92]	9,449.14 (1,227.37) [21]
520	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (-) [9/2019]	9,870.51 (-) [11,148.86]	5,651.48 (1,278.35) [0]
521	S/S EXTENSION FOR TRANSMISSION SYSTEM ASSOCIATED WITH VINDHYACHAL-V PROJECT OF NTPC (PART B)	4/2016	6/2018 (-) [10/2018]	287.99 (-) [287.99]	155.62 (0.00) [4]
522	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR PARK (750 MW)	1/2016	3/2017 (9/2018) [9/2018]	305.04 (-) [305.04]	199.28 (0.00) [18]
523	TRANSMISSION SYSTEM STRENGTHENING ASSOCIATED WITH VINDHYACHAL V	2/2015	6/2018 (-) [10/2018]	1,750.00 (-) [1,750.00]	1,171.00 (0.00) [4]
	<u>Railways</u>				
524	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.65 (-) [1,485.85]	797.18 (0.20) [0]
525	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]
526	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	12/2018 (-) [12/2018]	737.72 (-) [737.72]	104.10 (0.00) [0]
527	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	12/2020 (-) [12/2020]	1,762.94 (-) [1,762.94]	0.00 (0.00) [0]
528	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2020 (-) [3/2020]	582.13 (-) [582.13]	0.00 (0.00) [0]
529	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	112.07 (0.00) [0]
530	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [8/2019]	174.00 (-) [174.00]	135.50 (0.00) [5]
531	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2021]	470.92 (727.13) [2,713.09]	879.76 (2,242.17) [0]
532	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2012 (3/2019) [3/2022]	603.04 (2,473.40) [1,030.29]	932.24 (427.25) [120]

	Road Transport And Highways				
533	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/	950.27	0.00
			(-)	(-)	(0.00)
			[0/0]	[950.27]	[0]
534	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019	227.49	0.00
			(-)	(-)	(0.00)
			[1/2019]	[227.49]	[0]
535	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017	374.40	0.00
			(-)	(-)	(0.00)
			[0/0]	[374.40]	[0]
536	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017	990.61	0.00
			(-)	(-)	(0.00)
			[0/0]	[990.61]	[0]
537	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/	257.80	12.38
			(-)	(-)	(-0.80)
			[0/0]	[257.00]	[0]
538	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/	390.51	43.25
			(-)	(-)	(0.00)
			[0/0]	[390.51]	[0]
539	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015	670.82	590.00
			(-)	(-)	(0.00)
			[0/0]	[670.82]	[0]
540	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015	704.26	0.00
			(-)	(-)	(0.00)
			[0/0]	[704.26]	[0]
541	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016	257.80	59.30
			(-)	(-)	(0.00)
			[0/0]	[257.80]	[0]
542	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019	1,583.79	375.53
			(-)	(-)	(0.00)
			[1/2019]	[1,583.79]	[0]
543	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/	960.24	0.00
			(-)	(-)	(0.00)
			[0/0]	[960.24]	[0]
544	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016	1,012.90	439.07
			(-)	(-)	(0.00)
			[3/2019]	[1,012.90]	[36]
545	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015	1,055.00	1,328.85
			(-)	(-)	(546.77)
			[0/0]	[1,601.77]	[0]
546	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/	928.83	139.75
			(-)	(-)	(0.00)
			[0/0]	[928.83]	[0]
547	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/	794.30	63.42
			(-)	(-)	(0.00)
			[0/0]	[794.30]	[0]
548	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/	795.76	92.24
			(-)	(-)	(0.00)
			[0/0]	[795.76]	[0]
549	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/	810.22	63.60
			(-)	(-)	(0.00)
			[0/0]	[810.22]	[0]
550	FOUR LANING OF SHIVPURI - GUNA PACKAGE - I	1/2016	7/2018	830.36	315.98
			(-)	(-)	(0.00)
			[7/2018]	[830.36]	[0]
551	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017	639.97	0.00
			(-)	(-)	(0.00)
			[0/0]	[639.97]	[0]
552	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE	1/2018	/	770.73	0.00
			(-)	(-)	(0.00)
			[0/0]	[770.73]	[0]

553	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018 (-) [0/0]	927.54 (-) [927.54]	29.17 (0.00) [0]
554	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [0/0]	497.05 (-) [497.05]	0.00 (0.00) [0]
555	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
556	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [11/2018]	1,175.00 (-) [1,206.10]	1,209.67 (31.10) [67]
557	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	3/2018 (-) [0/0]	628.45 (-) [628.45]	20.74 (0.00) [0]
558	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017 (-) [0/0]	327.32 (-) [327.32]	142.73 (0.00) [0]
559	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017 (-) [0/0]	377.83 (-) [377.83]	57.42 (0.00) [0]
560	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017 (-) [0/0]	641.02 (-) [641.02]	89.88 (0.00) [0]
561	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	381.86 (-) [381.86]	252.03 (0.00) [0]
562	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
563	SHAHDOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017 (-) [0/0]	532.49 (-) [532.49]	137.08 (0.00) [0]
564	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [0/0]	871.15 (-) [871.15]	332.25 (0.00) [0]
565	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [0/0]	511.83 (-) [511.83]	40.87 (0.00) [0]
	<u>Urban Development</u>				
566	CONSTRUCTION OF 1003 NOS 900 NOS TYPE 2 AND 54 NOS TYPE3 AND 33 NOS TYPE 4 AND 16 NOS TYPE 5 FAMILY	5/2016	11/2018 (9/2018) [9/2018]	164.00 (-) [164.00]	111.06 (0.00) [-2]
	<u>MAHARASHTRA</u>				
	<u>Coal</u>				
567	ADASA UG TO OC	8/2015	3/2023 (-) [3/2023]	288.90 (-) [288.90]	0.00 (0.00) [0]
568	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2019]	198.68 (-) [198.68]	234.72 (0.00) [0]
569	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	81.65 (0.00) [0]
570	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	236.21 (0.00) [0]
571	BHANEGAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	91.90 (221.74) [0]
572	BHATADI EXPANSION OC MINE	2/2016	3/2019	304.52	128.39

			(-) [3/2019]	(-) [304.52]	(0.00) [0]
573	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	387.44 (0.00) [0]
574	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	207.28 (0.00) [0]
575	KAMPTEE DEEP OC MINE	11/2015	3/2021 (-) [3/2021]	277.65 (-) [277.65]	18.78 (0.00) [0]
576	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	257.09 (0.00) [0]
577	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	143.07 (0.00) [0]
578	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-) [3/2020]	498.42 (-) [498.42]	52.83 (0.00) [0]
579	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	89.32 (0.00) [0]
580	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	178.90 (0.00) [0]
581	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	100.50 (0.00) [0]
	<u>Fertilisers</u>				
582	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	18.14 (0.00) [0]
583	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT RCF THAL.	2/2016	12/2017 (5/2018) [5/2018]	482.85 (482.85) [482.85]	413.01 (0.00) [0]
584	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [4/2019]	197.79 (209.44) [209.44]	112.27 (11.65) [29]
	<u>Health And Family Welfare</u>				
585	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [1/2020]	582.99 (-) [582.99]	14.08 (0.00) [-]
586	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [3/2019]	274.19 (-) [272.54]	122.66 (-1.65) [0]
	<u>Petroleum</u>				
587	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	56.00 (0.00) [0]
588	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	185.84 (0.00) [0]
589	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	0.05 (0.00) [0]
590	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [1/2021]	212.00 (-) [212.00]	0.08 (0.00) [0]
591	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR	5/2016	1/2021 (-)	348.00 (-)	0.05 (0.00)

	PIPELINE		[1/2021]	[348.00]	[0]
592	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (12/2018) [12/2018]	861.79 (1,256.72) [1,256.72]	1,195.29 (394.93) [67]
593	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	47.18 (0.00) [0]
594	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019) [11/2019]	511.30 (511.30) [511.30]	33.34 (0.00) [0]
595	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,006.83) [4,006.83]	396.86 (0.00) [0]
596	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2019) [3/2019]	4,619.94 (4,619.94) [4,619.94]	3,878.77 (0.00) [15]
597	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	78.88 (0.00) [0]
598	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (3/2018) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,842.42 (606.02) [57]
599	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	456.52 (0.00) [0]
600	LAYING OF HEAT TRACED PIPE LINE WITH ASSOCIATED FACILITIES AT MUMBAI REFINERY	5/2015	1/2019 (-) [1/2019]	193.40 (-) [193.40]	76.81 (0.00) [0]
601	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2019) [5/2019]	3,190.69 (-) [3,247.19]	2,172.39 (56.50) [13]
602	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	107.14 (0.00) [0]
603	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (3/2019) [3/2019]	6,068.80 (6,068.80) [5,296.93]	4,511.38 (-771.87) [-1]
604	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]
605	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	1,429.33 (0.00) [14]
606	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY	1/2017	5/2019 (5/2019) [5/2019]	474.15 (474.15) [474.15]	255.08 (0.00) [0]
607	PIPELINE REPLACEMENT PROJECT -4	2/2015	5/2017 (12/2018) [12/2018]	2,899.93 (-) [2,504.61]	1,832.82 (-395.32) [19]
608	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	0.00 (0.00) [0]
609	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	43.55 (0.00) [0]
	Power				
610	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
611	SOLAPUR STPP	3/2012	11/2016 (3/2019)	9,395.18 (-)	8,774.15 (0.00)

			[3/2019]	[9,395.18]	[28]
612	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS OF NTPC PART-B	4/2015	1/2018 (-) [7/2018]	2,225.00 (2,225.00) [2,225.00]	1,556.00 (0.00) [6]
613	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (12/2018) [12/2018]	477.69 (738.48) [738.48]	664.31 (260.79) [99]
	<u>Railways</u>				
614	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2019]	184.06 (199.12) [199.12]	214.79 (15.06) [0]
615	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2021]	514.68 (2,271.50) [2,271.50]	1,600.99 (1,756.82) [0]
616	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999 (-) [0/0]	663.01 (668.34) [858.97]	713.16 (195.96) [0]
617	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [1,781.98]	1,300.41 (1,286.54) [192]
618	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	0.82 (205.27) [0]
619	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	1,514.45 (-) [1,750.00]	1,443.07 (235.55) [0]
620	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.22 (0.00) [-9]
621	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [8,857.98]	0.00 (-1,110.02) [0]
622	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,326.00 (2,449.91) [2,449.91]	67.04 (123.91) [0]
623	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2021]	277.70 (792.89) [792.89]	254.13 (515.19) [0]
624	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2023 (-) [3/2023]	854.00 (1,035.16) [1,035.16]	13.90 (181.16) [0]
625	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [3/2019]	305.00 (-) [305.00]	250.50 (0.00) [0]
626	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
627	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [3/2019]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [60]
628	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	4,670.00 (3,627.47) [3,627.47]	108.33 (-1,042.53) [0]
629	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
630	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	12/2021 (-) [12/2021]	1,273.00 (1,908.00) [1,908.00]	0.00 (635.00) [0]
631	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-)	714.10 (-)	65.20 (0.00)

			[0/0]	[714.10]	[0]
632	VAIBHAVWADI -KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
633	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
634	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2023]	912.00 (637.95) [637.95]	19.30 (-274.05) [0]
635	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2022]	630.00 (1,272.19) [1,272.19]	91.38 (642.19) [0]
636	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	499.30 (3,168.29) [3,168.29]	880.98 (2,668.99) [0]
637	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2022]	297.85 (540.02) [540.02]	145.70 (242.17) [0]
	<u>Road Transport And Highways</u>				
638	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
639	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	0.00 (0.00) [0]
640	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,479.56 (0.00) [0]
641	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [0/0]	607.00 (-) [607.00]	0.00 (0.00) [0]
642	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	0.00 (0.00) [0]
643	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	535.52 (0.00) [0]
644	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [3/2020]	744.64 (-) [982.00]	0.00 (237.36) [0]
645	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (-) [0/0]	1,071.61 (-) [1,071.61]	0.00 (0.00) [0]
646	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [3/2019]	446.17 (-) [446.17]	0.00 (0.00) [0]
647	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [3/2020]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]
648	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	0.00 (0.00) [0]
649	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	0.00 (0.00) [0]
650	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [3/2019]	400.25 (-) [400.25]	0.00 (0.00) [0]
651	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (-)	1,064.88 (-)	0.00 (0.00)

			[0/0]	[1,064.88]	[0]
652	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [11/2020]	1,059.73 (-) [1,071.00]	10.00 (11.27) [44]
653	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [5/2020]	1,030.44 (-) [1,065.51]	113.04 (35.07) [2]
654	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [8/2020]	988.34 (-) [1,043.28]	133.93 (54.94) [5]
655	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (-) [0/0]	505.00 (-) [505.00]	161.13 (0.00) [0]
656	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [7/2018]	197.69 (-) [197.69]	0.00 (0.00) [0]
657	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	7/2018 (-) [7/2018]	244.00 (-) [244.00]	0.00 (0.00) [0]
658	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (-) [3/2019]	649.50 (-) [649.50]	31.47 (0.00) [0]
659	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [5/2019]	244.90 (-) [244.90]	43.29 (0.00) [0]
660	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [0/0]	593.26 (-) [593.26]	45.11 (0.00) [0]
661	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [156.26]	65.16 (0.00) [0]
662	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/ (-) [0/0]	185.82 (292.00) [185.82]	205.97 (0.00) [0]
663	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [0/0]	531.13 (-) [531.13]	163.10 (0.00) [0]
664	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	13.43 (0.00) [0]
665	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	57.60 (0.00) [0]
666	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [3/2020]	247.02 (-) [157.49]	0.00 (-89.53) [0]
667	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [0/0]	414.51 (-) [414.00]	157.92 (-0.51) [0]
668	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [5/2019]	296.19 (-) [254.00]	86.42 (-42.19) [-10]
669	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,263.02 (0.00) [0]
670	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [0/0]	1,871.34 (-) [1,871.34]	2,881.81 (0.00) [0]
671	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [5/2020]	904.16 (-) [904.16]	34.61 (0.00) [3]

672	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	279.92 (0.00) [0]
673	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [7/2019]	546.00 (-) [546.00]	11.04 (0.00) [0]
674	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [7/2019]	591.66 (-) [591.66]	130.72 (0.00) [0]
675	PANVEL-INDAPUR	12/2011	6/2014 (-) [3/2019]	942.69 (-) [942.69]	437.90 (0.00) [57]
676	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [0/0]	1,724.55 (-) [1,724.55]	2,091.65 (0.00) [0]
677	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00	12/2013	11/2016 (-) [0/0]	220.72 (-) [220.72]	95.02 (0.00) [0]
678	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [0/0]	260.39 (-) [260.39]	87.43 (0.00) [0]
679	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	87.62 (0.00) [0]
680	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [0/0]	292.98 (-) [292.98]	95.60 (0.00) [0]
681	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
682	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [0/0]	404.94 (-) [404.94]	0.00 (0.00) [0]
683	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [0/0]	290.73 (-) [290.73]	0.00 (0.00) [0]
684	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
685	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	5,577.73 (0.00) [0]
Shipping And Ports					
686	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [12/2018]	366.39 (-) [669.46]	413.91 (303.07) [96]
Telecommunications					
687	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (10/2018) [10/2018]	215.30 (-) [215.30]	0.00 (0.00) [5]
688	MAHARASHTRA ACESS (LOT 1)	8/2017	5/2018 (8/2018) [8/2018]	212.70 (-) [212.70]	37.08 (0.00) [3]
689	MAHARASHTRA CORE (LOT1)	8/2017	4/2018 (8/2018) [8/2018]	167.68 (-) [167.68]	30.21 (0.00) [4]
690	MAHARASHTRA NODAL (LOT 1)	8/2017	4/2018 (8/2018) [8/2018]	159.30 (-) [159.30]	12.40 (0.00) [4]
691	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (10/2018)	231.80 (-)	0.00 (0.00)

			[10/2018]	[231.80]	[0]
	<u>Urban Development</u>				
692	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (9/2018) [9/2020]	223.37 (-) [223.37]	0.00 (0.00) [2]
693	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [0/0]	23,136.00 (-) [23,136.00]	0.00 (0.00) [0]
694	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	3,669.58 (0.00) [21]
695	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA	2/2011	3/2016 (12/2017) [4/2018]	241.33 (349.33) [349.33]	307.50 (108.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
696	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	727.56 (-) [13,809.00]	7,765.91 (13,081.44) [108]
	<u>Urban Development</u>				
697	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2018]	216.69 (-) [216.69]	52.00 (0.00) [44]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
698	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	69.24 (0.00) [16]
	<u>Railways</u>				
699	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	4,083.02 (-) [6,000.00]	259.12 (1,916.98) [0]
	<u>Road Transport And Highways</u>				
700	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
701	JORBAT - BARAPANI	1/2011	1/2014 (-) [8/2018]	536.00 (-) [536.00]	673.92 (0.00) [55]
702	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	6.14 (0.00) [0]
	<u>Steel</u>				
703	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	<u>MIZORAM</u>				
	<u>Railways</u>				
704	BHAIRABI SAIRONG, NL, NEFR	4/2008	4/2014 (-) [3/2020]	619.34 (-) [4,600.00]	2,252.69 (3,980.66) [71]
	<u>Road Transport And Highways</u>				
705	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
706	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
707	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]

	<u>MULTI STATE</u>				
	<u>Coal</u>				
708	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	16.00 (0.00) [0]
709	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	88.10 (0.00) [0]
710	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
711	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,827.30]	2,289.00 (2,109.30) [0]
	<u>Petroleum</u>				
712	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
713	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (-) [1,823.00]	279.79 (0.00) [0]
714	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	17.97 (0.00) [0]
715	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	0.00 (0.00) [0]
716	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	177.17 (0.00) [0]
717	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (5/2018) [5/2018]	736.65 (-) [571.47]	543.05 (-165.18) [0]
718	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	152.80 (0.00) [0]
719	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	24.62 (0.00) [0]
720	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [10/2019]	890.00 (-) [887.00]	437.05 (-3.00) [0]
721	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [2/2019]	2,915.00 (2,915.00) [2,915.00]	1,856.19 (0.00) [74]
722	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2019 (12/2020) [12/2019]	2,881.40 (-) [2,881.40]	467.97 (0.00) [0]
723	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	750.43 (0.00) [0]
724	PARADIP HALDIA DURGAPUR LPG PIPELINE	2/2011	6/2018 (-) [10/2018]	913.00 (1,330.00) [1,330.00]	1,291.40 (417.00) [4]
725	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (-) [2,321.00]	354.43 (0.00) [-4]
726	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	143.47 (0.00) [27]

727	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
728	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [12/2018]	3,957.00 (3,561.00) [3,397.00]	2,104.60 (-560.00) [0]
729	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	12.73 (0.00) [0]
730	RAMANMANDI BAHADURGERH PIPELINE CAPACITY EXPANSION PROJECT (PUNJAB,HARYANA)	11/2016	2/2019 (-) [2/2019]	230.00 (-) [230.00]	80.53 (0.00) [0]
731	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (11/2018) [3/2019]	352.56 (-) [438.84]	170.50 (86.28) [24]
732	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (2/2019) [2/2019]	309.81 (723.40) [723.40]	536.27 (413.59) [52]
	<u>Power</u>				
733	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [9/2019]	198.49 (-) [198.49]	0.18 (0.00) [0]
734	400KV D/C TEESTA III - KISHANGANJ TRANSMISSIAN LINE (JV)	8/2008	2/2013 (-) [10/2018]	771.00 (1,642.00) [1,642.00]	1,429.45 (871.00) [68]
735	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	3/2016 (9/2018) [9/2018]	155.57 (206.42) [206.42]	145.07 (50.85) [30]
736	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B	3/2013	12/2015 (6/2018) [9/2018]	2,514.88 (3,190.27) [3,190.27]	2,248.47 (675.39) [33]
737	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	3/2013	6/2015 (5/2018) [8/2018]	514.20 (703.10) [703.10]	603.15 (188.90) [38]
738	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (-) [12/2019]	4,754.42 (-) [9,141.97]	823.37 (4,387.55) [12]
739	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (-) [5/2020]	358.83 (-) [358.83]	0.00 (0.00) [0]
740	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (9/2018) [9/2018]	196.58 (225.28) [225.28]	146.48 (28.70) [31]
741	EASTERN REGION STRENGTHENING SCHEME XI	5/2016	11/2018 (-) [11/2018]	766.21 (-) [766.21]	303.68 (0.00) [0]
742	EASTERN REGION STRENGTHENING SCHEME XIV	5/2016	11/2018 (-) [11/2018]	167.01 (-) [167.01]	90.13 (0.00) [0]
743	EASTERN REGION STRENGTHENING SCHEME-III	7/2010	11/2012 (9/2018) [9/2018]	1,272.80 (1,731.10) [1,731.10]	1,456.53 (458.30) [70]
744	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (12/2018) [12/2018]	1,364.52 (1,891.41) [1,891.41]	1,200.95 (526.89) [32]
745	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (6/2019) [6/2019]	522.29 (550.18) [550.18]	423.38 (27.89) [31]
746	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	383.00 (0.00) [0]

747	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (-) [6/2019]	235.53 (-) [235.53]	14.29 (0.00) [0]
748	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (-) [2/2019]	322.30 (-) [322.30]	88.86 (0.00) [0]
749	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [9/2018]	197.40 (-) [197.40]	73.19 (0.00) [6]
750	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (-) [5/2019]	3,519.59 (-) [3,519.59]	1,680.63 (0.00) [0]
751	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B	4/2015	4/2018 (9/2018) [12/2018]	3,705.61 (-) [3,705.61]	2,490.86 (0.00) [8]
752	GREEN ENERGY CORRIDORS: INTER-STATE TRANSMISSION SCHEME (ISTS) - PART C	7/2015	7/2018 (-) [10/2018]	2,247.37 (-) [2,247.37]	1,395.18 (0.00) [3]
753	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (-) [4/2020]	5,070.13 (-) [5,070.13]	438.09 (0.00) [0]
754	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	5/2016	11/2019 (-) [11/2019]	14,733.37 (-) [14,733.37]	2,724.41 (0.00) [0]
755	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (-) [2/2020]	1,931.39 (-) [1,931.39]	157.04 (0.00) [0]
756	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (-) [6/2019]	251.60 (-) [251.60]	22.13 (0.00) [0]
757	INSTALLATION OF STATCOMS IN WESTERN REGION	3/2015	9/2017 (9/2018) [9/2018]	1,071.24 (-) [1,071.24]	611.76 (0.00) [12]
758	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (-) [12/2019]	5,111.33 (-) [6,652.57]	719.88 (1,541.24) [12]
759	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (13,762.80) [13,762.80]	12,705.71 (2,632.61) [103]
760	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (9/2018) [12/2018]	539.82 (-) [539.82]	416.39 (0.00) [30]
761	PG WORK ASSOCIATED WITH TBCB LINES UNDER COMMON TRANSMISSION SYSTEM FOR PH -II GEN. PROJ. IN ODHISHA	3/2017	3/2019 (-) [3/2019]	162.31 (-) [162.31]	20.90 (0.00) [0]
762	POWERGRID WORK ASSOCIATED WITH SYSTEM STRENGTHENING FOR IPP IN CHATTISGARH AND OTHER GEN. PROJECT IN	7/2016	3/2019 (-) [3/2019]	333.17 (-) [333.17]	245.93 (0.00) [0]
763	PROVISION OF SERIES REACTORS IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	177.52 (-) [177.52]	74.98 (0.00) [0]
764	PROVISION OF STATECOM AT NALAGARH AND LUCKNOW IN NORTHERN REGION	8/2016	2/2019 (-) [2/2019]	431.89 (-) [431.89]	154.46 (0.00) [0]
765	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [11/2019]	283.72 (-) [283.72]	24.85 (0.00) [0]
766	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (-) [3/2019]	562.25 (-) [562.25]	24.20 (0.00) [0]
767	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND	12/2015	4/2019	3,654.00	2,141.00

	VEMAGIRI		(-) [4/2019]	(-) [3,654.00]	(0.00) [0]
768	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [4/2019]	608.24 (-) [608.24]	301.40 (0.00) [0]
769	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID	8/2014	2/2017 (6/2018) [9/2018]	288.49 (-) [376.09]	264.15 (87.60) [19]
770	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [6/2019]	203.28 (260.03) [260.03]	180.99 (56.75) [23]
771	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (-) [12/2019]	379.95 (-) [379.95]	21.24 (0.00) [0]
772	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (-) [6/2019]	337.75 (-) [337.75]	6.80 (0.00) [0]
773	SYSTEM STRENGTHENING XXIV IN SOUTHERN REGION	1/2016	7/2018 (-) [8/2018]	1,455.47 (-) [1,455.47]	1,015.50 (0.00) [1]
774	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	12/2011	8/2014 (9/2018) [9/2018]	297.33 (534.02) [534.02]	418.03 (236.69) [49]
775	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (12/2018) [12/2018]	487.49 (639.46) [639.46]	493.77 (151.97) [54]
776	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2018) [2/2019]	4,824.12 (5,071.94) [5,071.94]	4,531.14 (247.82) [76]
777	TRANSMISSION SYSTEM ASSOCIATED WITH GADARWARA STPS (2X800 MW) OF NTPC (PART A)	4/2015	11/2017 (-) [7/2018]	2,525.00 (-) [2,525.00]	1,940.00 (0.00) [8]
778	TRANSMISSION SYSTEM ASSOCIATED WITH IPPS OF NAGAPATTINAM/ CUDDALORE AREA PACKAGE A	3/2015	12/2015 (-) [9/2018]	955.00 (1,161.00) [1,364.00]	1,158.00 (409.00) [33]
779	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	1/2015	3/2018 (9/2018) [9/2018]	268.80 (340.88) [340.88]	222.24 (72.08) [6]
780	TRANSMISSION SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	2/2010	12/2012 (6/2018) [9/2018]	2,144.00 (2,932.88) [2,932.88]	2,643.53 (788.88) [69]
781	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (-) [871.62]	269.23 (0.00) [23]
782	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [1/2019]	408.46 (-) [408.46]	123.13 (0.00) [0]
783	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-I	4/2016	12/2018 (-) [12/2018]	810.48 (-) [810.48]	512.21 (0.00) [0]
784	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (3/2019) [3/2019]	5,151.37 (-) [5,151.37]	2,543.37 (0.00) [12]
785	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (3/2019) [3/2019]	808.63 (-) [808.63]	316.47 (0.00) [14]
786	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [10/2018]	374.63 (-) [374.63]	180.77 (0.00) [30]
787	WESTERN REGION STRENGTHENING SCHEME-XVI	7/2016	7/2018 (-)	150.99 (-)	85.46 (0.00)

			[8/2018]	[150.99]	[1]
788	WESTERN REGION STRENGTHENING SCHEME XVII	2/2017	9/2019 (-) [9/2019]	204.12 (-) [204.12]	74.37 (0.00) [0]
789	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020 (-) [2/2020]	195.05 (-) [195.05]	52.81 (0.00) [0]
	<u>Railways</u>				
790	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	557.99 (0.00) [0]
791	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	4/2010	/ (-) [0/0]	338.54 (-) [338.54]	212.64 (0.00) [0]
792	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [0/0]	288.35 (-) [238.36]	272.21 (-49.99) [0]
793	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [0/0]	450.55 (-) [251.05]	19.69 (-199.50) [0]
794	BHADRACHALAM ROAD-SATTUPALLI	4/2010	/ (3/2020) [3/2020]	337.49 (704.31) [704.31]	119.69 (366.82) [-]
795	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.54 (863.77) [0]
796	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [173.91]	140.05 (-1.89) [0]
797	CALICUT-MANGALORE (DL) (SR)	2/1996	/ (-) [0/0]	240.00 (-) [579.37]	537.30 (339.37) [0]
798	CHANDIGARH-BADDI NL	4/2007	/ (-) [0/0]	328.14 (-) [1,540.00]	45.20 (1,211.86) [0]
799	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [0/0]	337.96 (-) [186.89]	69.96 (-151.07) [0]
800	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,350.00]	2.27 (1,826.48) [0]
801	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2019]	295.00 (-) [477.31]	165.93 (182.31) [0]
802	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	8/2018 (-) [8/2018]	243.78 (-) [268.78]	96.74 (25.00) [0]
803	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	/ (-) [0/0]	595.91 (-) [595.91]	103.62 (0.00) [0]
804	CHOTTAUDEPUR-DHAR(NL)	4/2007	/ (3/2019) [3/2022]	1,347.26 (-) [1,347.26]	576.05 (0.00) [-]
805	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2019) [3/2022]	1,640.04 (-) [1,640.04]	585.99 (0.00) [0]
806	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	/ (-) [0/0]	296.44 (-) [198.88]	85.03 (-97.56) [0]
807	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/ (-)	1,239.00 (-)	0.00 (0.00)

			[0/0]	[1,239.00]	[0]
808	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	143.18
			(-)	(-)	(0.00)
			[0/0]	[336.91]	[0]
809	DEOGHAR - SULTANGANJ (INL), ER	4/2000	12/2012	607.09	1,069.18
			(12/2012)	(-)	(366.24)
			[0/0]	[973.33]	[0]
810	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	2/2019	622.41	10.34
			(-)	(-)	(1,408.09)
			[12/2022]	[2,030.50]	[46]
811	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	/	553.63	7.96
			(3/2024)	(553.63)	(886.37)
			[3/2024]	[1,440.00]	[-]
812	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/	11,589.00	0.00
			(-)	(-)	(16,592.00)
			[0/0]	[28,181.00]	[0]
813	GAYA-CHATRA (NL)	4/2008	/	415.67	14.62
			(-)	(-)	(134.08)
			[0/0]	[549.75]	[0]
814	GONDIA-JABALPUR(GC),(SECR)	2/1997	3/1998	386.30	967.96
			(-)	(-)	(1,390.51)
			[12/2019]	[1,776.81]	[261]
815	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-)	(-)	(0.00)
			[0/0]	[636.38]	[0]
816	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994	158.77	629.43
			(-)	(274.56)	(475.71)
			[0/0]	[634.48]	[0]
817	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	2/2020	1,176.09	1.92
			(-)	(-)	(2,669.51)
			[12/2022]	[3,845.60]	[34]
818	HAJIPUR - BACHAWARA	5/2015	12/2018	720.00	0.00
			(-)	(-)	(-41.46)
			[12/2018]	[678.54]	[0]
819	HANSDIHA-GODDA NL	4/2011	/	267.09	297.37
			(-)	(-)	(83.69)
			[0/0]	[350.78]	[0]
820	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	6.96
			(-)	(-)	(88.57)
			[0/0]	[260.60]	[0]
821	HATHUA-BHATNI (N L) (NER)	4/2005	5/2019	230.03	274.24
			(-)	(-)	(488.51)
			[5/2019]	[718.54]	[0]
822	HOTGI-KUDGI-GADAG	3/2015	/	1,618.00	635.98
			(3/2021)	(1,614.59)	(-3.41)
			[3/2021]	[1,614.59]	[-]
823	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018	157.94	51.06
			(-)	(-)	(0.00)
			[11/2018]	[157.94]	[0]
824	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	246.00
			(-)	(-)	(0.00)
			[0/0]	[166.89]	[0]
825	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/	162.96	153.31
			(-)	(-)	(0.00)
			[0/0]	[162.96]	[0]
826	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007	625.30	841.57
			(-)	(408.76)	(250.80)
			[0/0]	[876.10]	[0]
827	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	/	2,050.00	317.57
			(3/2023)	(-)	(82.77)
			[3/2023]	[2,132.77]	[-]

828	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	/ (-) [0/0]	923.52 (-) [923.52]	332.87 (0.00) [0]
829	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [0/0]	174.56 (-) [160.97]	70.86 (-13.59) [0]
830	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/ (-) [0/0]	744.71 (744.71) [1,126.79]	761.70 (382.08) [0]
831	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC	4/2010	3/2017 (-) [0/0]	423.66 (-) [720.59]	518.14 (296.93) [0]
832	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2021]	2,063.03 (-) [2,063.03]	295.91 (0.00) [0]
833	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	/ (3/2024) [3/2024]	1,054.35 (1,856.95) [2,200.00]	222.91 (1,145.65) [-]
834	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (346.15) [457.08]	343.65 (186.94) [0]
835	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	/ (-) [0/0]	406.99 (-) [319.58]	147.95 (-87.41) [0]
836	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	972.82 (5,845.65) [178]
837	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	/ (-) [0/0]	601.43 (-) [1,800.00]	98.26 (1,198.57) [0]
838	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	/ (-) [0/0]	493.96 (-) [681.68]	143.42 (187.72) [0]
839	MIRAJ-LONDA	3/2015	/ (3/2021) [3/2021]	1,830.00 (1,190.92) [1,190.92]	166.00 (-639.08) [-]
840	MM FROM BURAMARA-CHAKULIA	4/2008	1/1999 (12/2024) [12/2024]	466.48 (466.48) [1,000.00]	0.83 (533.52) [311]
841	MONIGRAM- NIMTITA	4/2012	/ (-) [0/0]	250.93 (-) [259.23]	176.89 (8.30) [0]
842	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2019 (3/2019) [3/2019]	218.24 (236.41) [645.00]	707.07 (426.76) [0]
843	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	165.82 (-) [450.00]	122.97 (284.18) [0]
844	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	968.28 (1,650.00) [0]
845	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	4/2010	/ (-) [0/0]	494.54 (-) [369.69]	31.99 (-124.85) [0]
846	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	63.66 (228.78) [0]
847	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (-) [394.28]	148.33 (152.76) [0]
848	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019	1,798.00	0.00

			(-) [3/2019]	(-) [1,798.00]	(0.00) [0]
849	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/	523.17	1,082.01
			(-) [3/2018]	(-) [1,871.00]	(1,347.83) [0]
850	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008	733.00	3,000.76
			(-) [3/2019]	(-) [3,040.00]	(2,307.00) [123]
851	PHULERA - DIGANA DOUBLING	5/2015	3/2020	600.00	3.38
			(-) [3/2020]	(-) [685.99]	(85.99) [0]
852	PIRPAINTI-BHAGALPUR	4/2011	/	261.38	321.05
			(-) [0/0]	(-) [332.14]	(70.76) [0]
853	PIRPAINTI-JASIDIH	4/2013	/	915.98	291.31
			(-) [0/0]	(-) [1,130.13]	(214.15) [0]
854	PLASSEY-JIAGANJ DOUBLING	4/2011	3/2015	248.07	161.17
			(-) [0/0]	(-) [234.41]	(-13.66) [0]
855	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017	299.60	1.12
			(-) [0/0]	(-) [269.60]	(-30.00) [0]
856	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/	280.00	834.87
			(-) [0/0]	(-) [1,122.00]	(842.00) [0]
857	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/	2,082.75	181.91
			(-) [0/0]	(-) [2,878.97]	(796.22) [0]
858	RAYADURGA-TUMKUR NL	4/2007	/	970.34	674.76
			(-) [3/2022]	(-) [2,062.20]	(1,091.86) [-]
859	SAINTHIA-TARAPITH 3RD LINE	4/2011	/	193.44	152.40
			(-) [0/0]	(-) [186.64]	(-6.80) [0]
860	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/	268.52	78.81
			(-) [0/0]	(-) [268.52]	(0.00) [0]
861	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/	297.47	52.02
			(-) [0/0]	(-) [153.02]	(-144.45) [0]
862	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	/	277.28	143.44
			(-) [0/0]	(-) [266.00]	(-11.28) [0]
863	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/	296.00	0.00
			(12/2023) [12/2023]	(-) [466.65]	(170.65) [-]
864	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/	450.00	9.31
			(-) [0/0]	(-) [290.85]	(-159.15) [0]
865	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/	365.17	1.76
			(-) [0/0]	(-) [365.67]	(0.50) [0]
866	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020	16,592.00	22,485.00
			(-) [3/2020]	(51,101.00) [51,101.00]	(34,509.00) [0]
867	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/	876.00	0.00
			(-) [0/0]	(-) [876.00]	(0.00) [0]
868	YELAHANKA-PENUKONDA	5/2015	3/2020	860.43	422.93
			(3/2020)	(860.43)	(0.00)

			[3/2020]	[860.43]	[0]
	<u>Road Transport And Highways</u>				
869	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,489.54 (0.00) [0]
870	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [1,928.22]	2,211.94 (0.00) [0]
871	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
872	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [0/0]	604.00 (-) [604.00]	423.83 (0.00) [0]
873	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [7/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [76]
874	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [0/0]	1,244.10 (-) [1,244.10]	0.00 (0.00) [0]
875	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,675.28 (0.00) [0]
876	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [0/0]	2,848.00 (-) [2,848.00]	1,135.19 (0.00) [0]
877	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/ (-) [0/0]	789.83 (-) [789.83]	109.77 (0.00) [0]
	<u>Telecommunications</u>				
878	NETWORK FOR SPECTRUM	3/2012	7/2015 (5/2020) [5/2020]	13,334.00 (24,664.00) [24,664.00]	8,397.00 (11,330.00) [58]
879	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
880	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
881	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2020]	850.00 (-) [3,000.00]	638.43 (2,150.00) [60]
	<u>Road Transport And Highways</u>				
882	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [9/2018]	239.30 (-) [239.30]	0.00 (0.00) [0]
883	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2018]	285.68 (-) [285.68]	0.00 (0.00) [0]
884	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [9/2018]	282.98 (-) [282.98]	0.00 (0.00) [0]
885	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2018]	387.00 (-) [387.00]	0.00 (0.00) [0]
886	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [9/2018]	500.09 (-) [500.09]	0.00 (0.00) [0]
887	CONSTRUCTION OF FOUR/ SIX LANING FROM KM	2/2017	4/2017	507.68	0.00

	132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683		(-) [0/0]	(-) [507.68]	(0.00) [0]
888	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	339.57 (-) [339.57]	0.00 (0.00) [0]
889	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [9/2018]	315.03 (-) [315.03]	0.00 (0.00) [0]
890	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [9/2018]	240.64 (-) [240.64]	0.00 (0.00) [0]
891	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	215.12 (-) [215.12]	0.00 (0.00) [0]
892	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [9/2018]	215.79 (-) [215.79]	0.00 (0.00) [0]
893	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [9/2018]	272.89 (-) [272.89]	0.00 (0.00) [0]
894	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
895	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [9/2018]	251.97 (-) [251.97]	0.00 (0.00) [0]
896	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [9/2018]	237.72 (-) [237.72]	0.00 (0.00) [0]
897	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
898	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
899	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
900	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
901	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	233.26 (0.00) [108]
902	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2019]	172.08 (-) [172.08]	263.24 (0.00) [108]
903	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2021]	479.15 (-) [479.15]	105.89 (0.00) [24]
904	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	344.12 (0.00) [36]
905	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	397.45 (0.00) [0]
906	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2020]	479.53 (-) [479.53]	242.14 (0.00) [84]

907	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	42.95 (0.00) [24]
908	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2019]	457.77 (-) [457.77]	581.49 (0.00) [72]
909	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	65.79 (0.00) [24]
910	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2018]	302.96 (-) [302.96]	334.77 (0.00) [0]
911	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	689.20 (0.00) [0]
	<u>Mines</u>				
912	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	94.71 (0.00) [0]
913	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (11/2020) [11/2020]	355.00 (355.00) [355.00]	31.92 (0.00) [0]
914	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
915	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	299.64 (0.00) [0]
	<u>Petroleum</u>				
916	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	2.12 (0.00) [0]
917	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	27.09 (0.00) [0]
918	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	181.20 (-) [181.20]	13.66 (0.00) [0]
919	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	421.08 (0.00) [0]
920	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (-) [1/2019]	429.00 (-) [429.00]	197.48 (0.00) [0]
921	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	32.91 (0.00) [0]
922	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (12/2018) [12/2018]	3,150.00 (-) [3,150.00]	2,061.99 (0.00) [15]
	<u>Power</u>				
923	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (6/2019) [6/2019]	12,532.44 (-) [13,740.53]	7,879.74 (1,208.09) [10]
924	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (-) [4/2019]	844.64 (-) [844.64]	274.50 (0.00) [0]
	<u>Railways</u>				
925	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [942.95]	874.64 (0.00) [24]

926	BHADRAK - NERGUNDI 3RD LINE	3/2013	3/2021 (-) [3/2021]	858.67 (843.04) [843.04]	70.62 (-15.63) [0]
927	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	3/2021 (-) [3/2021]	1,172.92 (-) [1,172.92]	202.87 (0.00) [0]
928	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
929	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
930	HARIDASPUR-PARADEEP(NL)	4/1996	3/2020 (9/2009) [3/2020]	301.64 (-) [1,844.47]	1,270.29 (1,542.83) [0]
931	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2021 (-) [3/2021]	1,547.38 (1,547.38) [1,547.38]	155.50 (0.00) [0]
932	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	3/2021 (-) [3/2021]	701.61 (-) [810.02]	81.68 (108.41) [0]
933	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [12/2018]	133.41 (207.00) [385.00]	366.77 (251.59) [117]
934	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	6/2021 (-) [6/2021]	470.21 (-) [3,798.80]	1,069.54 (3,328.59) [0]
935	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2021 (-) [3/2022]	2,361.74 (2,361.74) [2,361.74]	67.43 (0.00) [12]
936	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [6/2020]	969.83 (969.83) [969.83]	326.40 (0.00) [3]
937	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (12/2024) [12/2024]	524.43 (524.43) [939.00]	184.09 (414.57) [36]
938	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	178.13 (82.22) [0]
939	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2020]	960.18 (-) [970.00]	867.19 (9.82) [0]
940	SAMBALPUR-TALCHER DOUBLING	3/2011	3/2021 (-) [3/2021]	679.27 (1,539.28) [1,539.28]	716.89 (860.01) [0]
941	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	183.23 (-) [1,202.70]	592.80 (1,019.47) [82]
942	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	12/2022 (-) [3/2023]	810.78 (1,928.07) [1,928.07]	561.81 (1,117.29) [3]
943	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (2,735.00) [2,335.67]	241.54 (0.00) [0]
	<u>Road Transport And Highways</u>				
944	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	0.00 (0.00) [0]
945	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]

946	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
947	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
948	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	0.00 (0.00) [0]
949	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	0.00 (0.00) [0]
950	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	1,555.96 (0.00) [0]
951	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [0/0]	1,008.96 (-) [1,008.96]	0.00 (0.00) [0]
952	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPASS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	0.00 (0.00) [0]
953	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [0/0]	476.56 (-) [476.56]	0.00 (0.00) [0]
954	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
955	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [0/0]	953.09 (-) [953.09]	0.00 (0.00) [0]
956	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	0.00 (0.00) [0]
957	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [0/0]	614.48 (-) [614.48]	0.00 (0.00) [0]
958	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	0.00 (0.00) [0]
959	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
960	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	0.00 (0.00) [0]
961	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [0/0]	1,288.07 (-) [1,420.00]	0.00 (131.93) [0]
962	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
963	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [0/0]	686.65 (-) [686.65]	0.00 (0.00) [0]
964	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
965	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	0.00 (-0.05) [0]
966	REHABILITATION AND UPGRADATION OF SIX LANING OF	1/2018	/	999.00	0.00

	BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141		(-) [0/0]	(-) [999.00]	(0.00) [0]
967	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	0.00 (0.04) [0]
968	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
969	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
970	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,613.62 (0.00) [0]
971	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [0/0]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
972	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
973	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
974	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
975	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [11/2018]	157.30 (157.00) [157.00]	0.00 (-0.30) [5]
976	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	0.00 (0.00) [0]
977	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	0.00 (0.00) [0]
978	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]
	<u>Steel</u>				
979	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [2/2019]	3,127.30 (-) [3,127.30]	5,467.78 (0.00) [10]
	<u>PUNJAB</u>				
	<u>Fertilisers</u>				
980	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	17.76 (0.00) [0]
981	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	19.79 (0.00) [0]
	<u>Health And Family Welfare</u>				
982	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [6/2020]	703.00 (-) [703.00]	272.00 (0.00) [0]
983	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [12/2018]	152.95 (-) [152.95]	60.45 (0.00) [10]
	<u>Railways</u>				
984	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]

985	QADIAN-BEAS	4/2011	/	205.22	1.59
			(-)	(-)	(0.00)
			[0/0]	[205.22]	[0]
	Road Transport And Highways				
986	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/	573.96	209.74
			(-)	(605.00)	(31.04)
			[0/0]	[605.00]	[0]
987	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/	486.74	189.39
			(-)	(-)	(0.00)
			[0/0]	[486.74]	[0]
988	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/	1,169.61	59.82
			(-)	(-)	(0.00)
			[4/2020]	[1,169.61]	[-]
989	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/	463.65	280.16
			(-)	(546.00)	(0.00)
			[0/0]	[463.65]	[0]
990	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/	483.38	65.76
			(-)	(-)	(0.00)
			[0/0]	[483.38]	[0]
991	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/	616.36	68.58
			(-)	(-)	(0.00)
			[0/0]	[616.36]	[0]
992	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/	847.02	299.81
			(-)	(-)	(0.00)
			[0/0]	[847.02]	[0]
993	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/	889.24	389.64
			(-)	(-)	(0.00)
			[0/0]	[889.24]	[0]
994	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019	1,388.34	0.00
			(-)	(-)	(0.00)
			[9/2019]	[1,388.34]	[0]
995	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/	312.79	17.57
			(-)	(-)	(0.00)
			[0/0]	[312.79]	[0]
996	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K	7/2014	/	319.80	102.55
			(-)	(-)	(0.00)
			[0/0]	[319.80]	[0]
997	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020	754.54	0.00
			(-)	(-)	(1.73)
			[3/2020]	[756.27]	[0]
998	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS	12/2015	/	766.36	99.86
			(-)	(-)	(0.00)
			[0/0]	[766.36]	[0]
999	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/	578.38	128.53
			(-)	(-)	(0.00)
			[0/0]	[578.38]	[0]
1000	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017	447.29	4.88
			(-)	(-)	(0.00)
			[4/2019]	[447.29]	[16]
1001	FOUR LANING OF KHARAR - KURALI SECTION OF NH-21	12/2015	12/2017	239.23	123.47
			(-)	(-)	(0.00)
			[0/0]	[239.23]	[0]
1002	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/	479.00	391.33
			(-)	(-)	(0.00)
			[0/0]	[479.00]	[0]
1003	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/	273.06	17.85
			(-)	(-)	(0.00)
			[0/0]	[273.06]	[0]
1004	JALANDHAR - AMRITSAR	1/2014	1/2016	523.85	170.68
			(-)	(-)	(0.00)
			[0/0]	[523.85]	[0]

1005	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/ (-) [0/0]	435.90 (-) [435.90]	31.02 (0.00) [0]
1006	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/ (-) [0/0]	279.68 (-) [279.68]	25.28 (0.00) [0]
1007	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/ (-) [0/0]	899.21 (-) [899.21]	25.08 (0.00) [0]
1008	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	26.92 (0.00) [0]
	<u>Urban Development</u>				
1009	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (8/2018) [8/2018]	388.00 (-) [388.00]	354.09 (0.00) [15]
1010	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (6/2019) [6/2019]	294.00 (-) [294.00]	95.08 (0.00) [2]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1011	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (3/2017) [12/2020]	12,320.00 (-) [12,320.00]	9,520.00 (0.00) [48]
	<u>Coal</u>				
1012	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	176.76 (0.00) [0]
1013	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	10.45 (0.00) [0]
	<u>Petroleum</u>				
1014	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1015	LPG BP PROJECT JODHPUR	3/2018	/ (-) [0/0]	229.80 (-) [229.80]	69.00 (0.00) [0]
	<u>Power</u>				
1016	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (-) [1/2019]	1,429.38 (-) [1,429.38]	623.84 (0.00) [0]
1017	TRANSMISSION SYSTEM ASSOCIATED WITH RAPP 7 and 8 - PART B	7/2015	11/2017 (10/2018) [10/2018]	307.18 (-) [307.18]	203.36 (0.00) [11]
	<u>Railways</u>				
1018	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,103.04]	2.32 (229.33) [0]
1019	AJMER-BANGURGRAM	4/2011	11/2019 (-) [11/2019]	213.39 (-) [244.02]	150.49 (30.63) [0]
1020	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1021	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [2/2019]	242.09 (-) [349.00]	234.37 (106.91) [0]
1022	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2019]	246.08 (-) [348.55]	100.17 (102.47) [-6]

1023	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [2/2019]	410.08 (780.98) [795.01]	423.40 (384.93) [0]
1024	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [3/2020]	829.74 (-) [1,216.00]	630.24 (386.26) [60]
1025	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR)	4/2008	3/2014 (3/2019) [3/2019]	653.19 (-) [1,158.00]	723.56 (504.81) [60]
1026	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [8/2022]	808.85 (-) [808.85]	0.00 (0.00) [0]
1027	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	4/2013	12/2019 (-) [12/2019]	456.00 (295.02) [420.18]	56.05 (-35.82) [0]
1028	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [12/2019]	493.17 (-) [493.17]	402.91 (0.00) [21]
1029	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1030	RANI-MARWAR JN. PATCH DOUBLING	4/2012	11/2018 (-) [11/2018]	288.97 (-) [346.35]	270.36 (57.38) [0]
1031	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [10/2018]	236.93 (-) [294.90]	144.49 (57.97) [0]
	<u>Road Transport And Highways</u>				
1032	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	596.06 (0.00) [0]
1033	2-LANE WITH PAVED SHOULDER TONK- SAWAIMADHOPUR	8/2016	1/2019 (-) [1/2019]	320.30 (-) [320.30]	170.51 (0.00) [0]
1034	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA	11/2012	8/2016 (-) [11/2018]	530.07 (-) [530.07]	556.02 (0.00) [27]
1035	2-LANING WITH PS BHILWARA-LODPURA SECTION	3/2014	3/2016 (-) [0/0]	240.10 (-) [240.10]	151.72 (0.00) [0]
1036	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	0.00 (0.00) [0]
1037	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [0/0]	1,031.95 (-) [1,031.95]	0.00 (0.00) [0]
1038	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [12/2018]	822.90 (-) [822.90]	620.00 (0.00) [8]
1039	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	2/2010 (-) [0/0]	275.00 (-) [281.31]	168.31 (6.31) [0]
1040	DEOLI KOTA	1/2011	7/2013 (-) [0/0]	593.00 (-) [593.00]	1,036.26 (0.00) [0]
1041	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	0.00 (0.00) [0]
1042	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [6/2019]	763.23 (-) [763.23]	0.00 (0.00) [0]

1043	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM	6/2016	6/2019 (-) [6/2019]	649.00 (-) [649.00]	0.00 (0.00) [0]
1044	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	0.00 (0.00) [0]
1045	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [10/2018]	1,673.70 (-) [1,673.70]	3,079.44 (0.00) [84]
1046	JAISALMER - BARMER	8/2015	2/2018 (-) [0/0]	482.27 (-) [482.27]	297.50 (0.00) [0]
1047	JODHPUR - BARMER SECTION OF PACKAGE -I	10/2014	4/2017 (-) [0/0]	264.72 (-) [264.72]	98.18 (0.00) [0]
1048	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1049	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1050	PADI - DAHOD	11/2014	5/2017 (-) [9/2018]	279.14 (-) [279.14]	211.04 (0.00) [16]
1051	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	9/2015	3/2018 (-) [11/2018]	567.51 (-) [567.51]	42.79 (0.00) [8]
1052	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1053	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI	1/1991	5/2016 (-) [0/0]	208.87 (-) [208.87]	206.78 (0.00) [0]
1054	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [0/0]	269.26 (-) [269.26]	212.72 (0.00) [0]
1055	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1056	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [0/0]	1,100.19 (-) [1,100.19]	0.00 (0.00) [0]
1057	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [0/0]	1,239.82 (-) [1,239.82]	0.00 (0.00) [0]
1058	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [4/2020]	894.00 (-) [894.00]	0.00 (0.00) [0]
1059	TWO LANE WITH PAVED SHOULDERS OF JODHPUR - POKARAN SECTION OF NH-114 (NEW NH NO -50)	7/2015	7/2017 (-) [0/0]	455.60 (-) [455.60]	54.50 (0.00) [0]
1060	TWO LANING WITH PAVED SHOULDER BARMER - SANCHOR - GUJARAT BODER (UP TO GANDHAV BRIDGE) SECTION OF N	8/2015	2/2018 (-) [0/0]	538.08 (-) [538.08]	30.08 (0.00) [0]
1061	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [3/2019]	425.19 (-) [425.19]	274.20 (0.00) [30]
1062	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [10/2018]	275.90 (-) [275.90]	223.48 (0.00) [-]
1063	TWO LANNING WITH PAVED SHOULDER OF	7/2016	10/2018	331.46	0.00

	MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM		(-) [10/2018]	(-) [331.46]	(0.00) [0]
1064	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	474.40 (0.00) [3]
1065	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.80 (0.00) [0]
1066	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [0/0]	383.40 (-) [383.40]	224.68 (0.00) [0]
1067	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1068	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	0.00 (0.00) [0]
	<u>Steel</u>				
1069	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [8/2018]	189.00 (-) [189.00]	0.00 (0.00) [17]
	<u>Urban Development</u>				
1070	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [7/2019]	549.31 (-) [549.31]	126.11 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Civil Aviation</u>				
1071	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	1/2009	1/2011 (-) [9/2018]	309.46 (-) [553.53]	546.69 (244.07) [92]
	<u>Railways</u>				
1072	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
1073	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
1074	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
1075	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
1076	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1077	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	8,761.00 (0.00) [36]
1078	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (9/2016) [3/2019]	3,492.00 (5,677.00) [6,100.00]	5,655.69 (2,608.00) [102]
	<u>Coal</u>				
1079	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	388.25 (-749.11) [51]
1080	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (12/2018)	5,907.11 (-)	5,547.98 (0.00)

			[12/2018]	[5,907.11]	[36]
1081	NEYVELI SOLAR POWER PROJECT 130 MW	5/2016	6/2017 (12/2017) [12/2017]	687.28 (759.19) [759.19]	758.30 (71.91) [0]
	<u>Petroleum</u>				
1082	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	0.28 (0.00) [0]
1083	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	351.69 (0.00) [0]
1084	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [10/2020]	466.43 (-) [466.43]	1.18 (0.00) [0]
1085	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [12/2018]	4,497.00 (-) [4,497.00]	253.96 (0.00) [0]
1086	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1087	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [4/2019]	390.52 (390.52) [390.52]	131.04 (0.00) [1]
1088	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.12 (0.00) [0]
1089	NEW CRUDE OIL PIPELINE PROJECT FROM CHENNAI PORT TO MANALI REFINERY	5/2015	11/2016 (-) [7/2018]	257.87 (-) [257.87]	226.81 (0.00) [20]
1090	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	1.31 (0.00) [0]
1091	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]
	<u>Power</u>				
1092	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	9/2011	9/2014 (9/2018) [9/2018]	1,940.13 (2,702.65) [2,702.65]	2,492.04 (762.52) [48]
1093	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (9/2018) [12/2018]	1,779.29 (2,187.32) [2,187.32]	2,041.61 (408.03) [121]
1094	TRANSMISSION SYSTEM FOR EVACUTION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (-) [7/2019]	186.17 (-) [186.17]	41.36 (0.00) [0]
	<u>Railways</u>				
1095	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (257.00) [257.00]	0.00 (0.00) [0]
1096	ATTIPPATTU PUTTUR	4/2008	/ (-) [0/0]	446.87 (527.37) [1,105.00]	3.34 (658.13) [0]
1097	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	4/1998	/ (-) [0/0]	271.24 (-) [520.00]	468.18 (248.76) [0]
1098	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/ (-) [0/0]	343.17 (-) [1,065.00]	1,049.68 (721.83) [0]
1099	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]

1100	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (3/2019) [3/2019]	495.74 (495.74) [734.01]	433.38 (238.27) [69]
1101	KARUR-SALEM(NL),SR	2/1997	/	155.55	856.94
			(-)	(-)	(764.45)
			[0/0]	[920.00]	[0]
1102	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020	760.00	0.00
			(-)	(-)	(422.31)
			[3/2020]	[1,182.31]	[0]
1103	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	2/1997	3/2015	458.63	0.92
			(-)	(-)	(0.00)
			[0/0]	[458.63]	[0]
1104	MADURAI-BODINAYAKKANUR	4/2008	/	164.41	55.87
			(-)	(-)	(285.59)
			[3/2020]	[450.00]	[-]
1105	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	2/2003	3/2009	199.55	2.12
			(-)	(-)	(130.77)
			[0/0]	[330.32]	[0]
1106	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	2/2006	3/2012	208.00	3.58
			(-)	(-)	(0.00)
			[0/0]	[208.00]	[0]
1107	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022	1,700.00	0.00
			(-)	(-)	(0.00)
			[3/2022]	[1,700.00]	[0]
1108	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI	9/2007	/	404.19	1,102.29
			(-)	(-)	(1,668.31)
			[0/0]	[2,072.50]	[0]
1109	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/	839.00	0.61
			(-)	(-)	(661.00)
			[0/0]	[1,500.00]	[0]
1110	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005	268.87	304.07
			(-)	(-)	(33.15)
			[0/0]	[302.02]	[0]
1111	TIDIVANAM-NAGARI (NL)	9/2006	/	456.00	233.59
			(-)	(-)	(1,844.00)
			[0/0]	[2,300.00]	[0]
1112	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024	1,567.00	0.00
			(-)	(-)	(0.00)
			[3/2026]	[1,567.00]	[24]
1113	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	2/2000	3/2014	200.84	394.26
			(-)	(-)	(0.00)
			[0/0]	[200.84]	[0]
1114	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	2/2005	3/2010	600.00	671.00
			(-)	(600.00)	(45.54)
			[0/0]	[645.54]	[0]
	Road Transport And Highways				
1115	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013	485.00	406.68
			(-)	(-)	(0.00)
			[12/2018]	[485.00]	[64]
1116	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014	624.00	350.79
			(-)	(-)	(0.00)
			[0/0]	[624.00]	[0]
1117	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017	244.27	0.00
			(-)	(-)	(0.00)
			[0/0]	[244.27]	[0]
1118	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017	1,227.87	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,227.87]	[0]
1119	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015	258.97	0.00
			(-)	(-)	(9.95)
			[0/0]	[268.92]	[0]

1120	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1121	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	322.45 (0.00) [0]
1122	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [5/2019]	1,387.11 (-) [1,387.11]	830.16 (0.00) [18]
1123	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [4/2019]	641.17 (-) [641.17]	244.33 (0.00) [33]
1124	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [0/0]	1,176.37 (-) [1,176.37]	0.00 (0.00) [0]
1125	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [6/2019]	707.82 (-) [707.82]	164.24 (0.00) [10]
1126	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [3/2020]	848.45 (-) [848.45]	5.00 (0.00) [0]
1127	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [7/2018]	641.17 (-) [641.17]	204.31 (0.00) [0]
1128	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1129	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [0/0]	379.90 (-) [379.90]	0.00 (0.00) [0]
1130	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [12/2018]	1,250.00 (-) [1,250.00]	1,329.31 (0.00) [60]
1131	THANJAVUR - PUDUKOTTAI SECTION OF NH-226	11/2014	11/2016 (-) [0/0]	563.92 (-) [563.92]	186.50 (0.00) [0]
1132	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1133	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	761.19 (0.00) [0]
1134	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [12/2018]	374.00 (-) [374.00]	237.00 (0.00) [67]
1135	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [6/2019]	563.92 (-) [563.92]	95.89 (0.00) [18]
	<u>Shipping And Ports</u>				
1136	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (-) [5/2020]	600.00 (258.00) [257.90]	1.45 (-342.10) [29]
1137	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (-) [0/0]	244.50 (258.00) [275.98]	275.98 (31.48) [0]
1138	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1139	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]

	<u>Urban Development</u>				
1140	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [10/2019]	209.00 (-) [209.00]	26.00 (0.00) [0]
1141	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1142	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (12/2018) [12/2018]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [36]
1143	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [0/0]	348.77 (-) [348.77]	0.00 (0.00) [0]
1144	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM	4/2014	9/2016 (3/2018) [9/2018]	332.72 (-) [342.00]	316.94 (9.28) [24]
	<u>TELANGANA</u>				
	<u>Coal</u>				
1145	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	0.00 (0.00) [0]
1146	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018 (-) [3/2019]	426.79 (-) [426.79]	0.00 (0.00) [12]
1147	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (3/2021) [3/2021]	447.06 (437.51) [437.51]	353.61 (-9.55) [72]
1148	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1149	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2019]	413.84 (-) [413.84]	0.00 (0.00) [0]
1150	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (3/2019) [3/2019]	397.09 (442.42) [442.42]	79.96 (45.33) [0]
1151	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (384.32) [384.32]	146.45 (-33.01) [44]
1152	KISTARAM OCP	11/2010	3/2015 (3/2021) [3/2021]	242.29 (164.04) [164.04]	12.69 (-78.25) [72]
1153	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (3/2018) [3/2018]	181.19 (-) [181.19]	159.87 (0.00) [0]
1154	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (3/2023) [3/2023]	418.97 (489.62) [489.62]	477.74 (70.65) [132]
1155	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (3/2021) [3/2021]	162.76 (349.28) [349.28]	1.31 (186.52) [72]
1156	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (3/2019) [3/2019]	430.45 (415.37) [415.37]	160.45 (-15.08) [36]
1157	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (3/2019) [3/2019]	365.01 (-) [365.01]	204.26 (0.00) [45]
1158	RKP OCP PHASE-I	3/2010	3/2015 (3/2019) [3/2019]	209.78 (-) [209.78]	154.52 (0.00) [48]
1159	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012	249.03	186.91

			(3/2024) [3/2024]	(448.86) [448.86]	(199.83) [144]
	<u>Power</u>				
1160	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (10/2020) [10/2020]	10,598.98 (-) [10,598.98]	2,201.67 (0.00) [3]
	<u>Railways</u>				
1161	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2020]	632.68 (-) [816.55]	546.32 (183.87) [57]
1162	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	169.16 (0.00) [0]
1163	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	616.08 (-) [616.08]	0.00 (0.00) [0]
1164	MACHERLA-NALGONDA(NL)(SCR)	7/1998	7/2008 (-) [0/0]	125.00 (-) [458.26]	3.69 (333.26) [0]
1165	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	0.00 (65.24) [0]
1166	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2022 (3/2022) [3/2022]	378.56 (-) [1,160.47]	71.23 (781.91) [0]
1167	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (2,911.84) [2,911.84]	0.92 (1,799.84) [0]
1168	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	12/1994	/ (3/2017) [3/2017]	124.43 (926.23) [1,025.00]	1,016.69 (900.57) [0]
1169	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	728.10 (-) [773.94]	174.56 (45.84) [0]
	<u>Road Transport And Highways</u>				
1170	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016 (-) [0/0]	340.00 (-) [340.00]	0.00 (0.00) [0]
1171	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [6/2019]	1,266.60 (-) [1,544.00]	1,399.30 (277.40) [33]
1172	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	3/2011	12/2015 (-) [0/0]	218.31 (-) [339.82]	208.28 (121.51) [0]
1173	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1174	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1175	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [3/2019]	1,423.96 (-) [1,423.96]	454.64 (0.00) [4]
1176	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016 (-) [0/0]	158.65 (-) [158.65]	103.50 (0.00) [0]
1177	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016 (-) [0/0]	177.18 (-) [177.18]	40.51 (0.00) [0]
1178	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR	1/2014	3/2016 (-)	270.00 (-)	19.84 (0.00)

	DAM SECT		[0/0]	[270.00]	[0]
1179	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [313.27]	0.00 (17.80) [0]
1180	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [0/0]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1181	YAN TO NIRMAL SEREHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW	12/2013	3/2016 (-) [0/0]	244.08 (-) [244.08]	38.32 (0.00) [0]
	<u>Urban Development</u>				
1182	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	3.72 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
1183	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
1184	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (-) [3/2020]	813.34 (-) [3,374.00]	2,951.92 (2,560.66) [72]
1185	AGARTALA-AKHAURA NL	4/2012	3/2019 (-) [7/2019]	252.00 (-) [580.00]	0.00 (328.00) [4]
1186	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,857.00]	1,540.32 (962.00) [0]
	<u>Road Transport And Highways</u>				
1187	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	36.90 (0.00) [0]
1188	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Steel</u>				
1189	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1190	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1191	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1192	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	6/2011	3/2018 (-) [3/2019]	1,131.28 (-) [1,131.28]	562.24 (0.00) [12]
1193	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	2,649.27 (0.80) [0]
	<u>Health And Family Welfare</u>				
1194	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [4/2020]	785.00 (-) [785.00]	39.35 (0.00) [0]
1195	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	18.50 (0.00) [-]

	Petroleum				
1196	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	0.90 (0.00) [0]
1197	AURAIYA PHULPUR PIPELINE PROJECT	7/2015	12/2018 (-) [12/2018]	1,427.94 (-) [750.00]	558.94 (-677.94) [0]
1198	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	137.03 (0.00) [0]
1199	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	84.64 (0.00) [0]
1200	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.00 (0.00) [0]
1201	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [8/2021]	318.80 (-) [318.80]	0.00 (0.00) [0]
	Power				
1202	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [3/2019]	195.42 (294.60) [294.60]	187.40 (99.18) [61]
1203	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1204	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [8/2019]	9,750.89 (-) [9,750.89]	8,270.00 (0.00) [32]
1205	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (9/2019) [9/2019]	9,188.98 (-) [9,188.98]	4,820.27 (0.00) [6]
	Railways				
1206	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1207	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1208	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	8/2018 (-) [8/2018]	199.75 (-) [270.00]	249.40 (70.25) [0]
1209	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,900.00]	0.00 (0.00) [0]
1210	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	858.40 (0.00) [3]
1211	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [474.30]	441.25 (278.66) [0]
1212	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1213	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1214	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [245.39]	210.67 (125.39) [0]
1215	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ	4/2013	/	654.00	0.00

	AND RAEBARELI		(-) [0/0]	(-) [654.00]	(0.00) [0]
1216	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/	182.92	0.00
			(-) [0/0]	(-) [197.73]	(14.81) [0]
1217	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	4/1997	4/1999	233.00	326.10
			(-) [0/0]	(-) [318.42]	(85.42) [0]
1218	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016	213.00	0.00
			(-) [1/2022]	(-) [213.35]	(0.35) [69]
1219	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/	643.00	0.00
			(-) [0/0]	(-) [644.00]	(1.00) [0]
1220	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2018	528.57	0.61
			(-) [12/2019]	(-) [528.57]	(0.00) [21]
1221	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019	927.01	921.55
			(-) [3/2020]	(-) [977.00]	(49.99) [12]
1222	MANDHANA - BRAHMAWART NEW LINE PROJECT.	4/1997	4/1999	609.04	1,792.10
			(-) [11/2018]	(1,063.00) [1,807.88]	(1,198.84) [235]
1223	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020	524.00	0.00
			(-) [3/2020]	(668.00) [668.00]	(144.00) [0]
1224	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	12/2025	1,765.90	213.57
			(-) [12/2025]	(-) [1,765.92]	(0.02) [0]
1225	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/	377.44	182.85
			(-) [0/0]	(-) [377.44]	(0.00) [0]
1226	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017	150.00	0.00
			(-) [10/2022]	(-) [150.00]	(0.00) [66]
1227	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018	1,343.00	0.00
			(-) [1/2018]	(-) [1,345.00]	(2.00) [0]
1228	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017	622.50	0.00
			(-) [10/2022]	(427.00) [426.74]	(-195.76) [66]
1229	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020	2,436.21	210.62
			(-) [3/2021]	(-) [2,436.21]	(0.00) [12]
1230	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022	1,750.00	69.56
			(-) [2/2019]	(-) [1,295.42]	(-454.58) [-37]
1231	UNCHAHAH-AMETHI	4/2012	/	380.00	4.12
			(-) [0/0]	(-) [380.00]	(0.00) [0]
1232	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010	325.00	618.19
			(-) [0/0]	(-) [1,581.53]	(1,256.53) [0]
1233	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	12/2024	750.55	86.24
			(-) [12/2024]	(-) [750.56]	(0.01) [0]
	<u>Road Transport And Highways</u>				
1234	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016	368.73	223.82
			(-) [0/0]	(-) [368.73]	(0.00) [0]
1235	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-	11/2010	3/2017	305.49	0.00

	52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE		(-) [0/0]	(-) [305.49]	(0.00) [0]
1236	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	409.92 (0.00) [0]
1237	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	566.34 (0.00) [0]
1238	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	411.64 (0.00) [56]
1239	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	187.43 (0.00) [0]
1240	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [4/2019]	2,016.00 (-) [2,016.00]	149.36 (0.00) [0]
1241	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [0/0]	1,668.00 (-) [1,668.00]	0.00 (0.00) [0]
1242	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	596.99 (0.00) [0]
1243	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	0.00 (0.00) [-]
1244	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	0.00 (0.00) [-]
1245	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	28.08 (0.00) [0]
1246	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [4/2019]	1,587.49 (-) [1,587.49]	70.80 (0.00) [0]
1247	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	83.05 (0.00) [0]
1248	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [1/2019]	1,657.20 (-) [1,657.20]	1,825.00 (0.00) [0]
1249	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	314.52 (382.01) [0]
1250	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1251	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [4/2019]	676.73 (-) [676.73]	115.21 (0.00) [0]
1252	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018 (-) [0/0]	774.57 (-) [774.57]	0.00 (0.00) [0]
1253	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	10/2016 (-) [0/0]	397.04 (-) [397.04]	0.00 (0.00) [0]
1254	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	3/2017 (-) [0/0]	317.76 (-) [317.76]	15.47 (0.00) [0]
1255	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-)	1,046.00 (-)	805.19 (0.00)

			[0/0]	[1,046.00]	[0]
1256	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/ (-) [0/0]	629.74 (-) [629.74]	0.00 (0.00) [0]
1257	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [534.55]	49.05 (0.00) [0]
1258	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1259	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	165.66 (0.00) [0]
1260	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	0.00 (0.00) [0]
1261	DELHI-MEERUT EXPRESSWAY PKG-I KM 0 TO 8.360 KM	1/2016	5/2019 (-) [5/2019]	701.12 (-) [701.12]	841.92 (0.00) [0]
1262	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [6/2019]	1,081.57 (-) [1,081.57]	0.00 (0.00) [0]
1263	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,232.21]	0.00 (0.00) [0]
1264	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [3/2020]	1,989.00 (-) [1,989.00]	0.00 (0.00) [0]
1265	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	839.01 (0.00) [0]
1266	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-IV)	9/2015	3/2018 (-) [0/0]	789.31 (-) [789.31]	372.34 (0.00) [0]
1267	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-V)	9/2015	3/2018 (-) [0/0]	664.53 (-) [664.53]	1,494.46 (0.00) [0]
1268	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-VI)	9/2015	3/2018 (-) [0/0]	768.56 (-) [768.56]	1,643.18 (0.00) [0]
1269	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,898.25 (0.00) [0]
1270	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	247.31 (0.00) [0]
1271	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	195.03 (0.00) [0]
1272	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	228.89 (0.00) [0]
1273	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	235.71 (0.00) [0]
1274	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	211.01 (0.00) [0]
1275	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [3/2020]	1,373.28 (-) [1,373.28]	0.00 (0.00) [0]

1276	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [3/2020]	1,184.71 (-) [1,310.00]	0.00 (125.29) [0]
1277	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [4/2019]	899.00 (-) [899.00]	0.00 (0.00) [0]
1278	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,986.56 (0.00) [0]
1279	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016 (-) [0/0]	283.45 (-) [283.45]	0.00 (0.00) [0]
1280	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	359.94 (0.00) [0]
1281	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [445.89]	0.00 (0.00) [0]
1282	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [0/0]	493.94 (-) [493.94]	0.00 (0.00) [0]
1283	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [0/0]	227.74 (-) [227.74]	0.00 (0.00) [0]
1284	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1285	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1286	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1287	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	0.00 (0.00) [0]
	<u>Steel</u>				
1288	FORGED WHEEL PLANT	4/2014	9/2018 (-) [1/2019]	1,682.85 (-) [1,682.85]	502.10 (0.00) [4]
	<u>Telecommunications</u>				
1289	UP (EAST) ACCESS LOT1	11/2017	8/2018 (8/2018) [8/2018]	169.45 (-) [169.45]	77.74 (0.00) [0]
	<u>Urban Development</u>				
1290	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [3/2020]	171.72 (-) [171.72]	0.00 (0.00) [0]
1291	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1292	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [2/2020]	160.10 (-) [160.10]	24.22 (0.00) [0]
	<u>Power</u>				
1293	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	146.27 (274.07) [0]
1294	NAITWAR MORI HEP	10/2017	12/2021	648.33	111.89

			(-) [12/2021]	(-) [648.33]	(0.00) [0]
1295	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,611.12 (867.82) [93]
1296	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (12/2020) [5/2021]	1,657.00 (2,978.86) [4,401.90]	2,597.73 (2,744.90) [63]
1297	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2021]	2,491.58 (-) [3,789.61]	1,446.85 (1,298.03) [102]
	<u>Railways</u>				
1298	HARIDWAR-LAKSAR	4/2012	/	219.83	38.33
			(-) [0/0]	(-) [346.63]	(126.80) [0]
1299	KICHHA-KHATIMA (NL) - NER	4/2003	/	142.45	0.15
			(-) [0/0]	(-) [228.40]	(85.95) [0]
1300	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2026 (-) [3/2026]	4,295.30 (-) [16,216.00]	877.71 (11,920.70) [-9]
	<u>Road Transport And Highways</u>				
1301	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	0.00 (0.00) [0]
1302	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	0.00 (0.00) [0]
1303	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [7/2018]	605.84 (-) [605.84]	722.46 (0.00) [0]
1304	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/	1,443.00	0.00
			(-) [0/0]	(-) [1,443.00]	(0.00) [0]
1305	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	0.00 (0.00) [0]
1306	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/	720.00	0.00
			(-) [0/0]	(-) [720.00]	(0.00) [0]
1307	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [12/2018]	478.51 (-) [478.00]	409.17 (-0.51) [62]
	<u>Urban Development</u>				
1308	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1309	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	294.63 (0.00) [0]
1310	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	349.57 (0.00) [24]
	<u>Health And Family Welfare</u>				
1311	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [9/2018]	244.00 (-) [244.00]	214.62 (0.00) [0]
1312	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-)	168.90 (-)	191.38 (22.48)

			[9/2018]	[191.38]	[16]
1313	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/	651.99	19.50
			(-)	(-)	(0.00)
			[1/2020]	[651.99]	[-]
1314	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019	355.15	71.50
			(-)	(-)	(0.00)
			[3/2019]	[355.15]	[0]
	<u>Petroleum</u>				
1315	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022	3,712.00	0.00
			(-)	(-)	(0.00)
			[9/2022]	[3,712.00]	[0]
1316	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019	2,934.40	536.51
			(-)	(-)	(0.00)
			[9/2019]	[2,934.40]	[0]
1317	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	9/2017	3,076.00	2,945.09
			(6/2018)	(4,190.00)	(1,114.00)
			[6/2018]	[4,190.00]	[0]
1318	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020	1,740.00	18.21
			(-)	(-)	(0.00)
			[12/2020]	[1,740.00]	[0]
1319	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020	1,021.00	5.73
			(-)	(-)	(0.00)
			[12/2020]	[1,021.00]	[0]
1320	HALDIA LPG IMPORT FACILITY	3/2015	10/2018	694.00	431.49
			(12/2018)	(1,097.54)	(0.00)
			[12/2018]	[694.00]	[2]
1321	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020	163.02	31.03
			(-)	(-)	(0.00)
			[4/2020]	[163.02]	[0]
	<u>Power</u>				
1322	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018	454.11	229.72
			(-)	(-)	(0.00)
			[8/2018]	[454.11]	[4]
1323	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019	1,381.84	349.94
			(2/2022)	(-)	(0.00)
			[2/2022]	[1,381.84]	[29]
	<u>Railways</u>				
1324	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	4/1999	12/2012	207.52	334.51
			(-)	(-)	(127.35)
			[0/0]	[334.87]	[0]
1325	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003	1,027.40	484.39
			(3/2030)	(1,966.70)	(1,345.60)
			[3/2030]	[2,373.00]	[324]
1326	BARDHAMAN-KATWA (GC)	4/2007	12/2010	1,106.62	689.50
			(-)	(-)	(0.00)
			[0/0]	[1,106.62]	[0]
1327	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/	255.64	60.68
			(-)	(-)	(16.56)
			[0/0]	[272.20]	[0]
1328	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/	289.64	0.13
			(-)	(289.64)	(691.36)
			[0/0]	[981.00]	[0]
1329	BOWAICHANDI-ARAMBAGH	4/2010	/	267.37	40.77
			(3/2025)	(267.37)	(352.63)
			[3/2025]	[620.00]	[-]
1330	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/	573.78	0.67
			(-)	(-)	(-305.26)
			[0/0]	[268.52]	[0]
1331	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	12/2011	533.38	144.51
			(-)	(-)	(0.00)
			[0/0]	[533.38]	[0]

1332	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [4,874.58]	1,881.65 (0.00) [0]
1333	GHUTIASHARIF-CANNING (ER)	4/2009	12/2011 (-) [0/0]	611.03 (-) [611.03]	149.77 (0.00) [0]
1334	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2025) [3/2025]	393.46 (393.46) [662.00]	182.49 (268.54) [216]
1335	MM FROM PANSKURA-GHATAL NL	4/2011	1/1999 (3/2030) [3/2030]	276.69 (276.69) [426.00]	0.00 (149.31) [374]
1336	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	3/2020 (-) [3/2020]	221.42 (-) [380.00]	97.41 (158.58) [0]
1337	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	36.80 (274.41) [614.00]	266.92 (577.20) [12]
1338	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	283.55 (-) [451.00]	455.01 (167.45) [0]
1339	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	3/2020 (-) [3/2020]	556.31 (-) [612.00]	14.25 (55.69) [0]
1340	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.16 (435.44) [141]
1341	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (4,200.00) [2,913.50]	760.90 (-0.01) [108]
1342	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1343	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	1,801.39 (307.50) [108]
1344	PANDABESWAR-CHINPAI DOUBLING (ER)	4/2004	12/2010 (-) [0/0]	293.74 (-) [229.33]	140.60 (-64.41) [0]
1345	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (12/2021) [12/2021]	763.18 (1,013.45) [1,428.00]	484.48 (664.82) [0]
1346	TAMLUK DIGHA,LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (293.97) [749.69]	0.00 (455.72) [0]
1347	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2019]	1,188.91 (-) [1,319.33]	837.35 (130.42) [0]
1348	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
<u>Road Transport And Highways</u>					
1349	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [5/2019]	1,083.00 (-) [1,083.00]	184.92 (0.00) [11]
1350	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [0/0]	998.79 (-) [998.79]	1,952.35 (0.00) [0]
1351	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [0/0]	1,078.84 (-) [1,078.84]	2,436.15 (0.00) [0]

1352	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	2,811.29 (0.00) [0]
1353	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [12/2019]	361.15 (-) [361.15]	0.00 (0.00) [-]
1354	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [11/2018]	229.37 (-) [229.37]	35.17 (0.00) [0]
1355	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [8/2018]	767.03 (-) [767.03]	123.31 (0.00) [0]
1356	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [0/0]	702.16 (-) [702.16]	464.39 (0.00) [0]
1357	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1358	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [1,665.00]	2,313.68 (0.00) [0]
	<u>Steel</u>				
1359	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
	<u>Urban Development</u>				
1360	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [11/2018]	156.57 (-) [156.57]	138.67 (0.00) [27]
1361	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	67.79 (0.00) [15]
	Total			16,78,634.82 (3,91,095.93) [20,16,360.99]	7,68,186.93 (3,37,726.17)

North East Ongoing Project List

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					31.07.2018)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Petroleum</u>				
1	RAZE REBUILD AND REVAMP OF MARKETING DEPOT AT DOIMUKH	1/2016	2/2019 (-) [12/2018]	247.52 (-) [247.52]	130.75 (0.00) [-2]
	<u>Power</u>				
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (10/2018) [3/2019]	2,496.90 (6,179.96) [6,179.96]	6,604.01 (3,683.06) [111]
3	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,234.01 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
4	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
6	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
7	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [1/2019]	179.82 (-) [179.82]	8.99 (0.00) [0]
8	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
9	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
10	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [10/2018]	197.16 (-) [197.16]	38.50 (0.00) [0]
13	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
14	CONSTRUCTION OF TWO LANE WITH PAVED	2/2017	4/2017	167.28	0.00

	SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI		(-) [0/0]	(-) [167.28]	(0.00) [0]
15	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]
16	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
17	FUNDED)2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
18	FUNDED)CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
19	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
20	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
21	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
22	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
23	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
24	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
25	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
26	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
27	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
28	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
29	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
30	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
31	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
32	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
33	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (3/2019)	2,465.15 (-)	2,099.23 (-86.26)

			[3/2019]	[2,378.89]	[72]
34	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	179.85 (0.00) [0]
35	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
36	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	31.35 (127.41) [70]
37	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [8/2019]	423.00 (-) [423.00]	122.85 (0.00) [0]
38	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [543.91]	1.65 (0.00) [0]
39	DIESEL HYDROTREATOR	7/2015	1/2018 (-) [0/0]	1,031.37 (-) [1,031.37]	305.91 (0.00) [0]
40	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	917.79 (0.00) [0]
41	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	35.56 (-5.15) [0]
42	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	961.00 (328.65) [0]
	<u>Power</u>				
43	BONGAIGAON THERMAL POWER PROJECT	1/2008	9/2011 (6/2018) [9/2018]	4,375.35 (8,150.00) [8,150.00]	7,117.65 (3,774.65) [84]
	<u>Railways</u>				
44	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	312.12 (-) [551.00]	590.20 (238.88) [0]
45	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2022]	2,232.32 (-) [2,182.00]	178.69 (-50.32) [0]
46	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	9/1997	4/2008 (12/2011) [6/2018]	1,500.00 (4,857.00) [5,820.00]	5,178.44 (4,320.00) [0]
47	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [871.00]	148.14 (0.04) [0]
48	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (-) [398.93]	203.30 (152.86) [0]
49	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	200.00 (-) [1,532.00]	525.15 (1,332.00) [12]
	<u>Road Transport And Highways</u>				
50	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
51	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
52	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [12/2018]	225.02 (-) [159.20]	0.00 (-65.82) [0]

53	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
54	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
55	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [11/2018]	588.95 (-) [588.95]	80.00 (0.00) [0]
56	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2018]	289.99 (-) [289.99]	0.00 (0.00) [0]
57	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
58	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
59	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
60	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [0/0]	217.61 (-) [309.56]	389.08 (91.95) [0]
61	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [0/0]	160.00 (-) [160.00]	198.82 (0.00) [0]
62	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [1/2019]	829.00 (-) [829.00]	59.85 (0.00) [0]
63	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2018]	168.39 (-) [168.39]	16.84 (0.00) [0]
64	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
65	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
66	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [361.00]	410.32 (81.00) [0]
67	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
68	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
69	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [385.13]	209.80 (185.32) [0]
70	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [9/2018]	167.64 (-) [167.64]	268.94 (0.00) [118]
71	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	12/2003	4/2009 (-) [10/2018]	200.00 (-) [200.00]	245.83 (0.00) [114]
72	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [0/0]	208.00 (-) [208.00]	0.00 (0.00) [0]
73	NALBARI TO BIJNI (AS-6)	12/2003	6/2008	225.00	312.79

			(-) [0/0]	(-) [225.00]	(0.00) [0]
74	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [11/2017]	245.00 (-) [245.00]	214.88 (0.00) [0]
75	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM	5/2011	2/2018 (-) [0/0]	176.22 (-) [176.22]	0.00 (0.00) [0]
76	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
77	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	727.56 (-) [13,809.00]	7,765.91 (13,081.44) [108]
	<u>Urban Development</u>				
78	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [11/2018]	216.69 (-) [216.69]	52.00 (0.00) [44]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
79	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	69.24 (0.00) [16]
	<u>Railways</u>				
80	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	4,083.02 (-) [6,000.00]	259.12 (1,916.98) [0]
	<u>Road Transport And Highways</u>				
81	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
82	JORBAT - BARAPANI	1/2011	1/2014 (-) [8/2018]	536.00 (-) [536.00]	673.92 (0.00) [55]
83	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	6.14 (0.00) [0]
	<u>Steel</u>				
84	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [12/2018]	151.33 (-) [151.33]	7.15 (0.00) [15]
	<u>MIZORAM</u>				
	<u>Railways</u>				
85	BHAIRABI SAIRONG, NL, NEFR	4/2008	4/2014 (-) [3/2020]	619.34 (-) [4,600.00]	2,252.69 (3,980.66) [71]
	<u>Road Transport And Highways</u>				
86	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
87	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
88	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
89	DIMAPUR-TIZIT NL	4/2013	3/2020	4,274.00	0.00

			(-) [3/2020]	(-) [4,274.00]	(0.00) [0]
90	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (-) [3/2020]	850.00 (-) [3,000.00]	638.43 (2,150.00) [60]
	<u>Road Transport And Highways</u>				
91	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [9/2018]	239.30 (-) [239.30]	0.00 (0.00) [0]
92	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2018]	285.68 (-) [285.68]	0.00 (0.00) [0]
93	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [9/2018]	282.98 (-) [282.98]	0.00 (0.00) [0]
94	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [9/2018]	387.00 (-) [387.00]	0.00 (0.00) [0]
95	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [9/2018]	500.09 (-) [500.09]	0.00 (0.00) [0]
96	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
97	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	339.57 (-) [339.57]	0.00 (0.00) [0]
98	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [9/2018]	315.03 (-) [315.03]	0.00 (0.00) [0]
99	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [9/2018]	240.64 (-) [240.64]	0.00 (0.00) [0]
100	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [9/2018]	215.12 (-) [215.12]	0.00 (0.00) [0]
101	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [9/2018]	215.79 (-) [215.79]	0.00 (0.00) [0]
102	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [9/2018]	272.89 (-) [272.89]	0.00 (0.00) [0]
103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [9/2018]	323.98 (-) [323.98]	0.00 (0.00) [0]
104	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [9/2018]	251.97 (-) [251.97]	0.00 (0.00) [0]
105	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [9/2018]	237.72 (-) [237.72]	0.00 (0.00) [0]
106	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
107	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
108	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
109	WIDENING OF 2(TWO) LANING OF LONGLENG-	12/2010	2/2011	1,296.00	0.00

	CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA		(-) [0/0]	(-) [1,296.00]	(0.00) [0]
	<u>SIKKIM</u>				
	<u>Civil Aviation</u>				
110	CONSTRUCTION OF NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	1/2009	1/2011 (-) [9/2018]	309.46 (-) [553.53]	546.69 (244.07) [92]
	<u>Railways</u>				
111	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
112	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
113	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
114	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
115	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TRIPURA</u>				
	<u>Power</u>				
116	TRIPURA GAS BASED POWER PROJECT	7/2009	7/2013 (-) [0/0]	421.01 (-) [1,078.31]	963.23 (657.30) [0]
	<u>Railways</u>				
117	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (-) [3/2020]	813.34 (-) [3,374.00]	2,951.92 (2,560.66) [72]
118	AGARTALA-AKHAURA NL	4/2012	3/2019 (-) [7/2019]	252.00 (-) [580.00]	0.00 (328.00) [4]
119	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (4,118.00) [1,857.00]	1,540.32 (962.00) [0]
	<u>Road Transport And Highways</u>				
120	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	36.90 (0.00) [0]
121	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Steel</u>				
122	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
123	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
124	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			73,123.34 (24,934.22) [1,29,702.61]	58,002.73 (56,579.27)
